

 NISOC	نگهداشت و افزایش تولید میدان نفتی بینک سطح الارض و ابنیه تحت الارض خرید بسته نم زدای گاز ایستگاه تقویت فشار گاز بینک (قرارداد BK-HD-GCS-CO-0010_08)								
	Time Schedule								
شماره پیمان:	پروژه	بسته کاری	صادر کننده	تسهیلات	رشته	نوع مدرک	سریال	نسخه	شماره صفحه: 1 از 9
053 – 073 – 9184	BK	GCS	MF	120	GE	SH	0001	V01	

طرح نگهداشت و افزایش تولید 27 مخزن

Time Schedule

نگهداشت و افزایش تولید میدان نفتی بینک

V01	01.Oct.2024	IFI	MFS	M.Fakharian	M.Sadeghian	
V00	28.Jan.2024	IFA	MFS	M.Fakharian	M.Sadeghian	
Rev.	Date	Purpose of Issue / Status	Prepared by:	Checked by:	Approved by:	CLIENT Approval

status:


IFA: Issued For Approval

IFI: Issued For Information

AFC: Approved For Construction



TIME SCHEDULE OF BINAK OILFIELD DEVELOPMENT REV.01

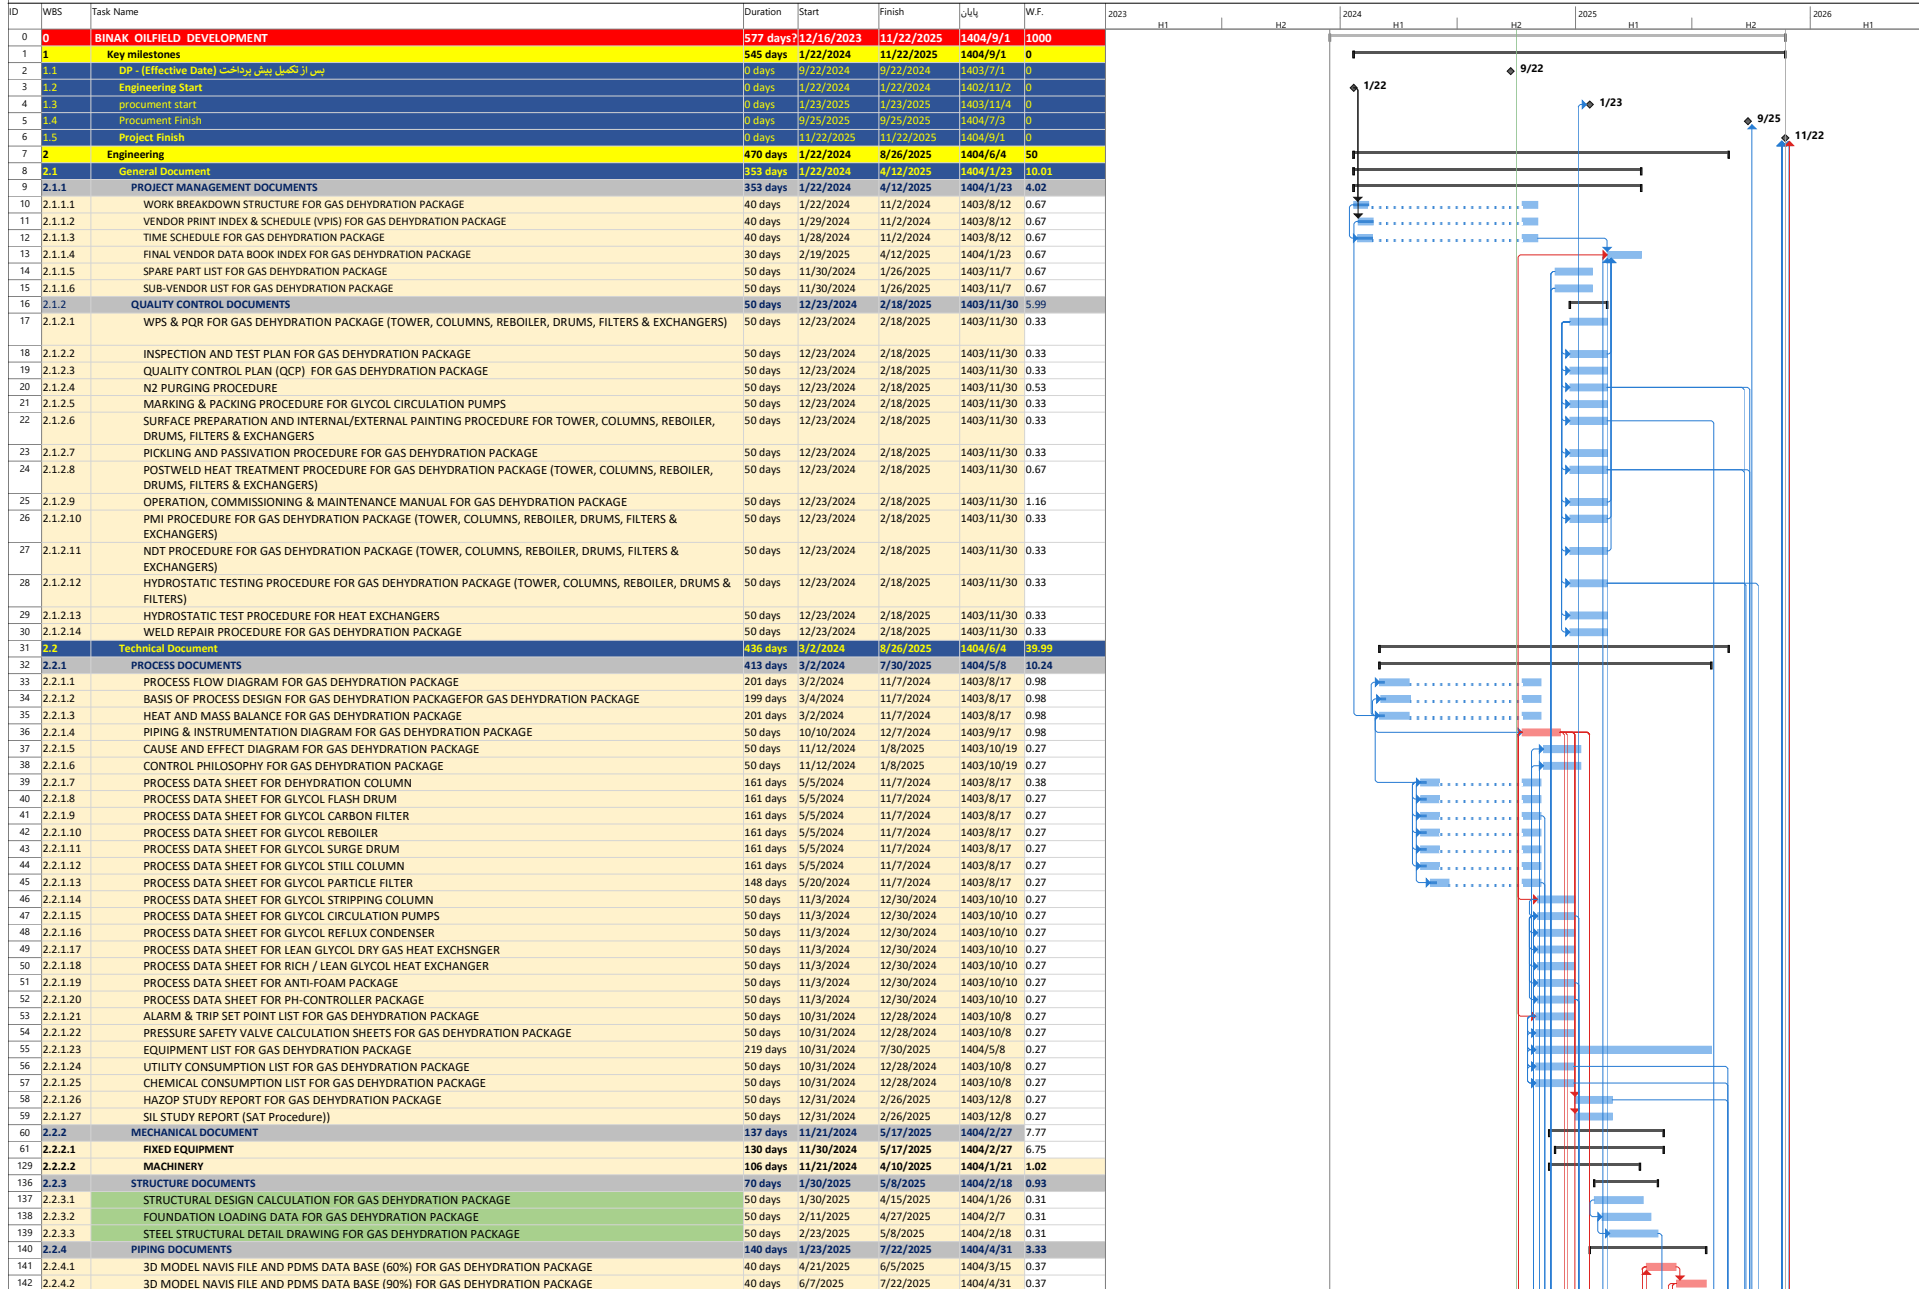



TIME SCHEDULE OF BINAK OILFIELD DEVELOPMENT REV.01



ID	WBS	Task Name	Duration	Start	Finish	پایان	W.F.	2023	H1	H2	2024	H1	H2	2025	H1	H2	2026	H1
143	2.2.4.3	PIPING ISOMETRIC DRAWING FOR GAS DEHYDRATION PACKAGE	40 days	5/3/2025	6/17/2025	1404/3/27	0.37											
144	2.2.4.4	PIPING GENERAL ARRANGEMENT DRAWING FOR GAS DEHYDRATION PACKAGE	40 days	5/3/2025	6/17/2025	1404/3/27	0.37											
145	2.2.4.5	PACKAGE PLOT PLAN FOR GAS DEHYDRATION PACKAGE	40 days	5/3/2025	6/17/2025	1404/3/27	0.37											
146	2.2.4.6	LINE LIST FOR GAS DEHYDRATION PACKAGE	40 days	1/23/2025	3/10/2025	1403/12/20	0.37											
147	2.2.4.7	TIE-IN-LIST FOR GAS DEHYDRATION PACKAGE	40 days	1/23/2025	3/10/2025	1403/12/20	0.37											
148	2.2.4.8	SUPPORT LIST FOR GAS DEHYDRATION PACKAGE	40 days	1/23/2025	3/10/2025	1403/12/20	0.37											
149	2.2.4.9	STRESS ANALYSIS REPORT FOR GAS DEHYDRATION PACKAGE	40 days	1/23/2025	3/10/2025	1403/12/20	0.37											
150	2.2.5	ELECTRICAL DOCUMENTS	220 days	11/26/2024	8/26/2025	1404/6/4	5.42											
151	2.2.5.1	Electrical single line diagram	50 days	11/26/2024	1/22/2025	1403/11/3	0.44											
152	2.2.5.2	ELECTRICAL PANEL LAYOUT AND WIRING DIAGRAM	50 days	11/26/2024	1/22/2025	1403/11/3	0.44											
153	2.2.5.3	Local control station (LCS) panel layout and wiring diagram	50 days	11/26/2024	1/22/2025	1403/11/3	0.44											
154	2.2.5.4	Earthing detail layout	50 days	6/30/2025	8/26/2025	1404/6/4	0.31											
155	2.2.5.5	ELECTRICAL EQUIPMENT LAYOUT	50 days	6/30/2025	8/26/2025	1404/6/4	0.31											
156	2.2.5.6	Electrical Cable Route	50 days	6/30/2025	8/26/2025	1404/6/4	0.44											
157	2.2.5.7	Power and control cable list	50 days	6/30/2025	8/26/2025	1404/6/4	0.44											
158	2.2.5.8	Electrical load list	50 days	6/30/2025	8/26/2025	1404/6/4	0.44											
159	2.2.5.9	ELECTRICAL SIGNAL LIST	50 days	6/30/2025	8/26/2025	1404/6/4	0.44											
160	2.2.5.10	Electrical motor data sheets , CURVES, DRAWINGS AND CERTIFICATES	50 days	4/3/2025	5/31/2025	1404/3/10	0.44											
161	2.2.5.11	CABLE DATASHEETS	50 days	4/3/2025	5/31/2025	1404/3/10	0.44											
162	2.2.5.12	ELECTRICAL PANEL DATASHEETS	50 days	4/3/2025	5/31/2025	1404/3/10	0.44											
163	2.2.5.13	LOCAL CONTROL STATION (LCS) DATASHEETS	50 days	4/3/2025	5/31/2025	1404/3/10	0.4											
164	2.2.6	INSTRUMENT DOCUMENTS	190 days	12/8/2024	8/3/2025	1404/5/12	12.3											
165	2.2.6.1	Instrument list	50 days	12/19/2024	2/15/2025	1403/11/27	0.3											
166	2.2.6.2	Input/Output signal list	50 days	12/19/2024	2/15/2025	1403/11/27	0.3											
167	2.2.6.3	Instrument cable list	50 days	12/19/2024	2/15/2025	1403/11/27	0.3											
168	2.2.6.4	UCP and BMS system power consumption list	50 days	12/19/2024	2/15/2025	1403/11/27	0.3											
169	2.2.6.5	Modbus IO list (Modbus mapping list)	50 days	12/19/2024	2/15/2025	1403/11/27	0.3											
170	2.2.6.6	CONTROL SYSTEM CONFIGURATION BLOCK DIAGRAM	50 days	12/8/2024	2/3/2025	1403/11/15	0.3											
171	2.2.6.7	ESD/BMS SYSTEM CONFIGURATION BLOCK DIAGRAM	50 days	12/8/2024	2/3/2025	1403/11/15	0.3											
172	2.2.6.8	Instrument junction box layout and wiring termination diagram	50 days	12/8/2024	2/3/2025	1403/11/15	0.3											
173	2.2.6.9	Burner operation panel layout & wiring diagram with connections & dimensions	50 days	12/8/2024	2/3/2025	1403/11/15	0.3											
174	2.2.6.10	Instrument D.S. for control valves	50 days	12/31/2024	2/26/2025	1403/12/8	0.3											
175	2.2.6.11	Instrument D.S. for On/Off valves	50 days	12/31/2024	2/26/2025	1403/12/8	0.3											
176	2.2.6.12	Instrument D.S. for H2O analyzer	50 days	12/31/2024	2/26/2025	1403/12/8	0.3											
177	2.2.6.13	Instrument D.S. for temperature gauge	50 days	12/31/2024	2/26/2025	1403/12/8	0.3											
178	2.2.6.14	Instrument D.S. for temperature transmitters	50 days	12/31/2024	2/26/2025	1403/12/8	0.3											
179	2.2.6.15	Instrument D.S. for pressure gauges and differential gauges	50 days	12/31/2024	2/26/2025	1403/12/8	0.3											
180	2.2.6.16	Instrument D.S. for pressure transmitters and differentia pressure transmitters	50 days	12/31/2024	2/26/2025	1403/12/8	0.3											
181	2.2.6.17	INSTRUMENT D.S. FOR SAFETY VALVES	50 days	12/31/2024	2/26/2025	1403/12/8	0.3											
182	2.2.6.18	Instrument D.S. for pressure regulator valves	50 days	12/31/2024	2/26/2025	1403/12/8	0.3											
183	2.2.6.19	Instrument D.S. for flow elements	50 days	12/31/2024	2/26/2025	1403/12/8	0.3											
184	2.2.6.20	Instrument D.S. for level gauges	50 days	12/31/2024	2/26/2025	1403/12/8	0.3											
185	2.2.6.21	Instrument D.S. for level transmitters	50 days	12/31/2024	2/26/2025	1403/12/8	0.3											
186	2.2.6.22	Flame scanner data sheet	50 days	12/31/2024	2/26/2025	1403/12/8	0.3											
187	2.2.6.23	Instrument location layout	50 days	6/7/2025	8/3/2025	1404/5/12	0.3											
188	2.2.6.24	INSTRUMENT EARTH DISTRIBUTION DIAGRAM	50 days	6/7/2025	8/3/2025	1404/5/12	0.3											
189	2.2.6.25	INSTRUMENT CABLE ROUTE/ MAIN TUBING LAYOUT DRAWING	50 days	6/7/2025	8/3/2025	1404/5/12	0.3											
190	2.2.6.26	CONTROL PANEL LAYOUT AND ARRANGEMENT	50 days	1/23/2025	4/8/2025	1404/1/19	0.3											
191	2.2.6.27	ESD/BMS PANEL LAYOUT AND ARRANGEMENT	50 days	1/23/2025	4/8/2025	1404/1/19	0.3											
192	2.2.6.28	CONTROL SYSTEM WIRING DIAGRAM AND CONNECTIONS	50 days	1/23/2025	4/8/2025	1404/1/19	0.3											
193	2.2.6.29	ESD/BMS SYSTEM WIRING DIAGRAM AND CONNECTIONS	50 days	1/23/2025	4/8/2025	1404/1/19	0.3											
194	2.2.6.30	CONTROL SYSTEM CABINETS AND CONSOLES LAYOUT DRAWING	50 days	1/23/2025	4/8/2025	1404/1/19	0.3											
195	2.2.6.31	CONTROL SYSTEM LOGIC DIAGRAM	50 days	1/23/2025	4/8/2025	1404/1/19	0.3											
196	2.2.6.32	ESD/BMS SYSTEM LOGIC DIAGRAM	50 days	1/23/2025	4/8/2025	1404/1/19	0.3											
197	2.2.6.33	PRINT OUT OF HMI FOR BMS and UCP	50 days	1/23/2025	4/8/2025	1404/1/19	0.3											
198	2.2.6.34	Hook up drawing	50 days	1/23/2025	4/8/2025	1404/1/19	0.3											
199	2.2.6.35	ESD LEVEL HIERARCHY	50 days	1/23/2025	4/8/2025	1404/1/19	0.3											
200	2.2.6.36	FAT PROCEDURE FOR CONTROL SYSTEM	50 days	5/3/2025	6/29/2025	1404/4/8	0.3											
201	2.2.6.37	FAT PROCEDURE FOR ESD/BMS SYSTEM	50 days	5/3/2025	6/29/2025	1404/4/8	0.3											
202	2.2.6.38	SAT PROCEDURE FOR CONTROL SYSTEM	50 days	5/3/2025	6/29/2025	1404/4/8	0.3											
203	2.2.6.39	SAT PROCEDURE FOR ESD/BMS SYSTEM	50 days	5/3/2025	6/29/2025	1404/4/8	0.3											
204	2.2.6.40	ITP FOR CONTROL SYSTEM	50 days	5/3/2025	6/29/2025	1404/4/8	0.3											
205	2.2.6.41	ITP FOR ESD/BMS SYSTEM	50 days	5/3/2025	6/29/2025	1404/4/8	0.3											
206	3	RAW MATERIAL	300 days	11/9/2024	11/10/2025	1404/8/19	450											
207	3.1	BMS & UCP	240 days	12/19/2024	10/12/2025	1404/7/20	99											
208	3.1.1	PO	30 days	12/19/2024	1/22/2025	1403/11/3	29.7											
209	3.1.2	Supply/Receive	210 days	1/23/2025	10/12/2025	1404/7/20	69.3											
210	3.2	Field Instrument	135 days	2/27/2025	8/20/2025	1404/5/29	99											
211	3.2.1	PO	15 days	2/27/2025	4/2/2025	1404/1/13	29.7											
212	3.2.2	Supply/Receive	120 days	4/3/2025	8/20/2025	1404/5/29	69.3											
213	3.3	Pipe	30 days	3/15/2025	5/5/2025	1404/2/15	36											
214	3.3.1	PO	5 days	3/15/2025	4/6/2025	1404/1/17	10.8											
215	3.3.2	Supply/Receive	25 days	4/7/2025	5/5/2025	1404/2/15	25.2											
216	3.4	plate	60 days	2/8/2025	5/5/2025	1404/2/15	36											
217	3.4.1	PO	10 days	2/8/2025	2/18/2025	1403/11/30	10.8											



TIME SCHEDULE OF BINAK OILFIELD DEVELOPMENT REV.01



ID	WBS	Task Name	Duration	Start	Finish	پایان	W.F.	2023	H1	H2	2024	H1	H2	2025	H1	H2	2026	H1
218	3.4.2	Supply/Receive	50 days	2/19/2025	5/5/2025	1404/2/15	25.2											
219	3.5	Flange	110 days	3/15/2025	8/6/2025	1404/5/15	13.5											
220	3.5.1	PO	5 days	3/15/2025	4/6/2025	1404/1/17	4.05											
221	3.5.2	Supply/Receive	105 days	4/7/2025	8/6/2025	1404/5/15	9.45											
222	3.6	Gasket	45 days	7/29/2025	9/18/2025	1404/6/27	4.5											
223	3.6.1	PO	5 days	7/29/2025	8/3/2025	1404/5/12	1.35											
224	3.6.2	Supply/Receive	40 days	8/4/2025	9/18/2025	1404/6/27	3.15											
225	3.7	Fitting	30 days	3/15/2025	5/5/2025	1404/2/15	4.5											
226	3.7.1	PO	5 days	3/15/2025	4/6/2025	1404/1/17	1.35											
227	3.7.2	Supply/Receive	25 days	4/7/2025	5/5/2025	1404/2/15	3.15											
228	3.8	Bolt & Nut	45 days	7/29/2025	9/18/2025	1404/6/27	4.5											
229	3.8.1	PO	5 days	7/29/2025	8/3/2025	1404/5/12	1.35											
230	3.8.2	Supply/Receive	40 days	8/4/2025	9/18/2025	1404/6/27	3.15											
231	3.9	Valves	184 days	2/27/2025	10/16/2025	1404/7/24	13.5											
232	3.9.1	PO	15 days	2/27/2025	4/2/2025	1404/1/13	4.05											
233	3.9.2	Supply/Receive	169 days	4/3/2025	10/16/2025	1404/7/24	9.45											
234	3.10	TEG Pumps - 2 Sets	170 days	12/31/2024	8/3/2025	1404/5/12	9											
235	3.10.1	PO	20 days	12/31/2024	1/22/2025	1403/11/3	2.7											
236	3.10.2	Supply/Receive	150 days	1/23/2025	8/3/2025	1404/5/12	6.3											
237	3.11	Internals	125 days	12/31/2024	6/11/2025	1404/3/21	13.5											
238	3.11.1	PO	15 days	12/31/2024	1/16/2025	1403/10/27	4.05											
239	3.11.2	Supply/Receive	110 days	1/18/2025	6/11/2025	1404/3/21	9.45											
240	3.12	Analyzer	170 days	12/31/2024	8/3/2025	1404/5/12	10											
241	3.12.1	PO	20 days	12/31/2024	1/22/2025	1403/11/3	5.4											
242	3.12.2	Supply/Receive	150 days	1/23/2025	8/3/2025	1404/5/12	12.6											
243	3.13	Burner	220 days	12/26/2024	9/25/2025	1404/7/3	27											
244	3.13.1	PO	20 days	12/26/2024	1/18/2025	1403/10/29	8.1											
245	3.13.2	Supply/Receive	200 days	1/19/2025	9/25/2025	1404/7/3	18.9											
246	3.14	Panel & Junction Box	125 days	2/4/2025	7/16/2025	1404/4/25	13.5											
247	3.14.1	PO	15 days	2/4/2025	2/20/2025	1403/12/2	4.05											
248	3.14.2	Supply/Receive	110 days	2/22/2025	7/16/2025	1404/4/25	9.45											
249	3.15	Profile	30 days	3/15/2025	5/5/2025	1404/2/15	9											
250	3.15.1	PO	5 days	3/15/2025	4/6/2025	1404/1/17	2.7											
251	3.15.2	Supply/Receive	25 days	4/7/2025	5/5/2025	1404/2/15	6.3											
252	3.16	Injection Package	180 days	12/31/2024	8/14/2025	1404/5/23	9											
253	3.16.1	PO	15 days	12/31/2024	1/16/2025	1403/10/27	2.7											
254	3.16.2	Supply/Receive	165 days	1/18/2025	8/14/2025	1404/5/23	6.3											
255	3.17	INSTRUMEN and Electrical Tray,support,ladder,Connection,...(Installation Cable Accessory)	135 days	6/7/2025	11/10/2025	1404/8/19	27											
256	3.17.1	PO	15 days	6/7/2025	6/23/2025	1404/4/2	8.1											
257	3.17.2	Supply/Receive	120 days	6/24/2025	11/10/2025	1404/8/19	18.9											
258	3.18	Cable	55 days	8/27/2025	10/29/2025	1404/8/7	4.5											
259	3.18.1	PO	10 days	8/27/2025	9/7/2025	1404/6/16	1.35											
260	3.18.2	Supply/Receive	45 days	9/8/2025	10/29/2025	1404/8/7	3.15											
261	3.19	Filter	120 days	11/9/2024	4/14/2025	1404/3/25	4.5											
262	3.19.1	PO	15 days	11/9/2024	11/25/2024	1403/9/5	1.35											
263	3.19.2	Supply/Receive	105 days	11/26/2024	4/14/2025	1404/1/25	3.15											
264	3.20	Paint	35 days	8/4/2025	9/13/2025	1404/6/22	4.5											
265	3.20.1	PO	5 days	8/4/2025	8/9/2025	1404/5/18	1.35											
266	3.20.2	Supply/Receive	30 days	8/10/2025	9/13/2025	1404/6/22	3.15											
267	4	Construction	168 days	5/6/2025	11/17/2025	1404/8/26	400											
268	4.1	Pressure Vessel	150 days	5/6/2025	10/27/2025	1404/8/5	236.98											
269	4.1.1	C-100 Glycol Contactor	150 days	5/6/2025	10/27/2025	1404/8/5	50.24											
270	4.1.1.1	Shell	11 days	5/6/2025	5/18/2025	1404/2/28	12.26											
276	4.1.1.2	Head	34 days	5/6/2025	6/14/2025	1404/3/24	7.59											
279	4.1.1.3	External Part	86 days	5/6/2025	8/13/2025	1404/5/22	6.01											
289	4.1.1.4	Internal Part	9 days	5/6/2025	5/15/2025	1404/2/25	1.54											
294	4.1.1.5	Final Assembly	91 days	6/15/2025	9/28/2025	1404/7/6	20.29											
305	4.1.1.6	Final Activity	25 days	9/29/2025	10/27/2025	1404/8/5	2.55											
312	4.1.2	C-200 Still Column	125 days	5/6/2025	9/28/2025	1404/7/6	28.57											
313	4.1.2.1	Shell	7 days	5/6/2025	5/13/2025	1404/2/23	7.18											
319	4.1.2.2	Head	34 days	5/6/2025	6/14/2025	1404/3/24	4.31											
322	4.1.2.3	External Part	86 days	5/6/2025	8/13/2025	1404/5/22	3.46											
332	4.1.2.4	Internal Part	9 days	5/6/2025	5/15/2025	1404/2/25	0.86											
337	4.1.2.5	Final Assembly	77 days	6/15/2025	9/11/2025	1404/6/20	11.26											
348	4.1.2.6	Final Activity	14 days	9/13/2025	9/28/2025	1404/7/6	1.5											
355	4.1.3	Lean Glycol Filter (F-300)	116 days	5/6/2025	9/17/2025	1404/6/26	18.36											
356	4.1.3.1	Shell	14 days	5/6/2025	5/21/2025	1404/2/31	4.67											
362	4.1.3.2	Head	31 days	5/6/2025	6/10/2025	1404/3/20	2.73											
365	4.1.3.3	External Part	83 days	5/6/2025	8/10/2025	1404/5/19	2.22											
375	4.1.3.4	Internal Part	6 days	5/6/2025	5/12/2025	1404/2/22	0.56											
380	4.1.3.5	Final Assembly	70 days	6/11/2025	8/31/2025	1404/6/9	7.27											
391	4.1.3.6	Final Activity	15 days	9/1/2025	9/17/2025	1404/6/26	0.91											
398	4.1.4	V-120 Glycol Flash Drum	130 days	5/6/2025	10/4/2025	1404/7/12	39.45											
399	4.1.4.1	Shell	13 days	5/6/2025	5/20/2025	1404/2/30	9.92											
405	4.1.4.2	Head	33 days	5/6/2025	6/12/2025	1404/3/22	5.92											



TIME SCHEDULE OF BINAK OILFIELD DEVELOPMENT
REV.01



ID	WBS	Task Name	Duration	Start	Finish	پایان	W.F.	2023	H1	H2	2024	H1	H2	2025	H1	H2	2026	H1
408	4.1.4.3	External Part	89 days	5/6/2025	8/17/2025	1404/5/26	4.83											
418	4.1.4.4	Internal Part	6 days	5/6/2025	5/12/2025	1404/2/22	1.26											
423	4.1.4.5	Final Assembly	83 days	6/14/2025	9/17/2025	1404/6/26	15.5											
434	4.1.4.6	Final Activity	14 days	9/18/2025	10/4/2025	1404/7/12	2.02											
441	4.1.5	F-100A Particle Glycol Filter	124 days	5/6/2025	9/27/2025	1404/7/5	14.1											
442	4.1.5.1	Shell	6 days	5/10/2025	5/15/2025	1404/2/25	3.58											
448	4.1.5.2	Head	31 days	5/10/2025	6/14/2025	1404/3/24	2.05											
451	4.1.5.3	External Part	85 days	5/6/2025	8/12/2025	1404/5/21	1.64											
461	4.1.5.4	Internal Part	6 days	5/24/2025	5/29/2025	1404/3/8	0.42											
466	4.1.5.5	Final Assembly	72 days	6/15/2025	9/6/2025	1404/6/15	5.72											
477	4.1.5.6	Final Activity	18 days	9/7/2025	9/27/2025	1404/7/5	0.69											
484	4.1.6	F-100B Particle Glycol Filter	114 days	5/6/2025	9/15/2025	1404/6/24	13.99											
485	4.1.6.1	Shell	6 days	5/6/2025	5/12/2025	1404/2/22	3.05											
491	4.1.6.2	Head	31 days	5/6/2025	6/10/2025	1404/3/20	2.6											
494	4.1.6.3	External Part	85 days	5/6/2025	8/12/2025	1404/5/21	1.94											
504	4.1.6.4	Internal Part	6 days	5/6/2025	5/12/2025	1404/2/22	0.66											
509	4.1.6.5	Final Assembly	64 days	6/11/2025	8/24/2025	1404/6/2	4.6											
520	4.1.6.6	Final Activity	19 days	8/25/2025	9/15/2025	1404/6/24	1.14											
527	4.1.7	F-200 Carbon Glycol Filter	116 days	5/6/2025	9/17/2025	1404/6/26	16.18											
528	4.1.7.1	Shell	6 days	5/10/2025	5/15/2025	1404/2/25	4.03											
534	4.1.7.2	Head	31 days	5/10/2025	6/14/2025	1404/3/24	2.42											
537	4.1.7.3	External Part	88 days	5/6/2025	8/16/2025	1404/5/25	1.96											
547	4.1.7.4	Internal Part	7 days	5/6/2025	5/13/2025	1404/2/23	0.49											
552	4.1.7.5	Final Assembly	64 days	6/15/2025	8/27/2025	1404/6/5	6.47											
563	4.1.7.6	Final Activity	18 days	8/28/2025	9/17/2025	1404/6/26	0.81											
570	4.1.8	E-100 Glycol reflux condenser COIL TYPE	129 days	5/6/2025	10/2/2025	1404/7/10	24.2											
571	4.1.8.1	Shell	5 days	5/18/2025	5/22/2025	1404/3/1	6.05											
577	4.1.8.2	External Part	83 days	5/6/2025	8/10/2025	1404/5/19	2.44											
587	4.1.8.3	Coil	10 days	5/6/2025	5/17/2025	1404/2/27	4.82											
591	4.1.8.4	Final Assembly	98 days	5/24/2025	9/14/2025	1404/6/23	9.66											
602	4.1.8.5	Final Activity	16 days	9/15/2025	10/2/2025	1404/7/10	1.23											
610	4.1.9	V-130 Surge Tank	136 days	5/6/2025	10/11/2025	1404/7/19	31.89											
611	4.1.9.1	Shell	16 days	5/6/2025	5/24/2025	1404/3/3	7.98											
617	4.1.9.2	Head	36 days	5/6/2025	6/16/2025	1404/3/26	4.78											
620	4.1.9.3	External Part	90 days	5/6/2025	8/18/2025	1404/5/27	3.83											
630	4.1.9.4	Internal Part	10 days	5/6/2025	5/17/2025	1404/2/27	0.96											
635	4.1.9.5	Final Assembly	85 days	6/17/2025	9/23/2025	1404/7/1	12.75											
646	4.1.9.6	Final Activity	15 days	9/24/2025	10/11/2025	1404/7/19	1.59											
653	4.2	Heat exchanger	138 days	5/6/2025	10/13/2025	1404/7/21	46.96											
654	4.2.1	E -200 Rich-Lean HE	135 days	5/6/2025	10/9/2025	1404/7/17	22.08											
655	4.2.1.1	Shell	5 days	5/15/2025	5/20/2025	1404/2/30	7.59											
661	4.2.1.2	External Part	83 days	5/6/2025	8/10/2025	1404/5/19	2.23											
671	4.2.1.3	Internal Plate	5 days	5/6/2025	5/11/2025	1404/2/21	1.9											
674	4.2.1.4	Final Assembly	106 days	5/21/2025	9/21/2025	1404/6/30	8.65											
685	4.2.1.5	Final Activity	16 days	9/22/2025	10/9/2025	1404/7/17	1.71											
693	4.2.2	E -300 LEAN TEG - DRY GAS EXCH	138 days	5/6/2025	10/13/2025	1404/7/21	24.88											
694	4.2.2.1	Shell	5 days	5/6/2025	5/11/2025	1404/2/21	6.2											
700	4.2.2.2	External Part	83 days	5/6/2025	8/10/2025	1404/5/19	2.5											
710	4.2.2.3	Tube Bundle	33 days	5/6/2025	6/12/2025	1404/3/22	4.96											
715	4.2.2.4	Final Assembly	117 days	5/12/2025	9/24/2025	1404/7/2	9.94											
728	4.2.2.5	Final Activity	16 days	9/25/2025	10/13/2025	1404/7/21	1.28											
736	4.3	R-100 Reboiler	128 days	5/6/2025	10/1/2025	1404/7/9	42.5											
737	4.3.1	Shell	7 days	5/6/2025	5/13/2025	1404/2/23	10.66											
738	4.3.1.1	Marking & Cutting & Beveling	1 day	5/6/2025	5/6/2025	1404/2/16	1.52											
739	4.3.1.2	Pre- Assembling & Per-Welding of Plates	1 day	5/7/2025	5/7/2025	1404/2/17	1.52											
740	4.3.1.3	Rolling	2 days	5/8/2025	5/10/2025	1404/2/20	3.05											
741	4.3.1.4	Assemble & Welding of Plates	2 days	5/11/2025	5/12/2025	1404/2/22	3.05											
742	4.3.1.5	Rerolling	1 day	5/13/2025	5/13/2025	1404/2/23	1.52											
743	4.3.2	Head	32 days	5/6/2025	6/11/2025	1404/3/21	6.39											
744	4.3.2.1	Marking & Cutting & Beveling head plate	2 days	5/6/2025	5/7/2025	1404/2/17	0.39											
745	4.3.2.2	Forming Head plate (sub contractor)	30 days	5/8/2025	6/11/2025	1404/3/21	6											
746	4.3.3	External Part	93 days	5/6/2025	8/21/2025	1404/5/30	5.12											
747	4.3.3.1	Nozzles & Manholes	93 days	5/6/2025	8/21/2025	1404/5/30	2.71											
751	4.3.3.2	Lifting & Other External Part	16 days	5/6/2025	5/24/2025	1404/3/3	2.41											
756	4.3.4	Internal Part	9 days	5/6/2025	5/15/2025	1404/2/25	1.29											
757	4.3.4.1	Marking & Cutting & Beveling Internal Part	1 day	5/6/2025	5/6/2025	1404/2/16	0.14											
758	4.3.4.2	Drilling Internal Part	2 days	5/7/2025	5/8/2025	1404/2/18	0.29											
759	4.3.4.3	Assembling of internal parts together	2 days	5/10/2025	5/11/2025	1404/2/21	0.29											
760	4.3.4.4	Welding of internal parts together	4 days	5/12/2025	5/15/2025	1404/2/25	0.57											
761	4.3.5	Final Assembly	83 days	6/12/2025	9/16/2025	1404/6/25	16.64											
762	4.3.5.1	Assembling Shell course & head	5 days	6/12/2025	6/17/2025	1404/3/27	2.44											
763	4.3.5.2	Welding Shell course & head	6 days	6/18/2025	6/24/2025	1404/4/3	2.9											
764	4.3.5.3	Marking & Opening Nozzle	2 days	6/25/2025	6/26/2025	1404/4/5	0.9											
765	4.3.5.4	Assembling nozzle & manhole	2 days	8/23/2025	8/24/2025	1404/6/2	0.9											
766	4.3.5.5	Welding of nozzle & manhole	5 days	8/25/2025	8/30/2025	1404/6/8	2.44											



TIME SCHEDULE OF BINAK OILFIELD DEVELOPMENT
REV.01




ID	WBS	Task Name	Duration	Start	Finish	پایان	W.F.	2023	H1	H2	2024	H1	H2	2025	H1	H2	2026	H1
767	4.3.5.6	Assembling of Lifting & Other External Part	3 days	8/31/2025	9/2/2025	1404/6/11	1.46											
768	4.3.5.7	Welding of Lifting & Other External Part	4 days	9/3/2025	9/7/2025	1404/6/16	1.9											
769	4.3.5.8	Assembling of internal parts	2 days	9/8/2025	9/9/2025	1404/6/18	0.9											
770	4.3.5.9	Welding of internal parts	4 days	9/10/2025	9/14/2025	1404/6/23	1.9											
771	4.3.5.10	Final dimensional inspection	2 days	9/15/2025	9/16/2025	1404/6/25	0.9											
772	4.3.6	Final Activity	13 days	9/17/2025	10/1/2025	1404/7/9	2.4											
773	4.3.6.1	prepare for PWHT	2 days	9/17/2025	9/18/2025	1404/6/27	0.3											
774	4.3.6.2	PWHT	1 day	9/20/2025	9/20/2025	1404/6/29	0.15											
775	4.3.6.3	NDT after PWHT	1 day	9/21/2025	9/21/2025	1404/6/30	0.5											
776	4.3.6.4	Prepare for Hydrotest	1 day	9/22/2025	9/22/2025	1404/6/31	0.15											
777	4.3.6.5	Hydrotest	2 days	9/23/2025	9/24/2025	1404/7/2	0.65											
778	4.3.6.6	Sanblasting & Painting	4 days	9/28/2025	10/1/2025	1404/7/9	0.65											
779	4.4	Skid of Gas Dehydration	163 days	5/10/2025	11/15/2025	1404/8/24	59.75											
780	4.4.1	Profile and Plate	70 days	5/10/2025	7/29/2025	1404/5/7	56.99											
781	4.4.1.1	Marking & Cutting & Beveling of Profile and Plate	15 days	5/10/2025	5/26/2025	1404/3/5	11.03											
782	4.4.1.2	Drilling Profile and Plate	15 days	5/27/2025	6/12/2025	1404/3/22	11.64											
783	4.4.1.3	Assembling of Profile and Plate together	20 days	6/14/2025	7/6/2025	1404/4/15	15.32											
784	4.4.1.4	Welding of Profile and Plate together	20 days	7/7/2025	7/29/2025	1404/5/7	19											
785	4.4.2	Final Activity	4 days	11/11/2025	11/15/2025	1404/8/24	2.76											
786	4.4.2.1	Final dimensional inspection	2 days	11/11/2025	11/12/2025	1404/8/21	0.62											
787	4.4.2.2	Sanblasting & Painting	2 days	11/13/2025	11/15/2025	1404/8/24	2.14											
788	4.5	Piping of Gas Dehydration	131 days	6/18/2025	11/17/2025	1404/8/26	13.61											
789	4.5.1	Piping and External support	85 days	6/18/2025	9/24/2025	1404/7/2	12.4											
790	4.5.1.1	Cutting & Beveling Pipe	20 days	6/18/2025	7/10/2025	1404/4/19	4											
791	4.5.1.2	Assembling of Pipe To Flange	10 days	8/7/2025	8/18/2025	1404/5/27	2											
792	4.5.1.3	Welding of Pipe To Flange	15 days	8/19/2025	9/4/2025	1404/6/13	3											
793	4.5.1.4	Marking & Cutting & Beveling External Plate	5 days	9/6/2025	9/10/2025	1404/6/19	1											
794	4.5.1.5	Assembling of External Plate To Pipe	4 days	9/11/2025	9/15/2025	1404/6/24	0.8											
795	4.5.1.6	Welding of External Plate To Pipe	8 days	9/16/2025	9/24/2025	1404/7/2	1.6											
796	4.5.2	Final Activity	46 days	9/25/2025	11/17/2025	1404/8/26	1.41											
797	4.5.2.1	prepare for PWHT	3 days	9/25/2025	9/28/2025	1404/7/6	0.22											
798	4.5.2.2	PWHT	3 days	9/29/2025	10/1/2025	1404/7/9	0.11											
799	4.5.2.3	NDT after PWHT	3 days	10/2/2025	10/5/2025	1404/7/13	0.11											
800	4.5.2.4	Prepare for Hydrotest	5 days	10/6/2025	10/11/2025	1404/7/19	0.11											
801	4.5.2.5	Hydrotest	6 days	10/12/2025	10/18/2025	1404/7/26	0.43											
802	4.5.2.6	Sanblasting & Painting	4 days	11/13/2025	11/17/2025	1404/8/26	0.43											
803	5	Test & Inspection	573 days	12/16/2023	11/17/2025	1404/8/26	10											
804	5.1	Material Inspection	569 days	12/16/2023	11/12/2025	1404/8/21	5.03											
805	5.1.1	Field Instruments (Transmitter/ Switch/ Gauge/ Analyzer etc)	6 days	8/21/2025	8/27/2025	1404/6/5	0.38											
806	5.1.1.1	Visual Dimensional Inspection(Appearance)	1 day	8/21/2025	8/21/2025	1404/5/30	0.06											
807	5.1.1.2	Calibration Check	1 day	8/23/2025	8/23/2025	1404/6/1	0.06											
808	5.1.1.3	Tag & Model No & Specification Check	1 day	8/24/2025	8/24/2025	1404/6/2	0.06											
809	5.1.1.4	Review Material, IP,ATEX Certificate	1 day	8/25/2025	8/25/2025	1404/6/3	0.06											
810	5.1.1.5	Pressure & Performance Test	1 day	8/26/2025	8/26/2025	1404/6/4	0.07											
811	5.1.1.6	Packing Inspection& Painting	1 day	8/27/2025	8/27/2025	1404/6/5	0.07											
812	5.1.2	Cable, Wires & tray	12 days	10/30/2025	11/12/2025	1404/8/21	0.72											
813	5.1.2.1	Cable & Wires	2 days	10/30/2025	11/1/2025	1404/8/10	0.36											
816	5.1.2.2	Tray	2 days	11/1/2025	11/12/2025	1404/8/21	0.36											
819	5.1.3	Filter	1 day	12/16/2023	12/16/2023	1404/1/26	0.36											
820	5.1.3.1	Inspection for visual and dimensional check	1 day	4/15/2025	4/15/2025	1404/1/26	0.36											
821	5.1.4	Junction Box	4 days	7/17/2025	7/21/2025	1404/4/30	0.36											
822	5.1.4.1	Review IP, ATEX Certificate	1 day	7/17/2025	7/17/2025	1404/4/26	0.09											
823	5.1.4.2	Tag & Model No Check	1 day	7/19/2025	7/19/2025	1404/4/28	0.09											
824	5.1.4.3	Review IP, ATEX certificate	1 day	7/20/2025	7/20/2025	1404/4/29	0.09											
825	5.1.4.4	Packing inspection and painting	1 day	7/21/2025	7/21/2025	1404/4/30	0.09											
826	5.1.5	Local Panel (Outdoor, Hazardous Area)	5 days	7/17/2025	7/22/2025	1404/4/31	0.35											
827	5.1.5.1	Visual Inspection & Dimensional Check	1 day	7/17/2025	7/17/2025	1404/4/26	0.07											
828	5.1.5.2	Accessories Tag & Model No Check	1 day	7/19/2025	7/19/2025	1404/4/28	0.07											
829	5.1.5.3	Construction	1 day	7/20/2025	7/20/2025	1404/4/29	0.07											
830	5.1.5.4	Review IP, ATEX Certificate	1 day	7/21/2025	7/21/2025	1404/4/30	0.07											
831	5.1.5.5	Packing Inspection & Painting	1 day	7/22/2025	7/22/2025	1404/4/31	0.07											
832	5.1.6	Control Panel (Indoor, Safe Area)	4 days	10/13/2025	10/16/2025	1404/7/24	0.36											
833	5.1.6.1	Visual Inspection/ QTY & Dimensional Check	1 day	10/13/2025	10/13/2025	1404/7/21	0.09											
834	5.1.6.2	Tag & Model No Check	1 day	10/14/2025	10/14/2025	1404/7/22	0.09											
835	5.1.6.3	Function & Performance test (Power & Start-up Check, I/O Check)	1 day	10/15/2025	10/15/2025	1404/7/23	0.09											
836	5.1.6.4	Main equipment & Accessories Certificate IP , ATEX, SIL Certificate Check)	1 day	10/16/2025	10/16/2025	1404/7/24	0.09											
837	5.1.7	Valves	7 days	10/18/2025	10/25/2025	1404/8/3	0.71											
838	5.1.7.1	Manual Valves	3 days	10/18/2025	10/20/2025	1404/7/28	0.36											
842	5.1.7.2	Inst.Valves (Shut Down, On/Off, Control & Safety Valves)	7 days	10/18/2025	10/25/2025	1404/8/3	0.35											
850	5.1.8	Strainers	3 days	5/6/2025	5/8/2025	1404/2/18	0.36											



TIME SCHEDULE OF BINAK OILFIELD DEVELOPMENT REV.01



ID	WBS	Task Name	Duration	Start	Finish	پایان	W.F.	2023	H1	H2	2024	H1	H2	2025	H1	H2	2026	H1
851	5.1.8.1	Material Inspection	1 day	5/6/2025	5/6/2025	1404/2/16	0.12											
852	5.1.8.2	Visual and Dimensional Inspection	1 day	5/7/2025	5/7/2025	1404/2/17	0.12											
853	5.1.8.3	Hydro Test	1 day	5/8/2025	5/8/2025	1404/2/18	0.12											
854	5.1.9	Piping Items (Pipe, Flange, Fitting, Gasket, Bolt & Nut)	6 days	9/20/2025	9/25/2025	1404/7/3	0.36											
855	5.1.9.1	Material Inspection	1 day	9/20/2025	9/20/2025	1404/6/29	0.06											
856	5.1.9.2	Visual and Dimensional Inspection	1 day	9/21/2025	9/21/2025	1404/6/30	0.06											
857	5.1.9.3	Weld Preparation and Fit-Up	1 day	9/22/2025	9/22/2025	1404/6/31	0.06											
858	5.1.9.4	Welding	1 day	9/23/2025	9/23/2025	1404/7/1	0.06											
859	5.1.9.5	NDT[VT, MT, PT, UT, RT]	1 day	9/24/2025	9/24/2025	1404/7/2	0.06											
860	5.1.9.6	Hydrostatic Test	1 day	9/25/2025	9/25/2025	1404/7/3	0.06											
861	5.1.10	Pump	2 days	8/4/2025	8/5/2025	1404/5/14	0.36											
862	5.1.10.1	Final Visual and Dimensional Inspection	1 day	8/4/2025	8/4/2025	1404/5/13	0.18											
863	5.1.10.2	Performance test	1 day	8/5/2025	8/5/2025	1404/5/14	0.18											
864	5.1.11	Chemical Injection Package	7 days	8/4/2025	8/11/2025	1404/5/20	0.35											
865	5.1.11.1	Raw Material for Tank	1 day	8/4/2025	8/4/2025	1404/5/13	0.05											
866	5.1.11.2	Final Inspection For Fabricated Tank	1 day	8/5/2025	8/5/2025	1404/5/14	0.05											
867	5.1.11.3	Piping & Structure Works	1 day	8/6/2025	8/6/2025	1404/5/15	0.05											
868	5.1.11.4	Performance test	1 day	8/7/2025	8/7/2025	1404/5/16	0.05											
869	5.1.11.5	Packing Inspection	1 day	8/9/2025	8/9/2025	1404/5/18	0.05											
870	5.1.11.6	IRN	1 day	8/10/2025	8/10/2025	1404/5/19	0.05											
871	5.1.11.7	Final Book	1 day	8/11/2025	8/11/2025	1404/5/20	0.05											
872	5.1.12	Reboiler Burner	2 days	8/16/2025	8/17/2025	1404/5/26	0.36											
873	5.1.12.1	Final Visual and Dimensional Inspection	1 day	8/16/2025	8/16/2025	1404/5/25	0.18											
874	5.1.12.2	Burner Test	1 day	8/17/2025	8/17/2025	1404/5/26	0.18											
875	5.2	Construction Inspection	168 days	5/6/2025	11/17/2025	1404/8/26	4.97											
876	5.2.1	Vessel	150 days	5/6/2025	10/27/2025	1404/8/5	1.27											
877	5.2.1.1	C-100 Glycol Contactor	148 days	5/8/2025	10/27/2025	1404/8/5	0.15											
893	5.2.1.2	C-200 Still Column	124 days	5/7/2025	9/28/2025	1404/7/6	0.14											
908	5.2.1.3	Lean Glycol Filter (F-300)	116 days	5/6/2025	9/17/2025	1404/6/26	0.14											
923	5.2.1.4	V-120 Glycol Flash Drum	129 days	5/7/2025	10/4/2025	1404/7/12	0.14											
938	5.2.1.5	F-100A Particle Glycol Filter	121 days	5/10/2025	9/27/2025	1404/7/5	0.14											
953	5.2.1.6	F-100B Particle Glycol Filter	114 days	5/6/2025	9/15/2025	1404/6/24	0.14											
968	5.2.1.7	F-200 Carbon Glycol Filter	113 days	5/10/2025	9/17/2025	1404/6/26	0.14											
983	5.2.1.8	E-100 Glycol reflux condenser COIL TYPE	119 days	5/18/2025	10/2/2025	1404/7/10	0.14											
998	5.2.1.9	V-130 Surge Tank	135 days	5/7/2025	10/11/2025	1404/7/19	0.14											
1013	5.2.2	Heat Exchanger	138 days	5/6/2025	10/13/2025	1404/7/21	1.2											
1014	5.2.2.1	E -200 Rich-Lean HE	127 days	5/15/2025	10/9/2025	1404/7/17	0.6											
1030	5.2.2.2	E -300 LEAN TEG - DRY GAS EXCH	138 days	5/6/2025	10/13/2025	1404/7/21	0.6											
1046	5.2.3	Reboiler	128 days	5/6/2025	10/1/2025	1404/7/9	0.7											
1047	5.2.3.1	Inspection for marking & cutting	1 day	5/6/2025	5/6/2025	1404/2/16	0.05											
1048	5.2.3.2	Inspection for rolling & forming	1 day	6/11/2025	6/11/2025	1404/3/21	0.05											
1049	5.2.3.3	Inspection for weld preparation and fit up (shell , nozzle , ...)	1 day	8/24/2025	8/24/2025	1404/6/2	0.05											
1050	5.2.3.4	Inspection for welding	1 day	6/24/2025	6/24/2025	1404/4/3	0.05											
1051	5.2.3.5	Inspection for NDT (VT, MT, PT, UT, RT)	1 day	9/21/2025	9/21/2025	1404/6/30	0.05											
1052	5.2.3.6	Inspection for final visual and dimensional	1 day	9/16/2025	9/16/2025	1404/6/25	0.05											
1053	5.2.3.7	Inspection for PWHT	1 day	9/20/2025	9/20/2025	1404/6/29	0.05											
1054	5.2.3.8	Inspection for hardness check	1 day	9/21/2025	9/21/2025	1404/6/30	0.05											
1055	5.2.3.9	Inspection for pneumatic test (pad test)	1 day	9/7/2025	9/7/2025	1404/6/16	0.05											
1056	5.2.3.10	Inspection for hydrostatic test water quality	1 day	9/22/2025	9/22/2025	1404/6/31	0.05											
1057	5.2.3.11	Inspection for hydrostatic test	1 day	9/24/2025	9/24/2025	1404/7/2	0.05											
1058	5.2.3.12	Inspection for draining & drying	1 day	9/25/2025	9/25/2025	1404/7/3	0.05											
1059	5.2.3.13	Inspection for abrasive & paint material	1 day	9/27/2025	9/27/2025	1404/7/5	0.05											
1060	5.2.3.14	Inspection for blasting & painting (each layer DFT)	1 day	10/1/2025	10/1/2025	1404/7/9	0.05											
1061	5.2.4	L&P	1 day	11/12/2025	11/12/2025	1404/8/21	0.75											
1062	5.2.4.1	Inspection for visual and dimensional check after welding	1 day	11/12/2025	11/12/2025	1404/8/21	0.75											
1063	5.2.5	Painting Of Package Assembly (Piping, Structure)	5 days	11/12/2025	11/17/2025	1404/8/26	0.3											
1064	5.2.5.1	Inspection for abrasive & paint material	1 day	11/12/2025	11/12/2025	1404/8/21	0.15											
1065	5.2.5.2	Inspection for blasting & painting (each layer DFT)	1 day	11/17/2025	11/17/2025	1404/8/26	0.15											
1066	5.2.6	Pickling (For Stainless Steel Part)	1 day	9/11/2025	9/11/2025	1404/6/20	0.75											
1067	5.2.6.1	Inspection for pickling and passivation	1 day	9/11/2025	9/11/2025	1404/6/20	0.75											
1068	6	Final Inspection & Releases note	33 days	10/13/2025	11/19/2025	1404/8/28	30											
1069	6.1	C-100 Glycol Contactor	2 days	10/28/2025	10/29/2025	1404/8/7	4.35											
1070	6.1.1	Final Inspection & Releases note	2 days	10/28/2025	10/29/2025	1404/8/7	4.35											
1071	6.2	C-200 Still Column	2 days	10/13/2025	10/14/2025	1404/7/22	2.46											
1072	6.2.1	Final Inspection & Releases note	2 days	10/13/2025	10/14/2025	1404/7/22	2.46											
1073	6.3	Lean Glycol Filter (F-300)	2 days	10/13/2025	10/14/2025	1404/7/22	1.56											
1074	6.3.1	Final Inspection & Releases note	2 days	10/13/2025	10/14/2025	1404/7/22	1.56											
1075	6.4	V-120 Glycol Flash Drum	2 days	10/13/2025	10/14/2025	1404/7/22	3.39											
1076	6.4.1	Final Inspection & Releases note	2 days	10/13/2025	10/14/2025	1404/7/22	3.39											





TIME SCHEDULE OF BINAK OILFIELD DEVELOPMENT
REV.01



ID	WBS	Task Name	Duration	Start	Finish	پایان	W.F.	2023	H1	H2	2024	H1	H2	2025	H1	H2	2026	H1
1077	6.5	F-100A Particle Glycol Filter	2 days	10/13/2025	10/14/2025	1404/7/22	1.17											
1078	6.5.1	Final Inspection & Releases note	2 days	10/13/2025	10/14/2025	1404/7/22	1.17											
1079	6.6	F-100B Particle Glycol Filter	2 days	10/13/2025	10/14/2025	1404/7/22	1.17											
1080	6.6.1	Final Inspection & Releases note	2 days	10/13/2025	10/14/2025	1404/7/22	1.17											
1081	6.7	F-200 Carbon Glycol Filter	2 days	10/13/2025	10/14/2025	1404/7/22	1.38											
1082	6.7.1	Final Inspection & Releases note	2 days	10/13/2025	10/14/2025	1404/7/22	1.38											
1083	6.8	E-100 Glycol reflux condenser COIL TYPE	2 days	10/13/2025	10/14/2025	1404/7/22	2.07											
1084	6.8.1	Final Inspection & Releases note	2 days	10/13/2025	10/14/2025	1404/7/22	2.07											
1085	6.9	E -200 Rich-Lean HE	2 days	10/13/2025	10/14/2025	1404/7/22	1.89											
1086	6.9.1	Final Inspection & Releases note	2 days	10/13/2025	10/14/2025	1404/7/22	1.89											
1087	6.10	E -300 LEAN TEG - DRY GAS EXCH	2 days	10/14/2025	10/15/2025	1404/7/23	2.13											
1088	6.10.1	Final Inspection & Releases note	2 days	10/14/2025	10/15/2025	1404/7/23	2.13											
1089	6.11	V-130 Surge Tank	2 days	10/13/2025	10/14/2025	1404/7/22	2.73											
1090	6.11.1	Final Inspection & Releases note	2 days	10/13/2025	10/14/2025	1404/7/22	2.73											
1091	6.12	R-100 Reboiler	2 days	10/13/2025	10/14/2025	1404/7/22	3.66											
1092	6.12.1	Final Inspection & Releases note	2 days	10/13/2025	10/14/2025	1404/7/22	3.66											
1093	6.13	Skid of Gas Dehydration	2 days	11/18/2025	11/19/2025	1404/8/28	0.84											
1094	6.13.1	Final Inspection & Releases note	2 days	11/18/2025	11/19/2025	1404/8/28	0.84											
1095	6.14	Piping of Gas Dehydration	2 days	11/18/2025	11/19/2025	1404/8/28	1.2											
1096	6.14.1	Final Inspection & Releases note	2 days	11/18/2025	11/19/2025	1404/8/28	1.2											
1097	7	Ready for Shipment	33 days	10/15/2025	11/22/2025	1404/9/1	30											
1098	7.1	C-100 Glycol Contactor	2 days	10/30/2025	11/1/2025	1404/8/10	4.35											
1099	7.1.1	Preparing and shipment	2 days	10/30/2025	11/1/2025	1404/8/10	4.35											
1100	7.2	C-200 Still Column	2 days	10/15/2025	10/16/2025	1404/7/24	2.46											
1101	7.2.1	Preparing and shipment	2 days	10/15/2025	10/16/2025	1404/7/24	2.46											
1102	7.3	Lean Glycol Filter (F-300)	2 days	10/15/2025	10/16/2025	1404/7/24	1.56											
1103	7.3.1	Preparing and shipment	2 days	10/15/2025	10/16/2025	1404/7/24	1.56											
1104	7.4	V-120 Glycol Flash Drum	2 days	10/15/2025	10/16/2025	1404/7/24	3.39											
1105	7.4.1	Preparing and shipment	2 days	10/15/2025	10/16/2025	1404/7/24	3.39											
1106	7.5	F-100A Particle Glycol Filter	2 days	10/15/2025	10/16/2025	1404/7/24	1.17											
1107	7.5.1	Preparing and shipment	2 days	10/15/2025	10/16/2025	1404/7/24	1.17											
1108	7.6	F-100B Particle Glycol Filter	2 days	10/15/2025	10/16/2025	1404/7/24	1.17											
1109	7.6.1	Preparing and shipment	2 days	10/15/2025	10/16/2025	1404/7/24	1.17											
1110	7.7	F-200 Carbon Glycol Filter	2 days	10/15/2025	10/16/2025	1404/7/24	1.38											
1111	7.7.1	Preparing and shipment	2 days	10/15/2025	10/16/2025	1404/7/24	1.38											
1112	7.8	E-100 Glycol reflux condenser COIL TYPE	2 days	10/15/2025	10/16/2025	1404/7/24	2.07											
1113	7.8.1	Preparing and shipment	2 days	10/15/2025	10/16/2025	1404/7/24	2.07											
1114	7.9	E -200 Rich-Lean HE	2 days	10/15/2025	10/16/2025	1404/7/24	1.89											
1115	7.9.1	Preparing and shipment	2 days	10/15/2025	10/16/2025	1404/7/24	1.89											
1116	7.10	E -300 LEAN TEG - DRY GAS EXCH	2 days	10/16/2025	10/18/2025	1404/7/26	2.13											
1117	7.10.1	Preparing and shipment	2 days	10/16/2025	10/18/2025	1404/7/26	2.13											
1118	7.11	V-130 Surge Tank	2 days	10/15/2025	10/16/2025	1404/7/24	2.73											
1119	7.11.1	Preparing and shipment	2 days	10/15/2025	10/16/2025	1404/7/24	2.73											
1120	7.12	R-100 Reboiler	2 days	10/15/2025	10/16/2025	1404/7/24	3.66											
1121	7.12.1	Preparing and shipment	2 days	10/15/2025	10/16/2025	1404/7/24	3.66											
1122	7.13	Skid of Gas Dehydration	2 days	11/20/2025	11/22/2025	1404/9/1	0.84											
1123	7.13.1	Preparing and shipment	2 days	11/20/2025	11/22/2025	1404/9/1	0.84											
1124	7.14	Piping of Gas Dehydration	1 day	11/20/2025	11/20/2025	1404/8/29	1.2											
1125	7.14.1	Preparing and shipment	1 day	11/20/2025	11/20/2025	1404/8/29	1.2											
1126	8	Final data book	539 days?	1/29/2024	11/22/2025	1404/9/1	30											
1127	8.1	Final data book	4 days	11/18/2025	11/22/2025	1404/9/1	30											
1128	8.2		1 day?	1/29/2024	1/29/2024	1402/11/9	0											
