طرح نگهداشت و افزایش تولید ۲۷ مخزن

DETAILED SCHEDULE & UPDATING

نگهداشت و افزایش تولید میدان نفتی بینک

G04	JUN. 2022	AFD	P.Ghadamian	M.Fakharian	M.Mehrshad	
G03	MAY. 2022	AFD	P.Ghadamian	M.Fakharian	M.Mehrshad	
G02	APR. 2022	IFA	P.Ghadamian	M.Fakharian	M.Mehrshad	
G01	MAR. 2022	IFA	P.Ghadamian	M.Fakharian	M.Mehrshad	
G00	FEB. 2022	IFC	P.Ghadamian	M.Fakharian	M.Mehrshad	
Rev.	**Date**	**Purpose of Issue/Status**	**Prepared by:**	**Checked by:**	**Approved by:**	**CLIENT Approval**

Class:2 | **CLIENT Doc. Number: F0Z-707039**

Status:

IDC: Inter-Discipline Check
IFC: Issued For Comment
IFA: Issued For Approval
AFD: Approved For Design
AFC: Approved For Construction
AFP: Approved For Purchase
AFQ: Approved For Quotation
IFI: Issued For Information
AB-R: As-Built for CLIENT Review
AB-A: As-Built –Approved

REVISION RECORG SHEET

PAGE	G00	G01	G02	G03	G04
1	X	X	X	X	X
2	X	X	X	X	X
3	X	X	X		X
4	X	X	X		X
5	X	X	X		X
6	X	X	X		X
7	X	X	X		X
8	X	X	X		X
9	X	X	X		X
10	X	X	X		X
11	X	X	X		X
12	X	X	X		X
13	X	X	X		X
14	X	X	X		X
15	X	X	X		X
16	X	X	X		X
17	X	X	X		X
18	X	X	X		X
19	X	X	X		X
20	X	X	X		X
21	X	X	X		X
22	X	X	X		X
23	X	X	X		X
24	X	X	X		X
25	X	X	X		X
26	X	X	X		X
27	X	X	X		X
28	X	X	X		X
29	X	X	X		X
30	X	X	X		X
31	X	X	X		X
32	X	X	X		X
33	X	X	X		X
34	X	X	X		X
35	X	X	X		X
36	X	X	X		X
37	X	X	X		X
38	X	X	X		X
39	X	X	X		X
40	X	X	X		X
41	X	X	X		X
42	X	X	X		X
43	X	X	X		X
44	X	X	X		X
45	X	X	X		X
46	X	X	X		X
47	X	X	X		X
48	X	X	X		X
49	X	X	X		X
50	X	X	X		X
51	X	X	X		X
52	X	X	X		X
53	X	X	X		X
54	X	X	X		X
55	X	X	X		X
56	X	X	X		X
57	X	X	X		X
58	X	X	X		X
59	X	X	X		X
60	X	X	X		X
61	X	X	X		X
62	X	X	X		X
63	X	X	X		X
64	X	X	X		X
65	X	X	X		X

PAGE	G00	G01	G02	G03	G04
66	X	X	X		X
67	X	X	X		X
68	X	X	X		X
69	X	X	X		X
70	X	X	X		X
71	X	X	X		X
72	X	X	X		X
73	X	X	X		X
74	X	X	X		X
75	X	X	X		X
76	X	X	X		X
77	X	X	X		X
78	X	X	X		X
79	X	X	X		X
80	X	X	X		X
81	X	X	X		X
82	X	X	X		X
83	X	X	X		X
84	X	X	X		X
85	X	X	X		X
86	X	X	X		X
87	X	X	X		X
88	X	X	X		X
89	X	X	X		X
90	X	X	X		X
91	X	X	X		X
92	X	X	X		X
93	X	X	X		X
94	X	X	X		X
95	X	X	X		X
96	X	X	X		X
97	X	X	X		X
98	X	X	X		X
99	X	X	X		X
100	X	X	X		X
101	X	X	X		X
102	X	X	X		X
103	X	X	X		X
104	X	X	X		X
105	X	X	X		X
106	X	X	X		X
107	X	X	X		X
108	X	X	X		X
109	X	X	X		X
110	X	X	X		X
111	X	X	X		X
112	X	X	X		X
113	X	X	X		X
114	X	X	X		X
115	X	X	X		X
116	X	X	X		X
117	X	X	X		X
118	X	X	X		X
119	X	X	X		X
120	X	X	X		X
121	X	X	X		X
...	X	X	X		X
279	X	X	X		X
280	X	X	X		X
...	X	X	X		
371	X	X	X		
372		X	X		
...		X	X		
405		X	X		
406		X			

فهرست مطالب

۱- مقدمه ٤

۱- مقدمه

میدان نفتی بینک در استان بوشهر در فاصله ۲۰ کیلومتری شمال غربی شهرستان گناوه، واقع شده است. شرکت ملی مناطق نفتخیز جنوب به عنوان کارفرمای اصلی، پروژه نگهداشت و افزایش تولید میدان نفتی بینک (بسته بینک) را در قالب پیمان EPG-EPC به شرکت توسعه پترو ایران محول نموده است. شرکت توسعه پترو ایران نیز (به عنوان پیمانکار عمومی پروژه/ General Contractor) بخش سطح الارض و ابنیه تحت الارض این بسته را به صورت EPC به مشارکت "هیرگان انرژی- طرح و بازرسی" واگذار کرده است.

تعاریف


کارفرمای اصلی:	شرکت ملی نفت خیز جنوب
پروژه:	نگهداشت و افزایش تولید میدان نفتی بینک / سطح الارض و ابنیه تحت الارض
پیمانکار EPG/EPC (GC):	شرکت پترو ایران
پیمانکار EPC:	مشارکت "هیرگان انرژی- طرح و بازرسی"

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
BINAK-Baseline (EPC)-Actual		1096	2.53%	$35,909,880.00	23-Jun-21 A	22-Jun-24
Milestone		1096	0%	$0.00	23-Jun-21 A	22-Jun-24
General		1096	0%	$0.00	23-Jun-21 A	22-Jun-24
BK-MI-GN	Project Start	0	0%	$0.00		23-Jun-21 A
BK-MI-GN	Contract Effectiveness with PEDCO	0	0%	$0.00		20-Mar-22
BK-MI-GN	Completion of Engineering	0	0%	$0.00		30-Jan-24
BK-MI-GN	Completion of Project Common Documents	0	0%	$0.00		25-Oct-22
BK-MI-GN	Detail Design Completion-Project Common Doc (Eng & QA/Q	0	0%	$0.00		30-Jan-24
BK-MI-GN	Detail Design Completion-Subsurface Common Docs	0	0%	$0.00		25-Dec-22
BK-MI-GN	Completion of Construction & Erection	0	0%	$0.00		23-Mar-24
BK-MI-GN	Completion of Procurement	0	0%	$0.00		04-Mar-24
BK-MI-GN	Project Finish	0	0%	$0.00		22-Jun-24
Work Packages Delivery		437	0%	$0.00	13-Apr-23	22-Jun-24
BK-MI-WF	Hand Over of Package 01-New Well # W018S	0	0%	$0.00		13-Apr-23
BK-MI-WF	Handover of Package 02-New Well # W028 (Bangestan)	0	0%	$0.00		08-May-23
BK-MI-WF	Handover of Package 03-New Well # W046S (Bangestan)	0	0%	$0.00		29-Jun-23
BK-MI-WF	Handover of Package 04-New Well # W035 (Bangestan)	0	0%	$0.00		03-Nov-23
BK-MI-WF	Handover of Package 05-New Well # W008N	0	0%	$0.00		10-Feb-24
BK-MI-WF	Handover of Package 06-New Well # W007S/Manifold Exter	0	0%	$0.00		17-Mar-24
BK-MI-WF	Handover of Package 07-Workover # 14	0	0%	$0.00		02-Sep-23
BK-MI-WF	Handover of Package 08-Workover # 12	0	0%	$0.00		14-Aug-23
BK-MI-WF	Handover of Package 09-Workover # 15	0	0%	$0.00		31-Jul-23
BK-MI-WF	Handover of Package 10-Workover # 05	0	0%	$0.00		22-Sep-23
BK-MI-WF	Handover of Package 11- EPC Pipeline 8" & 4"	0	0%	$0.00		18-Jan-24
BK-MI-WF	Handover of Package 12- EPC # Compressor Station	0	0%	$0.00		22-Jun-24
Subsurface Development		641	0%	$0.00	05-Mar-22	20-Dec-23
Interface With PEDCO		509	0%	$0.00	05-Mar-22	19-Nov-23
Wellpad Handover		312	0%	$0.00	05-Mar-22	06-May-23
BK-MI-W	Wellpad Handover To Sub-Surface Contractor W018S	0	0%	$0.00		05-Mar-22 A
BK-MI-W	Wellpad Handover To Sub-Surface Contractor W028B (Ban	0	0%	$0.00		28-Jun-22
BK-MI-W	Wellpad Handover To Sub-Surface Contractor W046S (Ban	0	0%	$0.00		10-Aug-22
BK-MI-W	Wellpad Handover To Sub-Surface Contractor W035B (Ban	0	0%	$0.00		07-Dec-22
BK-MI-W	Wellpad Handover To Sub-Surface Contractor W008N	0	0%	$0.00		05-May-23
BK-MI-W	Wellpad Handover To Sub-Surface Contractor W007S	0	0%	$0.00		06-May-23
BK-MI-W	Wellpad Handover To Sub-Surface Contractor Well # 14	0	0%	$0.00		22-Aug-22
BK-MI-W	Wellpad Handover To Sub-Surface Contractor Well # 12	0	0%	$0.00		01-Oct-22
BK-MI-W	Wellpad Handover To Sub-Surface Contractor Well # 15	0	0%	$0.00		21-Nov-22
BK-MI-W	Wellpad Handover To Sub-Surface Contractor Well # 05	0	0%	$0.00		21-Jan-23
Finish Drilling of Wells		394	0%	$0.00	21-Oct-22	19-Nov-23
BK-MI-D	Finish Drilling W018S	0	0%	$0.00		07-Dec-22
BK-MI-D	Finish Drilling W028B (Bangestan)	0	0%	$0.00		10-Dec-22
BK-MI-D	Finish Drilling W046S (Bangestan)	0	0%	$0.00		18-Apr-23
BK-MI-D	Finish Drilling W035B (Bangestan)	0	0%	$0.00		01-Jul-23
BK-MI-D	Finish Drilling W008N	0	0%	$0.00		19-Sep-23
BK-MI-D	Finish Drilling W007S	0	0%	$0.00		19-Nov-23
BK-MI-D	Finish Drilling Well # 14	0	0%	$0.00		21-Oct-22
BK-MI-D	Finish Drilling Well # 12	0	0%	$0.00		30-Nov-22
BK-MI-D	Finish Drilling Well # 15	0	0%	$0.00		20-Jan-23



© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
BK-MI-[	Finish Drilling Well # 05	0	0%	$0.00		22-Mar-23
Package 01-New Well # W018S		352	0%	$0.00	03-Apr-22	21-Mar-23
BK-MI-01	PMR of Piping Material	0	0%	$0.00		26-Sep-22
BK-MI-01	PMR of Line Pipe	0	0%	$0.00		03-Apr-22
Engineering		161	0%	$0.00	05-Aug-22	13-Jan-23
BK-MI-[	PDMS Model Review Report (60%) - W018S	0	0%	$0.00		05-Aug-22
BK-MI-[	PDMS Model Review Report (90%) - W018S	0	0%	$0.00		19-Sep-22
BK-MI-[	Detail Design Completion for W018S	0	0%	$0.00		13-Jan-23
Procurement		322	0%	$0.00	03-May-22	21-Mar-23
BK-MI-[	Procurement Completion-# W018S	0	0%	$0.00		21-Mar-23
BK-MI-[	PO. of Piping Material	0	0%	$0.00		31-Oct-22
BK-MI-[	PO. of Line Pipe	0	0%	$0.00		07-May-22
BK-MI-[	PO. Of WHCP	0	0%	$0.00		03-May-22
BK-MI-[	Forwarding to Job Site-Piping Material	0	0%	$0.00		03-Jan-23
BK-MI-[	Forwarding to Job Site-Line Pipe	0	0%	$0.00		30-Jul-22
BK-MI-[	Forwarding to Job Site-WHCP	0	0%	$0.00		14-Aug-22
Construction		4	0%	$0.00	13-Jan-23	17-Jan-23
BK-MI-[	Finish Wellhead Facilities-# W018S	0	0%	$0.00		13-Jan-23
BK-MI-[	Finish Flowline-# W018S	0	0%	$0.00		17-Jan-23
BK-MI-[	Construction Completion-# W018S	0	0%	$0.00		17-Jan-23
Package 02-New Well # W028 (Bangestan)		361	0%	$0.00	20-Mar-22	15-Mar-23
BK-MI-02	PMR of Piping Material	0	0%	$0.00		13-Aug-22
BK-MI-02	PMR of Line Pipe	0	0%	$0.00		20-Mar-22
Engineering		197	0%	$0.00	07-Jul-22	20-Jan-23
BK-MI-[	PDMS Model Review Report (60%) - W028	0	0%	$0.00		07-Jul-22
BK-MI-[	PDMS Model Review Report (90%) - W028	0	0%	$0.00		06-Aug-22
BK-MI-[	Detail Design Completion for W028 (Bangestan)	0	0%	$0.00		20-Jan-23
Procurement		349	0%	$0.00	31-Mar-22	15-Mar-23
BK-MI-[	Procurement Completion-# W028	0	0%	$0.00		15-Mar-23
BK-MI-[	PO. of Piping Material	0	0%	$0.00		23-Sep-22
BK-MI-[	PO. of Line Pipe	0	0%	$0.00		31-Mar-22
BK-MI-[	PO. Of WHCP	0	0%	$0.00		03-May-22
BK-MI-[	Forwarding to Job Site-Piping Material	0	0%	$0.00		11-Dec-22
BK-MI-[	Forwarding to Job Site-Line Pipe	0	0%	$0.00		02-Aug-22
BK-MI-[	Forwarding to Job Site-WHCP	0	0%	$0.00		18-Aug-22
Construction		118	0%	$0.00	11-Oct-22	05-Feb-23
BK-MI-[	Finish Wellhead Facilities-# W028	0	0%	$0.00		05-Feb-23
BK-MI-[	Finish Flowline-# W028	0	0%	$0.00		11-Oct-22
BK-MI-[	Construction Completion-# W028	0	0%	$0.00		05-Feb-23
Package 03-New Well # W046S (Bangestan)		374	0%	$0.00	22-May-22	31-May-23
BK-MI-03	PMR of Piping Material	0	0%	$0.00		09-Oct-22
BK-MI-03	PMR of Line Pipe	0	0%	$0.00		24-Jun-22
BK-MI-03	PMR of Transformers	0	0%	$0.00		27-May-22
BK-MI-03	PMR of LV Swichgear & MCC	0	0%	$0.00		22-May-22
BK-MI-03	PMR of UPS System	0	0%	$0.00		20-Aug-22
BK-MI-03	PMR of DC Charger	0	0%	$0.00		01-Jun-22
Engineering		288	0%	$0.00	09-Aug-22	24-May-23
BK-MI-[	PDMS Model Review Report (60%) - W046S	0	0%	$0.00		09-Aug-22
BK-MI-[	PDMS Model Review Report (90%) - W046S	0	0%	$0.00		22-Sep-22

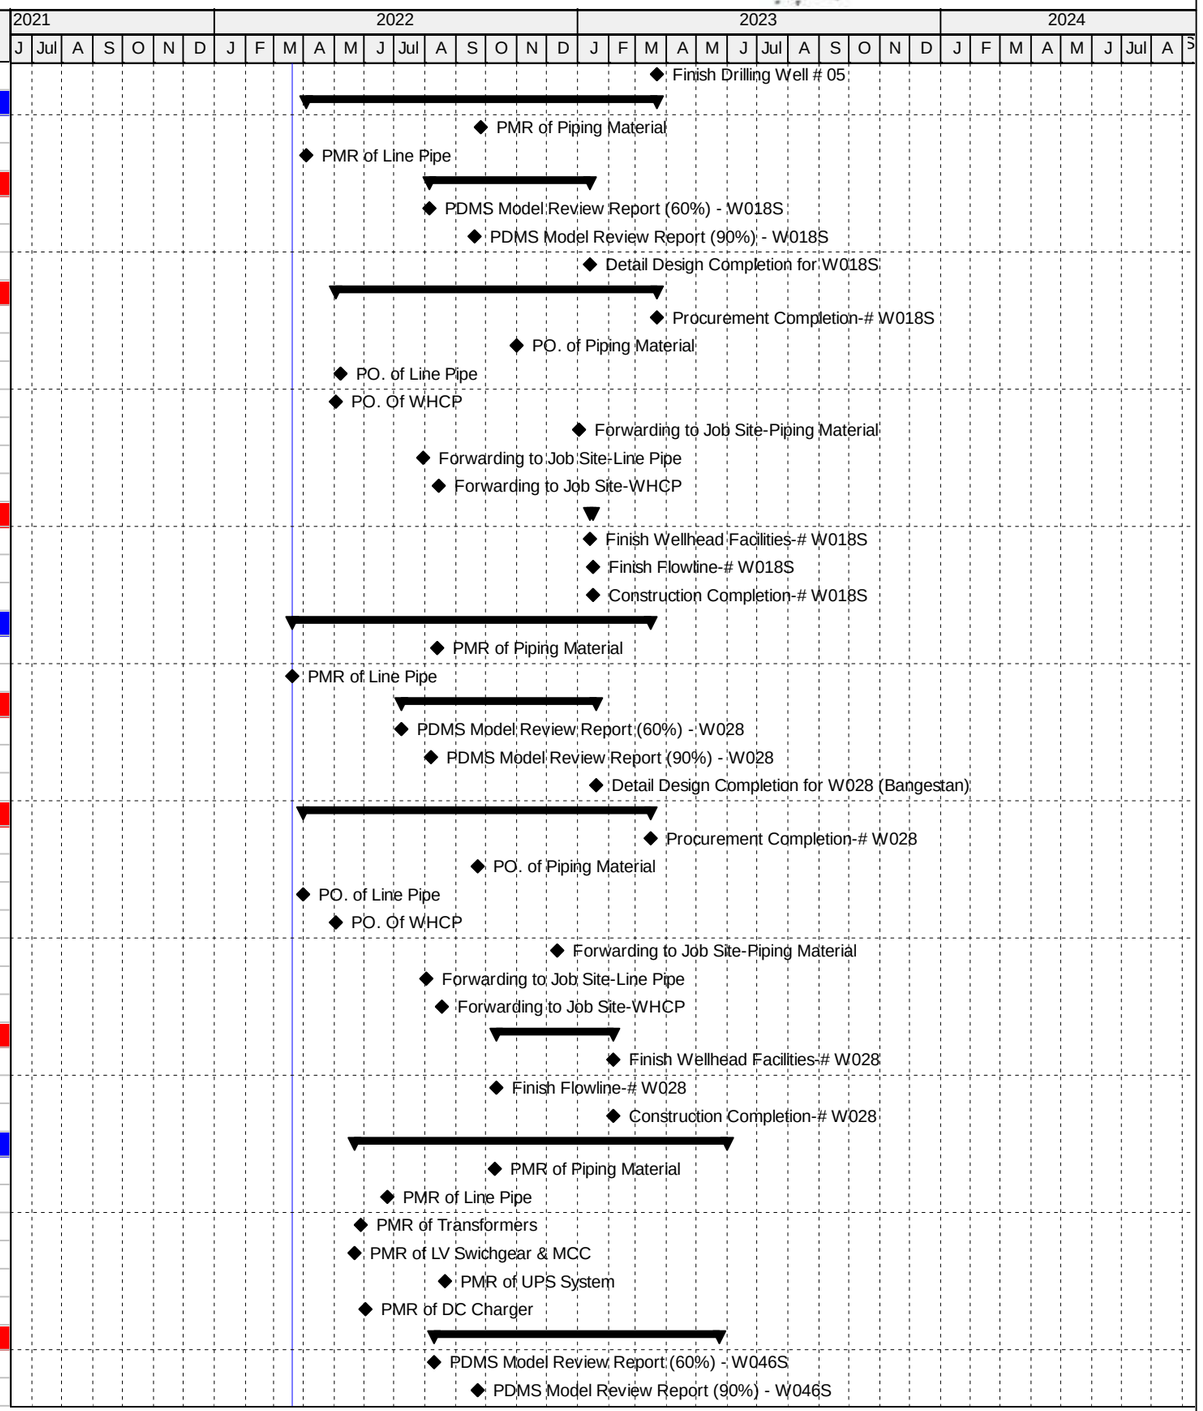


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
BK-MI-0	Detail Design Completion for W046S (Bangestan)	0	0%	$0.00		24-May-23
Procurement		308	0%	$0.00	30-Jun-22	04-May-23
BK-MI-0	Procurement Completion-# W046S	0	0%	$0.00		04-May-23
BK-MI-0	PO. of Piping Material	0	0%	$0.00		27-Nov-22
BK-MI-0	PO. of Line Pipe	0	0%	$0.00		06-Jul-22
BK-MI-0	PO. Of Transformers	0	0%	$0.00		08-Jul-22
BK-MI-0	PO. Of LV Swichgear & MCC	0	0%	$0.00		30-Jun-22
BK-MI-0	PO. of UPS System	0	0%	$0.00		08-Oct-22
BK-MI-0	PO. of DC Charger	0	0%	$0.00		10-Jul-22
BK-MI-0	Forwarding to Job Site-UPS	0	0%	$0.00		09-Feb-23
BK-MI-0	Forwarding to Job Site-DC Charger	0	0%	$0.00		11-Dec-22
BK-MI-0	Forwarding to Job Site-Transformer	0	0%	$0.00		09-Nov-22
BK-MI-0	Forwarding to Job Site-Swichgear	0	0%	$0.00		01-Nov-22
BK-MI-0	Forwarding to Job Site-Piping Material	0	0%	$0.00		31-Mar-23
BK-MI-0	Forwarding to Job Site-Line Pipe	0	0%	$0.00		18-Oct-22
Construction		119	0%	$0.00	01-Feb-23	31-May-23
BK-MI-0	Finish Wellhead Facilities-# W046S	0	0%	$0.00		31-May-23
BK-MI-0	Finish Flowline-# W046S	0	0%	$0.00		01-Feb-23
BK-MI-0	Construction Completion-# W046S	0	0%	$0.00		31-May-23
Package 04-New Well # W035 (Bangestan)		434	0%	$0.00	28-May-22	05-Aug-23
BK-MI-04	PMR of Piping Material	0	0%	$0.00		04-Oct-22
BK-MI-04	PMR of Line Pipe	0	0%	$0.00		28-May-22
Engineering		287	0%	$0.00	04-Aug-22	18-May-23
BK-MI-0	PDMS Model Review Report (60%) - W035	0	0%	$0.00		04-Aug-22
BK-MI-0	PDMS Model Review Report (90%) - W035	0	0%	$0.00		17-Sep-22
BK-MI-0	Detail Design Completion for W035 (Bangestan)	0	0%	$0.00		18-May-23
Procurement		335	0%	$0.00	12-Jun-22	13-May-23
BK-MI-0	Procurement Completion-# W035	0	0%	$0.00		13-May-23
BK-MI-0	PO. of Piping Material	0	0%	$0.00		15-Nov-22
BK-MI-0	PO. of Line Pipe	0	0%	$0.00		12-Jun-22
BK-MI-0	PO. Of WHCP	0	0%	$0.00		22-Jun-22
BK-MI-0	Forwarding to Job Site-Piping Material	0	0%	$0.00		08-May-23
BK-MI-0	Forwarding to Job Site-Line Pipe	0	0%	$0.00		23-Nov-22
BK-MI-0	Forwarding to Job Site-WHCP	0	0%	$0.00		28-Nov-22
Construction		96	0%	$0.00	02-May-23	05-Aug-23
BK-MI-0	Finish Wellhead Facilities-# W035	0	0%	$0.00		05-Aug-23
BK-MI-0	Finish Flowline-# W035	0	0%	$0.00		02-May-23
BK-MI-0	Construction Completion-# W035	0	0%	$0.00		05-Aug-23
Package 05-New Well # W008N		550	0%	$0.00	13-May-22	14-Nov-23
BK-MI-05	PMR of Piping Material	0	0%	$0.00		17-Nov-22
BK-MI-05	PMR of Line Pipe	0	0%	$0.00		13-May-22
Engineering		142	0%	$0.00	04-Aug-22	24-Dec-22
BK-MI-0	PDMS Model Review Report (60%) - W008N	0	0%	$0.00		04-Aug-22
BK-MI-0	PDMS Model Review Report (90%) - W008N	0	0%	$0.00		31-Oct-22
BK-MI-0	Detail Design Completion for W008N	0	0%	$0.00		24-Dec-22
Procurement		469	0%	$0.00	22-Jun-22	04-Oct-23
BK-MI-0	Procurement Completion-# W008N	0	0%	$0.00		04-Oct-23
BK-MI-0	PO. of Piping Material	0	0%	$0.00		18-Jan-23
BK-MI-0	PO. of Line Pipe	0	0%	$0.00		24-Jun-22

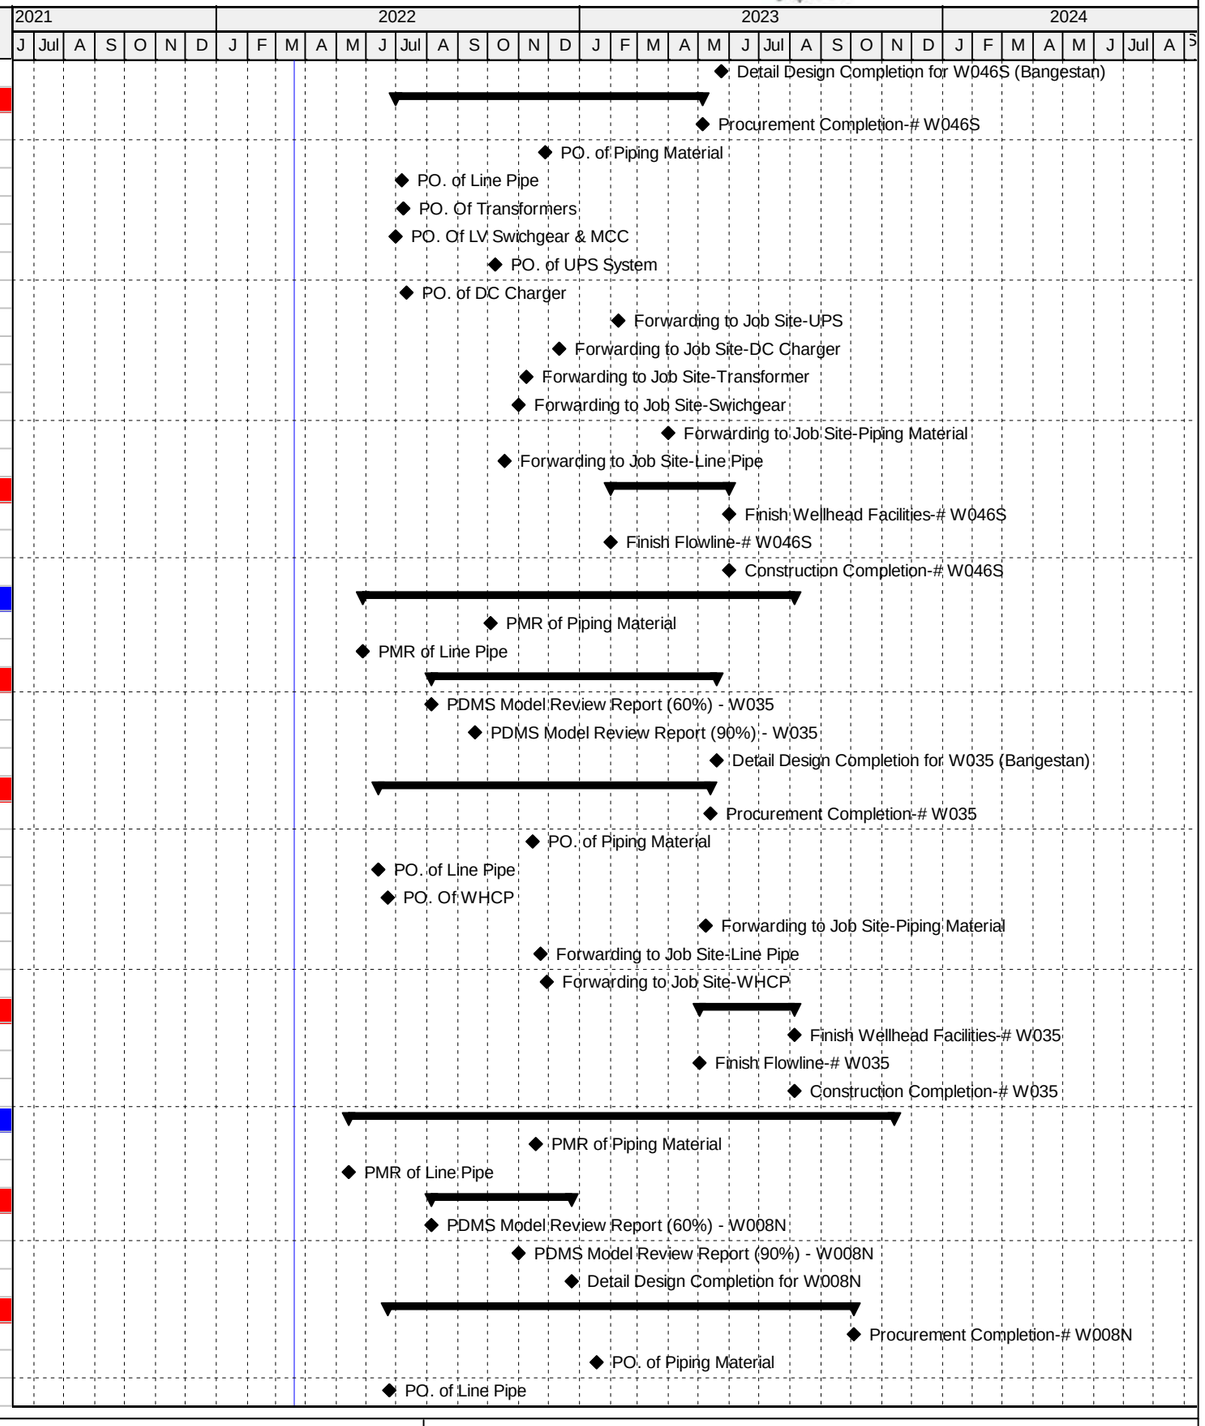


Actual Level of Effort | Remaining Work | Milestone

Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
BK-MI-0	PO. Of WHCP	0	0%	$0.00		22-Jun-22
BK-MI-0	Forwarding to Job Site-Piping Material	0	0%	$0.00		24-Sep-23
BK-MI-0	Forwarding to Job Site-Line Pipe	0	0%	$0.00		08-Feb-23
BK-MI-0	Forwarding to Job Site-WHCP	0	0%	$0.00		07-Jan-23
Construction		64	0%	$0.00	12-Sep-23	14-Nov-23
BK-MI-0	Finish Wellhead Facilities-# W008N	0	0%	$0.00		14-Nov-23
BK-MI-0	Finish Flowline-# W008N	0	0%	$0.00		12-Sep-23
BK-MI-0	Construction Completion-# W008N	0	0%	$0.00		14-Nov-23
Package 06-New Well # W007S/Manifold Extension (Bangestan)		587	0%	$0.00	12-May-22	20-Dec-23
BK-MI-0	PMR of DC Charger	0	0%	$0.00		18-May-22
BK-MI-0	PMR of UPS System	0	0%	$0.00		20-Aug-22
BK-MI-0	PMR of LV Swichgear & MCC	0	0%	$0.00		18-May-22
BK-MI-0	PMR of Transformers	0	0%	$0.00		27-May-22
BK-MI-0	PMR of Line Pipe	0	0%	$0.00		12-May-22
BK-MI-0	PMR of Piping Material	0	0%	$0.00		24-Oct-22
Engineering		491	0%	$0.00	01-Aug-22	05-Dec-23
BK-MI-0	Detail Design Completion for W007S/Manifold Extension (Bar	0	0%	$0.00		05-Dec-23
BK-MI-0	PDMS Model Review Report (90%) - Manifold Extension	0	0%	$0.00		10-Oct-22
BK-MI-0	PDMS Model Review Report (60%) - Manifold Extension	0	0%	$0.00		31-Aug-22
BK-MI-0	PDMS Model Review Report (90%) - W007S	0	0%	$0.00		10-Sep-22
BK-MI-0	PDMS Model Review Report (60%) - W007S	0	0%	$0.00		01-Aug-22
Procurement		398	0%	$0.00	23-Jun-22	26-Jul-23
BK-MI-0	Procurement Completion-# W007S	0	0%	$0.00		26-Jul-23
BK-MI-0	Procurement Completion-# Manifold Extension	0	0%	$0.00		28-Mar-23
BK-MI-0	PO. of UPS System	0	0%	$0.00		05-Dec-22
BK-MI-0	PO. Of Transformers	0	0%	$0.00		12-Aug-22
BK-MI-0	PO. of Piping Material	0	0%	$0.00		09-Dec-22
BK-MI-0	PO. Of LV Swichgear & MCC	0	0%	$0.00		03-Aug-22
BK-MI-0	PO. of Line Pipe	0	0%	$0.00		23-Jun-22
BK-MI-0	PO. of DC Charger	0	0%	$0.00		29-Jun-22
BK-MI-0	Forwarding to Job Site-UPS	0	0%	$0.00		22-Jun-23
BK-MI-0	Forwarding to Job Site-Transformer	0	0%	$0.00		29-Mar-23
BK-MI-0	Forwarding to Job Site-Swichgear	0	0%	$0.00		19-Jan-23
BK-MI-0	Forwarding to Job Site-Piping Material	0	0%	$0.00		26-Jul-23
BK-MI-0	Forwarding to Job Site-Line Pipe	0	0%	$0.00		08-Jan-23
BK-MI-0	Forwarding to Job Site-DC Charger	0	0%	$0.00		14-Jan-23
Construction		211	0%	$0.00	23-May-23	20-Dec-23
BK-MI-0	Construction Completion-# Manifold Extension	0	0%	$0.00		23-May-23
BK-MI-0	Construction Completion-# W007S	0	0%	$0.00		20-Dec-23
BK-MI-0	Finish Flowline-# W007S	0	0%	$0.00		31-Oct-23
BK-MI-0	Finish Wellhead Facilities-# W007S	0	0%	$0.00		20-Dec-23
Package 07-Workover # 14		408	0%	$0.00	25-Apr-22	07-Jun-23
BK-MI-07	PMR of DC Charger	0	0%	$0.00		30-Apr-22
BK-MI-07	PMR of LV Swichgear & MCC	0	0%	$0.00		25-Apr-22
BK-MI-07	PMR of Transformers	0	0%	$0.00		25-Apr-22
BK-MI-07	PMR of UPS System	0	0%	$0.00		19-Jul-22
Engineering		0	0%	$0.00	08-May-23	08-May-23
BK-MI-0	Detail Design Completion for W#14	0	0%	$0.00		08-May-23
Procurement		144	0%	$0.00	04-Jun-22	26-Oct-22

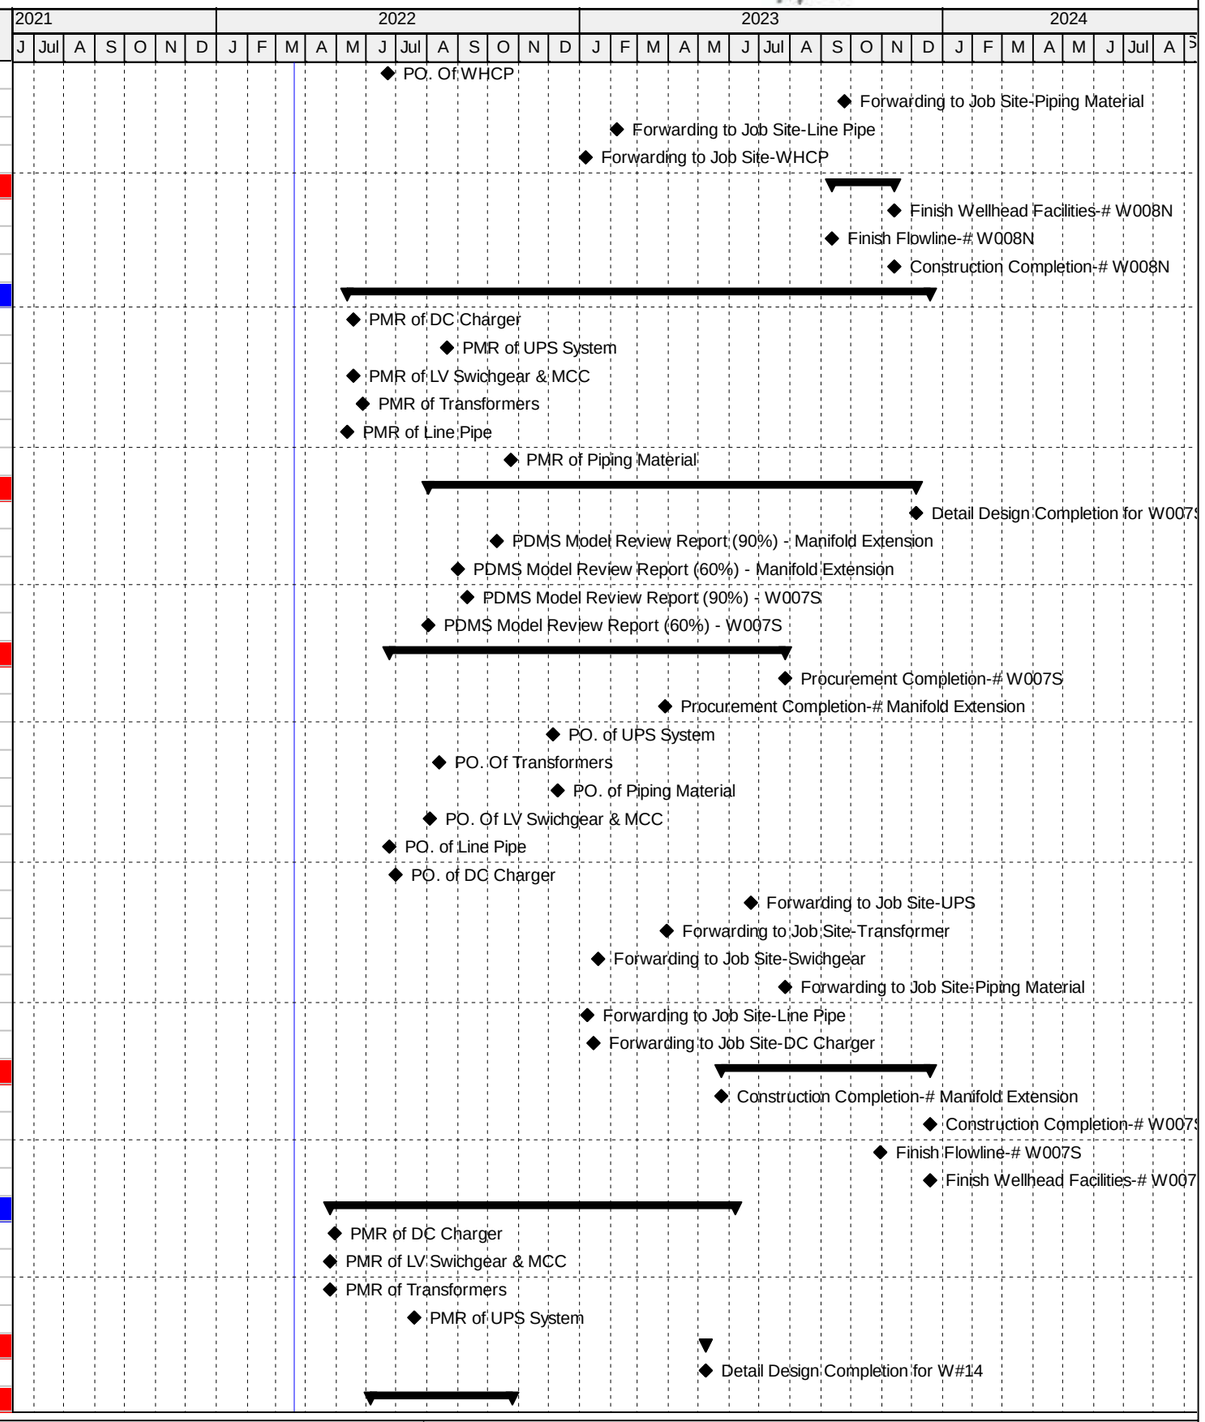


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
BK-MI-0	Forwarding to Job Site-DC Charger	0	0%	$0.00		23-Jul-22
BK-MI-0	Forwarding to Job Site-Swichgear	0	0%	$0.00		18-Jul-22
BK-MI-0	Forwarding to Job Site-Transformer	0	0%	$0.00		23-Jul-22
BK-MI-0	Forwarding to Job Site-UPS	0	0%	$0.00		16-Oct-22
BK-MI-0	PO. of DC Charger	0	0%	$0.00		04-Jun-22
BK-MI-0	PO. Of LV Swichgear & MCC	0	0%	$0.00		04-Jun-22
BK-MI-0	PO. Of Transformers	0	0%	$0.00		04-Jun-22
BK-MI-0	PO. of UPS System	0	0%	$0.00		28-Aug-22
BK-MI-0	Procurement Completion-#14	0	0%	$0.00		26-Oct-22
Construction		0	0%	$0.00	07-Jun-23	07-Jun-23
BK-MI-0	Construction Completion-# 14	0	0%	$0.00		07-Jun-23
BK-MI-0	Finish Wellhead Facilities-# 14	0	0%	$0.00		07-Jun-23
Package 08-Workover # 12		376	0%	$0.00	08-May-22	19-May-23
BK-MI-08	PMR of DC Charger	0	0%	$0.00		13-May-22
BK-MI-08	PMR of LV Swichgear & MCC	0	0%	$0.00		08-May-22
BK-MI-08	PMR of Transformers	0	0%	$0.00		08-May-22
BK-MI-08	PMR of UPS System	0	0%	$0.00		01-Aug-22
Engineering		0	0%	$0.00	14-Jan-23	14-Jan-23
BK-MI-0	Detail Design Completion for W#12	0	0%	$0.00		14-Jan-23
Procurement		274	0%	$0.00	10-May-22	08-Feb-23
BK-MI-0	Procurement Completion-# 12	0	0%	$0.00		08-Feb-23
BK-MI-0	PO. of UPS System	0	0%	$0.00		31-Jul-22
BK-MI-0	PO. Of Transformers	0	0%	$0.00		10-May-22
BK-MI-0	PO. Of LV Swichgear & MCC	0	0%	$0.00		10-May-22
BK-MI-0	PO. of DC Charger	0	0%	$0.00		10-May-22
BK-MI-0	Forwarding to Job Site-UPS	0	0%	$0.00		23-Oct-22
BK-MI-0	Forwarding to Job Site-Transformer	0	0%	$0.00		28-Jul-22
BK-MI-0	Forwarding to Job Site-Swichgear	0	0%	$0.00		23-Jul-22
BK-MI-0	Forwarding to Job Site-DC Charger	0	0%	$0.00		13-Jul-22
Construction		0	0%	$0.00	19-May-23	19-May-23
BK-MI-0	Finish Wellhead Facilities-# 12	0	0%	$0.00		19-May-23
BK-MI-0	Construction Completion-# 12	0	0%	$0.00		19-May-23
Package 09-Workover # 15		355	0%	$0.00	15-May-22	05-May-23
BK-MI-09	PMR of DC Charger	0	0%	$0.00		01-Jun-22
BK-MI-09	PMR of LV Swichgear & MCC	0	0%	$0.00		15-May-22
BK-MI-09	PMR of Transformers	0	0%	$0.00		27-May-22
BK-MI-09	PMR of UPS System	0	0%	$0.00		01-Jun-22
Engineering		0	0%	$0.00	25-Nov-22	25-Nov-22
BK-MI-0	Detail Design Completion for W#15	0	0%	$0.00		25-Nov-22
Procurement		190	0%	$0.00	16-Jun-22	23-Dec-22
BK-MI-0	Procurement Completion-#15	0	0%	$0.00		23-Dec-22
BK-MI-0	PO. of UPS System	0	0%	$0.00		03-Jul-22
BK-MI-0	PO. Of Transformers	0	0%	$0.00		25-Jun-22
BK-MI-0	PO. Of LV Swichgear & MCC	0	0%	$0.00		16-Jun-22
BK-MI-0	PO. of DC Charger	0	0%	$0.00		30-Jun-22
BK-MI-0	Forwarding to Job Site-UPS	0	0%	$0.00		25-Sep-22
BK-MI-0	Forwarding to Job Site-Transformer	0	0%	$0.00		22-Sep-22
BK-MI-0	Forwarding to Job Site-Swichgear	0	0%	$0.00		13-Sep-22
BK-MI-0	Forwarding to Job Site-DC Charger	0	0%	$0.00		17-Sep-22

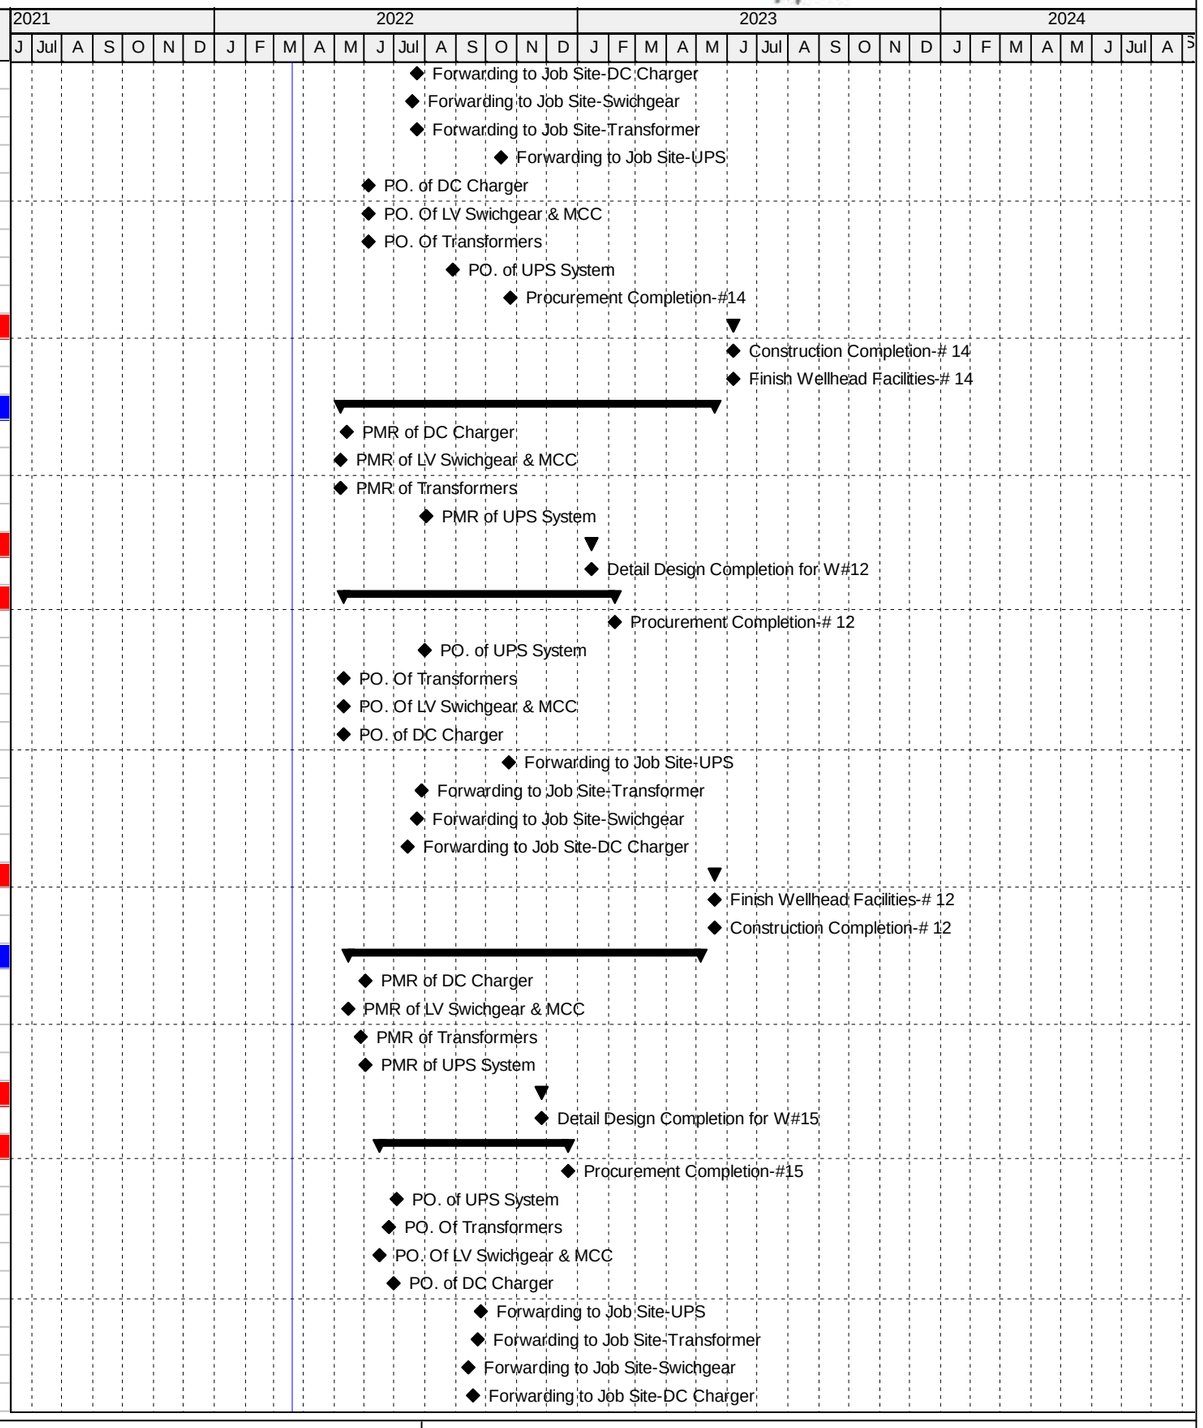

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Construction		0	0%	$0.00	05-May-23	05-May-23
BK-MI-0	Finish Wellhead Facilities-# 15	0	0%	$0.00		05-May-23
BK-MI-0	Construction Completion-# 15	0	0%	$0.00		05-May-23
Package 10-Workover # 05		386	0%	$0.00	06-Jun-22	27-Jun-23
BK-MI-10	PMR of DC Charger	0	0%	$0.00		16-Jun-22
BK-MI-10	PMR of LV Swichgear & MCC	0	0%	$0.00		06-Jun-22
BK-MI-10	PMR of Transformers	0	0%	$0.00		11-Jun-22
BK-MI-10	PMR of UPS System	0	0%	$0.00		04-Sep-22
Engineering		0	0%	$0.00	23-May-23	23-May-23
BK-MI-1	Detail Design Completion for W#05	0	0%	$0.00		23-May-23
Procurement		240	0%	$0.00	13-Jul-22	10-Mar-23
BK-MI-1	Procurement Completion-# 05	0	0%	$0.00		10-Mar-23
BK-MI-1	PO. of UPS System	0	0%	$0.00		11-Oct-22
BK-MI-1	PO. Of Transformers	0	0%	$0.00		13-Jul-22
BK-MI-1	PO. Of LV Swichgear & MCC	0	0%	$0.00		13-Jul-22
BK-MI-1	PO. of DC Charger	0	0%	$0.00		18-Jul-22
BK-MI-1	Forwarding to Job Site-UPS	0	0%	$0.00		22-Feb-23
BK-MI-1	Forwarding to Job Site-Transformer	0	0%	$0.00		24-Nov-22
BK-MI-1	Forwarding to Job Site-Swichgear	0	0%	$0.00		29-Nov-22
BK-MI-1	Forwarding to Job Site-DC Charger	0	0%	$0.00		19-Nov-22
Construction		0	0%	$0.00	27-Jun-23	27-Jun-23
BK-MI-1	Finish Wellhead Facilities-# 05	0	0%	$0.00		27-Jun-23
BK-MI-1	Construction Completion-# 05	0	0%	$0.00		27-Jun-23
Surface Development (EPC)		696	0%	$0.00	27-Apr-22	23-Mar-24
Package 11- EPC Pipeline 8" & 4"		511	0%	$0.00	27-Apr-22	20-Sep-23
BK-MI-11	PMR For JB, Bulk Item and Installation Accessories	0	0%	$0.00		04-Nov-22
BK-MI-11	PMR For Pig Traps	0	0%	$0.00		23-May-22
BK-MI-11	PMR For Bulk Item & Earthing System	0	0%	$0.00		04-Sep-22
BK-MI-11	PMR For ON/OFF & Shutdown Valve	0	0%	$0.00		04-Aug-22
BK-MI-11	PMR For Cathodic Protection System	0	0%	$0.00		04-Sep-22
BK-MI-11	PMR For LBV	0	0%	$0.00		27-Apr-22
BK-MI-11	PMR For Pressure Safety Valve	0	0%	$0.00		04-Aug-22
BK-MI-11	PMR For Field Instrument	0	0%	$0.00		18-Aug-22
BK-MI-11	PMR For Line Pipe	0	0%	$0.00		26-Jul-22
BK-MI-11	PMR For Piping Material	0	0%	$0.00		25-Jan-23
BK-MI-11	PMR For F&G Devices	0	0%	$0.00		29-Jul-22
Engineering		352	0%	$0.00	02-May-22	19-Apr-23
BK-MI-1	Detail Design Completion for Pipeline	0	0%	$0.00		19-Apr-23
BK-MI-1	Unit Plot Plan for Binak Production Unit	0	0%	$0.00		08-Jan-23
BK-MI-1	A/G Piping Isometric	0	0%	$0.00		01-Apr-23
BK-MI-1	HAZID & HAZOP Report	0	0%	$0.00		30-Jul-22
BK-MI-1	Piping Material Specification	0	0%	$0.00		17-Jun-22
BK-MI-1	Unit Plot Plan for Pig Receiver Area	0	0%	$0.00		25-Jul-22
BK-MI-1	A/G Piping Plan	0	0%	$0.00		21-Feb-23
BK-MI-1	Line List	0	0%	$0.00		16-Jun-22
BK-MI-1	Corrosion Study & Material Selection Report	0	0%	$0.00		16-Jun-22
BK-MI-1	Pipeline Hydraulic Calculation	0	0%	$0.00		16-Jun-22
BK-MI-1	P&ID for Condensate Pipeline (to Binak PU)	0	0%	$0.00		16-Jun-22
BK-MI-1	P&ID for Gas Pipeline (to Siahmakan G.I. Station)	0	0%	$0.00		16-Jun-22

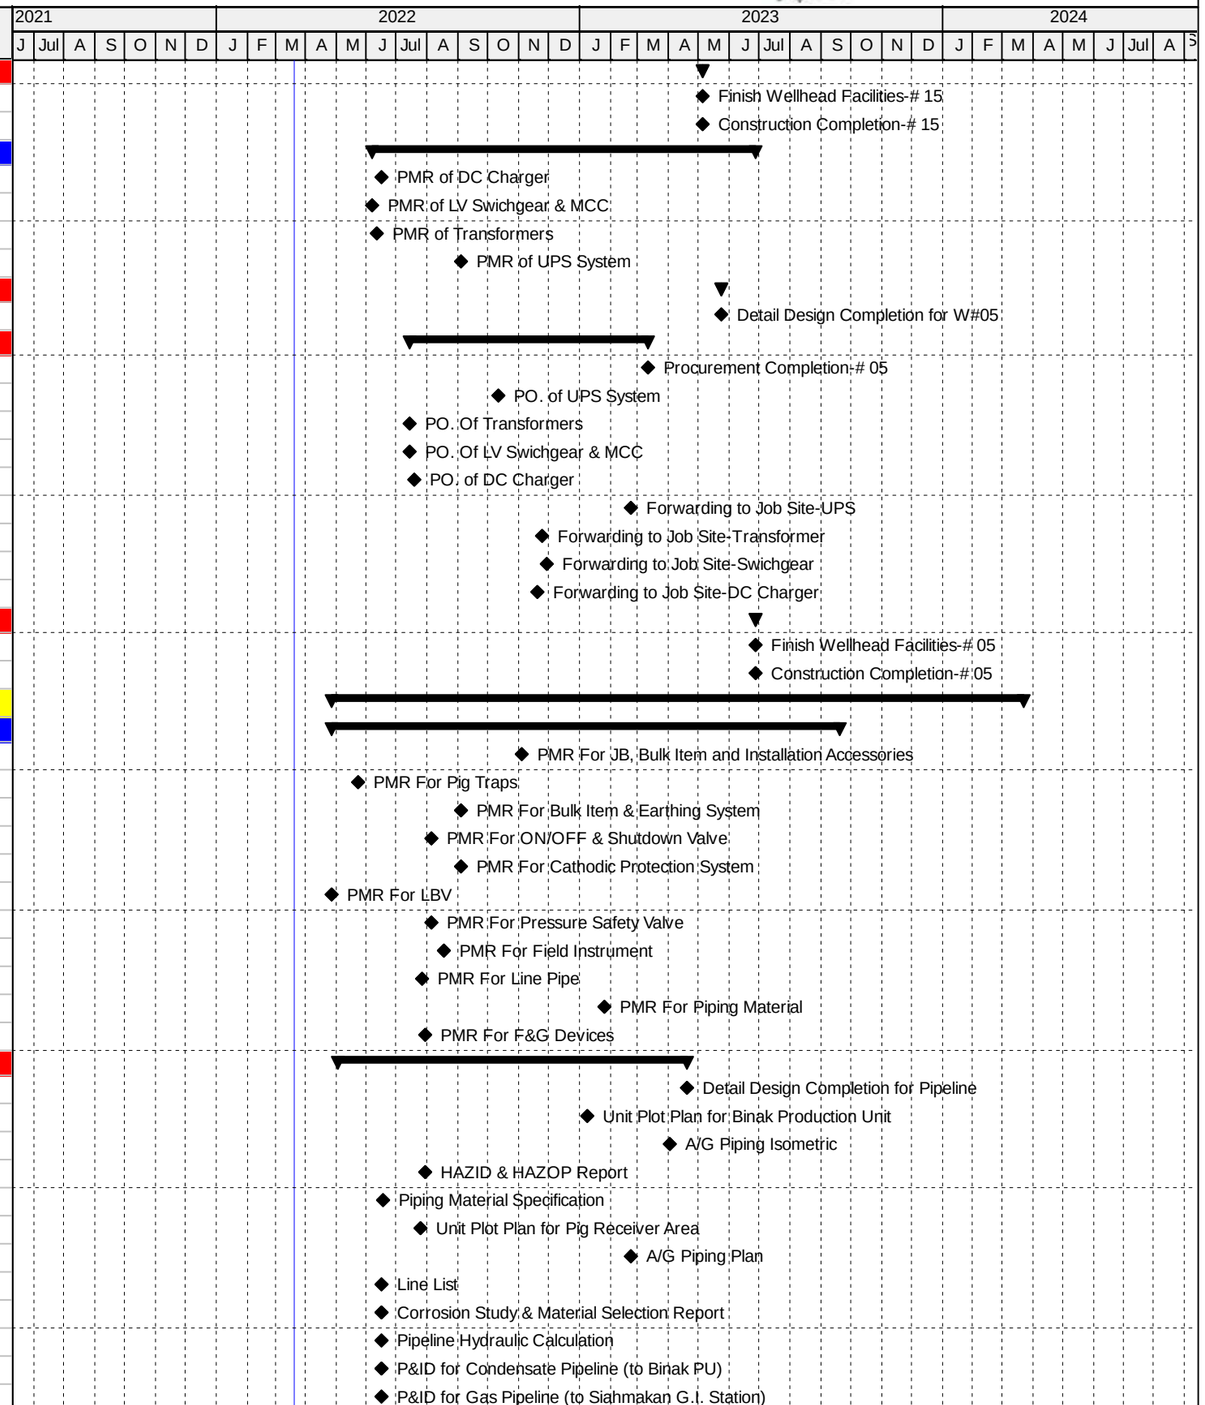


Actual Level of Effort | Remaining Work | Milestone

Actual Work | Critical Remaining Work | summary

TASK filter: All Activities


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
BK-MI-1	PFD for Pipelines	0	0%	$0.00		16-Jun-22
BK-MI-1	Plan & Profile Drawings For Condensate Pipeline (to Binak Pl	0	0%	$0.00		25-Jul-22
BK-MI-1	Plan & Profile Drawings For Gas Pipeline (to Siahmakan)	0	0%	$0.00		30-Jul-22
BK-MI-1	Wall Thickness Calculation Report	0	0%	$0.00		17-Jun-22
BK-MI-1	Geotechnical Investigation Report	0	0%	$0.00		02-May-22
BK-MI-1	MTO for Line Pipe	0	0%	$0.00		26-Jul-22
BK-MI-1	Wall Thickness Calculation	0	0%	$0.00		17-Jun-22
BK-MI-1	Instrument Hook-up Diagram	0	0%	$0.00		26-Jul-22
BK-MI-1	PDMS Model Review Report (60%)	0	0%	$0.00		15-Nov-22
BK-MI-1	PDMS Model Review Report (90%)	0	0%	$0.00		08-Jan-23
Procurement		176	0%	$0.00	17-Mar-23	09-Sep-23
BK-MI-1	Forwarding to Job Site of Line Pipes 8" & 4"	0	0%	$0.00		07-Jun-23
BK-MI-1	Forwarding to Job Site of PL/PR	0	0%	$0.00		17-Mar-23
BK-MI-1	Forwarding to Job Site of Instrument Cable	0	0%	$0.00		14-Jul-23
BK-MI-1	Forwarding to Job Site of Valves	0	0%	$0.00		23-Apr-23
BK-MI-1	Forwarding to Job Site of Piping Material	0	0%	$0.00		25-Aug-23
BK-MI-1	Forwarding to Job Site of Instrument Devices	0	0%	$0.00		31-Mar-23
BK-MI-1	Forwarding to Job Site of Instrument Bulk Material	0	0%	$0.00		14-Jul-23
BK-MI-1	Procurement Completion-#Pipeline 8" & 4"	0	0%	$0.00		09-Sep-23
Construction		333	0%	$0.00	22-Oct-22	20-Sep-23
8" Gas Pipeline (to Siahmakan)		259	0%	$0.00	04-Jan-23	20-Sep-23
BK-MI-	ROW	0	0%	$0.00		04-Jan-23
BK-MI-	Trench	0	0%	$0.00		25-Mar-23
BK-MI-	Pipe Stringing	0	0%	$0.00		26-May-23
BK-MI-	Welding	0	0%	$0.00		16-Aug-23
BK-MI-	Hydrotest	0	0%	$0.00		10-Sep-23
BK-MI-	Instrument Installation	0	0%	$0.00		13-Aug-23
BK-MI-	Catodic Protection Installation	0	0%	$0.00		20-Sep-23
BK-MI-	Construction Completion-# 8" Pipeline	0	0%	$0.00		20-Sep-23
4" Condensate Pipeline (to Binak PU)		310	0%	$0.00	22-Oct-22	28-Aug-23
BK-MI-	ROW	0	0%	$0.00		22-Oct-22
BK-MI-	Pipeline Support Foundation	0	0%	$0.00		30-Oct-22
BK-MI-	Pipeline Support Erection	0	0%	$0.00		07-Apr-23
BK-MI-	Welding	0	0%	$0.00		20-Jun-23
BK-MI-	Hydrotest	0	0%	$0.00		10-Jul-23
BK-MI-	Instrument Installation	0	0%	$0.00		28-Aug-23
BK-MI-	Construction Completion-#4" Pipeline	0	0%	$0.00		28-Aug-23
Package 12- EPC # Compressor Station		681	0%	$0.00	12-May-22	23-Mar-24
BK-MI-12	PMR for Gas Compressors	0	0%	$0.00		13-May-22
BK-MI-12	PMR For Storage Tanks	0	0%	$0.00		23-May-22
BK-MI-12	PMR For Centrifugal Pumps For General Services	0	0%	$0.00		06-Jul-22
BK-MI-12	PMR For Pressure Vessels	0	0%	$0.00		12-Jun-22
BK-MI-12	PMR For Overhead Travelling Cranes	0	0%	$0.00		01-Jun-22
BK-MI-12	PMR For Fire Water Pump	0	0%	$0.00		13-May-22
BK-MI-12	PMR For Flare Packages	0	0%	$0.00		01-Jun-22
BK-MI-12	PMR For Centrifugal Pumps For Process Services	0	0%	$0.00		26-Jun-22
BK-MI-12	PMR For Chemical Injection Packages	0	0%	$0.00		01-Jun-22
BK-MI-12	PMR For Gas Air Coolers	0	0%	$0.00		23-May-22

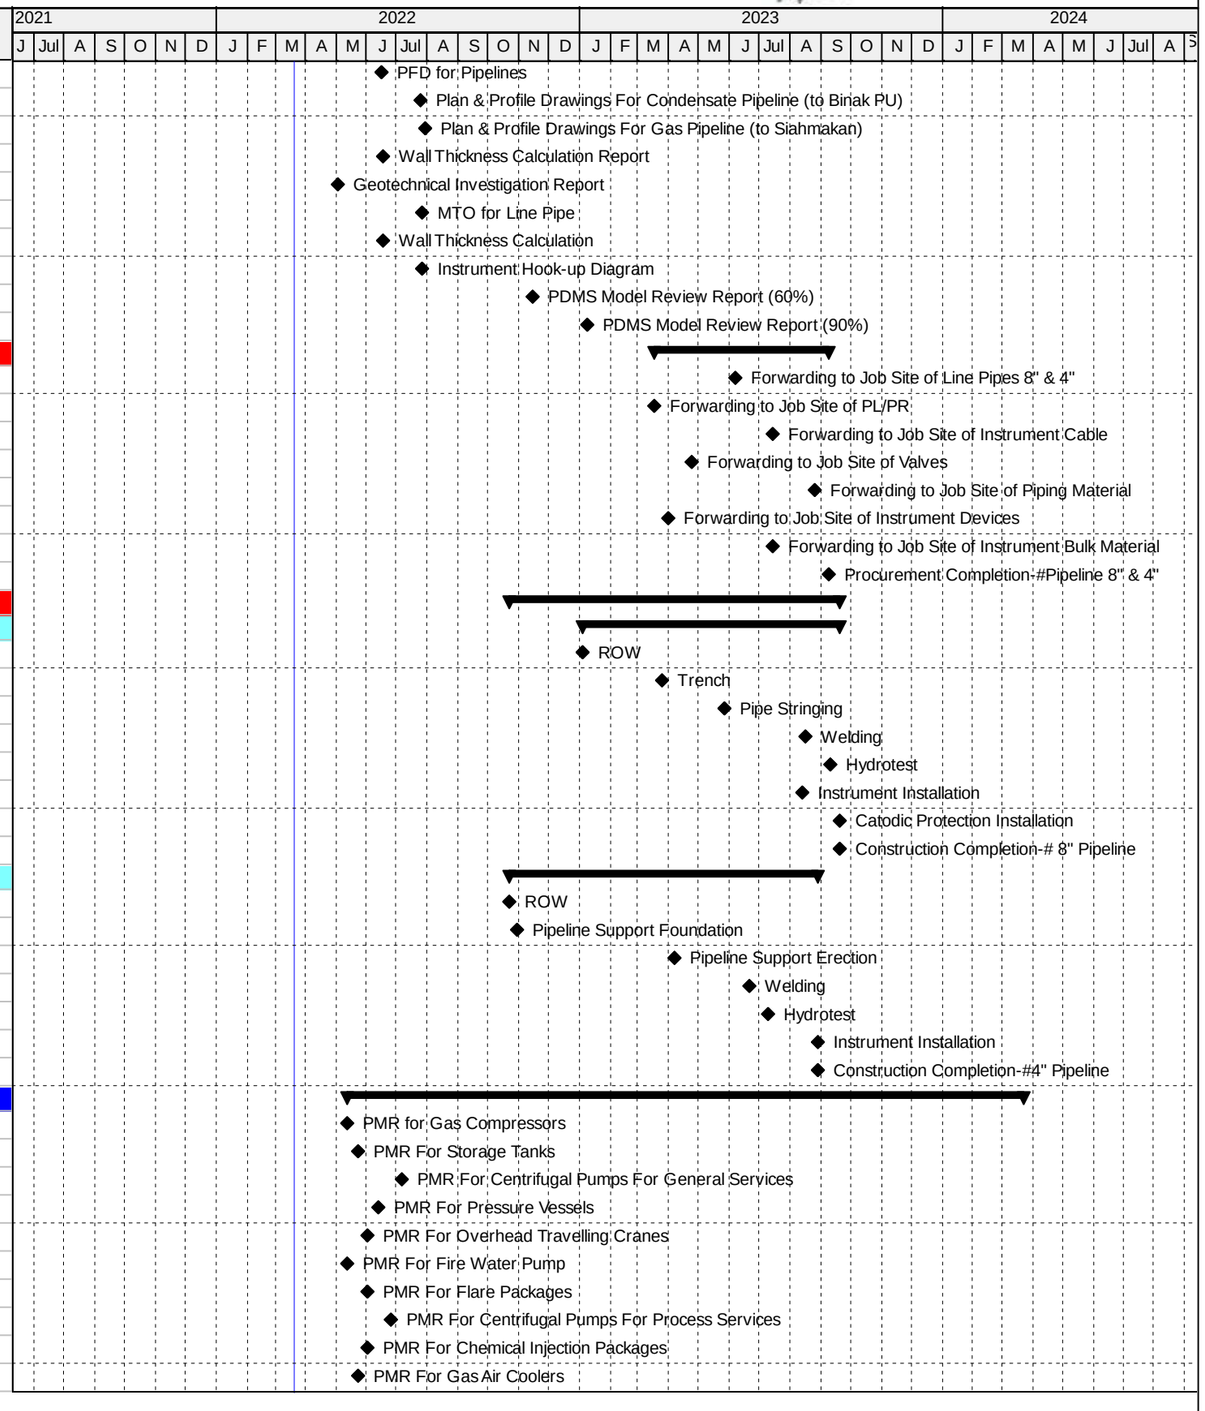

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
BK-MI-12	PMR For Instrument/Plant Air & Nitrogen Packages	0	0%	$0.00		01-Jun-22
BK-MI-12	PMR For Gas Dehydration Package	0	0%	$0.00		23-May-22
BK-MI-12	PMR For Transformers	0	0%	$0.00		27-May-22
BK-MI-12	PMR For LV Switchgear, MCC	0	0%	$0.00		30-May-22
BK-MI-12	PMR For Emergency Diesel Generator	0	0%	$0.00		01-Jun-22
BK-MI-12	PMR For Total Flooding System	0	0%	$0.00		22-May-22
BK-MI-12	PMR for Telecommunication System	0	0%	$0.00		28-May-23
BK-MI-12	PMR for Piping Material	0	0%	$0.00		31-Jan-23
BK-MI-12	PMR For ESD System	0	0%	$0.00		22-May-22
BK-MI-12	PMR For Pressure Safety Valves (PSV)	0	0%	$0.00		23-Aug-22
BK-MI-12	PMR For On/off & Shutdown Valves	0	0%	$0.00		23-Aug-22
BK-MI-12	PMR for Field Instrumentations	0	0%	$0.00		19-Aug-22
BK-MI-12	PMR For Control Valves	0	0%	$0.00		23-Aug-22
BK-MI-12	PMR For Control System/Console/Furniture	0	0%	$0.00		30-Jun-22
Engineering		389	0%	$0.00	12-May-22	05-Jun-23
BK-MI-1	Detail Design Completion for Binak GCS	0	0%	$0.00		05-Jun-23
BK-MI-1	Process Flow Diagram (PFD)	0	0%	$0.00		12-May-22
BK-MI-1	P&ID - Gas Compression Inlet Gas Pipeline (Binak)	0	0%	$0.00		12-May-22
BK-MI-1	P&ID - Gas Compression Inlet Gas Pipeline (Golkhari)	0	0%	$0.00		12-May-22
BK-MI-1	P&ID - Slug Catcher System	0	0%	$0.00		12-May-22
BK-MI-1	P&ID - Gas Compression Inlet Knock Out Drum	0	0%	$0.00		12-May-22
BK-MI-1	P&ID - 1st Stage Gas Compression Suction Drums	0	0%	$0.00		12-May-22
BK-MI-1	P&ID - 1st Stage Gas Compression Compressors	0	0%	$0.00		13-May-22
BK-MI-1	P&ID - 1st Stage Gas Compression Air Coolers	0	0%	$0.00		13-May-22
BK-MI-1	P&ID - 2nd Stage Gas Compression Suction Drums	0	0%	$0.00		13-May-22
BK-MI-1	P&ID - 1st Stage Gas Compression Air Coolers	0	0%	$0.00		13-May-22
BK-MI-1	P&ID - 2nd Stage Gas Compression Suction Drums	0	0%	$0.00		13-May-22
BK-MI-1	P&ID - 2nd Stage Gas Compression Compressors	0	0%	$0.00		13-May-22
BK-MI-1	P&ID - 2nd Stage Gas Compression Air Coolers	0	0%	$0.00		13-May-22
BK-MI-1	P&ID - 2nd Stage Gas Compression Discharge Drum	0	0%	$0.00		13-May-22
BK-MI-1	P&ID - Gas Compression Dehydration Package	0	0%	$0.00		13-May-22
BK-MI-1	P&ID - Lean Glycol Storage Tank	0	0%	$0.00		13-May-22
BK-MI-1	P&ID - Instrument & Plant Air System	0	0%	$0.00		12-May-22
BK-MI-1	P&ID - Nitrogen Generation System	0	0%	$0.00		12-May-22
BK-MI-1	P&ID - Close Drain System	0	0%	$0.00		12-May-22
BK-MI-1	P&ID - Corrosion Inhibitor Package	0	0%	$0.00		12-May-22
BK-MI-1	P&ID - Methanol Injection Package	0	0%	$0.00		12-May-22
BK-MI-1	P&ID - LP Flare System	0	0%	$0.00		12-May-22
BK-MI-1	Electrical Load List	0	0%	$0.00		13-May-22
BK-MI-1	PDMS Model Review Report (60%)	0	0%	$0.00		25-Nov-22
BK-MI-1	SIL Study Report	0	0%	$0.00		08-Aug-22
BK-MI-1	PDMS Model Review Report (30%)	0	0%	$0.00		29-Aug-22
BK-MI-1	Unit Plot Plan Drawing	0	0%	$0.00		13-May-22
BK-MI-1	Wall Thickness Calculation Report	0	0%	$0.00		13-May-22
BK-MI-1	Piping Material Specification	0	0%	$0.00		13-May-22
BK-MI-1	Piping Corrosion Study & Material Selection Report	0	0%	$0.00		13-May-22
BK-MI-1	HAZOP Study Report	0	0%	$0.00		25-Jun-22
BK-MI-1	PDMS Model Review Report (90%)	0	0%	$0.00		14-Jan-23
BK-MI-1	HAZID Study Report	0	0%	$0.00		25-Jun-22
Procurement		331	0%	$0.00	08-Apr-23	04-Mar-24

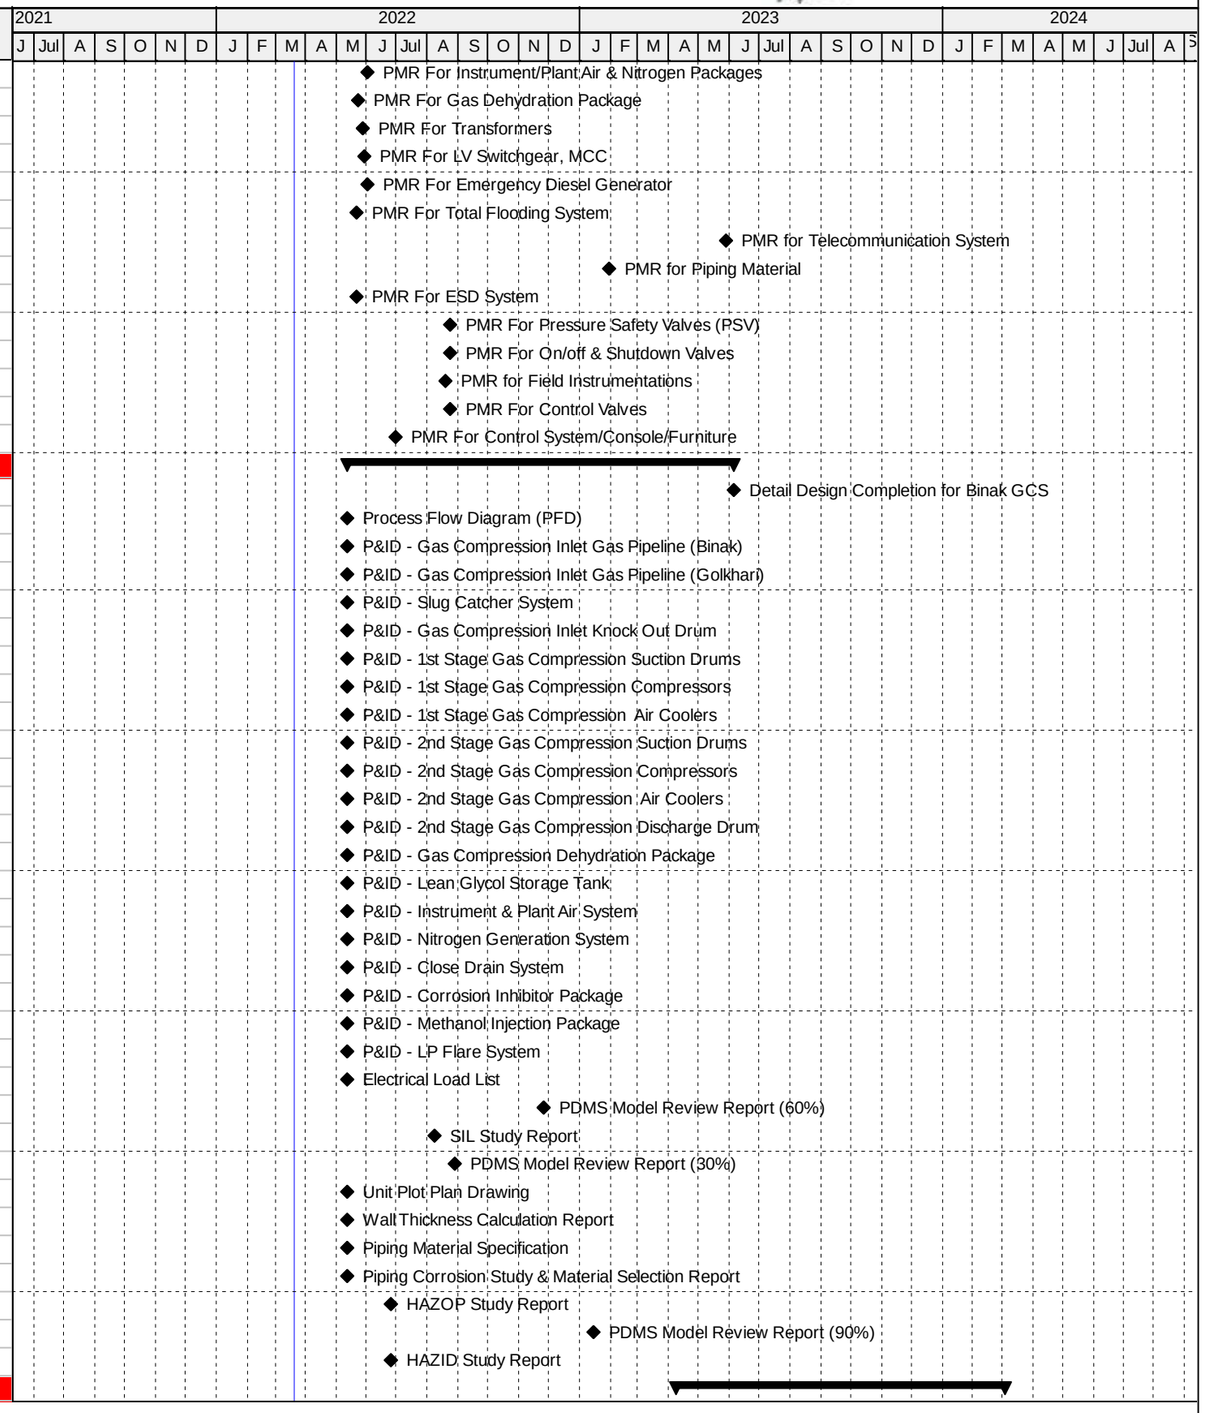

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
BK-MI-1	Procurement Completion-# Compressor Station	0	0%	$0.00		04-Mar-24
BK-MI-1	Forwarding to Job Site of Storage Tanks for GCS	0	0%	$0.00		27-Apr-23
BK-MI-1	Forwarding to Job Site of Gas Compressors	0	0%	$0.00		22-Jan-24
BK-MI-1	Forwarding to Job Site of Gas Dehydration Package	0	0%	$0.00		13-Nov-23
BK-MI-1	Forwarding to Job Site of Gas Air Coolers	0	0%	$0.00		24-Sep-23
BK-MI-1	Forwarding to Job Site of Chemical Injection Packages for GC	0	0%	$0.00		24-May-23
BK-MI-1	Forwarding to Job Site of Process Pumps for GCS	0	0%	$0.00		10-Aug-23
BK-MI-1	Forwarding to Job Site of Fire Water Pumps for GCS	0	0%	$0.00		15-Sep-23
BK-MI-1	Forwarding to Job Site of LP Flare Package for GCS	0	0%	$0.00		28-Jul-23
BK-MI-1	Forwarding to Job Site of Overhead Travelling Cranes for GC	0	0%	$0.00		19-Apr-23
BK-MI-1	Forwarding to Job Site of Piping Material for GCS	0	0%	$0.00		21-Sep-23
BK-MI-1	Forwarding to Job Site of DCS System for GCS	0	0%	$0.00		24-Jun-23
BK-MI-1	Forwarding to Job Site of ESD, F&G for GCS	0	0%	$0.00		01-Jun-23
BK-MI-1	Forwarding to Job Site of On/off & Shutdown Valves for GCS	0	0%	$0.00		12-Sep-23
BK-MI-1	Forwarding to Job Site of Pressure Safety Valves (PSV) for G	0	0%	$0.00		20-May-23
BK-MI-1	Forwarding to Job Site of Control Valves for GCS	0	0%	$0.00		13-Aug-23
BK-MI-1	Forwarding to Job Site of Telecom. System for GCS	0	0%	$0.00		30-Jul-23
BK-MI-1	Forwarding to Job Site of Existent MV Switchgear Expansion	0	0%	$0.00		08-Apr-23
BK-MI-1	Forwarding to Job Site of Emergency Diesel Generator for G	0	0%	$0.00		26-Aug-23
BK-MI-1	Forwarding to Job Site of Transformers for GCS	0	0%	$0.00		10-May-23
BK-MI-1	Forwarding to Job Site of LV Switchgear & MCC for GCS	0	0%	$0.00		08-Apr-23
Construction		247	0%	$0.00	20-Jul-23	23-Mar-24
BK-MI-1	Installation of Gas Compressor of first & Second Stage	0	0%	$0.00		23-Mar-24
BK-MI-1	Installation of Dehydration Package	0	0%	$0.00		20-Jul-23
BK-MI-1	Construction Completion-#Gas Compressor	0	0%	$0.00		23-Mar-24
GENERAL		720	25.09%	$1,911,960.00	23-Jun-21 A	08-Mar-24
Project Management		720	36.86%	$175,000.00	30-Jun-21 A	30-Jan-24
Project Plans		260	36.8%	$43,750.00	07-Jul-21 A	25-Oct-22
GE1000	Master Document List (MDL) & Updating	50	100%	$2,187.50	07-Jul-21 A	20-Mar-22
GE1010	Detailed Schedule & Updating	59	40%	$8,750.00	08-Dec-21	17-May-22
GE1020	Work Breakdown Structure (WBS)	54	40%	$3,937.50	16-Nov-21	20-Mar-22
GE1030	Cost Breakdown Structure (CBS)	44	40%	$2,187.50	16-Nov-21	20-Mar-22
GE1040	Production Capacity Realization Plan	60	0%	$875.00	20-Mar-22	18-May-22
GE1050	Procurement & Services Contracting Plan	39	0%	$1,750.00	20-Mar-22	27-Apr-22
GE1060	Material Equipment & Control Index (MCI)	39	0%	$1,750.00	09-Apr-22	17-May-22
GE1070	Progress S-curves & Updating	5	20%	$875.00	10-May-22	06-Jun-22
GE1080	Cash Flow Plan	5	0%	$3,937.50	20-Mar-22	24-Mar-22
GE1090	Project Organization Charts	5	100%	$875.00	11-Jul-21 A	20-Mar-22
GE1100	EPC HSE Plan	50	80%	$4,812.50	20-Nov-21	20-Mar-22
GE1110	Emergency Response Plan (ERP)	50	40%	$1,750.00	22-May-22	08-May-22
GE1120	Guideline on Permit To Work System(PTWS)	40	100%	$875.00	23-Nov-21	09-May-22
GE1130	HSE Operation Control Procedure	50	0%	$1,312.50	09-May-22	27-Jun-22
GE1140	Environmental Management Plan (EMP)	40	40%	$1,750.00	21-Feb-22	27-Jun-22
GE1150	Specification for Medical Services	40	0%	$875.00	28-Jun-22	06-Aug-22
GE1160	EPC Waste Management Plan	40	0%	$1,750.00	07-Aug-22	15-Sep-22
GE1170	Crisis Management Plan	40	0%	$1,312.50	07-Aug-22	15-Sep-22
GE1180	EPC FMEA report	40	60%	$1,312.50	28-Dec-21	15-Sep-22
GE1190	PSSR Procedure	40	0%	$437.50	16-Sep-22	25-Oct-22




Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
GE1200	Pigging Safety Requirement	40	0%	$437.50	16-Sep-22	25-Oct-22
Project Procedures		104	53.5%	$17,500.00	11-Jul-21 A	02-May-22
GE-1325	Project Control Procedure (WBS, PMS, Invoicing)	44	0%	$0.00	20-Mar-22	02-May-22
GE1210	Project Coordination Procedure	44	80%	$875.00	11-Jul-21 A	20-Mar-22
GE1220	Progress Measurement Procedure	44	20%	$1,750.00	01-May-22	02-May-22
GE1230	Document Numbering Procedure	44	80%	$1,750.00	11-Jul-21 A	20-Mar-22
GE1240	Change Control Procedure	44	30%	$875.00	01-May-22	02-May-22
GE1250	Invoicing Procedure	39	30%	$1,750.00	25-Apr-22	27-Apr-22
GE1260	Correspondence Procedure	39	80%	$875.00	11-Jul-21 A	20-Mar-22
GE1270	Meeting Procedure	39	80%	$875.00	11-Jul-21 A	20-Mar-22
GE1280	Reporting Procedure	34	80%	$2,625.00	11-Jul-21 A	09-Apr-22
GE1290	Procurement & Services Contracting Procedure	44	100%	$875.00	22-Nov-21	20-Mar-22
GE1300	Eng. Document Control Procedure	44	100%	$1,750.00	11-Jul-21 A	20-Mar-22
GE1310	Material Control Procedure	44	0%	$1,750.00	20-Mar-22	02-May-22
GE1320	Completion & Handover Procedure	44	0%	$1,750.00	20-Mar-22	02-May-22
Tendering & Contracting		10	50%	$70,000.00	20-Mar-22	29-Mar-22
Surface		10	50%	$70,000.00	20-Mar-22	29-Mar-22
EPC Contractor (Contractor #1)		10	100%	$17,500.00	20-Mar-22	27-Mar-22
GE1710	Tendering & Selection	5	100%	$7,000.00	20-Mar-22	23-Mar-22
GE1720	Contract Effectiveness	5	100%	$10,500.00	25-Mar-22	27-Mar-22
EPC Contractor (Contractor #2)		10	100%	$17,500.00	20-Mar-22	27-Mar-22
GE1730	Tendering & Selection	5	100%	$7,000.00	20-Mar-22	23-Mar-22
GE1740	Contract Effectiveness	5	100%	$10,500.00	25-Mar-22	27-Mar-22
EPC Contractor (Contractor #3)		10	0%	$17,500.00	20-Mar-22	29-Mar-22
GE1750	Tendering & Selection	5	0%	$7,000.00	20-Mar-22	24-Mar-22
GE1760	Contract Effectiveness	5	0%	$10,500.00	25-Mar-22	29-Mar-22
EPC Contractor (Contractor #4)		10	0%	$17,500.00	20-Mar-22	29-Mar-22
GE1770	Tendering & Selection	5	0%	$7,000.00	20-Mar-22	24-Mar-22
GE1780	Contract Effectiveness	5	0%	$10,500.00	25-Mar-22	29-Mar-22
Project Performance Report		720	9.26%	$43,750.00	30-Jun-21	30-Jan-24
GE1790	Monthly Progress Report 01	1	100%	$364.58	11-Jul-21 A	20-Mar-22
GE1800	Monthly Progress Report 02	1	100%	$364.58	11-Aug-21	18-Apr-22
GE1810	Monthly Progress Report 03	1	100%	$364.58	11-Sep-21	17-May-22
GE1820	Monthly Progress Report 04	1	100%	$364.58	11-Oct-21 A	15-Jun-22
GE1830	Monthly Progress Report 05	1	100%	$364.58	11-Nov-21	14-Jul-22
GE1840	Monthly Progress Report 06	1	100%	$364.58	11-Dec-21	12-Aug-22
GE1850	Monthly Progress Report 07	1	100%	$364.58	11-Jan-22 A	10-Sep-22
GE1860	Monthly Progress Report 08	1	100%	$364.58	11-Feb-22	09-Oct-22
GE1870	Monthly Progress Report 09	1	100%	$364.58	13-Mar-22	07-Nov-22
GE1880	Monthly Progress Report 10	1	0%	$364.58	06-Dec-22	06-Dec-22
GE1890	Monthly Progress Report 11	1	0%	$364.58	05-Jan-23	05-Jan-23
GE1900	Monthly Progress Report 12	1	0%	$364.58	04-Feb-23	04-Feb-23
GE1910	Monthly Progress Report 13	1	0%	$364.58	06-Mar-23	06-Mar-23
GE1920	Monthly Progress Report 14	1	0%	$364.58	05-Apr-23	05-Apr-23
GE1930	Monthly Progress Report 15	1	0%	$364.58	05-May-23	05-May-23
GE1940	Monthly Progress Report 16	1	0%	$364.58	04-Jun-23	04-Jun-23
GE1950	Monthly Progress Report 17	1	0%	$364.58	04-Jul-23	04-Jul-23
GE1960	Monthly Progress Report 18	1	0%	$364.58	03-Aug-23	03-Aug-23
GE1970	Monthly Progress Report 19	1	0%	$364.58	02-Sep-23	02-Sep-23

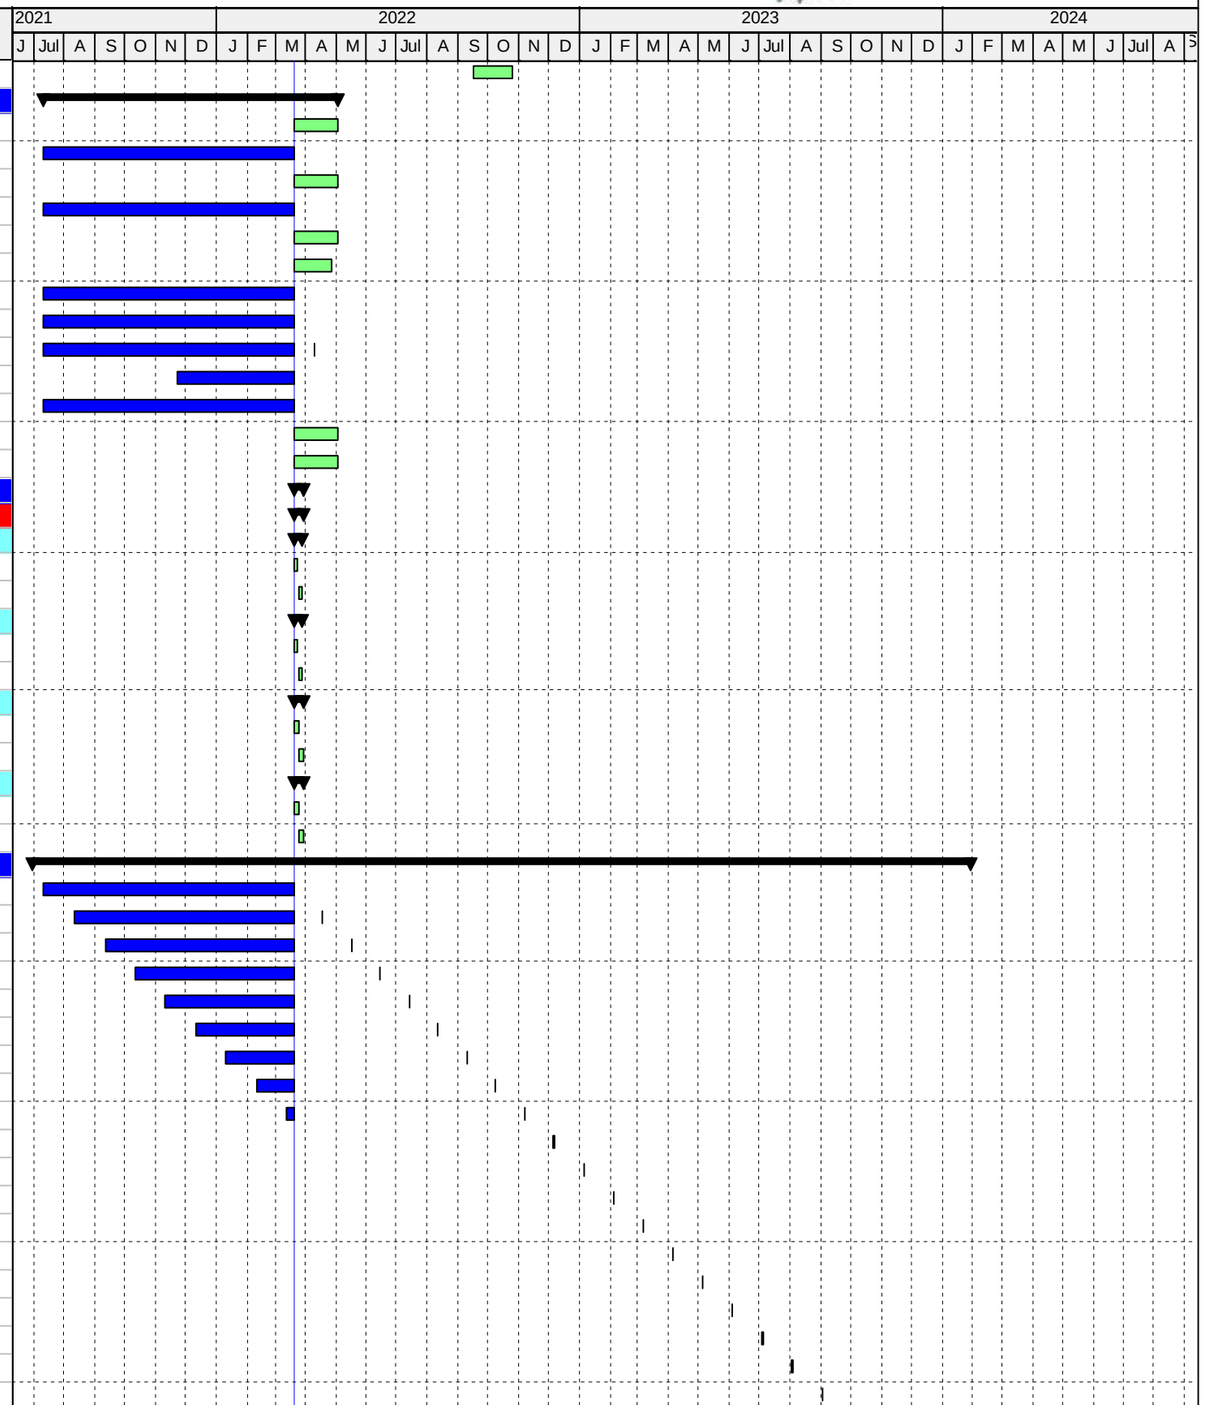


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
GE1980	Monthly Progress Report 20	1	0%	$364.58	02-Oct-23	02-Oct-23
GE1990	Monthly Progress Report 21	1	0%	$364.58	01-Nov-23	01-Nov-23
GE2000	Monthly Progress Report 22	1	0%	$364.58	01-Dec-23	01-Dec-23
GE2010	Monthly Progress Report 23	1	0%	$364.58	31-Dec-23	31-Dec-23
GE2020	Monthly Progress Report 24	1	0%	$364.58	30-Jan-24	30-Jan-24
GE2030	Weekly Reports	720	2.51%	$30,625.00	30-Jun-21	20-Mar-22
GE2040	Delay Analysis Report 01	1	0%	$1,093.75	20-Mar-22	20-Mar-22
GE2050	Delay Analysis Report 02	1	0%	$1,093.75	17-Sep-22	17-Sep-22
GE2060	Delay Analysis Report 03	1	0%	$1,093.75	17-Mar-23	17-Mar-23
GE2070	Delay Analysis Report 04	1	0%	$1,093.75	14-Sep-23	14-Sep-23
Project Insurance		715	0%	$140,000.00	20-Mar-22	03-Mar-24
Full-Risk engineering insurance		715	0%	$77,000.00	20-Mar-22	03-Mar-24
GE2080	Insurance Contract Awarded	5	0%	$0.00	20-Mar-22	24-Mar-22
GE2090	Providing Insurance Coverage	710	0%	$77,000.00	25-Mar-22	03-Mar-24
Employer's Civil liability towards Staff and Third Parties Insurance		575	0%	$35,000.00	23-Jun-22	18-Jan-24
GE2100	Insurance Contract Awarded	5	0%	$0.00	23-Jun-22	27-Jun-22
GE2110	Providing Insurance Coverage	570	0%	$35,000.00	28-Jun-22	18-Jan-24
Cargo Transportation Insurance		425	0%	$14,000.00	18-Nov-22	16-Jan-24
GE2120	Insurance Contract Awarded	5	0%	$0.00	18-Nov-22	22-Nov-22
GE2130	Providing Insurance Coverage	420	0%	$14,000.00	23-Nov-22	16-Jan-24
Vehicle insurance		655	0%	$7,000.00	07-Apr-22	22-Jan-24
GE2140	Insurance Contract Awarded	5	0%	$0.00	07-Apr-22	12-Apr-22
GE2150	Providing Insurance Coverage	650	0%	$7,000.00	12-Apr-22	22-Jan-24
Machineries insurance		655	0%	$4,200.00	07-Apr-22	22-Jan-24
GE2160	Insurance Contract Awarded	5	0%	$0.00	07-Apr-22	12-Apr-22
GE2170	Providing Insurance Coverage	650	0%	$4,200.00	12-Apr-22	22-Jan-24
Full-Risk property insurance		705	0%	$2,800.00	20-Mar-22	22-Feb-24
GE2180	Insurance Contract Awarded	5	0%	$0.00	20-Mar-22	24-Mar-22
GE2190	Providing Insurance Coverage	700	0%	$2,800.00	25-Mar-22	22-Feb-24
Service to Company		718	17.09%	$1,100,000.00	23-Jun-21	28-Jan-24
Camp Engineering Documents		106	0%	$0.00	20-Mar-22	03-Jul-22
HVAC/Plumbing		56	0%	$0.00	23-Mar-22	17-May-22
Drawing/Diagram		39	0%	$0.00	23-Mar-22	30-Apr-22
GE2220	Plumbing & Sewage Piping Layout	39	0%	$0.00	23-Mar-22	30-Apr-22
GE2230	HVAC System Layout	39	0%	$0.00	23-Mar-22	30-Apr-22
List		36	0%	$0.00	12-Apr-22	17-May-22
GE2240	HVAC Equipment Schedule	36	0%	$0.00	12-Apr-22	17-May-22
Safety & Fire Fighting		37	0%	$0.00	25-Mar-22	30-Apr-22
Drawing/Diagram		37	0%	$0.00	25-Mar-22	30-Apr-22
GE2250	Safety & Fire Fighting Equipment Location Layout	37	0%	$0.00	25-Mar-22	30-Apr-22
Electrical		103	0%	$0.00	23-Mar-22	03-Jul-22
Calculations		67	0%	$0.00	23-Mar-22	28-May-22
GE2260	Earthing & Lightning calculation	50	0%	$0.00	09-Apr-22	28-May-22
GE2270	Lighting Calculation	30	0%	$0.00	23-Mar-22	21-Apr-22
Drawing/Diagram		73	0%	$0.00	23-Mar-22	03-Jun-22
GE2280	Lighting & Small Power Layout For Camp Area	39	0%	$0.00	23-Mar-22	30-Apr-22
GE2290	Earthing & Lightning Layout For Camp Area	39	0%	$0.00	09-Apr-22	17-May-22
GE2300	Cable Route for For Camp Area	39	0%	$0.00	26-Apr-22	03-Jun-22
List		36	0%	$0.00	29-May-22	03-Jul-22
GE2310	Electrical Load List	36	0%	$0.00	29-May-22	03-Jul-22

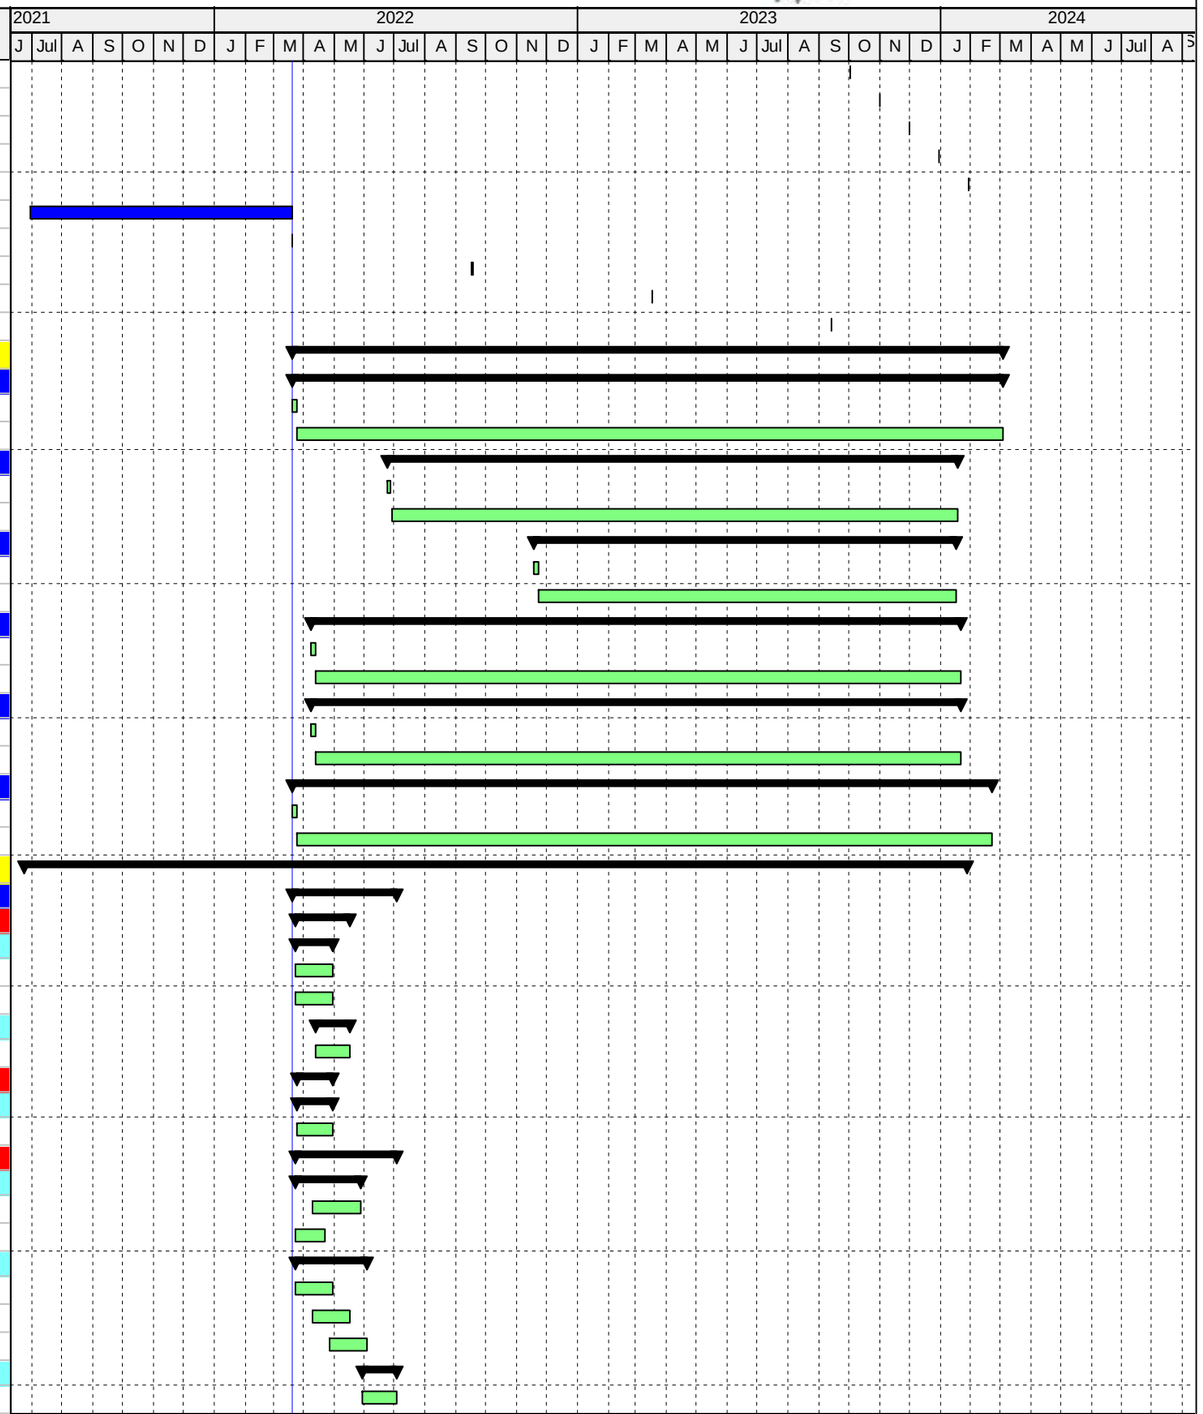

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Architecture		25	0%	$0.00	20-Mar-22	13-Apr-22
Drawing/Diagram		25	0%	$0.00	20-Mar-22	13-Apr-22
GE2320	Architectural Drawing For NISOC Office Building	25	0%	$0.00	20-Mar-22	13-Apr-22
GE2330	Architectural Drawing For NISOC Residental Building	25	0%	$0.00	20-Mar-22	13-Apr-22
GE2340	Architectural Drawing For Petro Iran Office Building	25	0%	$0.00	20-Mar-22	13-Apr-22
GE2350	Architectural Drawing For Petro Iran/Contractor Restaurant	25	0%	$0.00	20-Mar-22	13-Apr-22
GE2360	Architectural Drawing For Warehouse of Site Mobilization	25	0%	$0.00	20-Mar-22	13-Apr-22
GE2370	Architectural Drawing For Drivers Rest Room	25	0%	$0.00	20-Mar-22	13-Apr-22
GE2380	Architectural Drawing For Petro Iran Residental Building	25	0%	$0.00	20-Mar-22	13-Apr-22
Civil		56	0%	$0.00	23-Mar-22	17-May-22
Drawing/Diagram		56	0%	$0.00	23-Mar-22	17-May-22
GE2390	Overall Layout for Camp Area	39	0%	$0.00	23-Mar-22	30-Apr-22
GE2400	Rough Grading Plan For Camp Area	39	0%	$0.00	09-Apr-22	17-May-22
Structure		39	0%	$0.00	23-Mar-22	30-Apr-22
Drawing/Diagram		39	0%	$0.00	23-Mar-22	30-Apr-22
GE2410	Foundation Location Drawing For Camp Area	39	0%	$0.00	23-Mar-22	30-Apr-22
GE2420	Structural Drawing For NISOC Residental Building	39	0%	$0.00	23-Mar-22	30-Apr-22
GE2430	Structural Drawing For For Warehouse	39	0%	$0.00	23-Mar-22	30-Apr-22
Client Facilities		718	18.68%	$990,000.00	23-Jun-21	28-Jan-24
Providing Urban Facilities		663	64.61%	$49,500.00	27-Jan-22	03-Jan-24
Client Residetial		663	65.88%	$48,510.00	27-Jan-22	03-Jan-24
GE2440	Furnish	38	100%	$31,531.50	27-Jan-22	18-Apr-22
GE2450	Building Maintenance	625	2.52%	$4,851.00	27-Jan-22	03-Jan-24
GE2460	Serving Food & Dessert	625	2.52%	$12,127.50	27-Jan-22	19-Apr-22
HSE		625	2.52%	$990.00	27-Jan-22	03-Jan-24
GE2470	Personal Protection Equipment	625	2.52%	$495.00	27-Jan-22	19-Apr-22
GE2480	Fire Extinguisher Capsule	625	2.52%	$396.00	27-Jan-22	03-Jan-24
GE2490	Warning Signs	625	2.52%	$99.00	27-Jan-22	19-Apr-22
Providing Job Site Facilities		705	16.27%	$940,500.00	23-Jun-21	28-Jan-24
Serving Food & Dessert		680	2.52%	$235,125.00	27-Jan-22	19-Apr-22
GE2500	Serving Food & Dessert	680	2.52%	$235,125.00	27-Jan-22	19-Apr-22
IT Devices		25	30%	$56,430.00	27-Jan-22	18-Apr-22
GE2510	Purchase & Delivery On Site	25	30%	$56,430.00	27-Jan-22	18-Apr-22
Building Establishment		201	24.84%	$517,275.00	27-Nov-21	31-Oct-22
Camp Guard Connexes		150	20%	$2,586.38	06-Feb-22	31-Oct-22
GE25	Purchase	113	20%	$2,069.10	06-Feb-22	24-Sep-22
GE25	Furnish	38	20%	$517.28	13-Feb-22	31-Oct-22
NISOC Office Building		138	46%	$108,627.75	06-Feb-22	15-Sep-22
GE25	Construction	100	50%	$99,937.53	06-Feb-22	08-Aug-22
GE25	Furnish	38	0%	$8,690.22	09-Aug-22	15-Sep-22
NISOC Residental Building		113	18.4%	$113,800.50	27-Nov-21	24-Aug-22
GE25	Construction	75	20%	$104,696.46	27-Nov-21	17-Jul-22
GE25	Furnish	38	0%	$9,104.04	18-Jul-22	24-Aug-22
PetroIran Office Building		56	9.2%	$98,282.25	27-Nov-21	02-May-22
GE25	Construction	56	10%	$90,419.67	27-Nov-21	14-Apr-22
GE25	Furnish	19	0%	$7,862.58	14-Apr-22	02-May-22
PetroIran Residental Building		38	46%	$82,764.00	06-Feb-22	22-May-22
GE26	Construction	38	50%	$76,142.88	06-Feb-22	04-May-22
GE26	Furnish	19	0%	$6,621.12	04-May-22	22-May-22
PetroIran / Contractor Restaurant		150	0%	$75,004.88	14-Apr-22	10-Sep-22




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
GE26	Construction	94	0%	$63,754.14	14-Apr-22	16-Jul-22
GE26	Furnish	56	0%	$11,250.73	16-Jul-22	10-Sep-22
PetroIran Drivers Rest Room		81	0%	$15,518.25	14-Apr-22	04-Jul-22
GE26	Construction	56	0%	$14,276.79	14-Apr-22	09-Jun-22
GE26	Furnish	25	0%	$1,241.46	09-Jun-22	04-Jul-22
Client Parking		56	50%	$5,172.75	06-Feb-22	01-May-22
GE26	Construction	56	50%	$5,172.75	06-Feb-22	01-May-22
Other Connexe		113	47.5%	$15,518.25	06-Feb-22	04-Aug-22
GE26	Purchase	94	50%	$14,742.34	06-Feb-22	16-Jul-22
GE26	Furnish	19	0%	$775.91	16-Jul-22	04-Aug-22
Building Maintenance &Continuous Services		604	1.25%	$112,860.00	23-Jun-21	28-Jan-24
GE2690	Camp Guard Connexes	500	1.25%	$564.30	23-Jun-21	28-Jan-24
GE2700	NISOC Office Building	500	1.25%	$10,157.40	23-Jun-21	28-Jan-24
GE2710	NISOC Residental Building	500	1.25%	$11,286.00	23-Jun-21	06-Jan-24
GE2720	PetroIran Office Building	500	1.25%	$10,157.40	23-Jun-21	04-Oct-23
GE2730	PetroIran Residental Building	500	1.25%	$9,028.80	23-Jun-21	22-May-22
GE2740	PetroIran / Contractor Restaurant	500	1.25%	$9,028.80	23-Jun-21	11-Sep-22
GE2750	PetroIran Drivers Rest Room	500	1.25%	$1,128.60	23-Jun-21	04-Jul-22
GE2760	Client Parking	500	1.25%	$564.30	23-Jun-21	12-Sep-23
GE2770	Other Connexes (Well-Locations, Pipeline Route..)	500	1.25%	$1,128.60	23-Jun-21	04-Aug-22
GE2780	Providing Manpower &Machinary	500	1.25%	$59,815.80	23-Jun-21	04-Jun-22
HSE		500	1.25%	$18,810.00	23-Jun-21	24-Jan-24
GE2790	HSE Continus Service	500	1.25%	$4,702.50	23-Jun-21	15-Sep-22
GE2800	HSE Training	500	1.25%	$1,881.00	23-Jun-21	15-Sep-22
GE2810	Clinic Continus Service	500	1.25%	$9,405.00	23-Jun-21	15-Sep-22
GE2820	Personal Protection Equipment	19	1.25%	$1,504.80	23-Jun-21	15-Sep-22
GE2830	Fire Extinguisher Capsule	450	1.25%	$1,316.70	23-Jun-21	24-Jan-24
Domestic & Foreign Visits		450	2.7%	$110,000.00	23-Jun-21	09-Dec-23
GE2840	Domestic	450	3%	$99,000.00	23-Jun-21	15-Sep-22
GE2850	Foreign	450	0%	$11,000.00	15-Sep-22	09-Dec-23
Training Courses		720	0%	$50,000.00	20-Mar-22	08-Mar-24
GE2860	Holding Training Courses	720	0%	$50,000.00	20-Mar-22	08-Mar-24
EPC Contractor Mobilization & Demobilization		693	50.85%	$446,960.00	23-Jun-21	10-Feb-24
Site Establishment & Mobilization		115	78.76%	$286,054.40	25-Jul-21 A	05-Jul-22
Camp Building		90	100%	$108,700.67	25-Jul-21 A	08-Jun-22
GE2870	Construction	70	100%	$97,830.60	25-Jul-21 A	08-Jun-22
GE2880	Furnish	40	100%	$10,870.07	25-Jul-21 A	20-May-22
Office Building / Conexes		80	90%	$71,513.60	25-Jul-21 A	02-Jul-22
GE2890	Construction	70	90%	$64,362.24	25-Jul-21 A	22-Jun-22
GE2900	Furnish	35	90%	$7,151.36	25-Jul-21 A	02-Jul-22
Warehouse		71	80%	$42,908.16	25-Jul-21 A	07-Jun-22
GE2910	Construction	65	80%	$34,326.53	25-Jul-21 A	01-May-22
GE2920	Furnish	38	80%	$8,581.63	25-Jul-21 A	07-Jun-22
Parking		31	80%	$8,581.63	25-Jul-21 A	20-Apr-22
GE2930	Purchase	19	80%	$6,865.31	25-Jul-21 A	07-Apr-22
GE2940	Installation	25	80%	$1,716.33	25-Jul-21 A	20-Apr-22
Septic Tank (sewage treatment package)		31	100%	$5,721.09	25-Jul-21 A	09-Jun-22
GE2950	Purchase	19	100%	$4,576.87	25-Jul-21 A	01-Jun-22
GE2960	Installation	25	100%	$1,144.22	25-Jul-21 A	09-Jun-22

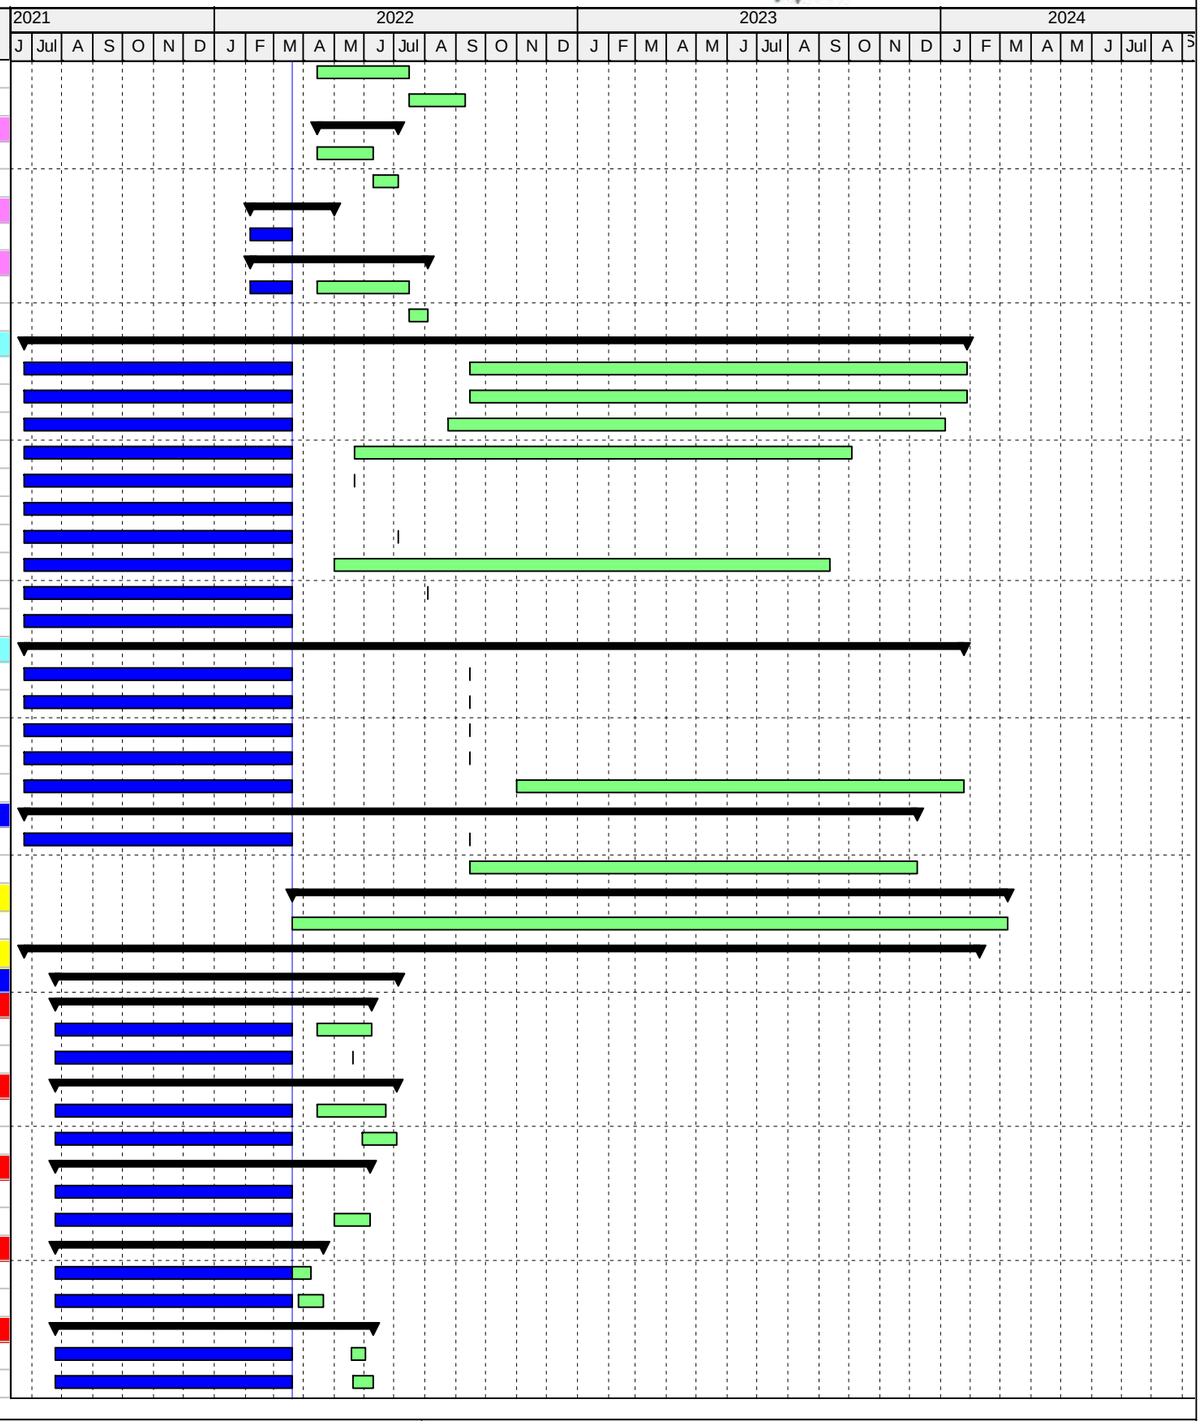

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
HSE		31	1.25%	$14,302.72	25-Jul-21 A	05-Jul-22
GE3000	Personal Protection Equipment	25	1.25%	$11,442.18	25-Jul-21 A	29-Jun-22
GE3010	Fire extinguisher Capsule	25	1.25%	$2,860.54	25-Jul-21 A	05-Jul-22
Yard Area		58	15%	$34,326.53	25-Jul-21 A	10-Jun-22
GE2970	Concrete and Geotechnics lab	19	50%	$10,297.96	25-Jul-21 A	14-Apr-22
GE2980	Piping Workshop	45	0%	$12,014.28	14-Apr-22	28-May-22
GE2990	Blasting Workshop	45	0%	$12,014.28	26-Apr-22	10-Jun-22
Site Administration & Maintenance		576	1.25%	$156,436.00	23-Jun-21	06-Jan-24
GE3020	Camp Continuous Service	550	1.25%	$54,752.60	23-Jun-21	20-Nov-23
GE3030	Office Continuous Service	550	1.25%	$46,930.80	23-Jun-21	03-Jul-22
GE3040	Concrete and Geotechnics lab	550	1.25%	$26,594.12	23-Jun-21	03-Jan-24
GE3050	Piping Workshop	550	1.25%	$12,514.88	23-Jun-21	29-May-22
GE3060	Blasting Workshop	550	1.25%	$7,821.80	23-Jun-21	10-Jun-22
GE3070	HSE Continous Service	550	1.25%	$4,693.08	23-Jun-21	06-Jan-24
GE3080	HSE Training	550	1.25%	$3,128.72	23-Jun-21	06-Jan-24
Site Demobilization		35	0%	$4,469.60	06-Jan-24	10-Feb-24
GE3090	Job Site Demobilization	35	0%	$4,469.60	06-Jan-24	10-Feb-24
SUB-Surface DEVELOPMENT		929	4.16%	$6,530,000.01	24-Jul-21 A	17-Mar-24
Package 01-New Well # W018S		649	28.48%	$318,124.00	24-Jul-21 A	13-Apr-23
ENGINEERING		449	39.32%	$8,125.00	24-Jul-21 A	13-Feb-23
Basic Design Endorsement		30	100%	$406.25	31-Jul-21 A	20-Mar-22
P01-EP	Endorsement Report For Basic Design & Scope of Work	30	100%	$406.25	31-Jul-21 A	20-Mar-22
Value Engineering		75	40.5%	$243.75	01-Feb-22	02-Jul-22
P01-EP	Value Engineering Study Report	44	60%	$164.53	01-Feb-22	02-May-22
P01-EP	HAZID Report For WHF & Flowlines	44	0%	$79.22	20-May-22	02-Jul-22
Detail Design Engineering		449	57.41%	$4,468.75	24-Jul-21 A	25-Dec-22
Process		90	59.72%	$446.88	27-Jul-21 A	08-Jun-22
Basis/Criteria		30	87%	$89.38	27-Jul-21 A	18-Apr-22
P01-E	Process Design Criteria	30	100%	$31.28	27-Jul-21 A	20-Mar-22
P01-E	Process Basis Of Design	30	80%	$58.09	27-Jul-21 A	18-Apr-22
Drawing/Diagram		90	67.6%	$111.72	30-Oct-21	03-May-22
P01-E	Symbol & Legend For PFD and P&ID	45	80%	$5.59	30-Oct-21	03-May-22
P01-E	Process Flow Diagram - W018S	45	60%	$69.27	02-Nov-21	03-May-22
P01-E	P&ID - W018S	45	80%	$36.87	01-Nov-21	03-May-22
Philosophy		75	10.81%	$67.03	21-Nov-21	02-Jun-22
P01-E	Drainage Philosophy	45	0%	$6.70	19-Apr-22	02-Jun-22
P01-E	Control Philosophy	45	0%	$16.76	19-Apr-22	02-Jun-22
P01-E	Flare,Blow Down And Relief Philosophy	45	0%	$16.76	19-Apr-22	02-Jun-22
P01-E	Isolation Philosophy	45	60%	$12.07	21-Nov-21	03-May-22
P01-E	ESD Philosophy	45	0%	$14.75	19-Apr-22	02-Jun-22
Data Sheet		36	0%	$44.69	04-May-22	08-Jun-22
P01-E	Process Data Sheets For Instrument Devices - W018S	36	0%	$44.69	04-May-22	08-Jun-22
Report		44	80%	$89.38	30-Oct-21	02-May-22
P01-E	Flowline Hydraulic Calculation Report	44	80%	$89.38	30-Oct-21	02-May-22
List		70	77.99%	$44.69	08-Nov-21	02-May-22
P01-E	Line List - W018S	44	80%	$40.22	08-Nov-21	02-May-22
P01-E	Consumption List	40	60%	$4.47	23-Feb-22	28-Apr-22
Piping		277	33.8%	$893.75	24-Jul-21 A	08-Dec-22
Basis/Criteria		39	100%	$1.79	24-Jul-21 A	20-Mar-22
P01-E	Piping Design Criteria	39	100%	$1.79	24-Jul-21 A	20-Mar-22




Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Specification		111	61.55%	$35.84	24-Jul-21 A	09-May-22
P01-E	Specification For Color Coding and Marking	30	60%	$0.36	09-Aug-21	22-Apr-22
P01-E	Specification For Transportation, Handling, Storage of pipes	30	80%	$0.36	12-Dec-21	22-Apr-22
P01-E	Specification For Metallic Pipes	30	80%	$0.36	24-Jul-21 A	22-Apr-22
P01-E	Specification For Fittings, Flanges, Gaskets and Bolts	30	100%	$0.36	24-Jul-21 A	24-Mar-22
P01-E	Specification For Painting	30	100%	$0.36	24-Jul-21 A	27-Mar-22
P01-E	Specification For Material Requirements in Sour service	30	60%	$0.36	09-Aug-21	25-Apr-22
P01-E	Specification For Manual Valves	30	60%	$0.36	09-Aug-21	25-Apr-22
P01-E	Specification For Plant Piping Systems Pressure Testing	30	60%	$0.36	09-Aug-21	25-Apr-22
P01-E	Specification For Welding of Plant Piping System	30	60%	$0.36	09-Aug-21	25-Apr-22
P01-E	Specification For Pipe Support	30	60%	$0.36	09-Aug-21	28-Apr-22
P01-E	Specification For Piping Construction, Fabrication & Erection	30	60%	$0.72	09-Aug-21	28-Apr-22
P01-E	Specification For Piping Design & Plant Layout	30	60%	$1.08	09-Aug-21	28-Apr-22
P01-E	Piping Material Specification	30	60%	$30.11	28-Nov-21	28-Apr-22
P01-E	Specification For Piping Cleaning and Flushing	30	100%	$0.36	24-Aug-21	09-May-22
Procedure/Plan		39	100%	$1.79	24-Jul-21 A	03-Apr-22
P01-E	3D-Model (PDMS) Review Procedure	39	100%	$1.79	24-Jul-21 A	03-Apr-22
Data Sheets		39	60%	$2.68	27-Dec-21	12-May-22
P01-E	Data Sheets For Stone Trap	39	60%	$2.68	27-Dec-21	12-May-22
Drawing/Diagram		234	41.99%	$206.19	22-Aug-21	08-Dec-22
P01-E	Standard Pipe Support Drawings	14	100%	$6.19	19-Feb-22	20-Mar-22
P01-E	Piping Assembly Drawing	40	0%	$20.62	13-May-22	21-Jun-22
P01-E	Piping Hydrostatic Test Diagram - Sub Surface	40	0%	$4.12	22-Jun-22	31-Jul-22
P01-E	Plot Plan Drawing - W018S	40	80%	$61.86	22-Aug-21	28-Apr-22
P01-E	Piping Plan - W018S	40	0%	$37.11	20-Sep-22	29-Oct-22
P01-E	Isometric Drawings - W018S	40	0%	$24.74	30-Oct-22	08-Dec-22
P01-E	Material Flow Diagram - W018S	35	60%	$51.55	08-Nov-21	12-May-22
List		44	0%	$35.84	29-Apr-22	11-Jun-22
P01-E	Piping Support List - W018S	44	0%	$17.92	29-Apr-22	11-Jun-22
P01-E	Critical Line List - W018S	39	0%	$17.92	03-May-22	10-Jun-22
Report		90	6%	$448.22	28-Nov-21	19-Sep-22
P01-E	PDMS Model Review Report (60%) - W018S	45	0%	$246.52	22-Jun-22	05-Aug-22
P01-E	PDMS Model Review Report (90%) - W018S	45	0%	$156.88	06-Aug-22	19-Sep-22
P01-E	Piping Corrosion Study & Material Selection Report	40	60%	$44.82	28-Nov-21	12-May-22
MTO		52	100%	$161.41	04-Dec-21	20-Sep-22
P01-E	MTO For Pipes - W018S	7	100%	$28.25	04-Dec-21	06-Aug-22
P01-E	MTO For Fittings - W018S	7	100%	$26.63	20-Dec-21	20-Sep-22
P01-E	MTO For Flanges - W018S	7	100%	$26.63	20-Dec-21	20-Sep-22
P01-E	MTO For Manual Valves - W018S	7	100%	$26.63	20-Dec-21	06-Aug-22
P01-E	MTO For Gaskets - W018S	7	100%	$26.63	20-Dec-21	20-Sep-22
P01-E	MTO For Bolt & Nuts - W018S	7	100%	$26.63	20-Dec-21	20-Sep-22
Pipeline & Flow line		182	40.47%	$134.06	24-Jul-21 A	25-Jul-22
Basis/Criteria		39	100%	$0.94	28-Aug-21	20-Mar-22
P01-E	Pipeline Design Criteria	39	100%	$0.94	28-Aug-21	20-Mar-22
Specification		49	81.59%	$13.07	24-Jul-21 A	07-May-22
P01-E	Specification For Line Pipes	39	100%	$0.26	24-Jul-21 A	24-Mar-22
P01-E	Specification For Pipeline Cold Bending	39	80%	$0.26	28-Aug-21	01-May-22
P01-E	Specification For Barred Tee	39	80%	$0.26	28-Aug-21	01-May-22
P01-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$0.26	24-Jul-21 A	24-Mar-22

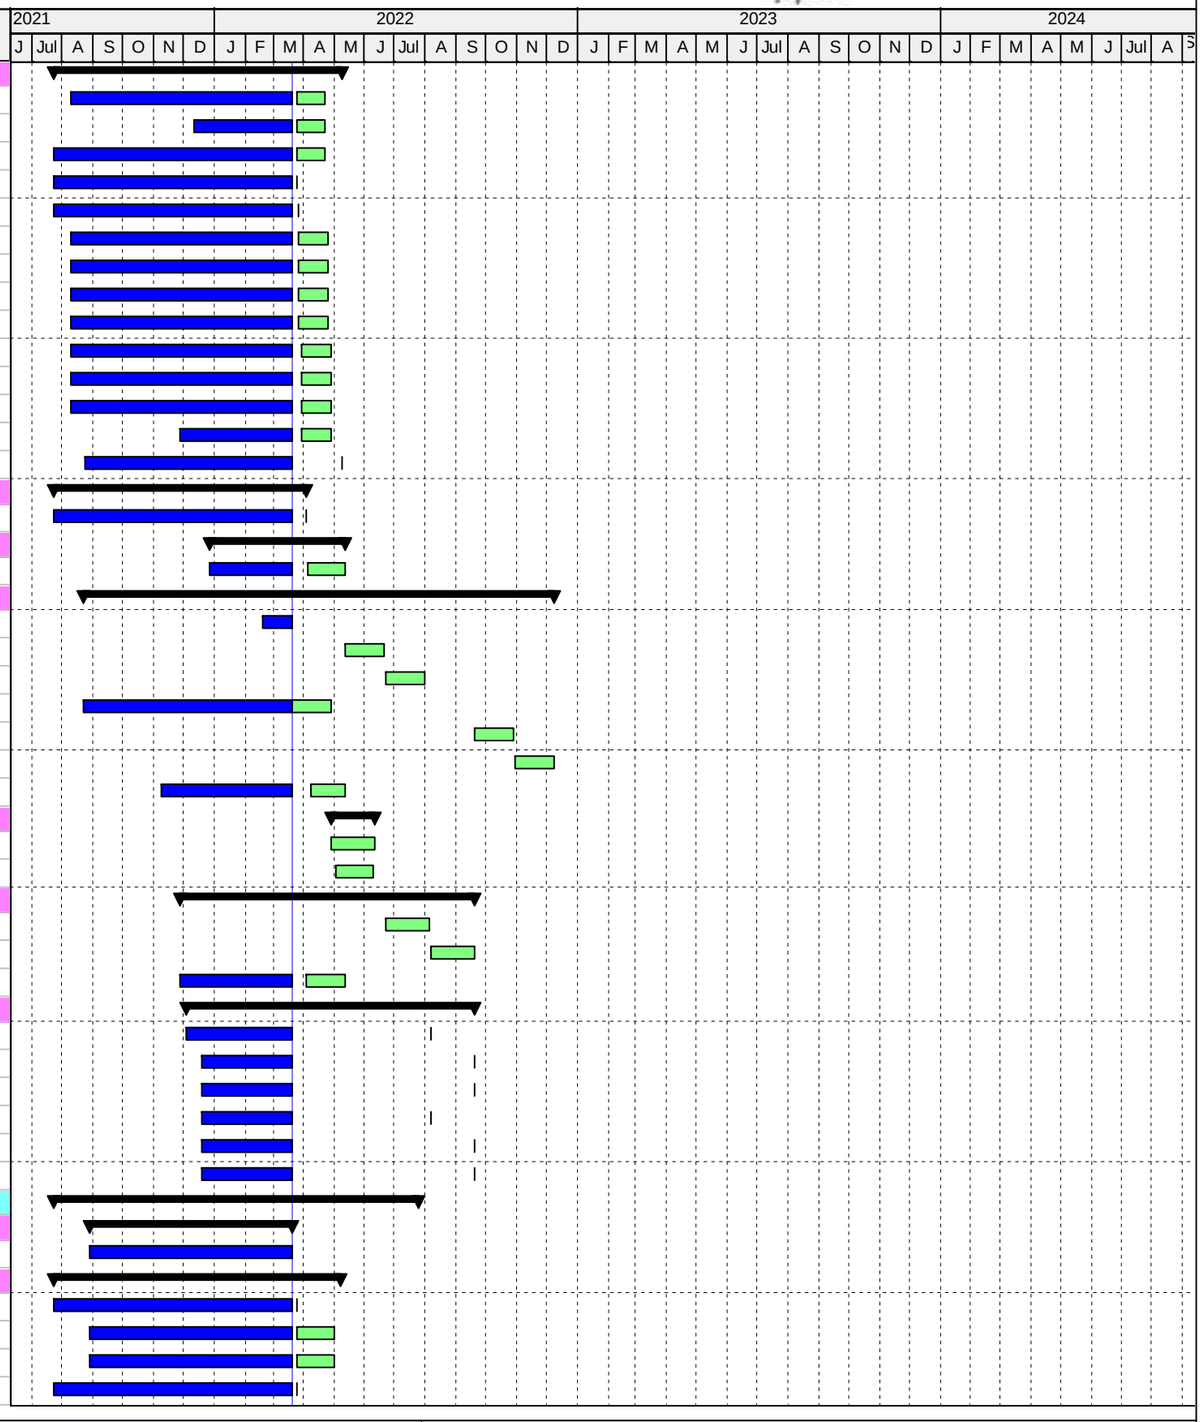


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P01-E	Specification For Pipeline Valves	39	80%	$0.26	28-Aug-21	01-May-22
P01-E	Specification For Pipeline Coating	39	100%	$0.26	24-Jul-21 A	24-Mar-22
P01-E	Specification For Pipeline Flushing, Cleaning And Hydrostatic	39	100%	$0.26	24-Jul-21 A	27-Mar-22
P01-E	Specification For Welding of Transportation Pipeline	39	80%	$0.26	12-Dec-21	04-May-22
P01-E	Specification For Pipeline Stress Analysis	39	80%	$0.26	24-Jul-21 A	04-May-22
P01-E	Specification For Pipeline Insulation Joint	39	100%	$0.26	24-Jul-21 A	27-Mar-22
P01-E	Specification For Pipeline Construction	39	80%	$0.26	25-Jan-22	04-May-22
P01-E	Specification For Anchor Flanges	39	80%	$0.26	28-Aug-21	07-May-22
P01-E	Specification For Pigs	39	80%	$0.26	28-Aug-21	07-May-22
P01-E	Pipeline Material Specification	44	80%	$9.41	27-Oct-21	02-May-22
P01-E	Specification For Pipeline Cleaning and Flushing	39	60%	$0.26	24-Jul-21 A	07-May-22
Drawing/Diagram		84	25.01%	$74.30	27-Jul-21 A	22-May-22
P01-E	Pipeline Standard Support Drawings	14	100%	$2.97	27-Jul-21 A	20-Mar-22
P01-E	Standard Drawing For Above Ground Pipeline Construction F	44	80%	$2.97	27-Nov-21	12-May-22
P01-E	Standard Drawing For Under Ground Pipeline Construction F	44	100%	$2.97	04-Dec-21	30-Mar-22
P01-E	Pipeline Standard Drawing For Anchor Support	44	60%	$2.23	22-Dec-21	12-May-22
P01-E	Standard Drawing For A/G Pipeline Road Crossing	44	60%	$2.23	05-Dec-21	12-May-22
P01-E	Standard Drawing For Existing Pipeline Crossing	44	60%	$2.23	18-Dec-21	12-May-22
P01-E	Pipeline Standard Drawing For Irish Crossing	44	60%	$2.23	04-Dec-21	12-May-22
P01-E	Pipeline Standard Drawing For Water - Way Crossing	44	60%	$2.23	22-Nov-21	12-May-22
P01-E	Pipeline Standard Drawing For Pig Signaller Concrete Pit	44	60%	$2.23	27-Nov-21	12-May-22
P01-E	Pipeline Standard Drawing For H-Pipe Support	44	100%	$2.23	27-Nov-21	30-Mar-22
P01-E	Flowline Transversal Drawings - W018S	64	0%	$49.78	20-Mar-22	22-May-22
Procedure/Plan		44	0%	$2.71	09-Apr-22	22-May-22
P01-E	Pipeline Hydrostatic Test Diagram - Sub Surface	44	0%	$2.71	09-Apr-22	22-May-22
List		64	0%	$14.71	23-May-22	25-Jul-22
P01-E	Road Crossing Location List	64	0%	$14.71	23-May-22	25-Jul-22
Report		44	80%	$21.34	27-Oct-21	22-May-22
P01-E	Pipeline Corrosion Study & Material Selection Report	44	80%	$21.34	27-Oct-21	22-May-22
MTO		30	100%	$7.00	22-Aug-21	20-Mar-22
P01-E	MTO For Line Pipes (Flowlines) - W018S	30	100%	$7.00	22-Aug-21	20-Mar-22
Control & Instrumentation		279	88.39%	$357.50	26-Jul-21 A	05-Aug-22
Basis/Criteria		44	93.99%	$15.84	14-Aug-21	29-Apr-22
P01-E	Fire & Gas Detection Design Criteria	38	100%	$13.46	14-Aug-21	27-Mar-22
P01-E	Instrument & Control System Design Criteria	38	60%	$2.38	03-Jan-22	29-Apr-22
Specification		42	87%	$81.33	26-Jul-21 A	26-Apr-22
P01-E	Specification For Instrumentation	39	100%	$28.47	26-Jul-21 A	23-Mar-22
P01-E	Specification For WHCP/HPU	38	80%	$52.87	08-Aug-21	26-Apr-22
Data Sheets		118	80%	$20.34	22-Aug-21	12-May-22
P01-E	Data Sheets For WHCP/HPU - Wellheads	30	80%	$10.17	22-Aug-21	18-Apr-22
P01-E	Data Sheets For Pressure Gauge - Wellheads	30	80%	$5.09	07-Dec-21	12-May-22
P01-E	Data Sheets For Temperature Gauge - Wellheads	30	80%	$5.09	07-Dec-21	12-May-22
Drawing/Diagram		239	68.99%	$83.58	22-Aug-21	05-Aug-22
P01-E	Instrument Hook-up Diagram - Wellheads	42	80%	$12.54	14-Nov-21	12-May-22
P01-E	WHCP Hydraulic \Peneumatic Diagrams - Wellheads	42	100%	$12.54	22-Aug-21	19-Apr-22
P01-E	Instrument Location Layout Drawing - W018S	54	60%	$58.51	23-Feb-22	05-Aug-22
List		7	100%	$43.40	10-Nov-21	13-May-22
P01-E	Instrument Index For New Wells & Manifold Extension	7	100%	$43.40	10-Nov-21	13-May-22
MTO		80	100%	$113.01	14-Nov-21	13-May-22

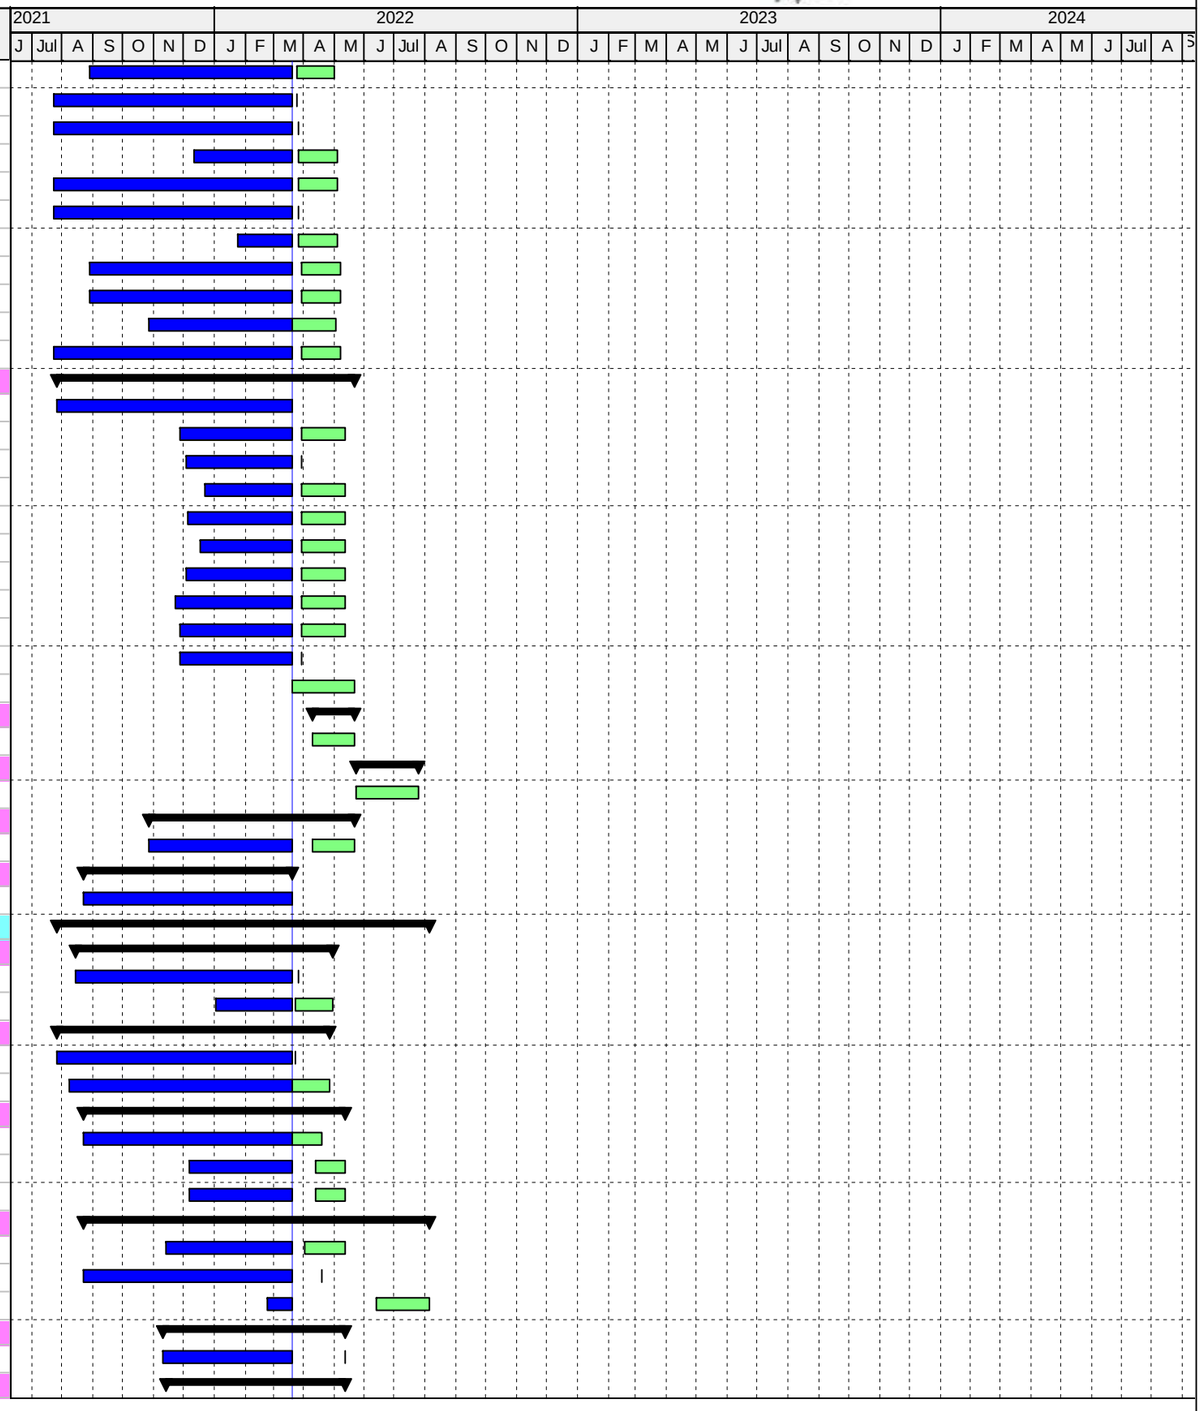


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P01-E	MTO For Instrument Tube and Fitting - W018S	30	100%	$56.50	14-Nov-21	13-May-22
P01-E	MTO For Instrument Cable Tray - W018S	30	100%	$56.50	14-Nov-21	04-May-22
Safety		194	85.36%	$134.06	24-Jul-21 A	23-May-22
Basis/Criteria		44	100%	$13.41	29-Aug-21	27-Mar-22
P01-E	Active Fire Protection and Safety Concept	44	100%	$13.41	29-Aug-21	27-Mar-22
Specification		47	93.61%	$26.81	24-Jul-21 A	06-May-22
P01-E	Specification For Fire Fighting Equipment	44	100%	$4.29	29-Aug-21	24-Mar-22
P01-E	Specification For Hazardous Area Classification	44	100%	$4.29	24-Jul-21 A	24-Mar-22
P01-E	Specification For Environmental Job	44	60%	$4.29	11-Aug-21	06-May-22
P01-E	Specification For Safety Equipment	44	100%	$6.97	29-Aug-21	27-Mar-22
P01-E	Specification For Safety Signs	44	100%	$6.97	24-Jul-21 A	27-Mar-22
Data Sheets		47	100%	$13.41	08-Dec-21	27-Mar-22
P01-E	Data Sheets For Fire Fighting Equipment	44	100%	$4.56	08-Dec-21	24-Mar-22
P01-E	Data Sheets For Safety Equipment	44	100%	$4.42	08-Dec-21	27-Mar-22
P01-E	Data Sheets For Safety Sign	44	100%	$4.42	08-Dec-21	27-Mar-22
Drawing/Diagram		146	71.6%	$53.63	29-Aug-21	22-May-22
P01-E	Typical Installation Detail for Safety & Fire Fighting Equipment	14	100%	$4.02	29-Dec-21	27-Mar-22
P01-E	Symbol & Legend For Safety & Firefighting Systems	44	100%	$4.02	29-Aug-21	27-Mar-22
P01-E	Hazardous Area Classification Layout - W018S	64	60%	$15.28	15-Nov-21	22-May-22
P01-E	Safety & Fire Fighting Equipment Location Layout - W018S	64	80%	$15.02	07-Sep-21	22-May-22
P01-E	Escape Route & Safety Sign Layout - W018S	64	60%	$15.28	15-Nov-21	22-May-22
List		64	80%	$13.41	09-Nov-21	22-May-22
P01-E	Hazard Source List - W018S	64	80%	$13.41	09-Nov-21	22-May-22
MTO		30	100%	$13.41	15-Nov-21	23-May-22
P01-E	MTO For Safety Sign - W018S	30	100%	$5.36	15-Nov-21	23-May-22
P01-E	MTO For Fire Fighting & Safety Equipment - W018S	30	100%	$8.04	15-Nov-21	23-May-22
Architecture		100	60%	$134.06	18-Dec-21	01-Jun-22
Basis/Criteria		74	60%	$26.81	08-Feb-22	01-Jun-22
P01-E	Architectural Design Criteria	74	60%	$26.81	08-Feb-22	01-Jun-22
Drawing/Diagram		100	60%	$107.25	18-Dec-21	18-May-22
P01-E	Architectural Drawing For WHCP/HPU Shelter of Well Pads -	60	60%	$77.22	21-Feb-22	18-May-22
P01-E	Standard Drawing for Architectural Details	60	60%	$30.03	18-Dec-21	18-May-22
Civil		449	75.06%	$804.38	28-Jul-21 A	25-Dec-22
Basis/Criteria		90	20%	$2.98	13-Feb-22	22-May-22
P01-E	Civil Design Criteria	64	60%	$0.99	13-Feb-22	22-May-22
P01-E	Design Criteria for Sewerage & Drainage	44	0%	$0.99	24-Mar-22	06-May-22
P01-E	Design Criteria for Road and Paving	44	0%	$0.99	27-Mar-22	09-May-22
Specification		94	72.14%	$15.04	09-Aug-21	06-Jun-22
P01-E	Specification For Civil Works	79	0%	$1.50	20-Mar-22	06-Jun-22
P01-E	Specification For Road & Paving	64	80%	$3.01	09-Aug-21	22-May-22
P01-E	Specification For Fence & Gate	64	100%	$3.01	18-Sep-21	20-Mar-22
P01-E	Specification For Earth Work	64	80%	$3.01	09-Aug-21	22-May-22
P01-E	Specification For Sewerage & Drainage	64	100%	$3.01	09-Aug-21	20-Mar-22
P01-E	Specification For Geological & Geotechnical Survey	44	0%	$1.50	20-Mar-22	02-May-22
Drawing/Diagram		108	84.4%	$641.89	28-Jul-21 A	05-Jun-22
P01-E	Standard Drawing For Civil Works	64	0%	$12.84	30-Mar-22	01-Jun-22
P01-E	Standard Drawing For Slope Protection Details	64	100%	$12.84	22-Aug-21	30-Mar-22
P01-E	Standard Drawing For Roads	64	80%	$12.84	22-Aug-21	01-Jun-22
P01-E	Standard Drawing For Electrical Cable Trench	64	100%	$12.84	22-Aug-21	30-Mar-22

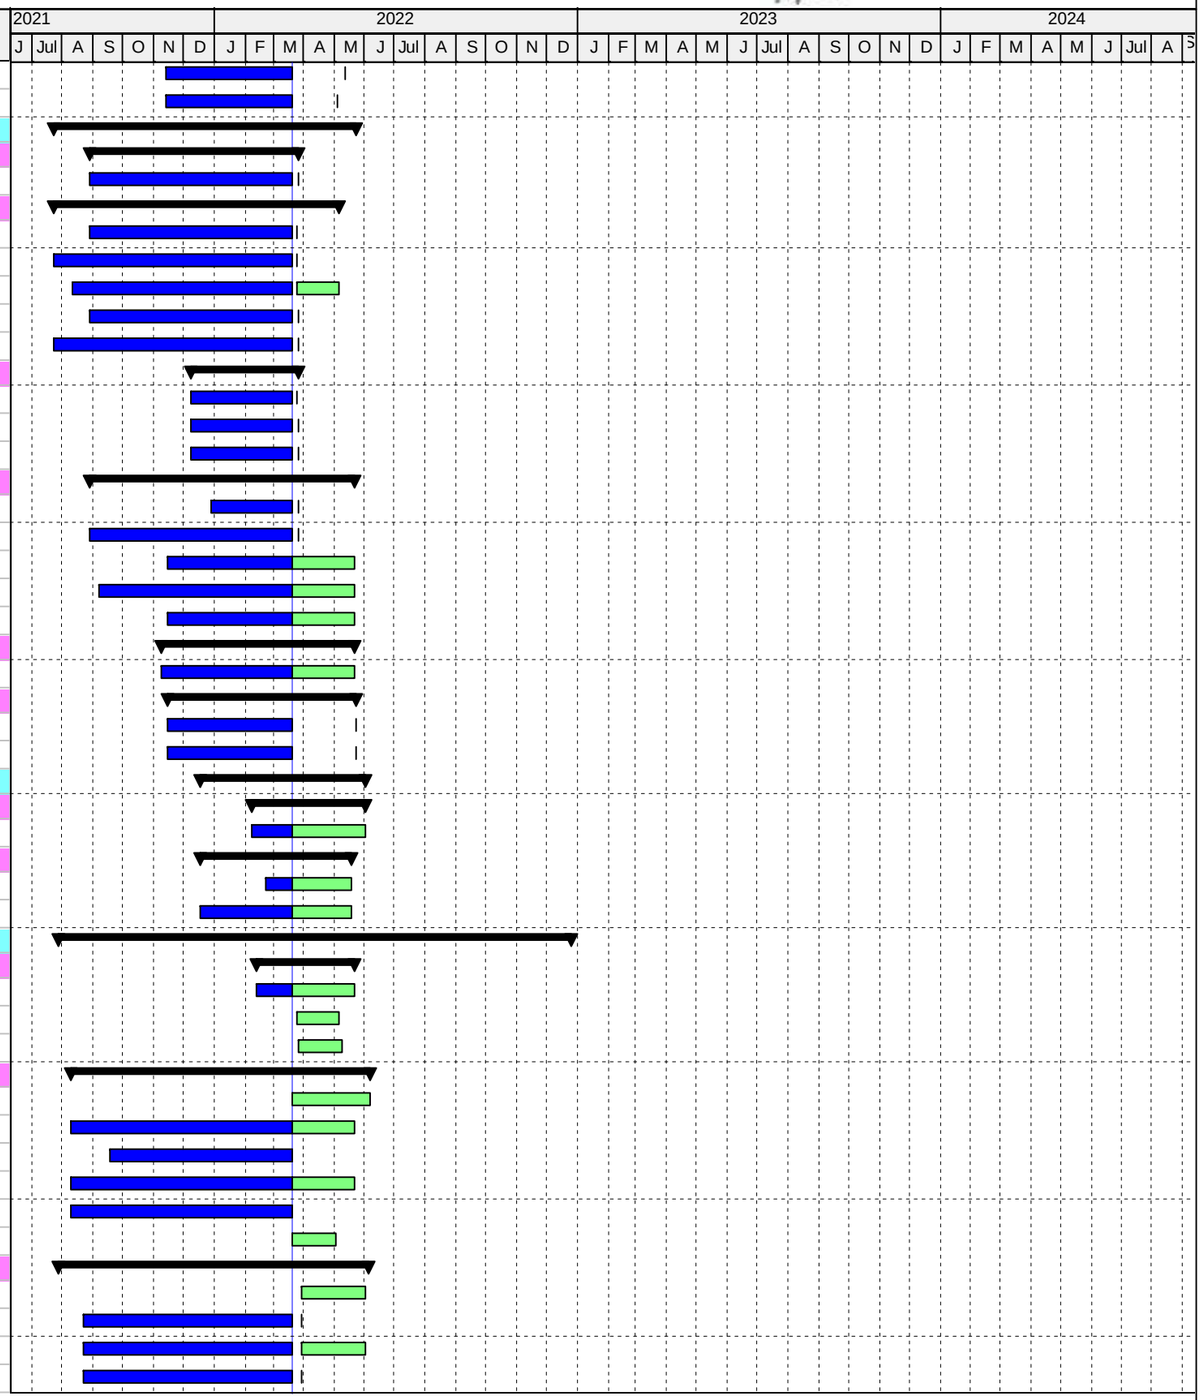


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P01-E	Standard Drawing For Manholes	64	80%	$12.84	22-Aug-21	01-Jun-22
P01-E	Standard Drawing For Catch Basins	64	80%	$12.84	22-Aug-21	05-Jun-22
P01-E	Standard Drawing For Sewerage & Drainage Details	64	60%	$12.84	02-Feb-22	05-Jun-22
P01-E	Standard Drawing For Civil Underground Crossings	38	60%	$19.26	07-Feb-22	10-May-22
P01-E	Standard Drawing For Fence & Gate Details	64	100%	$12.84	18-Sep-21	03-Apr-22
P01-E	Standard Drawing For Concrete Continues Weight	38	100%	$19.26	01-Aug-21	20-Mar-22
P01-E	Standard Drawing For Major Floodway Crossing	38	0%	$19.26	03-Apr-22	10-May-22
P01-E	Standard Drawing For Culvert & Details	38	100%	$19.26	25-Sep-21	03-Apr-22
P01-E	Standard Drawing For Valve Box	38	100%	$19.26	12-Jan-22	03-Apr-22
P01-E	Standard Drawing For Fire Hydrant Pit	38	60%	$19.26	13-Mar-22	10-May-22
P01-E	Standard Drawing For Cable Pull Pit	40	0%	$12.84	03-Apr-22	12-May-22
P01-E	Standard Drawing For Pavings	38	60%	$19.26	08-Jan-22	10-May-22
P01-E	Standard Drawing For Earth Pit	38	60%	$19.26	13-Feb-22	10-May-22
P01-E	Standard Detail For Pipe Bedding	40	100%	$12.84	22-Aug-21	03-Apr-22
P01-E	Standard Details of Miscellaneous Items	40	60%	$12.84	06-Mar-22	12-May-22
P01-E	BINAK Oil Field Project Overall Well Location/Facilities Layout	38	0%	$6.42	20-Mar-22	26-Apr-22
P01-E	General Civil Layout - W018S	20	100%	$128.38	28-Jul-21 A	29-Apr-22
P01-E	Civil and Structural drawings - W018S	40	100%	$128.38	28-Jul-21 A	04-Apr-22
P01-E	Rough Grading Plans -W018S	40	100%	$83.45	30-Oct-21	25-Mar-22
Calculation		364	70%	$72.23	05-Dec-21	25-Dec-22
P01-E	Calculation Note For Heli Pad, Well Pad & Diesel Storage Pac	38	60%	$36.12	19-Feb-22	11-May-22
P01-E	Calculation Note For Flood Control	39	80%	$36.12	05-Dec-21	25-Dec-22
MTO		7	0%	$72.23	29-Apr-22	05-May-22
P01-E	MTO For Civil Works - W018S	7	0%	$72.23	29-Apr-22	05-May-22
Structure		111	38.66%	$491.56	08-Aug-21	08-Jul-22
Basis/Criteria		64	0%	$5.36	20-Mar-22	22-May-22
P01-E	Structural Design Criteria	64	0%	$1.79	20-Mar-22	22-May-22
P01-E	Design Criteria For Steel Structure	44	0%	$1.79	20-Mar-22	02-May-22
P01-E	Design Criteria For Load & Forces	44	0%	$1.79	20-Mar-22	02-May-22
Specification		98	78.39%	$40.95	14-Aug-21	26-May-22
P01-E	Specification For Concrete Work	64	80%	$7.37	14-Aug-21	26-May-22
P01-E	Specification for Fabrication of Steel Structures	64	100%	$9.42	24-Jan-22	24-Mar-22
P01-E	Specification For Grouting	64	100%	$7.37	14-Aug-21	24-Mar-22
P01-E	Specification for Erection of Steel Structures	64	100%	$9.42	24-Jan-22	24-Mar-22
P01-E	Specification For Steel Structural Works	37	0%	$7.37	20-Mar-22	25-Apr-22
Drawing/Diagram		98	49.81%	$317.01	08-Aug-21	01-Jul-22
P01-E	Standard Drawing For Fire Proofing	64	100%	$6.34	08-Aug-21	03-Apr-22
P01-E	Standard Drawing For Anchor Bolts	64	100%	$6.34	15-Dec-21	03-Apr-22
P01-E	Standard Drawing For Steel Stairs	64	100%	$6.34	18-Dec-21	03-Apr-22
P01-E	Standard Drawing For Operating Platform	38	100%	$6.34	27-Dec-21	30-Mar-22
P01-E	Standard Drawing For Handrail	38	100%	$9.51	18-Dec-21	30-Mar-22
P01-E	Standard Drawing For Insert Plates in Concrete	38	100%	$9.51	08-Aug-21	30-Mar-22
P01-E	Standard Details For Ladder & Safety Cage	64	100%	$6.34	15-Dec-21	03-Apr-22
P01-E	Standard Drawing For Lighting pole foundation Plan & Details	38	60%	$9.51	29-Jan-22	06-May-22
P01-E	General Notes - Steel Structures	38	100%	$6.34	25-Jan-22	30-Mar-22
P01-E	General Notes - Reinforced Concrete Structures	38	100%	$9.51	20-Dec-21	30-Mar-22
P01-E	Standard Drawing For Structural Built-up Sections	44	80%	$9.51	04-Dec-21	12-May-22
P01-E	Standard Drawing For Steel Flooring, Grating and Chequere	44	100%	$9.51	05-Jan-22	30-Mar-22
P01-E	Concrete Reinforcement Shape Code	44	0%	$9.51	30-Mar-22	12-May-22

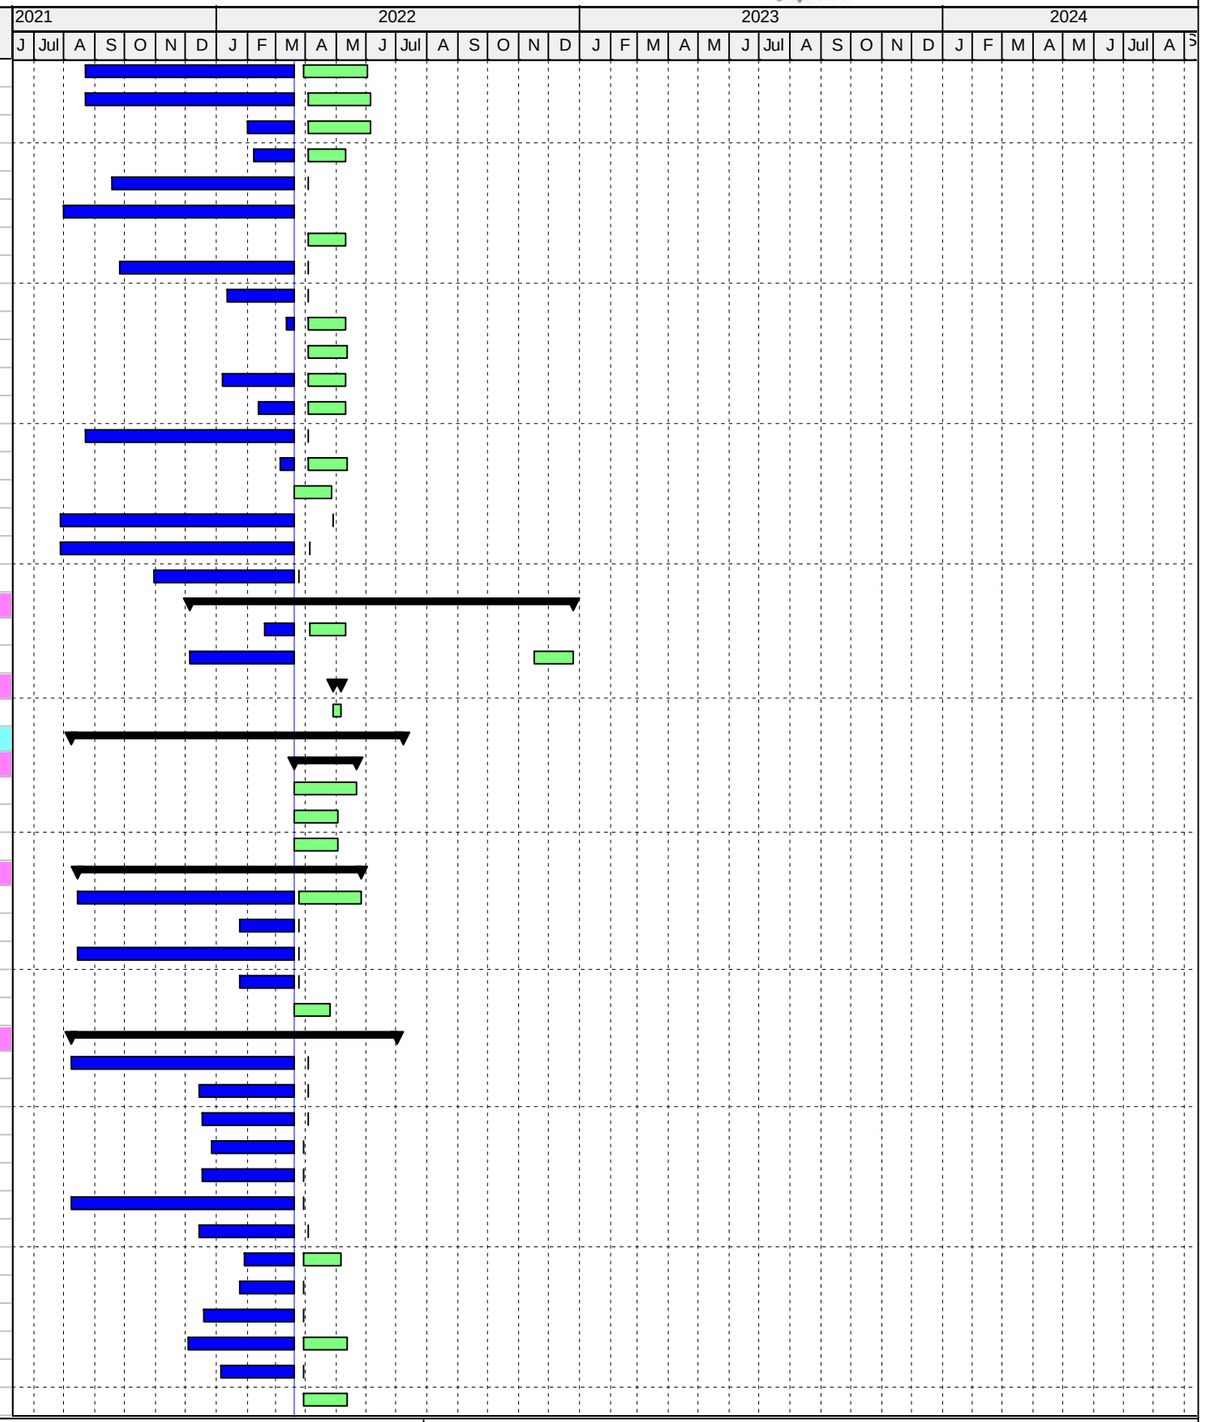


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P01-E	Standard Drawing For Septic Tank	44	80%	$9.51	22-Jan-22	12-May-22
P01-E	Structure Drawing For WHCP/HPU Shelter - W018S	44	0%	$101.44	19-May-22	01-Jul-22
P01-E	Platform Structure Drawing - W018S	44	60%	$101.44	17-Apr-22	02-May-22
MTO		7	0%	$128.25	02-Jul-22	08-Jul-22
P01-E	MTO For Structural Works - W018S	7	0%	$128.25	02-Jul-22	08-Jul-22
General		116	59.46%	$1,072.50	11-Aug-21	13-Jul-22
Risk Assessment		44	100%	$53.63	05-Sep-21	20-Mar-22
Procedure/Plan		44	100%	$53.63	05-Sep-21	20-Mar-22
P01-	HAZID Study Procedure	44	100%	$53.63	05-Sep-21	20-Mar-22
Survey (Topography) & Geotechnic		50	62.82%	$911.63	11-Aug-21	07-Jun-22
Geotechnic		44	63.2%	$804.38	11-Aug-21	19-Apr-22
Procedure/Plan		44	100%	$64.35	11-Aug-21	19-Apr-22
P01	Geotechnical Investigation Plan for Well Pads	44	100%	$64.35	11-Aug-21	19-Apr-22
Report		44	60%	$740.03	26-Feb-22	19-Apr-22
P01	Geotechnical Investigation Report - W018S	44	60%	$740.03	26-Feb-22	19-Apr-22
Survey		30	60%	$107.25	26-Feb-22	07-Jun-22
Drawing/Diagram		30	60%	$107.25	26-Feb-22	07-Jun-22
P01	Flowline Plan & Profile Drawings - W018S	30	60%	$107.25	26-Feb-22	07-Jun-22
QC/QA		116	10.59%	$107.25	20-Sep-21	13-Jul-22
QC Management		116	39.14%	$8.72	08-Dec-21	13-Jul-22
P01-	Project Audit Procedure	44	0%	$0.44	20-Mar-22	02-May-22
P01-	Specification For Final Data Book (FDB) Requirements	44	0%	$0.44	20-Mar-22	02-May-22
P01-	Non Conformance Control Procedure	36	0%	$0.44	03-May-22	07-Jun-22
P01-	Corrective Action Procedure	36	0%	$0.44	08-Jun-22	13-Jul-22
P01-	Material Reciving, Storage, Handling Procedure	39	60%	$0.44	20-Feb-22	27-Apr-22
P01-	Packing, Marking, Transportation Procedure	39	0%	$0.44	20-Mar-22	27-Apr-22
P01-	Criticality Assessment Procedure	39	0%	$1.74	20-Mar-22	27-Apr-22
P01-	Project Quality Plan	44	80%	$3.92	08-Dec-21	02-May-22
P01-	Technical Query Procedure	44	0%	$0.44	30-Mar-22	12-May-22
QC General Document		55	8.57%	$12.73	28-Nov-21	16-May-22
P01-	Quality Control Plan (QCP)	39	60%	$1.82	28-Nov-21	27-Apr-22
P01-	Specification for Welding Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P01-	Heat Treatment Procedure (Pre Heating , PWHT)	44	0%	$1.82	03-Apr-22	16-May-22
P01-	Welder Performance Qualification Test (WQT) Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P01-	NDT Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P01-	Surface Preparation and Coating/Painting Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P01-	Control of Inspection Measuring and Test Equipment Procedu	44	0%	$1.81	03-Apr-22	16-May-22
QC Discipline Document		81	7.99%	$85.80	20-Sep-21	16-May-22
Piping		51	0%	$21.45	27-Mar-22	16-May-22
P01	ITP For Piping Works	44	0%	$2.15	27-Mar-22	09-May-22
P01	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$2.41	03-Apr-22	16-May-22
P01	PIPING WPS (Welding Procedure Specification)	44	0%	$2.41	03-Apr-22	16-May-22
P01	PIPING PQR (Procedure Qualification Record)	44	0%	$2.41	03-Apr-22	16-May-22
P01	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$2.41	03-Apr-22	16-May-22
P01	PIPING WPS (Preliminary Welding Procedure Specification) f	44	0%	$2.41	03-Apr-22	16-May-22
P01	PIPING PQR (Procedure Qualification Record) for Repair We	44	0%	$2.41	03-Apr-22	16-May-22
P01	Field Joint Coating Procedure For Pipeline	44	0%	$2.41	03-Apr-22	16-May-22
P01	Pressure Test Procedure	44	0%	$2.41	03-Apr-22	16-May-22
Telecomm.		44	0%	$4.29	27-Mar-22	09-May-22
P01	ITP For Telecommunication Installation	44	0%	$4.29	27-Mar-22	09-May-22

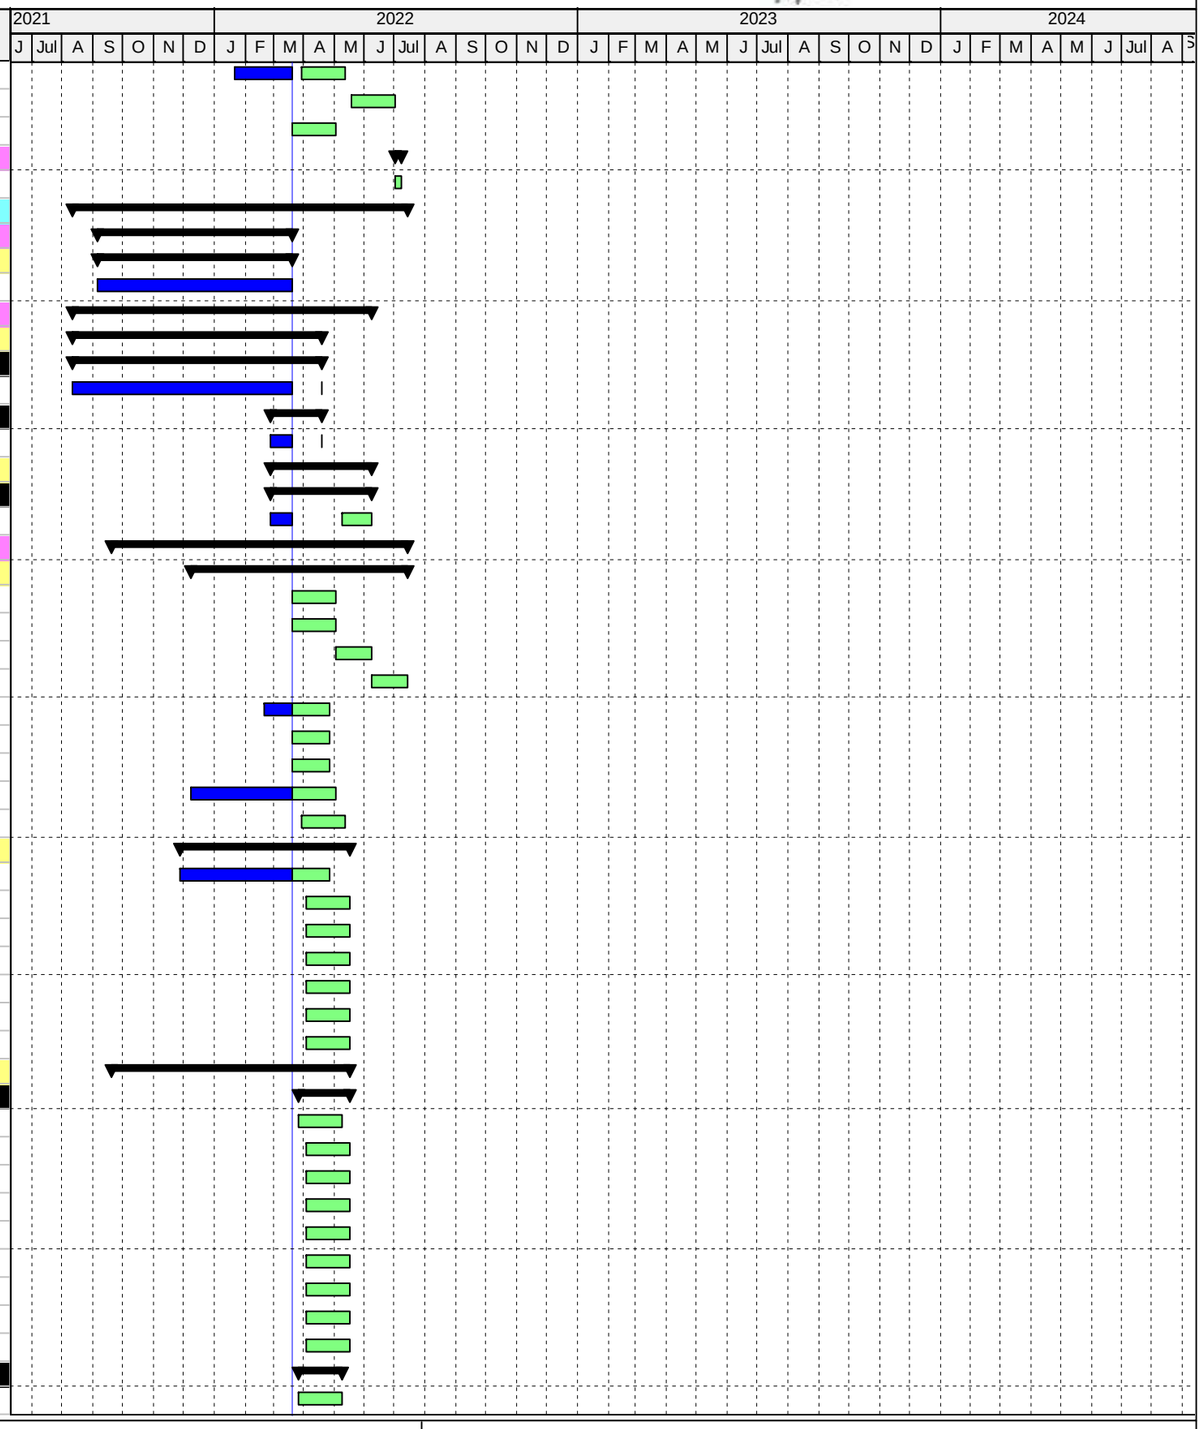


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Safety		44	0%	$4.29	27-Mar-22	09-May-22
P01	ITP For Safety Installation	44	0%	$4.29	27-Mar-22	09-May-22
Architectural		44	0%	$4.29	27-Mar-22	09-May-22
P01	ITP For Architectural Works	44	0%	$4.29	27-Mar-22	09-May-22
Mechanical		44	0%	$4.29	27-Mar-22	09-May-22
P01	ITP For Mechanical Installation	44	0%	$4.29	27-Mar-22	09-May-22
Structure		51	0%	$17.16	27-Mar-22	16-May-22
P01	ITP For Steel Structural Works	44	0%	$1.72	27-Mar-22	09-May-22
P01	Steel Structure WPS (Welding Procedure Specification)	44	0%	$2.57	03-Apr-22	16-May-22
P01	Steel Structure PQR (Procedure Qualification Record)	44	0%	$2.57	03-Apr-22	16-May-22
P01	Steel Structure WPS (Welding Procedure Specification) For F	44	0%	$2.57	03-Apr-22	16-May-22
P01	Steel Structure PQR (Procedure Qualification Record) For R	44	0%	$2.57	03-Apr-22	16-May-22
P01	Weld Map For Steel Structures	44	0%	$2.57	03-Apr-22	16-May-22
P01	NDT Plan For steel Structures	44	0%	$2.57	03-Apr-22	16-May-22
Instrumentation		44	0%	$4.29	27-Mar-22	09-May-22
P01	ITP For I&C Installation	44	0%	$4.29	27-Mar-22	09-May-22
Pipeline		74	15%	$17.16	16-Jan-22	16-May-22
P01	ITP For Pipeline	44	60%	$1.72	16-Jan-22	09-May-22
P01	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	60%	$2.57	23-Feb-22	16-May-22
P01	PIPELINE WPS (Welding Procedure Specification)	44	0%	$2.57	03-Apr-22	16-May-22
P01	PIPELINE PQR (Procedure Qualification Record)	44	0%	$2.57	03-Apr-22	16-May-22
P01	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	0%	$2.57	03-Apr-22	16-May-22
P01	PIPELINE WPS (Preliminary Welding Procedure Specificatior	44	0%	$2.57	03-Apr-22	16-May-22
P01	PIPELINE PQR (Procedure Qualification Record) for Repair \	44	0%	$2.57	03-Apr-22	16-May-22
Civil		44	100%	$4.29	20-Sep-21	27-Mar-22
P01	ITP For Civil Works	44	100%	$4.29	20-Sep-21	27-Mar-22
Electrical		44	0%	$4.29	27-Mar-22	09-May-22
P01	ITP For Electrical Installation	44	0%	$4.29	27-Mar-22	09-May-22
Procurement Engineering		334	15.29%	$812.50	15-Nov-21	25-Nov-22
Piping		289	7.24%	$211.25	06-Dec-21	25-Nov-22
Pipes		130	10.02%	$23.49	06-Dec-21	01-Oct-22
P01-E	PMR For Pipes - W018S	7	100%	$2.35	06-Dec-21	06-Aug-22
P01-E	TBE For Pipes - W018S	20	0%	$3.52	06-Aug-22	25-Aug-22
P01-E	VDR For Pipes - W018S	25	0%	$17.62	07-Sep-22	01-Oct-22
Manual Valves		150	15.04%	$23.47	13-Feb-22	18-Sep-22
P01-E	PMR For Manual Valves - W018S	7	0%	$2.35	06-Aug-22	12-Aug-22
P01-E	TBE For Manual Valves - W018S	20	100%	$3.52	13-Feb-22	13-Aug-22
P01-E	VDR For Manual Valves - W018S	25	0%	$17.60	25-Aug-22	18-Sep-22
Fittings		64	0%	$23.47	20-Sep-22	22-Nov-22
P01-E	PMR For Fittings - W018S	7	0%	$2.35	20-Sep-22	26-Sep-22
P01-E	TBE For Fitting - W018S	20	0%	$3.52	27-Sep-22	16-Oct-22
P01-E	VDR For Fitting - W018S	25	0%	$17.60	29-Oct-22	22-Nov-22
Flanges		150	15.04%	$23.47	13-Feb-22	02-Nov-22
P01-E	PMR For Flanges - W018S	7	0%	$2.35	20-Sep-22	26-Sep-22
P01-E	TBE For Flanges - W018S	20	100%	$3.52	13-Feb-22	27-Sep-22
P01-E	VDR For Flanges - W018S	25	0%	$17.60	09-Oct-22	02-Nov-22
Gaskets		150	15.04%	$23.47	13-Feb-22	05-Nov-22
P01-E	PMR For Gaskets - W018S	7	0%	$2.35	20-Sep-22	26-Sep-22
P01-E	TBE For Gaskets - W018S	20	100%	$3.52	13-Feb-22	27-Sep-22
P01-E	VDR For Gaskets - W018S	25	0%	$17.60	12-Oct-22	05-Nov-22

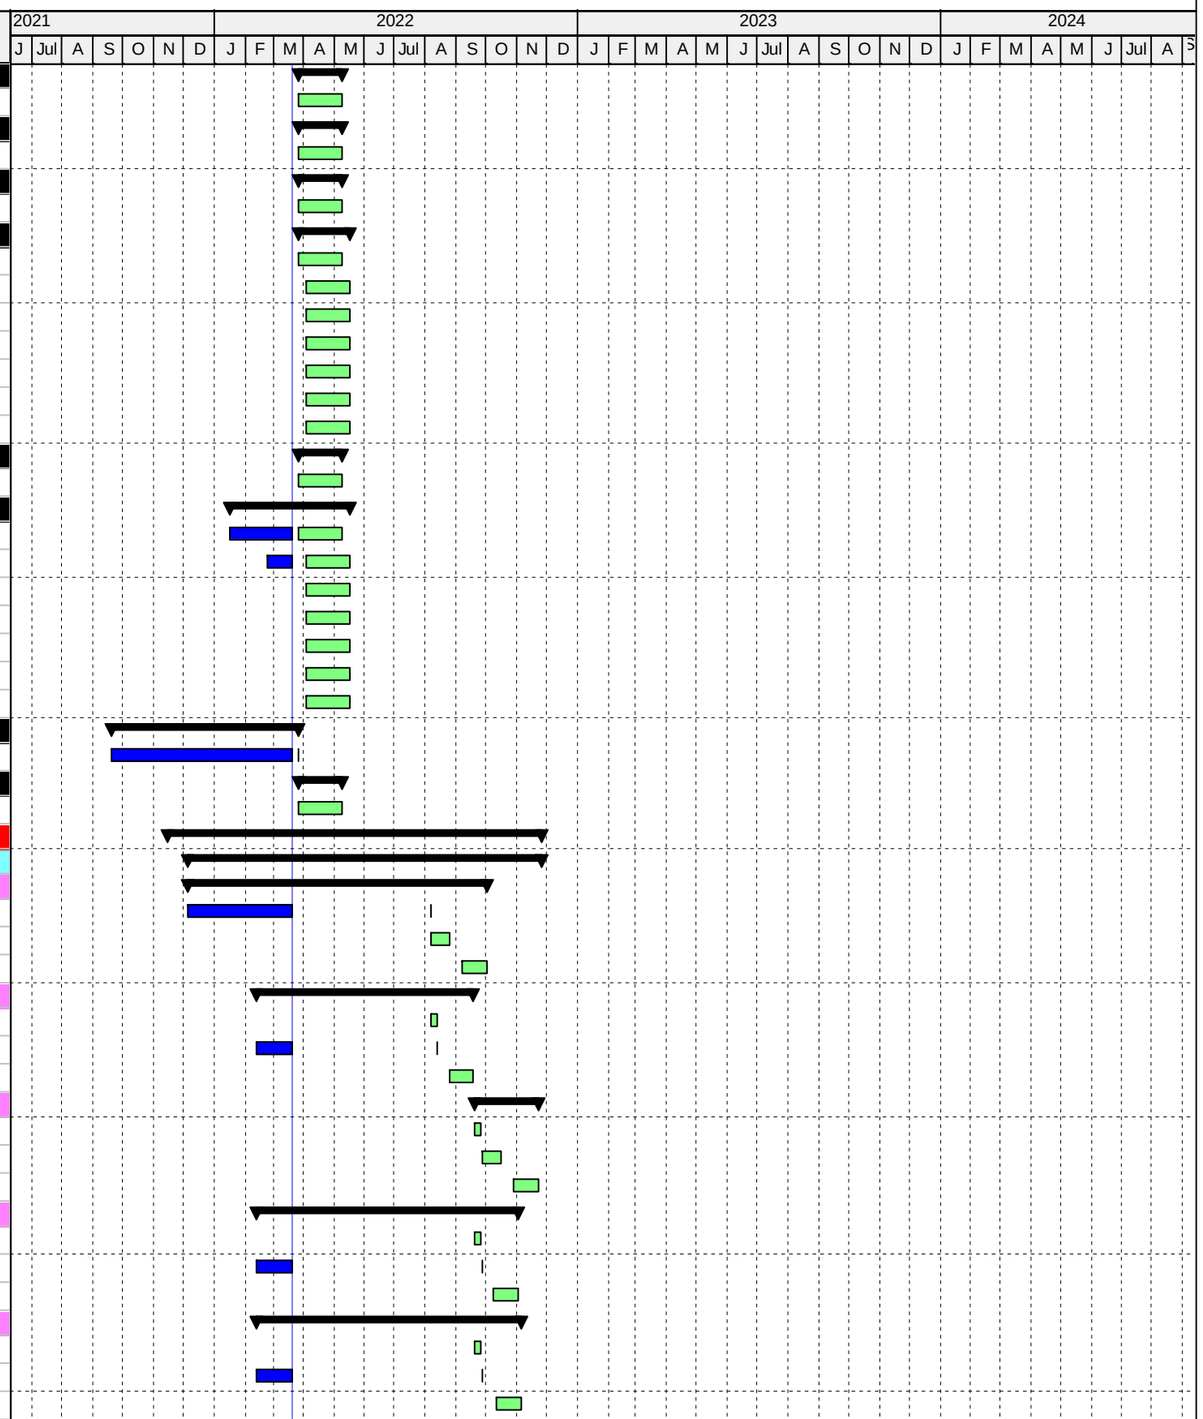


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Bolt & Nuts		67	0%	$23.47	20-Sep-22	25-Nov-22
P01-E	PMR For Bolt/Nuts - W018S	7	0%	$2.35	20-Sep-22	26-Sep-22
P01-E	TBE For Bolt/Nuts - W018S	20	0%	$3.52	27-Sep-22	16-Oct-22
P01-E	VDR For Bolt/Nuts - W018S	25	0%	$17.60	01-Nov-22	25-Nov-22
Sampling Connection		105	10.02%	$23.47	15-Feb-22	22-Jul-22
P01-E	PMR For Sampling Connection Set - W018S	7	100%	$2.35	15-Feb-22	04-May-22
P01-E	TBE For Sampling Connection	40	0%	$3.52	04-May-22	12-Jun-22
P01-E	VDR For Bolt/Nuts - W018S	25	0%	$17.60	28-Jun-22	22-Jul-22
Stone Trap		87	0%	$23.47	13-May-22	07-Aug-22
P01-E	PMR For Stone Trap - W018S	7	0%	$2.35	13-May-22	19-May-22
P01-E	TBE For Stone Trap - W018S	40	0%	$3.52	20-May-22	28-Jun-22
P01-E	VDR For Stone Trap - W018S	25	0%	$17.60	14-Jul-22	07-Aug-22
Pipe Support		72	0%	$23.47	06-Aug-22	16-Oct-22
P01-E	PMR For Pipe Support - W018S	7	0%	$2.35	06-Aug-22	12-Aug-22
P01-E	TBE For Pipe Support - W018S	20	0%	$3.52	13-Aug-22	01-Sep-22
P01-E	VDR For Pipe Support - W018S	20	0%	$17.60	27-Sep-22	16-Oct-22
Pipeline		122	12.5%	$47.13	06-Dec-21	10-Jul-22
Line Pipe		74	0%	$23.56	20-Mar-22	01-Jun-22
P01-E	PMR For Flowline Support - W018S	15	0%	$2.36	20-Mar-22	03-Apr-22
P01-E	TBE For Flowline Support - W018S	30	0%	$3.53	27-Mar-22	25-Apr-22
P01-E	VDR For Flowline Support - W018S	25	0%	$17.67	08-May-22	01-Jun-22
Flow Line Support		34	25%	$23.56	06-Dec-21	10-Jul-22
P01-E	PMR For Line Pipes - W018S	5	100%	$2.36	06-Dec-21	08-Jun-22
P01-E	TBE For Line Pipes - W018S	5	100%	$3.53	19-Feb-22	08-Jun-22
P01-E	VDR For Line Pipes - W018S	25	0%	$17.67	16-Jun-22	10-Jul-22
Control & Instrumentation		182	20.58%	$269.75	15-Nov-21	07-Jul-22
WHCP/HPU		52	24.98%	$95.22	15-Nov-21	23-May-22
P01-E	PMR For WHCP/HPU - W018S	7	100%	$9.52	15-Nov-21	19-Apr-22
P01-E	TBE/TBA For WHCP/HPU - W018S	20	100%	$14.28	30-Nov-21	19-Apr-22
P01-E	VDR/TBA For WHCP/HPU - W018S	20	0%	$71.42	04-May-22	23-May-22
Field Instrumentations		114	10%	$79.33	13-Dec-21	07-Jul-22
P01-E	PMR For Field Instrumentations - W018S	7	100%	$7.93	13-Dec-21	13-May-22
P01-E	TBE/TBA For Field Instrumentations - W018S	20	0%	$11.90	13-May-22	01-Jun-22
P01-E	VDR/TBA For Field Instrumentations - W018S	21	0%	$59.50	17-Jun-22	07-Jul-22
Instrument Bulk Items		153	24.99%	$95.19	18-Jan-22	21-Jun-22
P01-E	PMR For Instrument Bulk Items - W018S	7	100%	$9.52	18-Jan-22	13-May-22
P01-E	TBE/TBA For Instrument Bulk Items - W018S	20	100%	$14.28	02-Feb-22	13-May-22
P01-E	VDR/TBA For Instrument Bulk Items - W018S	20	0%	$71.40	02-Jun-22	21-Jun-22
Safety & Fire Fighting		171	25%	$190.13	08-Dec-21	16-Jul-22
Fire Fighting and Safety Equipment		171	24.99%	$133.09	08-Dec-21	16-Jul-22
P01-E	PMR For Fire Fighting and Safety Equipment - W018S	20	100%	$13.31	08-Dec-21	23-May-22
P01-E	TBE For Fire Fighting and Safety Equipment - W018S	30	100%	$19.96	12-Mar-22	23-May-22
P01-E	VDR For Fire Fighting and Safety Equipment - W018S	25	0%	$99.82	22-Jun-22	16-Jul-22
Safety Sign		171	25.03%	$57.04	08-Dec-21	16-Jul-22
P01-E	PMR For Fire Safety Sign - W018S	20	100%	$5.70	08-Dec-21	23-May-22
P01-E	TBE For Fire Safety Sign - W018S	30	100%	$8.56	12-Mar-22	23-May-22
P01-E	VDR For Fire Safety Sign - W018S	25	0%	$42.78	22-Jun-22	16-Jul-22
Structure		42	0%	$47.13	09-Jul-22	19-Aug-22
Steel Structure Items		42	0%	$23.56	09-Jul-22	19-Aug-22
P01-E	PMR For Steel Structure Items - W018S	15	0%	$2.36	09-Jul-22	23-Jul-22

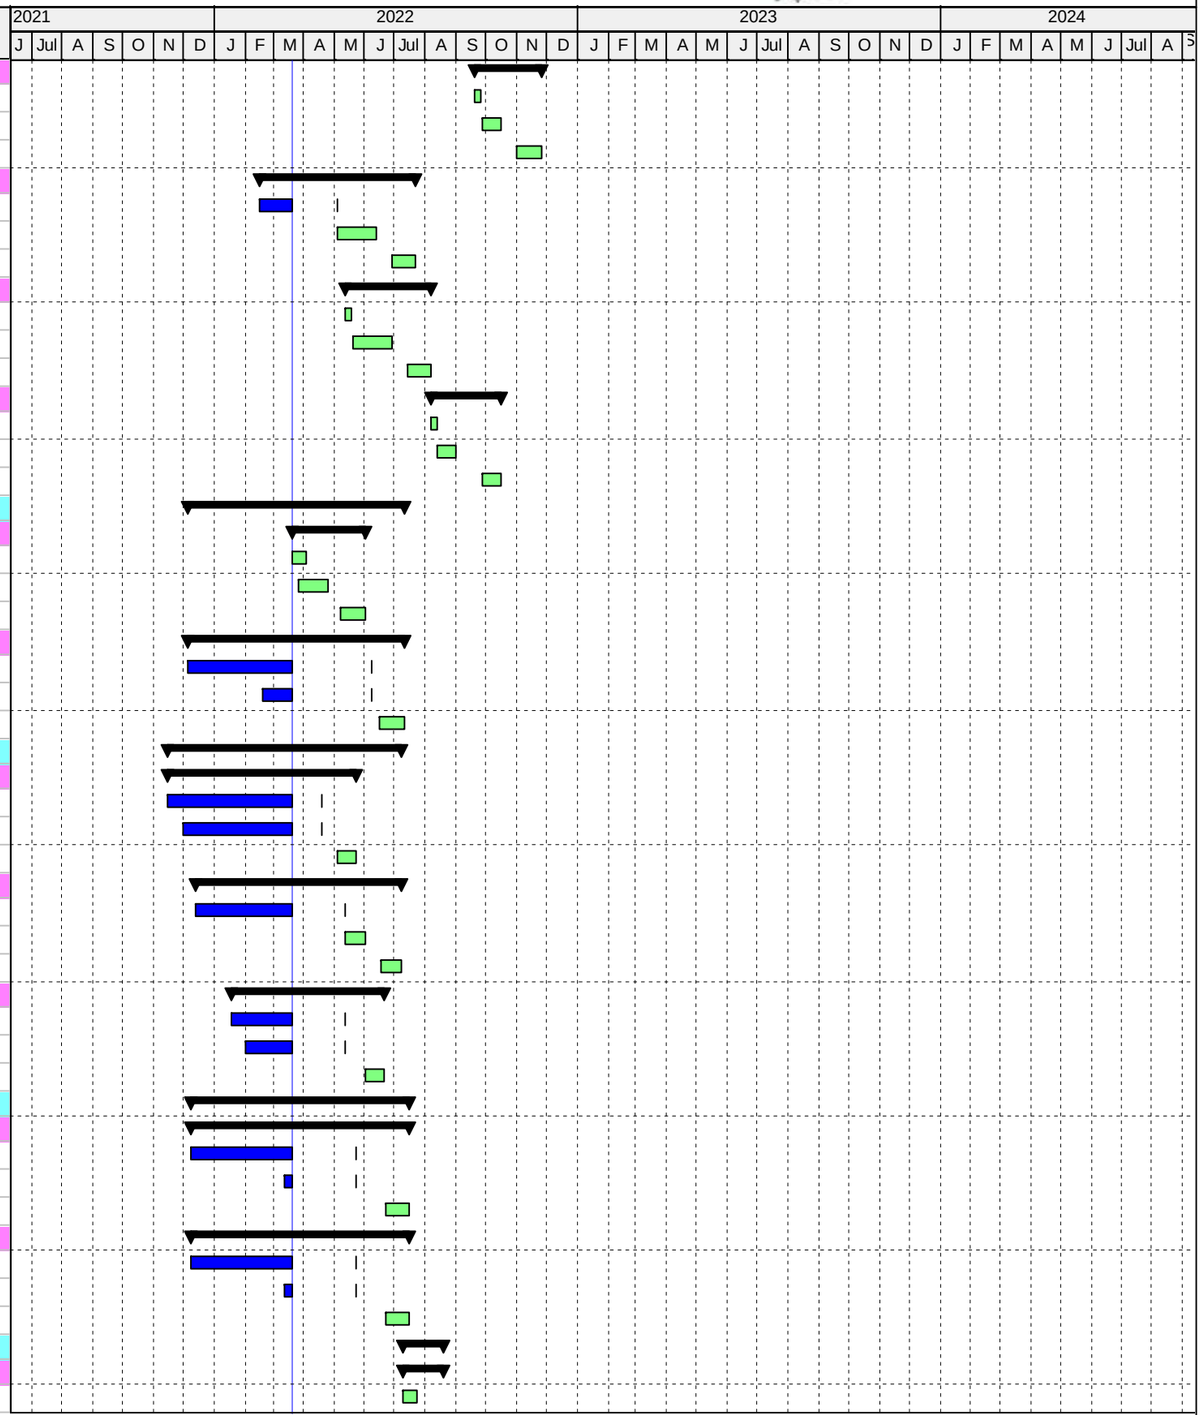


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P01-E	TBE For Steel Structure Items - W018S	30	0%	$3.53	16-Jul-22	14-Aug-22
P01-E	VDR For Steel Structure Items - W018S	5	0%	$17.67	15-Aug-22	19-Aug-22
Anchor Bolts		42	0%	$23.56	09-Jul-22	19-Aug-22
P01-E	PMR For Anchor Bolts - W018S	15	0%	$2.36	09-Jul-22	23-Jul-22
P01-E	TBE For Anchor Bolts - W018S	30	0%	$3.53	16-Jul-22	14-Aug-22
P01-E	VDR For Anchor Bolts - W018S	5	0%	$17.67	15-Aug-22	19-Aug-22
Civil		32	0%	$47.13	29-Apr-22	30-May-22
Geomembrane		32	0%	$23.56	29-Apr-22	30-May-22
P01-E	PMR For Geomembrane - W018S	5	0%	$2.36	29-Apr-22	03-May-22
P01-E	TBE For Geomembrane - W018S	20	0%	$3.53	06-May-22	25-May-22
P01-E	VDR For Geomembrane - W018S	5	0%	$17.67	26-May-22	30-May-22
Geotextile		32	0%	$23.56	29-Apr-22	30-May-22
P01-E	PMR For Geotextile - W018S	5	0%	$2.36	29-Apr-22	03-May-22
P01-E	TBE For Geotextile - W018S	20	0%	$3.53	06-May-22	25-May-22
P01-E	VDR For Geotextile - W018S	5	0%	$17.67	26-May-22	30-May-22
Commissioning Engineering		325	0%	$162.50	20-Mar-22	07-Feb-23
P01-EP	Operability Review	5	0%	$32.50	09-Jan-23	13-Jan-23
P01-EP	Pre-Commissioning, Commissioning & Startup Procedure - W	44	0%	$97.50	20-Mar-22	02-May-22
P01-EP	Operating Manual - W018S	30	0%	$32.50	09-Jan-23	07-Feb-23
Field Engineering		204	0%	$1,218.75	14-Jul-22	03-Feb-23
P01-EP	Technical/Site Queries	44	0%	$609.38	14-Jul-22	26-Aug-22
P01-EP	As-Built Document Booklets - W018S	10	0%	$609.38	24-Jan-23	03-Feb-23
Engineering Final Documentation		10	0%	$812.50	03-Feb-23	13-Feb-23
P01-EP	Final Engineering Dossier - W018S	10	0%	$812.50	03-Feb-23	13-Feb-23
PROCUREMENT		337	0%	$191,512.00	01-Feb-22	21-Mar-23
Wellhead Facility and Flowline		265	0%	$115,290.22	01-Feb-22	08-Jan-23
Piping - W018S		210	0%	$17,339.65	13-Jun-22	08-Jan-23
Pipes - W018S		89	0%	$3,467.93	26-Aug-22	22-Nov-22
P01-E	Tendering & Selection	7	0%	$138.72	26-Aug-22	01-Sep-22
P01-E	Contract Effectiveness / PO	5	0%	$208.08	02-Sep-22	06-Sep-22
P01-E	Manufacturing / Fabrication / Supply	60	0%	$1,733.96	07-Sep-22	05-Nov-22
P01-E	Final Inspection	7	0%	$346.79	06-Nov-22	12-Nov-22
P01-E	Delivery On Site	5	0%	$866.98	13-Nov-22	17-Nov-22
P01-E	Submitting Vendor Data Book	5	0%	$173.40	18-Nov-22	22-Nov-22
Fittings - W018S		84	0%	$1,300.47	17-Oct-22	08-Jan-23
P01-E	Tendering & Selection	7	0%	$52.02	17-Oct-22	23-Oct-22
P01-E	Contract Effectiveness / PO	5	0%	$78.03	24-Oct-22	28-Oct-22
P01-E	Manufacturing / Fabrication / Supply	55	0%	$650.24	29-Oct-22	22-Dec-22
P01-E	Final Inspection	7	0%	$130.05	23-Dec-22	29-Dec-22
P01-E	Delivery On Site	5	0%	$325.12	30-Dec-22	03-Jan-23
P01-E	Submitting Vendor Data Book	5	0%	$65.02	04-Jan-23	08-Jan-23
Flanges - W018S		84	0%	$1,300.47	27-Sep-22	19-Dec-22
P01-E	Tendering & Selection	7	0%	$52.02	27-Sep-22	03-Oct-22
P01-E	Contract Effectiveness / PO	5	0%	$78.03	04-Oct-22	08-Oct-22
P01-E	Manufacturing / Fabrication / Supply	55	0%	$650.24	09-Oct-22	02-Dec-22
P01-E	Final Inspection	7	0%	$130.05	03-Dec-22	09-Dec-22
P01-E	Delivery On Site	5	0%	$325.12	10-Dec-22	14-Dec-22
P01-E	Submitting Vendor Data Book	5	0%	$65.02	15-Dec-22	19-Dec-22
Manual Valves - W018S		91	0%	$6,068.88	13-Aug-22	11-Nov-22

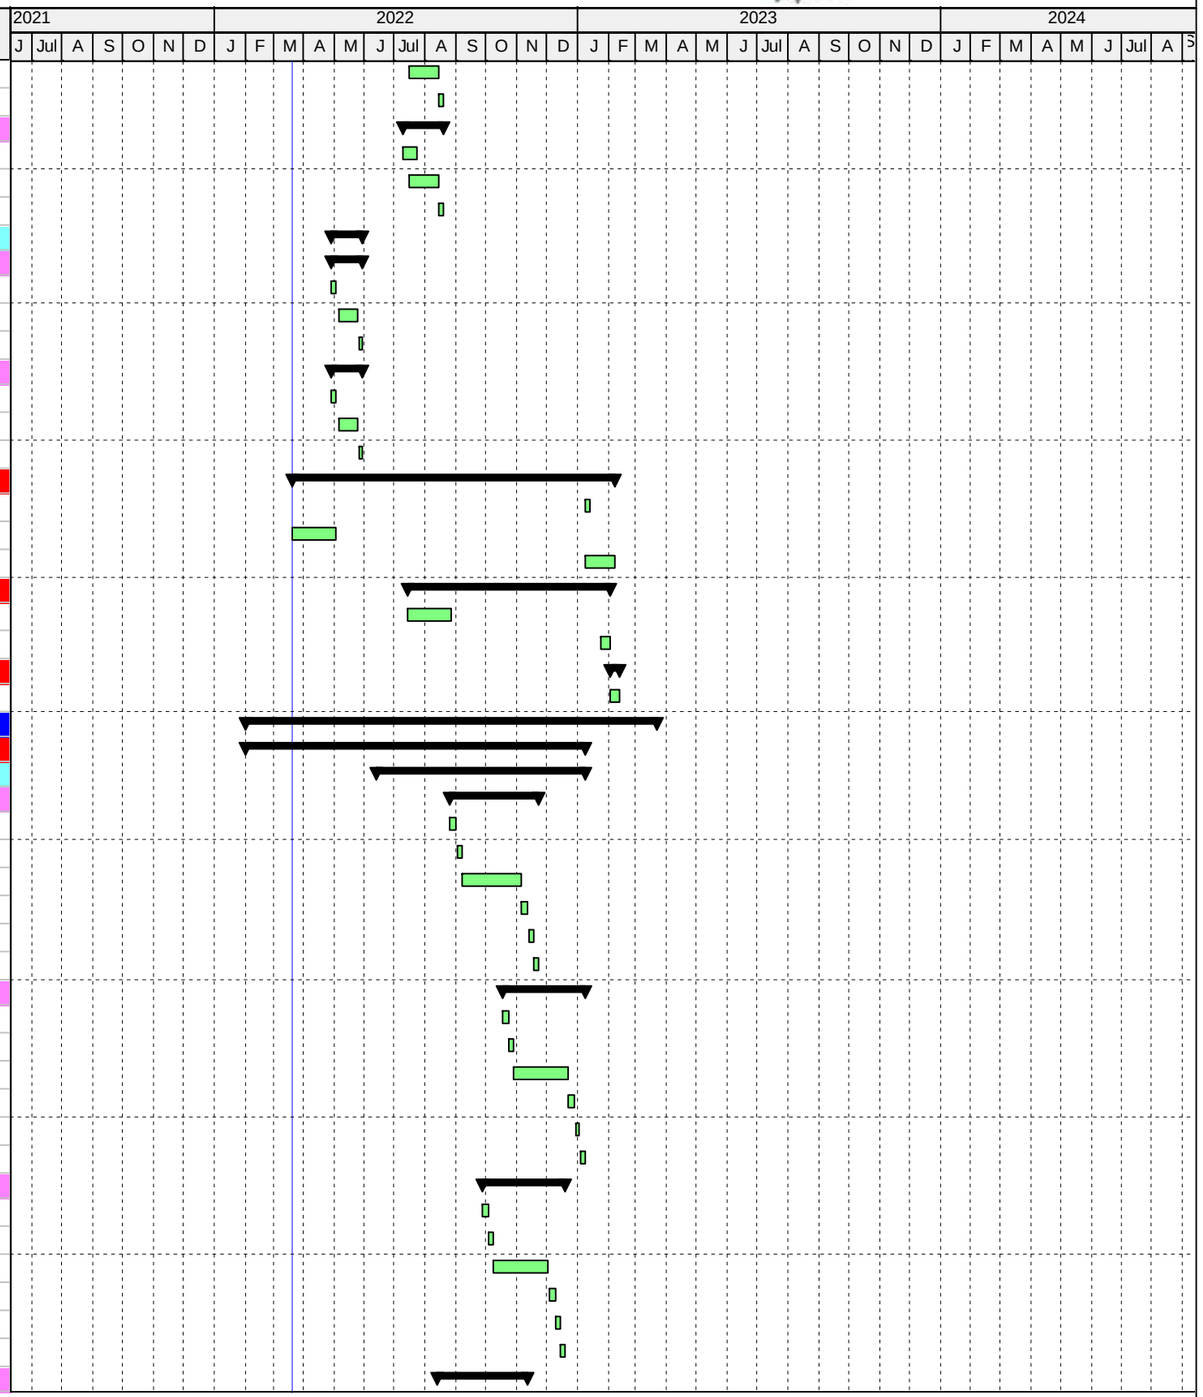


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P01-E	Tendering & Selection	7	0%	$242.76	13-Aug-22	19-Aug-22
P01-E	Contract Effectiveness / PO	5	0%	$364.13	20-Aug-22	24-Aug-22
P01-E	Manufacturing / Fabrication / Supply	60	0%	$3,034.44	25-Aug-22	23-Oct-22
P01-E	Final Inspection	7	0%	$606.89	24-Oct-22	30-Oct-22
P01-E	Delivery On Site	7	0%	$1,213.78	31-Oct-22	06-Nov-22
P01-E	Submitting Vendor Data Book	5	0%	$303.44	07-Nov-22	11-Nov-22
P01-E	Delivering Spare Parts	5	0%	$303.44	07-Nov-22	11-Nov-22
Gaskets - W018S		80	0%	$520.19	27-Sep-22	15-Dec-22
P01-E	Tendering & Selection	10	0%	$20.81	27-Sep-22	06-Oct-22
P01-E	Contract Effectiveness / PO	5	0%	$31.21	07-Oct-22	11-Oct-22
P01-E	Manufacturing / Fabrication / Supply	50	0%	$260.09	12-Oct-22	30-Nov-22
P01-E	Final Inspection	7	0%	$52.02	01-Dec-22	07-Dec-22
P01-E	Delivery On Site	5	0%	$130.05	08-Dec-22	12-Dec-22
P01-E	Submitting Vendor Data Book	3	0%	$26.01	13-Dec-22	15-Dec-22
Bolt/Nuts - W018S		80	0%	$346.79	17-Oct-22	04-Jan-23
P01-E	Tendering & Selection	10	0%	$13.87	17-Oct-22	26-Oct-22
P01-E	Contract Effectiveness / PO	5	0%	$20.81	27-Oct-22	31-Oct-22
P01-E	Manufacturing / Fabrication / Supply	50	0%	$173.40	01-Nov-22	20-Dec-22
P01-E	Final Inspection	7	0%	$34.68	21-Dec-22	27-Dec-22
P01-E	Delivery On Site	5	0%	$86.70	28-Dec-22	01-Jan-23
P01-E	Submitting Vendor Data Book	3	0%	$17.34	02-Jan-23	04-Jan-23
Sampling Connection Set - W018S		65	0%	$866.98	13-Jun-22	16-Aug-22
P01-E	Tendering & Selection	10	0%	$34.68	13-Jun-22	22-Jun-22
P01-E	Contract Effectiveness / PO	5	0%	$52.02	23-Jun-22	27-Jun-22
P01-E	Manufacturing / Fabrication / Supply	35	0%	$433.49	28-Jun-22	01-Aug-22
P01-E	Final Inspection	7	0%	$86.70	02-Aug-22	08-Aug-22
P01-E	Delivery On Site	5	0%	$216.75	09-Aug-22	13-Aug-22
P01-E	Submitting Vendor Data Book	3	0%	$43.35	14-Aug-22	16-Aug-22
Stone Trap - W018S		74	0%	$2,600.95	29-Jun-22	10-Sep-22
P01-E	Tendering & Selection	10	0%	$104.04	29-Jun-22	08-Jul-22
P01-E	Contract Effectiveness / PO	5	0%	$156.06	09-Jul-22	13-Jul-22
P01-E	Manufacturing / Fabrication / Supply	35	0%	$1,300.47	14-Jul-22	17-Aug-22
P01-E	Final Inspection	12	0%	$260.09	18-Aug-22	29-Aug-22
P01-E	Delivery On Site	7	0%	$650.24	30-Aug-22	05-Sep-22
P01-E	Submitting Vendor Data Book	5	0%	$130.05	06-Sep-22	10-Sep-22
Pipe Support - W018S		84	0%	$866.98	02-Sep-22	24-Nov-22
P01-E	Tendering & Selection	20	0%	$34.68	02-Sep-22	21-Sep-22
P01-E	Contract Effectiveness / PO	5	0%	$52.02	22-Sep-22	26-Sep-22
P01-E	Manufacturing / Fabrication / Supply	35	0%	$433.49	27-Sep-22	31-Oct-22
P01-E	Final Inspection	12	0%	$86.70	01-Nov-22	12-Nov-22
P01-E	Delivery On Site	7	0%	$216.75	13-Nov-22	19-Nov-22
P01-E	Submitting Vendor Data Book	5	0%	$43.35	20-Nov-22	24-Nov-22
Pipeline - W018S		106	0%	$79,792.36	26-Apr-22	09-Aug-22
Line Pipes - W018S		101	0%	$67,823.51	26-Apr-22	04-Aug-22
P01-E	Tendering & Selection	7	0%	$2,712.94	26-Apr-22	02-May-22
P01-E	Contract Effectiveness / PO	5	0%	$4,069.41	03-May-22	07-May-22
P01-E	Manufacturing / Fabrication / Supply	70	0%	$33,911.75	08-May-22	16-Jul-22
P01-E	Final Inspection	7	0%	$6,782.35	17-Jul-22	23-Jul-22
P01-E	Delivery On Site	7	0%	$16,955.88	24-Jul-22	30-Jul-22

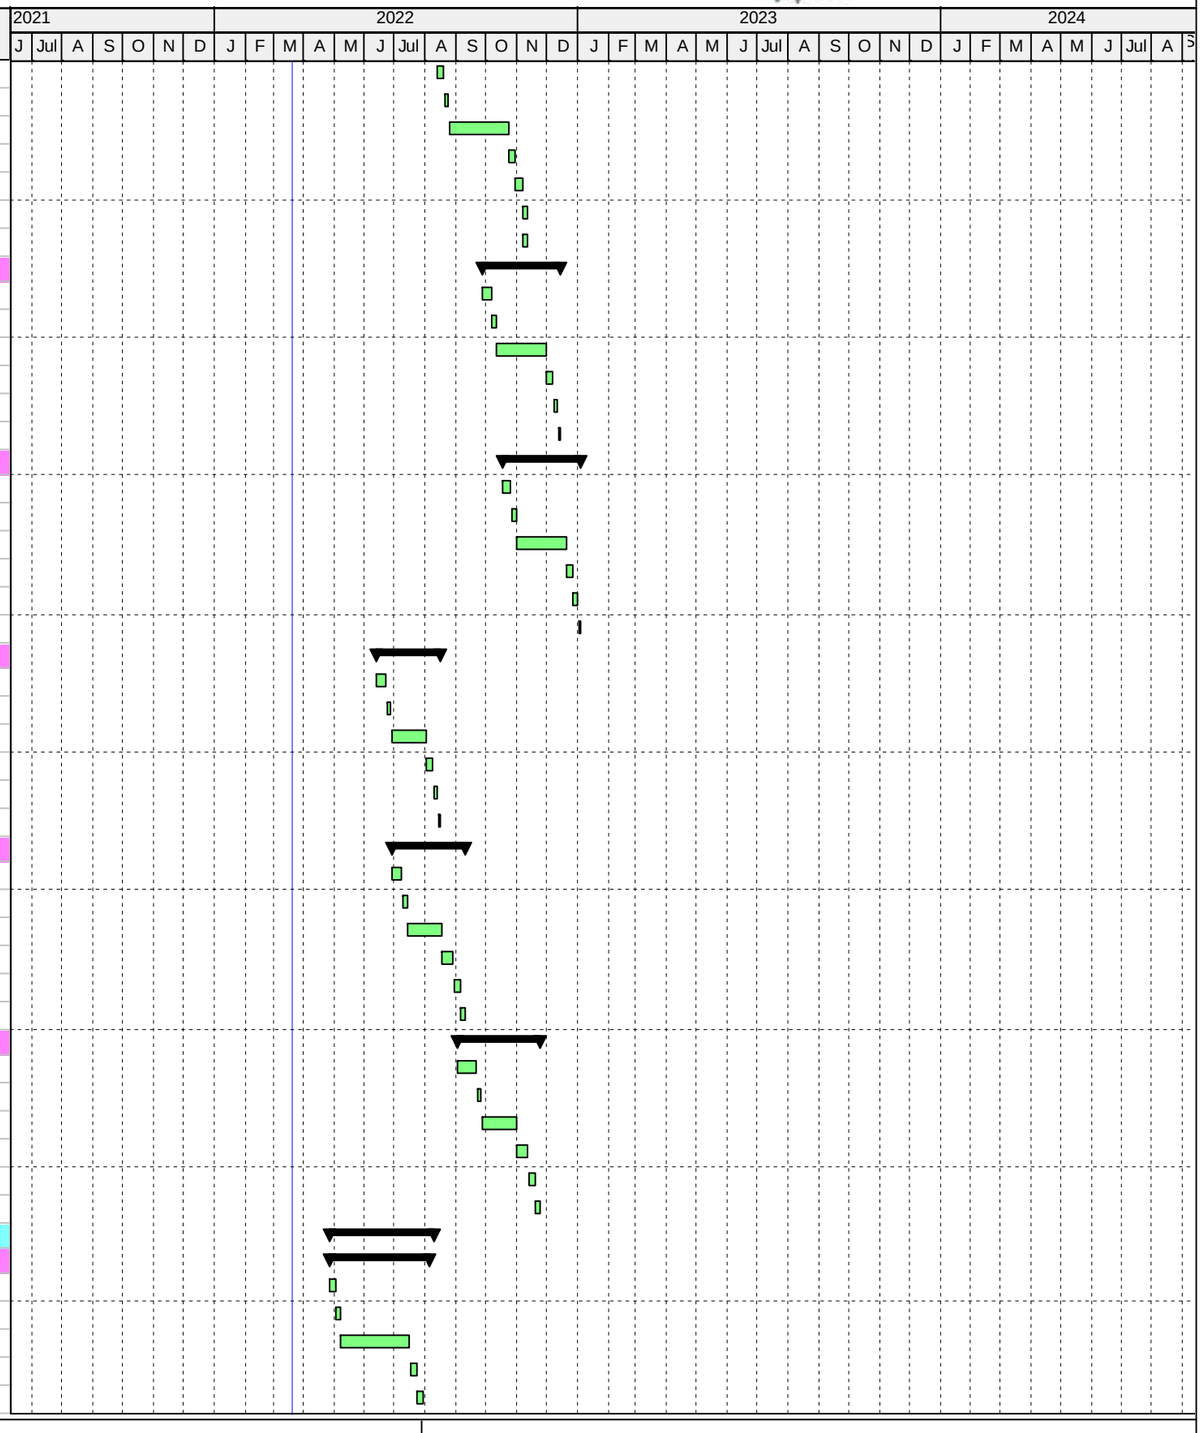


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P01-E	Submitting Vendor Data Book	5	0%	$3,391.18	31-Jul-22	04-Aug-22
Flow Line Support - W018S		63	0%	$11,968.85	08-Jun-22	09-Aug-22
P01-E	Tendering & Selection	5	0%	$478.75	08-Jun-22	12-Jun-22
P01-E	Contract Effectiveness / PO	3	0%	$718.13	13-Jun-22	15-Jun-22
P01-E	Manufacturing / Fabrication / Supply	40	0%	$5,984.43	16-Jun-22	25-Jul-22
P01-E	Final Inspection	7	0%	$1,196.89	26-Jul-22	01-Aug-22
P01-E	Delivery On Site	5	0%	$2,992.21	02-Aug-22	06-Aug-22
P01-E	Submitting Vendor Data Book	3	0%	$598.44	07-Aug-22	09-Aug-22
Control & Instrumentation - W018S		138	0%	$17,328.12	01-Feb-22	03-Sep-22
WHCP/HPU - W018S		123	0%	$16,288.43	01-Feb-22	19-Aug-22
P01-E	Tendering & Selection	10	0%	$651.54	01-Feb-22	28-Apr-22
P01-E	Contract Effectiveness / PO	5	0%	$977.31	29-Apr-22	03-May-22
P01-E	Manufacturing / Fabrication / Supply	90	0%	$8,144.22	04-May-22	01-Aug-22
P01-E	Final Inspection	7	0%	$1,628.84	02-Aug-22	08-Aug-22
P01-E	Delivery On Site	7	0%	$3,257.69	08-Aug-22	14-Aug-22
P01-E	Submitting Vendor Data Book	5	0%	$814.42	15-Aug-22	19-Aug-22
P01-E	Delivering Spare Parts	5	0%	$814.42	15-Aug-22	19-Aug-22
Field Instrumentations - W018S		94	0%	$866.41	02-Jun-22	03-Sep-22
P01-E	Tendering & Selection	10	0%	$34.66	02-Jun-22	11-Jun-22
P01-E	Contract Effectiveness / PO	5	0%	$51.98	12-Jun-22	16-Jun-22
P01-E	Manufacturing / Fabrication / Supply	60	0%	$433.20	17-Jun-22	15-Aug-22
P01-E	Final Inspection	7	0%	$86.64	16-Aug-22	22-Aug-22
P01-E	Delivery On Site	7	0%	$173.28	23-Aug-22	29-Aug-22
P01-E	Submitting Vendor Data Book	5	0%	$43.32	30-Aug-22	03-Sep-22
P01-E	Delivering Spare Parts	5	0%	$43.32	30-Aug-22	03-Sep-22
Instrument Tube and Fitting		91	0%	$138.62	18-May-22	16-Aug-22
P01-E	Tendering & Selection	7	0%	$5.54	18-May-22	24-May-22
P01-E	Contract Effectiveness / PO	5	0%	$8.32	25-May-22	29-May-22
P01-E	Manufacturing / Fabrication / Supply	60	0%	$69.31	30-May-22	28-Jul-22
P01-E	Final Inspection	7	0%	$13.86	29-Jul-22	04-Aug-22
P01-E	Delivery On Site	7	0%	$34.66	05-Aug-22	11-Aug-22
P01-E	Submitting Vendor Data Book	5	0%	$6.93	12-Aug-22	16-Aug-22
Instrument Cable Tray		94	0%	$34.66	18-May-22	19-Aug-22
P01-E	Tendering & Selection	10	0%	$1.39	18-May-22	27-May-22
P01-E	Contract Effectiveness / PO	5	0%	$2.08	28-May-22	01-Jun-22
P01-E	Manufacturing / Fabrication / Supply	60	0%	$17.33	02-Jun-22	31-Jul-22
P01-E	Final Inspection	7	0%	$3.47	01-Aug-22	07-Aug-22
P01-E	Delivery On Site	7	0%	$8.66	08-Aug-22	14-Aug-22
P01-E	Submitting Vendor Data Book	5	0%	$1.73	15-Aug-22	19-Aug-22
Safety & Fire Fighting - W018S		64	0%	$830.09	02-Jun-22	04-Aug-22
Fire Fighting and Safety Equipment - W018S		64	0%	$664.07	02-Jun-22	04-Aug-22
P01-E	Tendering & Selection	15	0%	$26.56	02-Jun-22	16-Jun-22
P01-E	Contract Effectiveness / PO	5	0%	$39.84	17-Jun-22	21-Jun-22
P01-E	Manufacturing / Fabrication / Supply	20	0%	$332.04	22-Jun-22	11-Jul-22
P01-E	Final Inspection	12	0%	$66.41	12-Jul-22	23-Jul-22
P01-E	Delivery On Site	7	0%	$166.02	24-Jul-22	30-Jul-22
P01-E	Submitting Vendor Data Book	5	0%	$33.20	31-Jul-22	04-Aug-22
Fire Safety Sign - W018S		64	0%	$166.02	02-Jun-22	04-Aug-22
P01-E	Tendering & Selection	15	0%	$6.64	02-Jun-22	16-Jun-22

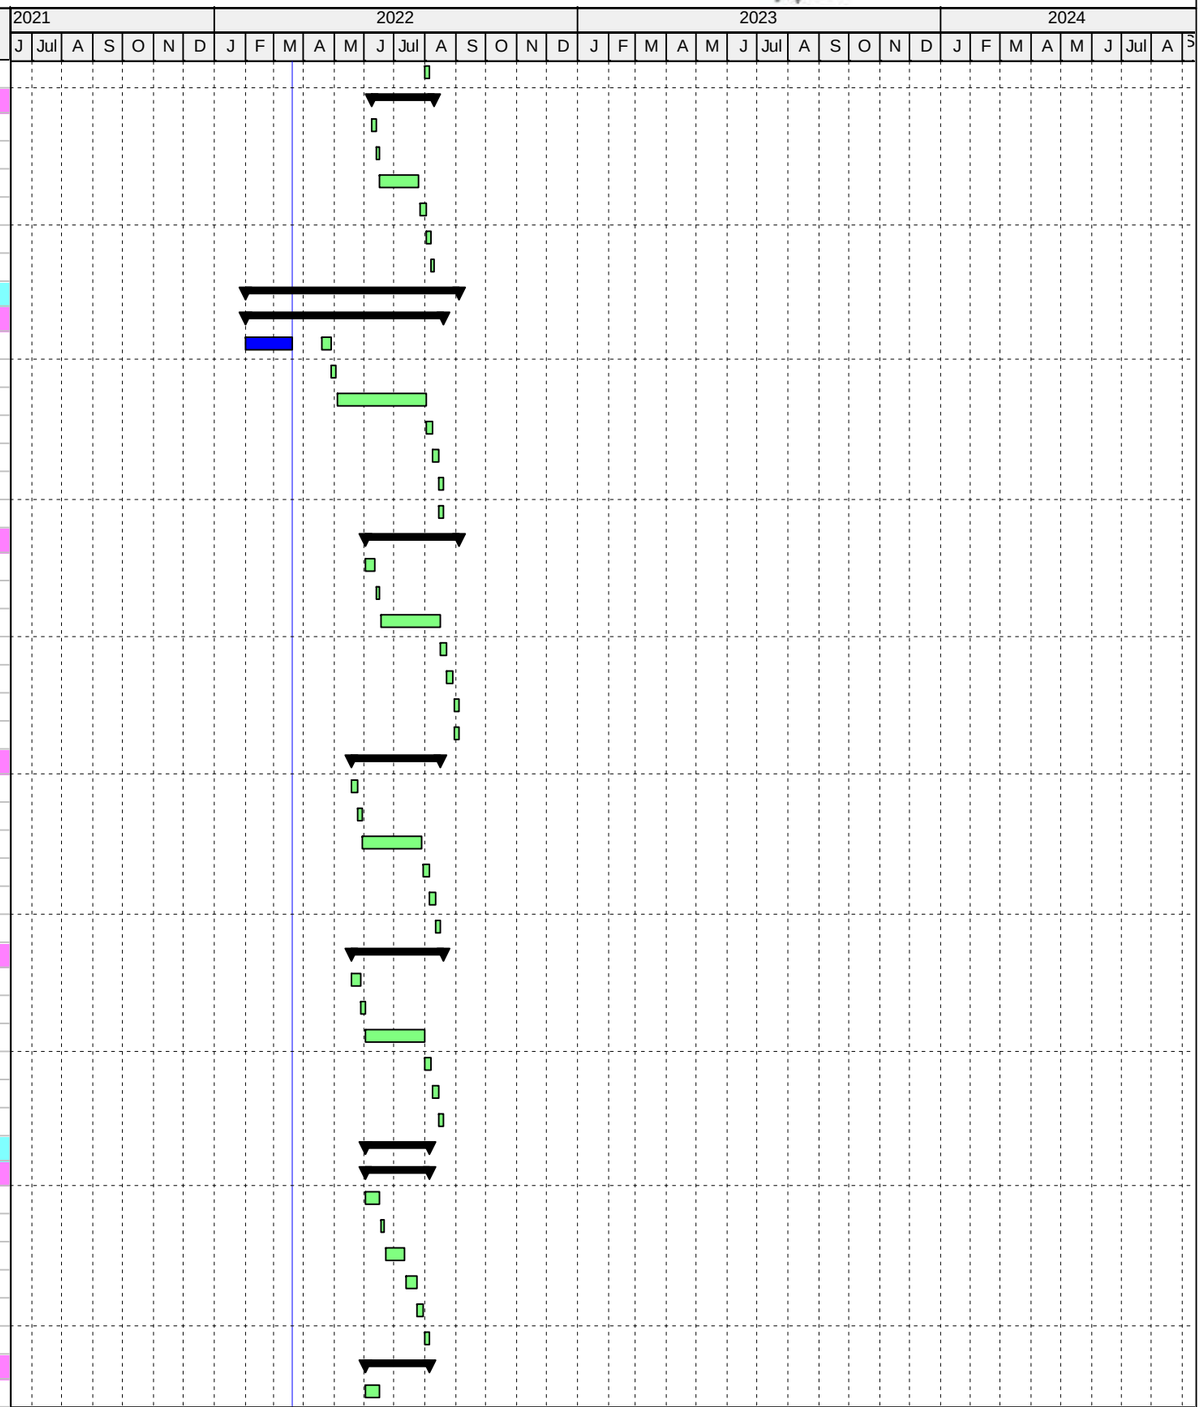


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P01-E	Contract Effectiveness / PO	5	0%	$9.96	17-Jun-22	21-Jun-22
P01-E	Manufacturing / Fabrication / Supply	20	0%	$83.01	22-Jun-22	11-Jul-22
P01-E	Final Inspection	12	0%	$16.60	12-Jul-22	23-Jul-22
P01-E	Delivery On Site	7	0%	$41.50	24-Jul-22	30-Jul-22
P01-E	Submitting Vendor Data Book	5	0%	$8.30	31-Jul-22	04-Aug-22
Extension of Binak B/C Manifold		313	0%	$76,221.78	13-May-22	21-Mar-23
Mechanical - Extension of Binak B/C Manifold		154	0%	$2,622.03	13-May-22	13-Oct-22
Pumps		154	0%	$2,622.03	13-May-22	13-Oct-22
P01-E	Tendering & Selection	15	0%	$104.88	13-May-22	27-May-22
P01-E	Contract Effectiveness / PO	5	0%	$157.32	28-May-22	01-Jun-22
P01-E	Manufacturing / Fabrication / Supply	110	0%	$1,311.01	02-Jun-22	19-Sep-22
P01-E	Final Inspection	7	0%	$262.20	20-Sep-22	26-Sep-22
P01-E	Delivery On Site	7	0%	$524.41	27-Sep-22	03-Oct-22
P01-E	Submitting Vendor Data Book	5	0%	$131.10	04-Oct-22	08-Oct-22
P01-E	Delivering Spare Parts	5	0%	$131.10	09-Oct-22	13-Oct-22
Piping - Extension of Binak B/C Manifold		301	0%	$16,631.59	16-May-22	12-Mar-23
Pipes		114	0%	$6,785.69	05-Oct-22	26-Jan-23
P01-E	Tendering & Selection	10	0%	$271.43	05-Oct-22	14-Oct-22
P01-E	Contract Effectiveness / PO	5	0%	$407.14	15-Oct-22	19-Oct-22
P01-E	Manufacturing / Fabrication / Supply	80	0%	$3,392.84	20-Oct-22	07-Jan-23
P01-E	Final Inspection	7	0%	$678.57	08-Jan-23	14-Jan-23
P01-E	Delivery On Site	7	0%	$1,696.42	15-Jan-23	21-Jan-23
P01-E	Submitting Vendor Data Book	5	0%	$339.28	22-Jan-23	26-Jan-23
Fittings		124	0%	$898.11	04-Nov-22	07-Mar-23
P01-E	Tendering & Selection	10	0%	$35.92	04-Nov-22	13-Nov-22
P01-E	Contract Effectiveness / PO	5	0%	$53.89	14-Nov-22	18-Nov-22
P01-E	Manufacturing / Fabrication / Supply	90	0%	$449.05	19-Nov-22	16-Feb-23
P01-E	Final Inspection	7	0%	$89.81	17-Feb-23	23-Feb-23
P01-E	Delivery On Site	7	0%	$224.53	24-Feb-23	02-Mar-23
P01-E	Submitting Vendor Data Book	5	0%	$44.91	03-Mar-23	07-Mar-23
Flanges		124	0%	$898.11	04-Nov-22	07-Mar-23
P01-E	Tendering & Selection	10	0%	$35.92	04-Nov-22	13-Nov-22
P01-E	Contract Effectiveness / PO	5	0%	$53.89	14-Nov-22	18-Nov-22
P01-E	Manufacturing / Fabrication / Supply	90	0%	$449.05	19-Nov-22	16-Feb-23
P01-E	Final Inspection	7	0%	$89.81	17-Feb-23	23-Feb-23
P01-E	Delivery On Site	7	0%	$224.53	24-Feb-23	02-Mar-23
P01-E	Submitting Vendor Data Book	5	0%	$44.91	03-Mar-23	07-Mar-23
Manual Valves		129	0%	$3,991.58	04-Nov-22	12-Mar-23
P01-E	Tendering & Selection	10	0%	$159.66	04-Nov-22	13-Nov-22
P01-E	Contract Effectiveness / PO	5	0%	$239.49	14-Nov-22	18-Nov-22
P01-E	Manufacturing / Fabrication / Supply	90	0%	$1,995.79	19-Nov-22	16-Feb-23
P01-E	Final Inspection	7	0%	$399.16	17-Feb-23	23-Feb-23
P01-E	Delivery On Site	7	0%	$798.32	24-Feb-23	02-Mar-23
P01-E	Submitting Vendor Data Book	5	0%	$199.58	03-Mar-23	07-Mar-23
P01-E	Delivering Spare Parts	5	0%	$199.58	08-Mar-23	12-Mar-23
Gaskets		124	0%	$1,081.05	04-Nov-22	07-Mar-23
P01-E	Tendering & Selection	10	0%	$43.24	04-Nov-22	13-Nov-22
P01-E	Contract Effectiveness / PO	5	0%	$64.86	14-Nov-22	18-Nov-22
P01-E	Manufacturing / Fabrication / Supply	90	0%	$540.53	19-Nov-22	16-Feb-23

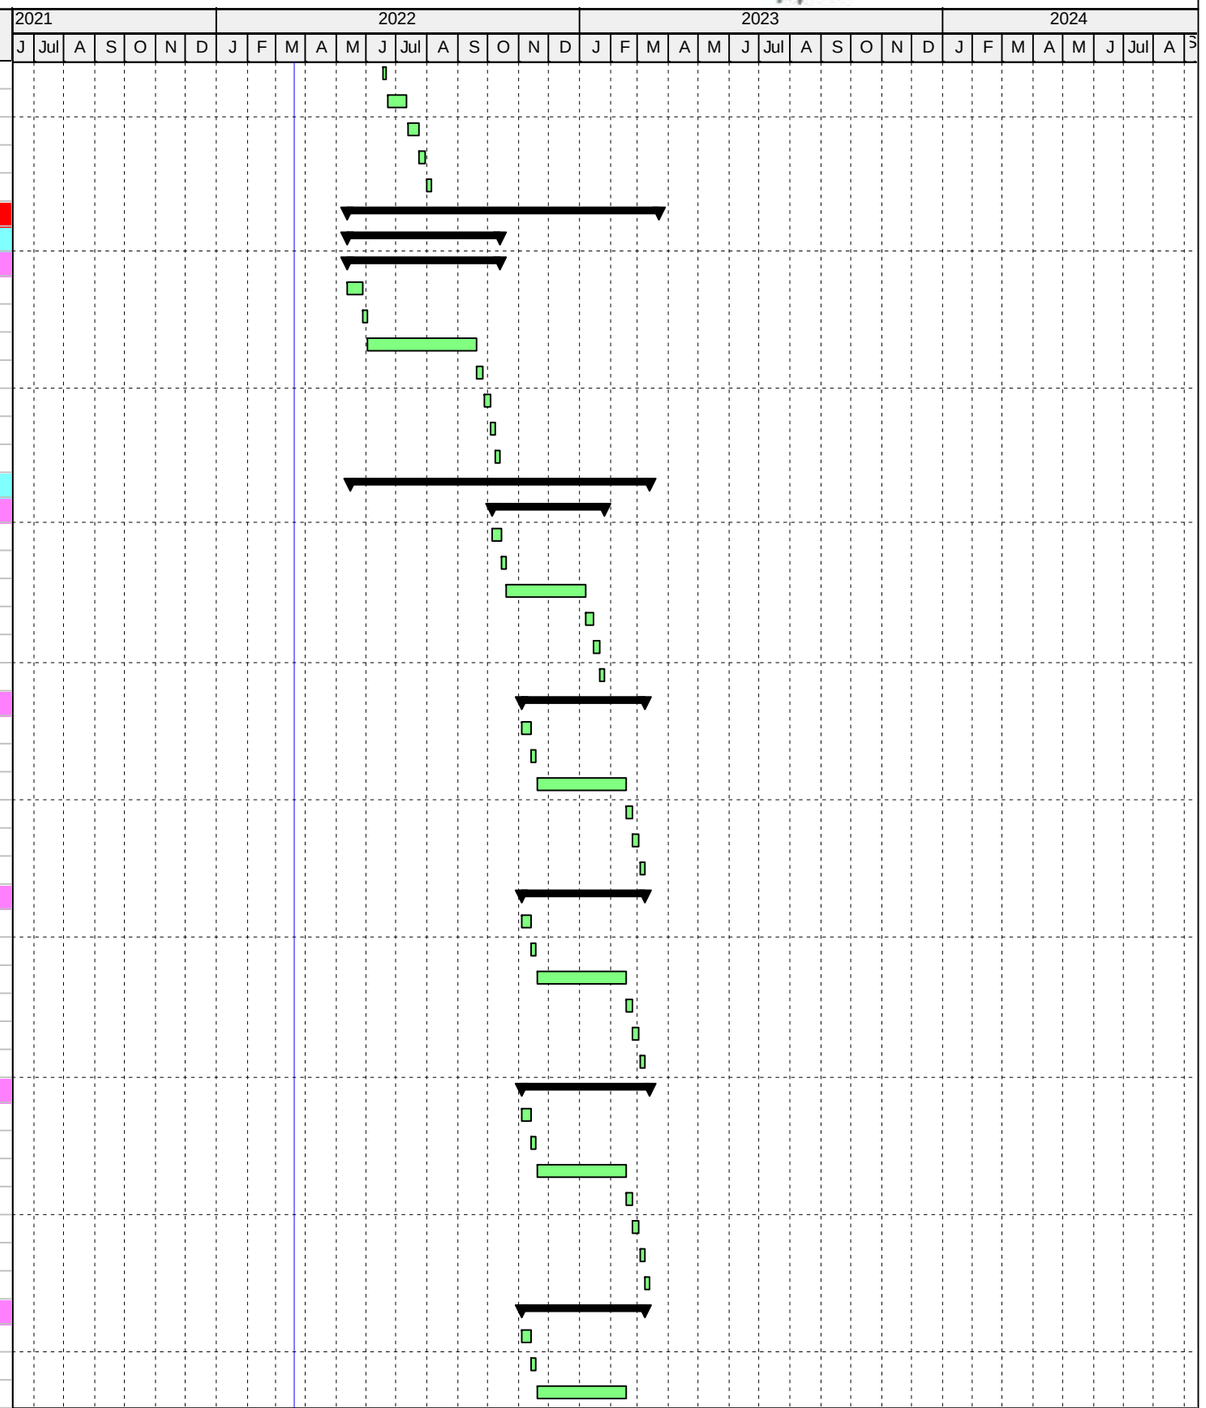


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P01-E	Final Inspection	7	0%	$108.11	17-Feb-23	23-Feb-23
P01-E	Delivery On Site	7	0%	$270.26	24-Feb-23	02-Mar-23
P01-E	Submitting Vendor Data Book	5	0%	$54.05	03-Mar-23	07-Mar-23
Bolt/Nuts		114	0%	$1,663.16	04-Nov-22	25-Feb-23
P01-E	Tendering & Selection	10	0%	$66.53	04-Nov-22	13-Nov-22
P01-E	Contract Effectiveness / PO	5	0%	$99.79	14-Nov-22	18-Nov-22
P01-E	Manufacturing / Fabrication / Supply	80	0%	$831.58	19-Nov-22	06-Feb-23
P01-E	Final Inspection	7	0%	$166.32	07-Feb-23	13-Feb-23
P01-E	Delivery On Site	7	0%	$415.79	14-Feb-23	20-Feb-23
P01-E	Submitting Vendor Data Book	5	0%	$83.16	21-Feb-23	25-Feb-23
Sampling Connection Set		94	0%	$898.11	16-May-22	17-Aug-22
P01-E	Tendering & Selection	10	0%	$35.92	16-May-22	25-May-22
P01-E	Contract Effectiveness / PO	5	0%	$53.89	26-May-22	30-May-22
P01-E	Manufacturing / Fabrication / Supply	60	0%	$449.05	31-May-22	29-Jul-22
P01-E	Final Inspection	7	0%	$89.81	30-Jul-22	05-Aug-22
P01-E	Delivery On Site	7	0%	$224.53	06-Aug-22	12-Aug-22
P01-E	Submitting Vendor Data Book	5	0%	$44.91	13-Aug-22	17-Aug-22
Pipe Supports		94	0%	$415.79	07-Oct-22	08-Jan-23
P01-E	Tendering & Selection	10	0%	$16.63	07-Oct-22	16-Oct-22
P01-E	Contract Effectiveness / PO	5	0%	$24.95	17-Oct-22	21-Oct-22
P01-E	Manufacturing / Fabrication / Supply	60	0%	$207.89	22-Oct-22	20-Dec-22
P01-E	Final Inspection	7	0%	$41.58	21-Dec-22	27-Dec-22
P01-E	Delivery On Site	7	0%	$103.95	28-Dec-22	03-Jan-23
P01-E	Submitting Vendor Data Book	5	0%	$20.79	04-Jan-23	08-Jan-23
Control & Instrumentation - Extension of Binak B/C Manifold		312	0%	$41,998.20	14-May-22	21-Mar-23
DCS System		164	0%	$17,219.26	21-May-22	31-Oct-22
P01-E	Tendering & Selection	20	0%	$688.77	21-May-22	09-Jun-22
P01-E	Contract Effectiveness / PO	5	0%	$1,033.16	10-Jun-22	14-Jun-22
P01-E	Manufacturing / Fabrication / Supply	120	0%	$8,609.63	15-Jun-22	12-Oct-22
P01-E	Final Inspection	7	0%	$1,721.93	13-Oct-22	19-Oct-22
P01-E	Delivery On Site	7	0%	$3,443.85	20-Oct-22	26-Oct-22
P01-E	Submitting Vendor Data Book	5	0%	$860.96	27-Oct-22	31-Oct-22
P01-E	Delivering Spare Parts	5	0%	$860.96	27-Oct-22	31-Oct-22
ESD System		164	0%	$12,179.48	05-Jun-22	15-Nov-22
P01-E	Tendering & Selection	20	0%	$487.18	05-Jun-22	24-Jun-22
P01-E	Contract Effectiveness / PO	5	0%	$730.77	25-Jun-22	29-Jun-22
P01-E	Manufacturing / Fabrication / Supply	120	0%	$6,089.74	30-Jun-22	27-Oct-22
P01-E	Final Inspection	7	0%	$1,217.95	28-Oct-22	03-Nov-22
P01-E	Delivery On Site	7	0%	$2,435.90	04-Nov-22	10-Nov-22
P01-E	Submitting Vendor Data Book	5	0%	$608.97	11-Nov-22	15-Nov-22
P01-E	Delivering Spare Parts	5	0%	$608.97	11-Nov-22	15-Nov-22
F&G System		164	0%	$8,399.64	05-Jun-22	15-Nov-22
P01-E	Tendering & Selection	20	0%	$335.99	05-Jun-22	24-Jun-22
P01-E	Contract Effectiveness / PO	5	0%	$503.98	25-Jun-22	29-Jun-22
P01-E	Manufacturing / Fabrication / Supply	120	0%	$4,199.82	30-Jun-22	27-Oct-22
P01-E	Final Inspection	7	0%	$839.96	28-Oct-22	03-Nov-22
P01-E	Delivery On Site	7	0%	$1,679.93	04-Nov-22	10-Nov-22
P01-E	Submitting Vendor Data Book	5	0%	$419.98	11-Nov-22	15-Nov-22
P01-E	Delivering Spare Parts	5	0%	$419.98	11-Nov-22	15-Nov-22

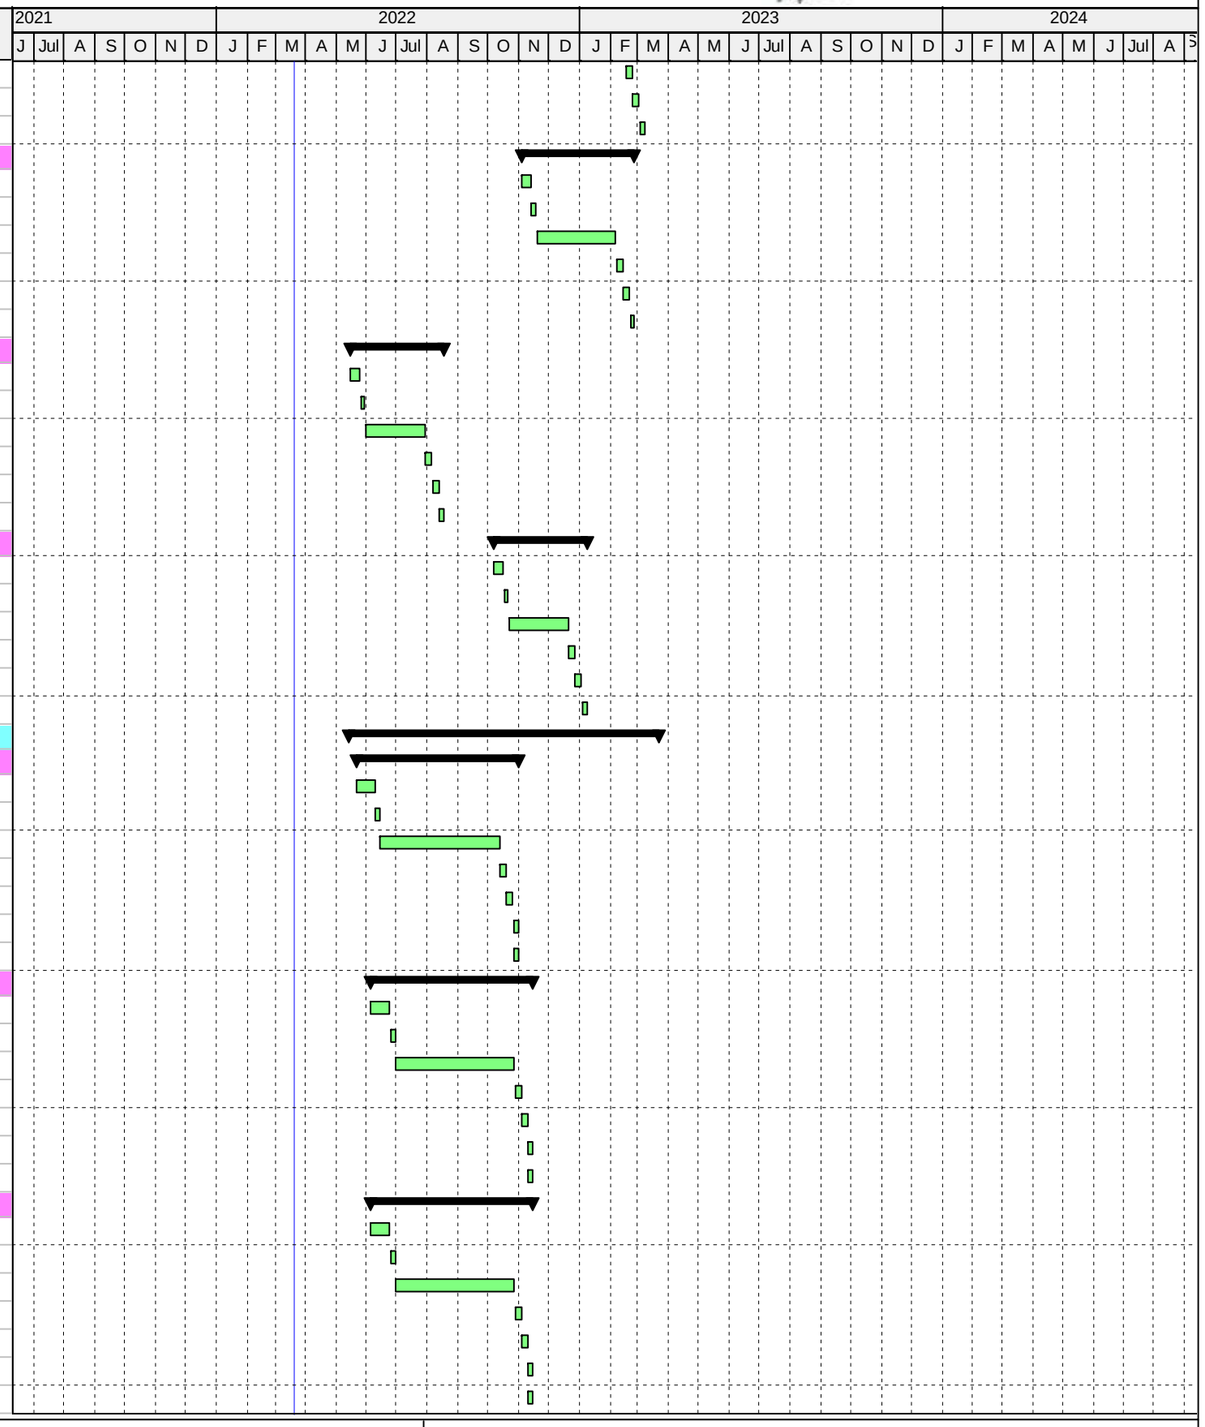


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
ON/OFF & Shutdown Valves		169	0%	$461.98	02-Jun-22	17-Nov-22
P01-E	Tendering & Selection	20	0%	$18.48	02-Jun-22	21-Jun-22
P01-E	Contract Effectiveness / PO	5	0%	$27.72	22-Jun-22	26-Jun-22
P01-E	Manufacturing / Fabrication / Supply	120	0%	$230.99	27-Jun-22	24-Oct-22
P01-E	Final Inspection	7	0%	$46.20	25-Oct-22	31-Oct-22
P01-E	Delivery On Site	7	0%	$92.40	01-Nov-22	07-Nov-22
P01-E	Submitting Vendor Data Book	5	0%	$23.10	08-Nov-22	12-Nov-22
P01-E	Delivering Spare Parts	5	0%	$23.10	13-Nov-22	17-Nov-22
Control Valves		144	0%	$461.98	04-Jul-22	24-Nov-22
P01-E	Tendering & Selection	15	0%	$18.48	04-Jul-22	18-Jul-22
P01-E	Contract Effectiveness / PO	5	0%	$27.72	19-Jul-22	23-Jul-22
P01-E	Manufacturing / Fabrication / Supply	100	0%	$230.99	24-Jul-22	31-Oct-22
P01-E	Final Inspection	7	0%	$46.20	01-Nov-22	07-Nov-22
P01-E	Delivery On Site	7	0%	$92.40	08-Nov-22	14-Nov-22
P01-E	Submitting Vendor Data Book	5	0%	$23.10	15-Nov-22	19-Nov-22
P01-E	Delivering Spare Parts	5	0%	$23.10	20-Nov-22	24-Nov-22
Pressure Safety Valves (PSV)		144	0%	$461.98	15-Jul-22	05-Dec-22
P01-E	Tendering & Selection	15	0%	$18.48	15-Jul-22	29-Jul-22
P01-E	Contract Effectiveness / PO	5	0%	$27.72	30-Jul-22	03-Aug-22
P01-E	Manufacturing / Fabrication / Supply	100	0%	$230.99	04-Aug-22	11-Nov-22
P01-E	Final Inspection	7	0%	$46.20	12-Nov-22	18-Nov-22
P01-E	Delivery On Site	7	0%	$92.40	19-Nov-22	25-Nov-22
P01-E	Submitting Vendor Data Book	5	0%	$23.10	26-Nov-22	30-Nov-22
P01-E	Delivering Spare Parts	5	0%	$23.10	01-Dec-22	05-Dec-22
F&G Devices		154	0%	$398.98	04-Aug-22	04-Jan-23
P01-E	Tendering & Selection	15	0%	$15.96	04-Aug-22	18-Aug-22
P01-E	Contract Effectiveness / PO	5	0%	$23.94	19-Aug-22	23-Aug-22
P01-E	Manufacturing / Fabrication / Supply	110	0%	$199.49	24-Aug-22	11-Dec-22
P01-E	Final Inspection	7	0%	$39.90	12-Dec-22	18-Dec-22
P01-E	Delivery On Site	7	0%	$79.80	19-Dec-22	25-Dec-22
P01-E	Submitting Vendor Data Book	5	0%	$19.95	26-Dec-22	30-Dec-22
P01-E	Delivering Spare Parts	5	0%	$19.95	31-Dec-22	04-Jan-23
Orifice and Restriction Orifice Plate		172	0%	$172.19	25-May-22	12-Nov-22
P01-E	Tendering & Selection	15	0%	$6.89	25-May-22	08-Jun-22
P01-E	Contract Effectiveness / PO	5	0%	$10.33	22-Jun-22	26-Jun-22
P01-E	Manufacturing / Fabrication / Supply	110	0%	$86.10	27-Jun-22	14-Oct-22
P01-E	Final Inspection	12	0%	$17.22	15-Oct-22	26-Oct-22
P01-E	Delivery On Site	7	0%	$34.44	27-Oct-22	02-Nov-22
P01-E	Submitting Vendor Data Book	5	0%	$8.61	03-Nov-22	07-Nov-22
P01-E	Delivering Spare Parts	5	0%	$8.61	08-Nov-22	12-Nov-22
Corrosion Coupon/Probe		176	0%	$172.19	21-May-22	12-Nov-22
P01-E	Tendering & Selection	15	0%	$6.89	21-May-22	04-Jun-22
P01-E	Contract Effectiveness / PO	5	0%	$10.33	22-Jun-22	26-Jun-22
P01-E	Manufacturing / Fabrication / Supply	110	0%	$86.10	27-Jun-22	14-Oct-22
P01-E	Final Inspection	12	0%	$17.22	15-Oct-22	26-Oct-22
P01-E	Delivery On Site	7	0%	$34.44	27-Oct-22	02-Nov-22
P01-E	Submitting Vendor Data Book	5	0%	$8.61	03-Nov-22	07-Nov-22
P01-E	Delivering Spare Parts	5	0%	$8.61	08-Nov-22	12-Nov-22
Pressure Transmitter		159	0%	$230.99	03-Jul-22	08-Dec-22

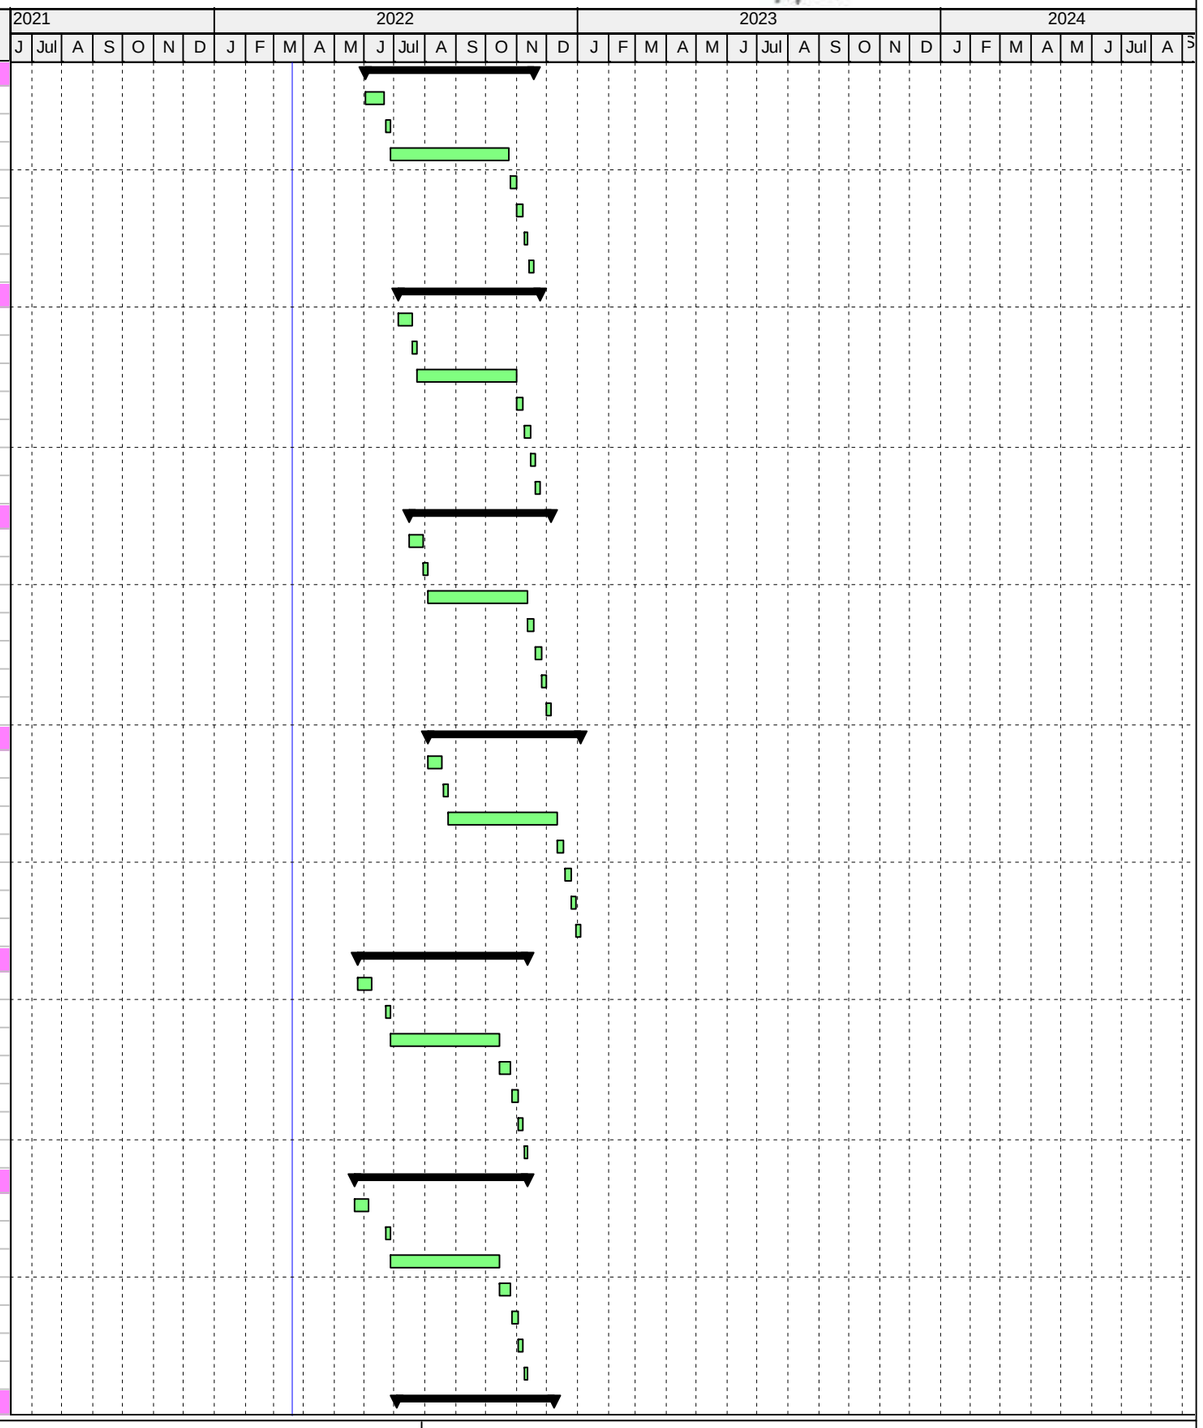


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P01-E	Tendering & Selection	15	0%	$9.24	03-Jul-22	17-Jul-22
P01-E	Contract Effectiveness / PO	5	0%	$13.86	18-Jul-22	22-Jul-22
P01-E	Manufacturing / Fabrication / Supply	110	0%	$115.50	23-Jul-22	09-Nov-22
P01-E	Final Inspection	12	0%	$23.10	10-Nov-22	21-Nov-22
P01-E	Delivery On Site	7	0%	$46.20	22-Nov-22	28-Nov-22
P01-E	Submitting Vendor Data Book	5	0%	$11.55	29-Nov-22	03-Dec-22
P01-E	Delivering Spare Parts	5	0%	$11.55	04-Dec-22	08-Dec-22
Flow Transmitter/ Diff. Pressure Transmitter		183	0%	$230.99	14-May-22	12-Nov-22
P01-E	Tendering & Selection	15	0%	$9.24	14-May-22	28-May-22
P01-E	Contract Effectiveness / PO	5	0%	$13.86	22-Jun-22	26-Jun-22
P01-E	Manufacturing / Fabrication / Supply	110	0%	$115.50	27-Jun-22	14-Oct-22
P01-E	Final Inspection	12	0%	$23.10	15-Oct-22	26-Oct-22
P01-E	Delivery On Site	7	0%	$46.20	27-Oct-22	02-Nov-22
P01-E	Submitting Vendor Data Book	5	0%	$11.55	03-Nov-22	07-Nov-22
P01-E	Delivering Spare Parts	5	0%	$11.55	08-Nov-22	12-Nov-22
Instrument/F&G Cable		127	0%	$285.59	08-Nov-22	14-Mar-23
P01-E	Tendering & Selection	15	0%	$11.42	08-Nov-22	22-Nov-22
P01-E	Contract Effectiveness / PO	5	0%	$17.14	23-Nov-22	27-Nov-22
P01-E	Manufacturing / Fabrication / Supply	90	0%	$142.79	28-Nov-22	25-Feb-23
P01-E	Final Inspection	7	0%	$28.56	26-Feb-23	04-Mar-23
P01-E	Delivery On Site	5	0%	$71.40	05-Mar-23	09-Mar-23
P01-E	Submitting Vendor Data Book	5	0%	$14.28	10-Mar-23	14-Mar-23
Instrument/F&G Junction box and Gland		139	0%	$230.99	03-Nov-22	21-Mar-23
P01-E	Tendering & Selection	15	0%	$9.24	03-Nov-22	17-Nov-22
P01-E	Contract Effectiveness / PO	5	0%	$13.86	18-Nov-22	22-Nov-22
P01-E	Manufacturing / Fabrication / Supply	100	0%	$115.50	23-Nov-22	02-Mar-23
P01-E	Final Inspection	7	0%	$23.10	03-Mar-23	09-Mar-23
P01-E	Delivery On Site	7	0%	$57.75	10-Mar-23	16-Mar-23
P01-E	Submitting Vendor Data Book	5	0%	$11.55	17-Mar-23	21-Mar-23
Instrument Installation Accessories		139	0%	$172.19	30-Sep-22	15-Feb-23
P01-E	Tendering & Selection	15	0%	$6.89	30-Sep-22	14-Oct-22
P01-E	Contract Effectiveness / PO	5	0%	$10.33	15-Oct-22	19-Oct-22
P01-E	Manufacturing / Fabrication / Supply	100	0%	$86.10	20-Oct-22	27-Jan-23
P01-E	Final Inspection	7	0%	$17.22	28-Jan-23	03-Feb-23
P01-E	Delivery On Site	7	0%	$43.05	04-Feb-23	10-Feb-23
P01-E	Submitting Vendor Data Book	5	0%	$8.61	11-Feb-23	15-Feb-23
Differential Pressure/Pressure Gauge		173	0%	$230.99	14-May-22	02-Nov-22
P01-E	Tendering & Selection	15	0%	$9.24	14-May-22	28-May-22
P01-E	Contract Effectiveness / PO	5	0%	$13.86	22-Jun-22	26-Jun-22
P01-E	Manufacturing / Fabrication / Supply	100	0%	$115.50	27-Jun-22	04-Oct-22
P01-E	Final Inspection	12	0%	$23.10	05-Oct-22	16-Oct-22
P01-E	Delivery On Site	7	0%	$46.20	17-Oct-22	23-Oct-22
P01-E	Submitting Vendor Data Book	5	0%	$11.55	24-Oct-22	28-Oct-22
P01-E	Delivering Spare Parts	5	0%	$11.55	29-Oct-22	02-Nov-22
Temperature Gauge		149	0%	$230.99	07-Jun-22	02-Nov-22
P01-E	Tendering & Selection	15	0%	$9.24	07-Jun-22	21-Jun-22
P01-E	Contract Effectiveness / PO	5	0%	$13.86	22-Jun-22	26-Jun-22
P01-E	Manufacturing / Fabrication / Supply	100	0%	$115.50	27-Jun-22	04-Oct-22
P01-E	Final Inspection	12	0%	$23.10	05-Oct-22	16-Oct-22

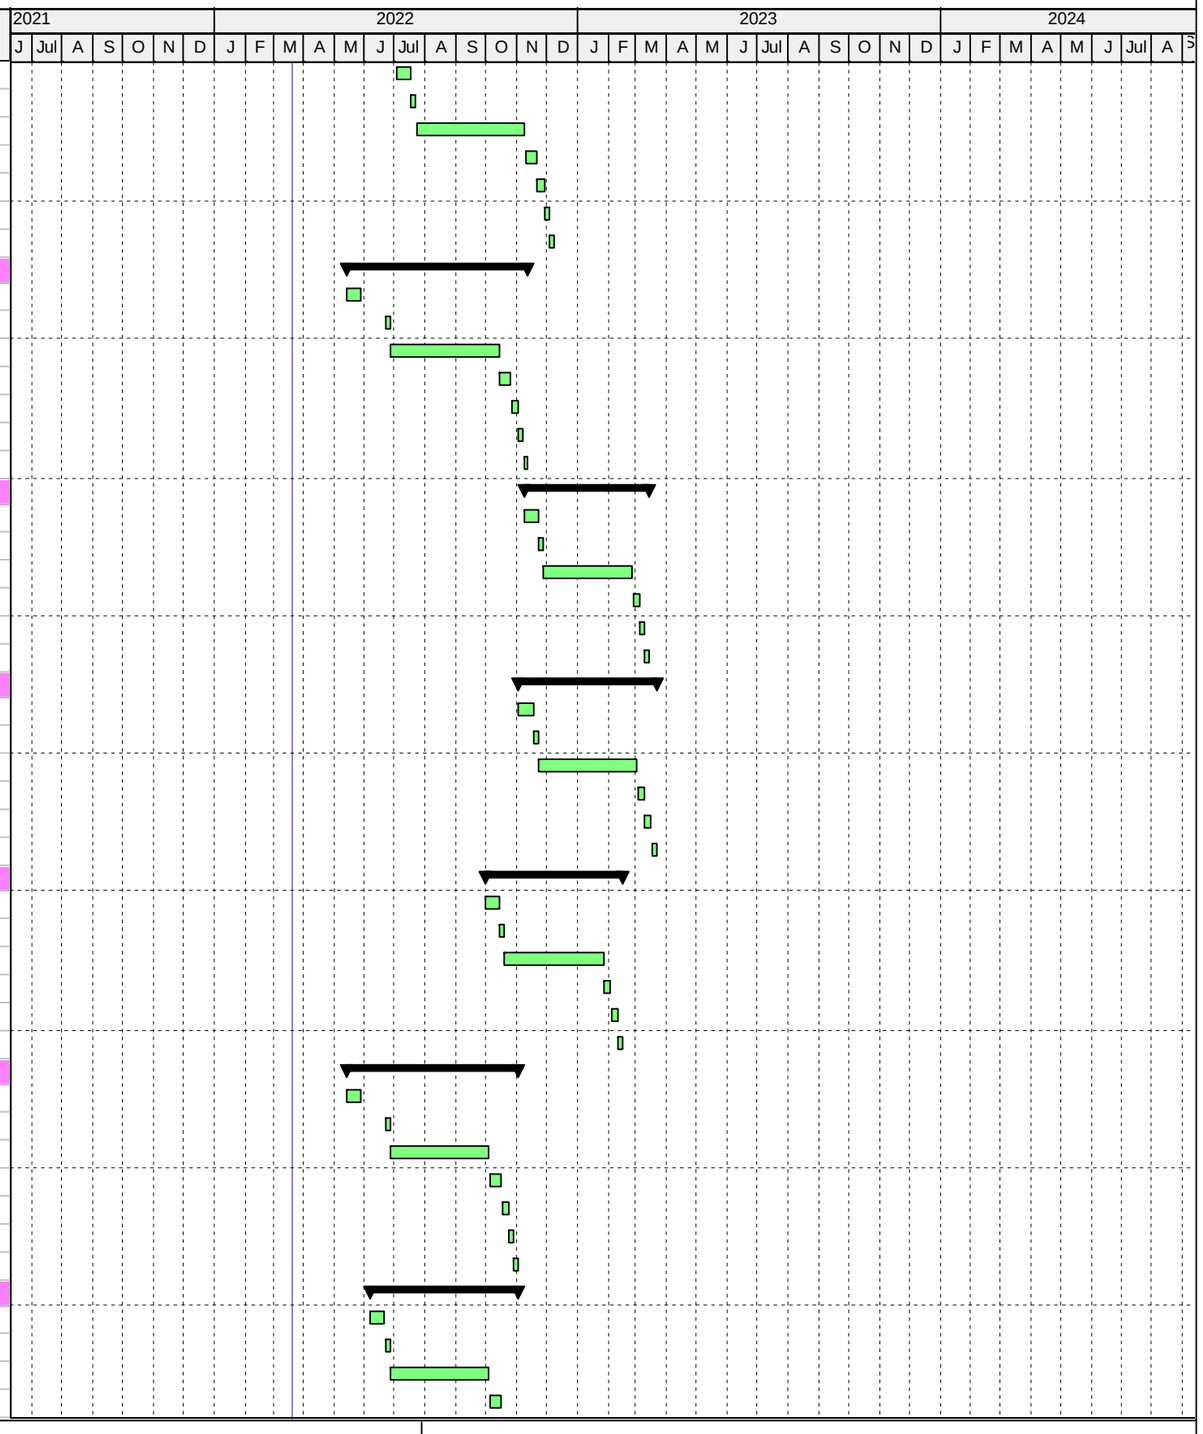


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P01-E	Delivery On Site	7	0%	$46.20	17-Oct-22	23-Oct-22
P01-E	Submitting Vendor Data Book	5	0%	$11.55	24-Oct-22	28-Oct-22
P01-E	Delivering Spare Parts	5	0%	$11.55	29-Oct-22	02-Nov-22
Instrument Tube and Fitting		129	0%	$285.59	07-Jul-22	12-Nov-22
P01-E	Tendering & Selection	10	0%	$11.42	07-Jul-22	16-Jul-22
P01-E	Contract Effectiveness / PO	5	0%	$17.14	17-Jul-22	21-Jul-22
P01-E	Manufacturing / Fabrication / Supply	90	0%	$142.79	22-Jul-22	19-Oct-22
P01-E	Final Inspection	12	0%	$28.56	20-Oct-22	31-Oct-22
P01-E	Delivery On Site	7	0%	$71.40	01-Nov-22	07-Nov-22
P01-E	Submitting Vendor Data Book	5	0%	$14.28	08-Nov-22	12-Nov-22
Instrument Cable Tray		134	0%	$172.19	30-Sep-22	10-Feb-23
P01-E	Tendering & Selection	15	0%	$6.89	30-Sep-22	14-Oct-22
P01-E	Contract Effectiveness / PO	5	0%	$10.33	15-Oct-22	19-Oct-22
P01-E	Manufacturing / Fabrication / Supply	90	0%	$86.10	20-Oct-22	17-Jan-23
P01-E	Final Inspection	12	0%	$17.22	18-Jan-23	29-Jan-23
P01-E	Delivery On Site	7	0%	$43.05	30-Jan-23	05-Feb-23
P01-E	Submitting Vendor Data Book	5	0%	$8.61	06-Feb-23	10-Feb-23
Safety & Fire Fighting - Extension of Binak B/C Manifold		121	0%	$830.82	03-Sep-22	01-Jan-23
Fire Fighting and Safety Equipment		79	0%	$619.04	03-Sep-22	20-Nov-22
P01-E	Tendering & Selection	30	0%	$24.76	03-Sep-22	02-Oct-22
P01-E	Contract Effectiveness / PO	5	0%	$37.14	03-Oct-22	07-Oct-22
P01-E	Manufacturing / Fabrication / Supply	20	0%	$309.52	08-Oct-22	27-Oct-22
P01-E	Final Inspection	12	0%	$61.90	28-Oct-22	08-Nov-22
P01-E	Delivery On Site	7	0%	$154.76	09-Nov-22	15-Nov-22
P01-E	Submitting Vendor Data Book	5	0%	$30.95	16-Nov-22	20-Nov-22
Fire Safety Sign		79	0%	$211.78	15-Oct-22	01-Jan-23
P01-E	Tendering & Selection	30	0%	$8.47	15-Oct-22	13-Nov-22
P01-E	Contract Effectiveness / PO	5	0%	$12.71	14-Nov-22	18-Nov-22
P01-E	Manufacturing / Fabrication / Supply	20	0%	$105.89	19-Nov-22	08-Dec-22
P01-E	Final Inspection	12	0%	$21.18	09-Dec-22	20-Dec-22
P01-E	Delivery On Site	5	0%	$52.94	21-Dec-22	25-Dec-22
P01-E	Submitting Vendor Data Book	5	0%	$10.59	28-Dec-22	01-Jan-23
Electrical - Extension of Binak B/C Manifold		289	0%	$14,139.14	05-Jun-22	20-Mar-23
LV Switchgear & MCC		149	0%	$2,269.33	05-Jun-22	31-Oct-22
P01-E	Tendering & Selection	15	0%	$90.77	05-Jun-22	19-Jun-22
P01-E	Contract Effectiveness / PO	5	0%	$136.16	20-Jun-22	24-Jun-22
P01-E	Manufacturing / Fabrication / Supply	110	0%	$1,134.67	25-Jun-22	12-Oct-22
P01-E	Final Inspection	7	0%	$226.93	13-Oct-22	19-Oct-22
P01-E	Delivery On Site	7	0%	$453.87	20-Oct-22	26-Oct-22
P01-E	Submitting Vendor Data Book	5	0%	$113.47	27-Oct-22	31-Oct-22
P01-E	Delivering Spare Parts	5	0%	$113.47	27-Oct-22	31-Oct-22
UPS System		139	0%	$5,671.21	12-Sep-22	28-Jan-23
P01-E	Tendering & Selection	15	0%	$226.85	12-Sep-22	26-Sep-22
P01-E	Contract Effectiveness / PO	5	0%	$340.27	27-Sep-22	01-Oct-22
P01-E	Manufacturing / Fabrication / Supply	100	0%	$2,835.60	02-Oct-22	09-Jan-23
P01-E	Final Inspection	7	0%	$567.12	10-Jan-23	16-Jan-23
P01-E	Delivery On Site	7	0%	$1,134.24	17-Jan-23	23-Jan-23
P01-E	Submitting Vendor Data Book	5	0%	$283.56	24-Jan-23	28-Jan-23
P01-E	Delivering Spare Parts	5	0%	$283.56	27-Oct-22	31-Oct-22

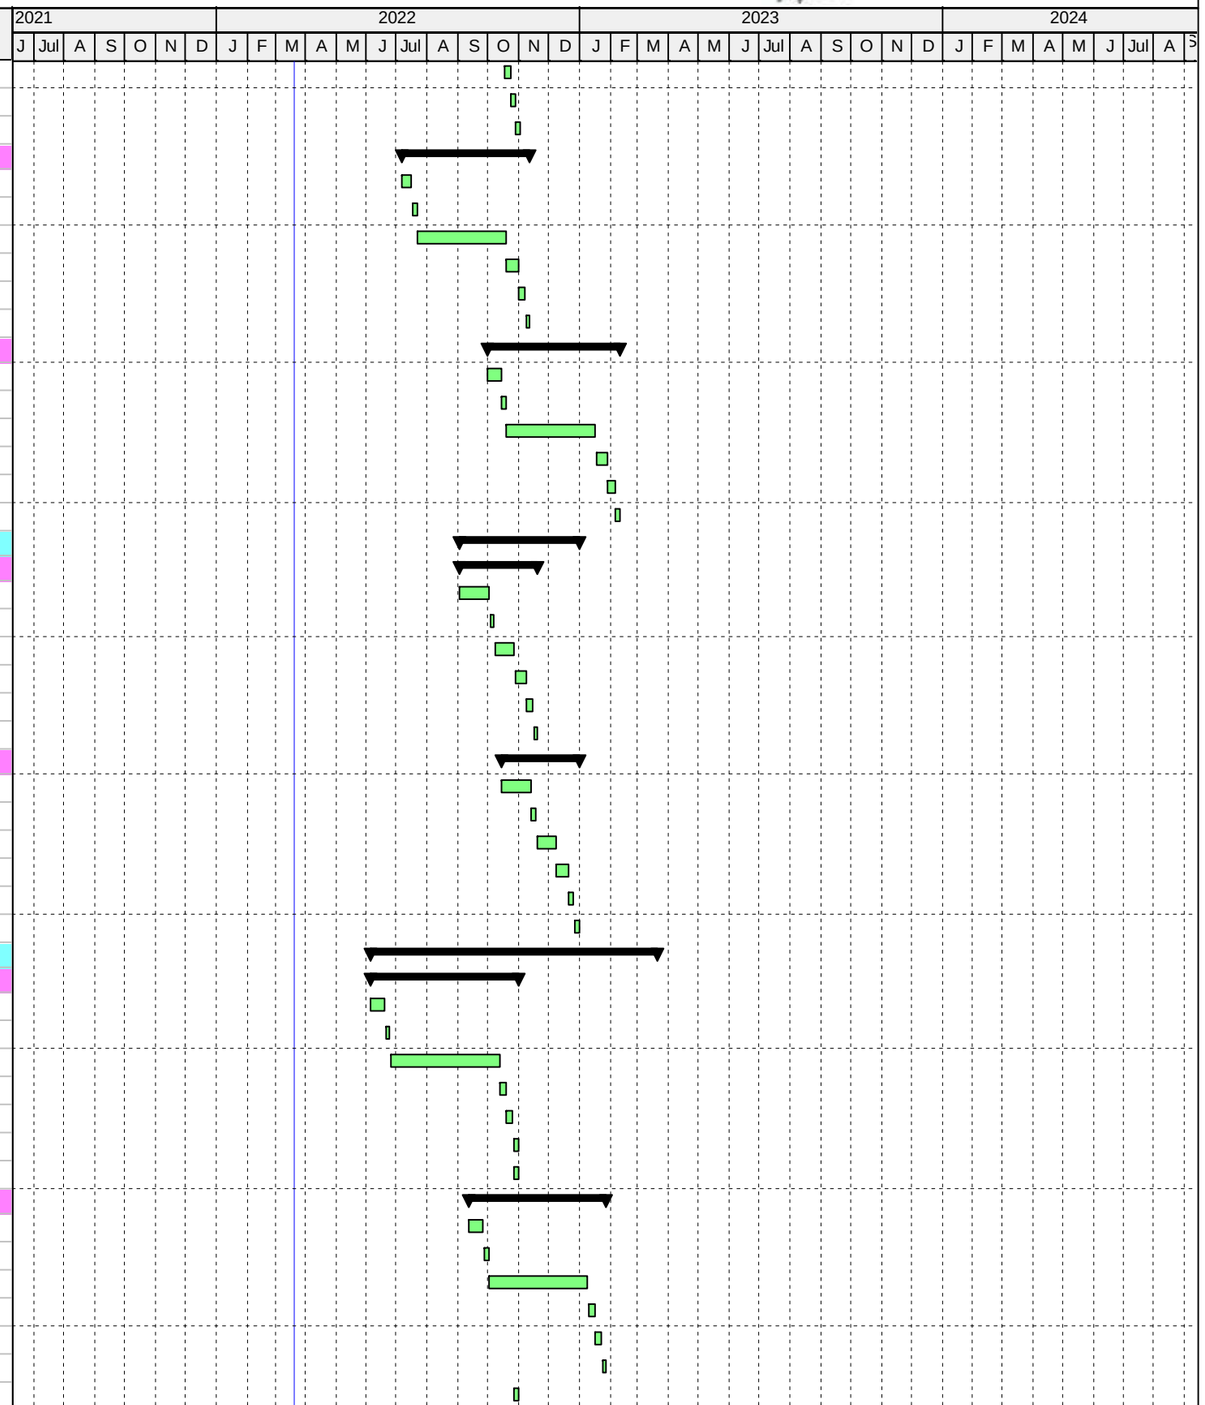

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
DC Charger		149	0%	$3,779.39	05-Jun-22	31-Oct-22
P01-E	Tendering & Selection	15	0%	$151.18	05-Jun-22	19-Jun-22
P01-E	Contract Effectiveness / PO	5	0%	$226.76	20-Jun-22	24-Jun-22
P01-E	Manufacturing / Fabrication / Supply	110	0%	$1,889.70	25-Jun-22	12-Oct-22
P01-E	Final Inspection	7	0%	$377.94	13-Oct-22	19-Oct-22
P01-E	Delivery On Site	7	0%	$755.88	20-Oct-22	26-Oct-22
P01-E	Submitting Vendor Data Book	5	0%	$188.97	27-Oct-22	31-Oct-22
P01-E	Delivering Spare Parts	5	0%	$188.97	27-Oct-22	31-Oct-22
Earthing & Lightning System		153	0%	$377.52	11-Sep-22	10-Feb-23
P01-E	Tendering & Selection	15	0%	$15.10	11-Sep-22	25-Sep-22
P01-E	Contract Effectiveness / PO	5	0%	$22.65	26-Sep-22	30-Sep-22
P01-E	Manufacturing / Fabrication / Supply	100	0%	$188.76	01-Oct-22	08-Jan-23
P01-E	Final Inspection	12	0%	$37.75	09-Jan-23	20-Jan-23
P01-E	Delivery On Site	7	0%	$75.50	21-Jan-23	27-Jan-23
P01-E	Submitting Vendor Data Book	5	0%	$18.88	28-Jan-23	01-Feb-23
P01-E	Delivering Spare Parts	5	0%	$18.88	06-Feb-23	10-Feb-23
Power & Control Cables		99	0%	$756.44	07-Dec-22	15-Mar-23
P01-E	Tendering & Selection	15	0%	$30.26	07-Dec-22	21-Dec-22
P01-E	Contract Effectiveness / PO	5	0%	$45.39	22-Dec-22	26-Dec-22
P01-E	Manufacturing / Fabrication / Supply	60	0%	$378.22	27-Dec-22	24-Feb-23
P01-E	Final Inspection	7	0%	$75.64	25-Feb-23	03-Mar-23
P01-E	Delivery On Site	7	0%	$189.11	04-Mar-23	10-Mar-23
P01-E	Submitting Vendor Data Book	5	0%	$37.82	11-Mar-23	15-Mar-23
Tray/Ladder and Accessories		227	0%	$514.66	01-Aug-22	15-Mar-23
P01-E	Tendering & Selection	15	0%	$20.59	01-Aug-22	15-Aug-22
P01-E	Contract Effectiveness / PO	5	0%	$30.88	22-Dec-22	26-Dec-22
P01-E	Manufacturing / Fabrication / Supply	60	0%	$257.33	27-Dec-22	24-Feb-23
P01-E	Final Inspection	7	0%	$51.47	25-Feb-23	03-Mar-23
P01-E	Delivery On Site	7	0%	$128.67	04-Mar-23	10-Mar-23
P01-E	Submitting Vendor Data Book	5	0%	$25.73	11-Mar-23	15-Mar-23
Electrical Bulk Items		287	0%	$770.58	07-Jun-22	20-Mar-23
P01-E	Tendering & Selection	15	0%	$30.82	07-Jun-22	21-Jun-22
P01-E	Contract Effectiveness / PO	5	0%	$46.23	22-Jun-22	26-Jun-22
P01-E	Manufacturing / Fabrication / Supply	110	0%	$385.29	27-Jun-22	14-Oct-22
P01-E	Final Inspection	12	0%	$77.06	25-Feb-23	08-Mar-23
P01-E	Delivery On Site	7	0%	$192.65	09-Mar-23	15-Mar-23
P01-E	Submitting Vendor Data Book	5	0%	$38.53	16-Mar-23	20-Mar-23
Construction		589	73.78%	$118,487.00	20-Aug-21	13-Apr-23
Wellpad and Access Road		356	100%	$84,007.28	20-Aug-21	12-Aug-22
Access Road		116	100%	$16,801.46	20-Aug-21	26-Jul-22
Wellpad Access Road		29	100%	$13,441.17	04-Sep-21	16-May-22
P01-E	Access Road Preparation	10	100%	$5,376.47	12-Sep-21	06-May-22
P01-E	Filling and Compaction	7	100%	$3,360.29	12-Sep-21	07-May-22
P01-E	Sub-Base Layer	12	100%	$4,704.41	04-Sep-21	16-May-22
Burn Pit Access Road		40	100%	$3,360.29	20-Aug-21	26-Jul-22
P01-E	ROW Preparation	10	100%	$2,184.19	20-Aug-21	14-Jul-22
P01-E	Filling and Compaction	15	100%	$672.06	20-Aug-21	25-Jul-22
P01-E	Sub-Base Layer	15	100%	$504.04	01-Jan-22	26-Jul-22
Wellpad		345	100%	$67,205.83	20-Aug-21	12-Aug-22




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Water Supply		20	100%	$4,704.41	20-Aug-21	28-Jul-22
P01-E	Water Supply	20	100%	$4,704.41	20-Aug-21	28-Jul-22
Site Preparation		20	100%	$3,360.29	01-Sep-21	29-Apr-22
P01-E	Site Preparation W018S	20	100%	$3,360.29	01-Sep-21	29-Apr-22
Mud Channel		37	100%	$10,080.87	20-Aug-21	28-May-22
P01-E	Excavation	15	100%	$1,008.09	20-Aug-21	18-May-22
P01-E	Soil Removal, Filling and Compaction of Mud Pit Area	10	100%	$1,512.13	29-Nov-21	06-May-22
P01-E	Construction of Mud Pit's Walls	7	100%	$3,528.31	14-Dec-21	24-May-22
P01-E	Supply & Installation sealling Layer	7	100%	$3,024.26	14-Dec-21	04-May-22
P01-E	Backfill	5	100%	$1,008.09	07-Jan-22	28-May-22
Mud Pit		28	100%	$27,554.39	20-Aug-21	02-Jun-22
P01-E	Soil Removal, Filling and Compaction of Mud Pit Area	15	100%	$9,644.04	20-Aug-21	17-May-22
P01-E	Construction of Mud Pit's Walls	10	100%	$5,510.88	19-Oct-21	10-May-22
P01-E	Supply & Installation sealling Layer	10	100%	$12,399.47	09-Dec-21	02-Jun-22
SepticTank		210	100%	$6,720.58	09-Dec-21	17-May-22
P01-E	Excavation & Soil Transfer	6	100%	$2,016.17	09-Dec-21	03-May-22
P01-E	Levelling	3	100%	$33.60	09-Dec-21	05-May-22
P01-E	Tank Supply	25	100%	$3,830.73	09-Dec-21	06-May-22
P01-E	Tank Execution	13	100%	$638.46	09-Dec-21	15-May-22
P01-E	Backfilling & Compaction	3	100%	$201.62	09-Dec-21	17-May-22
Burn Pit		33	100%	$6,720.58	20-Aug-21	12-Aug-22
P01-E	Soil Removal, Triming ,Filling and Compaction of Burn Pit Are	20	100%	$5,376.47	20-Aug-21	14-May-22
P01-E	Construction & Installation of Support	10	100%	$336.03	20-Aug-21	22-May-22
P01-E	Welding, Installation and Testing	5	100%	$1,008.09	21-Aug-21	12-Aug-22
Gasoil Pad		16	100%	$672.06	20-Aug-21	11-May-22
P01-E	Excavation	6	100%	$134.41	20-Aug-21	03-May-22
P01-E	Lean Concrete	2	100%	$268.82	20-Aug-21	05-May-22
P01-E	Formwork	4	100%	$201.62	20-Aug-21	08-May-22
P01-E	Armed Concrete	6	100%	$67.21	20-Aug-21	11-May-22
Surface Preparation		13	100%	$6,720.58	21-Sep-21	20-May-22
P01-E	Gravel Paving	13	100%	$6,720.58	21-Sep-21	20-May-22
Civil Work		14	100%	$672.06	21-Sep-21	17-May-22
P01-E	Excavation and Soil Removal (Cellar)	4	100%	$436.84	21-Sep-21	11-May-22
P01-E	Installation of Conductor Pipe	5	100%	$33.60	21-Sep-21	12-May-22
P01-E	Form Work (Above Cellar)	9	100%	$33.60	21-Sep-21	13-May-22
P01-E	Armed Concrete	5	100%	$168.01	21-Sep-21	17-May-22
Wellhead Facility and Flowline		162	6.6%	$31,517.54	06-Sep-21	24-Jan-23
Civil		127	15%	$11,188.73	06-Sep-21	27-Dec-22
P01-EF	Right of Way	20	20%	$8,391.55	06-Sep-21	01-Sep-22
P01-EF	Steel Works(Wellhead Facilities)	20	0%	$1,902.08	12-Nov-22	01-Dec-22
P01-EF	Construction & Installation of Shelter for Wellhead Control Pa	15	0%	$559.44	02-Dec-22	16-Dec-22
P01-EF	Well Pad Fencing	20	0%	$335.66	07-Dec-22	27-Dec-22
Flowline		39	3%	$13,394.96	16-Sep-21	17-Jan-23
P01-EF	Construction of Pipe Support	10	20%	$2,009.24	16-Sep-21	09-Dec-22
P01-EF	Installation of Pipe Supports	20	0%	$2,009.24	09-Dec-22	28-Dec-22
6" Flowline Installation		33	0%	$8,706.72	09-Dec-22	10-Jan-23
P01-E	COLD CUT	5	0%	$435.34	09-Dec-22	13-Dec-22
P01-E	Material Handeling	15	0%	$1,044.81	14-Dec-22	28-Dec-22
P01-E	Fit-Up & Welding	20	0%	$5,746.44	14-Dec-22	02-Jan-23

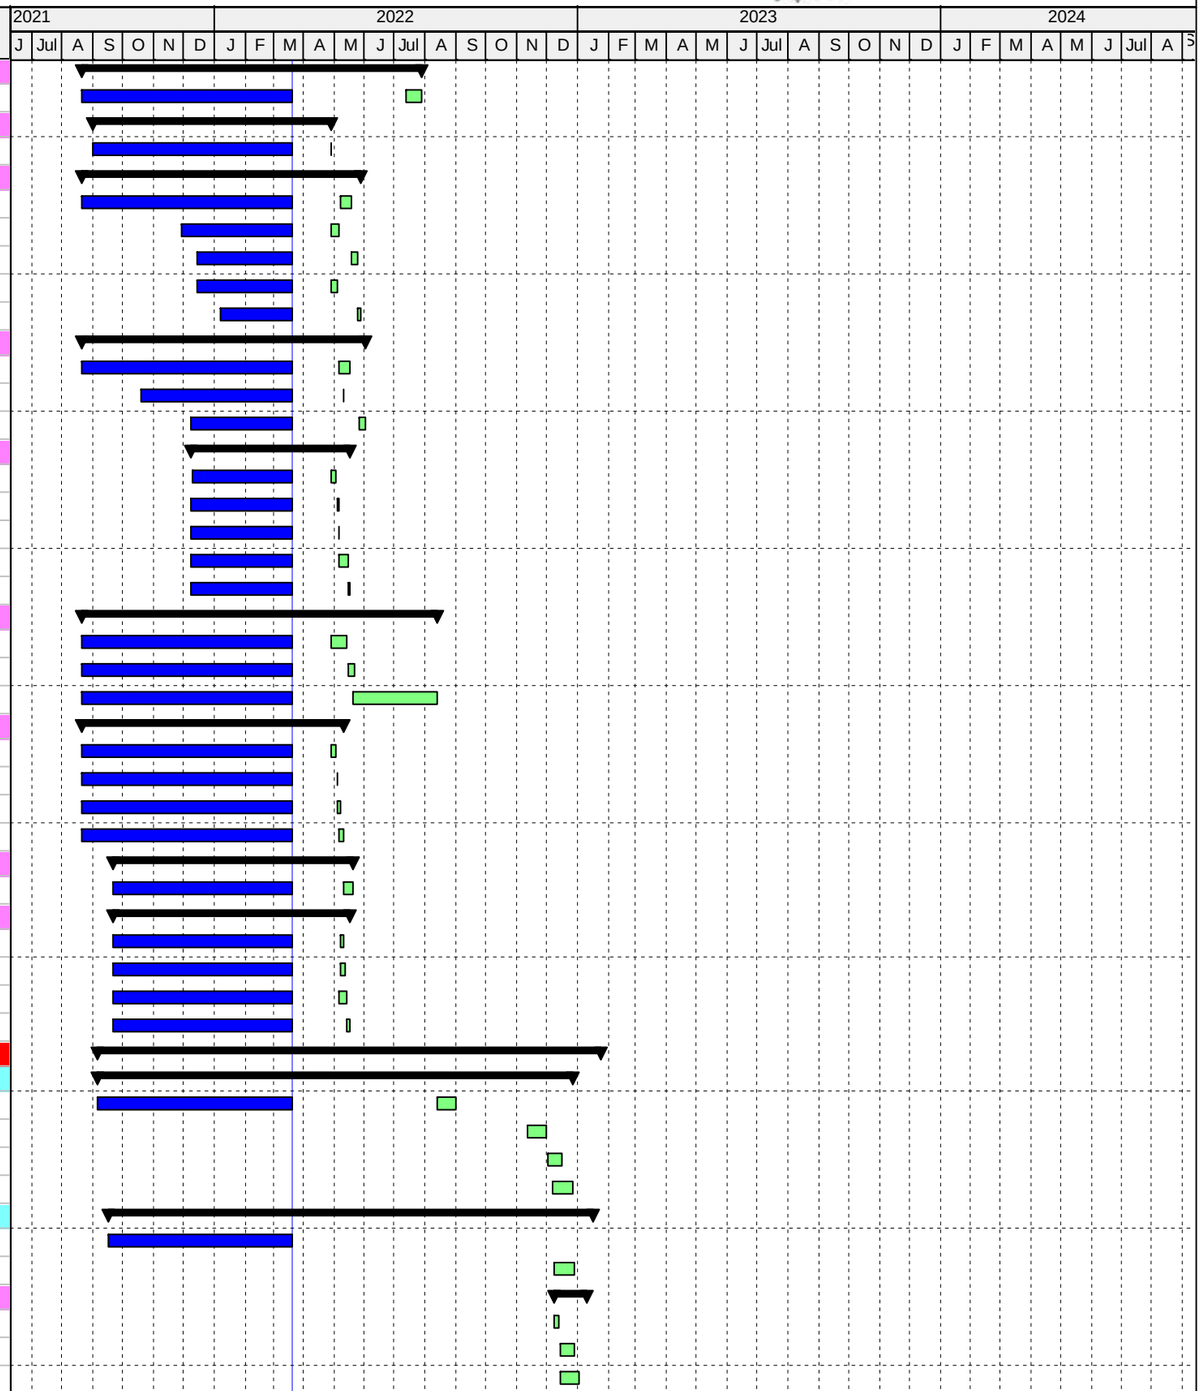


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P01-E	Bending	4	0%	$914.21	03-Jan-23	06-Jan-23
P01-E	NDT	4	0%	$565.94	07-Jan-23	10-Jan-23
Hydrostatic Test		6	0%	$669.75	11-Jan-23	17-Jan-23
P01-E	6" Pigging and Hydrostatic Test	6	0%	$669.75	11-Jan-23	17-Jan-23
Piping		14	0%	$2,678.99	29-Dec-22	12-Jan-23
P01-EI	Sweep Bend Installation	7	0%	$133.95	04-Jan-23	10-Jan-23
P01-EI	Construction of Spools (Fit up, Welding, NDT…)	7	0%	$937.65	29-Dec-22	05-Jan-23
P01-EI	Valves, Fitting and Spools Installation and Hydrotest	5	0%	$1,473.45	04-Jan-23	08-Jan-23
P01-EI	Painting	4	0%	$133.95	09-Jan-23	12-Jan-23
Instrument Works		126	0%	$2,678.99	15-Aug-22	18-Dec-22
P01-EI	Wellhead Control Panel Installation	10	0%	$1,339.50	15-Aug-22	24-Aug-22
P01-EI	Devices Installation and Piping Connecton	12	0%	$1,339.50	07-Dec-22	18-Dec-22
Pre-commissioning		13	0%	$1,575.88	11-Jan-23	24-Jan-23
P01-EI	Pre-commissioning	7	0%	$1,418.29	17-Jan-23	24-Jan-23
P01-EI	Ready for Comm.Certificate(RFCC)	2	0%	$157.59	11-Jan-23	13-Jan-23
Helipad		53	100%	$1,184.87	21-Sep-21	08-Jun-22
P01-EP	Excavation & Soil Transfer	13	100%	$118.49	21-Sep-21	08-May-22
P01-EP	Levelling	13	100%	$142.18	21-Sep-21	12-May-22
P01-EP	Lean Concrete	2	100%	$177.73	21-Sep-21	14-May-22
P01-EP	Reinforced Work	13	100%	$177.73	21-Sep-21	24-May-22
P01-EP	Form Work	13	100%	$177.73	21-Sep-21	28-May-22
P01-EP	Main Concrete Pouring	5	100%	$236.97	21-Sep-21	01-Jun-22
P01-EP	Backfilling & Compaction	4	100%	$130.34	21-Sep-21	04-Jun-22
P01-EP	Paint Marking	5	100%	$23.70	21-Sep-21	08-Jun-22
Job Site HSE Supervision (Surface)		180	60%	$236.97	21-Sep-21	09-Jan-23
P01-EP	Job Site HSE Supervision (Surface)	180	60%	$236.97	21-Sep-21	09-Jan-23
Commissioning , Startup & Handover		90	0%	$1,540.33	13-Jan-23	13-Apr-23
Commissioning		34	0%	$462.10	13-Jan-23	16-Feb-23
P01-EI	Materials & Utilities Ready for Commissioning	4	0%	$23.10	13-Jan-23	17-Jan-23
P01-EI	Receiving Facilities Ready for Commissioning	3	0%	$23.10	17-Jan-23	19-Jan-23
P01-EI	Permits Obtained for Commissioning	10	0%	$23.10	20-Jan-23	29-Jan-23
P01-EI	Integrated Commissioning	3	0%	$369.68	30-Jan-23	01-Feb-23
P01-EI	Ready for Startup Certificate (RFSU)	15	0%	$23.10	01-Feb-23	16-Feb-23
Startup & Performance Test		19	0%	$616.13	16-Feb-23	07-Mar-23
P01-EI	Startup & Performance Test Run	4	0%	$492.91	16-Feb-23	20-Feb-23
P01-EI	Start of Production (SOP)	15	0%	$123.23	20-Feb-23	07-Mar-23
Handover		37	0%	$462.10	07-Mar-23	13-Apr-23
P01-EI	Compiling & Submitting Final Documentation	20	0%	$138.63	07-Mar-23	27-Mar-23
P01-EI	Training of Operator's Personnel	2	0%	$184.84	27-Mar-23	29-Mar-23
P01-EI	Provisional Acceptance Certificate (PAC)	15	0%	$138.63	29-Mar-23	13-Apr-23
Package 02-New Well # W028 (Bangestan)		449	16.1%	$462,616.00	24-Jul-21 A	08-May-23
ENGINEERING		449	30.04%	$8,125.00	24-Jul-21 A	22-Feb-23
Basic Design Endorsement		30	100%	$406.25	31-Jul-21 A	20-Mar-22
P02-EP	Endorsement Report For Basic Design & Scope of Work	30	100%	$406.25	31-Jul-21 A	20-Mar-22
Value Engineering		75	22.5%	$243.75	01-Feb-22	02-Jul-22
P02-EP	Value Engineering Study Report	44	60%	$91.41	01-Feb-22	02-May-22
P02-EP	HAZID Report For WHF & Flowlines	44	0%	$152.34	20-May-22	02-Jul-22
Detail Design		449	42.15%	$4,468.75	24-Jul-21 A	25-Dec-22
Process		124	59.82%	$446.88	27-Jul-21 A	03-Jun-22
Basis/Criteria		54	87%	$89.38	27-Jul-21 A	12-May-22

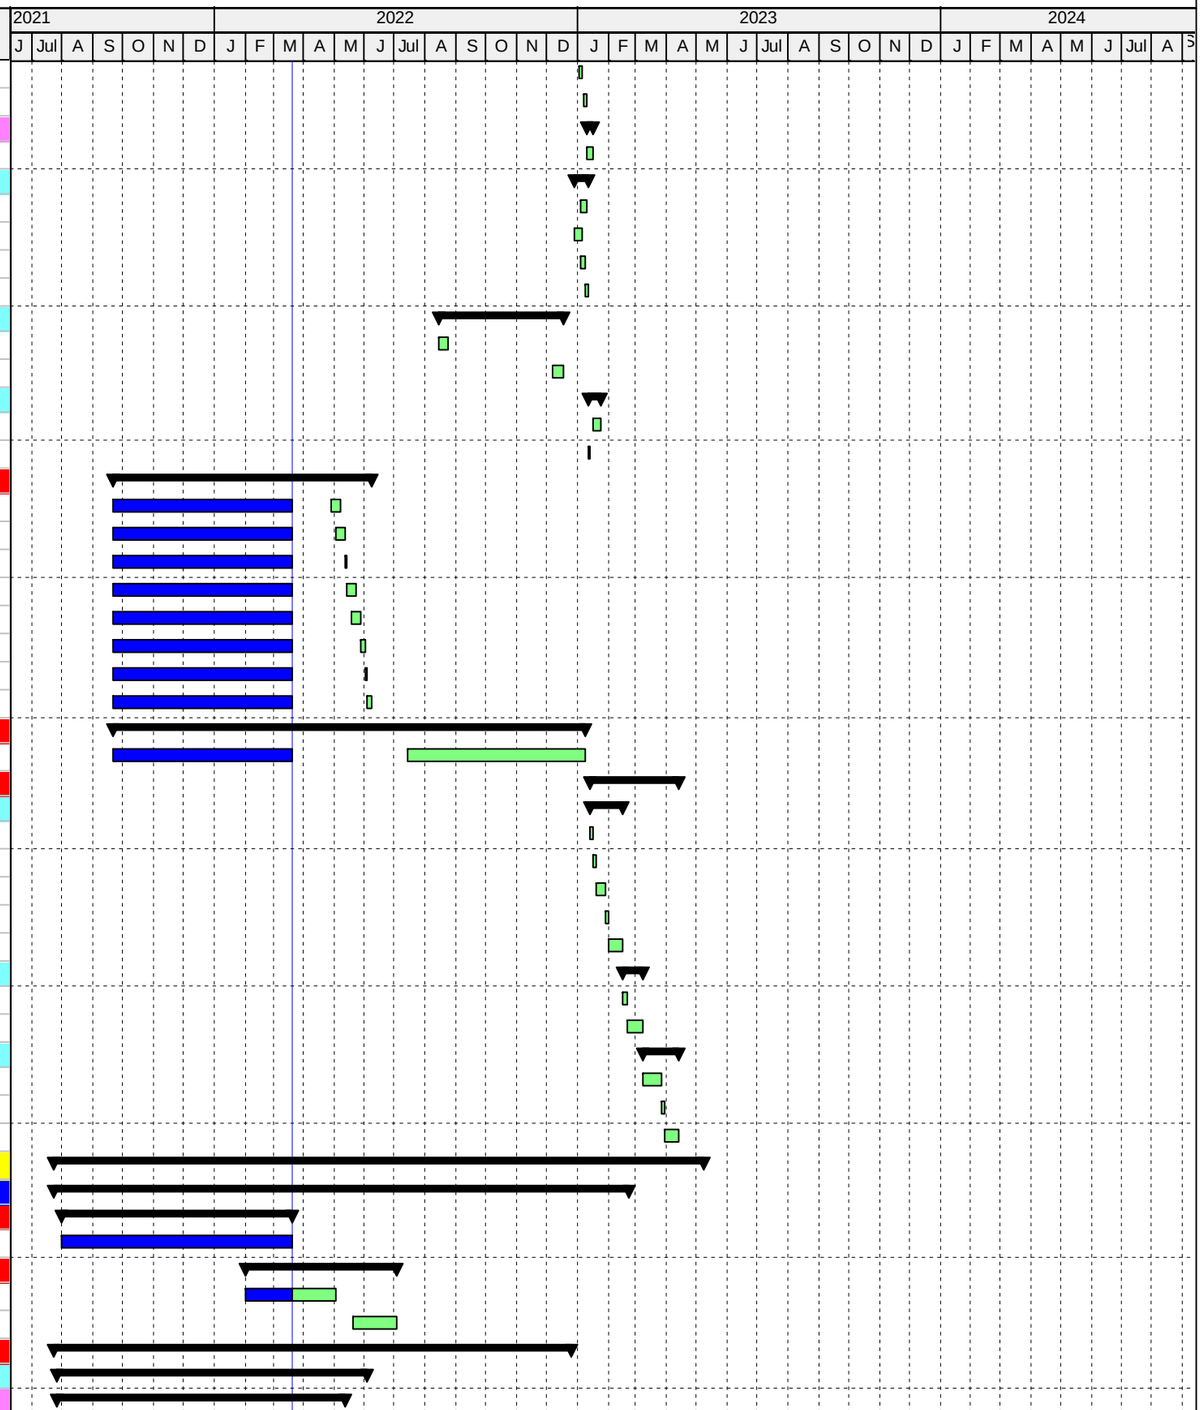


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P02-E	Process Design Criteria	39	100%	$31.28	27-Jul-21 A	20-Mar-22
P02-E	Process Basis Of Design	54	80%	$58.09	27-Jul-21 A	12-May-22
Drawing/Diagram		80	67.67%	$111.72	30-Oct-21	28-Apr-22
P02-E	Symbol & Legend For PFD and P&ID	40	80%	$6.12	30-Oct-21	28-Apr-22
P02-E	Process Flow Diagram - W028	40	60%	$68.86	02-Nov-21	28-Apr-22
P02-E	P&ID - W028	40	80%	$36.73	01-Nov-21	28-Apr-22
Philosophy		74	11.01%	$67.03	21-Nov-21	01-Jun-22
P02-E	Drainage Philosophy	44	0%	$2.65	19-Apr-22	01-Jun-22
P02-E	Control Philosophy	44	0%	$18.37	19-Apr-22	01-Jun-22
P02-E	Flare,Blow Down And Relief Philosophy	44	0%	$18.37	19-Apr-22	01-Jun-22
P02-E	Isolation Philosophy	44	60%	$12.31	21-Nov-21	02-May-22
P02-E	ESD Philosophy	44	0%	$15.34	19-Apr-22	01-Jun-22
Data Sheet		36	0%	$44.69	29-Apr-22	03-Jun-22
P02-E	Process Data Sheets For Instrument Devices - W028	36	0%	$44.69	29-Apr-22	03-Jun-22
Report		44	80%	$89.38	30-Oct-21	02-May-22
P02-E	Flowline Hydraulic Calculation Report	44	80%	$89.38	30-Oct-21	02-May-22
List		94	78.46%	$44.69	08-Nov-21	02-May-22
P02-E	Line List - W028	44	80%	$41.25	08-Nov-21	02-May-22
P02-E	Consumption List	44	60%	$3.44	23-Feb-22	02-May-22
Piping		214	32.18%	$893.75	24-Jul-21 A	18-Nov-22
Basis/Criteria		39	100%	$1.79	24-Jul-21 A	20-Mar-22
P02-E	Piping Design Criteria	39	100%	$1.79	24-Jul-21 A	20-Mar-22
Specification		198	61.98%	$35.84	24-Jul-21 A	22-May-22
P02-E	Piping Material Specification	64	60%	$30.51	28-Nov-21	22-May-22
P02-E	Specification For Color Coding and Marking	39	60%	$0.34	09-Aug-21	01-May-22
P02-E	Specification For the Design of Piping in Mechanical Packages	39	60%	$0.51	09-Aug-21	01-May-22
P02-E	Specification For Metallic Pipes	39	80%	$0.34	24-Jul-21 A	01-May-22
P02-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$0.34	24-Jul-21 A	24-Mar-22
P02-E	Specification For Painting	39	100%	$0.34	24-Jul-21 A	27-Mar-22
P02-E	Specification For Lining (Internal Protection of Equipment by F	39	60%	$0.40	09-Aug-21	04-May-22
P02-E	Specification For Material Requirements in Sour service	39	60%	$0.34	09-Aug-21	04-May-22
P02-E	Specification For Manual Valves	39	60%	$0.34	09-Aug-21	04-May-22
P02-E	Specification For Plant Piping Systems Pressure Testing	39	60%	$0.34	09-Aug-21	04-May-22
P02-E	Specification For Welding of Plant Piping System	39	60%	$0.34	09-Aug-21	04-May-22
P02-E	Specification For Flexibility Analysis	39	60%	$0.37	09-Aug-21	04-May-22
P02-E	Specification For Coating Of Underground Piping	39	100%	$0.58	24-Jul-21 A	30-Mar-22
P02-E	Specification For Pipe Support	39	60%	$0.45	09-Aug-21	07-May-22
P02-E	Specification For Piping Cleaning and Flushing	39	100%	$0.34	24-Aug-21	30-Mar-22
Data Sheets		39	60%	$1.79	27-Dec-21	12-May-22
P02-E	Data Sheets For Stone Trap	39	60%	$1.79	27-Dec-21	12-May-22
Procedure/Plan		39	100%	$2.68	24-Jul-21 A	03-Apr-22
P02-E	3D-Model (PDMS) Review Procedure	39	100%	$2.68	24-Jul-21 A	03-Apr-22
Drawing/Diagram		214	36.07%	$206.19	08-Nov-21	18-Nov-22
P02-E	Standard Pipe Support Drawings	14	100%	$6.21	19-Feb-22	20-Mar-22
P02-E	Piping Assembly Drawing	35	0%	$20.95	29-Apr-22	02-Jun-22
P02-E	Piping Hydrostatic Test Diagram - Sub Surface	30	0%	$3.36	03-Jun-22	02-Jul-22
P02-E	Plot Plan Drawing - W028	30	60%	$62.06	02-Feb-22	18-Apr-22
P02-E	Piping Plan - W028	30	0%	$37.24	20-Sep-22	19-Oct-22
P02-E	Isometric Drawings - W028	30	0%	$24.83	20-Oct-22	18-Nov-22

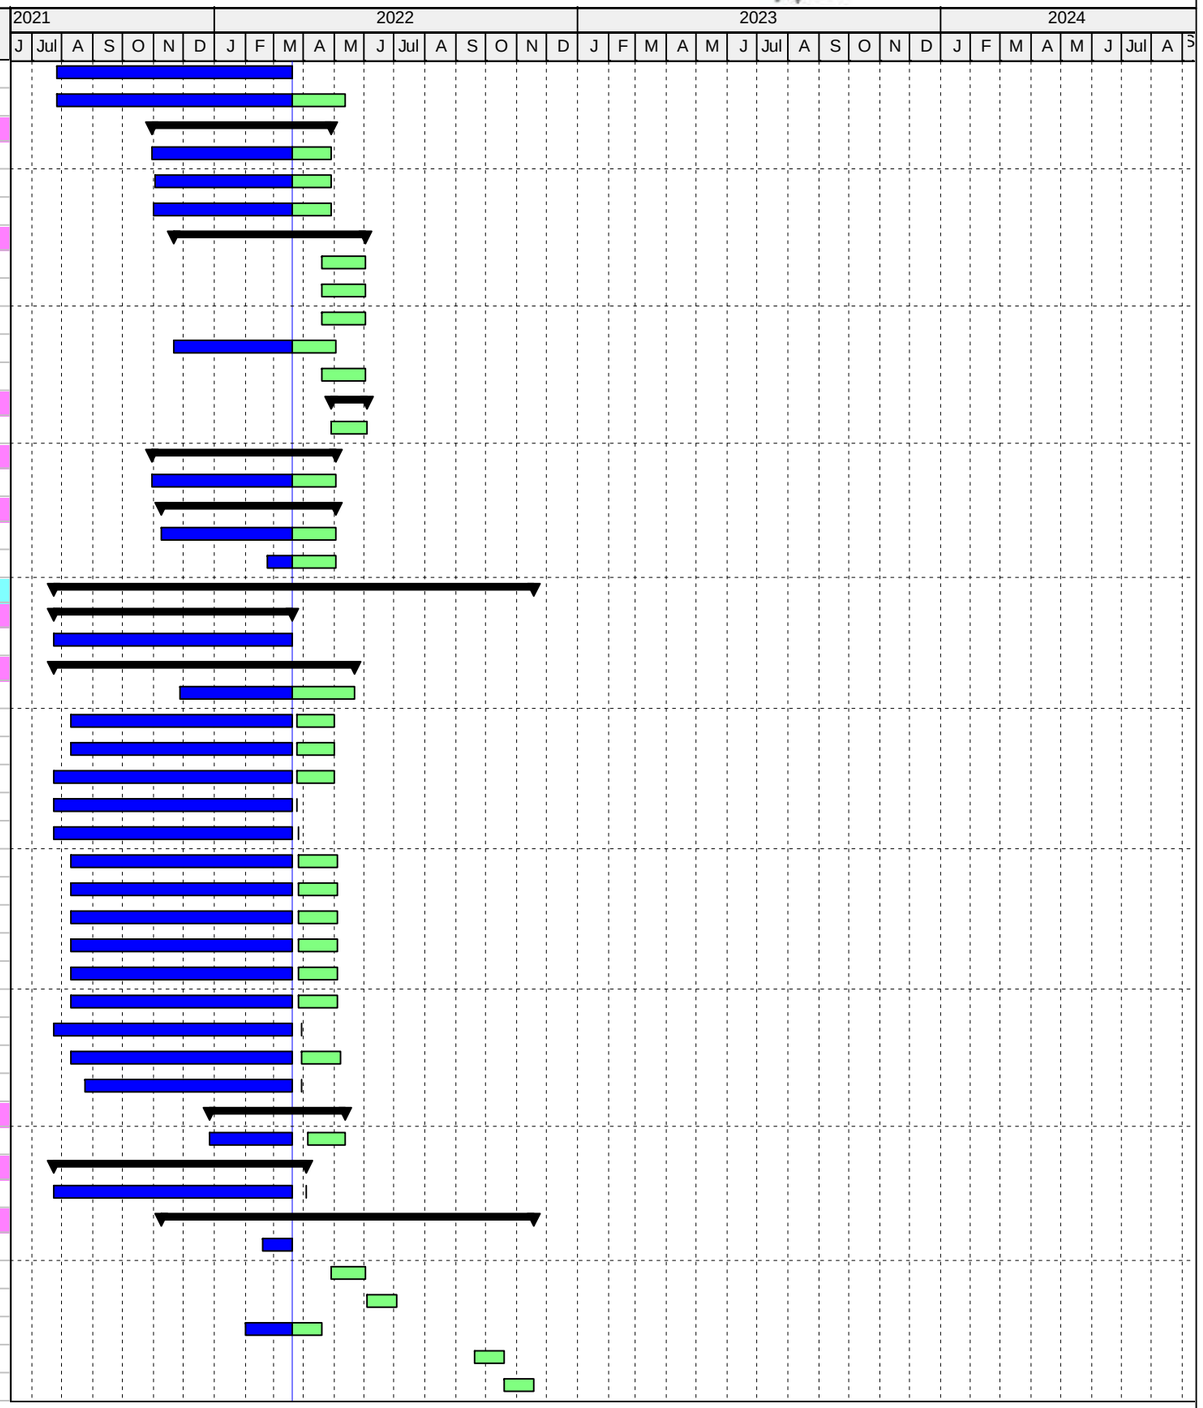


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P02-E	Material Flow Diagram - W028	35	60%	$51.55	08-Nov-21	12-May-22
List		140	0%	$35.84	03-May-22	19-Sep-22
P02-E	Piping Support List - W028	44	0%	$17.92	07-Aug-22	19-Sep-22
P02-E	Critical Line List - W028	39	0%	$17.92	03-May-22	10-Jun-22
Report		93	5.36%	$448.22	28-Nov-21	06-Aug-22
P02-E	PDMS Model Review Report (60%) - W028	35	0%	$244.50	03-Jun-22	07-Jul-22
P02-E	PDMS Model Review Report (90%) - W028	30	0%	$163.64	08-Jul-22	06-Aug-22
P02-E	Piping Corrosion Study & Material Selection Report	40	60%	$40.07	28-Nov-21	12-May-22
MTO		7	100%	$161.41	04-Dec-21	07-Aug-22
P02-E	MTO For Pipes - W028	7	100%	$26.91	04-Dec-21	07-Aug-22
P02-E	MTO For Fittings - W028	7	100%	$26.89	20-Dec-21	07-Aug-22
P02-E	MTO For Flanges - W028	7	100%	$26.89	20-Dec-21	07-Aug-22
P02-E	MTO For Manual Valves - W028	7	100%	$26.91	20-Dec-21	07-Aug-22
P02-E	MTO For Gaskets - W028	7	100%	$26.91	20-Dec-21	07-Aug-22
P02-E	MTO For Bolt & Nuts - W028	7	100%	$26.91	20-Dec-21	07-Aug-22
Pipeline & Flow line		182	38.56%	$134.06	24-Jul-21 A	22-May-22
Basis/Criteria		39	100%	$0.94	28-Aug-21	20-Mar-22
P02-E	Pipeline Design Criteria	39	100%	$0.94	28-Aug-21	20-Mar-22
Specification		49	81.84%	$13.07	24-Jul-21 A	07-May-22
P02-E	Specification For Line Pipes	39	100%	$0.25	24-Jul-21 A	24-Mar-22
P02-E	Specification For Pipeline Cold Bending	39	80%	$0.23	28-Aug-21	01-May-22
P02-E	Specification For Barred Tee	39	80%	$0.23	28-Aug-21	01-May-22
P02-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$0.23	24-Jul-21 A	24-Mar-22
P02-E	Specification For Pipeline Valves	39	80%	$0.23	28-Aug-21	01-May-22
P02-E	Specification For Pipeline Coating	39	100%	$0.23	24-Jul-21 A	24-Mar-22
P02-E	Specification For Pipeline Flushing, Cleaning And Hydrostatic	39	100%	$0.25	24-Jul-21 A	27-Mar-22
P02-E	Specification For Welding of Transportation Pipeline	39	80%	$0.23	12-Dec-21	04-May-22
P02-E	Specification For Pipeline Stress Analysis	39	80%	$0.23	24-Jul-21 A	04-May-22
P02-E	Specification For Pipeline Insulation Joint	39	100%	$0.23	24-Jul-21 A	27-Mar-22
P02-E	Specification For Pipeline Construction	39	80%	$0.23	25-Jan-22	04-May-22
P02-E	Specification For Anchor Flanges	39	80%	$0.25	28-Aug-21	07-May-22
P02-E	Specification For Pigs	39	80%	$0.23	28-Aug-21	07-May-22
P02-E	Pipeline Material Specification	44	80%	$10.03	27-Oct-21	02-May-22
Drawings		84	21.47%	$74.30	27-Jul-21 A	12-May-22
P02-E	Pipeline Standard Support Drawings	14	100%	$2.48	27-Jul-21 A	20-Mar-22
P02-E	Standard Drawing For Above Ground Pipeline Construction F	44	80%	$2.16	27-Nov-21	12-May-22
P02-E	Standard Drawing For Under Ground Pipeline Construction F	44	100%	$2.16	04-Dec-21	30-Mar-22
P02-E	Pipeline Standard Drawing For Anchor Support	44	60%	$2.16	22-Dec-21	12-May-22
P02-E	Standard Drawing For A/G Pipeline Road Crossing	44	60%	$2.16	05-Dec-21	12-May-22
P02-E	Standard Drawing For Existing Pipeline Crossing	44	60%	$2.16	18-Dec-21	12-May-22
P02-E	Pipeline Standard Drawing For Irish Crossing	44	60%	$2.04	04-Dec-21	12-May-22
P02-E	Pipeline Standard Drawing For Water - Way Crossing	44	60%	$2.04	22-Nov-21	12-May-22
P02-E	Pipeline Standard Drawing For Pig Signaller Concrete Pit	44	60%	$2.04	27-Nov-21	12-May-22
P02-E	Pipeline Standard Drawing For H-Pipe Support	44	100%	$2.04	27-Nov-21	30-Mar-22
P02-E	Flowline Transversal Drawings - W028	44	0%	$48.26	20-Mar-22	02-May-22
P02-E	Pipeline Hydrostatic Test Diagram - Sub Surface	44	0%	$4.57	20-Mar-22	02-May-22
Procedure/Plan		44	0%	$2.71	09-Apr-22	22-May-22
P02-E	Pipeline Hydrostatic Test Diagram - Sub Surface	44	0%	$2.71	09-Apr-22	22-May-22
List		30	0%	$14.71	20-Mar-22	18-Apr-22

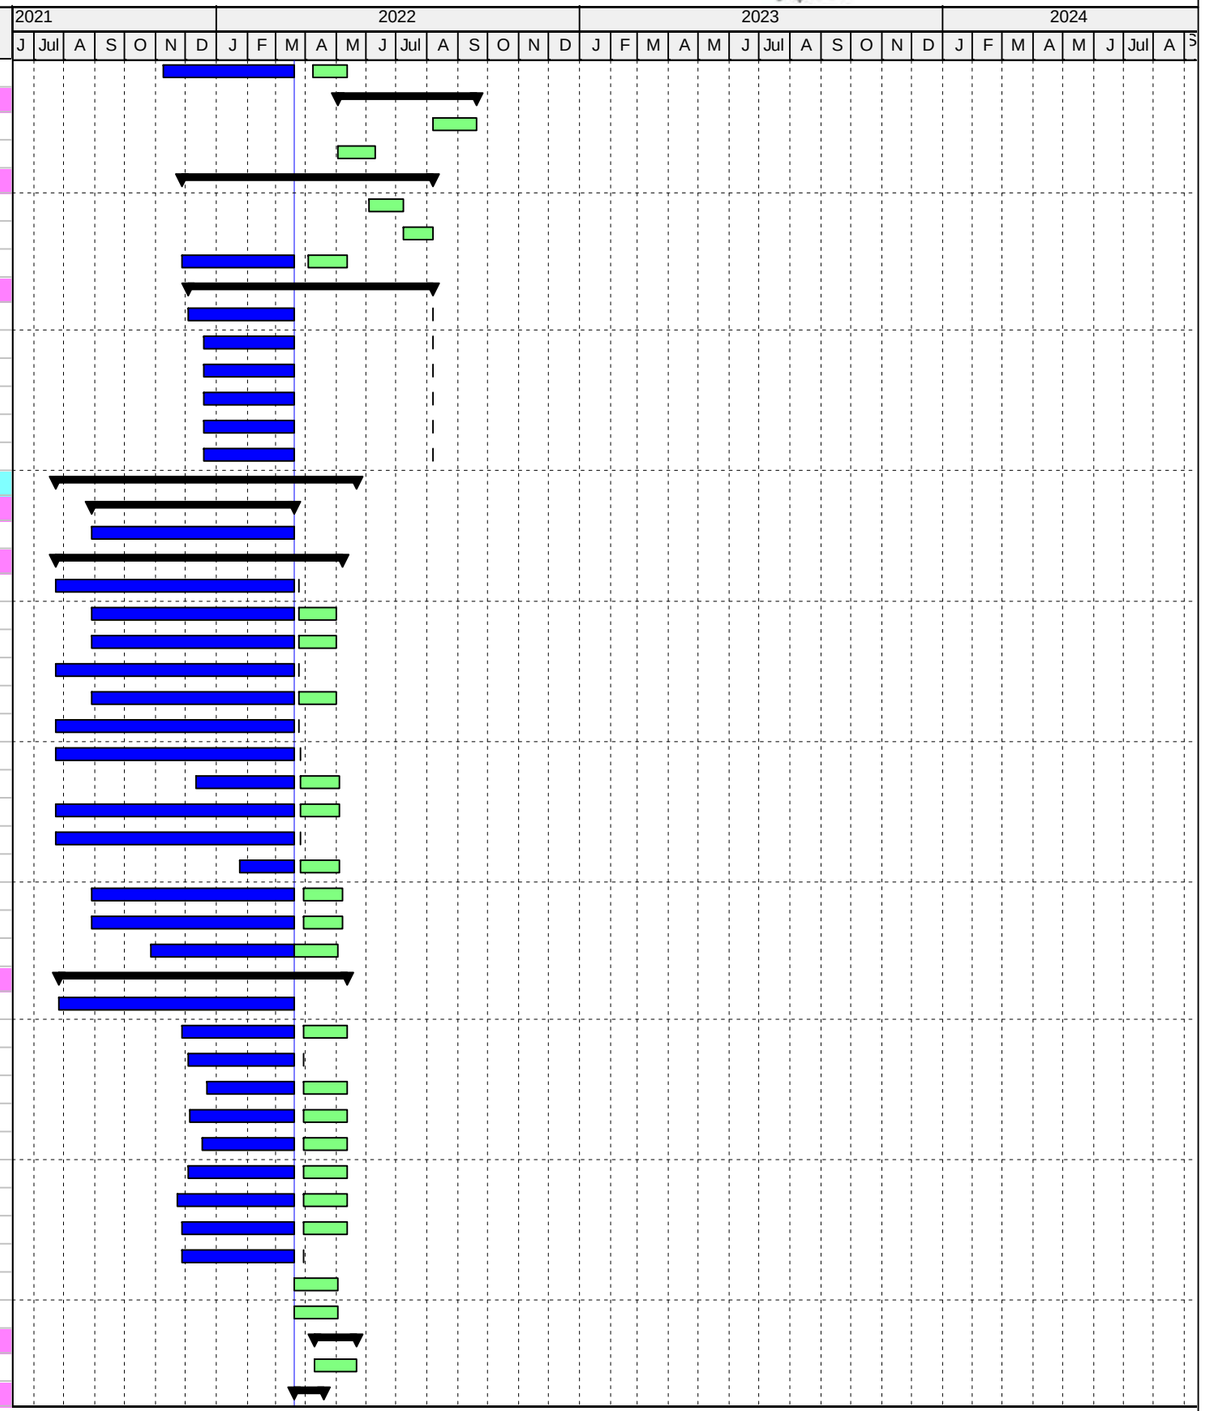


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P02-E	Road Crossing Location List	30	0%	$14.71	20-Mar-22	18-Apr-22
Report		44	80%	$21.34	27-Oct-21	22-May-22
P02-E	Pipeline Corrosion Study & Material Selection Report	44	80%	$21.34	27-Oct-21	22-May-22
MTO		7	100%	$7.00	22-Aug-21	20-Mar-22
P02-E	MTO For Line Pipes (Flowlines) - W028	7	100%	$7.00	22-Aug-21	20-Mar-22
Control & Instrumentation		147	78.5%	$357.50	26-Jul-21 A	20-Aug-22
Basis/Criteria		44	94.56%	$15.84	14-Aug-21	29-Apr-22
P02-E	Fire & Gas Detection Design Criteria	38	100%	$13.68	14-Aug-21	27-Mar-22
P02-E	Instrument & Control System Design Criteria	38	60%	$2.16	03-Jan-22	29-Apr-22
Specification		42	86.9%	$81.33	26-Jul-21 A	26-Apr-22
P02-E	Specification For WHCP/HPU	38	80%	$53.29	08-Aug-21	26-Apr-22
P02-E	Specification For Instrumentation	39	100%	$28.04	26-Jul-21 A	23-Mar-22
Data Sheets		120	80%	$20.34	22-Aug-21	24-May-22
P02-E	Data Sheets For WHCP/HPU - Wellheads	49	80%	$10.04	22-Aug-21	07-May-22
P02-E	Data Sheets For Pressure Gauge - Wellheads	42	80%	$5.15	07-Dec-21	24-May-22
P02-E	Data Sheets For Temperature Gauge - Wellheads	42	80%	$5.15	07-Dec-21	24-May-22
Drawing/Diagram		100	26.69%	$83.58	22-Aug-21	20-Aug-22
P02-E	Instrument Hook-up Diagram - Wellheads	42	80%	$13.23	14-Nov-21	12-May-22
P02-E	WHCP Hydraulic \Peneumatic Diagrams - Wellheads	42	100%	$11.73	22-Aug-21	19-Apr-22
P02-E	Instrument Location Layout Drawing - W028	44	0%	$58.63	08-Jul-22	20-Aug-22
List		7	100%	$43.40	10-Nov-21	13-May-22
P02-E	Instrument Index For New Wells & Manifold Extension	7	100%	$43.40	10-Nov-21	13-May-22
MTO		67	100%	$113.01	14-Nov-21	13-May-22
P02-E	MTO For Instrument Tube and Fitting - W028	7	100%	$56.50	14-Nov-21	13-May-22
P02-E	MTO For Instrument Cable Tray - W028	7	100%	$56.50	14-Nov-21	29-Apr-22
Safety		148	61.44%	$134.06	24-Jul-21 A	05-Aug-22
Basis/Criteria		44	100%	$13.41	29-Aug-21	19-Apr-22
P02-E	Active Fire Protection and Safety Concept	44	100%	$13.41	29-Aug-21	19-Apr-22
Specification		47	88.24%	$26.81	24-Jul-21 A	09-May-22
P02-E	Specification For Fire Fighting Equipment	44	100%	$4.73	29-Aug-21	24-Mar-22
P02-E	Specification For Hazardous Area Classification	44	100%	$4.73	24-Jul-21 A	24-Mar-22
P02-E	Specification For Fire Water System	44	80%	$6.31	24-Jul-21 A	09-May-22
P02-E	Specification For Environmental Job	44	60%	$4.73	11-Aug-21	06-May-22
P02-E	Specification For Total Flooding System	44	100%	$6.31	24-Jul-21 A	27-Mar-22
Data Sheets		47	100%	$13.41	08-Dec-21	27-Mar-22
P02-E	Data Sheets For Fire Fighting Equipment	44	100%	$4.47	08-Dec-21	24-Mar-22
P02-E	Data Sheets For Safety Equipment	44	100%	$4.47	08-Dec-21	27-Mar-22
P02-E	Data Sheets For Safety Sign	44	100%	$4.47	08-Dec-21	27-Mar-22
Drawing/Diagram		108	14.45%	$53.63	29-Aug-21	04-Aug-22
P02-E	Typical Installation Detail for Safety & Fire Fighting Equipment	14	100%	$3.87	29-Dec-21	27-Mar-22
P02-E	Symbol & Legend For Safety & Firefighting Systems	44	100%	$3.87	29-Aug-21	27-Mar-22
P02-E	Hazardous Area Classification Layout - W028	44	0%	$15.30	12-Jun-22	25-Jul-22
P02-E	Safety & Fire Fighting Equipment Location Layout - W028	44	0%	$15.30	19-Apr-22	01-Jun-22
P02-E	Escape Route & Safety Sign Layout - W028	64	0%	$15.29	02-Jun-22	04-Aug-22
List		44	80%	$13.41	09-Nov-21	11-Jun-22
P02-E	Hazard Source List - W028	44	80%	$13.41	09-Nov-21	11-Jun-22
MTO		10	100%	$13.41	08-Dec-21	05-Aug-22
P02-E	MTO For Fire Fighting & Safety Equipment - W028	7	100%	$7.66	08-Dec-21	05-Aug-22
P02-E	MTO For Safety Sign - W028	5	100%	$5.75	08-Dec-21	05-Aug-22
Architecture		84	60%	$134.06	18-Dec-21	01-Jun-22

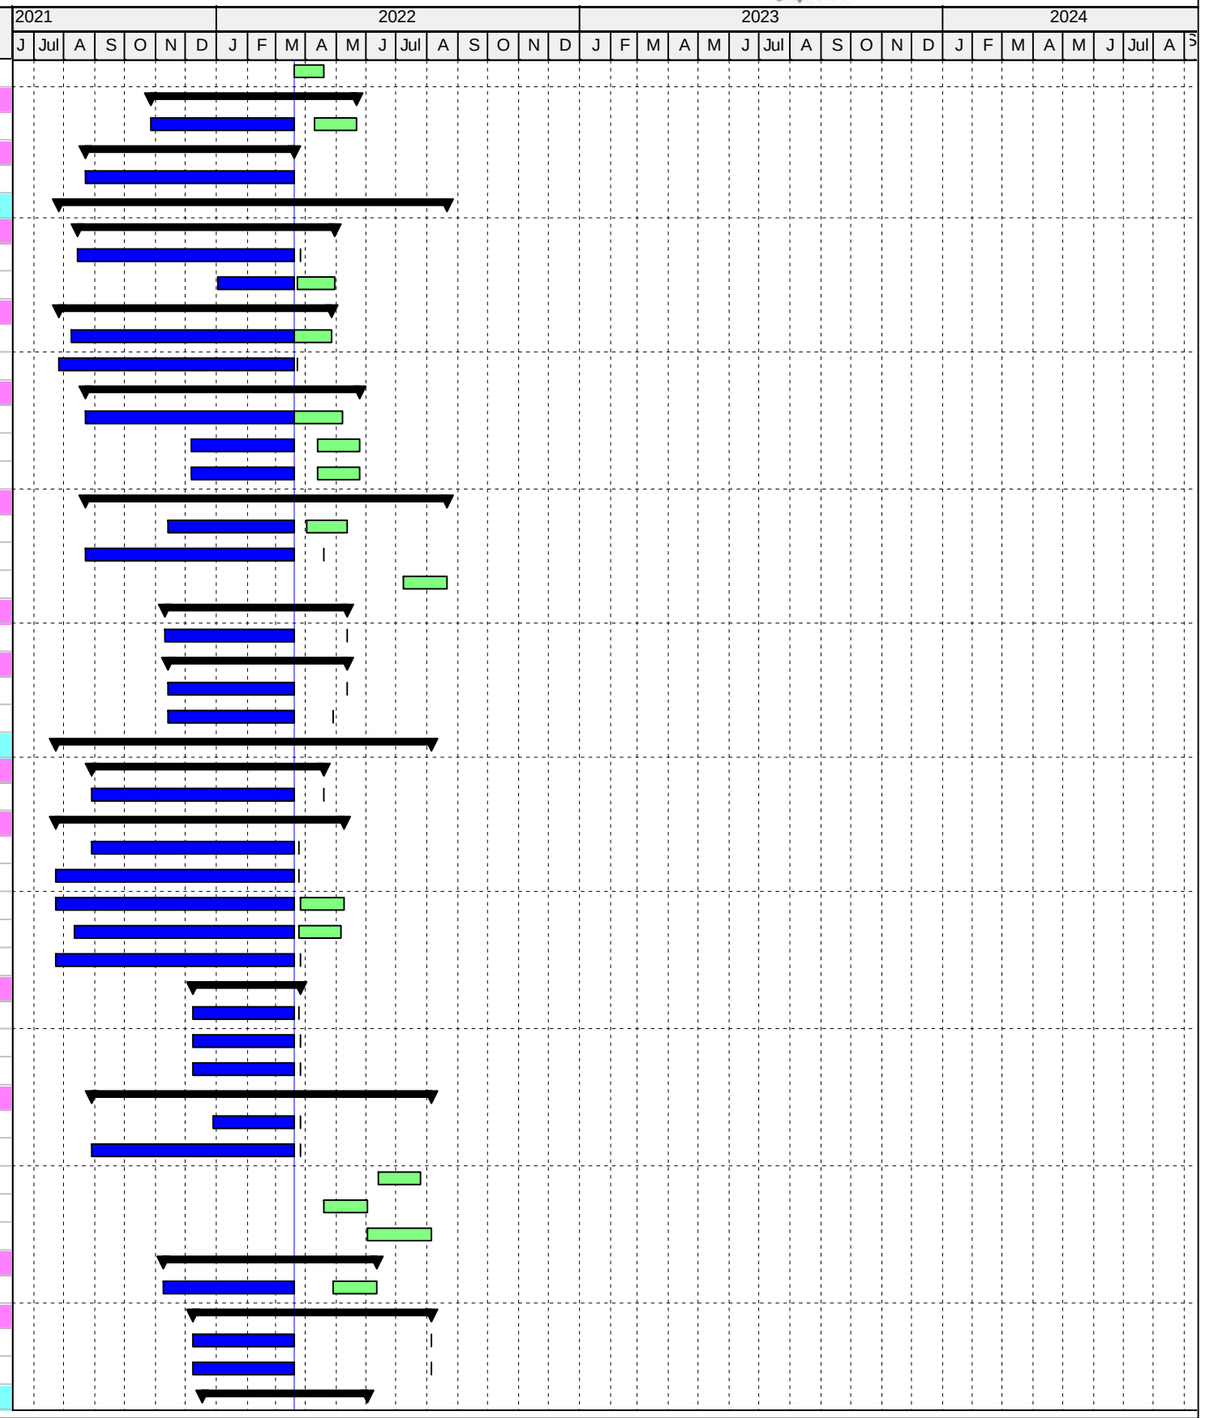


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Basis/Criteria		74	60%	$26.81	08-Feb-22	01-Jun-22
P02-E	Architectural Design Criteria	74	60%	$26.81	08-Feb-22	01-Jun-22
Drawing/Diagram		84	60%	$107.25	18-Dec-21	01-Jun-22
P02-E	Architectural Drawing For WHCP/HPU Shelter of Well Pads -	44	60%	$77.50	26-Feb-22	01-Jun-22
P02-E	Standard Drawing for Architectural Details	44	60%	$29.75	18-Dec-21	02-May-22
Civil		449	66.97%	$804.38	01-Aug-21	25-Dec-22
Basis/Criteria		90	20%	$2.98	13-Feb-22	22-May-22
P02-E	Civil Design Criteria	64	60%	$0.99	13-Feb-22	22-May-22
P02-E	Design Criteria for Sewerage & Drainage	44	0%	$0.99	24-Mar-22	06-May-22
P02-E	Design Criteria for Road and Paving	44	0%	$0.99	27-Mar-22	09-May-22
Specification		94	72.14%	$15.04	09-Aug-21	06-Jun-22
P02-E	Specification For Civil Works	79	0%	$1.50	20-Mar-22	06-Jun-22
P02-E	Specification For Road & Paving	64	80%	$3.01	09-Aug-21	22-May-22
P02-E	Specification For Fence & Gate	64	100%	$3.01	18-Sep-21	20-Mar-22
P02-E	Specification For Earth Work	64	80%	$3.01	09-Aug-21	22-May-22
P02-E	Specification For Sewerage & Drainage	64	100%	$3.01	09-Aug-21	20-Mar-22
P02-E	Specification For Geological & Geotechnical Survey	44	0%	$1.50	20-Mar-22	02-May-22
Calculation		374	70%	$72.23	05-Dec-21	25-Dec-22
P02-E	Calculation Note For Heli Pad, Well Pad & Diesel Storage Pa	38	60%	$36.12	05-Dec-21	10-Jun-22
P02-E	Calculation Note For Flood Control	39	80%	$36.12	05-Dec-21	25-Dec-22
Drawing/Diagram		94	74.26%	$641.89	01-Aug-21	22-May-22
P02-E	Standard Drawing For Civil Works	50	0%	$10.59	30-Mar-22	18-May-22
P02-E	Standard Drawing For Slope Protection Details	50	100%	$10.59	22-Aug-21	30-Mar-22
P02-E	Standard Drawing For Roads	50	80%	$10.59	22-Aug-21	18-May-22
P02-E	Standard Drawing For Electrical Cable Trench	50	100%	$10.59	22-Aug-21	30-Mar-22
P02-E	Standard Drawing For Manholes	50	80%	$10.59	22-Aug-21	18-May-22
P02-E	Standard Drawing For Catch Basins	50	80%	$10.59	22-Aug-21	22-May-22
P02-E	Standard Drawing For Sewerage & Drainage Details	50	60%	$10.59	02-Feb-22	22-May-22
P02-E	Standard Drawing For Civil Underground Crossings	38	60%	$18.04	07-Feb-22	10-May-22
P02-E	Standard Drawing For Fence & Gate Details	50	100%	$10.59	18-Sep-21	03-Apr-22
P02-E	Standard Drawing For Concrete Continues Weight	38	100%	$17.65	01-Aug-21	20-Mar-22
P02-E	Standard Drawing For Major Floodway Crossing	38	0%	$17.65	03-Apr-22	10-May-22
P02-E	Standard Drawing For Culvert & Details	25	100%	$17.65	25-Sep-21	03-Apr-22
P02-E	Standard Drawing For Valve Box	25	100%	$17.65	12-Jan-22	03-Apr-22
P02-E	Standard Drawing For Fire Hydrant Pit	25	60%	$17.65	13-Mar-22	27-Apr-22
P02-E	Standard Drawing For Cable Pull Pit	50	0%	$10.59	03-Apr-22	22-May-22
P02-E	Standard Drawing For Pavings	25	60%	$17.65	08-Jan-22	27-Apr-22
P02-E	Standard Drawing For Earth Pit	25	60%	$17.65	13-Feb-22	27-Apr-22
P02-E	Standard Detail For Pipe Bedding	50	100%	$10.59	22-Aug-21	03-Apr-22
P02-E	Standard Details of Miscellaneous Items	50	60%	$10.59	06-Mar-22	22-May-22
P02-E	BINAK Oil Field Project Overall Well Location/Facilities Layou	25	0%	$8.02	20-Mar-22	13-Apr-22
P02-E	General Civil Layout -W028	25	80%	$141.02	19-Oct-21	13-Apr-22
P02-E	Civil and Structural drawings -W028	45	80%	$141.02	19-Oct-21	03-May-22
P02-E	Rough Grading Plans -W028	25	80%	$93.72	11-Oct-21 A	13-Apr-22
MTO		7	0%	$72.23	14-Apr-22	20-Apr-22
P02-E	MTO For Civil Works - W028	7	0%	$72.23	14-Apr-22	20-Apr-22
Structure		108	33.66%	$491.56	08-Aug-21	06-Jun-22
Basis/Criteria		64	0%	$5.36	20-Mar-22	22-May-22
P02-E	Structural Design Criteria	64	0%	$1.79	20-Mar-22	22-May-22

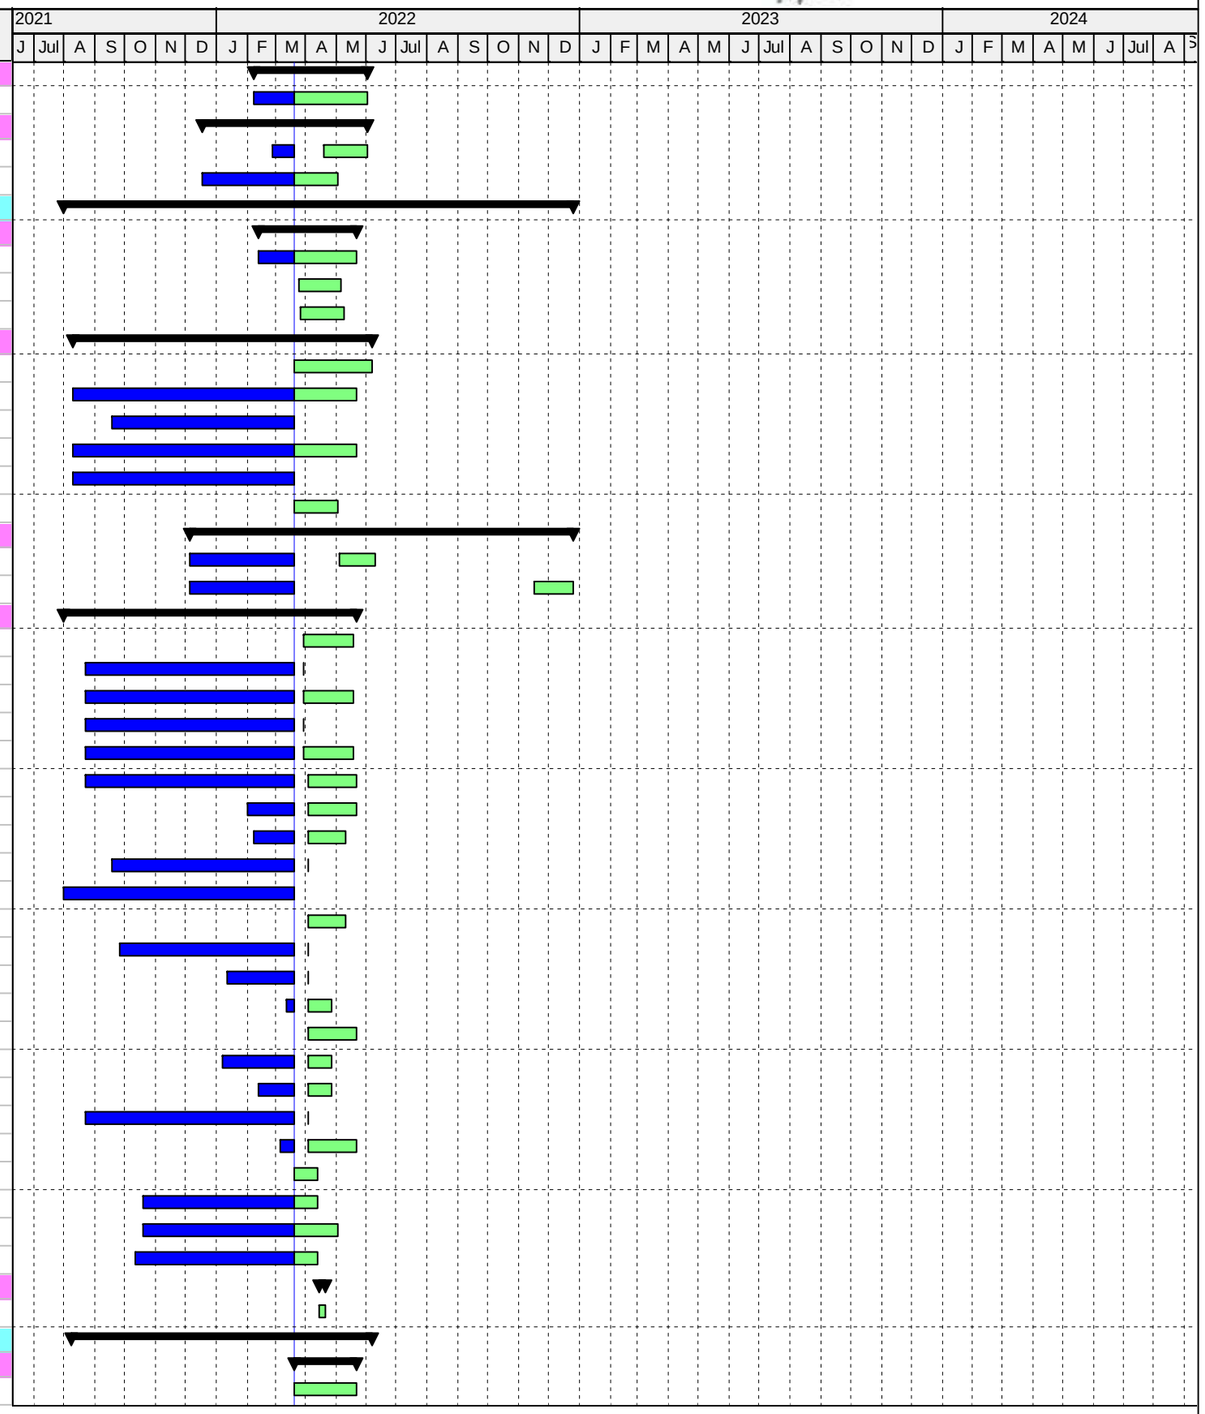


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P02-E	Design Criteria For Steel Structure	44	0%	$1.79	20-Mar-22	02-May-22
P02-E	Design Criteria For Load & Forces	44	0%	$1.79	20-Mar-22	02-May-22
Specification		98	79.06%	$40.95	14-Aug-21	26-May-22
P02-E	Specification For Concrete Work	64	80%	$7.41	14-Aug-21	26-May-22
P02-E	Specification for Fabrication of Steel Structures	64	100%	$9.57	24-Jan-22	24-Mar-22
P02-E	Specification For Grouting	64	100%	$7.41	14-Aug-21	24-Mar-22
P02-E	Specification for Fireproofing	64	100%	$9.47	18-Sep-21	24-Mar-22
P02-E	Specification For Steel Structural Works	37	0%	$7.10	20-Mar-22	25-Apr-22
Drawing/Diagram		98	41.97%	$317.01	08-Aug-21	01-Jun-22
P02-E	Standard Drawing For Fire Proofing	64	100%	$7.96	08-Aug-21	03-Apr-22
P02-E	Standard Drawing For Anchor Bolts	64	100%	$7.96	15-Dec-21	03-Apr-22
P02-E	Standard Drawing For Steel Stairs	64	100%	$7.96	18-Dec-21	03-Apr-22
P02-E	Standard Drawing For Operating Platform	38	100%	$9.35	27-Dec-21	30-Mar-22
P02-E	Standard Drawing For Handrail	38	100%	$13.31	18-Dec-21	30-Mar-22
P02-E	Standard Drawing For Insert Plates in Concrete	38	100%	$13.31	08-Aug-21	30-Mar-22
P02-E	Standard Details For Ladder & Safety Cage	64	100%	$7.96	15-Dec-21	03-Apr-22
P02-E	Standard Drawing For Lighting pole foundation Plan & Details	38	60%	$13.31	29-Jan-22	06-May-22
P02-E	General Notes - Steel Structures	38	100%	$9.35	25-Jan-22	30-Mar-22
P02-E	General Notes - Reinforced Concrete Structures	38	100%	$13.31	20-Dec-21	30-Mar-22
P02-E	Standard Drawing For Structural Built-up Sections	44	80%	$13.31	04-Dec-21	12-May-22
P02-E	Standard Drawing For Steel Flooring, Grating and Chequere	44	100%	$13.31	05-Jan-22	30-Mar-22
P02-E	Concrete Reinforcement Shape Code	44	0%	$13.31	30-Mar-22	12-May-22
P02-E	Standard Drawing For Septic Tank	44	80%	$13.31	22-Jan-22	12-May-22
P02-E	Platform Structure Drawing - W028	44	0%	$159.96	19-Apr-22	01-Jun-22
MTO		5	0%	$128.25	02-Jun-22	06-Jun-22
P02-E	MTO For Structural Works - W028	5	0%	$128.25	02-Jun-22	06-Jun-22
General		170	12.06%	$1,072.50	11-Aug-21	05-Sep-22
Risk Assessment		44	100%	$53.63	05-Sep-21	20-Mar-22
Procedure/Plan		44	100%	$53.63	05-Sep-21	20-Mar-22
P02-	HAZID Study Procedure	44	100%	$53.63	05-Sep-21	20-Mar-22
Survey (Topography) & Geotechnic		170	7.06%	$911.63	11-Aug-21	05-Sep-22
Geotechnic		104	8%	$804.38	11-Aug-21	02-May-22
Procedure/Plan		44	100%	$64.35	11-Aug-21	19-Apr-22
P02	Geotechnical Investigation Plan for Well Pads	44	100%	$64.35	11-Aug-21	19-Apr-22
Report		44	0%	$740.03	20-Mar-22	02-May-22
P02	Geotechnical Investigation Report - W028	44	0%	$740.03	20-Mar-22	02-May-22
Survey		35	0%	$107.25	02-Aug-22	05-Sep-22
Drawing-diagram		35	0%	$107.25	02-Aug-22	05-Sep-22
P02	Flowline Plan & Profile Drawings - W028	35	0%	$107.25	02-Aug-22	05-Sep-22
QC/QA		116	10.59%	$107.25	20-Sep-21	13-Jul-22
QC Management		116	39.14%	$8.72	08-Dec-21	13-Jul-22
P02-	Project Audit Procedure	44	0%	$0.44	20-Mar-22	02-May-22
P02-	Specification For Final Data Book (FDB) Requirements	44	0%	$0.44	20-Mar-22	02-May-22
P02-	Non Conformance Control Procedure	36	0%	$0.44	03-May-22	07-Jun-22
P02-	Corrective Action Procedure	36	0%	$0.44	08-Jun-22	13-Jul-22
P02-	Material Reciving, Storage, Handling Procedure	39	60%	$0.44	20-Feb-22	27-Apr-22
P02-	Packing, Marking, Transportation Procedure	39	0%	$0.44	20-Mar-22	27-Apr-22
P02-	Criticality Assessment Procedure	39	0%	$1.74	20-Mar-22	27-Apr-22
P02-	Project Quality Plan	44	80%	$3.92	08-Dec-21	02-May-22

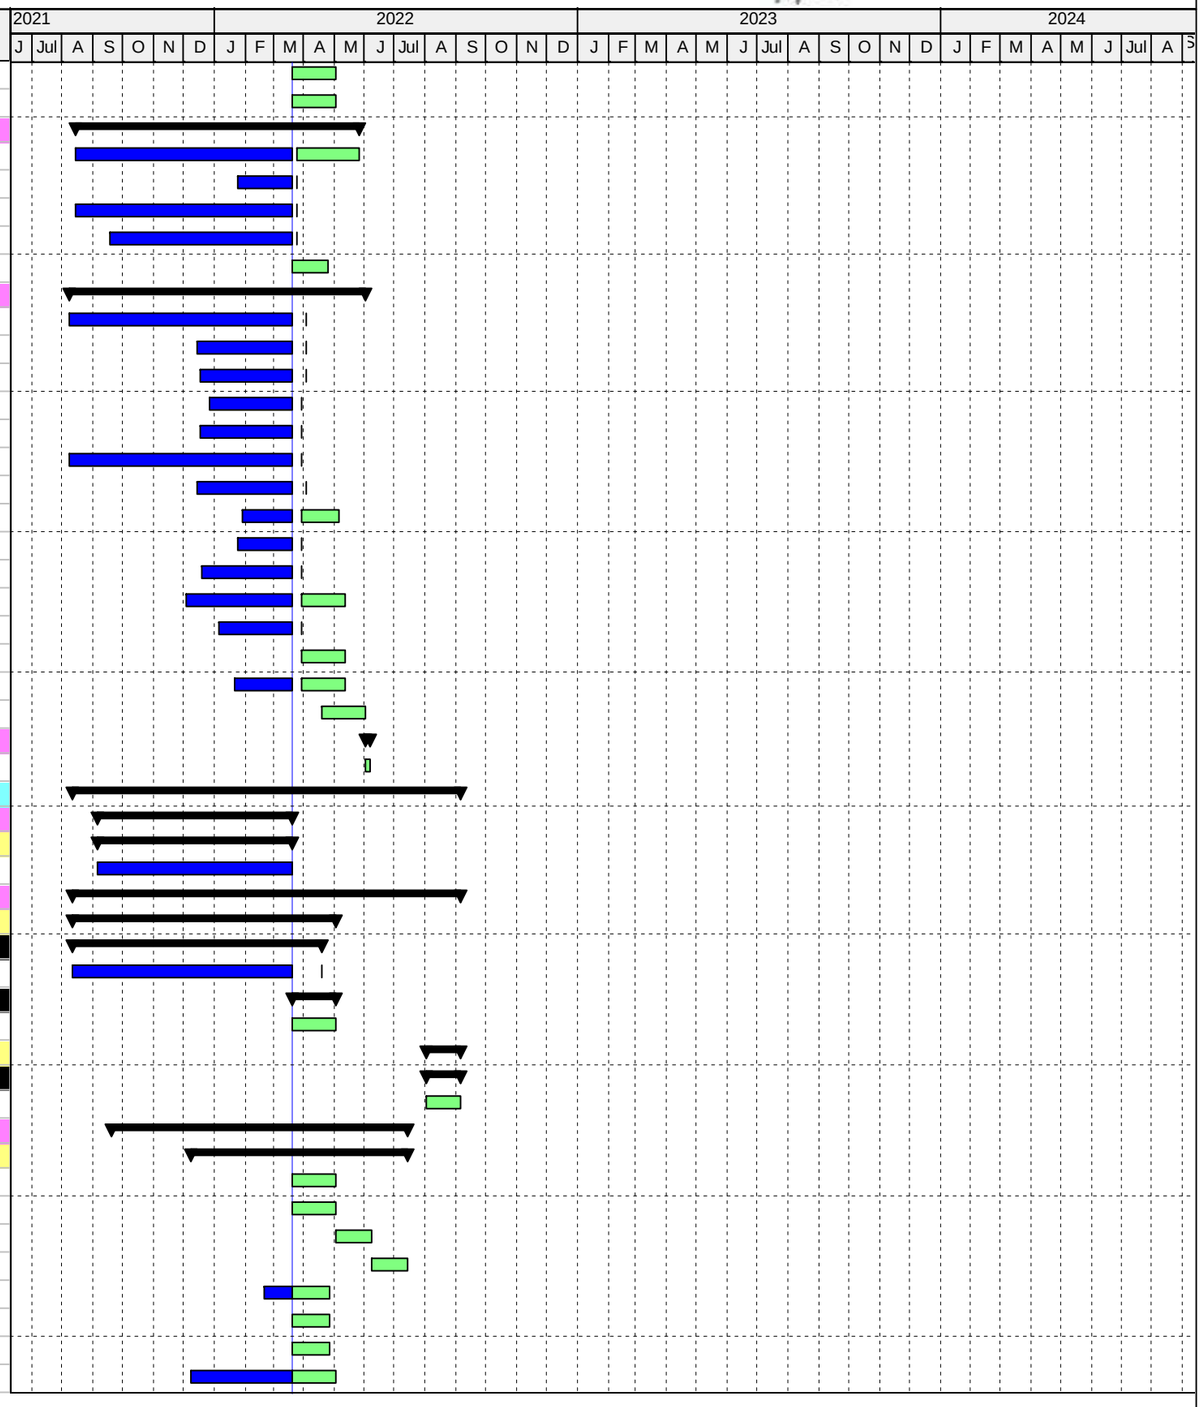


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P02-	Technical Query Procedure	44	0%	$0.44	30-Mar-22	12-May-22
QC General Document		55	8.57%	$12.73	28-Nov-21	16-May-22
P02-	Quality Control Plan (QCP)	39	60%	$1.82	28-Nov-21	27-Apr-22
P02-	Specification for Welding Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P02-	Heat Treatment Procedure (Pre Heating , PWHT)	44	0%	$1.82	03-Apr-22	16-May-22
P02-	Welder Performance Qualification Test (WQT) Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P02-	NDT Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P02-	Surface Preparation and Coating/Painting Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P02-	Control of Inspection Measuring and Test Equipment Procedu	44	0%	$1.81	03-Apr-22	16-May-22
QC Discipline Document		95	7.99%	$85.80	20-Sep-21	29-Jun-22
Piping		95	0%	$21.45	27-Mar-22	29-Jun-22
P02	ITP For Piping Works	44	0%	$2.15	27-Mar-22	09-May-22
P02	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$2.41	03-Apr-22	16-May-22
P02	PIPING WPS (Welding Procedure Specification)	44	0%	$2.41	03-Apr-22	16-May-22
P02	PIPING PQR (Procedure Qualification Record)	44	0%	$2.41	03-Apr-22	16-May-22
P02	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$2.41	03-Apr-22	16-May-22
P02	PIPING WPS (Preliminary Welding Procedure Specification) f	44	0%	$2.41	03-Apr-22	16-May-22
P02	PIPING PQR (Procedure Qualification Record) for Repair We	44	0%	$2.41	03-Apr-22	16-May-22
P02	Field Joint Coating Procedure For Pipeline	44	0%	$2.41	03-Apr-22	16-May-22
P02	Pressure Test Procedure	44	0%	$2.41	17-May-22	29-Jun-22
Telecomm.		44	0%	$4.29	27-Mar-22	09-May-22
P02	ITP For Telecommunication Installation	44	0%	$4.29	27-Mar-22	09-May-22
Safety		44	0%	$4.29	27-Mar-22	09-May-22
P02	ITP For Safety Installation	44	0%	$4.29	27-Mar-22	09-May-22
Architectural		44	0%	$4.29	27-Mar-22	09-May-22
P02	ITP For Architectural Works	44	0%	$4.29	27-Mar-22	09-May-22
Mechanical		44	0%	$4.29	27-Mar-22	09-May-22
P02	ITP For Mechanical Installation	44	0%	$4.29	27-Mar-22	09-May-22
Structure		51	0%	$17.16	27-Mar-22	16-May-22
P02	ITP For Steel Structural Works	44	0%	$1.72	27-Mar-22	09-May-22
P02	Steel Structure WPS (Welding Procedure Specification)	44	0%	$2.57	03-Apr-22	16-May-22
P02	Steel Structure PQR (Procedure Qualification Record)	44	0%	$2.57	03-Apr-22	16-May-22
P02	Steel Structure WPS (Welding Procedure Specification) For F	44	0%	$2.57	03-Apr-22	16-May-22
P02	Steel Structure PQR (Procedure Qualification Record) For Re	44	0%	$2.57	03-Apr-22	16-May-22
P02	Weld Map For Steel Structures	44	0%	$2.57	03-Apr-22	16-May-22
P02	NDT Plan For steel Structures	44	0%	$2.57	03-Apr-22	16-May-22
Instrumentation		44	0%	$4.29	27-Mar-22	09-May-22
P02	ITP For I&C Installation	44	0%	$4.29	27-Mar-22	09-May-22
Pipeline		74	15%	$17.16	16-Jan-22	16-May-22
P02	ITP For Pipeline	44	60%	$1.72	16-Jan-22	09-May-22
P02	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	60%	$2.57	23-Feb-22	16-May-22
P02	PIPELINE WPS (Welding Procedure Specification)	44	0%	$2.57	03-Apr-22	16-May-22
P02	PIPELINE PQR (Procedure Qualification Record)	44	0%	$2.57	03-Apr-22	16-May-22
P02	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	0%	$2.57	03-Apr-22	16-May-22
P02	PIPELINE WPS (Preliminary Welding Procedure Specificatior	44	0%	$2.57	03-Apr-22	16-May-22
P02	PIPELINE PQR (Procedure Qualification Record) for Repair \	44	0%	$2.57	03-Apr-22	16-May-22
Civil		44	100%	$4.29	20-Sep-21	27-Mar-22
P02	ITP For Civil Works	44	100%	$4.29	20-Sep-21	27-Mar-22
Electrical		44	0%	$4.29	27-Mar-22	09-May-22

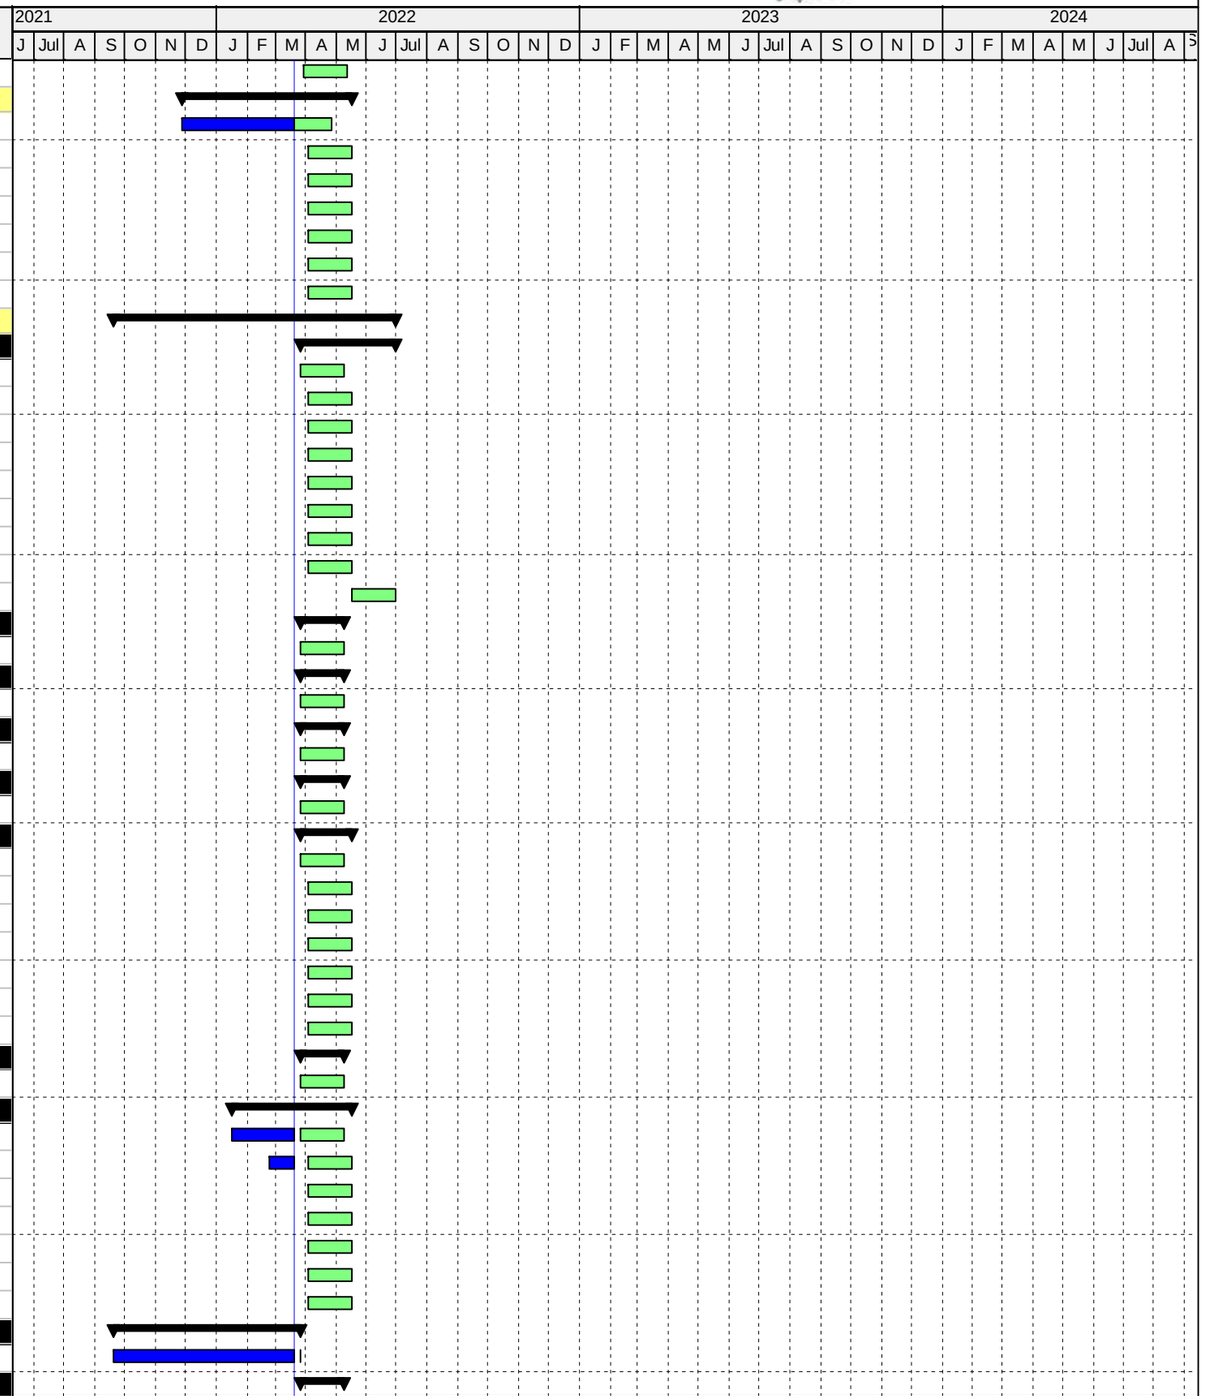


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P02	ITP For Electrical Installation	44	0%	$4.29	27-Mar-22	09-May-22
Procurement Engineering		261	11.78%	$812.50	01-Aug-21	05-Dec-22
Piping		221	7.24%	$211.25	01-Aug-21	05-Dec-22
Pipes		84	10.02%	$23.49	06-Dec-21	06-Oct-22
P02-E	PMR For Pipes - W028	7	100%	$2.35	06-Dec-21	07-Aug-22
P02-E	TBE For Pipes - W028	25	0%	$3.52	07-Aug-22	31-Aug-22
P02-E	VDR For Pipes - W028	25	0%	$17.62	12-Sep-22	06-Oct-22
Fittings		73	0%	$23.47	07-Aug-22	18-Oct-22
P02-E	PMR For Fittings - W028	7	0%	$2.35	07-Aug-22	13-Aug-22
P02-E	TBE For Fitting - W028	25	0%	$3.52	14-Aug-22	07-Sep-22
P02-E	VDR For Fitting - W028	25	0%	$17.60	24-Sep-22	18-Oct-22
Flanges		109	15.04%	$23.47	13-Feb-22	18-Sep-22
P02-E	PMR For Flanges - W028	7	0%	$2.35	07-Aug-22	13-Aug-22
P02-E	TBE For Flanges - W028	25	100%	$3.52	13-Feb-22	14-Aug-22
P02-E	VDR For Flanges - W028	20	0%	$17.60	30-Aug-22	18-Sep-22
Manual Valves		114	15.04%	$23.47	13-Feb-22	19-Sep-22
P02-E	PMR For Manual Valves - W028	7	0%	$2.35	07-Aug-22	13-Aug-22
P02-E	TBE For Manual Valves - W028	25	100%	$3.52	13-Feb-22	19-Aug-22
P02-E	VDR For Manual Valves - W028	20	0%	$17.60	31-Aug-22	19-Sep-22
Gaskets		109	15.04%	$23.47	13-Feb-22	14-Sep-22
P02-E	PMR For Gaskets - W028	7	0%	$2.35	07-Aug-22	13-Aug-22
P02-E	TBE For Gaskets - W028	25	100%	$3.52	13-Feb-22	14-Aug-22
P02-E	VDR For Gaskets - W028	20	0%	$17.60	26-Aug-22	14-Sep-22
Bolt & Nuts		64	0%	$23.47	07-Aug-22	09-Oct-22
P02-E	PMR For Bolt/Nuts - W028	7	0%	$2.35	07-Aug-22	13-Aug-22
P02-E	TBE For Bolt/Nuts - W028	25	0%	$3.52	14-Aug-22	07-Sep-22
P02-E	VDR For Bolt/Nuts - W028	20	0%	$17.60	20-Sep-22	09-Oct-22
Sampling Connection		90	10.02%	$23.47	01-Aug-21	27-Jul-22
P02-E	PMR For Sampling Connection Set - W028	7	100%	$2.35	01-Aug-21	29-Apr-22
P02-E	TBE For Sampling Connection Set - W028	25	0%	$3.52	29-Apr-22	23-May-22
P02-E	VDR For Sampling Connection Set - W028	20	0%	$17.60	08-Jul-22	27-Jul-22
Stone Trap		69	0%	$23.47	13-May-22	20-Jul-22
P02-E	PMR For Stone Trap - W028	7	0%	$2.35	13-May-22	19-May-22
P02-E	TBE For Stone Trap - W028	25	0%	$3.52	20-May-22	13-Jun-22
P02-E	VDR For Stone Trap - W028	20	0%	$17.60	01-Jul-22	20-Jul-22
Pipe Support		77	0%	$23.47	20-Sep-22	05-Dec-22
P02-E	PMR For Pipe Support - W028	5	0%	$2.35	20-Sep-22	24-Sep-22
P02-E	TBE For Pipe Support - W028	5	0%	$3.52	27-Sep-22	01-Oct-22
P02-E	VDR For Pipe Support - W028	20	0%	$17.60	16-Nov-22	05-Dec-22
Pipeline		74	12.5%	$47.13	06-Dec-21	25-Apr-22
Line Pipe		62	25%	$23.56	06-Dec-21	25-Apr-22
P02-E	PMR For Line Pipes - W028	10	100%	$2.36	06-Dec-21	20-Mar-22
P02-E	TBE For Line Pipes - W028	30	100%	$3.53	19-Feb-22	20-Mar-22
P02-E	VDR For Line Pipes - W028	25	0%	$17.67	01-Apr-22	25-Apr-22
Flow Line Support		27	0%	$23.56	20-Mar-22	15-Apr-22
P02-E	PMR For Flowline Support - W028	5	0%	$2.36	20-Mar-22	24-Mar-22
P02-E	TBE For Flowline Support - W028	5	0%	$3.53	11-Apr-22	15-Apr-22
P02-E	VDR For Flowline Support - W028	5	0%	$17.67	25-Mar-22	29-Mar-22
Control & Instrumentation		167	20.58%	$269.75	15-Nov-21	23-Jul-22
Field Instrumentations		114	10%	$79.33	13-Dec-21	23-Jul-22

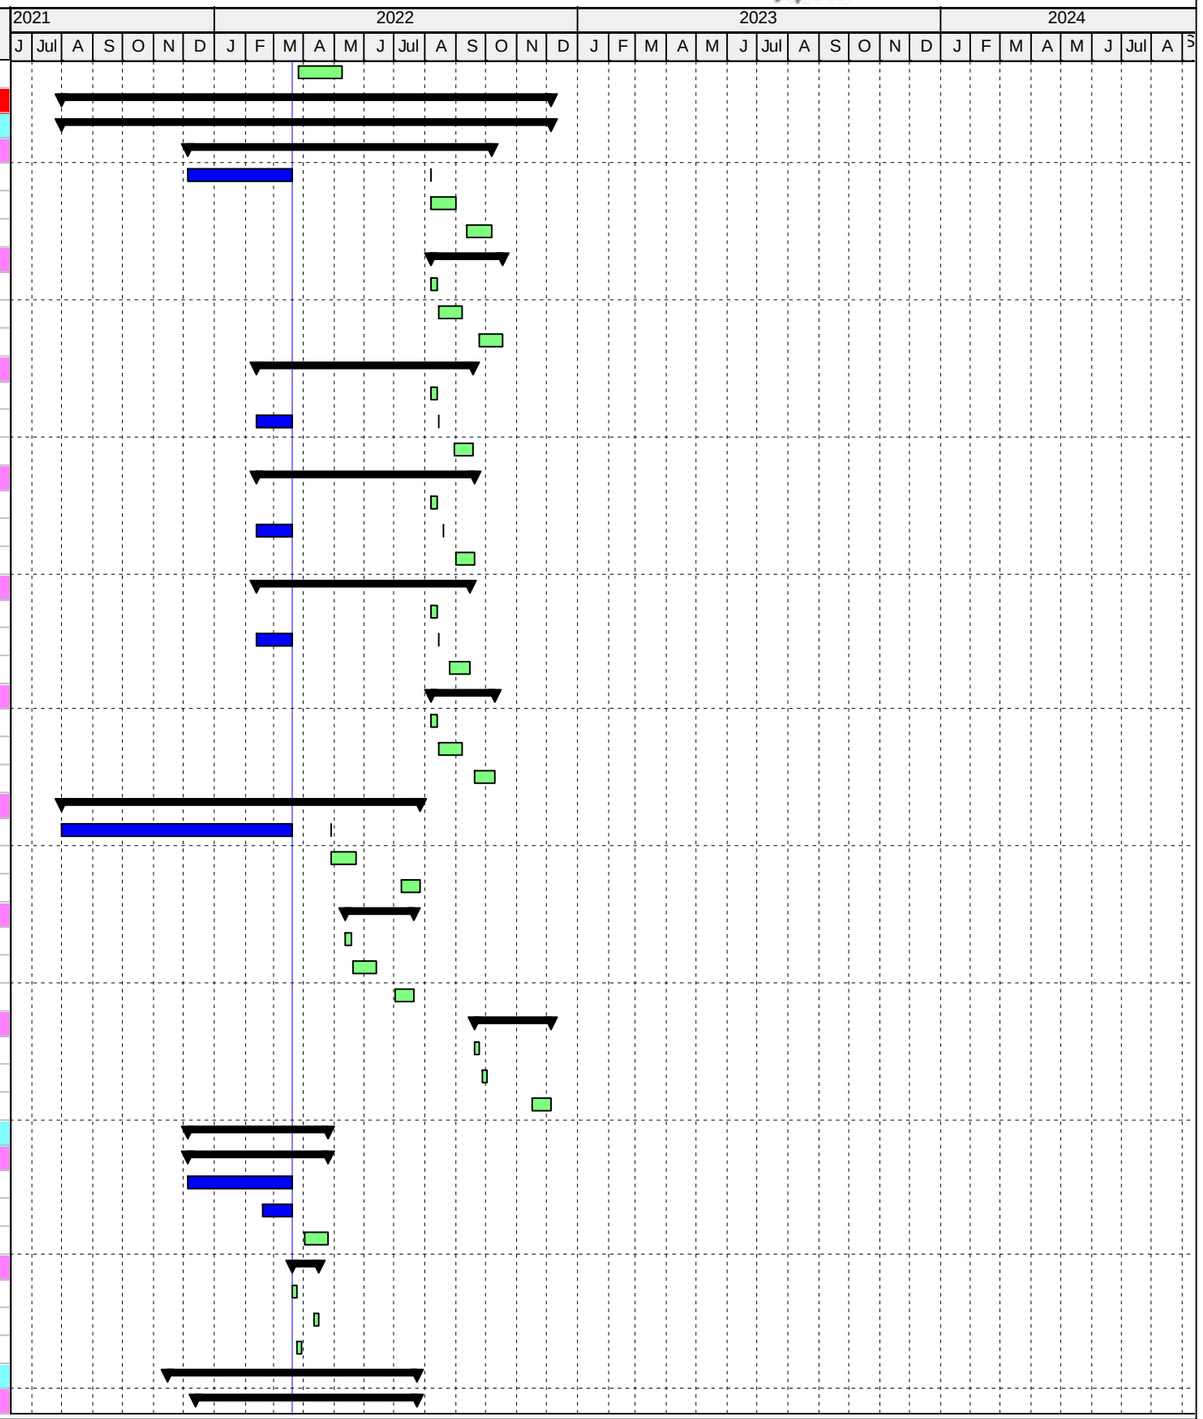


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P02-E	PMR For Field Instrumentations - W028	10	100%	$7.93	13-Dec-21	13-May-22
P02-E	TBE/TBA For Field Instrumentations - W028	30	0%	$11.90	13-May-22	11-Jun-22
P02-E	VDR/TBA For Field Instrumentations - W028	20	0%	$59.50	04-Jul-22	23-Jul-22
WHCP/HPU		62	24.98%	$95.22	15-Nov-21	23-May-22
P02-E	PMR For WHCP/HPU - W028	10	100%	$9.52	15-Nov-21	19-Apr-22
P02-E	TBE/TBA For WHCP/HPU - W028	30	100%	$14.28	01-Dec-21	19-Apr-22
P02-E	VDR/TBA For WHCP/HPU - W028	20	0%	$71.42	04-May-22	23-May-22
Instrument Bulk Items		136	24.99%	$95.19	16-Jan-22	23-Jun-22
P02-E	PMR For Instrument Bulk Items - W028	10	100%	$9.52	16-Jan-22	13-May-22
P02-E	TBE/TBA For Instrument Bulk Items - W028	20	100%	$14.28	02-Feb-22	18-May-22
P02-E	VDR/TBA For Instrument Bulk Items - W028	20	0%	$71.40	04-Jun-22	23-Jun-22
Safety & Fire Fighting		70	10%	$190.13	08-Dec-21	13-Oct-22
Safety Sign		70	9.99%	$87.13	08-Dec-21	13-Oct-22
P02-E	PMR For Fire Safety Sign - W028	10	100%	$8.71	08-Dec-21	05-Aug-22
P02-E	TBE For Fire Safety Sign - W028	30	0%	$13.07	05-Aug-22	03-Sep-22
P02-E	VDR For Fire Safety Sign - W028	20	0%	$65.35	24-Sep-22	13-Oct-22
Fire Fighting and Safety Equipment		62	10.01%	$102.99	08-Dec-21	05-Oct-22
P02-E	PMR For Fire Fighting and Safety Equipment - W028	10	100%	$10.30	08-Dec-21	05-Aug-22
P02-E	TBE For Fire Fighting and Safety Equipment - W028	30	0%	$15.45	05-Aug-22	03-Sep-22
P02-E	VDR For Fire Fighting and Safety Equipment - W028	20	0%	$77.24	16-Sep-22	05-Oct-22
Structure		15	0%	$47.13	07-Jun-22	21-Jun-22
Anchor Bolts		15	0%	$23.56	07-Jun-22	21-Jun-22
P02-E	PMR For Anchor Bolts - W028	5	0%	$2.36	07-Jun-22	11-Jun-22
P02-E	TBE For Anchor Bolts - W028	5	0%	$3.53	12-Jun-22	16-Jun-22
P02-E	VDR For Anchor Bolts - W028	5	0%	$17.67	17-Jun-22	21-Jun-22
Steel Structure Items		15	0%	$23.56	07-Jun-22	21-Jun-22
P02-E	PMR For Steel Structure Items - W028	5	0%	$2.36	07-Jun-22	11-Jun-22
P02-E	TBE For Steel Structure Items - W028	5	0%	$3.53	12-Jun-22	16-Jun-22
P02-E	VDR For Steel Structure Items - W028	5	0%	$17.67	17-Jun-22	21-Jun-22
Civil		17	0%	$47.13	14-Apr-22	30-Apr-22
Geomembrane		17	0%	$23.56	14-Apr-22	30-Apr-22
P02-E	PMR For Geomembrane - W028	5	0%	$2.36	14-Apr-22	18-Apr-22
P02-E	TBE For Geomembrane - W028	5	0%	$3.53	21-Apr-22	25-Apr-22
P02-E	VDR For Geomembrane - W028	5	0%	$17.67	26-Apr-22	30-Apr-22
Geotextile		17	0%	$23.56	14-Apr-22	30-Apr-22
P02-E	PMR For Geotextile - W028	5	0%	$2.36	14-Apr-22	18-Apr-22
P02-E	TBE For Geotextile - W028	5	0%	$3.53	21-Apr-22	25-Apr-22
P02-E	VDR For Geotextile - W028	5	0%	$17.67	26-Apr-22	30-Apr-22
Commissioning Engineering		267	0%	$162.50	29-Apr-22	20-Jan-23
P02-EP	Operability Review	5	0%	$32.50	16-Jan-23	20-Jan-23
P02-EP	Pre-Commissioning, Commissioning & Startup Procedure - W	44	0%	$97.50	29-Apr-22	11-Jun-22
P02-EP	Operating Manual - W028	30	0%	$32.50	17-Dec-22	15-Jan-23
Field Engineering		305	0%	$1,218.75	14-Apr-22	12-Feb-23
P02-EP	Technical/Site Queries	15	0%	$609.38	14-Apr-22	28-Apr-22
P02-EP	As-Built Document Booklets - W028	10	0%	$609.38	03-Feb-23	12-Feb-23
Engineering Final Documentation		10	0%	$812.50	13-Feb-23	22-Feb-23
P02-EP	Final Engineering Dossier - W028	10	0%	$812.50	13-Feb-23	22-Feb-23
PROCUREMENT		374	0%	$265,639.00	01-Feb-22	28-Mar-23
Wellhead Facility and Flowline		310	0%	$170,540.24	01-Feb-22	23-Jan-23
Piping - W028		235	0%	$25,939.17	03-Jun-22	23-Jan-23

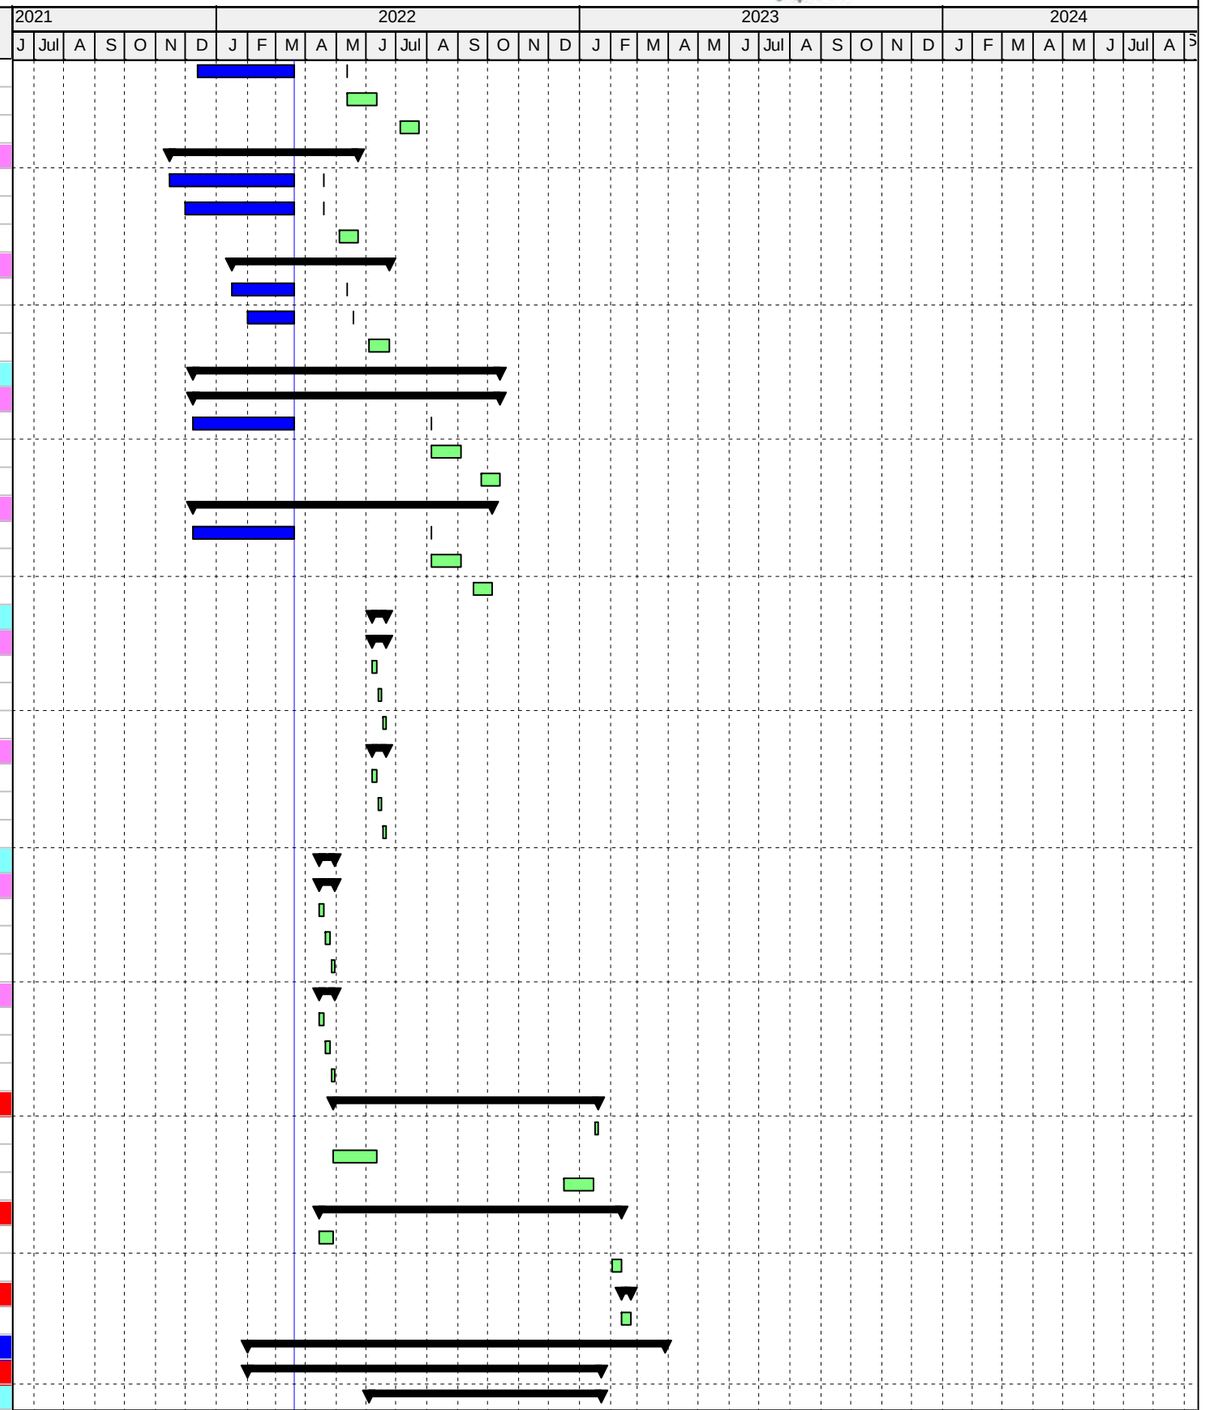


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Pipes		100	0%	$5,187.83	06-Sep-22	14-Dec-22
P02-E	Tendering & Selection	10	0%	$207.51	06-Sep-22	15-Sep-22
P02-E	Contract Effectiveness / PO	6	0%	$311.27	06-Sep-22	11-Sep-22
P02-E	Manufacturing / Fabrication / Supply	75	0%	$2,593.92	12-Sep-22	25-Nov-22
P02-E	Final Inspection	7	0%	$518.78	26-Nov-22	02-Dec-22
P02-E	Delivery On Site	7	0%	$1,296.96	03-Dec-22	09-Dec-22
P02-E	Submitting Vendor Data Book	5	0%	$259.39	10-Dec-22	14-Dec-22
Fittings		100	0%	$1,945.44	08-Sep-22	16-Dec-22
P02-E	Tendering & Selection	11	0%	$77.82	08-Sep-22	18-Sep-22
P02-E	Contract Effectiveness / PO	5	0%	$116.73	19-Sep-22	23-Sep-22
P02-E	Manufacturing / Fabrication / Supply	65	0%	$972.72	24-Sep-22	27-Nov-22
P02-E	Final Inspection	7	0%	$194.54	28-Nov-22	04-Dec-22
P02-E	Delivery On Site	7	0%	$486.36	05-Dec-22	11-Dec-22
P02-E	Submitting Vendor Data Book	5	0%	$97.27	12-Dec-22	16-Dec-22
Flanges		100	0%	$1,945.44	14-Aug-22	21-Nov-22
P02-E	Tendering & Selection	11	0%	$77.82	14-Aug-22	24-Aug-22
P02-E	Contract Effectiveness / PO	5	0%	$116.73	25-Aug-22	29-Aug-22
P02-E	Manufacturing / Fabrication / Supply	65	0%	$972.72	30-Aug-22	02-Nov-22
P02-E	Final Inspection	7	0%	$194.54	03-Nov-22	09-Nov-22
P02-E	Delivery On Site	7	0%	$486.36	10-Nov-22	16-Nov-22
P02-E	Submitting Vendor Data Book	5	0%	$97.27	17-Nov-22	21-Nov-22
Manual Valves		91	0%	$9,078.71	19-Aug-22	17-Nov-22
P02-E	Tendering & Selection	7	0%	$363.15	19-Aug-22	25-Aug-22
P02-E	Contract Effectiveness / PO	5	0%	$544.72	26-Aug-22	30-Aug-22
P02-E	Manufacturing / Fabrication / Supply	65	0%	$4,539.35	21-Aug-22	24-Oct-22
P02-E	Final Inspection	7	0%	$907.87	25-Oct-22	31-Oct-22
P02-E	Delivery On Site	7	0%	$1,815.74	01-Nov-22	07-Nov-22
P02-E	Submitting Vendor Data Book	5	0%	$453.94	08-Nov-22	12-Nov-22
P02-E	Delivering Spare Parts	5	0%	$453.94	13-Nov-22	17-Nov-22
Gaskets		91	0%	$778.18	14-Aug-22	12-Nov-22
P02-E	Tendering & Selection	7	0%	$31.13	14-Aug-22	20-Aug-22
P02-E	Contract Effectiveness / PO	5	0%	$46.69	21-Aug-22	25-Aug-22
P02-E	Manufacturing / Fabrication / Supply	60	0%	$389.09	26-Aug-22	24-Oct-22
P02-E	Final Inspection	7	0%	$77.82	25-Oct-22	31-Oct-22
P02-E	Delivery On Site	7	0%	$194.54	01-Nov-22	07-Nov-22
P02-E	Submitting Vendor Data Book	5	0%	$38.91	08-Nov-22	12-Nov-22
Bolt/Nuts		91	0%	$518.78	08-Sep-22	07-Dec-22
P02-E	Tendering & Selection	7	0%	$20.75	08-Sep-22	14-Sep-22
P02-E	Contract Effectiveness / PO	5	0%	$31.13	15-Sep-22	19-Sep-22
P02-E	Manufacturing / Fabrication / Supply	60	0%	$259.39	20-Sep-22	18-Nov-22
P02-E	Final Inspection	7	0%	$51.88	19-Nov-22	25-Nov-22
P02-E	Delivery On Site	7	0%	$129.70	26-Nov-22	02-Dec-22
P02-E	Submitting Vendor Data Book	5	0%	$25.94	03-Dec-22	07-Dec-22
Sampling Connection Set		129	0%	$1,296.96	03-Jun-22	09-Oct-22
P02-E	Tendering & Selection	30	0%	$51.88	03-Jun-22	02-Jul-22
P02-E	Contract Effectiveness / PO	5	0%	$77.82	03-Jul-22	07-Jul-22
P02-E	Manufacturing / Fabrication / Supply	70	0%	$648.48	08-Jul-22	15-Sep-22
P02-E	Final Inspection	12	0%	$129.70	16-Sep-22	27-Sep-22
P02-E	Delivery On Site	7	0%	$324.24	28-Sep-22	04-Oct-22

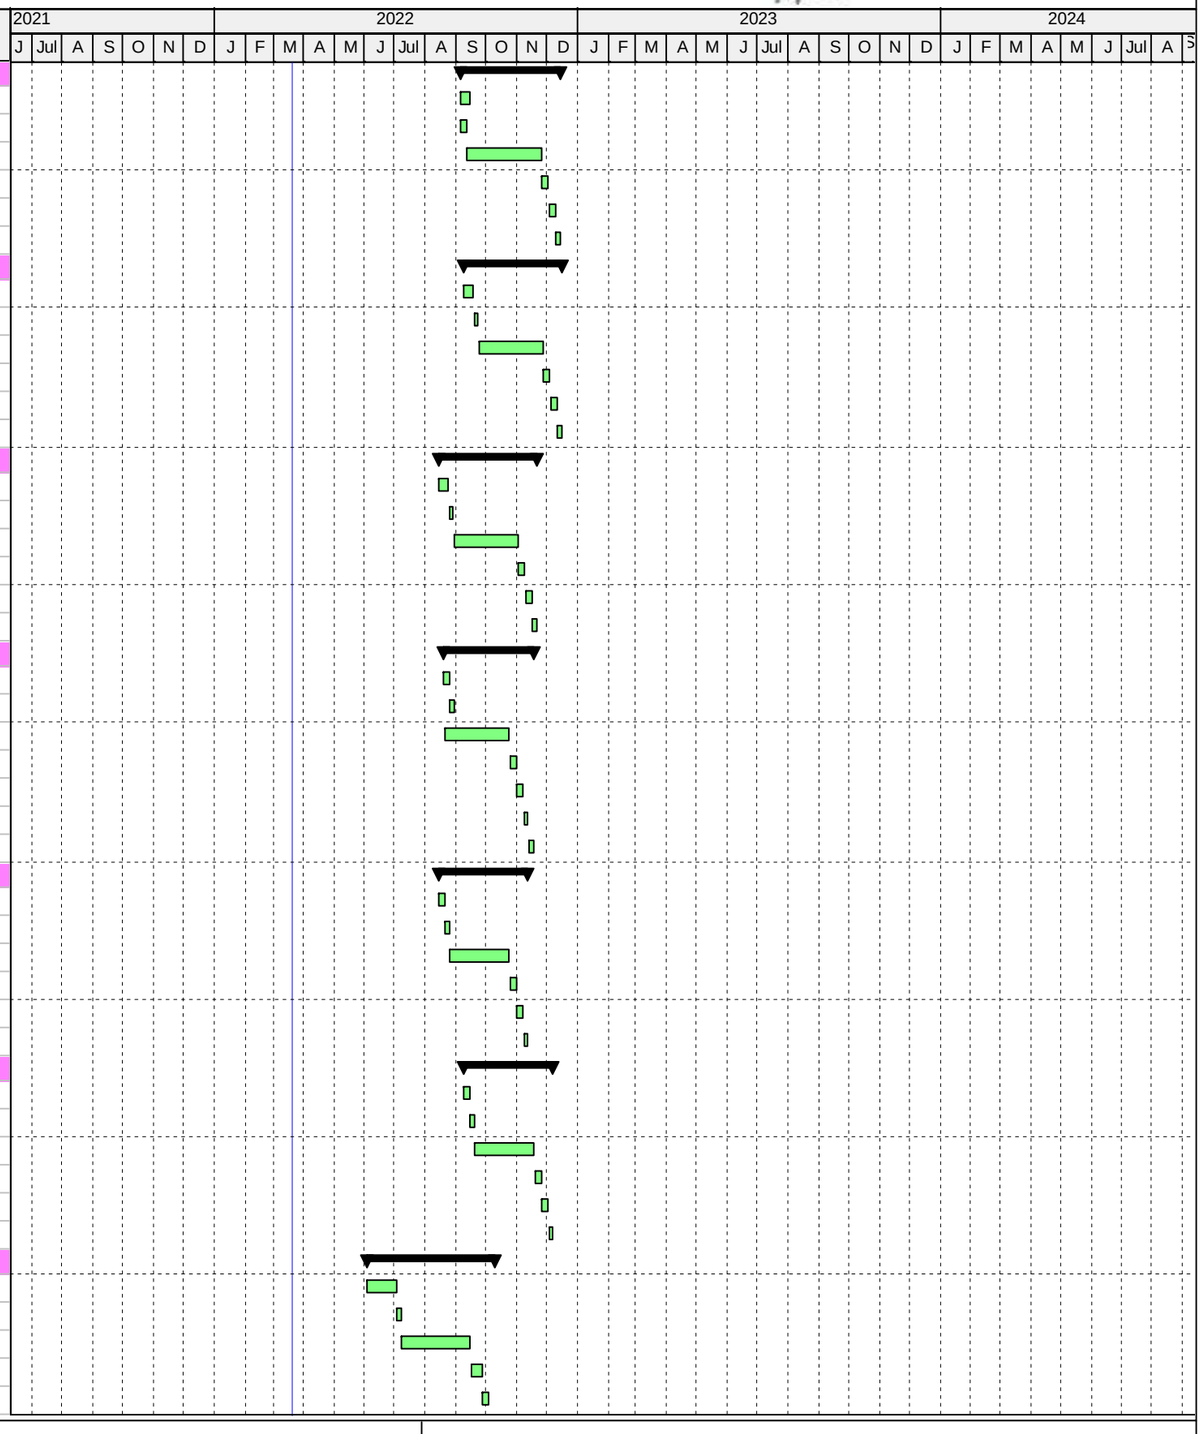


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P02-E	Submitting Vendor Data Book	5	0%	$64.85	05-Oct-22	09-Oct-22
Stone Trap		101	0%	$3,890.88	19-Jun-22	27-Sep-22
P02-E	Tendering & Selection	7	0%	$155.64	19-Jun-22	25-Jun-22
P02-E	Contract Effectiveness / PO	5	0%	$233.45	26-Jun-22	30-Jun-22
P02-E	Manufacturing / Fabrication / Supply	70	0%	$1,945.44	01-Jul-22	08-Sep-22
P02-E	Final Inspection	7	0%	$389.09	09-Sep-22	15-Sep-22
P02-E	Delivery On Site	7	0%	$972.72	16-Sep-22	22-Sep-22
P02-E	Submitting Vendor Data Book	5	0%	$194.54	23-Sep-22	27-Sep-22
Pipe Support		104	0%	$1,296.96	12-Oct-22	23-Jan-23
P02-E	Tendering & Selection	30	0%	$51.88	12-Oct-22	10-Nov-22
P02-E	Contract Effectiveness / PO	5	0%	$77.82	11-Nov-22	15-Nov-22
P02-E	Manufacturing / Fabrication / Supply	45	0%	$648.48	16-Nov-22	30-Dec-22
P02-E	Final Inspection	12	0%	$129.70	31-Dec-22	11-Jan-23
P02-E	Delivery On Site	7	0%	$324.24	12-Jan-23	18-Jan-23
P02-E	Submitting Vendor Data Book	5	0%	$64.85	19-Jan-23	23-Jan-23
Pipeline - W028		141	0%	$121,032.41	20-Mar-22	07-Aug-22
Line Pipes		141	0%	$102,877.55	20-Mar-22	07-Aug-22
P02-E	Tendering & Selection	7	0%	$4,115.10	20-Mar-22	26-Mar-22
P02-E	Contract Effectiveness / PO	5	0%	$6,172.65	27-Mar-22	31-Mar-22
P02-E	Manufacturing / Fabrication / Supply	110	0%	$51,438.77	01-Apr-22	19-Jul-22
P02-E	Final Inspection	7	0%	$10,287.75	20-Jul-22	26-Jul-22
P02-E	Delivery On Site	7	0%	$25,719.39	27-Jul-22	02-Aug-22
P02-E	Submitting Vendor Data Book	5	0%	$5,143.88	03-Aug-22	07-Aug-22
Flow Line Support		109	0%	$18,154.86	30-Mar-22	16-Jul-22
P02-E	Tendering & Selection	7	0%	$726.19	30-Mar-22	05-Apr-22
P02-E	Contract Effectiveness / PO	5	0%	$1,089.29	06-Apr-22	10-Apr-22
P02-E	Manufacturing / Fabrication / Supply	80	0%	$9,077.43	11-Apr-22	29-Jun-22
P02-E	Final Inspection	7	0%	$1,815.49	30-Jun-22	06-Jul-22
P02-E	Delivery On Site	5	0%	$4,538.72	07-Jul-22	11-Jul-22
P02-E	Submitting Vendor Data Book	5	0%	$907.74	12-Jul-22	16-Jul-22
Control & Instrumentation - W028		160	0%	$22,528.37	01-Feb-22	25-Sep-22
WHCP/HPU		127	0%	$21,176.66	01-Feb-22	23-Aug-22
P02-E	Tendering & Selection	10	0%	$847.07	01-Feb-22	28-Apr-22
P02-E	Contract Effectiveness / PO	5	0%	$1,270.60	29-Apr-22	03-May-22
P02-E	Manufacturing / Fabrication / Supply	90	0%	$10,588.33	04-May-22	01-Aug-22
P02-E	Final Inspection	10	0%	$2,117.67	02-Aug-22	11-Aug-22
P02-E	Delivery On Site	7	0%	$4,235.33	12-Aug-22	18-Aug-22
P02-E	Submitting Vendor Data Book	5	0%	$1,058.83	19-Aug-22	23-Aug-22
P02-E	Delivering Spare Parts	5	0%	$1,058.83	19-Aug-22	23-Aug-22
Instrument Bulk Items		91	0%	$180.23	23-May-22	21-Aug-22
P02-E	Tendering & Selection	7	0%	$7.21	23-May-22	29-May-22
P02-E	Contract Effectiveness / PO	5	0%	$10.81	30-May-22	03-Jun-22
P02-E	Manufacturing / Fabrication / Supply	60	0%	$90.11	04-Jun-22	02-Aug-22
P02-E	Final Inspection	7	0%	$18.02	03-Aug-22	09-Aug-22
P02-E	Delivery On Site	7	0%	$45.06	10-Aug-22	16-Aug-22
P02-E	Submitting Vendor Data Book	5	0%	$9.01	17-Aug-22	21-Aug-22
Instrument Tube and Fitting		101	0%	$1,126.42	17-Jun-22	25-Sep-22
P02-E	Tendering & Selection	7	0%	$45.06	17-Jun-22	23-Jun-22
P02-E	Contract Effectiveness / PO	5	0%	$67.59	24-Jun-22	28-Jun-22

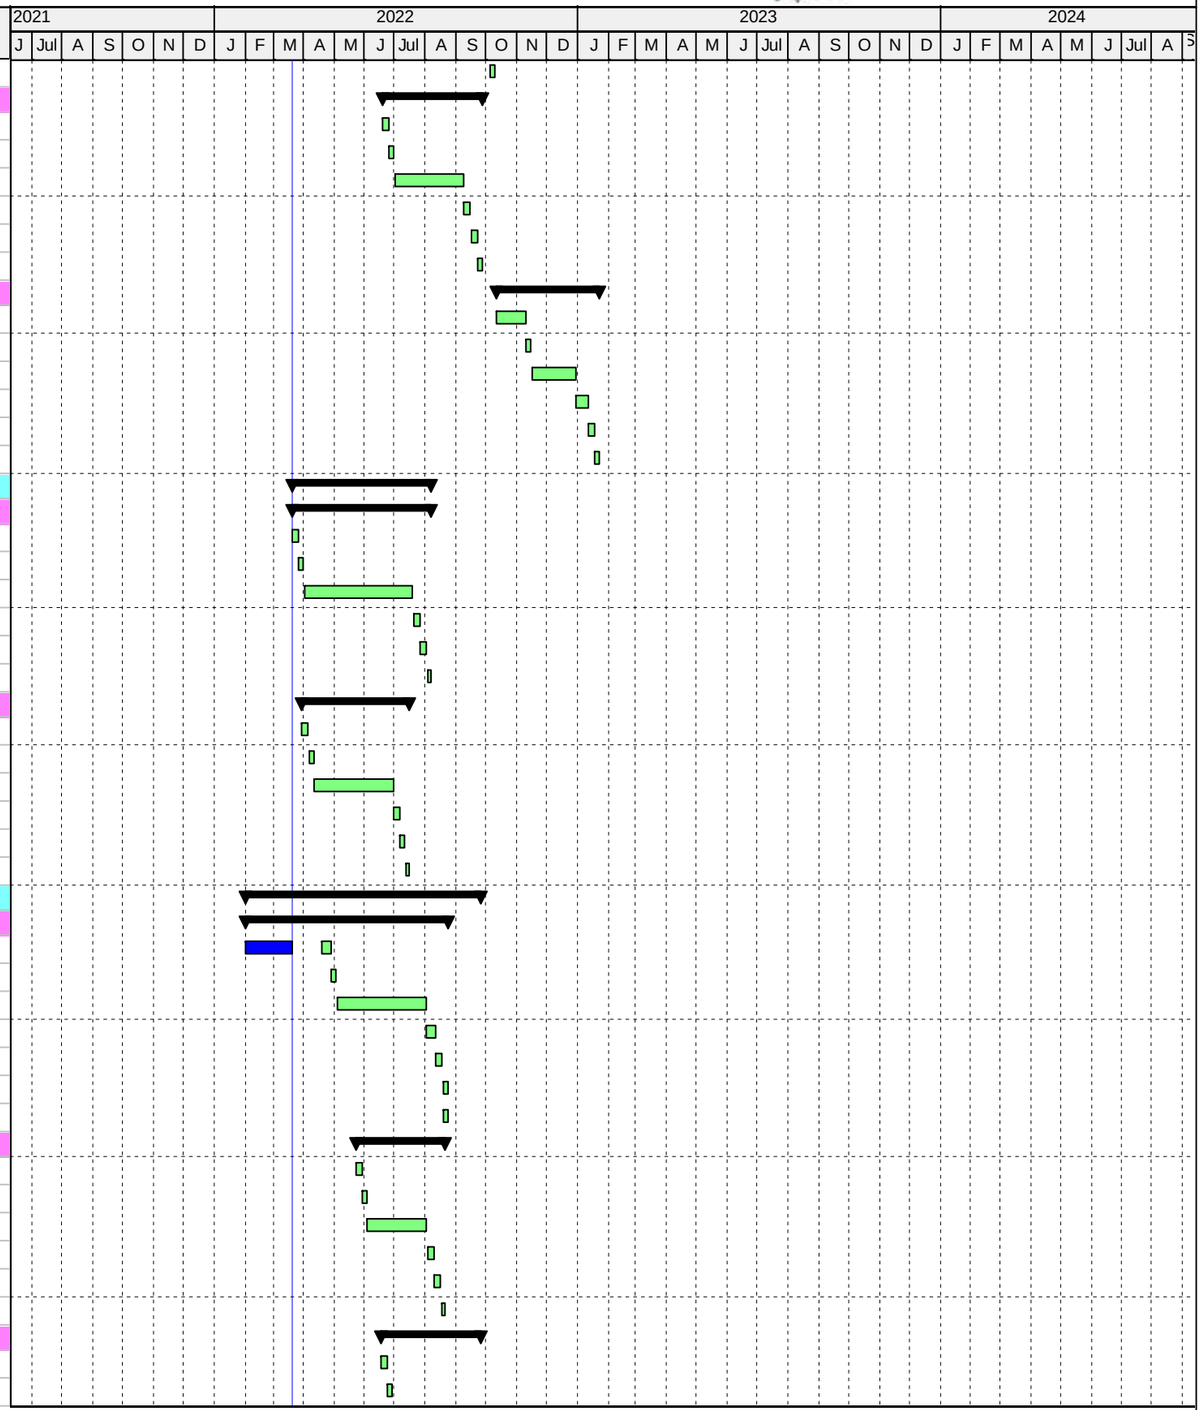


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P02-E	Manufacturing / Fabrication / Supply	70	0%	$563.21	29-Jun-22	06-Sep-22
P02-E	Final Inspection	7	0%	$112.64	07-Sep-22	13-Sep-22
P02-E	Delivery On Site	7	0%	$225.28	14-Sep-22	20-Sep-22
P02-E	Submitting Vendor Data Book	5	0%	$56.32	21-Sep-22	25-Sep-22
P02-E	Delivering Spare Parts	5	0%	$56.32	21-Sep-22	25-Sep-22
Instrument Cable Tray		81	0%	$45.06	22-Jun-22	10-Sep-22
P02-E	Tendering & Selection	7	0%	$1.80	22-Jun-22	28-Jun-22
P02-E	Contract Effectiveness / PO	5	0%	$2.70	29-Jun-22	03-Jul-22
P02-E	Manufacturing / Fabrication / Supply	50	0%	$22.53	04-Jul-22	22-Aug-22
P02-E	Final Inspection	7	0%	$4.51	23-Aug-22	29-Aug-22
P02-E	Delivery On Site	7	0%	$11.26	30-Aug-22	05-Sep-22
P02-E	Submitting Vendor Data Book	5	0%	$2.25	06-Sep-22	10-Sep-22
Safety & Fire Fighting - W028		104	0%	$1,040.30	04-Sep-22	16-Dec-22
Fire Fighting and Safety Equipment		91	0%	$208.06	04-Sep-22	03-Dec-22
P02-E	Tendering & Selection	7	0%	$8.32	04-Sep-22	10-Sep-22
P02-E	Contract Effectiveness / PO	5	0%	$12.48	11-Sep-22	15-Sep-22
P02-E	Manufacturing / Fabrication / Supply	60	0%	$104.03	16-Sep-22	14-Nov-22
P02-E	Final Inspection	7	0%	$20.81	15-Nov-22	21-Nov-22
P02-E	Delivery On Site	7	0%	$41.61	22-Nov-22	28-Nov-22
P02-E	Submitting Vendor Data Book	5	0%	$10.40	29-Nov-22	03-Dec-22
P02-E	Delivering Spare Parts	5	0%	$10.40	29-Nov-22	03-Dec-22
Fire Safety Sign		104	0%	$832.24	04-Sep-22	16-Dec-22
P02-E	Tendering & Selection	15	0%	$33.29	04-Sep-22	18-Sep-22
P02-E	Contract Effectiveness / PO	5	0%	$49.93	19-Sep-22	23-Sep-22
P02-E	Manufacturing / Fabrication / Supply	60	0%	$416.12	24-Sep-22	22-Nov-22
P02-E	Final Inspection	12	0%	$83.22	23-Nov-22	04-Dec-22
P02-E	Delivery On Site	7	0%	$166.45	05-Dec-22	11-Dec-22
P02-E	Submitting Vendor Data Book	5	0%	$41.61	12-Dec-22	16-Dec-22
P02-E	Delivering Spare Parts	5	0%	$41.61	12-Dec-22	16-Dec-22
Extension of Binak B/C Manifold		320	0%	$95,098.76	13-May-22	28-Mar-23
Mechanical - Extension of Binak B/C Manifold		154	0%	$3,271.40	13-May-22	13-Oct-22
Pumps		154	0%	$3,271.40	13-May-22	13-Oct-22
P02-E	Tendering & Selection	15	0%	$130.86	13-May-22	27-May-22
P02-E	Contract Effectiveness / PO	5	0%	$196.28	28-May-22	01-Jun-22
P02-E	Manufacturing / Fabrication / Supply	110	0%	$1,635.70	02-Jun-22	19-Sep-22
P02-E	Final Inspection	7	0%	$327.14	20-Sep-22	26-Sep-22
P02-E	Delivery On Site	7	0%	$654.28	27-Sep-22	03-Oct-22
P02-E	Submitting Vendor Data Book	5	0%	$163.57	04-Oct-22	08-Oct-22
P02-E	Delivering Spare Parts	5	0%	$163.57	09-Oct-22	13-Oct-22
Piping - Extension of Binak B/C Manifold		301	0%	$20,750.55	16-May-22	12-Mar-23
Pipes		114	0%	$8,466.22	05-Oct-22	26-Jan-23
P02-E	Tendering & Selection	10	0%	$338.65	05-Oct-22	14-Oct-22
P02-E	Contract Effectiveness / PO	5	0%	$507.97	15-Oct-22	19-Oct-22
P02-E	Manufacturing / Fabrication / Supply	80	0%	$4,233.11	20-Oct-22	07-Jan-23
P02-E	Final Inspection	7	0%	$846.62	08-Jan-23	14-Jan-23
P02-E	Delivery On Site	7	0%	$2,116.56	15-Jan-23	21-Jan-23
P02-E	Submitting Vendor Data Book	5	0%	$423.31	22-Jan-23	26-Jan-23
Fittings		124	0%	$1,120.53	04-Nov-22	07-Mar-23
P02-E	Tendering & Selection	10	0%	$44.82	04-Nov-22	13-Nov-22

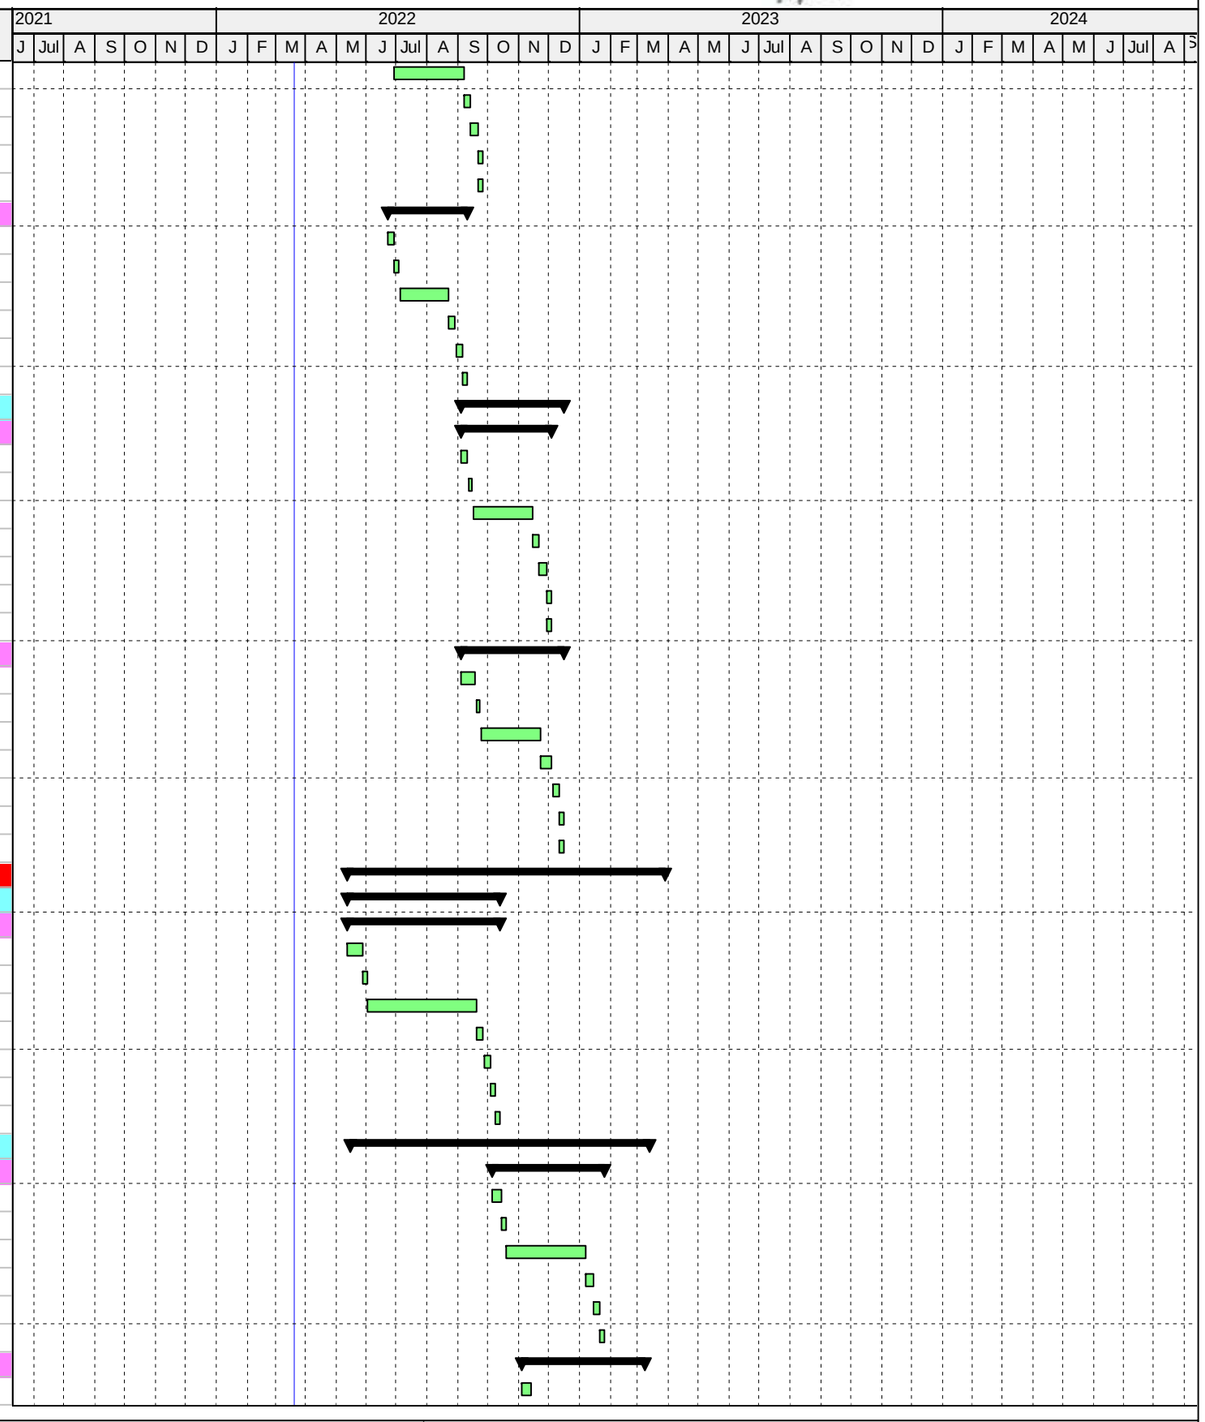


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P02-E	Contract Effectiveness / PO	5	0%	$67.23	14-Nov-22	18-Nov-22
P02-E	Manufacturing / Fabrication / Supply	90	0%	$560.26	19-Nov-22	16-Feb-23
P02-E	Final Inspection	7	0%	$112.05	17-Feb-23	23-Feb-23
P02-E	Delivery On Site	7	0%	$280.13	24-Feb-23	02-Mar-23
P02-E	Submitting Vendor Data Book	5	0%	$56.03	03-Mar-23	07-Mar-23
Flanges		124	0%	$1,120.53	04-Nov-22	07-Mar-23
P02-E	Tendering & Selection	10	0%	$44.82	04-Nov-22	13-Nov-22
P02-E	Contract Effectiveness / PO	5	0%	$67.23	14-Nov-22	18-Nov-22
P02-E	Manufacturing / Fabrication / Supply	90	0%	$560.26	19-Nov-22	16-Feb-23
P02-E	Final Inspection	7	0%	$112.05	17-Feb-23	23-Feb-23
P02-E	Delivery On Site	7	0%	$280.13	24-Feb-23	02-Mar-23
P02-E	Submitting Vendor Data Book	5	0%	$56.03	03-Mar-23	07-Mar-23
Manual Valves		129	0%	$4,980.13	04-Nov-22	12-Mar-23
P02-E	Tendering & Selection	10	0%	$199.21	04-Nov-22	13-Nov-22
P02-E	Contract Effectiveness / PO	5	0%	$298.81	14-Nov-22	18-Nov-22
P02-E	Manufacturing / Fabrication / Supply	90	0%	$2,490.07	19-Nov-22	16-Feb-23
P02-E	Final Inspection	7	0%	$498.01	17-Feb-23	23-Feb-23
P02-E	Delivery On Site	7	0%	$996.03	24-Feb-23	02-Mar-23
P02-E	Submitting Vendor Data Book	5	0%	$249.01	03-Mar-23	07-Mar-23
P02-E	Delivering Spare Parts	5	0%	$249.01	08-Mar-23	12-Mar-23
Gaskets		124	0%	$1,348.79	04-Nov-22	07-Mar-23
P02-E	Tendering & Selection	10	0%	$53.95	04-Nov-22	13-Nov-22
P02-E	Contract Effectiveness / PO	5	0%	$80.93	14-Nov-22	18-Nov-22
P02-E	Manufacturing / Fabrication / Supply	90	0%	$674.39	19-Nov-22	16-Feb-23
P02-E	Final Inspection	7	0%	$134.88	17-Feb-23	23-Feb-23
P02-E	Delivery On Site	7	0%	$337.20	24-Feb-23	02-Mar-23
P02-E	Submitting Vendor Data Book	5	0%	$67.44	03-Mar-23	07-Mar-23
Bolt/Nuts		114	0%	$2,075.05	04-Nov-22	25-Feb-23
P02-E	Tendering & Selection	10	0%	$83.00	04-Nov-22	13-Nov-22
P02-E	Contract Effectiveness / PO	5	0%	$124.50	14-Nov-22	18-Nov-22
P02-E	Manufacturing / Fabrication / Supply	80	0%	$1,037.53	19-Nov-22	06-Feb-23
P02-E	Final Inspection	7	0%	$207.51	07-Feb-23	13-Feb-23
P02-E	Delivery On Site	7	0%	$518.76	14-Feb-23	20-Feb-23
P02-E	Submitting Vendor Data Book	5	0%	$103.75	21-Feb-23	25-Feb-23
Sampling Connection Set		94	0%	$1,120.53	16-May-22	17-Aug-22
P02-E	Tendering & Selection	10	0%	$44.82	16-May-22	25-May-22
P02-E	Contract Effectiveness / PO	5	0%	$67.23	26-May-22	30-May-22
P02-E	Manufacturing / Fabrication / Supply	60	0%	$560.26	31-May-22	29-Jul-22
P02-E	Final Inspection	7	0%	$112.05	30-Jul-22	05-Aug-22
P02-E	Delivery On Site	7	0%	$280.13	06-Aug-22	12-Aug-22
P02-E	Submitting Vendor Data Book	5	0%	$56.03	13-Aug-22	17-Aug-22
Stone Trap		94	0%	$518.76	07-Oct-22	08-Jan-23
P02-E	Tendering & Selection	10	0%	$20.75	07-Oct-22	16-Oct-22
P02-E	Contract Effectiveness / PO	5	0%	$31.13	17-Oct-22	21-Oct-22
P02-E	Manufacturing / Fabrication / Supply	60	0%	$259.38	22-Oct-22	20-Dec-22
P02-E	Final Inspection	7	0%	$51.88	21-Dec-22	27-Dec-22
P02-E	Delivery On Site	7	0%	$129.69	28-Dec-22	03-Jan-23
P02-E	Submitting Vendor Data Book	5	0%	$25.94	04-Jan-23	08-Jan-23
Control & Instrumentation - Extension of Binak B/C Manifold		319	0%	$52,399.42	14-May-22	28-Mar-23

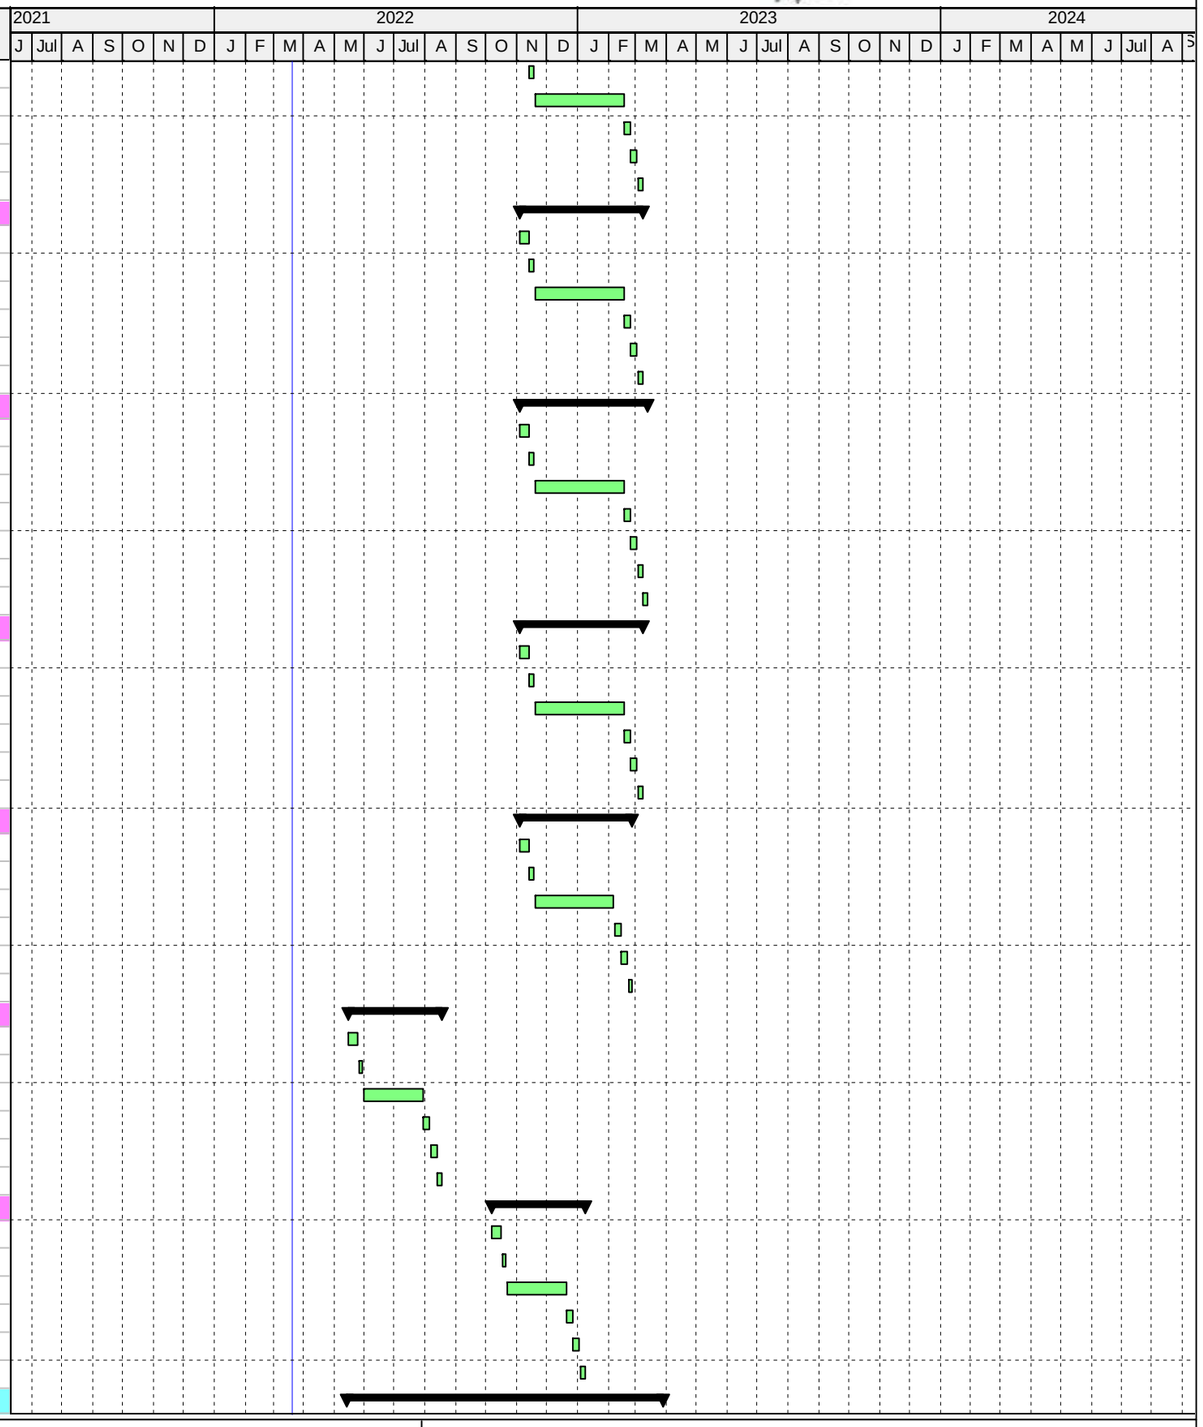


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Control System/Console/Furniture		164	0%	$21,483.76	21-May-22	31-Oct-22
P02-E	Tendering & Selection	20	0%	$859.35	21-May-22	09-Jun-22
P02-E	Contract Effectiveness / PO	5	0%	$1,289.03	10-Jun-22	14-Jun-22
P02-E	Manufacturing / Fabrication / Supply	120	0%	$10,741.88	15-Jun-22	12-Oct-22
P02-E	Final Inspection	7	0%	$2,148.38	13-Oct-22	19-Oct-22
P02-E	Delivery On Site	7	0%	$4,296.75	20-Oct-22	26-Oct-22
P02-E	Submitting Vendor Data Book	5	0%	$1,074.19	27-Oct-22	31-Oct-22
P02-E	Delivering Spare Parts	5	0%	$1,074.19	27-Oct-22	31-Oct-22
ESD System		169	0%	$15,195.83	05-Jun-22	20-Nov-22
P02-E	Tendering & Selection	20	0%	$607.83	05-Jun-22	24-Jun-22
P02-E	Contract Effectiveness / PO	5	0%	$911.75	25-Jun-22	29-Jun-22
P02-E	Manufacturing / Fabrication / Supply	120	0%	$7,597.92	30-Jun-22	27-Oct-22
P02-E	Final Inspection	7	0%	$1,519.58	28-Oct-22	03-Nov-22
P02-E	Delivery On Site	7	0%	$3,039.17	04-Nov-22	10-Nov-22
P02-E	Submitting Vendor Data Book	5	0%	$759.79	11-Nov-22	15-Nov-22
P02-E	Delivering Spare Parts	5	0%	$759.79	16-Nov-22	20-Nov-22
F&G System		169	0%	$10,479.88	05-Jun-22	20-Nov-22
P02-E	Tendering & Selection	20	0%	$419.20	05-Jun-22	24-Jun-22
P02-E	Contract Effectiveness / PO	5	0%	$628.79	25-Jun-22	29-Jun-22
P02-E	Manufacturing / Fabrication / Supply	120	0%	$5,239.94	30-Jun-22	27-Oct-22
P02-E	Final Inspection	7	0%	$1,047.99	28-Oct-22	03-Nov-22
P02-E	Delivery On Site	7	0%	$2,095.98	04-Nov-22	10-Nov-22
P02-E	Submitting Vendor Data Book	5	0%	$523.99	11-Nov-22	15-Nov-22
P02-E	Delivering Spare Parts	5	0%	$523.99	16-Nov-22	20-Nov-22
ON/OFF & Shutdown Valves		149	0%	$576.39	02-Jun-22	28-Oct-22
P02-E	Tendering & Selection	20	0%	$23.06	02-Jun-22	21-Jun-22
P02-E	Contract Effectiveness / PO	5	0%	$34.58	22-Jun-22	26-Jun-22
P02-E	Manufacturing / Fabrication / Supply	100	0%	$288.20	27-Jun-22	04-Oct-22
P02-E	Final Inspection	7	0%	$57.64	05-Oct-22	11-Oct-22
P02-E	Delivery On Site	7	0%	$115.28	12-Oct-22	18-Oct-22
P02-E	Submitting Vendor Data Book	5	0%	$28.82	19-Oct-22	23-Oct-22
P02-E	Delivering Spare Parts	5	0%	$28.82	24-Oct-22	28-Oct-22
Control Valves		144	0%	$576.39	04-Jul-22	24-Nov-22
P02-E	Tendering & Selection	15	0%	$23.06	04-Jul-22	18-Jul-22
P02-E	Contract Effectiveness / PO	5	0%	$34.58	19-Jul-22	23-Jul-22
P02-E	Manufacturing / Fabrication / Supply	100	0%	$288.20	24-Jul-22	31-Oct-22
P02-E	Final Inspection	7	0%	$57.64	01-Nov-22	07-Nov-22
P02-E	Delivery On Site	7	0%	$115.28	08-Nov-22	14-Nov-22
P02-E	Submitting Vendor Data Book	5	0%	$28.82	15-Nov-22	19-Nov-22
P02-E	Delivering Spare Parts	5	0%	$28.82	20-Nov-22	24-Nov-22
Pressure Safety Valves (PSV)		144	0%	$576.39	15-Jul-22	05-Dec-22
P02-E	Tendering & Selection	15	0%	$23.06	15-Jul-22	29-Jul-22
P02-E	Contract Effectiveness / PO	5	0%	$34.58	30-Jul-22	03-Aug-22
P02-E	Manufacturing / Fabrication / Supply	100	0%	$288.20	04-Aug-22	11-Nov-22
P02-E	Final Inspection	7	0%	$57.64	12-Nov-22	18-Nov-22
P02-E	Delivery On Site	7	0%	$115.28	19-Nov-22	25-Nov-22
P02-E	Submitting Vendor Data Book	5	0%	$28.82	26-Nov-22	30-Nov-22
P02-E	Delivering Spare Parts	5	0%	$28.82	01-Dec-22	05-Dec-22
F&G Devices		154	0%	$497.79	04-Aug-22	04-Jan-23

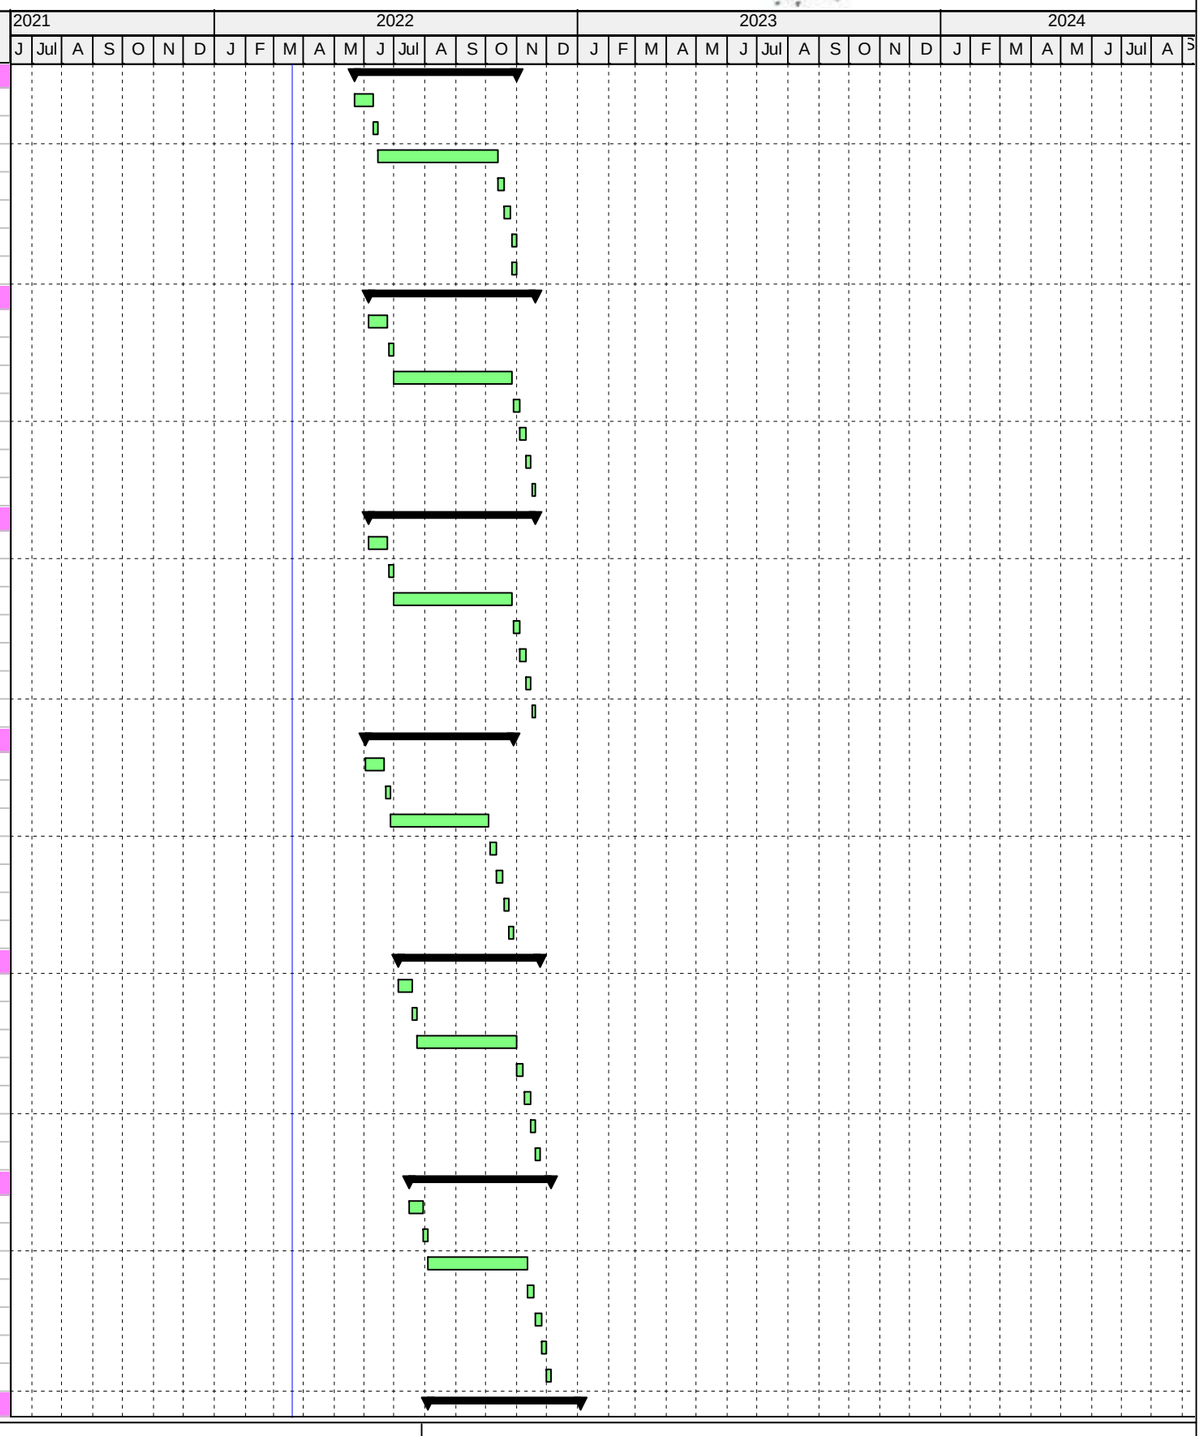


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P02-E	Tendering & Selection	15	0%	$19.91	04-Aug-22	18-Aug-22
P02-E	Contract Effectiveness / PO	5	0%	$29.87	19-Aug-22	23-Aug-22
P02-E	Manufacturing / Fabrication / Supply	110	0%	$248.90	24-Aug-22	11-Dec-22
P02-E	Final Inspection	7	0%	$49.78	12-Dec-22	18-Dec-22
P02-E	Delivery On Site	7	0%	$99.56	19-Dec-22	25-Dec-22
P02-E	Submitting Vendor Data Book	5	0%	$24.89	26-Dec-22	30-Dec-22
P02-E	Delivering Spare Parts	5	0%	$24.89	31-Dec-22	04-Jan-23
Orifice and Restriction Orifice Plate		159	0%	$214.84	25-May-22	30-Oct-22
P02-E	Tendering & Selection	15	0%	$8.59	25-May-22	08-Jun-22
P02-E	Contract Effectiveness / PO	5	0%	$12.89	09-Jun-22	13-Jun-22
P02-E	Manufacturing / Fabrication / Supply	110	0%	$107.42	14-Jun-22	01-Oct-22
P02-E	Final Inspection	12	0%	$21.48	02-Oct-22	13-Oct-22
P02-E	Delivery On Site	7	0%	$42.97	14-Oct-22	20-Oct-22
P02-E	Submitting Vendor Data Book	5	0%	$10.74	21-Oct-22	25-Oct-22
P02-E	Delivering Spare Parts	5	0%	$10.74	26-Oct-22	30-Oct-22
Corrosion Coupon/Probe		161	0%	$214.84	21-May-22	28-Oct-22
P02-E	Tendering & Selection	15	0%	$8.59	21-May-22	04-Jun-22
P02-E	Contract Effectiveness / PO	5	0%	$12.89	05-Jun-22	09-Jun-22
P02-E	Manufacturing / Fabrication / Supply	110	0%	$107.42	10-Jun-22	27-Sep-22
P02-E	Final Inspection	12	0%	$21.48	28-Sep-22	09-Oct-22
P02-E	Submitting Vendor Data Book	7	0%	$42.97	17-Oct-22	23-Oct-22
P02-E	Delivery On Site	7	0%	$10.74	10-Oct-22	16-Oct-22
P02-E	Delivering Spare Parts	5	0%	$10.74	24-Oct-22	28-Oct-22
Pressure Transmitter		161	0%	$288.20	03-Jul-22	10-Dec-22
P02-E	Tendering & Selection	15	0%	$11.53	03-Jul-22	17-Jul-22
P02-E	Contract Effectiveness / PO	5	0%	$17.29	18-Jul-22	22-Jul-22
P02-E	Manufacturing / Fabrication / Supply	110	0%	$144.10	23-Jul-22	09-Nov-22
P02-E	Final Inspection	12	0%	$28.82	10-Nov-22	21-Nov-22
P02-E	Submitting Vendor Data Book	7	0%	$57.64	29-Nov-22	05-Dec-22
P02-E	Delivery On Site	7	0%	$14.41	22-Nov-22	28-Nov-22
P02-E	Delivering Spare Parts	5	0%	$14.41	06-Dec-22	10-Dec-22
Flow Transmitter/ Diff. Pressure Transmitter		159	0%	$288.20	14-May-22	19-Oct-22
P02-E	Tendering & Selection	15	0%	$11.53	14-May-22	28-May-22
P02-E	Contract Effectiveness / PO	5	0%	$17.29	29-May-22	02-Jun-22
P02-E	Manufacturing / Fabrication / Supply	110	0%	$144.10	03-Jun-22	20-Sep-22
P02-E	Final Inspection	12	0%	$28.82	21-Sep-22	02-Oct-22
P02-E	Submitting Vendor Data Book	7	0%	$57.64	08-Oct-22	14-Oct-22
P02-E	Delivery On Site	5	0%	$14.41	03-Oct-22	07-Oct-22
P02-E	Delivering Spare Parts	5	0%	$14.41	15-Oct-22	19-Oct-22
Instrument/F&G Cable		131	0%	$356.32	08-Nov-22	18-Mar-23
P02-E	Tendering & Selection	15	0%	$14.25	08-Nov-22	22-Nov-22
P02-E	Contract Effectiveness / PO	5	0%	$21.38	23-Nov-22	27-Nov-22
P02-E	Manufacturing / Fabrication / Supply	90	0%	$178.16	28-Nov-22	25-Feb-23
P02-E	Final Inspection	7	0%	$35.63	26-Feb-23	04-Mar-23
P02-E	Submitting Vendor Data Book	7	0%	$89.08	12-Mar-23	18-Mar-23
P02-E	Delivery On Site	7	0%	$17.82	05-Mar-23	11-Mar-23
Instrument/F&G Junction box and Gland		146	0%	$288.20	03-Nov-22	28-Mar-23
P02-E	Tendering & Selection	15	0%	$11.53	03-Nov-22	17-Nov-22
P02-E	Contract Effectiveness / PO	5	0%	$17.29	18-Nov-22	22-Nov-22

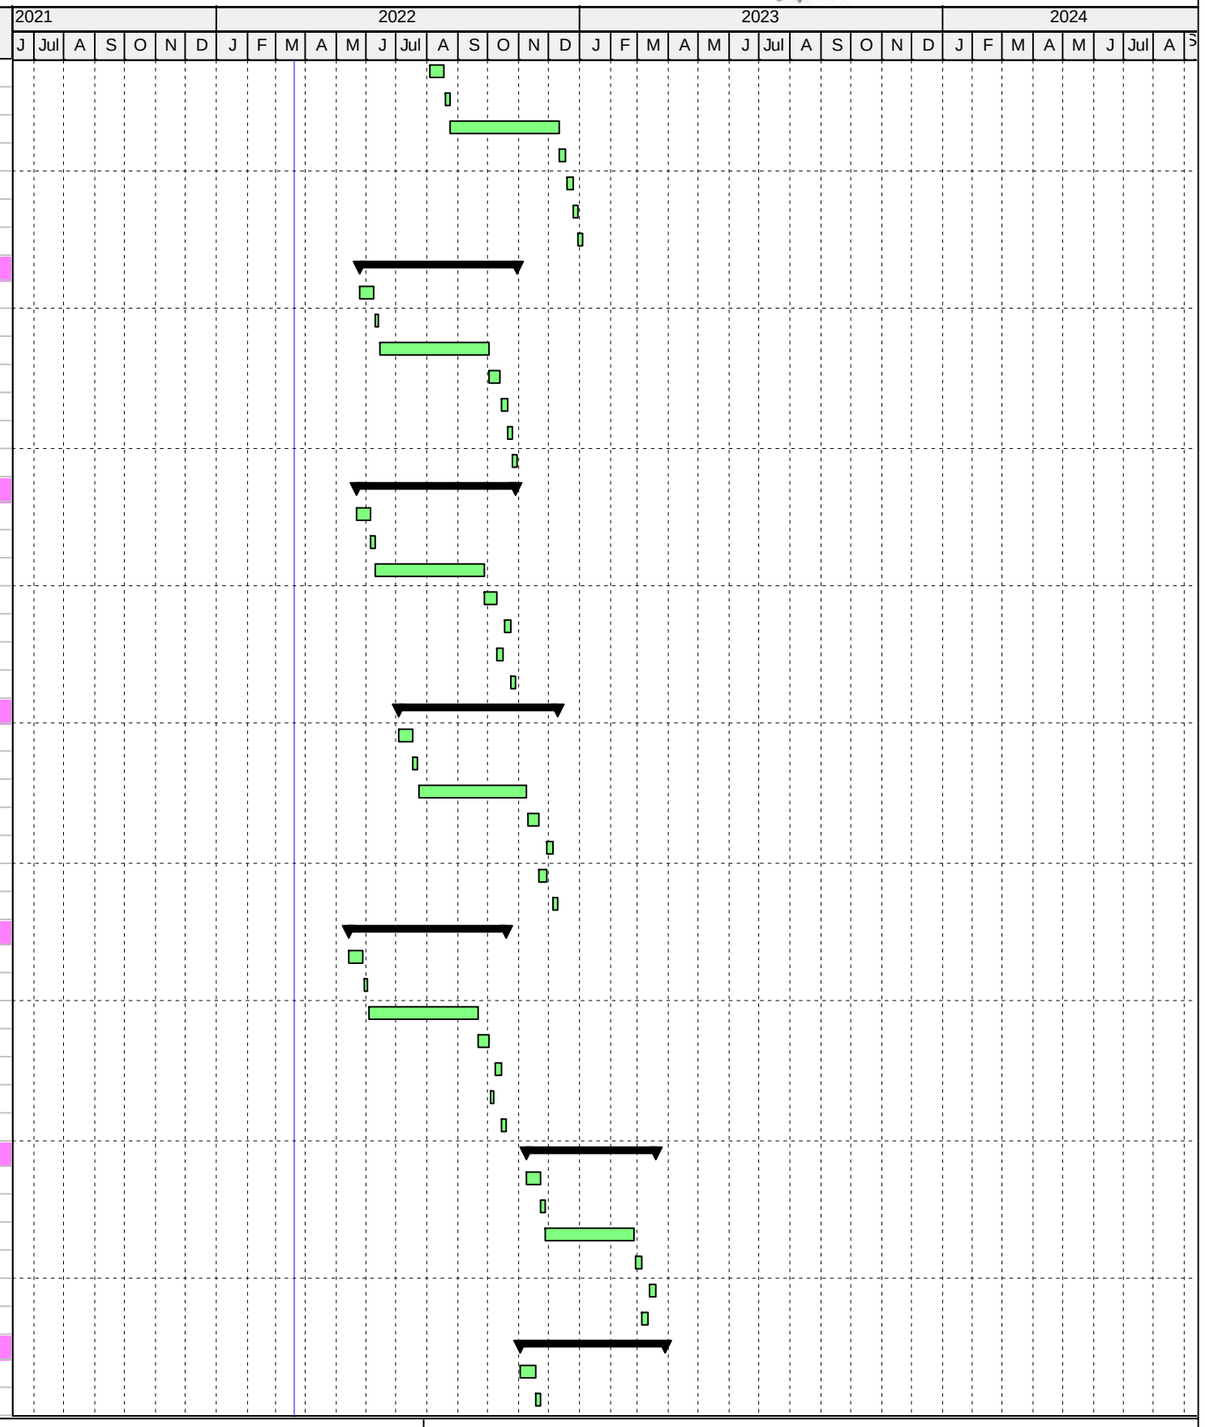


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P02-E	Manufacturing / Fabrication / Supply	100	0%	$144.10	23-Nov-22	02-Mar-23
P02-E	Final Inspection	12	0%	$28.82	03-Mar-23	14-Mar-23
P02-E	Submitting Vendor Data Book	7	0%	$72.05	22-Mar-23	28-Mar-23
P02-E	Delivery On Site	7	0%	$14.41	15-Mar-23	21-Mar-23
Instrument Installation Accessories		139	0%	$214.84	30-Sep-22	15-Feb-23
P02-E	Tendering & Selection	15	0%	$8.59	30-Sep-22	14-Oct-22
P02-E	Contract Effectiveness / PO	5	0%	$12.89	15-Oct-22	19-Oct-22
P02-E	Manufacturing / Fabrication / Supply	100	0%	$107.42	20-Oct-22	27-Jan-23
P02-E	Final Inspection	7	0%	$21.48	28-Jan-23	03-Feb-23
P02-E	Submitting Vendor Data Book	5	0%	$53.71	11-Feb-23	15-Feb-23
P02-E	Delivery On Site	7	0%	$10.74	04-Feb-23	10-Feb-23
Differential Pressure/Pressure Gauge		151	0%	$288.20	14-May-22	11-Oct-22
P02-E	Tendering & Selection	15	0%	$11.53	14-May-22	28-May-22
P02-E	Contract Effectiveness / PO	5	0%	$17.29	29-May-22	02-Jun-22
P02-E	Manufacturing / Fabrication / Supply	100	0%	$144.10	03-Jun-22	10-Sep-22
P02-E	Final Inspection	12	0%	$28.82	11-Sep-22	22-Sep-22
P02-E	Delivery On Site	7	0%	$57.64	23-Sep-22	29-Sep-22
P02-E	Submitting Vendor Data Book	7	0%	$14.41	30-Sep-22	06-Oct-22
P02-E	Delivering Spare Parts	5	0%	$14.41	07-Oct-22	11-Oct-22
Temperature Gauge		151	0%	$288.20	07-Jun-22	04-Nov-22
P02-E	Tendering & Selection	15	0%	$11.53	07-Jun-22	21-Jun-22
P02-E	Contract Effectiveness / PO	5	0%	$17.29	22-Jun-22	26-Jun-22
P02-E	Manufacturing / Fabrication / Supply	100	0%	$144.10	27-Jun-22	04-Oct-22
P02-E	Final Inspection	12	0%	$28.82	05-Oct-22	16-Oct-22
P02-E	Delivery On Site	7	0%	$57.64	17-Oct-22	23-Oct-22
P02-E	Submitting Vendor Data Book	7	0%	$14.41	24-Oct-22	30-Oct-22
P02-E	Delivering Spare Parts	5	0%	$14.41	31-Oct-22	04-Nov-22
Instrument Tube and Fitting		129	0%	$356.32	07-Jul-22	12-Nov-22
P02-E	Tendering & Selection	10	0%	$14.25	07-Jul-22	16-Jul-22
P02-E	Contract Effectiveness / PO	5	0%	$21.38	17-Jul-22	21-Jul-22
P02-E	Manufacturing / Fabrication / Supply	90	0%	$178.16	22-Jul-22	19-Oct-22
P02-E	Final Inspection	12	0%	$35.63	20-Oct-22	31-Oct-22
P02-E	Submitting Vendor Data Book	7	0%	$89.08	06-Nov-22	12-Nov-22
P02-E	Delivery On Site	5	0%	$17.82	01-Nov-22	05-Nov-22
Instrument Cable Tray		134	0%	$214.84	30-Sep-22	10-Feb-23
P02-E	Tendering & Selection	15	0%	$8.59	30-Sep-22	14-Oct-22
P02-E	Contract Effectiveness / PO	5	0%	$12.89	15-Oct-22	19-Oct-22
P02-E	Manufacturing / Fabrication / Supply	90	0%	$107.42	20-Oct-22	17-Jan-23
P02-E	Final Inspection	12	0%	$21.48	18-Jan-23	29-Jan-23
P02-E	Submitting Vendor Data Book	7	0%	$53.71	04-Feb-23	10-Feb-23
P02-E	Delivery On Site	5	0%	$10.74	30-Jan-23	03-Feb-23
Safety & Fire Fighting		121	0%	$1,036.58	03-Sep-22	01-Jan-23
Fire Fighting and Safety Equipment		79	0%	$772.35	03-Sep-22	20-Nov-22
P02-E	Tendering & Selection	30	0%	$30.89	03-Sep-22	02-Oct-22
P02-E	Contract Effectiveness / PO	5	0%	$46.34	03-Oct-22	07-Oct-22
P02-E	Manufacturing / Fabrication / Supply	20	0%	$386.18	08-Oct-22	27-Oct-22
P02-E	Final Inspection	12	0%	$77.24	28-Oct-22	08-Nov-22
P02-E	Delivery On Site	7	0%	$193.09	09-Nov-22	15-Nov-22
P02-E	Submitting Vendor Data Book	5	0%	$38.62	16-Nov-22	20-Nov-22

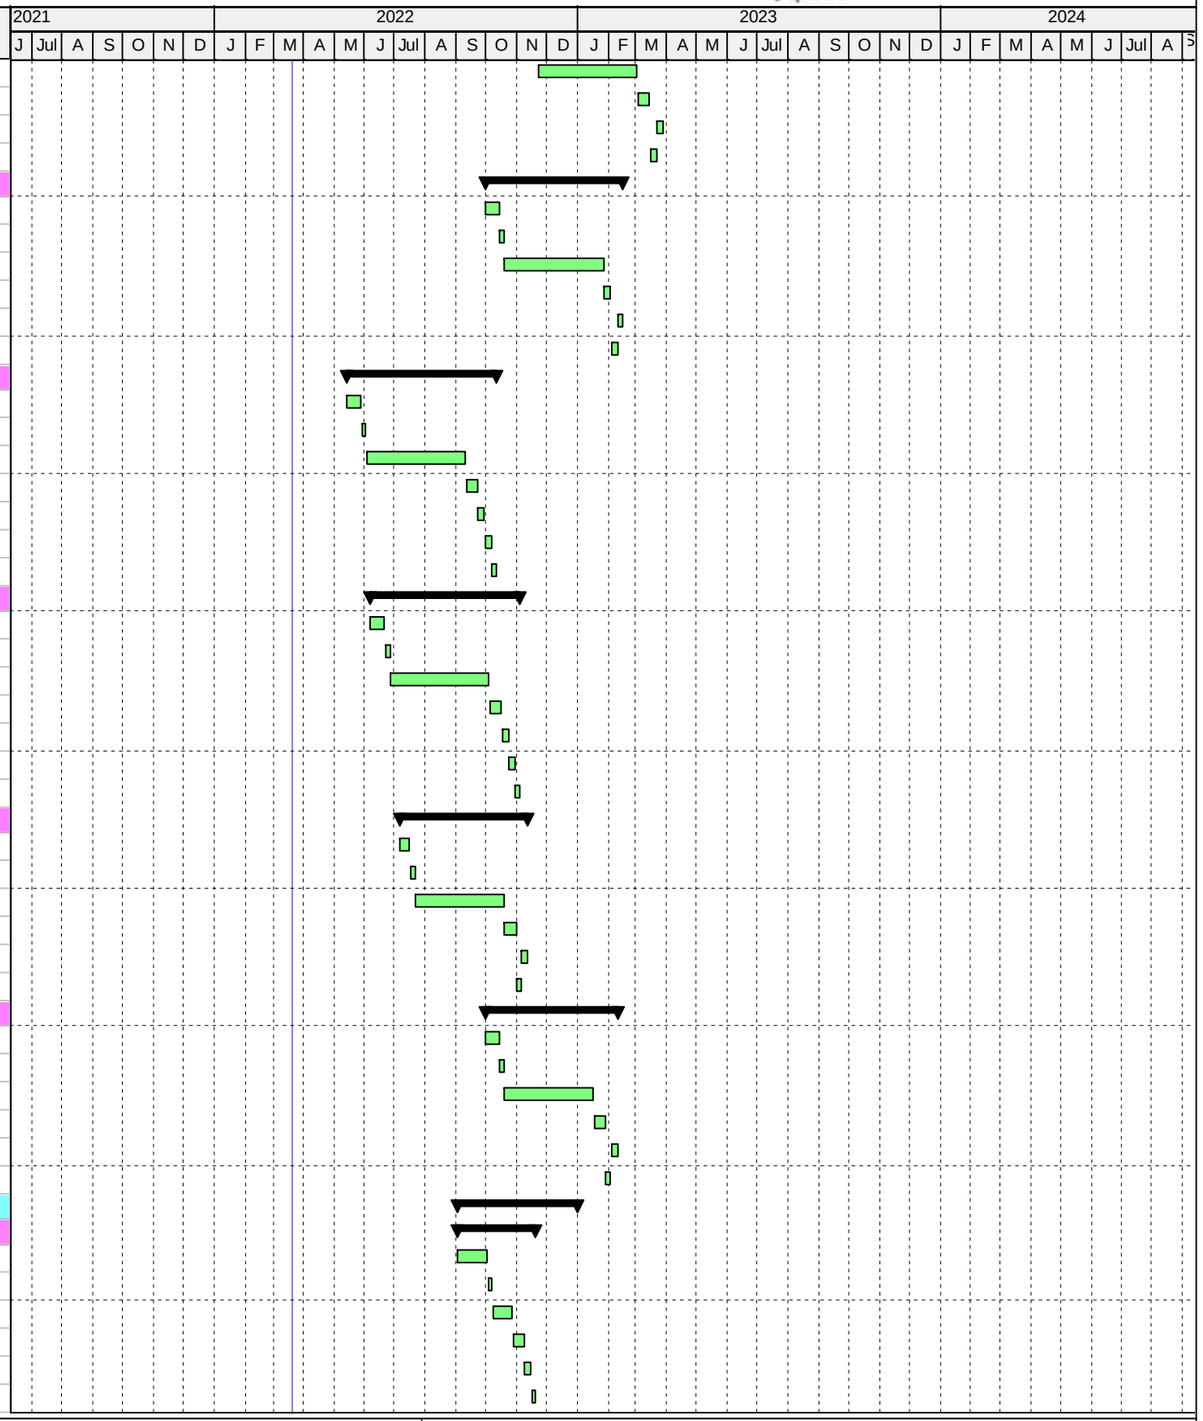


Actual Level of Effort | Remaining Work | Milestone

Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Fire Safety Sign		79	0%	$264.22	15-Oct-22	01-Jan-23
P02-E	Tendering & Selection	30	0%	$10.57	15-Oct-22	13-Nov-22
P02-E	Contract Effectiveness / PO	5	0%	$15.85	14-Nov-22	18-Nov-22
P02-E	Manufacturing / Fabrication / Supply	20	0%	$132.11	19-Nov-22	08-Dec-22
P02-E	Final Inspection	12	0%	$26.42	09-Dec-22	20-Dec-22
P02-E	Delivery On Site	7	0%	$66.06	21-Dec-22	27-Dec-22
P02-E	Submitting Vendor Data Book	5	0%	$13.21	28-Dec-22	01-Jan-23
Electrical		284	0%	$17,640.82	05-Jun-22	15-Mar-23
LV Switchgear & MCC		159	0%	$2,831.35	05-Jun-22	10-Nov-22
P02-E	Tendering & Selection	15	0%	$113.25	05-Jun-22	19-Jun-22
P02-E	Contract Effectiveness / PO	5	0%	$169.88	20-Jun-22	24-Jun-22
P02-E	Manufacturing / Fabrication / Supply	110	0%	$1,415.68	25-Jun-22	12-Oct-22
P02-E	Final Inspection	12	0%	$283.14	13-Oct-22	24-Oct-22
P02-E	Delivery On Site	7	0%	$566.27	25-Oct-22	31-Oct-22
P02-E	Submitting Vendor Data Book	5	0%	$141.57	01-Nov-22	05-Nov-22
P02-E	Delivering Spare Parts	5	0%	$141.57	06-Nov-22	10-Nov-22
UPS System		149	0%	$7,075.73	12-Sep-22	07-Feb-23
P02-E	Tendering & Selection	15	0%	$283.03	12-Sep-22	26-Sep-22
P02-E	Contract Effectiveness / PO	5	0%	$424.54	27-Sep-22	01-Oct-22
P02-E	Manufacturing / Fabrication / Supply	100	0%	$3,537.87	02-Oct-22	09-Jan-23
P02-E	Final Inspection	12	0%	$707.57	10-Jan-23	21-Jan-23
P02-E	Delivery On Site	7	0%	$1,415.15	22-Jan-23	28-Jan-23
P02-E	Submitting Vendor Data Book	5	0%	$353.79	29-Jan-23	02-Feb-23
P02-E	Delivering Spare Parts	5	0%	$353.79	03-Feb-23	07-Feb-23
DC Charger		154	0%	$4,715.39	05-Jun-22	05-Nov-22
P02-E	Tendering & Selection	15	0%	$188.62	05-Jun-22	19-Jun-22
P02-E	Contract Effectiveness / PO	5	0%	$282.92	20-Jun-22	24-Jun-22
P02-E	Manufacturing / Fabrication / Supply	110	0%	$2,357.70	25-Jun-22	12-Oct-22
P02-E	Final Inspection	7	0%	$471.54	13-Oct-22	19-Oct-22
P02-E	Delivery On Site	7	0%	$943.08	20-Oct-22	26-Oct-22
P02-E	Submitting Vendor Data Book	5	0%	$235.77	27-Oct-22	31-Oct-22
P02-E	Delivering Spare Parts	5	0%	$235.77	01-Nov-22	05-Nov-22
Earthing & Lightning System		154	0%	$471.01	05-Jun-22	05-Nov-22
P02-E	Tendering & Selection	15	0%	$18.84	05-Jun-22	19-Jun-22
P02-E	Contract Effectiveness / PO	5	0%	$28.26	20-Jun-22	24-Jun-22
P02-E	Manufacturing / Fabrication / Supply	110	0%	$235.50	25-Jun-22	12-Oct-22
P02-E	Final Inspection	7	0%	$47.10	13-Oct-22	19-Oct-22
P02-E	Delivery On Site	7	0%	$94.20	20-Oct-22	26-Oct-22
P02-E	Submitting Vendor Data Book	5	0%	$23.55	27-Oct-22	31-Oct-22
P02-E	Delivering Spare Parts	5	0%	$23.55	01-Nov-22	05-Nov-22
Power & Control Cables		99	0%	$943.78	07-Dec-22	15-Mar-23
P02-E	Tendering & Selection	15	0%	$37.75	07-Dec-22	21-Dec-22
P02-E	Contract Effectiveness / PO	5	0%	$56.63	22-Dec-22	26-Dec-22
P02-E	Manufacturing / Fabrication / Supply	60	0%	$471.89	27-Dec-22	24-Feb-23
P02-E	Final Inspection	7	0%	$94.38	25-Feb-23	03-Mar-23
P02-E	Delivery On Site	7	0%	$235.95	04-Mar-23	10-Mar-23
P02-E	Submitting Vendor Data Book	5	0%	$47.19	11-Mar-23	15-Mar-23
Tray/Ladder and Accessories		154	0%	$642.13	07-Jun-22	07-Nov-22
P02-E	Tendering & Selection	15	0%	$25.69	07-Jun-22	21-Jun-22

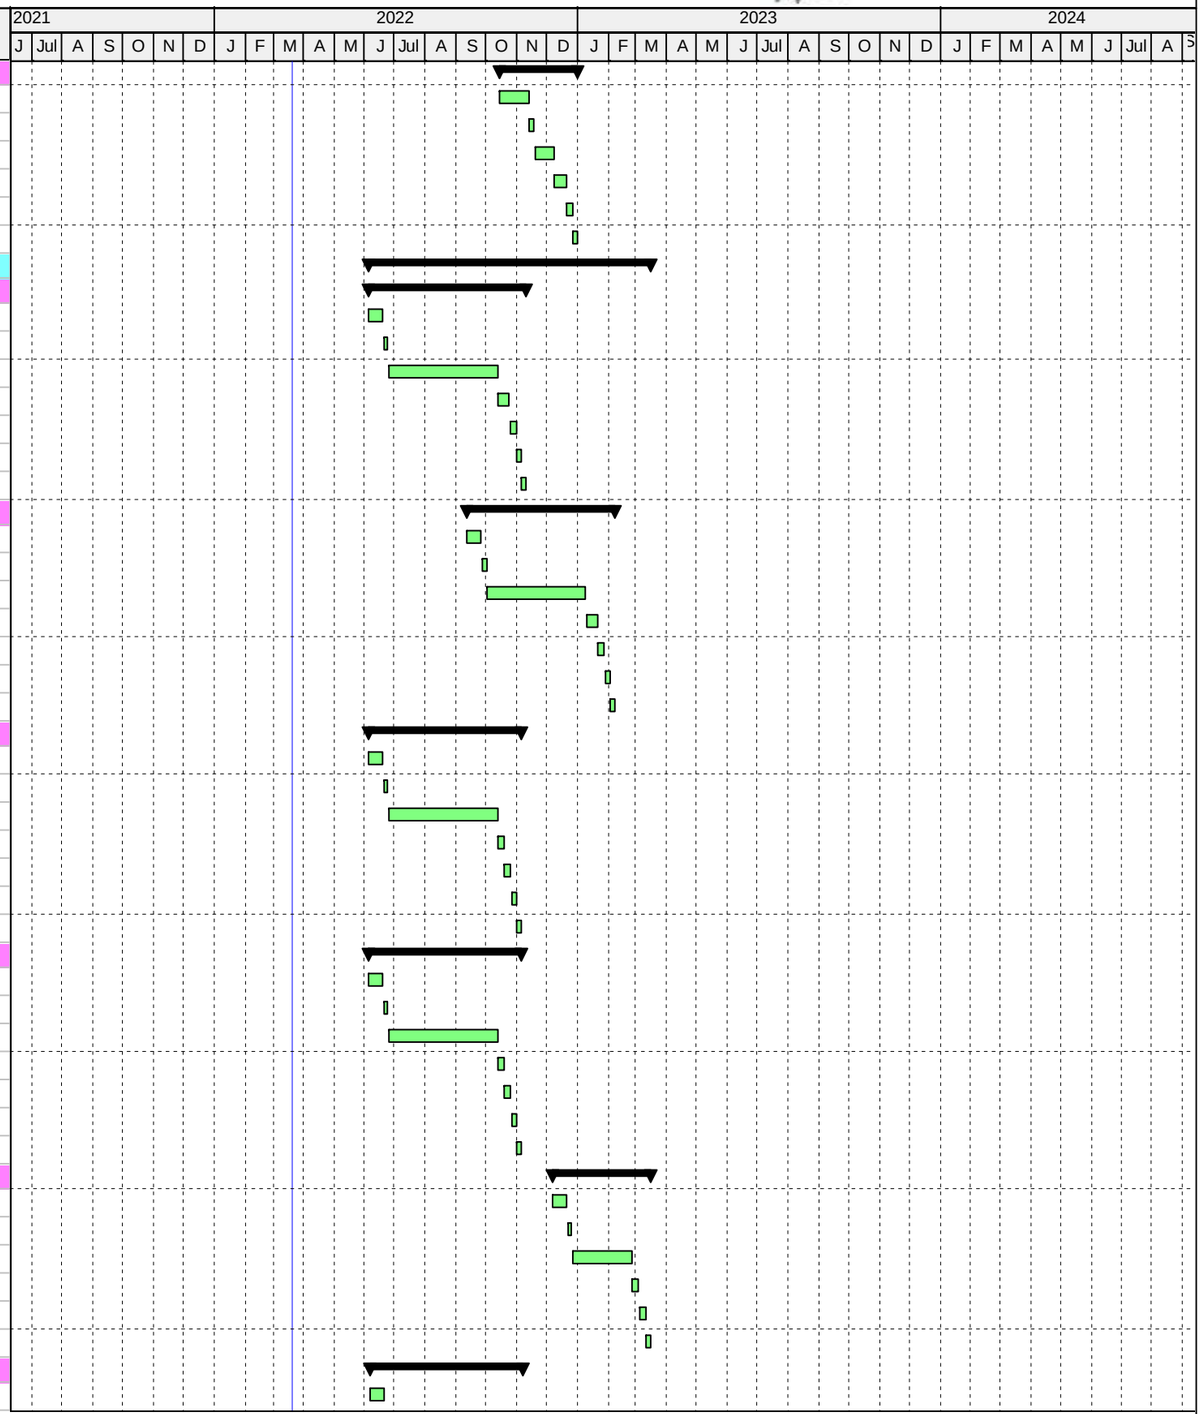


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P02-E	Contract Effectiveness / PO	5	0%	$38.53	22-Jun-22	26-Jun-22
P02-E	Manufacturing / Fabrication / Supply	60	0%	$321.06	27-Jun-22	25-Aug-22
P02-E	Final Inspection	7	0%	$64.21	15-Oct-22	21-Oct-22
P02-E	Delivery On Site	7	0%	$160.53	27-Oct-22	02-Nov-22
P02-E	Submitting Vendor Data Book	5	0%	$32.11	03-Nov-22	07-Nov-22
Electrical Bulk Items		154	0%	$961.42	07-Jun-22	07-Nov-22
P02-E	Tendering & Selection	15	0%	$38.46	07-Jun-22	21-Jun-22
P02-E	Contract Effectiveness / PO	5	0%	$57.69	22-Jun-22	26-Jun-22
P02-E	Manufacturing / Fabrication / Supply	110	0%	$480.71	27-Jun-22	14-Oct-22
P02-E	Final Inspection	12	0%	$96.14	15-Oct-22	26-Oct-22
P02-E	Delivery On Site	7	0%	$240.36	27-Oct-22	02-Nov-22
P02-E	Submitting Vendor Data Book	5	0%	$48.07	03-Nov-22	07-Nov-22
Construction		400	38.14%	$188,852.00	31-Aug-21	08-May-23
Wellpad and Access Road		86	53.71%	$133,896.07	31-Aug-21	28-Jun-22
Access Road		58	55.55%	$26,779.21	31-Aug-21	25-May-22
Wellpad Access Road		58	53.18%	$21,423.37	31-Aug-21	25-May-22
P02-E	Access Road Preparation	15	80%	$6,427.01	31-Aug-21	14-Apr-22
P02-E	Filling and Compaction	7	20%	$3,213.51	31-Aug-21	14-Apr-22
P02-E	Sub-Base Layer	10	0%	$5,355.84	04-Apr-22	13-Apr-22
Construction of Culvert and Bridge		51	87.28%	$6,427.01	15-Dec-21	25-May-22
bridge		33	68.2%	$2,570.80	15-Dec-21	25-May-22
P02	Excavation	7	100%	$257.08	15-Dec-21	19-Apr-22
P02	lean concrete	2	70%	$205.66	25-Dec-21	21-Apr-22
P02	wall	5	70%	$462.74	25-Dec-21	26-Apr-22
P02	reinforcement	7	60%	$514.16	06-Mar-22	03-May-22
P02	form working	7	70%	$257.08	28-Dec-21	10-May-22
P02	concrete pouring	5	70%	$771.24	06-Jan-22	15-May-22
P02	protect stone	3	0%	$51.42	15-May-22	18-May-22
P02	Backfill	7	0%	$51.42	18-May-22	25-May-22
culverts		15	100%	$3,856.21	15-Dec-21	19-Apr-22
P02	pipeway culvert	5	100%	$1,542.48	15-Dec-21	17-Apr-22
P02	pipeway	5	100%	$1,156.86	15-Dec-21	08-Apr-22
P02	pipeline culvert	7	100%	$1,156.86	15-Dec-21	19-Apr-22
Burn Pit Access Road		23	65%	$5,355.84	18-Jan-22	07-May-22
P02-E	ROW Preparation	15	100%	$3,481.30	18-Jan-22	25-Apr-22
P02-E	Filling and Compaction	10	0%	$1,071.17	21-Apr-22	30-Apr-22
P02-E	Sub-Base Layer	7	0%	$803.38	01-May-22	07-May-22
Wellpad		76	53.25%	$107,116.85	15-Sep-21	28-Jun-22
Site Preparation		30	85%	$37,490.90	15-Sep-21	03-May-22
P02-E	Site Prepaation W028	30	85%	$37,490.90	15-Sep-21	03-May-22
Water Supply		20	0%	$7,498.18	14-Apr-22	03-May-22
P02-E	Water Supply	20	0%	$7,498.18	14-Apr-22	03-May-22
Civil Work		56	65%	$32,135.06	25-Nov-21	28-Jun-22
P02-E	Excavation and Soil Removal (Cellar)	15	100%	$20,887.79	25-Nov-21	09-May-22
P02-E	Installation of Conductor Pipe	20	0%	$1,606.75	04-May-22	23-May-22
P02-E	Form Work (Above Cellar)	25	0%	$1,606.75	09-May-22	03-Jun-22
P02-E	Armed Concrete	25	0%	$8,033.76	03-Jun-22	28-Jun-22
Surface Preparation		25	0%	$1,071.17	14-Apr-22	08-May-22
P02-E	Gravel Paving	25	0%	$1,071.17	14-Apr-22	08-May-22
Mud Channel		24	0%	$6,427.01	04-May-22	27-May-22

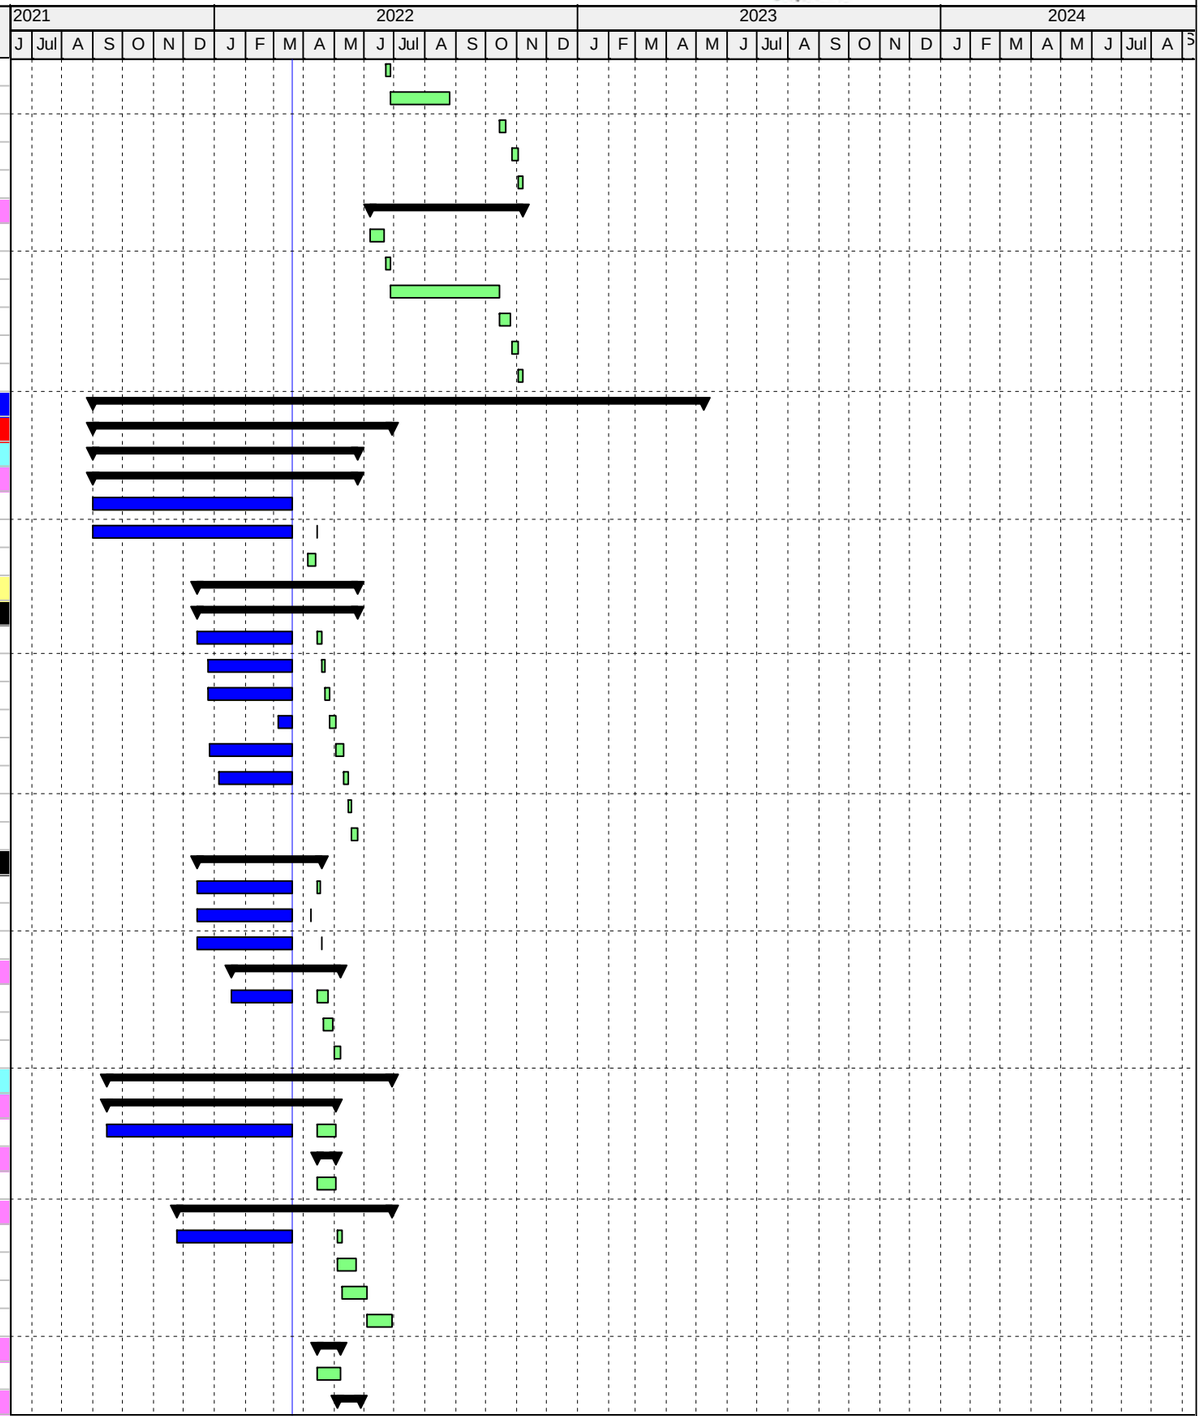


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P02-E	Excavation	7	0%	$642.70	11-May-22	17-May-22
P02-E	Soil Removal, Filling and Compaction of Mud Pit Area	7	0%	$964.05	04-May-22	10-May-22
P02-E	Construction of Mud Pit's Walls	5	0%	$2,249.45	18-May-22	22-May-22
P02-E	Installation sealling Layer	7	0%	$1,928.10	04-May-22	10-May-22
P02-E	Backfill	5	0%	$642.70	23-May-22	27-May-22
Mud Pit		13	0%	$10,711.69	29-Apr-22	12-May-22
P02-E	Soil Removal, Filling and Compaction of Mud Pit Area	7	0%	$3,749.09	04-May-22	10-May-22
P02-E	Construction of Mud Pit's Walls	7	0%	$2,142.34	29-Apr-22	05-May-22
P02-E	Installation sealling Layer	6	0%	$4,820.26	06-May-22	12-May-22
SepticTank		35	0%	$4,284.67	04-May-22	07-Jun-22
P02-E	Excavation & Soil Transfer	10	0%	$1,285.40	04-May-22	13-May-22
P02-E	Levelling	3	0%	$21.42	14-May-22	16-May-22
P02-E	Tank Supply	15	0%	$2,442.26	14-May-22	28-May-22
P02-E	Tank Execution	5	0%	$407.04	29-May-22	02-Jun-22
P02-E	Backfilling & Compaction	5	0%	$128.54	03-Jun-22	07-Jun-22
Burn Pit		19	80%	$5,355.84	18-Jan-22	16-May-22
P02-E	Soil Removal, Triming ,Filling and Compaction of Burn Pit Are	7	100%	$4,284.67	18-Jan-22	06-May-22
P02-E	Construction & Installation of Support	5	0%	$267.79	06-May-22	11-May-22
P02-E	Welding, Installation and Testing	7	0%	$803.38	09-May-22	16-May-22
Gasoil Pad		11	0%	$2,142.34	11-Jun-22	21-Jun-22
P02-E	Excavation	5	0%	$428.47	11-Jun-22	16-Jun-22
P02-E	Formwork	3	0%	$642.70	18-Jun-22	20-Jun-22
P02-E	Armed Concrete	4	0%	$214.23	18-Jun-22	21-Jun-22
P02-E	Lean Concrete	2	0%	$856.93	16-Jun-22	18-Jun-22
Wellhead Facility and Flowline		222	0%	$50,234.63	28-Jun-22	05-Feb-23
Civil		172	0%	$17,833.29	28-Jun-22	17-Dec-22
P02-EF	Right of Way	15	0%	$13,374.97	28-Jun-22	13-Jul-22
P02-EF	Steel Works(Wellhead Facilities)	10	0%	$3,031.66	13-Jul-22	23-Jul-22
P02-EF	Construction & Installation of Shelter for Wellhead Control Pa	5	0%	$891.66	23-Jul-22	28-Jul-22
P02-EF	Well Pad Fencing	7	0%	$535.00	10-Dec-22	17-Dec-22
Flowline		92	0%	$21,349.72	12-Jul-22	11-Oct-22
P02-EF	Construction of Pipe Support	30	0%	$3,202.46	12-Jul-22	10-Aug-22
P02-EF	Installation of Pipe Supports	10	0%	$3,202.46	06-Sep-22	15-Sep-22
6" Flowline Installation		26	0%	$13,877.32	08-Sep-22	04-Oct-22
P02-E	COLD CUT	5	0%	$693.87	08-Sep-22	13-Sep-22
P02-E	Material Handeling	5	0%	$1,665.28	13-Sep-22	18-Sep-22
P02-E	Fit-Up & Welding	7	0%	$9,159.03	15-Sep-22	22-Sep-22
P02-E	Bending	5	0%	$1,457.12	22-Sep-22	27-Sep-22
P02-E	NDT	7	0%	$902.03	27-Sep-22	04-Oct-22
Hydrostatic Test		7	0%	$1,067.49	04-Oct-22	11-Oct-22
P02-E	6" Pigging and Hydrostatic Test	7	0%	$1,067.49	04-Oct-22	11-Oct-22
Piping		51	0%	$4,269.94	10-Dec-22	30-Jan-23
P02-EF	Sweep Bend Installation	5	0%	$213.50	10-Dec-22	15-Dec-22
P02-EF	Construction of Spools (Fit up, Welding, NDT…)	5	0%	$1,494.48	19-Jan-23	23-Jan-23
P02-EF	Valves, Fitting and Spools Installation and Hydrotest	5	0%	$2,348.47	24-Jan-23	28-Jan-23
P02-EF	Painting	2	0%	$213.50	29-Jan-23	30-Jan-23
Instrument Works		6	0%	$4,269.94	10-Dec-22	16-Dec-22
P02-EF	Wellhead Control Panel Installation	3	0%	$2,134.97	10-Dec-22	13-Dec-22
P02-EF	Devices Installation and Piping Connecton	5	0%	$2,134.97	12-Dec-22	16-Dec-22

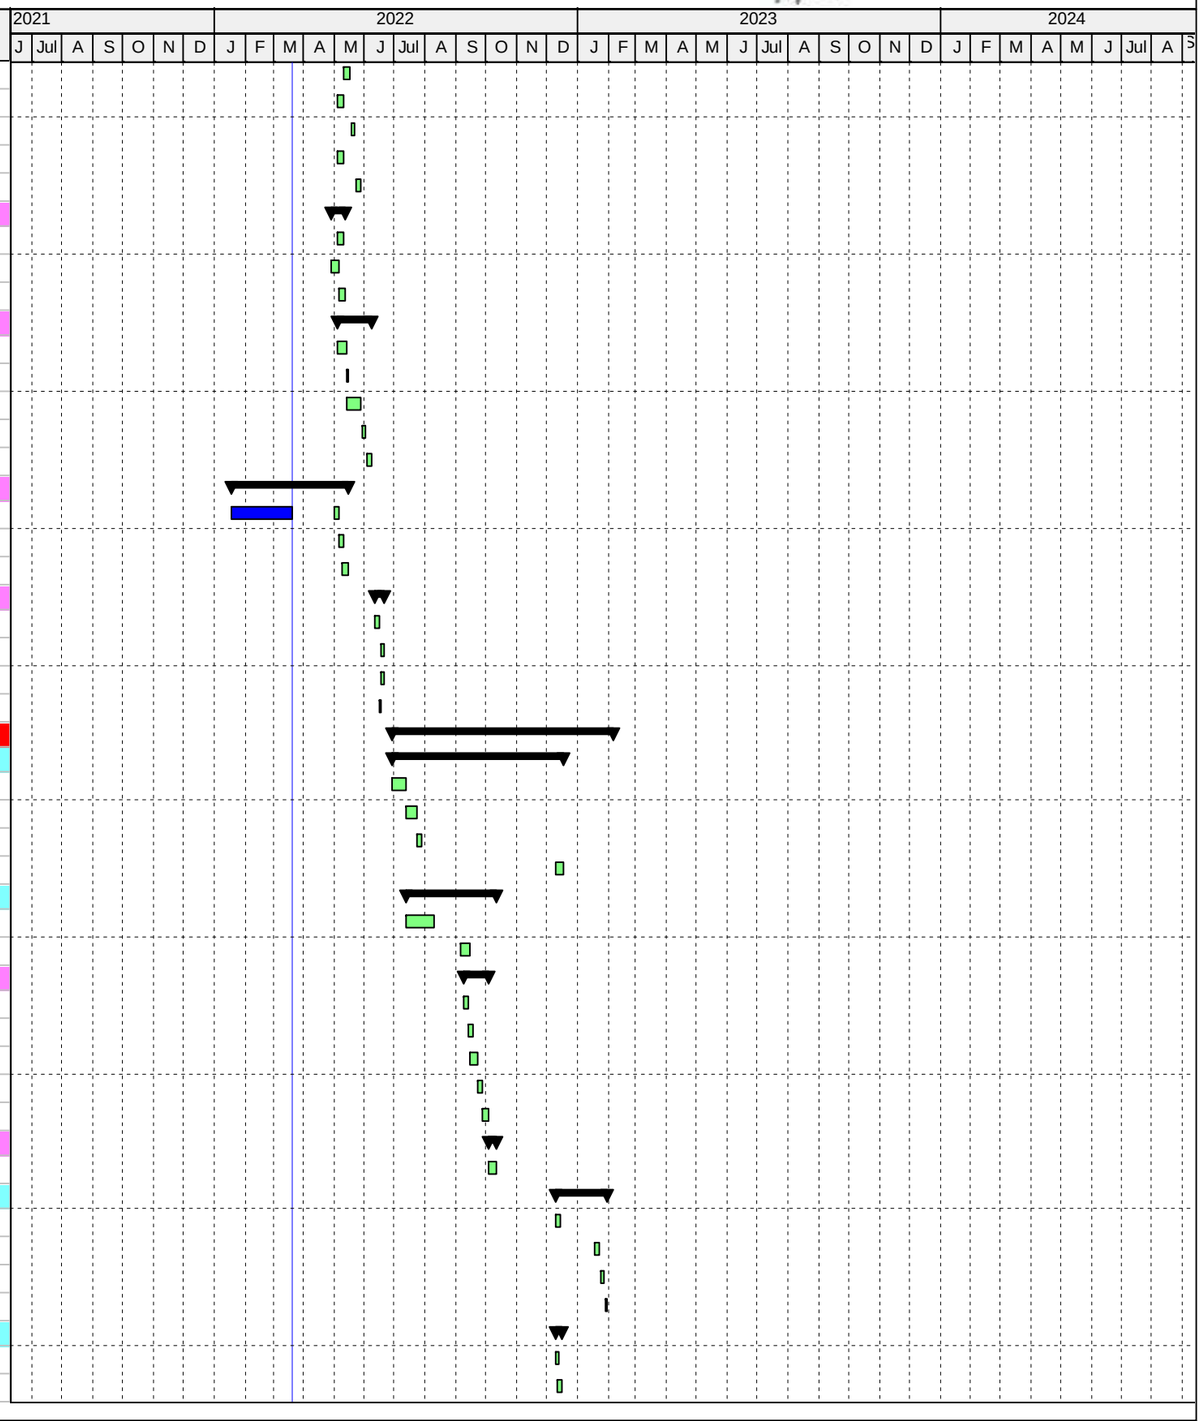


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Pre-commissioning		6	0%	$2,511.73	31-Jan-23	05-Feb-23
P02-EF	Pre-commissioning	3	0%	$2,260.56	31-Jan-23	02-Feb-23
P02-EF	Ready for Comm.Certificate(RFCC)	3	0%	$251.17	03-Feb-23	05-Feb-23
Helipad		86	0%	$1,888.52	14-Apr-22	08-Jul-22
P02-EP	Excavation & Soil Transfer	20	0%	$188.85	14-Apr-22	03-May-22
P02-EP	Levelling	15	0%	$226.62	27-Apr-22	12-May-22
P02-EP	Lean Concrete	3	0%	$283.28	12-May-22	15-May-22
P02-EP	Reinforced Work	15	0%	$283.28	15-May-22	30-May-22
P02-EP	Form Work	20	0%	$283.28	24-May-22	13-Jun-22
P02-EP	Main Concrete Pouring	3	0%	$377.70	13-Jun-22	16-Jun-22
P02-EP	Backfilling & Compaction	15	0%	$207.74	16-Jun-22	01-Jul-22
P02-EP	Paint Marking	7	0%	$37.77	01-Jul-22	08-Jul-22
Job Site HSE Supervision (Surface)		250	30%	$377.70	18-Jan-22	08-Jan-23
P02-EP	Job Site HSE Supervision (Surface)	250	30%	$377.70	18-Jan-22	08-Jan-23
Commissioning, Startup & Handover		92	0%	$2,455.08	06-Feb-23	08-May-23
Handover		38	0%	$736.52	01-Apr-23	08-May-23
P02-EF	Compiling & Submitting Final Documentation	20	0%	$220.96	01-Apr-23	20-Apr-23
P02-EF	Training of Operator's Personnel	3	0%	$294.61	21-Apr-23	23-Apr-23
P02-EF	Provisional Acceptance Certificate (PAC)	15	0%	$220.96	23-Apr-23	08-May-23
Startup & Performance Test		19	0%	$982.03	13-Mar-23	31-Mar-23
P02-EF	Startup & Performance Test Run	4	0%	$785.62	13-Mar-23	16-Mar-23
P02-EF	Start of Production (SOP)	15	0%	$196.41	17-Mar-23	31-Mar-23
Commissioning		35	0%	$736.52	06-Feb-23	12-Mar-23
P02-EF	Materials & Utilities Ready for Commissioning	4	0%	$36.83	06-Feb-23	09-Feb-23
P02-EF	Receiving Facilities Ready for Commissioning	3	0%	$36.83	10-Feb-23	12-Feb-23
P02-EF	Permits Obtained for Commissioning	10	0%	$36.83	13-Feb-23	22-Feb-23
P02-EF	Integrated Commissioning	3	0%	$589.22	23-Feb-23	25-Feb-23
P02-EF	Ready for Startup Certificate (RFSU)	15	0%	$36.83	26-Feb-23	12-Mar-23
Package 03-New Well # W046S (Bangestan)		475	2.06%	$2,128,404.00	24-Jul-21 A	29-Jun-23
ENGINEERING		475	20.99%	$16,250.00	24-Jul-21 A	14-Jun-23
Basic Design Endorsement		30	100%	$812.50	31-Jul-21 A	20-Mar-22
P03-EP	Endorsement Report For Basic Design & Scope of Work	30	100%	$812.50	31-Jul-21 A	20-Mar-22
Value Engineering		75	22.5%	$487.50	01-Feb-22	02-Jul-22
P03-EP	Value Engineering Study Report	44	60%	$182.81	01-Feb-22	02-May-22
P03-EP	HAZID Report For WHF & Flowlines	44	0%	$304.69	20-May-22	02-Jul-22
Detail Design		475	27.41%	$8,937.50	24-Jul-21 A	25-Dec-22
Process		114	64.9%	$715.00	27-Jul-21 A	16-Jul-22
Basis/Criteria		54	86.99%	$143.00	27-Jul-21 A	12-May-22
P03-E	Process Design Criteria	39	100%	$49.98	27-Jul-21 A	20-Mar-22
P03-E	Process Basis Of Design	54	80%	$93.02	27-Jul-21 A	12-May-22
Drawing/Diagram		100	88.01%	$178.75	30-Oct-21	23-May-22
P03-E	Symbol & Legend For PFD and P&ID	44	80%	$6.36	30-Oct-21	02-May-22
P03-E	Process Flow Diagram - W0046S	35	100%	$71.55	01-Nov-21	20-Mar-22
P03-E	P&ID - W0046S	35	80%	$38.16	01-Nov-21	23-Apr-22
P03-E	P&ID for Diesel Oil Drum- W0046S	30	80%	$31.33	16-Nov-21	23-May-22
P03-E	P&ID for Potable Water Tank - W0046S	30	80%	$31.33	16-Nov-21	23-May-22
Philosophy		74	11.01%	$107.25	21-Nov-21	01-Jun-22
P03-E	Drainage Philosophy	44	0%	$4.24	19-Apr-22	01-Jun-22
P03-E	Control Philosophy	44	0%	$29.39	19-Apr-22	01-Jun-22
P03-E	Flare,Blow Down And Relief Philosophy	44	0%	$29.39	19-Apr-22	01-Jun-22

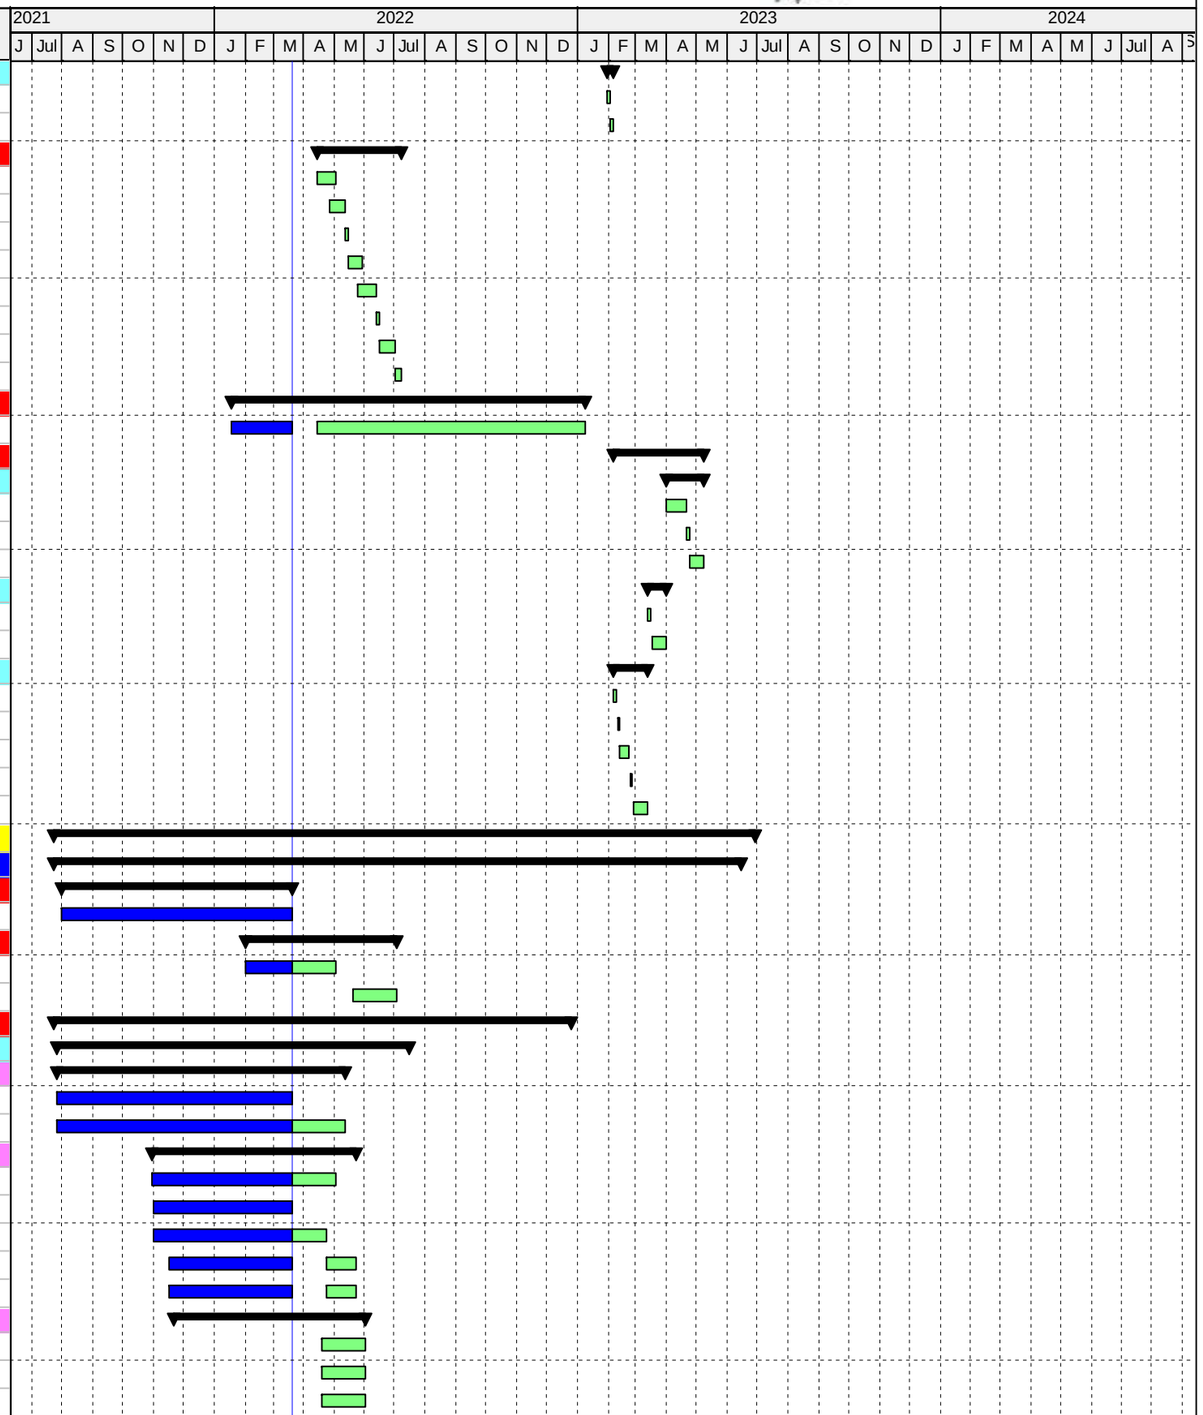


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	Isolation Philosophy	44	60%	$19.69	21-Nov-21	02-May-22
P03-E	ESD Philosophy	44	0%	$24.55	19-Apr-22	01-Jun-22
Data Sheet		84	0%	$71.50	24-Apr-22	16-Jul-22
P03-E	Process Data Sheets For Instrument Devices - W046S	39	0%	$24.31	24-Apr-22	01-Jun-22
P03-E	Process Data Sheets For Fuel Oil Storage Drum of Well Pads	35	0%	$23.60	12-Jun-22	16-Jul-22
P03-E	Process Data Sheets For Potable Water Tank of Well Pads	35	0%	$23.60	23-May-22	26-Jun-22
Report		44	80%	$143.00	30-Oct-21	06-Jun-22
P03-E	Flowline Hydraulic Calculation Report	44	80%	$143.00	30-Oct-21	06-Jun-22
List		84	78.46%	$71.50	08-Nov-21	02-May-22
P03-E	Line List - W0046S	44	80%	$66.00	08-Nov-21	02-May-22
P03-E	Consumption List	44	60%	$5.50	23-Feb-22	02-May-22
Mechanical		75	77.77%	$89.38	28-Jul-21 A	08-May-22
Basis/Criteria		40	60%	$9.93	28-Jul-21 A	28-Apr-22
P03-E	Mechanical Design Criteria	40	60%	$9.93	28-Jul-21 A	28-Apr-22
Specification		30	60%	$14.90	28-Jul-21 A	08-May-22
P03-E	Specification For Pressure Vessels	30	60%	$7.45	28-Jul-21 A	08-May-22
P03-E	Specification For Atmospheric Above Ground Welded Steel Ta	30	60%	$7.45	28-Jul-21 A	08-May-22
Data Sheet		35	60%	$24.83	16-Jan-22	08-May-22
P03-E	Data Sheets For Fuel Oil Storage Drum of Well Pads	25	60%	$11.41	16-Jan-22	03-May-22
P03-E	Data Sheets For Potable Water Tank of Well Pads	25	60%	$13.42	09-Feb-22	08-May-22
Drawing/Diagram		34	100%	$39.72	28-Jul-21 A	09-Apr-22
P03-E	Standard Detail Drawing For Pressure Vessels and Heat Exch	14	100%	$19.86	28-Jul-21 A	09-Apr-22
P03-E	Standard Detail Drawing For Storage Tanks	14	100%	$19.86	28-Jul-21 A	09-Apr-22
HVAC/Plumbing		402	11.68%	$178.75	24-Jul-21 A	24-Dec-22
Basis/Criteria		64	100%	$2.59	24-Jul-21 A	14-May-22
P03-E	HVAC & Plumbing Design Criteria	64	100%	$2.59	24-Jul-21 A	14-May-22
Specification		64	100%	$4.15	24-Jul-21 A	27-Mar-22
P03-E	Specification For HVAC Equipment	64	100%	$2.49	24-Jul-21 A	27-Mar-22
P03-E	Specification For Duct Work & Pipe Work	64	100%	$1.66	24-Jul-21 A	27-Mar-22
Calculation		233	30%	$41.45	14-Mar-22	20-Aug-22
P03-E	HVAC Calculation Note For Switchgear Building - W046S	55	60%	$20.73	14-Mar-22	13-May-22
P03-E	HVAC Calculation Note For Security Building - W046S	55	0%	$20.73	27-Jun-22	20-Aug-22
Data Sheets		64	0%	$20.72	22-Oct-22	24-Dec-22
P03-E	Data Sheets For Main HVAC Equipment - W046S	64	0%	$20.72	22-Oct-22	24-Dec-22
Drawing/Diagram		176	1.9%	$89.12	24-Jul-21 A	21-Oct-22
P03-E	Standard Drawing For HVAC & Plumbing	14	100%	$1.34	24-Jul-21 A	30-Mar-22
P03-E	Symbol & Legend For HVAC & Plumbing	48	60%	$0.59	22-Aug-21	16-May-22
P03-E	HVAC System Layout For Switchgear Building - W046S	62	0%	$21.80	14-May-22	14-Jul-22
P03-E	HVAC System Layout For Security Building - W046S	62	0%	$21.80	21-Aug-22	21-Oct-22
P03-E	Plumbing & Sewage Piping Layout For Switchgear Building - \	64	0%	$21.80	13-May-22	15-Jul-22
P03-E	Plumbing & Sewage Piping Layout For Security Building - W	64	0%	$21.80	27-Jun-22	29-Aug-22
MTO		7	0%	$20.72	22-Oct-22	28-Oct-22
P03-E	MTO For Building HVAC & Plumbing Systems - W046S	7	0%	$20.72	22-Oct-22	28-Oct-22
Piping		445	7.57%	$1,787.50	24-Jul-21 A	15-Dec-22
Basis/Criteria		39	100%	$3.04	24-Jul-21 A	20-Mar-22
P03-E	Piping Design Criteria	39	100%	$3.04	24-Jul-21 A	20-Mar-22
Specification		441	62.12%	$59.70	24-Jul-21 A	06-Jul-22
P03-E	Piping Material Specification	64	60%	$50.08	28-Nov-21	06-Jul-22
P03-E	Specification For Color Coding and Marking	39	60%	$0.55	09-Aug-21	01-May-22
P03-E	Specification For Transportation, Handling, Storage of pipes	39	80%	$0.60	12-Dec-21	01-May-22

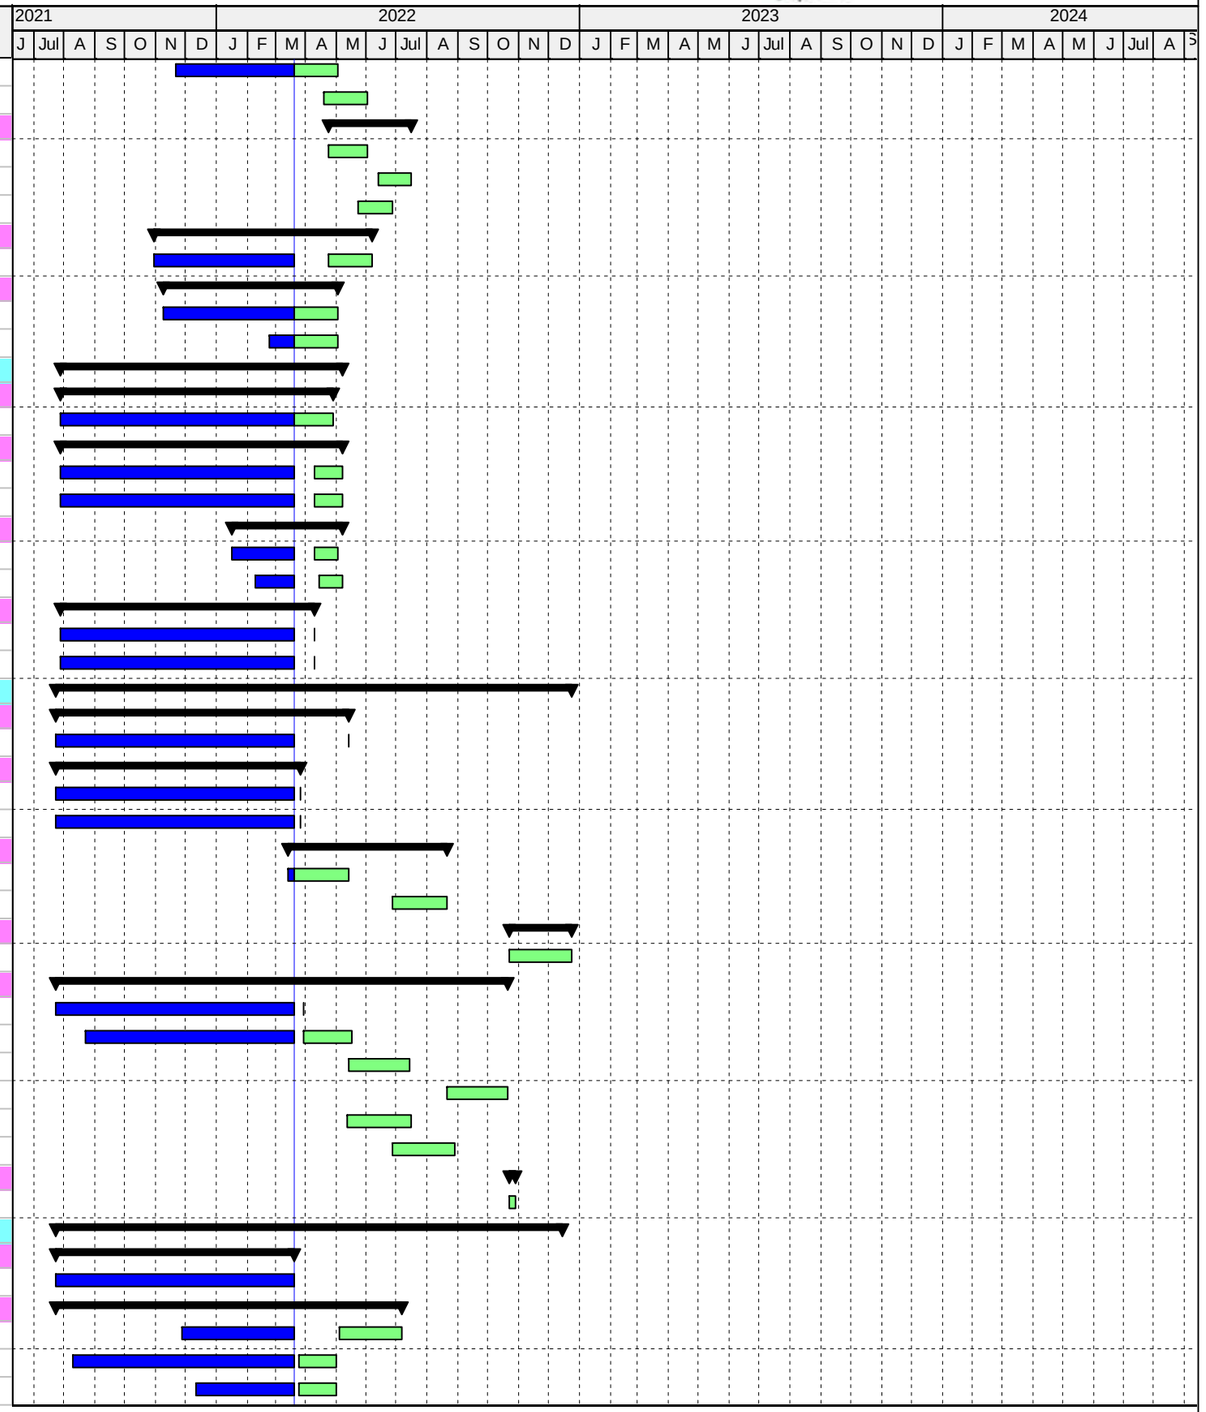


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	Specification For the Design of Piping in Mechanical Packages	39	60%	$0.83	09-Aug-21	01-May-22
P03-E	Specification For Metallic Pipes	39	80%	$0.55	24-Jul-21 A	01-May-22
P03-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$0.55	24-Jul-21 A	24-Mar-22
P03-E	Specification For Painting	39	100%	$0.55	24-Jul-21 A	27-Mar-22
P03-E	Specification For Material Requirements in Sour service	39	60%	$0.55	09-Aug-21	04-May-22
P03-E	Specification For Manual Valves	39	60%	$0.55	09-Aug-21	04-May-22
P03-E	Specification For Plant Piping Systems Pressure Testing	39	60%	$0.55	09-Aug-21	04-May-22
P03-E	Specification For Welding of Plant Piping System	39	60%	$0.55	09-Aug-21	04-May-22
P03-E	Specification For Flexibility Analysis	39	60%	$0.63	09-Aug-21	04-May-22
P03-E	Specification For Coating Of Underground Piping	39	100%	$0.94	24-Jul-21 A	30-Mar-22
P03-E	Specification For Pipe Support	39	60%	$0.73	09-Aug-21	07-May-22
P03-E	Specification For Piping Construction, Fabrication & Erection	39	60%	$0.94	09-Aug-21	07-May-22
P03-E	Specification For Piping Cleaning and Flushing	39	100%	$0.55	24-Aug-21	30-Mar-22
Procedure/Plan		74	100%	$3.04	24-Jul-21 A	15-Jul-22
P03-E	3D-Model (PDMS) Review Procedure	39	100%	$3.04	24-Jul-21 A	03-Apr-22
P03-E	Piping Hydrostatic Test Diagram - Sub Surface	44	0%	$0.00	02-Jun-22	15-Jul-22
Data Sheets		39	60%	$4.47	27-Dec-21	12-May-22
P03-E	Data Sheets For Stone Trap	39	60%	$4.47	27-Dec-21	12-May-22
Drawing/Diagram		241	14.11%	$343.38	08-Nov-21	15-Dec-22
P03-E	Standard Pipe Support Drawings	14	100%	$11.30	19-Feb-22	20-Mar-22
P03-E	Piping Assembly Drawing	20	0%	$38.12	13-May-22	01-Jun-22
P03-E	Piping Hydrostatic Test Diagram - Sub Surface	15	0%	$6.11	02-Jun-22	16-Jun-22
P03-E	Plot Plan Drawing - W046S	20	0%	$112.97	24-Apr-22	13-May-22
P03-E	Piping Plan - W046S	20	0%	$67.78	06-Nov-22	25-Nov-22
P03-E	Isometric Drawings - W046S	20	0%	$45.19	26-Nov-22	15-Dec-22
P03-E	Material Flow Diagram - W046S	39	60%	$61.91	08-Nov-21	27-Apr-22
List		196	0%	$59.70	24-Apr-22	05-Nov-22
P03-E	Piping Support List - W046S	44	0%	$29.85	23-Sep-22	05-Nov-22
P03-E	Critical Line List - W046S	39	0%	$29.85	24-Apr-22	01-Jun-22
Report		132	3.92%	$1,045.33	28-Nov-21	22-Sep-22
P03-E	PDMS Model Review Report (30%) - W046S	44	0%	$279.63	14-May-22	26-Jun-22
P03-E	PDMS Model Review Report (60%) - W046S	44	0%	$417.71	27-Jun-22	09-Aug-22
P03-E	PDMS Model Review Report (90%) - W046S	44	0%	$279.63	10-Aug-22	22-Sep-22
P03-E	Piping Corrosion Study & Material Selection Report	44	60%	$68.36	28-Nov-21	16-May-22
MTO		7	0%	$268.84	23-Sep-22	29-Sep-22
P03-E	MTO For Pipes - W046S	7	0%	$44.79	23-Sep-22	29-Sep-22
P03-E	MTO For Fittings - W046S	7	0%	$44.79	23-Sep-22	29-Sep-22
P03-E	MTO For Flanges - W046S	7	0%	$44.82	23-Sep-22	29-Sep-22
P03-E	MTO For Manual Valves - W046S	7	0%	$44.82	23-Sep-22	29-Sep-22
P03-E	MTO For Gaskets - W046S	7	0%	$44.82	23-Sep-22	29-Sep-22
P03-E	MTO For Bolt & Nuts - W046S	7	0%	$44.82	23-Sep-22	29-Sep-22
Pipeline & Flow line		182	38.67%	$268.13	24-Jul-21 A	18-Jun-22
Basis/Criteria		39	100%	$1.88	28-Aug-21	20-Mar-22
P03-E	Pipeline Design Criteria	39	100%	$1.88	28-Aug-21	20-Mar-22
Specification		49	81.84%	$26.14	24-Jul-21 A	07-May-22
P03-E	Specification For Line Pipes	39	100%	$0.51	24-Jul-21 A	24-Mar-22
P03-E	Specification For Pipeline Cold Bending	39	80%	$0.45	28-Aug-21	01-May-22
P03-E	Specification For Barred Tee	39	80%	$0.45	28-Aug-21	01-May-22
P03-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$0.45	24-Jul-21 A	24-Mar-22

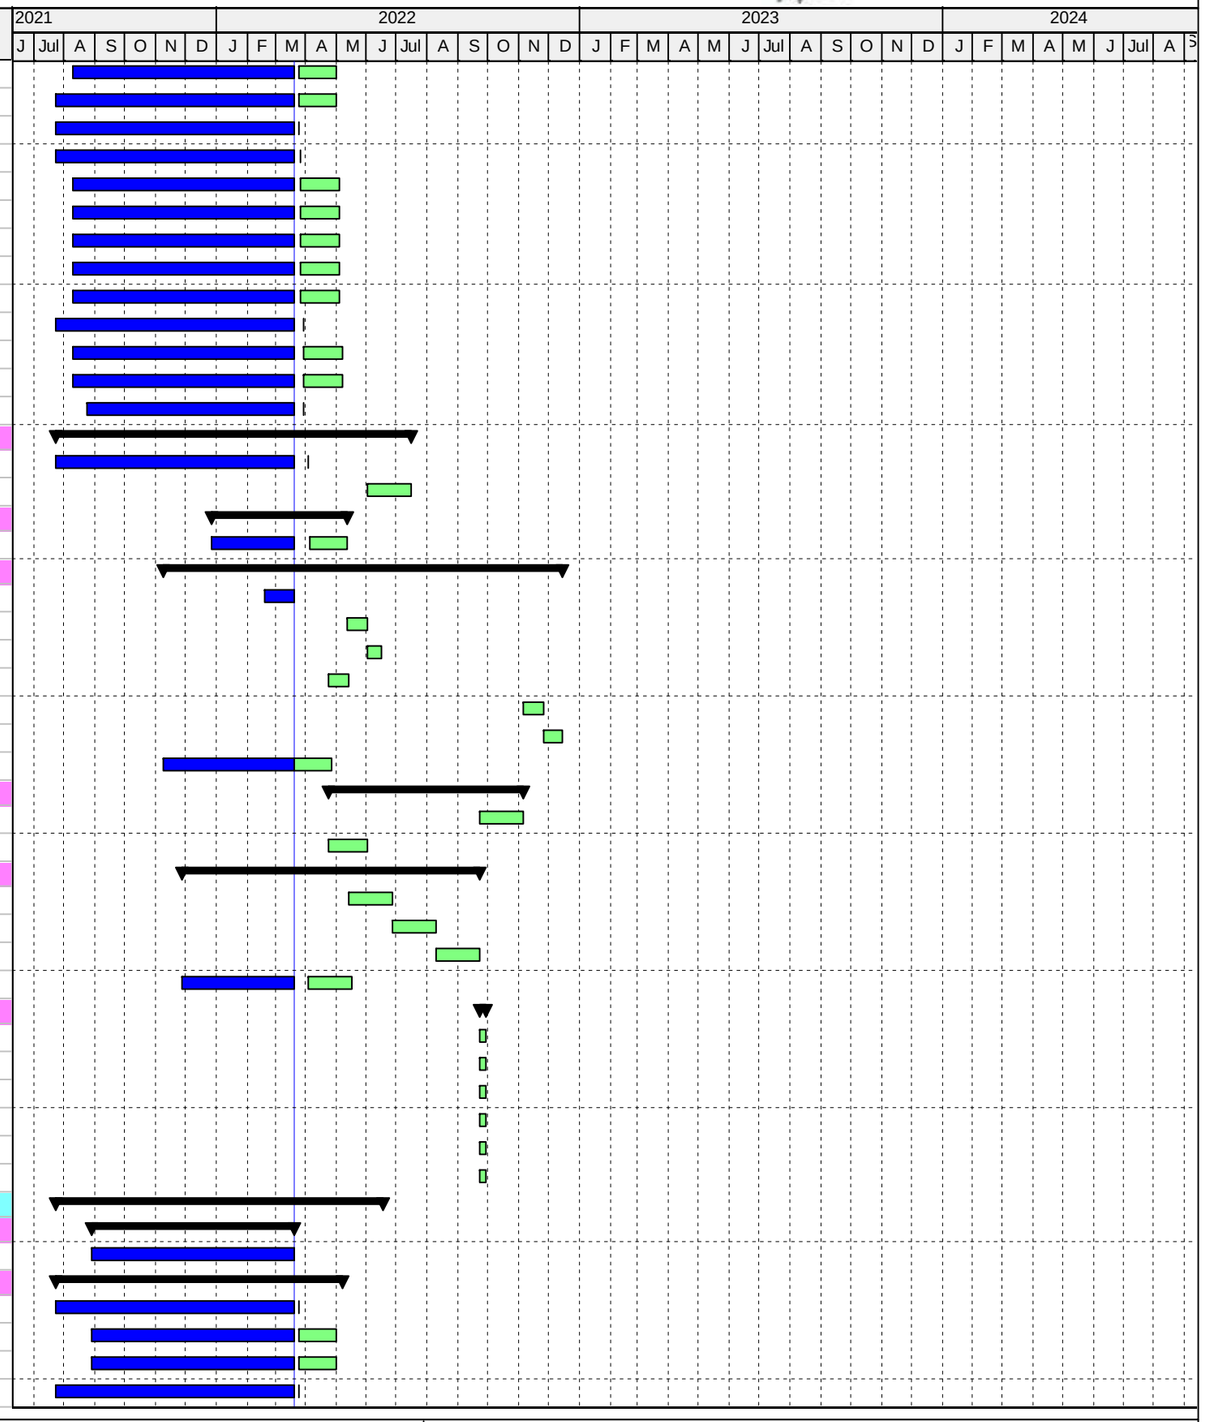


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	Specification For Pipeline Valves	39	80%	$0.45	28-Aug-21	01-May-22
P03-E	Specification For Pipeline Coating	39	100%	$0.45	24-Jul-21 A	24-Mar-22
P03-E	Specification For Pipeline Flushing, Cleaning And Hydrostatic	39	100%	$0.51	24-Jul-21 A	27-Mar-22
P03-E	Specification For Welding of Transportation Pipeline	39	80%	$0.45	12-Dec-21	04-May-22
P03-E	Specification For Pipeline Stress Analysis	39	80%	$0.45	24-Jul-21 A	04-May-22
P03-E	Specification For Pipeline Insulation Joint	39	100%	$0.45	24-Jul-21 A	27-Mar-22
P03-E	Specification For Pipeline Construction	39	80%	$0.45	25-Jan-22	04-May-22
P03-E	Specification For Anchor Flanges	39	80%	$0.51	28-Aug-21	07-May-22
P03-E	Specification For Pigs	39	80%	$0.45	28-Aug-21	07-May-22
P03-E	Pipeline Material Specification	44	80%	$20.06	27-Oct-21	02-May-22
Drawing/Diagram		90	21.7%	$148.59	27-Jul-21 A	18-May-22
P03-E	Pipeline Standard Support Drawings	14	100%	$4.96	27-Jul-21 A	20-Mar-22
P03-E	Pipeline Standard Drawing For Line Marker Post and Cathodi	60	80%	$3.64	18-Sep-21	18-May-22
P03-E	Standard Drawing For Above Ground Pipeline Construction F	44	80%	$3.60	27-Nov-21	12-May-22
P03-E	Standard Drawing For Under Ground Pipeline Construction F	44	100%	$3.60	04-Dec-21	30-Mar-22
P03-E	Pipeline Standard Drawing For Anchor Support	44	60%	$3.60	22-Dec-21	12-May-22
P03-E	Standard Drawing For A/G Pipeline Road Crossing	44	60%	$3.60	05-Dec-21	12-May-22
P03-E	Standard Drawing For Existing Pipeline Crossing	44	60%	$3.60	18-Dec-21	12-May-22
P03-E	Pipeline Standard Drawing For Irish Crossing	44	60%	$4.09	04-Dec-21	12-May-22
P03-E	Pipeline Standard Drawing For Water - Way Crossing	44	60%	$4.09	22-Nov-21	12-May-22
P03-E	Pipeline Standard Drawing For Pig Signaller Concrete Pit	44	60%	$4.09	27-Nov-21	12-May-22
P03-E	Pipeline Standard Drawing For H-Pipe Support	44	100%	$4.09	27-Nov-21	30-Mar-22
P03-E	Flowline Transversal Drawings - W046S	44	0%	$96.53	20-Mar-22	02-May-22
P03-E	Pipeline Hydrostatic Test Diagram - Sub Surface	44	0%	$9.14	20-Mar-22	02-May-22
Procedure/Plan		44	0%	$5.42	09-Apr-22	22-May-22
P03-E	Pipeline Hydrostatic Test Diagram - Sub Surface	44	0%	$5.42	09-Apr-22	22-May-22
List		44	0%	$29.41	20-Mar-22	02-May-22
P03-E	Road Crossing Location List	44	0%	$29.41	20-Mar-22	02-May-22
Report		44	80%	$42.69	27-Oct-21	22-May-22
P03-E	Pipeline Corrosion Study & Material Selection Report	44	80%	$42.69	27-Oct-21	22-May-22
MTO		7	100%	$14.00	22-Aug-21	18-Jun-22
P03-E	MTO For Line Pipes (Flowlines) - W046S	7	100%	$14.00	22-Aug-21	18-Jun-22
Control & Instrumentation		154	66.66%	$715.00	26-Jul-21 A	22-Sep-22
Basis/Criteria		44	94.53%	$38.47	14-Aug-21	29-Apr-22
P03-E	Fire & Gas Detection Design Criteria	38	100%	$33.22	14-Aug-21	27-Mar-22
P03-E	Instrument & Control System Design Criteria	38	60%	$5.25	03-Jan-22	29-Apr-22
Specification		39	73.33%	$197.98	26-Jul-21 A	30-Apr-22
P03-E	Specification For Instrumentation	39	100%	$65.99	26-Jul-21 A	23-Mar-22
P03-E	Specification For Instrument and Control of Package Unit Sys	39	60%	$132.00	04-Aug-21	30-Apr-22
Data Sheets		42	80%	$49.55	07-Dec-21	24-May-22
P03-E	Data Sheets For Pressure Gauge - Wellheads	42	80%	$24.77	07-Dec-21	24-May-22
P03-E	Data Sheets For Temperature Gauge - Wellheads	42	80%	$24.77	07-Dec-21	24-May-22
Drawing/Diagram		59	14.72%	$203.56	14-Nov-21	22-Sep-22
P03-E	Instrument Hook-up Diagram - Wellheads	42	80%	$37.48	14-Nov-21	12-May-22
P03-E	Instrument Location Layout Drawing - W046S	44	0%	$166.09	10-Aug-22	22-Sep-22
MTO		7	100%	$137.49	18-Dec-21	13-May-22
P03-E	MTO For Instrument Tube and Fitting - W046S	7	100%	$137.49	18-Dec-21	13-May-22
List		7	100%	$87.95	10-Nov-21	13-May-22
P03-E	Instrument Index For New Wells & Manifold Extension	7	100%	$87.95	10-Nov-21	13-May-22

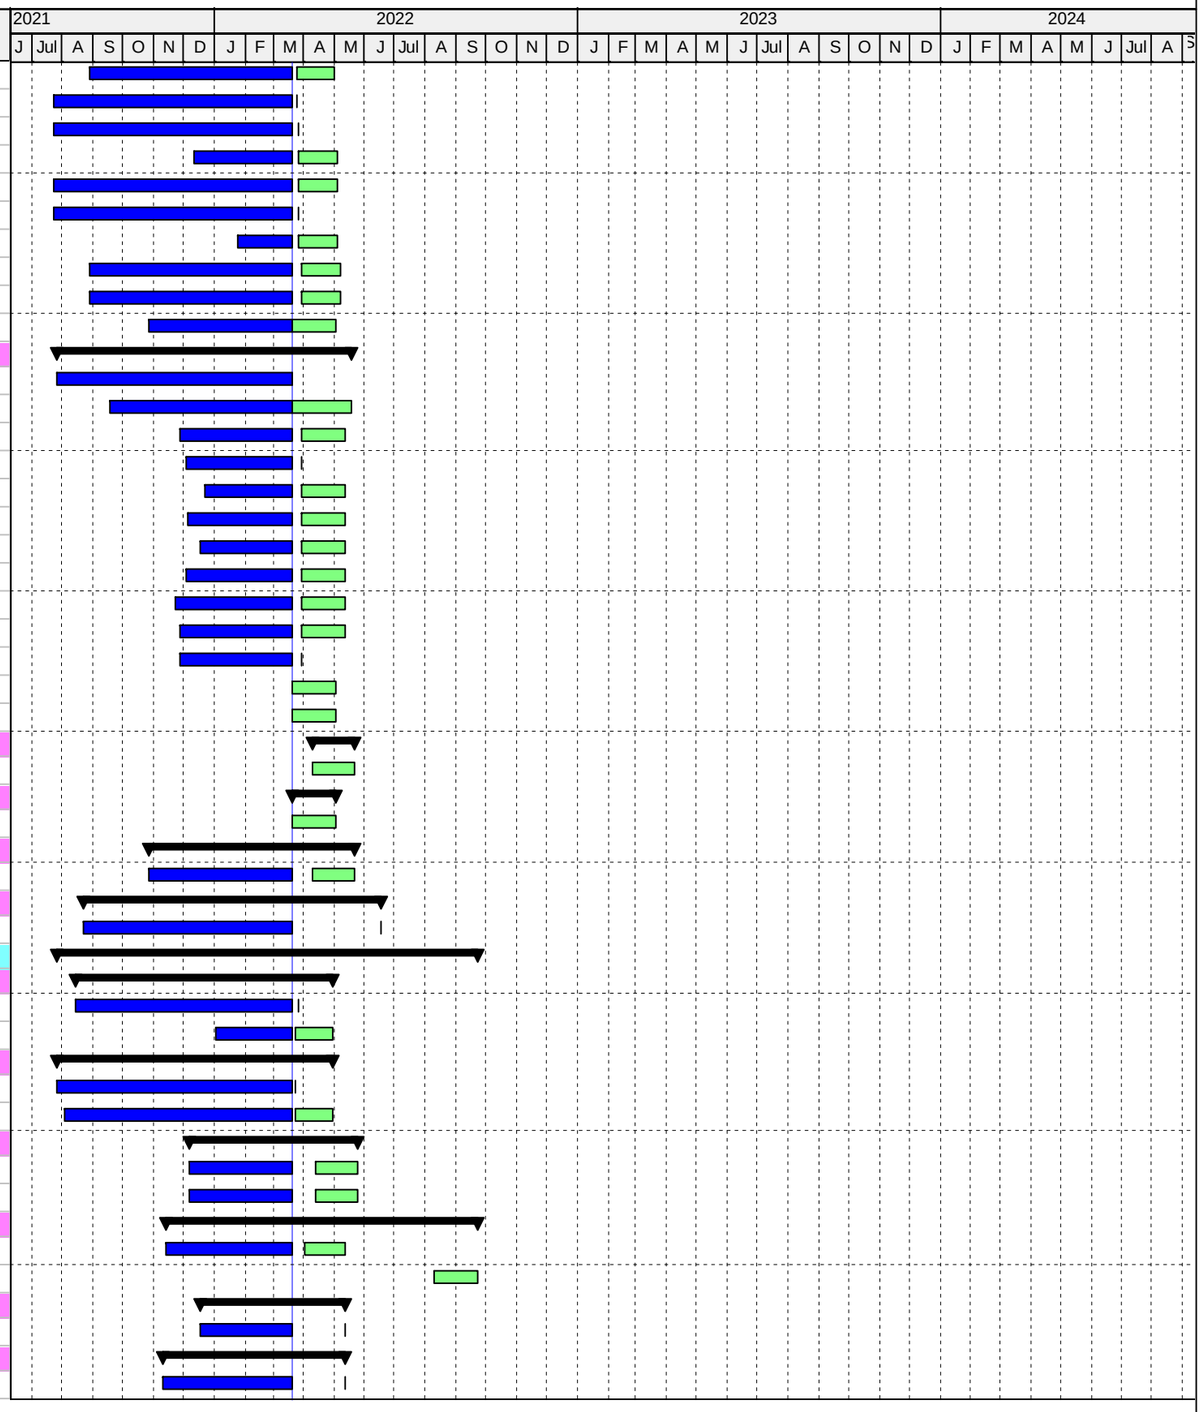


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Safety		131	52.7%	$268.13	24-Jul-21 A	31-Aug-22
Basis/Criteria		44	100%	$26.81	29-Aug-21	19-Apr-22
P03-E	Active Fire Protection and Safety Concept	44	100%	$26.81	29-Aug-21	19-Apr-22
Specification		47	94.69%	$53.63	24-Jul-21 A	06-May-22
P03-E	Specification For Fire Fighting Equipment	44	100%	$7.12	29-Aug-21	24-Mar-22
P03-E	Specification For Hazardous Area Classification	44	100%	$7.12	24-Jul-21 A	24-Mar-22
P03-E	Specification For Environmental Job	44	60%	$7.12	11-Aug-21	06-May-22
P03-E	Specification For Total Flooding System	44	100%	$9.50	24-Jul-21 A	27-Mar-22
P03-E	Specification For Safety Equipment	44	100%	$11.39	29-Aug-21	27-Mar-22
P03-E	Specification For Safety Signs	44	100%	$11.39	24-Jul-21 A	27-Mar-22
Data Sheets		47	100%	$26.81	08-Dec-21	27-Mar-22
P03-E	Data Sheets For Fire Fighting Equipment	44	100%	$8.94	08-Dec-21	24-Mar-22
P03-E	Data Sheets For Safety Equipment	44	100%	$8.94	08-Dec-21	27-Mar-22
P03-E	Data Sheets For Safety Sign	44	100%	$8.94	08-Dec-21	27-Mar-22
Drawing/Diagram		116	14.41%	$107.25	29-Aug-21	26-Aug-22
P03-E	Typical Installation Detail for Safety & Fire Fighting Equipment	14	100%	$7.73	29-Dec-21	27-Mar-22
P03-E	Symbol & Legend For Safety & Firefighting Systems	44	100%	$7.73	29-Aug-21	27-Mar-22
P03-E	Hazardous Area Classification Layout - W046S	44	0%	$30.60	03-May-22	15-Jun-22
P03-E	Safety & Fire Fighting Equipment Location Layout - W046S	44	0%	$30.60	31-May-22	13-Jul-22
P03-E	Escape Route & Safety Sign Layout - W046S	44	0%	$30.59	14-Jul-22	26-Aug-22
List		44	80%	$26.81	09-Nov-21	02-May-22
P03-E	Hazard Source List - W046S	44	80%	$26.81	09-Nov-21	02-May-22
MTO		39	0%	$26.81	24-Jul-22	31-Aug-22
P03-E	MTO For Fire Fighting & Safety Equipment - W046S	7	0%	$13.41	24-Jul-22	30-Jul-22
P03-E	MTO For Safety Sign - W046S	5	0%	$13.41	27-Aug-22	31-Aug-22
Electrical		243	27.51%	$1,072.50	24-Jul-21 A	29-Oct-22
Basis/Criteria		54	100%	$5.58	03-Aug-21	20-Mar-22
P03-E	Electrical System Design Criteria	54	100%	$5.58	03-Aug-21	20-Mar-22
Specification		55	100%	$67.14	24-Jul-21 A	30-Mar-22
P03-E	Specification For LV Switchgear & Motor Control Centers	49	100%	$3.48	24-Jul-21 A	24-Mar-22
P03-E	Specification For MV Switchgear	49	100%	$3.99	24-Jul-21 A	24-Mar-22
P03-E	Specification For UPS System	49	100%	$3.99	04-Aug-21	24-Mar-22
P03-E	Specification For Transformers	49	100%	$3.99	24-Jul-21 A	24-Mar-22
P03-E	Specification For DC Charger	49	100%	$3.99	04-Aug-21	24-Mar-22
P03-E	Specification For Earthing & Lightning System	49	100%	$2.54	28-Jul-21 A	24-Mar-22
P03-E	Specification For Lighting & Small Power System	49	100%	$3.48	28-Jul-21 A	27-Mar-22
P03-E	Specification For Bulk Materials	49	100%	$3.48	24-Jul-21 A	27-Mar-22
P03-E	Specification For Diesel Generator	49	100%	$3.99	28-Jul-21 A	27-Mar-22
P03-E	Specification For LV Induction Motors	49	100%	$3.65	24-Jul-21 A	27-Mar-22
P03-E	Specification For Electrical Requirements of Packaged Units	49	100%	$3.99	28-Jul-21 A	27-Mar-22
P03-E	Specification For Capacitor Bank	49	100%	$3.99	24-Jul-21 A	27-Mar-22
P03-E	Specification For Distribution & Lighting Panels	49	100%	$3.99	28-Jul-21 A	30-Mar-22
P03-E	Specification For Power & Control Cables	49	100%	$3.48	24-Jul-21 A	30-Mar-22
P03-E	Specification For Cathodic Protection System	49	100%	$3.48	31-Jul-21 A	30-Mar-22
P03-E	Specification For MV Induction Motors	49	100%	$3.65	24-Jul-21 A	30-Mar-22
P03-E	Specification For NGR	49	100%	$3.99	24-Jul-21 A	30-Mar-22
P03-E	Specification For Overhead Transmission Lines	49	100%	$3.99	28-Jul-21 A	30-Mar-22
Calculation		189	40.67%	$128.70	11-Oct-21 A	12-Jun-22
P03-E	Calculation Note For Lighting System of Well Pads Switchgea	40	0%	$9.50	27-Apr-22	05-Jun-22

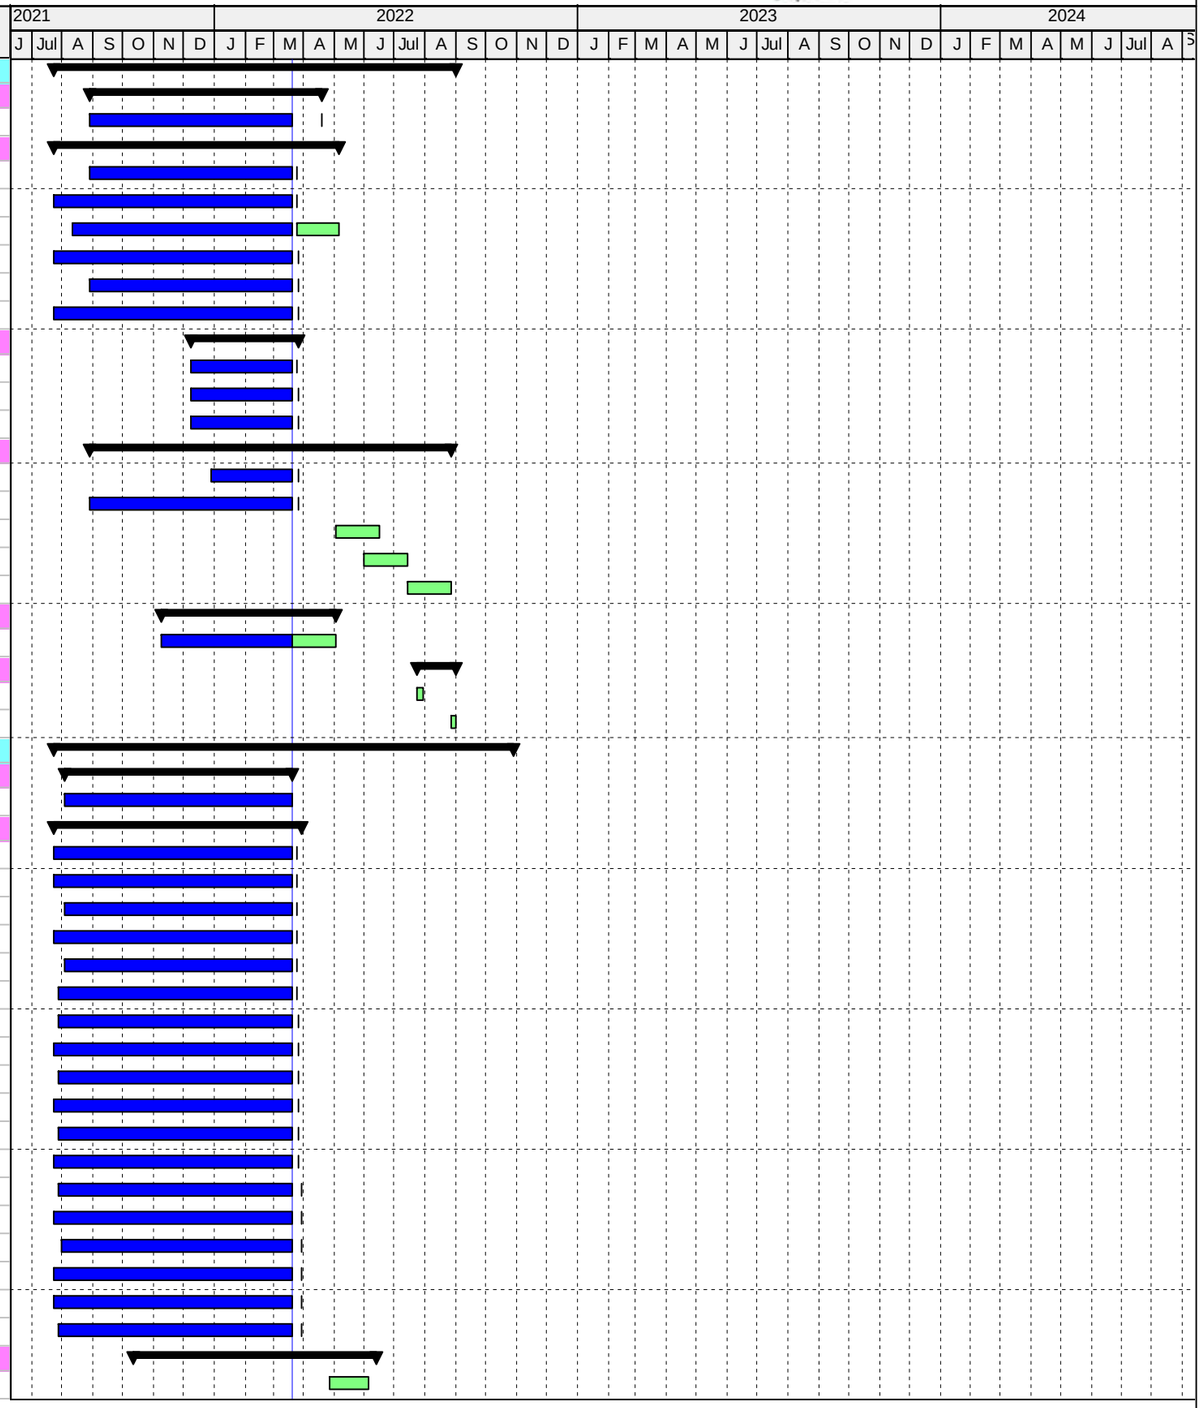


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	Calculation Note For Lighting System of Well Pads Security B	40	0%	$9.50	27-Apr-22	05-Jun-22
P03-E	Calculation Note For Lighting System of Well Pads Area	40	0%	$12.68	27-Apr-22	05-Jun-22
P03-E	Calculation Note For Cable Sizing of Well Pads	40	80%	$12.68	02-Nov-21	08-May-22
P03-E	Calculation Note For UPS System of Well Pads	40	0%	$12.68	04-May-22	12-Jun-22
P03-E	Calculation Note For Earthing & Lightning System of Well Pac	40	0%	$12.68	19-Apr-22	28-May-22
P03-E	Calculation Note For Diesel Generator Sizing of Well Pads	40	60%	$9.50	26-Jan-22	03-May-22
P03-E	Calculation Note For DC Charger of Well Pads	40	80%	$12.68	26-Jan-22	03-May-22
P03-E	Calculation Note For LV Capacitor Bank of Well Pads	30	60%	$15.43	29-Jan-22	03-May-22
P03-E	Calculation Note For 11 KV Over Head Line Sag and Tension	30	80%	$10.69	13-Oct-21	03-May-22
P03-E	Calculation Note For 33 KV Over Head Line Sag and Tension	30	80%	$10.69	11-Oct-21 A	03-May-22
Data Sheets		233	67.98%	$93.31	12-Sep-21	10-Aug-22
P03-E	Data Sheets For UPS of Well Pads	59	0%	$8.01	13-Jun-22	10-Aug-22
P03-E	Data Sheets For DC Charger of Well Pads	59	80%	$8.01	29-Jan-22	22-May-22
P03-E	Data Sheets For Diesel Generator of Well Pads	59	60%	$8.01	20-Sep-21	22-May-22
P03-E	Data Sheets For LV Capacitor Bank of Well Pads	59	80%	$8.01	12-Sep-21	17-May-22
P03-E	Data Sheets For LV Switchgear of Well Pads	54	60%	$8.01	19-Feb-22	12-May-22
P03-E	Data Sheets For Power & Control Cables of Well Pads	59	80%	$8.01	13-Sep-21	27-May-22
P03-E	Data Sheets For Power Transformers of Well Pads	59	80%	$8.01	15-Sep-21	17-May-22
P03-E	Data Sheets For Distribution & Lighting Panels of Well Pads	59	60%	$8.01	12-Sep-21	31-Jul-22
P03-E	Data Sheets For 11 KV Over Head Line Equipment	35	80%	$14.63	10-Nov-21	31-Jul-22
P03-E	Data Sheets For 33 KV Over Head Line Equipment	35	80%	$14.63	10-Nov-21	07-Jul-22
Drawing/Diagram		182	36.26%	$264.69	09-Aug-21	17-Oct-22
P03-E	Electrical Legend and Symbols	25	100%	$4.08	09-Aug-21	30-Mar-22
P03-E	Typical Installation Details & Notes For Earthing and Lightning	14	100%	$8.23	25-Aug-21	30-Mar-22
P03-E	Typical Installation Details & Notes For Lighting System	14	100%	$7.31	25-Aug-21	30-Mar-22
P03-E	Typical Installation Details & Notes For Power System	14	100%	$2.44	25-Aug-21	30-Mar-22
P03-E	Installation Details & Notes For Cathodic Protection Systems	30	100%	$2.46	25-Aug-21	30-Mar-22
P03-E	Typical Installation Details For Over Head Line Equipment	14	100%	$5.48	22-Aug-21	19-Apr-22
P03-E	Installation Detail & Notes for Connection OHL to Gantries for	25	60%	$22.26	06-Mar-22	13-Apr-22
P03-E	Electrical Typical Schematic Diagrams For LV Panels of Well F	14	100%	$13.71	30-Aug-21	20-Mar-22
P03-E	Control Logic Diagram For LV Incomers of Well Pads	30	80%	$10.96	30-Aug-21	18-Apr-22
P03-E	Earthing Layout For Electrical Tower (Gantry) of Well Pads	30	0%	$8.23	16-Jul-22	14-Aug-22
P03-E	Cable Route Layout For Electrical Tower (Gantry) of Well Pac	30	0%	$10.96	16-Jul-22	14-Aug-22
P03-E	Overall Single Line Diagram of Well Pads	30	60%	$13.71	02-Mar-22	03-May-22
P03-E	Single Line Diagram For LV Switchgear of Well Pads	30	60%	$10.96	08-Feb-22	03-May-22
P03-E	Single Line Diagram For LV Power Distribution Panel of Well	30	0%	$10.96	04-May-22	02-Jun-22
P03-E	Single Line Diagram For DC Charger of Well Pads	30	80%	$10.96	06-Feb-22	03-May-22
P03-E	Single Line Diagram For Capacitor Banks of Well Pads	30	60%	$10.96	02-Feb-22	03-May-22
P03-E	Interconnection Wiring Diagram of Well Pads	30	0%	$16.44	04-May-22	02-Jun-22
P03-E	Area Lighting & Small Power Layout of Well Pads of Well Pad	30	0%	$10.96	16-Jul-22	14-Aug-22
P03-E	Lighting & Small Power Layout For Switchgear Building of We	25	0%	$10.88	13-May-22	06-Jun-22
P03-E	Lighting & Small Power Layout For Security Building of Well P	25	0%	$10.88	23-Sep-22	17-Oct-22
P03-E	Area Electrical Cable Route & Section Layout of Well Pads	25	0%	$13.71	16-Jul-22	09-Aug-22
P03-E	Electrical Cable Route & Section Layout For Switchgear Buildi	25	0%	$22.26	16-Jul-22	09-Aug-22
P03-E	Electrical Equipment Arrangement Layout For Switchgear Buil	25	0%	$16.36	13-May-22	06-Jun-22
P03-E	Earthing & Lightning Layout for well pads	25	0%	$9.56	29-May-22	22-Jun-22
List		113	37.66%	$27.99	25-Jan-22	22-Oct-22
P03-E	Electrical Load List of Well Pads	45	80%	$13.18	25-Jan-22	03-May-22

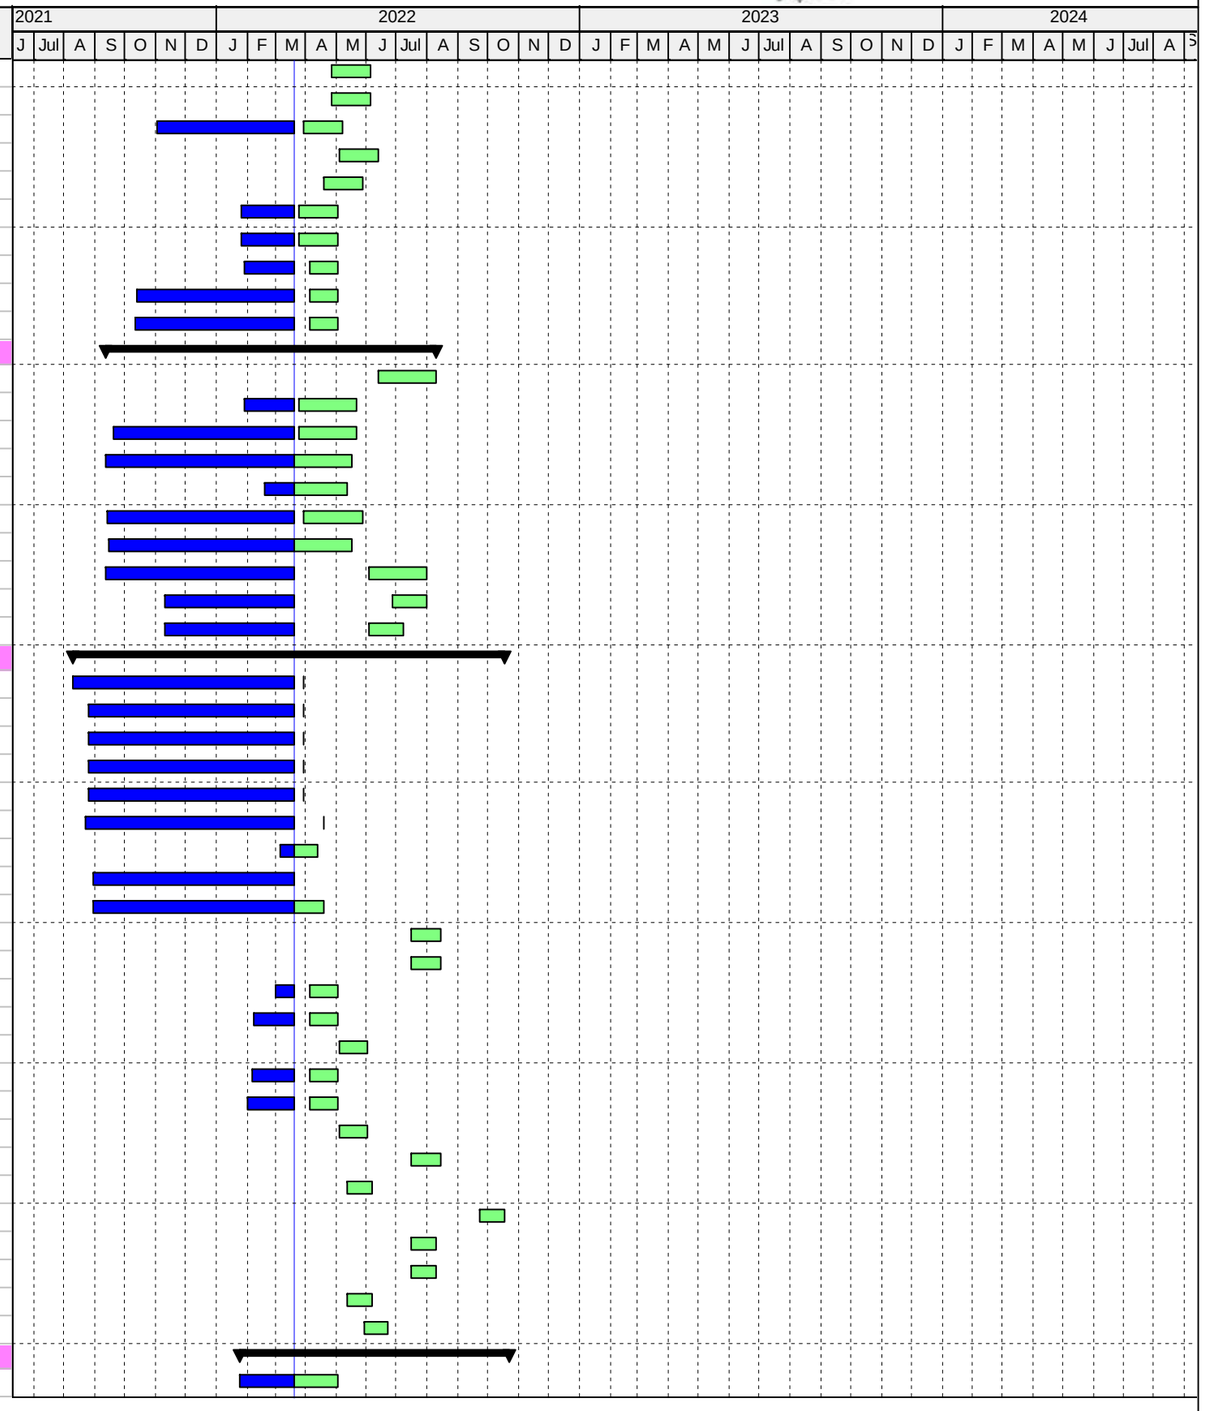


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	Electrical Power & Control Cable List of Well Pads	74	0%	$7.40	10-Aug-22	22-Oct-22
P03-E	Cable Drum Schedule and Cutting List of Well Pads	74	0%	$7.40	10-Aug-22	22-Oct-22
Report		133	0%	$186.62	04-May-22	13-Sep-22
P03-E	Electrical Network (Load Flow, Motor Starting & Short Circuit)	54	0%	$53.41	04-May-22	26-Jun-22
P03-E	Relay Coordination & Setting Study Report of Well Pads	54	0%	$53.41	27-Jun-22	19-Aug-22
P03-E	11KV Over Head Line Study Report	44	0%	$39.90	01-Aug-22	13-Sep-22
P03-E	33KV Over Head Line Study Report	44	0%	$39.90	08-Jul-22	20-Aug-22
MTO		194	0%	$298.48	19-Apr-22	29-Oct-22
P03-E	MTO For Transmission Over Head Line - W046S	7	0%	$55.96	19-Apr-22	25-Apr-22
P03-E	MTO For Earthing & Lightning Systems - W046S	7	0%	$55.96	23-Jun-22	29-Jun-22
P03-E	MTO For Lighting & Small Powers - W046S	7	0%	$37.31	18-Oct-22	24-Oct-22
P03-E	MTO For Power & Control Cables - W046S	7	0%	$37.31	23-Oct-22	29-Oct-22
P03-E	MTO For Tray/Ladder and Accessories - W046S	7	0%	$37.31	07-Jun-22	13-Jun-22
P03-E	MTO For Electrical Bulk Items - W046S	7	0%	$74.62	19-May-22	25-May-22
Architecture		277	16.71%	$268.13	18-Dec-21	12-Jul-22
Basis/Criteria		74	60%	$54.16	08-Feb-22	01-Jun-22
P03-E	Architectural Design Criteria	74	60%	$54.16	08-Feb-22	01-Jun-22
Specification		44	0%	$67.70	20-Mar-22	02-May-22
P03-E	Buildings General Specification	44	0%	$67.70	20-Mar-22	02-May-22
Drawing/Diagram		247	18.94%	$65.02	18-Dec-21	05-Jul-22
P03-E	Architectural Drawing For Diesel Generator Shelter of Well P	44	0%	$14.83	23-May-22	05-Jul-22
P03-E	Architectural Drawing For WHCP/HPU Shelter of Well Pads -	44	0%	$14.83	19-Apr-22	01-Jun-22
P03-E	Architectural Drawing For Switchgear Building of Well Pads -	44	60%	$14.83	18-May-22	12-May-22
P03-E	Architectural Drawing For Security Building of Well Pads - WC	44	0%	$14.83	14-May-22	26-Jun-22
P03-E	Standard Drawing for Architectural Details	44	60%	$5.70	18-Dec-21	02-May-22
MTO		7	0%	$81.24	06-Jul-22	12-Jul-22
P03-E	MTO For Architectural Works - W0046S	7	0%	$81.24	06-Jul-22	12-Jul-22
Civil		449	41.46%	$893.75	01-Aug-21	25-Dec-22
Basis/Criteria		90	20%	$3.31	13-Feb-22	22-May-22
P03-E	Civil Design Criteria	64	60%	$1.10	13-Feb-22	22-May-22
P03-E	Design Criteria for Sewerage & Drainage	44	0%	$1.10	24-Mar-22	06-May-22
P03-E	Design Criteria for Road and Paving	44	0%	$1.10	27-Mar-22	09-May-22
Specification		94	72%	$16.71	09-Aug-21	06-Jun-22
P03-E	Specification For Civil Works	79	0%	$1.67	20-Mar-22	06-Jun-22
P03-E	Specification For Road & Paving	64	80%	$3.34	09-Aug-21	22-May-22
P03-E	Specification For Fence & Gate	64	100%	$3.34	18-Sep-21	20-Mar-22
P03-E	Specification For Earth Work	64	80%	$3.34	09-Aug-21	22-May-22
P03-E	Specification For Sewerage & Drainage	64	100%	$3.34	09-Aug-21	20-Mar-22
P03-E	Specification For Geological & Geotechnical Survey	44	0%	$1.67	20-Mar-22	02-May-22
Drawing/Diagram		279	45.68%	$713.21	01-Aug-21	23-Jun-22
P03-E	Standard Drawing For Civil Works	64	0%	$14.26	30-Mar-22	01-Jun-22
P03-E	Standard Drawing For Slope Protection Details	64	100%	$14.26	22-Aug-21	30-Mar-22
P03-E	Standard Drawing For Roads	64	80%	$14.26	22-Aug-21	01-Jun-22
P03-E	Standard Drawing For Electrical Cable Trench	64	100%	$14.26	22-Aug-21	30-Mar-22
P03-E	Standard Drawing For Manholes	64	80%	$14.26	22-Aug-21	01-Jun-22
P03-E	Standard Drawing For Catch Basins	64	80%	$14.26	22-Aug-21	05-Jun-22
P03-E	Standard Drawing For Sewerage & Drainage Details	64	60%	$14.26	02-Feb-22	05-Jun-22
P03-E	Standard Drawing For Civil Underground Crossings	38	60%	$24.32	07-Feb-22	10-May-22
P03-E	Standard Drawing For Fence & Gate Details	64	100%	$14.26	18-Sep-21	03-Apr-22

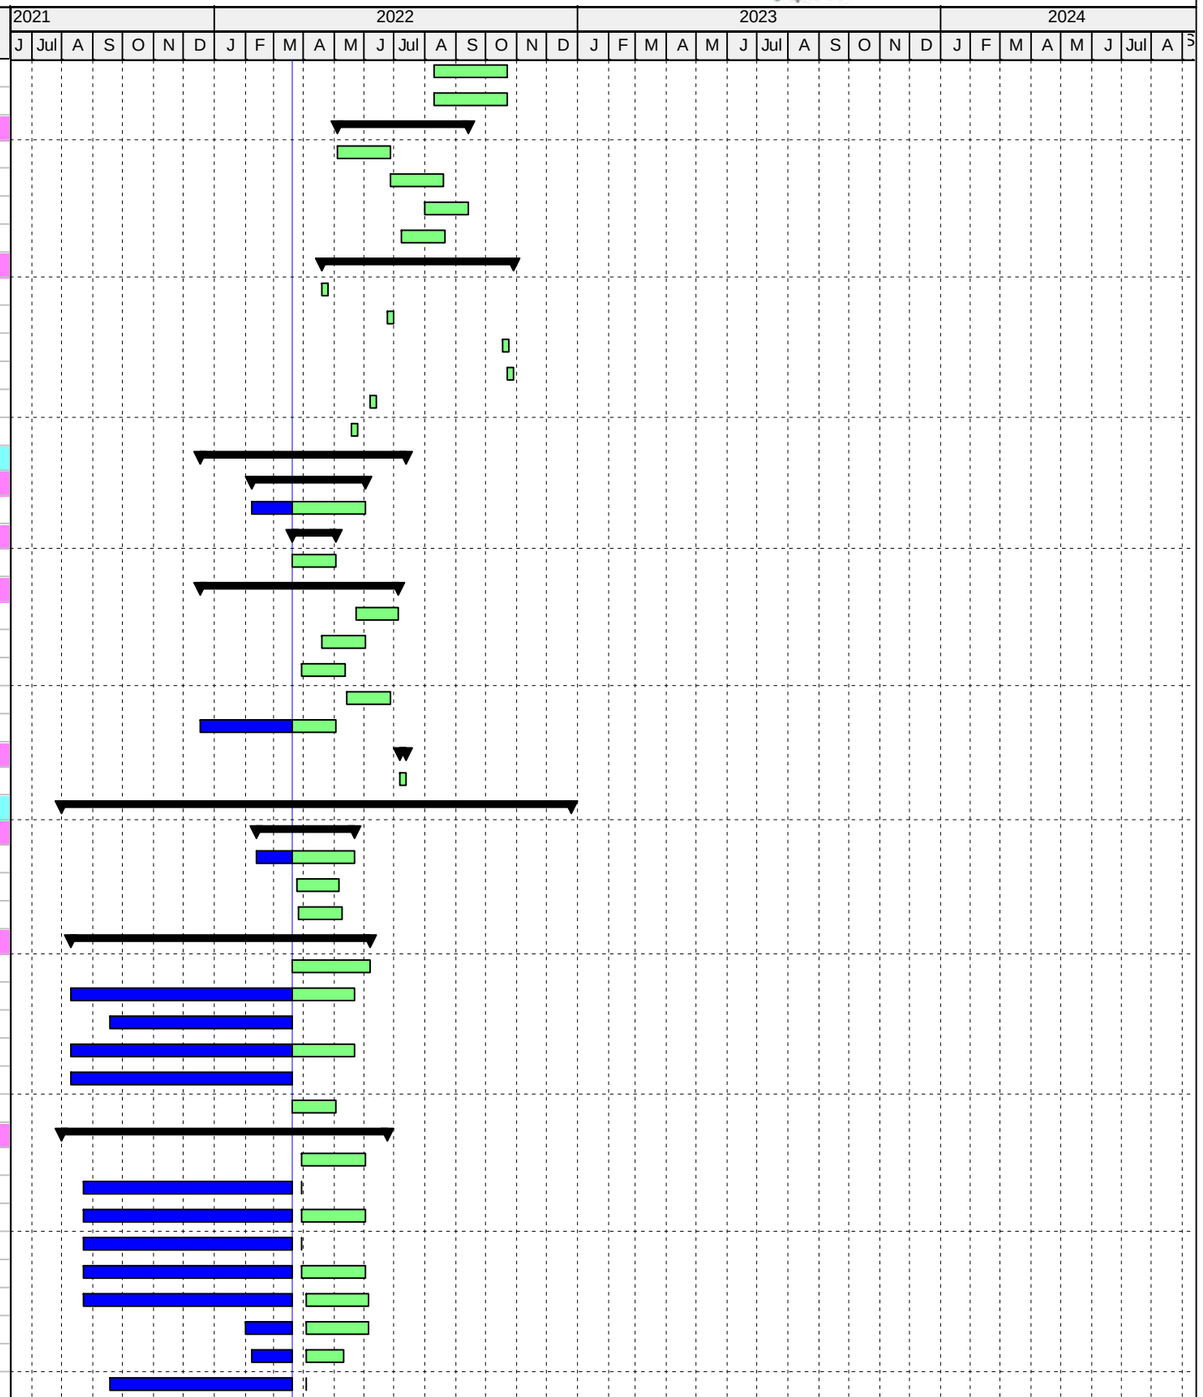


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	Standard Drawing For Concrete Continues Weight	38	100%	$23.75	01-Aug-21	20-Mar-22
P03-E	Standard Drawing For Major Floodway Crossing	38	0%	$23.75	03-Apr-22	10-May-22
P03-E	Standard Drawing For Culvert & Details	38	100%	$23.75	25-Sep-21	03-Apr-22
P03-E	Standard Drawing For Valve Box	38	100%	$23.75	12-Jan-22	03-Apr-22
P03-E	Standard Drawing For Fire Hydrant Pit	38	60%	$23.75	13-Mar-22	10-May-22
P03-E	Standard Drawing For Cable Pull Pit	30	0%	$14.26	03-Apr-22	02-May-22
P03-E	Standard Drawing For Pavings	38	60%	$23.75	08-Jan-22	10-May-22
P03-E	Standard Drawing For Earth Pit	38	60%	$23.75	13-Feb-22	10-May-22
P03-E	Standard Detail For Pipe Bedding	64	100%	$14.26	22-Aug-21	03-Apr-22
P03-E	Standard Details of Miscellaneous Items	64	60%	$14.26	06-Mar-22	05-Jun-22
P03-E	BINAK Oil Field Project Overall Well Location/Facilities Layou	30	0%	$10.84	20-Mar-22	18-Apr-22
P03-E	General Civil Layout -W046S	30	0%	$133.09	04-May-22	02-Jun-22
P03-E	Civil and Structural drawings -W046S	30	0%	$133.09	24-May-22	22-Jun-22
P03-E	Rough Grading Plans -W046S	20	100%	$88.72	12-Dec-21	23-Jun-22
Calculation		434	40%	$80.26	05-Dec-21	25-Dec-22
P03-E	Calculation Note For Heli Pad, Well Pad & Diesel Storage Pa	38	0%	$40.13	04-Apr-22	11-May-22
P03-E	Calculation Note For Flood Control	39	80%	$40.13	05-Dec-21	25-Dec-22
MTO		7	0%	$80.26	23-Jun-22	30-Jun-22
P03-E	MTO For Civil Works - W046S	7	0%	$80.26	23-Jun-22	30-Jun-22
Structure		213	12.6%	$893.75	08-Aug-21	18-Oct-22
Basis/Criteria		64	0%	$9.74	20-Mar-22	22-May-22
P03-E	Structural Design Criteria	64	0%	$3.25	20-Mar-22	22-May-22
P03-E	Design Criteria For Steel Structure	44	0%	$3.25	20-Mar-22	02-May-22
P03-E	Design Criteria For Load & Forces	44	0%	$3.25	20-Mar-22	02-May-22
Specification		98	84.92%	$74.45	14-Aug-21	26-May-22
P03-E	Specification For Concrete Work	64	80%	$7.21	14-Aug-21	26-May-22
P03-E	Specification For Storage Tank Foundation	38	100%	$18.02	23-Nov-21	24-Mar-22
P03-E	Specification for Fabrication of Steel Structures	64	100%	$9.31	24-Jan-22	24-Mar-22
P03-E	Specification For Grouting	64	100%	$7.21	14-Aug-21	24-Mar-22
P03-E	Specification for Erection of Steel Structures	64	100%	$9.37	24-Jan-22	24-Mar-22
P03-E	Specification for Fireproofing	64	100%	$9.21	18-Sep-21	24-Mar-22
P03-E	Specification for Design of Blast Resistant Buildings	64	60%	$7.21	12-Dec-21	26-May-22
P03-E	Specification For Steel Structural Works	37	0%	$6.91	20-Mar-22	25-Apr-22
Drawing/Diagram		203	8.58%	$576.38	08-Aug-21	18-Oct-22
P03-E	Standard Drawing For Fire Proofing	64	100%	$2.94	08-Aug-21	03-Apr-22
P03-E	Standard Drawing For Anchor Bolts	64	100%	$2.94	15-Dec-21	03-Apr-22
P03-E	Standard Drawing For Steel Stairs	64	100%	$2.94	18-Dec-21	03-Apr-22
P03-E	Standard Drawing For Operating Platform	38	100%	$3.46	27-Dec-21	30-Mar-22
P03-E	Standard Drawing For Handrail	38	100%	$4.96	18-Dec-21	30-Mar-22
P03-E	Standard Drawing For Insert Plates in Concrete	38	100%	$4.96	08-Aug-21	30-Mar-22
P03-E	Standard Details For Ladder & Safety Cage	64	100%	$2.94	15-Dec-21	03-Apr-22
P03-E	Standard Drawing For Lighting pole foundation Plan & Details	38	60%	$4.96	29-Jan-22	06-May-22
P03-E	General Notes - Steel Structures	38	100%	$3.46	25-Jan-22	30-Mar-22
P03-E	General Notes - Reinforced Concrete Structures	38	100%	$4.96	20-Dec-21	30-Mar-22
P03-E	Standard Drawing For Structural Built-up Sections	44	80%	$4.96	04-Dec-21	12-May-22
P03-E	Standard Drawing For Steel Flooring, Grating and Chequere	44	100%	$4.96	05-Jan-22	30-Mar-22
P03-E	Concrete Reinforcement Shape Code	44	0%	$4.96	30-Mar-22	12-May-22
P03-E	Standard Drawing For Septic Tank	44	80%	$4.96	22-Jan-22	12-May-22
P03-E	Fuel Oil Storage Drum Detail Drawing For Well Pads - W046S	44	0%	$59.37	05-Sep-22	18-Oct-22

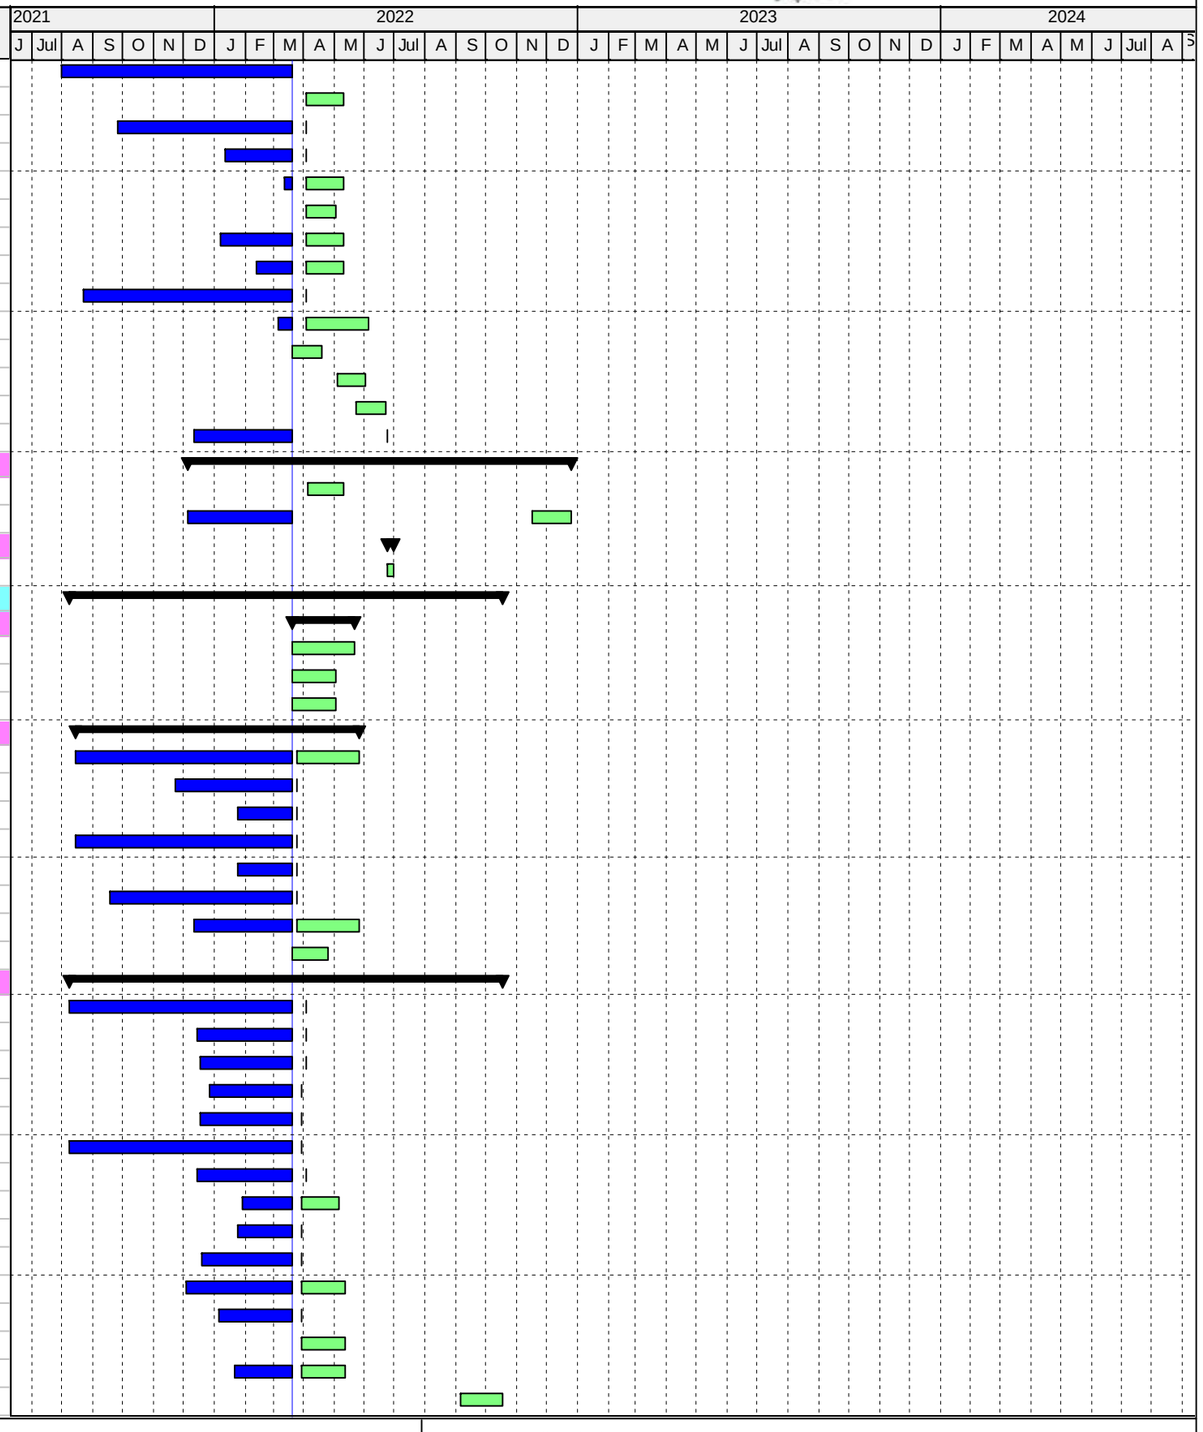


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	Foundation Drawing For Security Building For Well Pads - W	44	0%	$49.91	27-Jun-22	09-Aug-22
P03-E	Structural Drawing For Security Building For Well Pads - W0	44	0%	$49.91	27-Jun-22	09-Aug-22
P03-E	Foundation Drawing For Switchgear Building For Well Pads -	44	0%	$49.91	13-May-22	25-Jun-22
P03-E	Structural Drawing For Switchgear Building For Well Pads - V	44	0%	$49.91	13-May-22	25-Jun-22
P03-E	Foundation Drawing For Potable Water Tank For Well Pads -	44	0%	$49.91	16-Aug-22	28-Sep-22
P03-E	Foundation Drawing For Diesel Generator Shelter For Well F	44	0%	$49.91	06-Jul-22	18-Aug-22
P03-E	Structural Drawing For Diesel Generator Shelter For Well Pa	44	0%	$49.91	06-Jul-22	18-Aug-22
P03-E	Platform Structure Drawing - W046S	44	0%	$59.37	09-Apr-22	22-May-22
P03-E	Foundation Drawing For Transmission Line Tower - W046S	44	0%	$49.91	19-May-22	01-Jul-22
MTO		7	0%	$233.18	10-Aug-22	16-Aug-22
P03-E	MTO For Structural Works - W046S	7	0%	$233.18	10-Aug-22	16-Aug-22
General		194	12.06%	$1,787.50	11-Aug-21	29-Sep-22
Risk Assessment		44	100%	$89.38	05-Sep-21	20-Mar-22
Procedure/Plan		44	100%	$89.38	05-Sep-21	20-Mar-22
P03-	HAZID Study Procedure	44	100%	$89.38	05-Sep-21	20-Mar-22
Survey (Topography) & Geotechnic		194	7.06%	$1,519.38	11-Aug-21	29-Sep-22
Geotechnic		104	8%	$1,340.63	11-Aug-21	02-May-22
Procedure/Plan		44	100%	$107.25	11-Aug-21	19-Apr-22
P03	Geotechnical Investigation Plan for Well Pads	44	100%	$107.25	11-Aug-21	19-Apr-22
Report		44	0%	$1,233.38	20-Mar-22	02-May-22
P03	Geotechnical Investigation Report - W046S	44	0%	$1,233.38	20-Mar-22	02-May-22
Survey		99	0%	$178.75	23-Jun-22	29-Sep-22
Drawing/Diagram		99	0%	$178.75	23-Jun-22	29-Sep-22
P03	Flowline Plan & Profile Drawings - W046S	39	0%	$89.38	22-Aug-22	29-Sep-22
P03	Over Head Line Plan and Profile - W046S	50	0%	$89.38	23-Jun-22	12-Aug-22
QC/QA		116	10.6%	$178.75	20-Sep-21	13-Jul-22
QC Management		116	39.17%	$14.53	08-Dec-21	13-Jul-22
P03-	Project Audit Procedure	44	0%	$0.73	20-Mar-22	02-May-22
P03-	Specification For Final Data Book (FDB) Requirements	44	0%	$0.73	20-Mar-22	02-May-22
P03-	Non Conformance Control Procedure	36	0%	$0.73	03-May-22	07-Jun-22
P03-	Corrective Action Procedure	36	0%	$0.73	08-Jun-22	13-Jul-22
P03-	Material Reciving, Storage, Handling Procedure	39	60%	$0.73	20-Feb-22	27-Apr-22
P03-	Packing, Marking, Transportation Procedure	39	0%	$0.73	20-Mar-22	27-Apr-22
P03-	Criticality Assessment Procedure	39	0%	$2.91	20-Mar-22	27-Apr-22
P03-	Project Quality Plan	44	80%	$6.54	08-Dec-21	02-May-22
P03-	Technical Query Procedure	44	0%	$0.73	30-Mar-22	12-May-22
QC General Document		55	8.58%	$21.22	28-Nov-21	16-May-22
P03-	Quality Control Plan (QCP)	39	60%	$3.03	28-Nov-21	27-Apr-22
P03-	Specification for Welding Procedure	44	0%	$3.03	03-Apr-22	16-May-22
P03-	Heat Treatment Procedure (Pre Heating , PWHT)	44	0%	$3.03	03-Apr-22	16-May-22
P03-	Welder Performance Qualification Test (WQT) Procedure	44	0%	$3.03	03-Apr-22	16-May-22
P03-	NDT Procedure	44	0%	$3.03	03-Apr-22	16-May-22
P03-	Surface Preparation and Coating/Painting Procedure	44	0%	$3.03	03-Apr-22	16-May-22
P03-	Control of Inspection Measuring and Test Equipment Procedu	44	0%	$3.01	03-Apr-22	16-May-22
QC Discipline Document		81	8.01%	$143.00	20-Sep-21	16-May-22
Piping		51	0%	$35.75	27-Mar-22	16-May-22
P03	ITP For Piping Works	44	0%	$3.58	27-Mar-22	09-May-22
P03	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$4.02	03-Apr-22	16-May-22
P03	PIPING WPS (Welding Procedure Specification)	44	0%	$4.02	03-Apr-22	16-May-22
P03	PIPING PQR (Procedure Qualification Record)	44	0%	$4.02	03-Apr-22	16-May-22

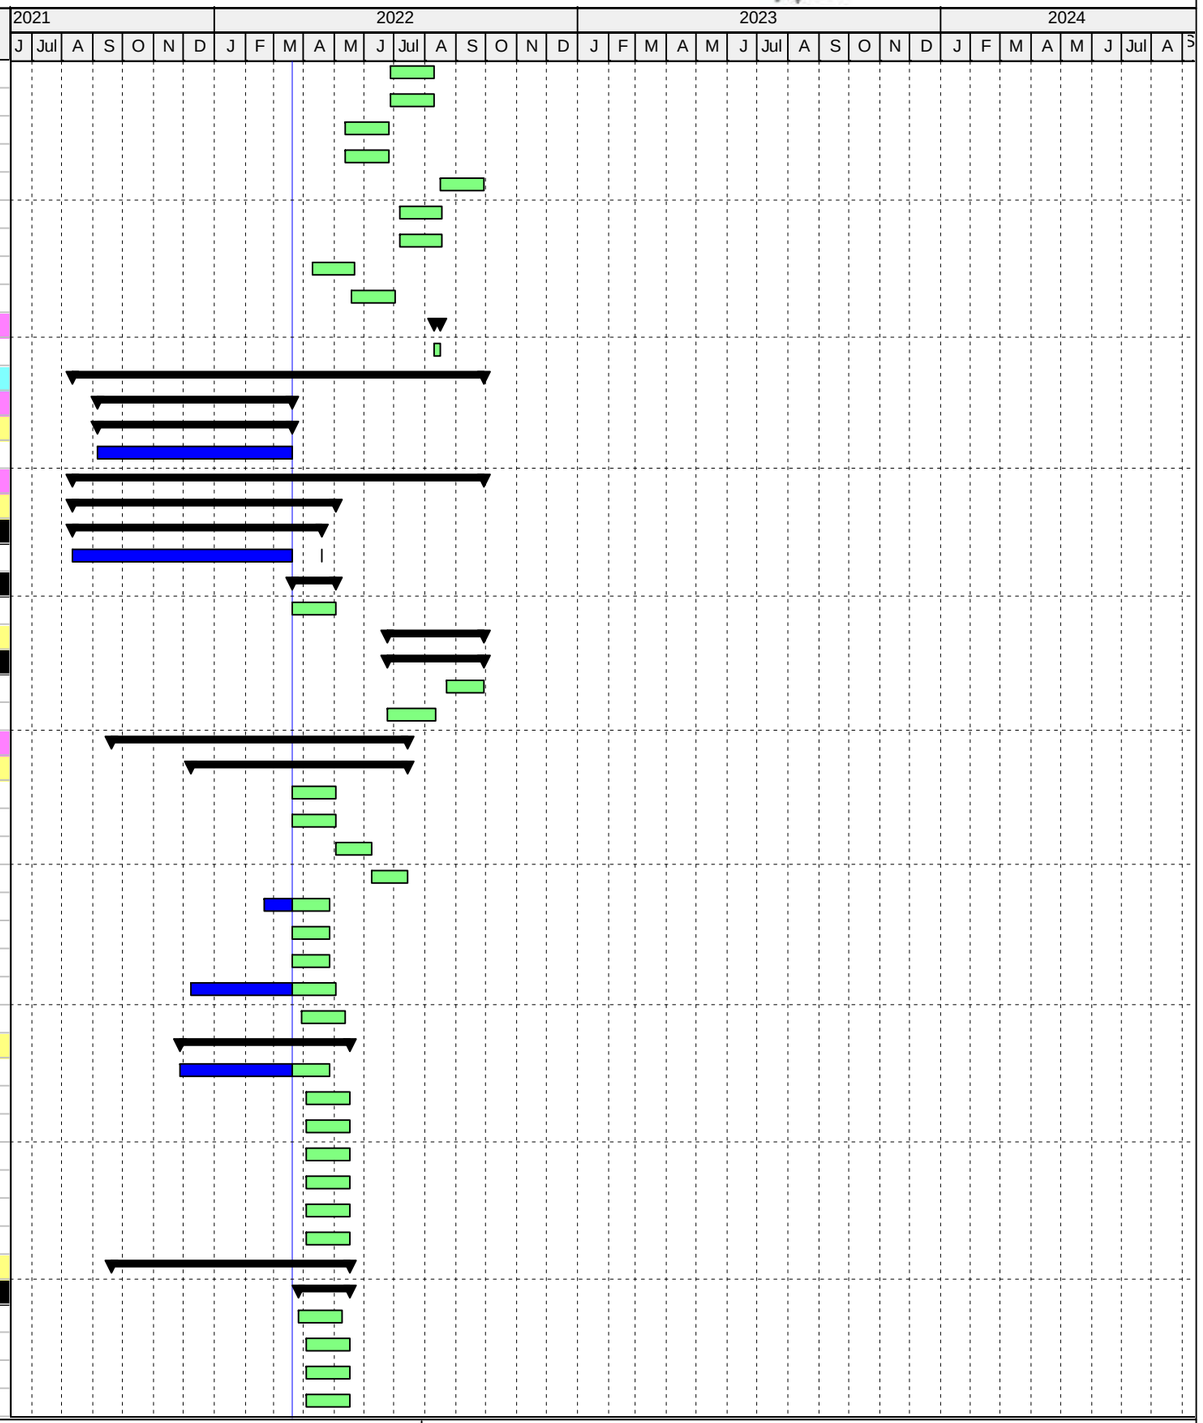

Actual Level of Effort Remaining Work Milestone
Actual Work Critical Remaining Work summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$4.02	03-Apr-22	16-May-22
P03	PIPING WPS (Preliminary Welding Procedure Specification) f	44	0%	$4.02	03-Apr-22	16-May-22
P03	PIPING PQR (Procedure Qualification Record) for Repair We	44	0%	$4.02	03-Apr-22	16-May-22
P03	Field Joint Coating Procedure For Pipeline	44	0%	$4.02	03-Apr-22	16-May-22
P03	Pressure Test Procedure	44	0%	$4.02	03-Apr-22	16-May-22
Telecomm.		44	0%	$7.15	27-Mar-22	09-May-22
P03	ITP For Telecommunication Installation	44	0%	$7.15	27-Mar-22	09-May-22
Safety		44	0%	$7.15	27-Mar-22	09-May-22
P03	ITP For Safety Installation	44	0%	$7.15	27-Mar-22	09-May-22
Architectural		44	0%	$7.15	27-Mar-22	09-May-22
P03	ITP For Architectural Works	44	0%	$7.15	27-Mar-22	09-May-22
Mechanical		44	0%	$7.15	27-Mar-22	09-May-22
P03	ITP For Mechanical Installation	44	0%	$7.15	27-Mar-22	09-May-22
Structure		51	0%	$28.60	27-Mar-22	16-May-22
P03	ITP For Steel Structural Works	44	0%	$2.86	27-Mar-22	09-May-22
P03	Steel Structure WPS (Welding Procedure Specification)	44	0%	$4.29	03-Apr-22	16-May-22
P03	Steel Structure PQR (Procedure Qualification Record)	44	0%	$4.29	03-Apr-22	16-May-22
P03	Steel Structure WPS (Welding Procedure Specification) For F	44	0%	$4.29	03-Apr-22	16-May-22
P03	Steel Structure PQR (Procedure Qualification Record) For Re	44	0%	$4.29	03-Apr-22	16-May-22
P03	Weld Map For Steel Structures	44	0%	$4.29	03-Apr-22	16-May-22
P03	NDT Plan For steel Structures	44	0%	$4.29	03-Apr-22	16-May-22
Instrumentation		44	0%	$7.15	27-Mar-22	09-May-22
P03	ITP For I&C Installation	44	0%	$7.15	27-Mar-22	09-May-22
Pipeline		74	15.03%	$28.60	16-Jan-22	16-May-22
P03	ITP For Pipeline	44	60%	$2.86	16-Jan-22	09-May-22
P03	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	60%	$4.29	23-Feb-22	16-May-22
P03	PIPELINE WPS (Welding Procedure Specification)	44	0%	$4.29	03-Apr-22	16-May-22
P03	PIPELINE PQR (Procedure Qualification Record)	44	0%	$4.29	03-Apr-22	16-May-22
P03	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	0%	$4.29	03-Apr-22	16-May-22
P03	PIPELINE WPS (Preliminary Welding Procedure Specificatior	44	0%	$4.29	03-Apr-22	16-May-22
P03	PIPELINE PQR (Procedure Qualification Record) for Repair \	44	0%	$4.29	03-Apr-22	16-May-22
Civil		44	100%	$7.15	20-Sep-21	27-Mar-22
P03	ITP For Civil Works	44	100%	$7.15	20-Sep-21	27-Mar-22
Electrical		44	0%	$7.15	27-Mar-22	09-May-22
P03	ITP For Electrical Installation	44	0%	$7.15	27-Mar-22	09-May-22
Procurement Engineering		325	2.35%	$1,625.00	13-Dec-21	16-Mar-23
Mechanical		70	0%	$129.68	27-Jun-22	04-Sep-22
Drum		50	0%	$77.81	17-Jul-22	04-Sep-22
P03-E	PMR For Drums - W046S	5	0%	$7.78	17-Jul-22	21-Jul-22
P03-E	TBE For Drums - W046S	5	0%	$11.67	22-Jul-22	26-Jul-22
P03-E	VDR For Drums - W046S	5	0%	$58.35	31-Aug-22	04-Sep-22
Potable Tanks		50	0%	$51.87	27-Jun-22	15-Aug-22
P03-E	PMR For Potable Tanks - W046S	5	0%	$5.19	27-Jun-22	01-Jul-22
P03-E	TBE For Potable Tanks - W046S	5	0%	$7.78	02-Jul-22	06-Jul-22
P03-E	VDR For Potable Tanks - W046S	5	0%	$38.90	11-Aug-22	15-Aug-22
Piping		147	0%	$228.96	30-Aug-22	23-Jan-23
Pipes		55	0%	$25.46	12-Sep-22	05-Nov-22
P03-E	PMR For Pipes - W046S	10	0%	$2.55	30-Sep-22	09-Oct-22
P03-E	TBE For Pipes - W046S	30	0%	$3.82	07-Oct-22	05-Nov-22
P03-E	VDR For Pipes - W046S	20	0%	$19.10	12-Sep-22	01-Oct-22




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Fittings		43	0%	$25.44	24-Sep-22	05-Nov-22
P03-E	PMR For Fittings - W046S	10	0%	$2.54	30-Sep-22	09-Oct-22
P03-E	TBE For Fitting - W046S	30	0%	$3.82	07-Oct-22	05-Nov-22
P03-E	VDR For Fitting - W046S	20	0%	$19.08	24-Sep-22	13-Oct-22
Flanges		68	0%	$25.44	30-Aug-22	05-Nov-22
P03-E	PMR For Flanges - W046S	10	0%	$2.54	30-Sep-22	09-Oct-22
P03-E	TBE For Flanges - W046S	30	0%	$3.82	07-Oct-22	05-Nov-22
P03-E	VDR For Flanges - W046S	20	0%	$19.08	30-Aug-22	18-Sep-22
Manual Valves		79	0%	$25.44	30-Sep-22	17-Dec-22
P03-E	PMR For Manual Valves - W046S	10	0%	$2.54	30-Sep-22	09-Oct-22
P03-E	TBE For Manual Valves - W046S	30	0%	$3.82	07-Oct-22	05-Nov-22
P03-E	VDR For Manual Valves - W046S	20	0%	$19.08	28-Nov-22	17-Dec-22
Gaskets		79	0%	$25.44	30-Sep-22	17-Dec-22
P03-E	PMR For Gaskets - W046S	10	0%	$2.54	30-Sep-22	09-Oct-22
P03-E	TBE For Gaskets - W046S	30	0%	$3.82	07-Oct-22	05-Nov-22
P03-E	VDR For Gaskets - W046S	20	0%	$19.08	28-Nov-22	17-Dec-22
Bolt & Nuts		79	0%	$25.44	30-Sep-22	17-Dec-22
P03-E	PMR For Bolt/Nuts - W046S	10	0%	$2.54	30-Sep-22	09-Oct-22
P03-E	TBE For Bolt/Nuts - W046S	30	0%	$3.82	07-Oct-22	05-Nov-22
P03-E	VDR For Bolt/Nuts - W046S	20	0%	$19.08	28-Nov-22	17-Dec-22
Sampling Connection		79	0%	$25.44	06-Nov-22	23-Jan-23
P03-E	PMR For Sampling Connection Set - W046S	10	0%	$2.54	06-Nov-22	15-Nov-22
P03-E	TBE For Sampling Connection - W046S	30	0%	$3.82	13-Nov-22	12-Dec-22
P03-E	VDR For Sampling Connection - W046S	20	0%	$19.08	04-Jan-23	23-Jan-23
Stone Trap		79	0%	$25.44	06-Nov-22	23-Jan-23
P03-E	PMR For Stone Trap - W046S	10	0%	$2.54	06-Nov-22	15-Nov-22
P03-E	TBE For Stone Trap - W046S	30	0%	$3.82	13-Nov-22	12-Dec-22
P03-E	VDR For Stone Trap - W046S	20	0%	$19.08	04-Jan-23	23-Jan-23
Pipe Support		54	0%	$25.44	06-Nov-22	29-Dec-22
P03-E	PMR For Pipe Support - W046S	5	0%	$2.54	06-Nov-22	10-Nov-22
P03-E	TBE For Pipe Support - W046S	5	0%	$3.82	13-Nov-22	17-Nov-22
P03-E	VDR For Pipe Support - W046S	20	0%	$19.08	10-Dec-22	29-Dec-22
HVAC		82	0%	$32.50	25-Dec-22	16-Mar-23
Main HVAC Equipment		82	0%	$32.50	25-Dec-22	16-Mar-23
P03-E	PMR For Main HVAC Equipment - W046S	10	0%	$3.25	25-Dec-22	03-Jan-23
P03-E	TBE For Main HVAC Equipment - W046S	30	0%	$4.88	01-Jan-23	30-Jan-23
P03-E	VDR For Main HVAC Equipment - W046S	20	0%	$24.38	25-Feb-23	16-Mar-23
Pipeline		74	7.52%	$51.19	19-Feb-22	12-Aug-22
Line Pipe		74	15.04%	$25.59	19-Feb-22	26-Jul-22
P03-E	PMR For Line Pipes - W046S	7	0%	$2.56	18-Jun-22	24-Jun-22
P03-E	TBE For Line Pipes - W046S	30	100%	$3.84	19-Feb-22	25-Jun-22
P03-E	VDR For Line Pipes - W046S	20	0%	$19.20	07-Jul-22	26-Jul-22
Flow Line Support		49	0%	$25.59	25-Jun-22	12-Aug-22
P03-E	PMR For Flowline Support - W046S	7	0%	$2.56	25-Jun-22	01-Jul-22
P03-E	TBE For Flowline Support - W046S	5	0%	$3.84	12-Jul-22	16-Jul-22
P03-E	VDR For Flowline Support - W046S	5	0%	$19.20	08-Aug-22	12-Aug-22
Control & Instrumentation		201	18.18%	$188.50	13-Dec-21	16-Dec-22
Field Instrumentations		130	9.99%	$85.67	13-Dec-21	16-Dec-22
P03-E	PMR For Field Instrumentations - W046S	10	100%	$8.57	13-Dec-21	23-Sep-22
P03-E	TBE/TBA For Field Instrumentations - W046S	30	0%	$12.85	23-Sep-22	22-Oct-22

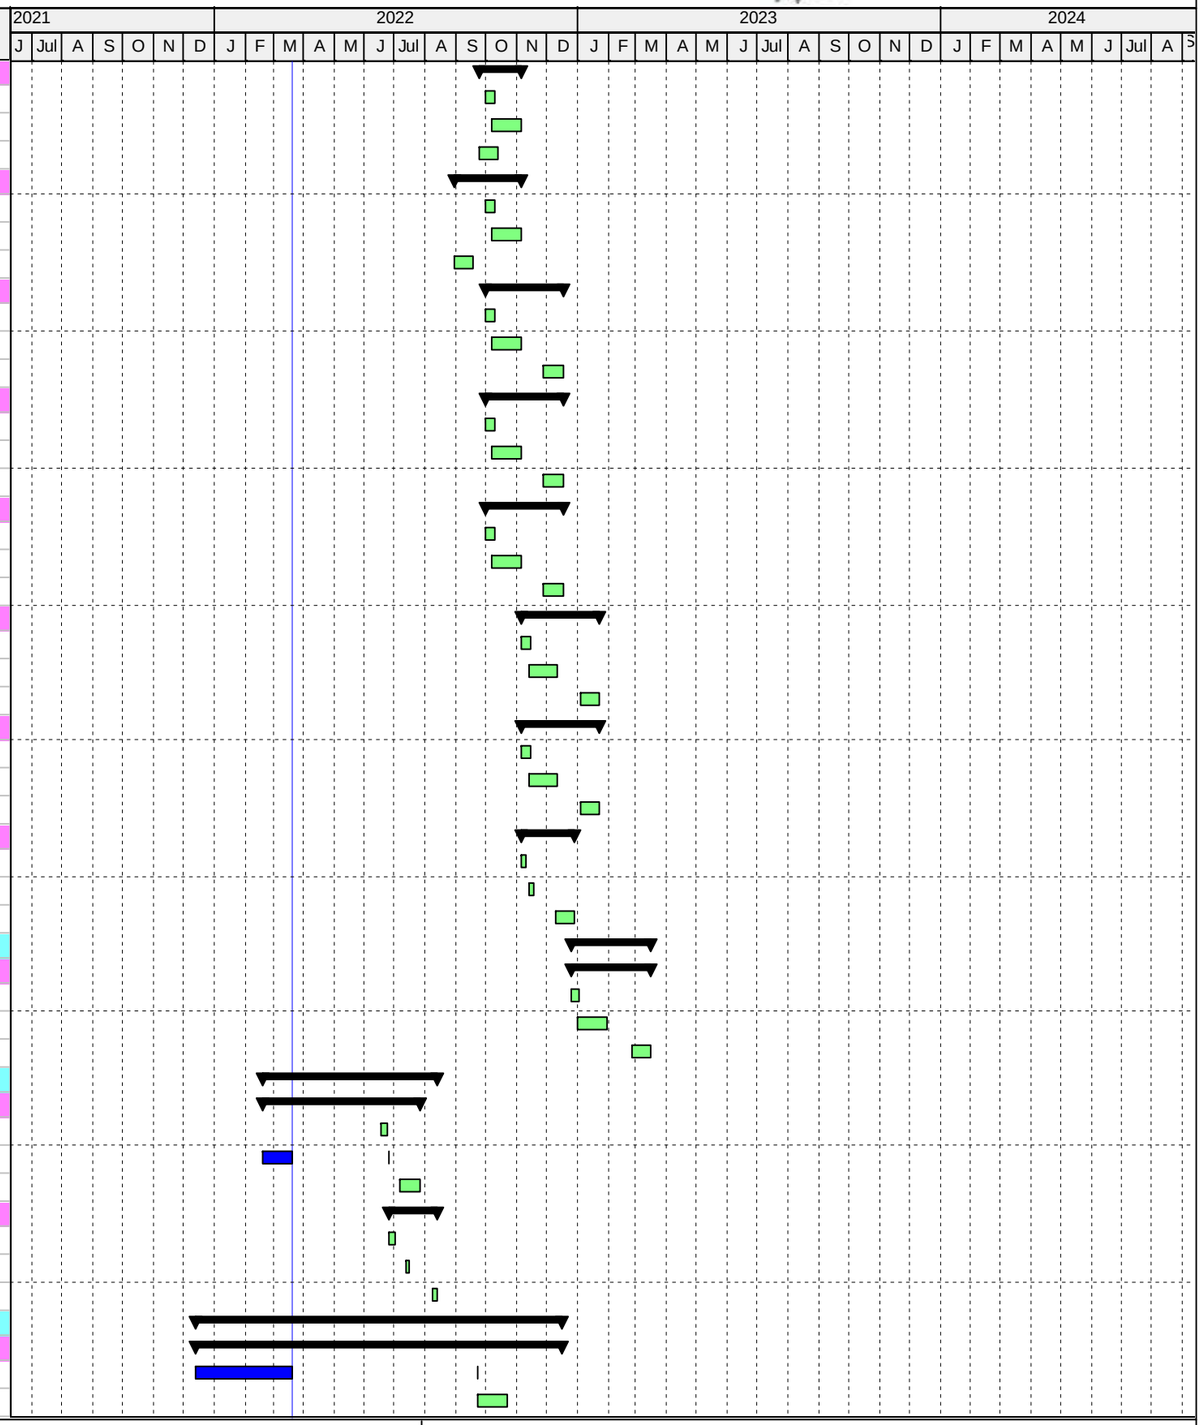


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	VDR/TBA For Field Instrumentations - W046S	20	0%	$64.25	27-Nov-22	16-Dec-22
Instrument Bulk Items		104	25%	$102.83	16-Jan-22	02-Aug-22
P03-E	PMR For Instrument Bulk Items - W046S	10	100%	$10.28	16-Jan-22	13-May-22
P03-E	TBE/TBA For Instrument Bulk Items - W046S	30	100%	$15.42	02-Feb-22	13-May-22
P03-E	VDR/TBA For Instrument Bulk Items - W046S	20	0%	$77.12	14-Jul-22	02-Aug-22
Safety & Fire Fighting		124	0%	$205.56	31-Jul-22	01-Dec-22
Safety Sign		92	0%	$107.07	01-Sep-22	01-Dec-22
P03-E	VDR For Fire Fighting and Safety Equipment - W046S	20	0%	$83.51	12-Nov-22	01-Dec-22
P03-E	PMR For Fire Safety Sign - W046S	10	0%	$9.42	01-Sep-22	10-Sep-22
P03-E	TBE For Fire Safety Sign - W046S	30	0%	$14.13	08-Sep-22	07-Oct-22
Fire Fighting and Safety Equipment		92	0%	$98.50	31-Jul-22	30-Oct-22
P03-E	PMR For Fire Fighting and Safety Equipment - W046S	10	0%	$11.14	31-Jul-22	09-Aug-22
P03-E	TBE For Fire Fighting and Safety Equipment - W046S	30	0%	$16.70	07-Aug-22	05-Sep-22
P03-E	VDR For Fire Safety Sign - W046S	20	0%	$70.66	11-Oct-22	30-Oct-22
Electrical		256	0%	$661.38	26-Apr-22	06-Jan-23
Transformers		72	0%	$50.93	18-May-22	28-Jul-22
P03-E	PMR For Transformers - W046S	10	0%	$5.09	18-May-22	27-May-22
P03-E	TBE For Transformers - W046S	30	0%	$7.64	28-May-22	26-Jun-22
P03-E	VDR For Transformers - W046S	20	0%	$38.19	09-Jul-22	28-Jul-22
LV Switchgear & MCC		69	0%	$50.93	13-May-22	20-Jul-22
P03-E	PMR For LV Switchgear & MCC - W046S	10	0%	$5.09	13-May-22	22-May-22
P03-E	TBE For LV Switchgear & MCC - W046S	30	0%	$7.64	20-May-22	18-Jun-22
P03-E	VDR For LV Switchgear & MCC - W046S	20	0%	$38.19	01-Jul-22	20-Jul-22
Emergency Diesel Generator		69	0%	$50.93	23-May-22	30-Jul-22
P03-E	PMR For Emergency Diesel Generator - W046S	10	0%	$5.09	23-May-22	01-Jun-22
P03-E	TBE For Emergency Diesel Generator - W046S	30	0%	$7.64	30-May-22	28-Jun-22
P03-E	VDR For Emergency Diesel Generator - W046S	20	0%	$38.19	11-Jul-22	30-Jul-22
UPS System		79	0%	$50.86	11-Aug-22	28-Oct-22
P03-E	PMR For UPS System - W046S	10	0%	$5.09	11-Aug-22	20-Aug-22
P03-E	TBE For UPS System - W046S	30	0%	$7.63	18-Aug-22	16-Sep-22
P03-E	VDR For UPS System - W046S	20	0%	$38.14	09-Oct-22	28-Oct-22
DC Charger		69	0%	$50.86	23-May-22	30-Jul-22
P03-E	PMR For DC Charger - W046S	10	0%	$5.09	23-May-22	01-Jun-22
P03-E	TBE For DC Charger - W046S	30	0%	$7.63	30-May-22	28-Jun-22
P03-E	VDR For DC Charger - W046S	20	0%	$38.14	11-Jul-22	30-Jul-22
Capacitor Bank		69	0%	$50.86	18-May-22	25-Jul-22
P03-E	PMR For Capacitor Bank - W046S	10	0%	$5.09	18-May-22	27-May-22
P03-E	TBE For Capacitor Bank - W046S	30	0%	$7.63	25-May-22	23-Jun-22
P03-E	VDR For Capacitor Bank - W046S	20	0%	$38.14	06-Jul-22	25-Jul-22
Lighting & Distribution Main Panels		69	0%	$50.86	01-Aug-22	08-Oct-22
P03-E	PMR For Lighting & Distribution Main Panels - W046S	10	0%	$5.09	01-Aug-22	10-Aug-22
P03-E	TBE For Lighting & Distribution Main Panels - W046S	30	0%	$7.63	08-Aug-22	06-Sep-22
P03-E	VDR For Lighting & Distribution Main Panels - W046S	20	0%	$38.14	19-Sep-22	08-Oct-22
Earthing & Lightning System		69	0%	$50.86	15-Aug-22	22-Oct-22
P03-E	PMR For Earthing & Lightning System - W046S	10	0%	$5.09	15-Aug-22	24-Aug-22
P03-E	TBE For Earthing & Lightning System - W046S	30	0%	$7.63	22-Aug-22	20-Sep-22
P03-E	VDR For Earthing & Lightning System - W046S	20	0%	$38.14	03-Oct-22	22-Oct-22
Lighting and Small Power Equipment		69	0%	$50.86	25-Oct-22	01-Jan-23
P03-E	PMR For Lighting and Small Power Equipment - W046S	10	0%	$5.09	25-Oct-22	03-Nov-22

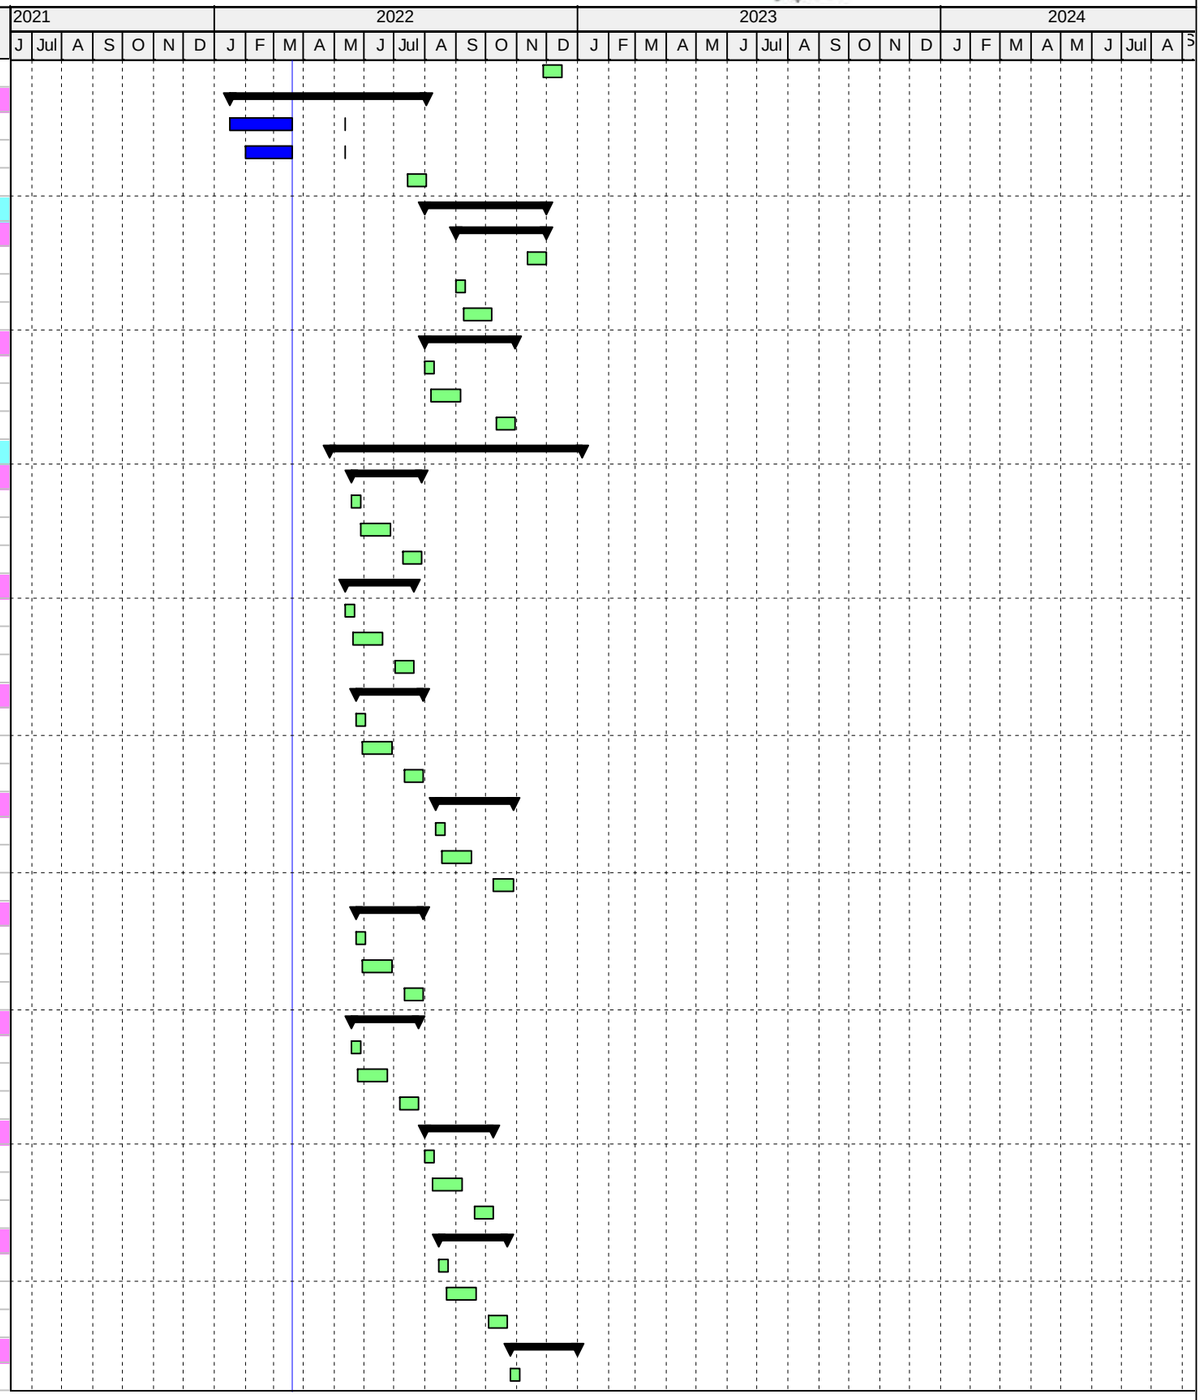

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	TBE For Lighting and Small Power Equipment - W046S	30	0%	$7.63	01-Nov-22	30-Nov-22
P03-E	VDR For Lighting and Small Power Equipment - W046S	20	0%	$38.14	13-Dec-22	01-Jan-23
Tray/Ladder and Accessories		69	0%	$50.86	14-Jun-22	21-Aug-22
P03-E	PMR For Tray/Ladder and Accessories - W046S	10	0%	$5.09	14-Jun-22	23-Jun-22
P03-E	TBE For Tray/Ladder and Accessories - W046S	30	0%	$7.63	21-Jun-22	20-Jul-22
P03-E	VDR For Tray/Ladder and Accessories - W046S	20	0%	$38.14	02-Aug-22	21-Aug-22
Power & Control Cables		69	0%	$50.86	30-Oct-22	06-Jan-23
P03-E	PMR For Power & Control Cables - W046S	10	0%	$5.09	30-Oct-22	08-Nov-22
P03-E	TBE For Power & Control Cables - W046S	30	0%	$7.63	06-Nov-22	05-Dec-22
P03-E	VDR For Power & Control Cables - W046S	20	0%	$38.14	18-Dec-22	06-Jan-23
Electrical Bulk Items		42	0%	$50.86	26-May-22	06-Jul-22
P03-E	PMR For Electrical Bulk Items - W046S	10	0%	$5.09	26-May-22	04-Jun-22
P03-E	TBE For Electrical Bulk Items - W046S	30	0%	$7.63	02-Jun-22	01-Jul-22
P03-E	VDR For Electrical Bulk Items - W046S	20	0%	$38.14	17-Jun-22	06-Jul-22
Transmission Over head Line		69	0%	$50.86	26-Apr-22	03-Jul-22
P03-E	PMR For Transmission Over head Line - W046S	10	0%	$5.09	26-Apr-22	05-May-22
P03-E	TBE For Transmission Over head Line - W046S	30	0%	$7.63	03-May-22	01-Jun-22
P03-E	VDR For Transmission Over head Line - W046S	20	0%	$38.14	14-Jun-22	03-Jul-22
Structure		47	0%	$76.38	17-Aug-22	02-Oct-22
Steel Structure Items		24	0%	$25.46	17-Aug-22	09-Sep-22
P03-E	PMR For Steel Structure Items - W046S	10	0%	$2.55	17-Aug-22	26-Aug-22
P03-E	TBE For Steel Structure Items - W046S	7	0%	$3.82	24-Aug-22	30-Aug-22
P03-E	VDR For Steel Structure Items - W046S	10	0%	$19.10	31-Aug-22	09-Sep-22
Anchor Bolts		47	0%	$25.46	17-Aug-22	02-Oct-22
P03-E	PMR For Anchor Bolts - W046S	10	0%	$2.55	17-Aug-22	26-Aug-22
P03-E	TBE For Anchor Bolts - W046S	30	0%	$3.82	24-Aug-22	22-Sep-22
P03-E	VDR For Anchor Bolts - W046S	10	0%	$19.09	23-Sep-22	02-Oct-22
Blast Proof Doors		47	0%	$25.46	17-Aug-22	02-Oct-22
P03-E	PMR For Blast Proof Doors - W046S	10	0%	$2.55	17-Aug-22	26-Aug-22
P03-E	TBE For Blast Proof Doors - W046S	30	0%	$3.82	24-Aug-22	22-Sep-22
P03-E	VDR For Blast Proof Doors - W046S	10	0%	$19.09	23-Sep-22	02-Oct-22
Civil		17	0%	$50.86	03-Jun-22	19-Jun-22
Geomembrane		17	0%	$25.43	03-Jun-22	19-Jun-22
P03-E	PMR For Geomembrane - W046S	5	0%	$2.54	03-Jun-22	07-Jun-22
P03-E	TBE For Geomembrane - W046S	5	0%	$3.81	10-Jun-22	14-Jun-22
P03-E	VDR For Geomembrane - W046S	5	0%	$19.07	15-Jun-22	19-Jun-22
Geotextile		17	0%	$25.43	03-Jun-22	19-Jun-22
P03-E	PMR For Geotextile - W046S	5	0%	$2.54	03-Jun-22	07-Jun-22
P03-E	TBE For Geotextile - W046S	5	0%	$3.81	10-Jun-22	14-Jun-22
P03-E	VDR For Geotextile - W046S	5	0%	$19.07	15-Jun-22	19-Jun-22
Commissioning Engineering		431	0%	$325.00	20-Mar-22	24-May-23
P03-EP	Operability Review	5	0%	$65.00	20-May-23	24-May-23
P03-EP	Pre-Commissioning, Commissioning & Startup Procedure - W	44	0%	$195.00	20-Mar-22	02-May-22
P03-EP	Operating Manual - W046S	20	0%	$65.00	30-Apr-23	19-May-23
Field Engineering		350	0%	$2,437.50	23-Jun-22	07-Jun-23
P03-EP	Technical/Site Queries	44	0%	$1,218.75	23-Jun-22	06-Aug-22
P03-EP	As-Built Document Booklets - W046S	7	0%	$1,218.75	01-Jun-23	07-Jun-23
Engineering Final Documentation		7	0%	$1,625.00	08-Jun-23	14-Jun-23
P03-EP	Final Engineering Dossier - W046S	7	0%	$1,625.00	08-Jun-23	14-Jun-23
PROCUREMENT		357	0%	$1,309,229.00	13-May-22	04-May-23




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Wellhead Facility and Flowline		357	0%	$1,067,807.17	13-May-22	04-May-23
Mechanical- W046S		119	0%	$20,288.34	07-Jul-22	02-Nov-22
Drum		99	0%	$12,173.00	27-Jul-22	02-Nov-22
P03-E	Tendering & Selection	30	0%	$486.92	27-Jul-22	25-Aug-22
P03-E	Contract Effectiveness / PO	5	0%	$730.38	26-Aug-22	30-Aug-22
P03-E	Manufacturing / Fabrication / Supply	40	0%	$6,086.50	31-Aug-22	09-Oct-22
P03-E	Final Inspection	12	0%	$1,217.30	10-Oct-22	21-Oct-22
P03-E	Delivery On Site	7	0%	$2,434.60	22-Oct-22	28-Oct-22
P03-E	Submitting Vendor Data Book	5	0%	$608.65	29-Oct-22	02-Nov-22
P03-E	Delivering Spare Parts	5	0%	$608.65	29-Oct-22	02-Nov-22
Potable Tanks		99	0%	$8,115.33	07-Jul-22	13-Oct-22
P03-E	Tendering & Selection	30	0%	$324.61	07-Jul-22	05-Aug-22
P03-E	Contract Effectiveness / PO	5	0%	$486.92	06-Aug-22	10-Aug-22
P03-E	Manufacturing / Fabrication / Supply	40	0%	$4,057.67	11-Aug-22	19-Sep-22
P03-E	Final Inspection	12	0%	$811.53	20-Sep-22	01-Oct-22
P03-E	Delivery On Site	7	0%	$1,623.07	02-Oct-22	08-Oct-22
P03-E	Submitting Vendor Data Book	5	0%	$405.77	09-Oct-22	13-Oct-22
P03-E	Delivering Spare Parts	5	0%	$405.77	09-Oct-22	13-Oct-22
HVAC/Plumbing - W046S		94	0%	$3,203.42	31-Jan-23	04-May-23
Main HVAC Equipment		94	0%	$3,203.42	31-Jan-23	04-May-23
P03-E	Tendering & Selection	20	0%	$128.14	31-Jan-23	19-Feb-23
P03-E	Contract Effectiveness / PO	5	0%	$192.21	20-Feb-23	24-Feb-23
P03-E	Manufacturing / Fabrication / Supply	40	0%	$1,601.71	25-Feb-23	05-Apr-23
P03-E	Final Inspection	12	0%	$320.34	06-Apr-23	17-Apr-23
P03-E	Delivery On Site	7	0%	$640.68	18-Apr-23	24-Apr-23
P03-E	Submitting Vendor Data Book	5	0%	$160.17	25-Apr-23	29-Apr-23
P03-E	Delivering Spare Parts	5	0%	$160.17	30-Apr-23	04-May-23
Piping - W046S		146	0%	$65,883.70	16-Nov-22	10-Apr-23
Pipes - W046S		141	0%	$13,176.74	16-Nov-22	05-Apr-23
P03-E	Tendering & Selection	7	0%	$527.07	16-Nov-22	22-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$790.60	23-Nov-22	27-Nov-22
P03-E	Manufacturing / Fabrication / Supply	110	0%	$6,588.37	28-Nov-22	17-Mar-23
P03-E	Final Inspection	7	0%	$1,317.67	18-Mar-23	24-Mar-23
P03-E	Delivery On Site	7	0%	$3,294.19	25-Mar-23	31-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$658.84	01-Apr-23	05-Apr-23
Fittings - W046S		141	0%	$4,941.28	16-Nov-22	05-Apr-23
P03-E	Tendering & Selection	7	0%	$197.65	16-Nov-22	22-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$296.48	23-Nov-22	27-Nov-22
P03-E	Manufacturing / Fabrication / Supply	110	0%	$2,470.64	28-Nov-22	17-Mar-23
P03-E	Final Inspection	7	0%	$494.13	18-Mar-23	24-Mar-23
P03-E	Delivery On Site	7	0%	$1,235.32	25-Mar-23	31-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$247.06	01-Apr-23	05-Apr-23
Flanges - W046S		141	0%	$4,941.28	16-Nov-22	05-Apr-23
P03-E	Tendering & Selection	7	0%	$197.65	16-Nov-22	22-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$296.48	23-Nov-22	27-Nov-22
P03-E	Manufacturing / Fabrication / Supply	110	0%	$2,470.64	28-Nov-22	17-Mar-23
P03-E	Final Inspection	7	0%	$494.13	18-Mar-23	24-Mar-23
P03-E	Delivery On Site	7	0%	$1,235.32	25-Mar-23	31-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$247.06	01-Apr-23	05-Apr-23

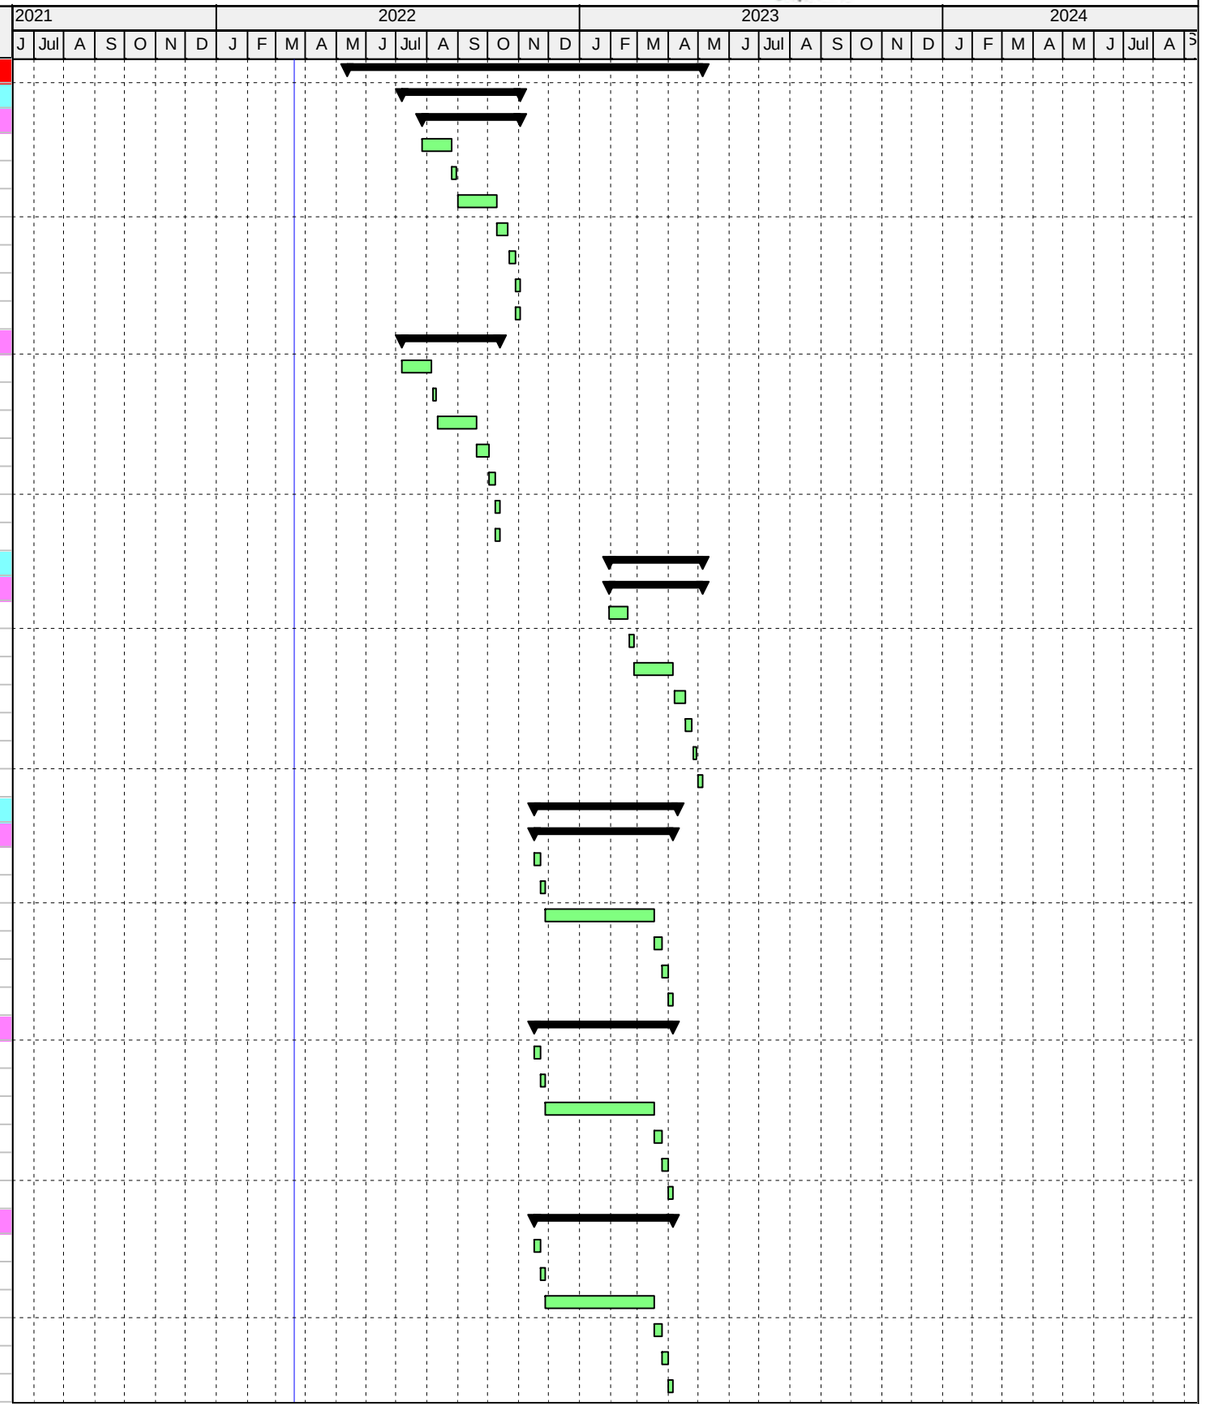


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Manual Valves - W046S		146	0%	$23,059.30	16-Nov-22	10-Apr-23
P03-E	Tendering & Selection	7	0%	$922.37	16-Nov-22	22-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$1,383.56	23-Nov-22	27-Nov-22
P03-E	Manufacturing / Fabrication / Supply	110	0%	$11,529.65	28-Nov-22	17-Mar-23
P03-E	Final Inspection	7	0%	$2,305.93	18-Mar-23	24-Mar-23
P03-E	Delivery On Site	7	0%	$4,611.86	25-Mar-23	31-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$1,152.96	01-Apr-23	05-Apr-23
P03-E	Delivering Spare Parts	5	0%	$1,152.96	06-Apr-23	10-Apr-23
Gaskets - W046S		141	0%	$1,976.51	16-Nov-22	05-Apr-23
P03-E	Tendering & Selection	7	0%	$79.06	16-Nov-22	22-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$118.59	23-Nov-22	27-Nov-22
P03-E	Manufacturing / Fabrication / Supply	110	0%	$988.26	28-Nov-22	17-Mar-23
P03-E	Final Inspection	7	0%	$197.65	18-Mar-23	24-Mar-23
P03-E	Delivery On Site	7	0%	$494.13	25-Mar-23	31-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$98.83	01-Apr-23	05-Apr-23
Bolt/Nuts - W046S		121	0%	$1,317.67	16-Nov-22	16-Mar-23
P03-E	Tendering & Selection	7	0%	$52.71	16-Nov-22	22-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$79.06	23-Nov-22	27-Nov-22
P03-E	Manufacturing / Fabrication / Supply	90	0%	$658.84	28-Nov-22	25-Feb-23
P03-E	Final Inspection	7	0%	$131.77	26-Feb-23	04-Mar-23
P03-E	Delivery On Site	7	0%	$329.42	05-Mar-23	11-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$65.88	12-Mar-23	16-Mar-23
Sampling Connection Set - W046S		81	0%	$3,294.19	23-Dec-22	13-Mar-23
P03-E	Tendering & Selection	7	0%	$131.77	23-Dec-22	29-Dec-22
P03-E	Contract Effectiveness / PO	5	0%	$197.65	30-Dec-22	03-Jan-23
P03-E	Manufacturing / Fabrication / Supply	50	0%	$1,647.09	04-Jan-23	22-Feb-23
P03-E	Final Inspection	7	0%	$329.42	23-Feb-23	01-Mar-23
P03-E	Delivery On Site	7	0%	$823.55	02-Mar-23	08-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$164.71	09-Mar-23	13-Mar-23
Stone Trap - W046S		81	0%	$9,882.56	23-Dec-22	13-Mar-23
P03-E	Tendering & Selection	7	0%	$395.30	23-Dec-22	29-Dec-22
P03-E	Contract Effectiveness / PO	5	0%	$592.95	30-Dec-22	03-Jan-23
P03-E	Manufacturing / Fabrication / Supply	50	0%	$4,941.28	04-Jan-23	22-Feb-23
P03-E	Final Inspection	7	0%	$988.26	23-Feb-23	01-Mar-23
P03-E	Delivery On Site	7	0%	$2,470.64	02-Mar-23	08-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$494.13	09-Mar-23	13-Mar-23
Pipe Support - W046S		81	0%	$3,294.19	28-Nov-22	16-Feb-23
P03-E	Tendering & Selection	7	0%	$131.77	28-Nov-22	04-Dec-22
P03-E	Contract Effectiveness / PO	5	0%	$197.65	05-Dec-22	09-Dec-22
P03-E	Manufacturing / Fabrication / Supply	50	0%	$1,647.09	10-Dec-22	28-Jan-23
P03-E	Final Inspection	7	0%	$329.42	29-Jan-23	04-Feb-23
P03-E	Delivery On Site	7	0%	$823.55	05-Feb-23	11-Feb-23
P03-E	Submitting Vendor Data Book	5	0%	$164.71	12-Feb-23	16-Feb-23
Pipeline - W046S		143	0%	$583,129.50	25-Jun-22	14-Nov-22
Line Pipes - W046S		121	0%	$495,660.07	25-Jun-22	23-Oct-22
P03-E	Tendering & Selection	7	0%	$19,826.40	25-Jun-22	01-Jul-22
P03-E	Contract Effectiveness / PO	5	0%	$29,739.60	02-Jul-22	06-Jul-22
P03-E	Manufacturing / Fabrication / Supply	90	0%	$247,830.04	07-Jul-22	04-Oct-22
P03-E	Final Inspection	7	0%	$49,566.01	05-Oct-22	11-Oct-22

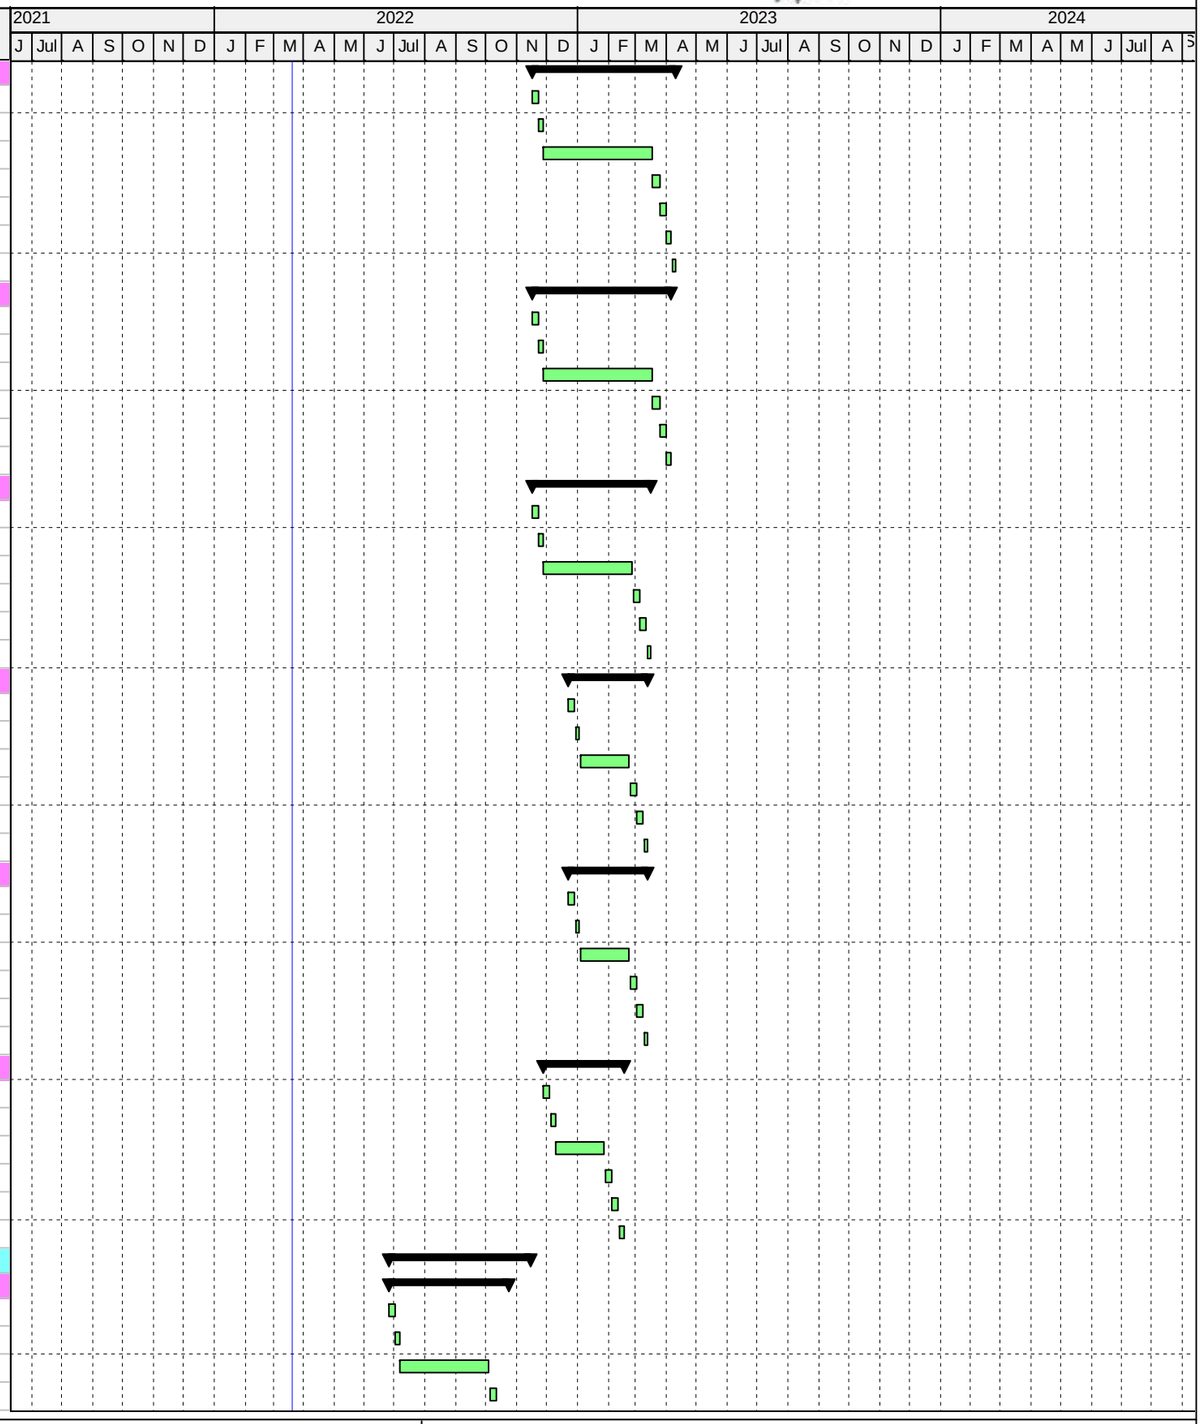


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	Delivery On Site	7	0%	$123,915.02	12-Oct-22	18-Oct-22
P03-E	Submitting Vendor Data Book	5	0%	$24,783.00	19-Oct-22	23-Oct-22
Flow Line Support - W046S		111	0%	$87,469.42	27-Jul-22	14-Nov-22
P03-E	Tendering & Selection	7	0%	$3,498.78	27-Jul-22	02-Aug-22
P03-E	Contract Effectiveness / PO	5	0%	$5,248.17	03-Aug-22	07-Aug-22
P03-E	Manufacturing / Fabrication / Supply	80	0%	$43,734.71	08-Aug-22	26-Oct-22
P03-E	Final Inspection	7	0%	$8,746.94	27-Oct-22	02-Nov-22
P03-E	Delivery On Site	7	0%	$21,867.36	03-Nov-22	09-Nov-22
P03-E	Submitting Vendor Data Book	5	0%	$4,373.47	10-Nov-22	14-Nov-22
Control & Instrumentation - W046S		307	0%	$12,813.69	13-May-22	15-Mar-23
Field Instrumentations		144	0%	$10,250.95	23-Oct-22	15-Mar-23
P03-E	Tendering & Selection	30	0%	$410.04	23-Oct-22	21-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$615.06	22-Nov-22	26-Nov-22
P03-E	Manufacturing / Fabrication / Supply	80	0%	$5,125.47	27-Nov-22	14-Feb-23
P03-E	Final Inspection	12	0%	$1,025.09	15-Feb-23	26-Feb-23
P03-E	Delivery On Site	7	0%	$2,050.19	27-Feb-23	05-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$512.55	06-Mar-23	10-Mar-23
P03-E	Delivering Spare Parts	5	0%	$512.55	11-Mar-23	15-Mar-23
Instrument Tube and Fitting - W046S		119	0%	$1,922.05	13-May-22	08-Sep-22
P03-E	Tendering & Selection	30	0%	$76.88	13-May-22	11-Jun-22
P03-E	Contract Effectiveness / PO	5	0%	$115.32	12-Jun-22	16-Jun-22
P03-E	Manufacturing / Fabrication / Supply	60	0%	$961.03	17-Jun-22	15-Aug-22
P03-E	Final Inspection	12	0%	$192.21	16-Aug-22	27-Aug-22
P03-E	Delivery On Site	7	0%	$480.51	28-Aug-22	03-Sep-22
P03-E	Submitting Vendor Data Book	5	0%	$96.10	04-Sep-22	08-Sep-22
Instrument Cable Tray - W046S		119	0%	$640.68	13-May-22	08-Sep-22
P03-E	Tendering & Selection	30	0%	$25.63	13-May-22	11-Jun-22
P03-E	Contract Effectiveness / PO	5	0%	$38.44	12-Jun-22	16-Jun-22
P03-E	Manufacturing / Fabrication / Supply	60	0%	$320.34	17-Jun-22	15-Aug-22
P03-E	Final Inspection	12	0%	$64.07	16-Aug-22	27-Aug-22
P03-E	Delivery On Site	7	0%	$160.17	28-Aug-22	03-Sep-22
P03-E	Submitting Vendor Data Book	5	0%	$32.03	04-Sep-22	08-Sep-22
Safety & Fire Fighting - W046S		111	0%	$2,669.52	06-Sep-22	25-Dec-22
Fire Fighting and Safety Equipment - W046S		79	0%	$2,135.61	06-Sep-22	23-Nov-22
P03-E	Tendering & Selection	30	0%	$85.42	06-Sep-22	05-Oct-22
P03-E	Contract Effectiveness / PO	5	0%	$128.14	06-Oct-22	10-Oct-22
P03-E	Manufacturing / Fabrication / Supply	20	0%	$1,067.81	11-Oct-22	30-Oct-22
P03-E	Final Inspection	12	0%	$213.56	31-Oct-22	11-Nov-22
P03-E	Delivery On Site	7	0%	$533.90	12-Nov-22	18-Nov-22
P03-E	Submitting Vendor Data Book	5	0%	$106.78	19-Nov-22	23-Nov-22
Safety Sign - W046S		79	0%	$533.90	08-Oct-22	25-Dec-22
P03-E	Tendering & Selection	30	0%	$21.36	08-Oct-22	06-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$32.03	07-Nov-22	11-Nov-22
P03-E	Manufacturing / Fabrication / Supply	20	0%	$266.95	12-Nov-22	01-Dec-22
P03-E	Final Inspection	12	0%	$53.39	02-Dec-22	13-Dec-22
P03-E	Delivery On Site	7	0%	$133.48	14-Dec-22	20-Dec-22
P03-E	Submitting Vendor Data Book	5	0%	$26.70	21-Dec-22	25-Dec-22
Electrical - W046S		318	0%	$379,819.01	02-Jun-22	15-Apr-23
Transformers - W046S		146	0%	$27,005.13	27-Jun-22	19-Nov-22

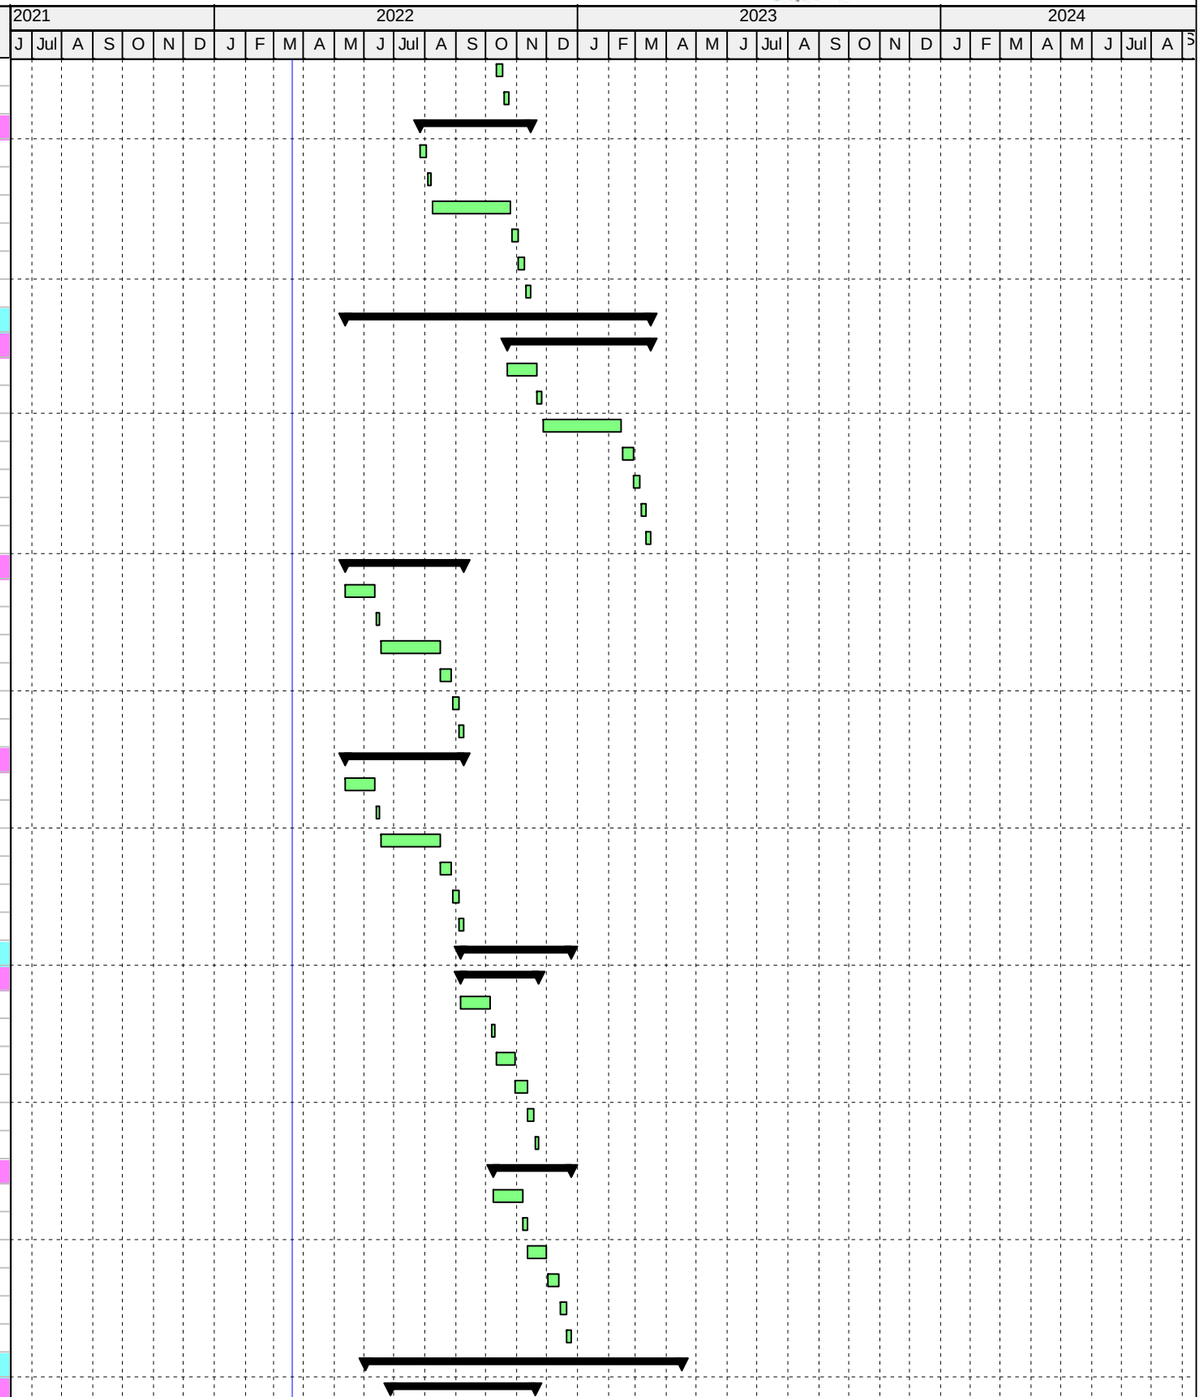


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID		Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E		Tendering & Selection	7	0%	$1,080.21	27-Jun-22	03-Jul-22
P03-E		Contract Effectiveness / PO	5	0%	$1,620.31	04-Jul-22	08-Jul-22
P03-E		Manufacturing / Fabrication / Supply	110	0%	$13,502.57	09-Jul-22	26-Oct-22
P03-E		Final Inspection	7	0%	$2,700.51	27-Oct-22	02-Nov-22
P03-E		Delivery On Site	7	0%	$5,401.03	03-Nov-22	09-Nov-22
P03-E		Submitting Vendor Data Book	5	0%	$1,350.26	10-Nov-22	14-Nov-22
P03-E		Delivering Spare Parts	5	0%	$1,350.26	15-Nov-22	19-Nov-22
LV Switchgear & MCC - W046S			146	0%	$20,890.05	19-Jun-22	11-Nov-22
P03-E		Tendering & Selection	7	0%	$835.60	19-Jun-22	25-Jun-22
P03-E		Contract Effectiveness / PO	5	0%	$1,253.40	26-Jun-22	30-Jun-22
P03-E		Manufacturing / Fabrication / Supply	110	0%	$10,445.02	01-Jul-22	18-Oct-22
P03-E		Final Inspection	7	0%	$2,089.00	19-Oct-22	25-Oct-22
P03-E		Delivery On Site	7	0%	$4,178.01	26-Oct-22	01-Nov-22
P03-E		Submitting Vendor Data Book	5	0%	$1,044.50	02-Nov-22	06-Nov-22
P03-E		Delivering Spare Parts	5	0%	$1,044.50	07-Nov-22	11-Nov-22
Emergency Diesel Generator - W046S			151	0%	$23,168.96	29-Jun-22	26-Nov-22
P03-E		Tendering & Selection	7	0%	$926.76	29-Jun-22	05-Jul-22
P03-E		Contract Effectiveness / PO	5	0%	$1,390.14	06-Jul-22	10-Jul-22
P03-E		Manufacturing / Fabrication / Supply	115	0%	$11,584.48	11-Jul-22	02-Nov-22
P03-E		Final Inspection	7	0%	$2,316.90	03-Nov-22	09-Nov-22
P03-E		Delivery On Site	7	0%	$4,633.79	10-Nov-22	16-Nov-22
P03-E		Submitting Vendor Data Book	5	0%	$1,158.45	17-Nov-22	21-Nov-22
P03-E		Delivering Spare Parts	5	0%	$1,158.45	22-Nov-22	26-Nov-22
UPS System - W046S			146	0%	$15,572.58	27-Sep-22	19-Feb-23
P03-E		Tendering & Selection	7	0%	$622.90	27-Sep-22	03-Oct-22
P03-E		Contract Effectiveness / PO	5	0%	$934.35	04-Oct-22	08-Oct-22
P03-E		Manufacturing / Fabrication / Supply	110	0%	$7,786.29	09-Oct-22	26-Jan-23
P03-E		Final Inspection	7	0%	$1,557.26	27-Jan-23	02-Feb-23
P03-E		Delivery On Site	7	0%	$3,114.52	03-Feb-23	09-Feb-23
P03-E		Submitting Vendor Data Book	5	0%	$778.63	10-Feb-23	14-Feb-23
P03-E		Delivering Spare Parts	5	0%	$778.63	15-Feb-23	19-Feb-23
DC Charger - W046S			176	0%	$16,332.22	29-Jun-22	21-Dec-22
P03-E		Tendering & Selection	7	0%	$653.29	29-Jun-22	05-Jul-22
P03-E		Contract Effectiveness / PO	5	0%	$979.93	06-Jul-22	10-Jul-22
P03-E		Manufacturing / Fabrication / Supply	140	0%	$8,166.11	11-Jul-22	27-Nov-22
P03-E		Final Inspection	7	0%	$1,633.22	28-Nov-22	04-Dec-22
P03-E		Delivery On Site	7	0%	$3,266.44	05-Dec-22	11-Dec-22
P03-E		Submitting Vendor Data Book	5	0%	$816.61	12-Dec-22	16-Dec-22
P03-E		Delivering Spare Parts	5	0%	$816.61	17-Dec-22	21-Dec-22
Capacitor Bank - W046S			166	0%	$3,418.37	24-Jun-22	06-Dec-22
P03-E		Tendering & Selection	7	0%	$136.73	24-Jun-22	30-Jun-22
P03-E		Contract Effectiveness / PO	5	0%	$205.10	01-Jul-22	05-Jul-22
P03-E		Manufacturing / Fabrication / Supply	130	0%	$1,709.19	06-Jul-22	12-Nov-22
P03-E		Final Inspection	7	0%	$341.84	13-Nov-22	19-Nov-22
P03-E		Delivery On Site	7	0%	$683.67	20-Nov-22	26-Nov-22
P03-E		Submitting Vendor Data Book	5	0%	$170.92	27-Nov-22	01-Dec-22
P03-E		Delivering Spare Parts	5	0%	$170.92	02-Dec-22	06-Dec-22
Lighting & Distribution Main Panels - W046S			136	0%	$5,317.47	07-Sep-22	20-Jan-23
P03-E		Tendering & Selection	7	0%	$212.70	07-Sep-22	13-Sep-22

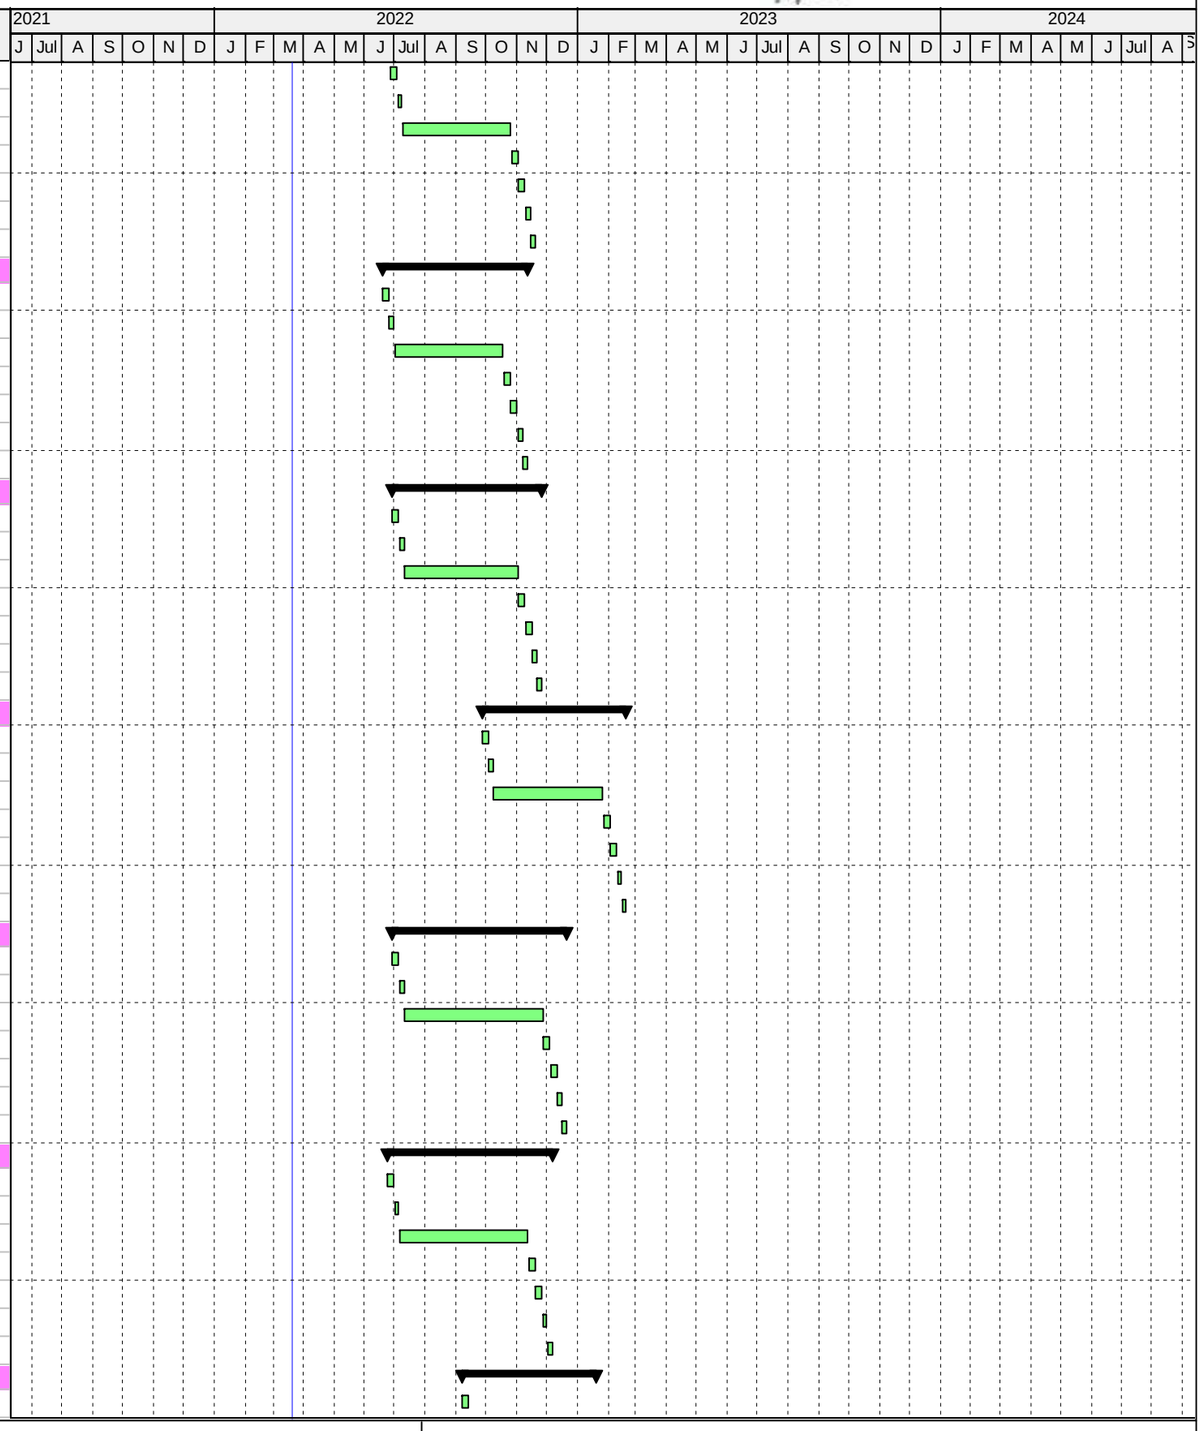


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	Contract Effectiveness / PO	5	0%	$319.05	14-Sep-22	18-Sep-22
P03-E	Manufacturing / Fabrication / Supply	100	0%	$2,658.73	19-Sep-22	27-Dec-22
P03-E	Final Inspection	7	0%	$531.75	28-Dec-22	03-Jan-23
P03-E	Delivery On Site	7	0%	$1,063.49	04-Jan-23	10-Jan-23
P03-E	Submitting Vendor Data Book	5	0%	$265.87	11-Jan-23	15-Jan-23
P03-E	Delivering Spare Parts	5	0%	$265.87	16-Jan-23	20-Jan-23
Earthing & Lightning System - W046S		96	0%	$8,621.89	21-Sep-22	25-Dec-22
P03-E	Tendering & Selection	7	0%	$344.88	21-Sep-22	27-Sep-22
P03-E	Contract Effectiveness / PO	5	0%	$517.31	28-Sep-22	02-Oct-22
P03-E	Manufacturing / Fabrication / Supply	60	0%	$4,310.95	03-Oct-22	01-Dec-22
P03-E	Final Inspection	7	0%	$862.19	02-Dec-22	08-Dec-22
P03-E	Delivery On Site	7	0%	$1,724.38	09-Dec-22	15-Dec-22
P03-E	Submitting Vendor Data Book	5	0%	$431.09	16-Dec-22	20-Dec-22
P03-E	Delivering Spare Parts	5	0%	$431.09	21-Dec-22	25-Dec-22
Lighting and Small Power Equipment - W046S		106	0%	$10,824.84	01-Dec-22	16-Mar-23
P03-E	Tendering & Selection	7	0%	$432.99	01-Dec-22	07-Dec-22
P03-E	Contract Effectiveness / PO	5	0%	$649.49	08-Dec-22	12-Dec-22
P03-E	Manufacturing / Fabrication / Supply	70	0%	$5,412.42	13-Dec-22	20-Feb-23
P03-E	Final Inspection	7	0%	$1,082.48	21-Feb-23	27-Feb-23
P03-E	Delivery On Site	7	0%	$2,164.97	28-Feb-23	06-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$541.24	07-Mar-23	11-Mar-23
P03-E	Delivering Spare Parts	5	0%	$541.24	12-Mar-23	16-Mar-23
Tray/Ladder and Accessories - W046S		131	0%	$1,899.10	21-Jul-22	28-Nov-22
P03-E	Tendering & Selection	7	0%	$75.96	21-Jul-22	27-Jul-22
P03-E	Contract Effectiveness / PO	5	0%	$113.95	28-Jul-22	01-Aug-22
P03-E	Manufacturing / Fabrication / Supply	100	0%	$949.55	02-Aug-22	09-Nov-22
P03-E	Final Inspection	7	0%	$189.91	10-Nov-22	16-Nov-22
P03-E	Delivery On Site	7	0%	$474.77	17-Nov-22	23-Nov-22
P03-E	Submitting Vendor Data Book	5	0%	$94.95	24-Nov-22	28-Nov-22
Power & Control Cables - W046S		131	0%	$12,913.85	06-Dec-22	15-Apr-23
P03-E	Tendering & Selection	7	0%	$516.55	06-Dec-22	12-Dec-22
P03-E	Contract Effectiveness / PO	5	0%	$774.83	13-Dec-22	17-Dec-22
P03-E	Manufacturing / Fabrication / Supply	100	0%	$6,456.92	18-Dec-22	27-Mar-23
P03-E	Final Inspection	7	0%	$1,291.38	28-Mar-23	03-Apr-23
P03-E	Delivery On Site	7	0%	$3,228.46	04-Apr-23	10-Apr-23
P03-E	Submitting Vendor Data Book	5	0%	$645.69	11-Apr-23	15-Apr-23
Electrical Bulk Items - W046S		111	0%	$1,899.10	02-Jul-22	20-Oct-22
P03-E	Tendering & Selection	7	0%	$75.96	02-Jul-22	08-Jul-22
P03-E	Contract Effectiveness / PO	5	0%	$113.95	09-Jul-22	13-Jul-22
P03-E	Manufacturing / Fabrication / Supply	80	0%	$949.55	14-Jul-22	01-Oct-22
P03-E	Final Inspection	7	0%	$189.91	02-Oct-22	08-Oct-22
P03-E	Delivery On Site	7	0%	$474.77	09-Oct-22	15-Oct-22
P03-E	Submitting Vendor Data Book	5	0%	$94.95	16-Oct-22	20-Oct-22
Transmission Over head Line - W046S		171	0%	$231,955.47	02-Jun-22	19-Nov-22
P03-E	Tendering & Selection	7	0%	$9,278.22	02-Jun-22	08-Jun-22
P03-E	Contract Effectiveness / PO	5	0%	$13,917.33	09-Jun-22	13-Jun-22
P03-E	Manufacturing / Fabrication / Supply	140	0%	$115,977.74	14-Jun-22	31-Oct-22
P03-E	Final Inspection	7	0%	$23,195.55	01-Nov-22	07-Nov-22
P03-E	Delivery On Site	7	0%	$57,988.87	08-Nov-22	14-Nov-22

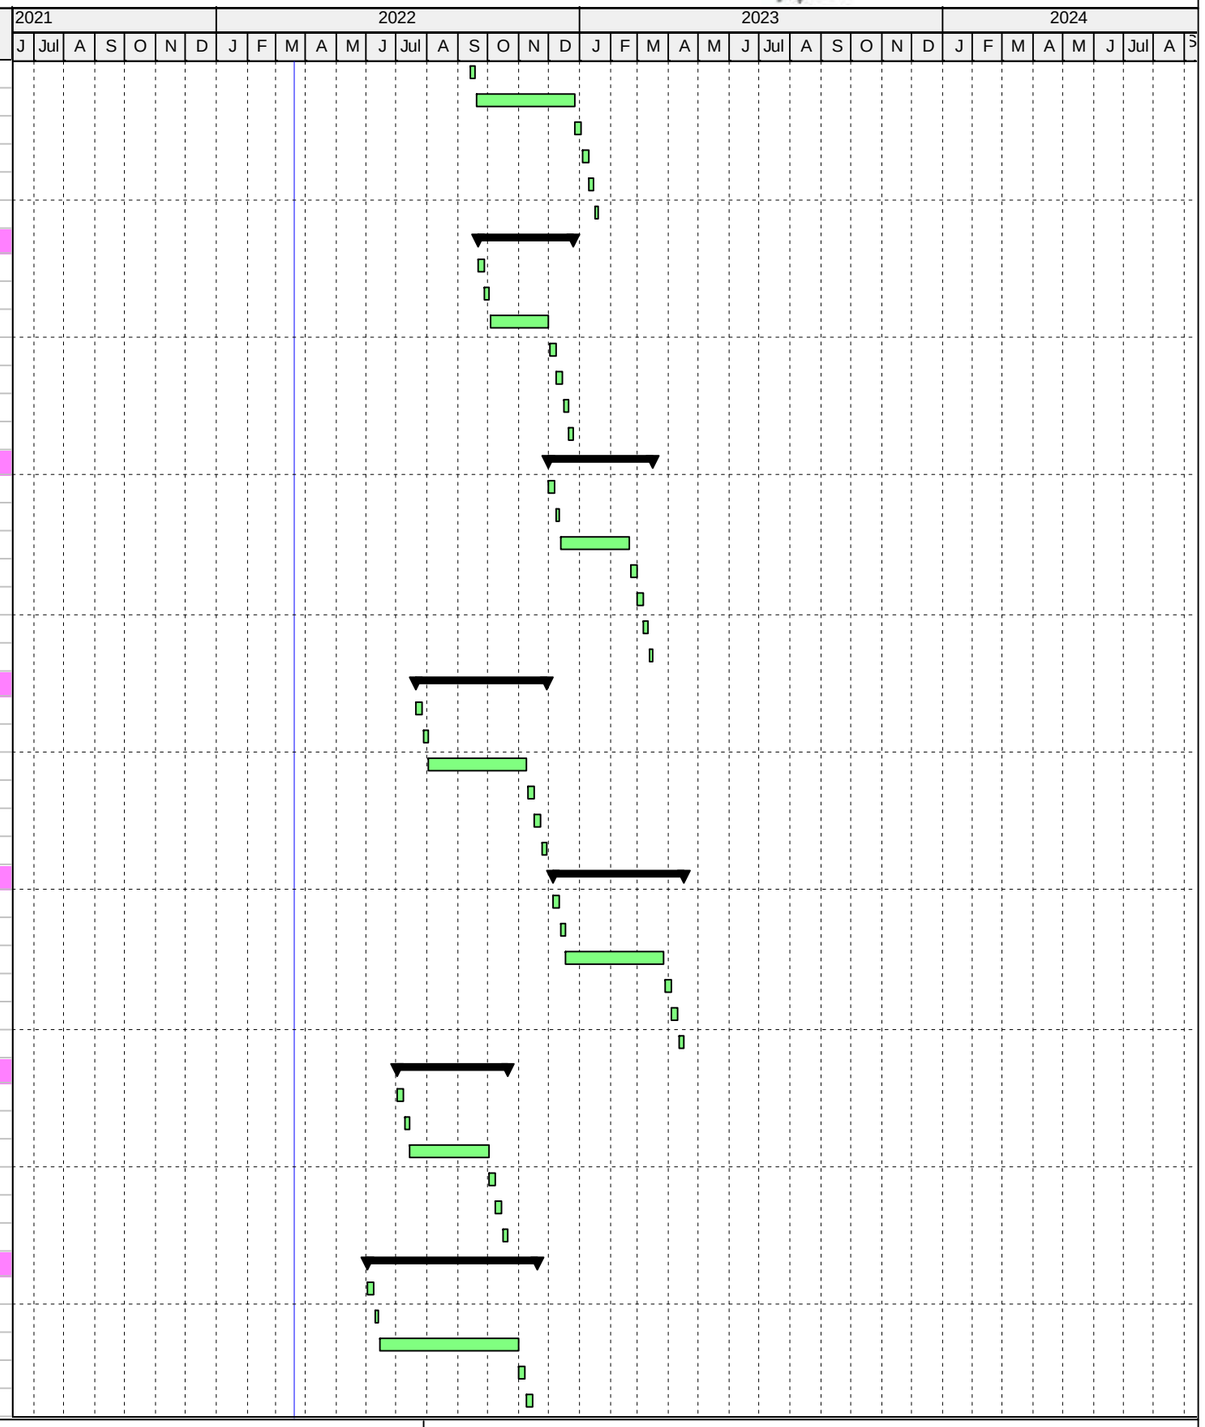


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	Submitting Vendor Data Book	5	0%	$11,597.77	15-Nov-22	19-Nov-22
Extension of Binak B/C Manifold		318	0%	$241,421.83	13-May-22	26-Mar-23
Mechanical		154	0%	$8,304.91	13-May-22	13-Oct-22
Pumps - Extension of Binak B/C Manifold		154	0%	$8,304.91	13-May-22	13-Oct-22
P03-E	Tendering & Selection	15	0%	$332.20	13-May-22	27-May-22
P03-E	Contract Effectiveness / PO	5	0%	$498.29	28-May-22	01-Jun-22
P03-E	Manufacturing / Fabrication / Supply	110	0%	$4,152.46	02-Jun-22	19-Sep-22
P03-E	Final Inspection	7	0%	$830.49	20-Sep-22	26-Sep-22
P03-E	Delivery On Site	7	0%	$1,660.98	27-Sep-22	03-Oct-22
P03-E	Submitting Vendor Data Book	5	0%	$415.25	04-Oct-22	08-Oct-22
P03-E	Delivering Spare Parts	5	0%	$415.25	09-Oct-22	13-Oct-22
Piping		301	0%	$52,678.24	16-May-22	12-Mar-23
Pipes - Extension of Binak B/C Manifold		114	0%	$21,492.72	05-Oct-22	26-Jan-23
P03-E	Tendering & Selection	10	0%	$859.71	05-Oct-22	14-Oct-22
P03-E	Contract Effectiveness / PO	5	0%	$1,289.56	15-Oct-22	19-Oct-22
P03-E	Manufacturing / Fabrication / Supply	80	0%	$10,746.36	20-Oct-22	07-Jan-23
P03-E	Final Inspection	7	0%	$2,149.27	08-Jan-23	14-Jan-23
P03-E	Delivery On Site	7	0%	$5,373.18	15-Jan-23	21-Jan-23
P03-E	Submitting Vendor Data Book	5	0%	$1,074.64	22-Jan-23	26-Jan-23
Fittings - Extension of Binak B/C Manifold		124	0%	$2,844.63	04-Nov-22	07-Mar-23
P03-E	Tendering & Selection	10	0%	$113.79	04-Nov-22	13-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$170.68	14-Nov-22	18-Nov-22
P03-E	Manufacturing / Fabrication / Supply	90	0%	$1,422.31	19-Nov-22	16-Feb-23
P03-E	Final Inspection	7	0%	$284.46	17-Feb-23	23-Feb-23
P03-E	Delivery On Site	7	0%	$711.16	24-Feb-23	02-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$142.23	03-Mar-23	07-Mar-23
Flanges - Extension of Binak B/C Manifold		124	0%	$2,844.63	04-Nov-22	07-Mar-23
P03-E	Tendering & Selection	10	0%	$113.79	04-Nov-22	13-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$170.68	14-Nov-22	18-Nov-22
P03-E	Manufacturing / Fabrication / Supply	90	0%	$1,422.31	19-Nov-22	16-Feb-23
P03-E	Final Inspection	7	0%	$284.46	17-Feb-23	23-Feb-23
P03-E	Delivery On Site	7	0%	$711.16	24-Feb-23	02-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$142.23	03-Mar-23	07-Mar-23
Manual Valves - Extension of Binak B/C Manifold		129	0%	$12,642.78	04-Nov-22	12-Mar-23
P03-E	Tendering & Selection	10	0%	$505.71	04-Nov-22	13-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$758.57	14-Nov-22	18-Nov-22
P03-E	Manufacturing / Fabrication / Supply	90	0%	$6,321.39	19-Nov-22	16-Feb-23
P03-E	Final Inspection	7	0%	$1,264.28	17-Feb-23	23-Feb-23
P03-E	Delivery On Site	7	0%	$2,528.56	24-Feb-23	02-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$632.14	03-Mar-23	07-Mar-23
P03-E	Delivering Spare Parts	5	0%	$632.14	08-Mar-23	12-Mar-23
Gaskets - Extension of Binak B/C Manifold		124	0%	$3,424.09	04-Nov-22	07-Mar-23
P03-E	Tendering & Selection	10	0%	$136.96	04-Nov-22	13-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$205.45	14-Nov-22	18-Nov-22
P03-E	Manufacturing / Fabrication / Supply	90	0%	$1,712.04	19-Nov-22	16-Feb-23
P03-E	Final Inspection	7	0%	$342.41	17-Feb-23	23-Feb-23
P03-E	Delivery On Site	7	0%	$856.02	24-Feb-23	02-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$171.20	03-Mar-23	07-Mar-23
Bolt/Nuts - Extension of Binak B/C Manifold		114	0%	$5,267.82	04-Nov-22	25-Feb-23

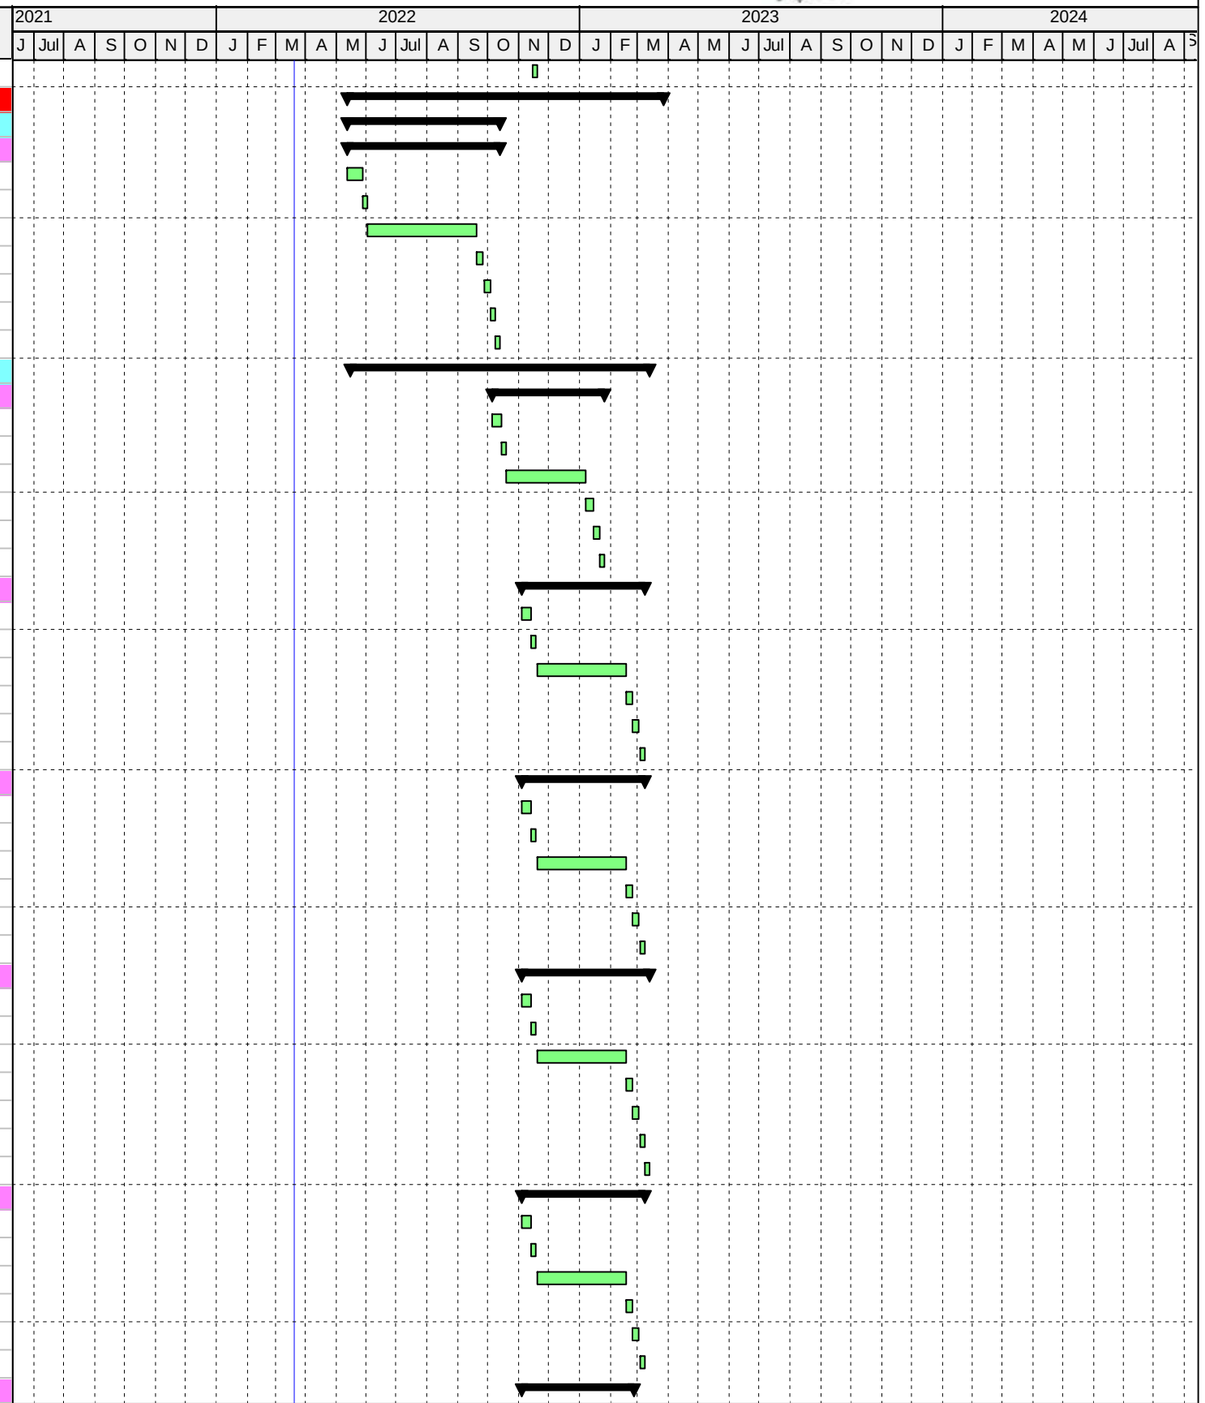


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	Tendering & Selection	10	0%	$210.71	04-Nov-22	13-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$316.07	14-Nov-22	18-Nov-22
P03-E	Manufacturing / Fabrication / Supply	80	0%	$2,633.91	19-Nov-22	06-Feb-23
P03-E	Final Inspection	7	0%	$526.78	07-Feb-23	13-Feb-23
P03-E	Delivery On Site	7	0%	$1,316.96	14-Feb-23	20-Feb-23
P03-E	Submitting Vendor Data Book	5	0%	$263.39	21-Feb-23	25-Feb-23
Sampling Connection Set - Extension of Binak B/C Manifold		94	0%	$2,844.63	16-May-22	17-Aug-22
P03-E	Tendering & Selection	10	0%	$113.79	16-May-22	25-May-22
P03-E	Contract Effectiveness / PO	5	0%	$170.68	26-May-22	30-May-22
P03-E	Manufacturing / Fabrication / Supply	60	0%	$1,422.31	31-May-22	29-Jul-22
P03-E	Final Inspection	7	0%	$284.46	30-Jul-22	05-Aug-22
P03-E	Delivery On Site	7	0%	$711.16	06-Aug-22	12-Aug-22
P03-E	Submitting Vendor Data Book	5	0%	$142.23	13-Aug-22	17-Aug-22
Stone Trap - Extension of Binak B/C Manifold		94	0%	$1,316.96	07-Oct-22	08-Jan-23
P03-E	Tendering & Selection	10	0%	$52.68	07-Oct-22	16-Oct-22
P03-E	Contract Effectiveness / PO	5	0%	$79.02	17-Oct-22	21-Oct-22
P03-E	Manufacturing / Fabrication / Supply	60	0%	$658.48	22-Oct-22	20-Dec-22
P03-E	Final Inspection	7	0%	$131.70	21-Dec-22	27-Dec-22
P03-E	Delivery On Site	7	0%	$329.24	28-Dec-22	03-Jan-23
P03-E	Submitting Vendor Data Book	5	0%	$65.85	04-Jan-23	08-Jan-23
Control & Instrumentation		317	0%	$133,023.43	14-May-22	26-Mar-23
Control System/Console/Furniture		169	0%	$54,539.61	21-May-22	05-Nov-22
P03-E	Tendering & Selection	20	0%	$2,181.58	21-May-22	09-Jun-22
P03-E	Contract Effectiveness / PO	5	0%	$3,272.38	10-Jun-22	14-Jun-22
P03-E	Manufacturing / Fabrication / Supply	120	0%	$27,269.80	15-Jun-22	12-Oct-22
P03-E	Final Inspection	7	0%	$5,453.96	13-Oct-22	19-Oct-22
P03-E	Delivery On Site	7	0%	$10,907.92	20-Oct-22	26-Oct-22
P03-E	Submitting Vendor Data Book	5	0%	$2,726.98	27-Oct-22	31-Oct-22
P03-E	Delivering Spare Parts	5	0%	$2,726.98	01-Nov-22	05-Nov-22
ESD System		169	0%	$38,576.79	05-Jun-22	20-Nov-22
P03-E	Tendering & Selection	20	0%	$1,543.07	05-Jun-22	24-Jun-22
P03-E	Contract Effectiveness / PO	5	0%	$2,314.61	25-Jun-22	29-Jun-22
P03-E	Manufacturing / Fabrication / Supply	120	0%	$19,288.40	30-Jun-22	27-Oct-22
P03-E	Final Inspection	7	0%	$3,857.68	28-Oct-22	03-Nov-22
P03-E	Delivery On Site	7	0%	$7,715.36	04-Nov-22	10-Nov-22
P03-E	Submitting Vendor Data Book	5	0%	$1,928.84	11-Nov-22	15-Nov-22
P03-E	Delivering Spare Parts	5	0%	$1,928.84	16-Nov-22	20-Nov-22
F&G System		169	0%	$26,604.69	05-Jun-22	20-Nov-22
P03-E	Tendering & Selection	20	0%	$1,064.19	05-Jun-22	24-Jun-22
P03-E	Contract Effectiveness / PO	5	0%	$1,596.28	25-Jun-22	29-Jun-22
P03-E	Manufacturing / Fabrication / Supply	120	0%	$13,302.34	30-Jun-22	27-Oct-22
P03-E	Final Inspection	7	0%	$2,660.47	28-Oct-22	03-Nov-22
P03-E	Delivery On Site	7	0%	$5,320.94	04-Nov-22	10-Nov-22
P03-E	Submitting Vendor Data Book	5	0%	$1,330.23	11-Nov-22	15-Nov-22
P03-E	Delivering Spare Parts	5	0%	$1,330.23	16-Nov-22	20-Nov-22
ON/OFF & Shutdown Valves		149	0%	$1,463.26	02-Jun-22	28-Oct-22
P03-E	Tendering & Selection	20	0%	$58.53	02-Jun-22	21-Jun-22
P03-E	Contract Effectiveness / PO	5	0%	$87.80	22-Jun-22	26-Jun-22
P03-E	Manufacturing / Fabrication / Supply	100	0%	$731.63	27-Jun-22	04-Oct-22

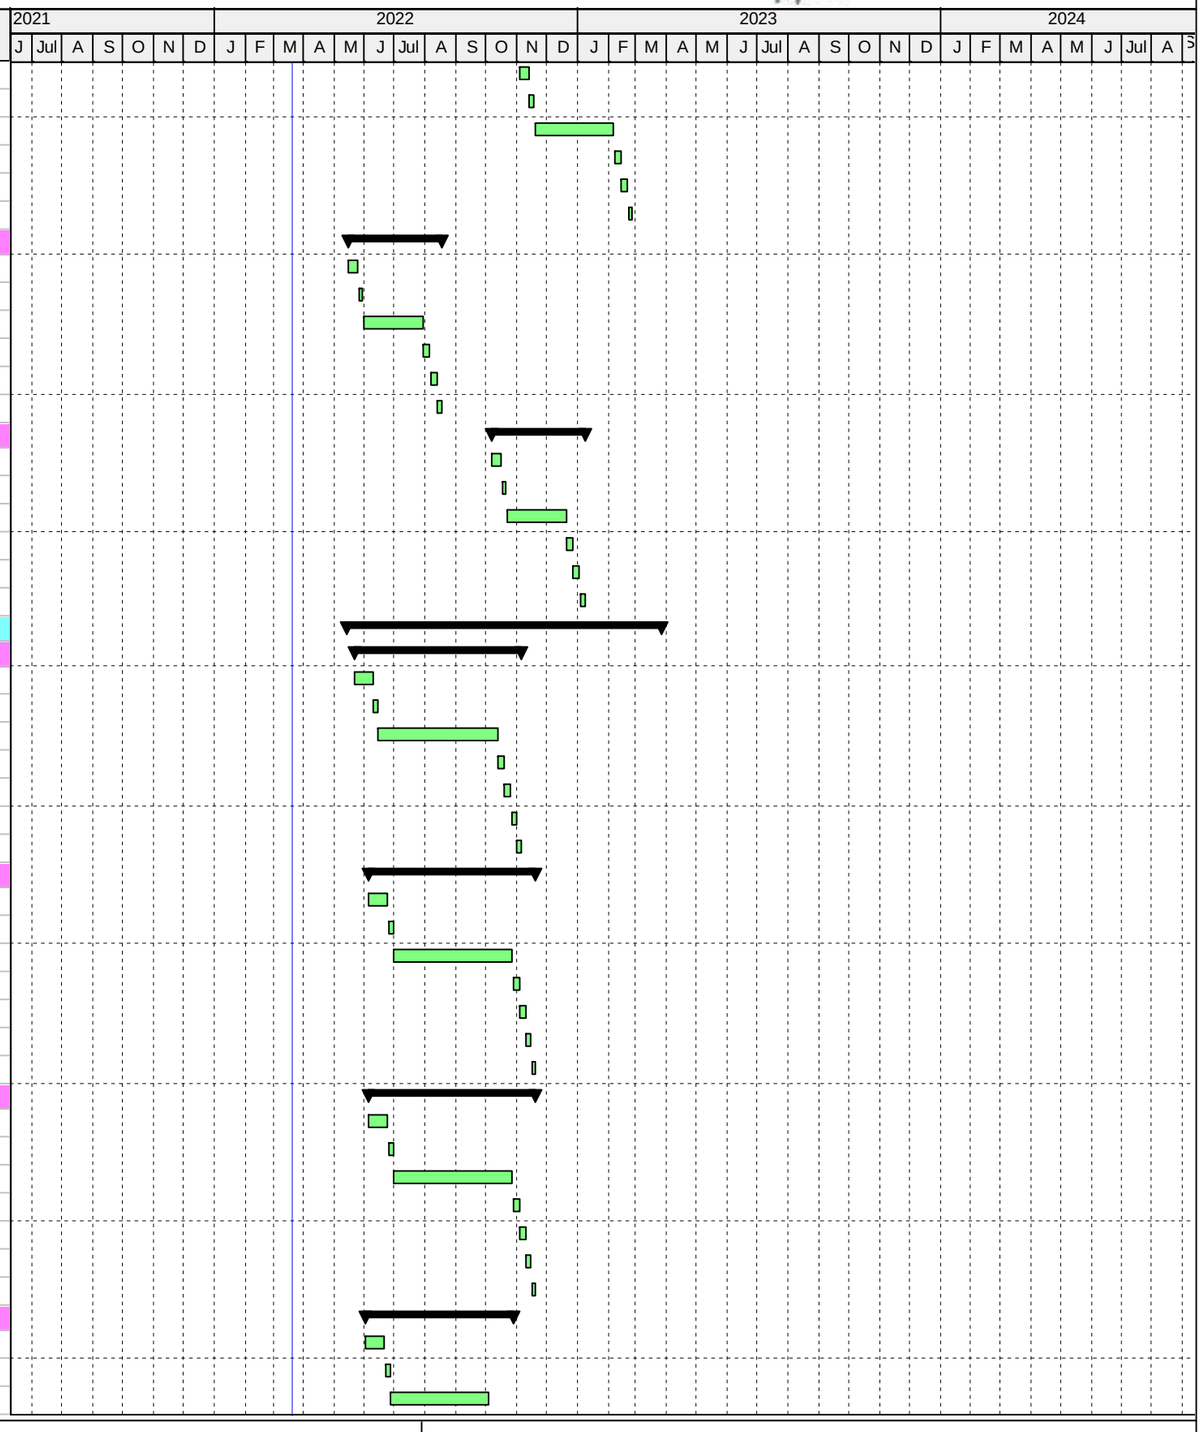


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	Final Inspection	7	0%	$146.33	05-Oct-22	11-Oct-22
P03-E	Delivery On Site	7	0%	$292.65	12-Oct-22	18-Oct-22
P03-E	Submitting Vendor Data Book	5	0%	$73.16	19-Oct-22	23-Oct-22
P03-E	Delivering Spare Parts	5	0%	$73.16	24-Oct-22	28-Oct-22
Control Valves		144	0%	$1,463.26	04-Jul-22	24-Nov-22
P03-E	Tendering & Selection	15	0%	$58.53	04-Jul-22	18-Jul-22
P03-E	Contract Effectiveness / PO	5	0%	$87.80	19-Jul-22	23-Jul-22
P03-E	Manufacturing / Fabrication / Supply	100	0%	$731.63	24-Jul-22	31-Oct-22
P03-E	Final Inspection	7	0%	$146.33	01-Nov-22	07-Nov-22
P03-E	Delivery On Site	7	0%	$292.65	08-Nov-22	14-Nov-22
P03-E	Submitting Vendor Data Book	5	0%	$73.16	15-Nov-22	19-Nov-22
P03-E	Delivering Spare Parts	5	0%	$73.16	20-Nov-22	24-Nov-22
Pressure Safety Valves (PSV)		144	0%	$1,463.26	15-Jul-22	05-Dec-22
P03-E	Tendering & Selection	15	0%	$58.53	15-Jul-22	29-Jul-22
P03-E	Contract Effectiveness / PO	5	0%	$87.80	30-Jul-22	03-Aug-22
P03-E	Manufacturing / Fabrication / Supply	100	0%	$731.63	04-Aug-22	11-Nov-22
P03-E	Final Inspection	7	0%	$146.33	12-Nov-22	18-Nov-22
P03-E	Delivery On Site	7	0%	$292.65	19-Nov-22	25-Nov-22
P03-E	Submitting Vendor Data Book	5	0%	$73.16	26-Nov-22	30-Nov-22
P03-E	Delivering Spare Parts	5	0%	$73.16	01-Dec-22	05-Dec-22
F&G Devices		154	0%	$1,263.72	04-Aug-22	04-Jan-23
P03-E	Tendering & Selection	15	0%	$50.55	04-Aug-22	18-Aug-22
P03-E	Contract Effectiveness / PO	5	0%	$75.82	19-Aug-22	23-Aug-22
P03-E	Manufacturing / Fabrication / Supply	110	0%	$631.86	24-Aug-22	11-Dec-22
P03-E	Final Inspection	7	0%	$126.37	12-Dec-22	18-Dec-22
P03-E	Delivery On Site	7	0%	$252.74	19-Dec-22	25-Dec-22
P03-E	Submitting Vendor Data Book	5	0%	$63.19	26-Dec-22	30-Dec-22
P03-E	Delivering Spare Parts	5	0%	$63.19	31-Dec-22	04-Jan-23
Orifice and Restriction Orifice Plate		159	0%	$545.40	25-May-22	30-Oct-22
P03-E	Tendering & Selection	15	0%	$21.82	25-May-22	08-Jun-22
P03-E	Contract Effectiveness / PO	5	0%	$32.72	09-Jun-22	13-Jun-22
P03-E	Manufacturing / Fabrication / Supply	110	0%	$272.70	14-Jun-22	01-Oct-22
P03-E	Final Inspection	12	0%	$54.54	02-Oct-22	13-Oct-22
P03-E	Delivery On Site	7	0%	$109.08	14-Oct-22	20-Oct-22
P03-E	Submitting Vendor Data Book	5	0%	$27.27	21-Oct-22	25-Oct-22
P03-E	Delivering Spare Parts	5	0%	$27.27	26-Oct-22	30-Oct-22
Corrosion Coupon/Probe		159	0%	$545.40	21-May-22	26-Oct-22
P03-E	Tendering & Selection	15	0%	$21.82	21-May-22	04-Jun-22
P03-E	Contract Effectiveness / PO	5	0%	$32.72	05-Jun-22	09-Jun-22
P03-E	Manufacturing / Fabrication / Supply	110	0%	$272.70	10-Jun-22	27-Sep-22
P03-E	Final Inspection	12	0%	$54.54	28-Sep-22	09-Oct-22
P03-E	Delivery On Site	7	0%	$109.08	10-Oct-22	16-Oct-22
P03-E	Submitting Vendor Data Book	5	0%	$27.27	17-Oct-22	21-Oct-22
P03-E	Delivering Spare Parts	5	0%	$27.27	22-Oct-22	26-Oct-22
Pressure Transmitter		159	0%	$731.63	03-Jul-22	08-Dec-22
P03-E	Tendering & Selection	15	0%	$29.27	03-Jul-22	17-Jul-22
P03-E	Contract Effectiveness / PO	5	0%	$43.90	18-Jul-22	22-Jul-22
P03-E	Manufacturing / Fabrication / Supply	110	0%	$365.81	23-Jul-22	09-Nov-22
P03-E	Final Inspection	12	0%	$73.16	10-Nov-22	21-Nov-22

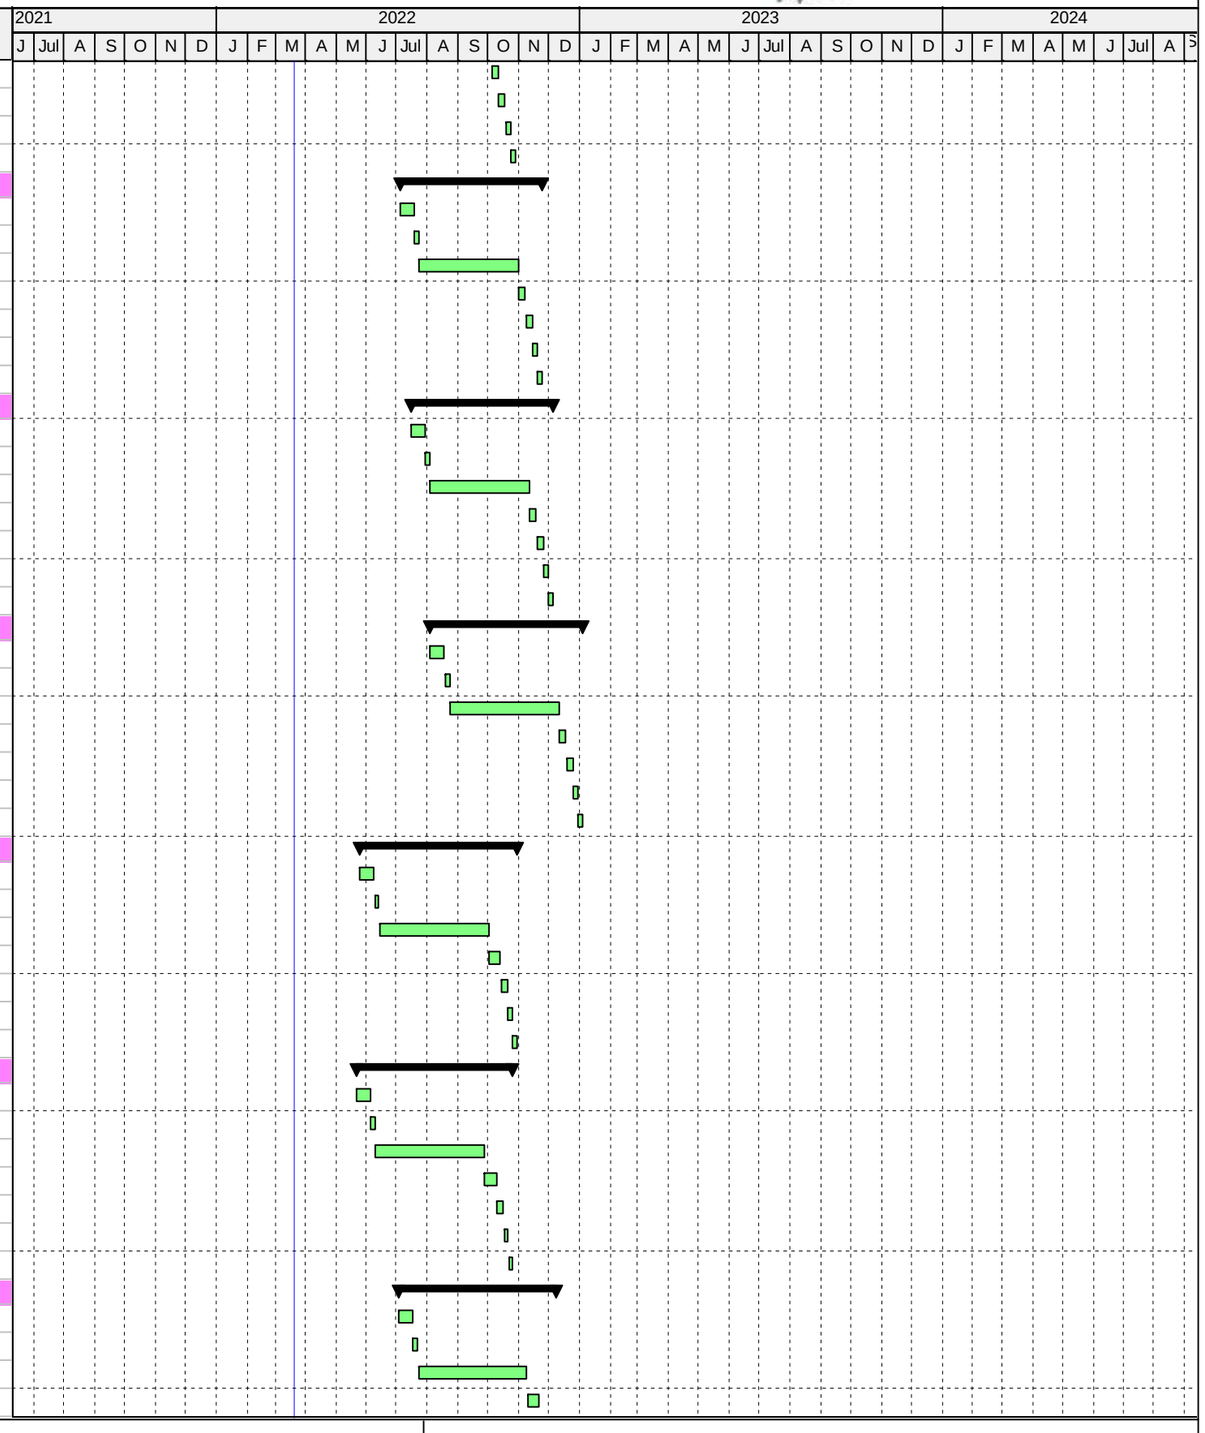


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	Delivery On Site	7	0%	$146.33	22-Nov-22	28-Nov-22
P03-E	Submitting Vendor Data Book	5	0%	$36.58	29-Nov-22	03-Dec-22
P03-E	Delivering Spare Parts	5	0%	$36.58	04-Dec-22	08-Dec-22
Flow Transmitter/ Diff. Pressure Transmitter		159	0%	$731.63	14-May-22	19-Oct-22
P03-E	Tendering & Selection	15	0%	$29.27	14-May-22	28-May-22
P03-E	Contract Effectiveness / PO	5	0%	$43.90	29-May-22	02-Jun-22
P03-E	Manufacturing / Fabrication / Supply	110	0%	$365.81	03-Jun-22	20-Sep-22
P03-E	Final Inspection	12	0%	$73.16	21-Sep-22	02-Oct-22
P03-E	Delivery On Site	7	0%	$146.33	03-Oct-22	09-Oct-22
P03-E	Submitting Vendor Data Book	5	0%	$36.58	10-Oct-22	14-Oct-22
P03-E	Delivering Spare Parts	5	0%	$36.58	15-Oct-22	19-Oct-22
Instrument/F&G Cable		129	0%	$904.56	08-Nov-22	16-Mar-23
P03-E	Tendering & Selection	15	0%	$36.18	08-Nov-22	22-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$54.27	23-Nov-22	27-Nov-22
P03-E	Manufacturing / Fabrication / Supply	90	0%	$452.28	28-Nov-22	25-Feb-23
P03-E	Final Inspection	7	0%	$90.46	26-Feb-23	04-Mar-23
P03-E	Delivery On Site	7	0%	$226.14	05-Mar-23	11-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$45.23	12-Mar-23	16-Mar-23
Instrument/F&G Junction box and Gland		144	0%	$731.63	03-Nov-22	26-Mar-23
P03-E	Tendering & Selection	15	0%	$29.27	03-Nov-22	17-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$43.90	18-Nov-22	22-Nov-22
P03-E	Manufacturing / Fabrication / Supply	100	0%	$365.81	23-Nov-22	02-Mar-23
P03-E	Final Inspection	12	0%	$73.16	03-Mar-23	14-Mar-23
P03-E	Delivery On Site	7	0%	$182.91	15-Mar-23	21-Mar-23
P03-E	Submitting Vendor Data Book	5	0%	$36.58	22-Mar-23	26-Mar-23
Instrument Installation Accessories		139	0%	$545.40	30-Sep-22	15-Feb-23
P03-E	Tendering & Selection	15	0%	$21.82	30-Sep-22	14-Oct-22
P03-E	Contract Effectiveness / PO	5	0%	$32.72	15-Oct-22	19-Oct-22
P03-E	Manufacturing / Fabrication / Supply	100	0%	$272.70	20-Oct-22	27-Jan-23
P03-E	Final Inspection	7	0%	$54.54	28-Jan-23	03-Feb-23
P03-E	Delivery On Site	7	0%	$136.35	04-Feb-23	10-Feb-23
P03-E	Submitting Vendor Data Book	5	0%	$27.27	11-Feb-23	15-Feb-23
Differential Pressure/Pressure Gauge		149	0%	$731.63	14-May-22	09-Oct-22
P03-E	Tendering & Selection	15	0%	$29.27	14-May-22	28-May-22
P03-E	Contract Effectiveness / PO	5	0%	$43.90	29-May-22	02-Jun-22
P03-E	Manufacturing / Fabrication / Supply	100	0%	$365.81	03-Jun-22	10-Sep-22
P03-E	Final Inspection	12	0%	$73.16	11-Sep-22	22-Sep-22
P03-E	Delivery On Site	7	0%	$146.33	23-Sep-22	29-Sep-22
P03-E	Submitting Vendor Data Book	5	0%	$36.58	30-Sep-22	04-Oct-22
P03-E	Delivering Spare Parts	5	0%	$36.58	05-Oct-22	09-Oct-22
Temperature Gauge		149	0%	$731.63	07-Jun-22	02-Nov-22
P03-E	Tendering & Selection	15	0%	$29.27	07-Jun-22	21-Jun-22
P03-E	Contract Effectiveness / PO	5	0%	$43.90	22-Jun-22	26-Jun-22
P03-E	Manufacturing / Fabrication / Supply	100	0%	$365.81	27-Jun-22	04-Oct-22
P03-E	Final Inspection	12	0%	$73.16	05-Oct-22	16-Oct-22
P03-E	Delivery On Site	7	0%	$146.33	17-Oct-22	23-Oct-22
P03-E	Submitting Vendor Data Book	5	0%	$36.58	24-Oct-22	28-Oct-22
P03-E	Delivering Spare Parts	5	0%	$36.58	29-Oct-22	02-Nov-22
Instrument Tube and Fitting		129	0%	$904.56	07-Jul-22	12-Nov-22

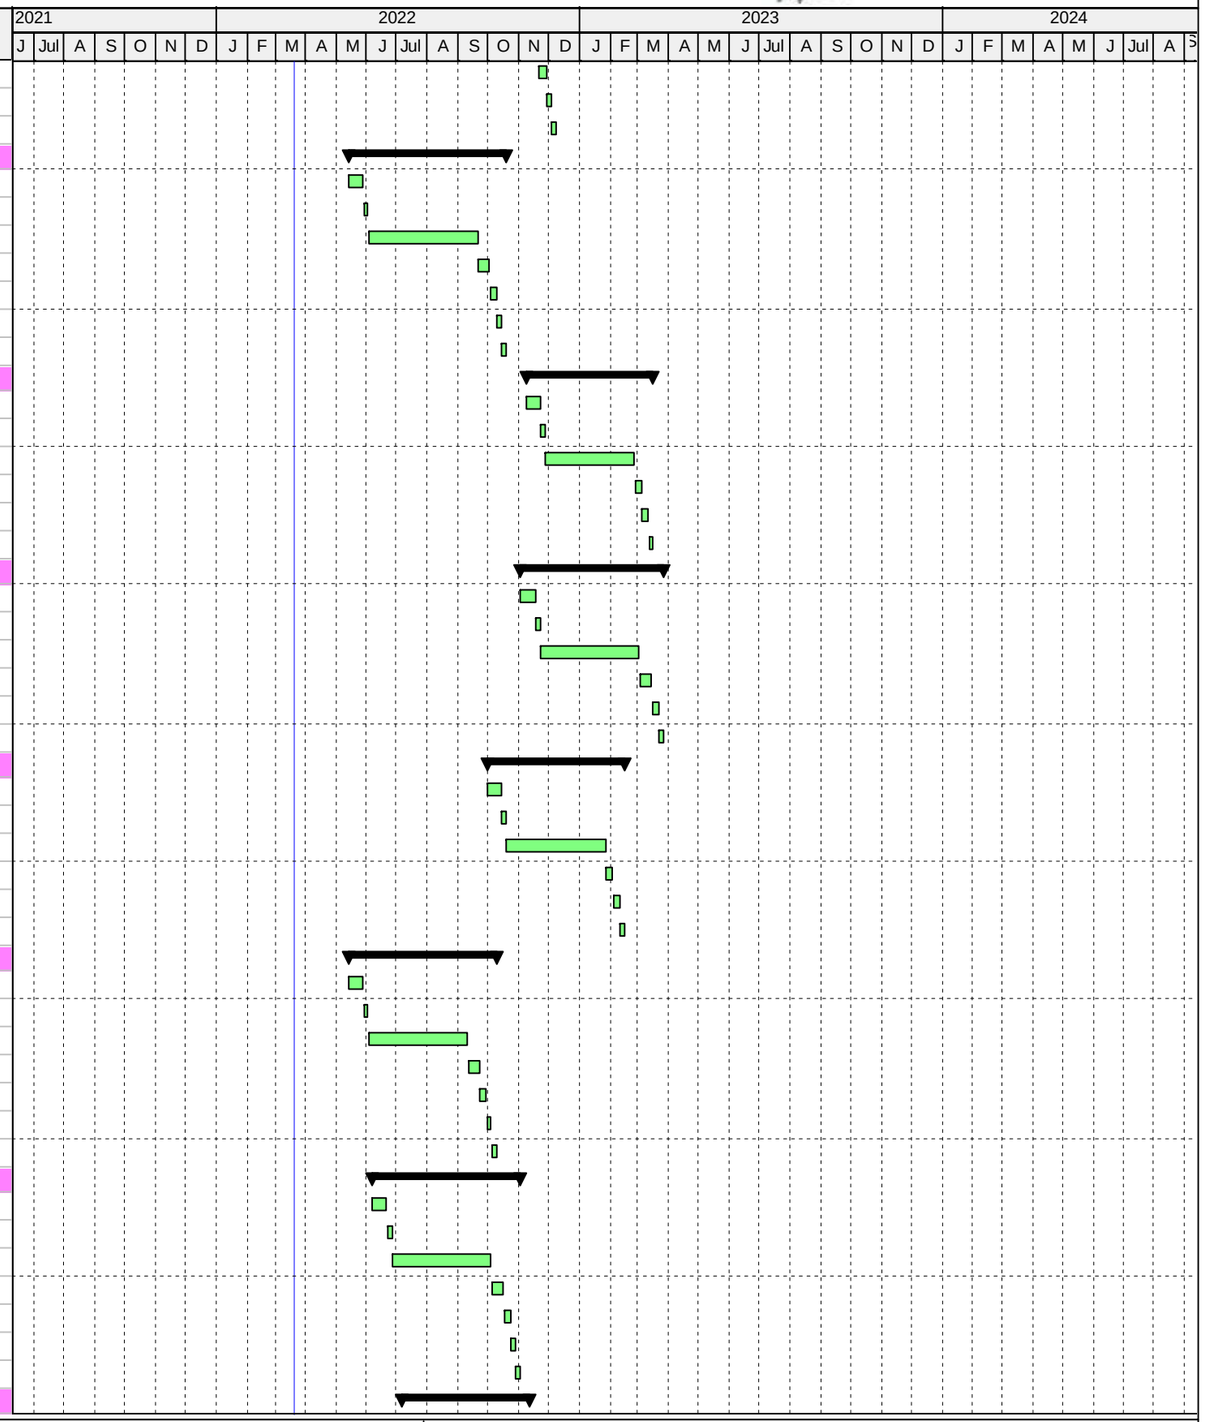


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	Tendering & Selection	10	0%	$36.18	07-Jul-22	16-Jul-22
P03-E	Contract Effectiveness / PO	5	0%	$54.27	17-Jul-22	21-Jul-22
P03-E	Manufacturing / Fabrication / Supply	90	0%	$452.28	22-Jul-22	19-Oct-22
P03-E	Final Inspection	12	0%	$90.46	20-Oct-22	31-Oct-22
P03-E	Delivery On Site	7	0%	$226.14	01-Nov-22	07-Nov-22
P03-E	Submitting Vendor Data Book	5	0%	$45.23	08-Nov-22	12-Nov-22
Instrument Cable Tray		134	0%	$545.40	30-Sep-22	10-Feb-23
P03-E	Tendering & Selection	15	0%	$21.82	30-Sep-22	14-Oct-22
P03-E	Contract Effectiveness / PO	5	0%	$32.72	15-Oct-22	19-Oct-22
P03-E	Manufacturing / Fabrication / Supply	90	0%	$272.70	20-Oct-22	17-Jan-23
P03-E	Final Inspection	12	0%	$54.54	18-Jan-23	29-Jan-23
P03-E	Delivery On Site	7	0%	$136.35	30-Jan-23	05-Feb-23
P03-E	Submitting Vendor Data Book	5	0%	$27.27	06-Feb-23	10-Feb-23
Safety & Fire Fighting		121	0%	$2,631.50	03-Sep-22	01-Jan-23
Fire Fighting and Safety Equipment - Extension of Binak B/C Ma		79	0%	$1,960.73	03-Sep-22	20-Nov-22
P03-E	Tendering & Selection	30	0%	$78.43	03-Sep-22	02-Oct-22
P03-E	Contract Effectiveness / PO	5	0%	$117.64	03-Oct-22	07-Oct-22
P03-E	Manufacturing / Fabrication / Supply	20	0%	$980.36	08-Oct-22	27-Oct-22
P03-E	Final Inspection	12	0%	$196.07	28-Oct-22	08-Nov-22
P03-E	Delivery On Site	7	0%	$490.18	09-Nov-22	15-Nov-22
P03-E	Submitting Vendor Data Book	5	0%	$98.04	16-Nov-22	20-Nov-22
Fire Safety Sign - Extension of Binak B/C Manifold		79	0%	$670.77	15-Oct-22	01-Jan-23
P03-E	Tendering & Selection	30	0%	$26.83	15-Oct-22	13-Nov-22
P03-E	Contract Effectiveness / PO	5	0%	$40.25	14-Nov-22	18-Nov-22
P03-E	Manufacturing / Fabrication / Supply	20	0%	$335.38	19-Nov-22	08-Dec-22
P03-E	Final Inspection	12	0%	$67.08	09-Dec-22	20-Dec-22
P03-E	Delivery On Site	7	0%	$167.69	21-Dec-22	27-Dec-22
P03-E	Submitting Vendor Data Book	5	0%	$33.54	28-Dec-22	01-Jan-23
Electrical		253	0%	$44,783.75	05-Jun-22	12-Feb-23
UPS System - Extension of Binak B/C Manifold		154	0%	$17,962.76	12-Sep-22	12-Feb-23
P03-E	Tendering & Selection	15	0%	$718.51	12-Sep-22	26-Sep-22
P03-E	Contract Effectiveness / PO	5	0%	$1,077.77	27-Sep-22	01-Oct-22
P03-E	Manufacturing / Fabrication / Supply	110	0%	$8,981.38	02-Oct-22	19-Jan-23
P03-E	Final Inspection	7	0%	$1,796.28	20-Jan-23	26-Jan-23
P03-E	Delivery On Site	7	0%	$3,592.55	27-Jan-23	02-Feb-23
P03-E	Submitting Vendor Data Book	5	0%	$898.14	03-Feb-23	07-Feb-23
P03-E	Delivering Spare Parts	5	0%	$898.14	08-Feb-23	12-Feb-23
LV Switchgear & MCC - Extension of Binak B/C Manifold		149	0%	$7,187.79	05-Jun-22	31-Oct-22
P03-E	Tendering & Selection	15	0%	$287.51	05-Jun-22	19-Jun-22
P03-E	Contract Effectiveness / PO	5	0%	$431.27	20-Jun-22	24-Jun-22
P03-E	Manufacturing / Fabrication / Supply	100	0%	$3,593.90	25-Jun-22	02-Oct-22
P03-E	Final Inspection	7	0%	$718.78	13-Oct-22	19-Oct-22
P03-E	Delivery On Site	7	0%	$1,437.56	20-Oct-22	26-Oct-22
P03-E	Submitting Vendor Data Book	5	0%	$359.39	27-Oct-22	31-Oct-22
P03-E	Delivering Spare Parts	5	0%	$359.39	27-Oct-22	31-Oct-22
DC Charger - Extension of Binak B/C Manifold		154	0%	$11,970.70	05-Jun-22	05-Nov-22
P03-E	Tendering & Selection	15	0%	$478.83	05-Jun-22	19-Jun-22
P03-E	Contract Effectiveness / PO	5	0%	$718.24	20-Jun-22	24-Jun-22
P03-E	Manufacturing / Fabrication / Supply	100	0%	$5,985.35	25-Jun-22	02-Oct-22

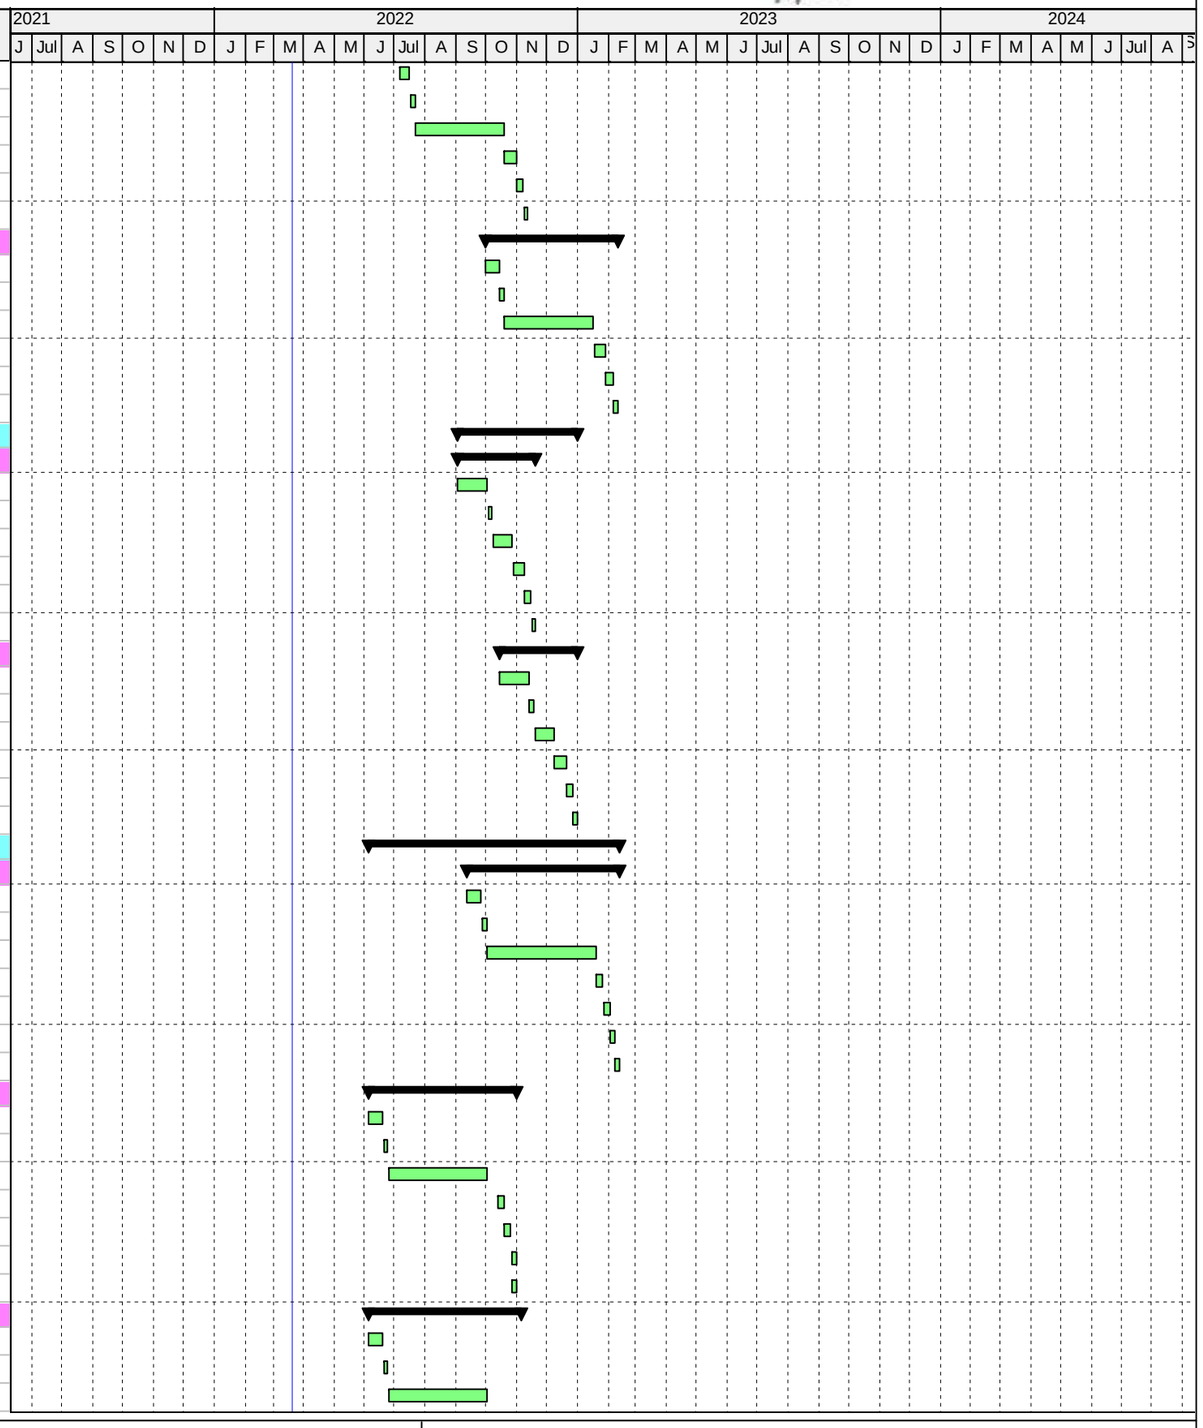


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-E	Final Inspection	7	0%	$1,197.07	13-Oct-22	19-Oct-22
P03-E	Delivery On Site	7	0%	$2,394.14	20-Oct-22	26-Oct-22
P03-E	Submitting Vendor Data Book	5	0%	$598.53	27-Oct-22	31-Oct-22
P03-E	Delivering Spare Parts	5	0%	$598.53	01-Nov-22	05-Nov-22
Earthing & Lightning System - Extension of Binak B/C Manifold		154	0%	$1,195.73	11-Sep-22	11-Feb-23
P03-E	Tendering & Selection	15	0%	$47.83	11-Sep-22	25-Sep-22
P03-E	Contract Effectiveness / PO	5	0%	$71.74	26-Sep-22	30-Sep-22
P03-E	Manufacturing / Fabrication / Supply	110	0%	$597.86	01-Oct-22	18-Jan-23
P03-E	Final Inspection	7	0%	$119.57	19-Jan-23	25-Jan-23
P03-E	Delivery On Site	7	0%	$239.15	26-Jan-23	01-Feb-23
P03-E	Submitting Vendor Data Book	5	0%	$59.79	02-Feb-23	06-Feb-23
P03-E	Delivering Spare Parts	5	0%	$59.79	07-Feb-23	11-Feb-23
Power & Control Cables - Extension of Binak B/C Manifold		154	0%	$2,395.93	07-Jun-22	07-Nov-22
P03-E	Tendering & Selection	15	0%	$95.84	07-Jun-22	21-Jun-22
P03-E	Contract Effectiveness / PO	5	0%	$143.76	22-Jun-22	26-Jun-22
P03-E	Manufacturing / Fabrication / Supply	60	0%	$1,197.97	27-Jun-22	25-Aug-22
P03-E	Final Inspection	7	0%	$239.59	15-Oct-22	21-Oct-22
P03-E	Delivery On Site	7	0%	$598.98	27-Oct-22	02-Nov-22
P03-E	Submitting Vendor Data Book	5	0%	$119.80	03-Nov-22	07-Nov-22
Tray/Ladder and Accessories		99	0%	$1,630.13	01-Aug-22	07-Nov-22
P03-E	Tendering & Selection	15	0%	$65.21	01-Aug-22	15-Aug-22
P03-E	Contract Effectiveness / PO	5	0%	$97.81	16-Aug-22	20-Aug-22
P03-E	Manufacturing / Fabrication / Supply	60	0%	$815.06	21-Aug-22	19-Oct-22
P03-E	Final Inspection	7	0%	$163.01	20-Oct-22	26-Oct-22
P03-E	Delivery On Site	7	0%	$407.53	27-Oct-22	02-Nov-22
P03-E	Submitting Vendor Data Book	5	0%	$81.51	03-Nov-22	07-Nov-22
Electrical Bulk Items		154	0%	$2,440.71	07-Jun-22	07-Nov-22
P03-E	Tendering & Selection	15	0%	$97.63	07-Jun-22	21-Jun-22
P03-E	Contract Effectiveness / PO	5	0%	$146.44	22-Jun-22	26-Jun-22
P03-E	Manufacturing / Fabrication / Supply	110	0%	$1,220.36	27-Jun-22	14-Oct-22
P03-E	Final Inspection	12	0%	$244.07	15-Oct-22	26-Oct-22
P03-E	Delivery On Site	7	0%	$610.18	27-Oct-22	02-Nov-22
P03-E	Submitting Vendor Data Book	5	0%	$122.04	03-Nov-22	07-Nov-22
Construction		372	5.05%	$802,925.00	20-Feb-22	29-Jun-23
Wellpad and Access Road		198	9.16%	$442,411.68	20-Feb-22	10-Aug-22
Access Road		163	10.8%	$88,482.34	20-Feb-22	10-Aug-22
Wellpad Access Road		163	13.5%	$70,785.87	20-Feb-22	10-Aug-22
P03-E	Access Road Preparation	20	45%	$21,235.76	20-Feb-22	13-Jul-22
P03-E	Filling and Compaction	9	0%	$10,617.88	24-Jul-22	01-Aug-22
P03-E	Sub-Base Layer	9	0%	$17,696.47	01-Aug-22	10-Aug-22
Construction of Culvert and Bridge		33	0%	$21,235.76	03-Jul-22	05-Aug-22
bridge		33	0%	$8,494.30	03-Jul-22	05-Aug-22
P03	Excavation	5	0%	$849.43	03-Jul-22	08-Jul-22
P03	lean concrete	2	0%	$679.54	08-Jul-22	10-Jul-22
P03	wall	7	0%	$1,528.97	10-Jul-22	17-Jul-22
P03	reinforcement	7	0%	$1,698.86	17-Jul-22	24-Jul-22
P03	form working	5	0%	$849.43	24-Jul-22	29-Jul-22
P03	concrete pouring	1	0%	$2,548.29	29-Jul-22	30-Jul-22
P03	protect stone	3	0%	$169.89	30-Jul-22	02-Aug-22

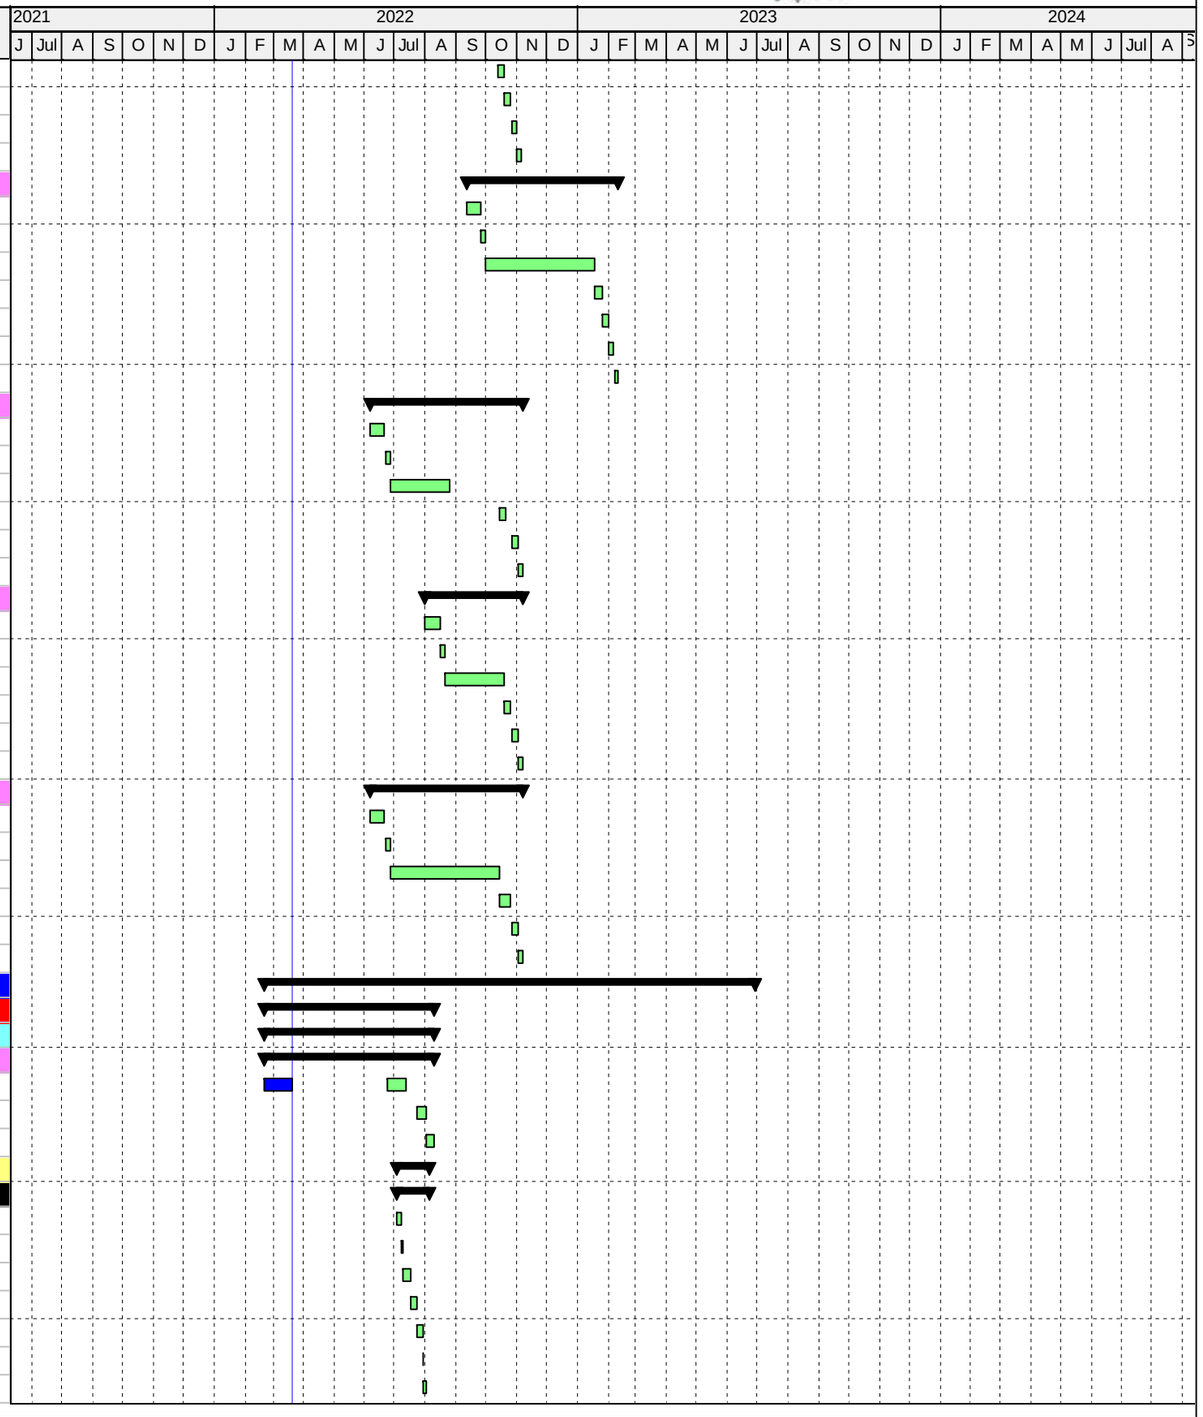


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03	Backfill	3	0%	$169.89	02-Aug-22	05-Aug-22
culverts		11	0%	$12,741.46	13-Jul-22	24-Jul-22
P03	pipeway culvert	5	0%	$5,096.58	13-Jul-22	18-Jul-22
P03	pipeway	3	0%	$4,459.51	18-Jul-22	21-Jul-22
P03	pipeline culvert	3	0%	$3,185.36	21-Jul-22	24-Jul-22
Burn Pit Access Road		18	0%	$17,696.47	13-Jul-22	31-Jul-22
P03-E	ROW Preparation	10	0%	$11,502.70	13-Jul-22	23-Jul-22
P03-E	Filling and Compaction	5	0%	$3,539.29	23-Jul-22	28-Jul-22
P03-E	Sub-Base Layer	3	0%	$2,654.47	28-Jul-22	31-Jul-22
Wellpad		198	8.75%	$353,929.34	21-Feb-22	26-Jul-22
Water Supply		25	0%	$24,775.05	23-Jun-22	18-Jul-22
P03-E	Water Supply	25	0%	$24,775.05	23-Jun-22	18-Jul-22
Site Preparation		10	25%	$123,875.27	21-Feb-22	07-Jul-22
P03-E	Site Preparation W046S	10	25%	$123,875.27	21-Feb-22	07-Jul-22
Civil Work		10	0%	$106,178.80	02-Jul-22	12-Jul-22
P03-E	Excavation and Soil Removal (Cellar)	5	0%	$69,016.22	02-Jul-22	07-Jul-22
P03-E	Installation of Conductor Pipe	5	0%	$5,308.94	02-Jul-22	07-Jul-22
P03-E	Form Work (Above Cellar)	5	0%	$5,308.94	07-Jul-22	12-Jul-22
P03-E	Armed Concrete	2	0%	$26,544.70	09-Jul-22	11-Jul-22
Surface Preparation		19	0%	$3,539.29	07-Jul-22	26-Jul-22
P03-E	Gravel Paving	19	0%	$3,539.29	07-Jul-22	26-Jul-22
Mud Channel		11	0%	$21,235.76	07-Jul-22	18-Jul-22
P03-E	Excavation	3	0%	$2,123.58	09-Jul-22	12-Jul-22
P03-E	Soil Removal, Filling and Compaction of Mud Pit Area	2	0%	$3,185.36	07-Jul-22	09-Jul-22
P03-E	Construction of Mud Pit's Walls	5	0%	$7,432.52	12-Jul-22	17-Jul-22
P03-E	Installation sealling Layer	3	0%	$6,370.73	07-Jul-22	10-Jul-22
P03-E	Backfill	1	0%	$2,123.58	17-Jul-22	18-Jul-22
Mud Pit		17	0%	$35,392.93	27-Jun-22	14-Jul-22
P03-E	Soil Removal, Filling and Compaction of Mud Pit Area	10	0%	$14,157.17	27-Jun-22	07-Jul-22
P03-E	Construction of Mud Pit's Walls	7	0%	$5,308.94	30-Jun-22	07-Jul-22
P03-E	Installation sealling Layer	7	0%	$15,926.82	07-Jul-22	14-Jul-22
SepticTank		16	0%	$14,157.17	07-Jul-22	23-Jul-22
P03-E	Excavation & Soil Transfer	5	0%	$4,247.15	07-Jul-22	12-Jul-22
P03-E	Levelling	5	0%	$70.79	12-Jul-22	17-Jul-22
P03-E	Tank Supply	5	0%	$8,069.59	12-Jul-22	17-Jul-22
P03-E	Tank Execution	3	0%	$1,344.93	17-Jul-22	20-Jul-22
P03-E	Backfilling & Compaction	3	0%	$424.72	20-Jul-22	23-Jul-22
Burn Pit		15	0%	$17,696.47	07-Jul-22	22-Jul-22
P03-E	Soil Removal, Triming ,Filling and Compaction of Burn Pit Are	5	0%	$14,157.17	07-Jul-22	12-Jul-22
P03-E	Construction & Installation of Support	7	0%	$884.82	12-Jul-22	19-Jul-22
P03-E	Welding, Installation and Testing	5	0%	$2,654.47	17-Jul-22	22-Jul-22
Gasoil Pad		15	0%	$7,078.59	07-Jul-22	22-Jul-22
P03-E	Lean Concrete	2	0%	$2,123.58	12-Jul-22	14-Jul-22
P03-E	Formwork	4	0%	$707.86	14-Jul-22	18-Jul-22
P03-E	Armed Concrete	4	0%	$2,831.43	18-Jul-22	22-Jul-22
P03-E	Excavation	5	0%	$1,415.72	07-Jul-22	12-Jul-22
Helipad		17	0%	$7,226.33	13-Jul-22	30-Jul-22
P03-EP	Excavation & Soil Transfer	2	0%	$722.63	13-Jul-22	15-Jul-22
P03-EP	Levelling	2	0%	$867.16	15-Jul-22	17-Jul-22

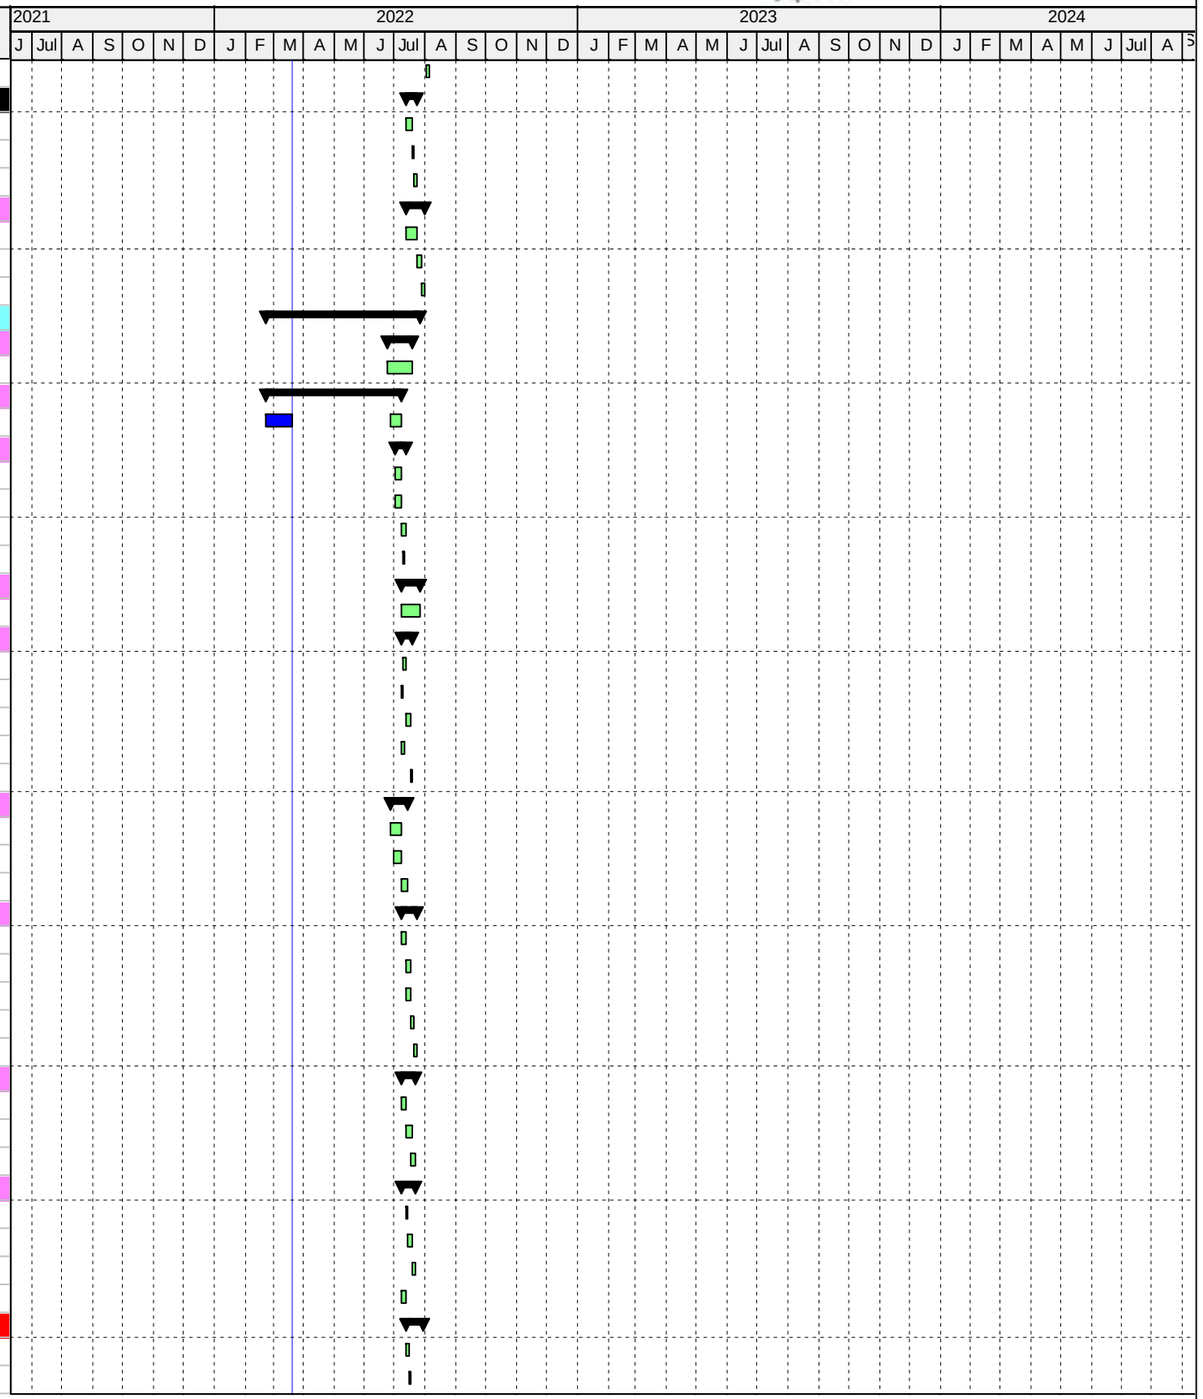

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-EP	Lean Concrete	1	0%	$1,083.95	17-Jul-22	18-Jul-22
P03-EP	Reinforced Work	5	0%	$1,083.95	18-Jul-22	23-Jul-22
P03-EP	Form Work	3	0%	$1,445.27	23-Jul-22	26-Jul-22
P03-EP	Backfilling & Compaction	2	0%	$1,083.95	27-Jul-22	29-Jul-22
P03-EP	Paint Marking	1	0%	$794.90	29-Jul-22	30-Jul-22
P03-EP	Main Concrete Pouring	1	0%	$144.53	26-Jul-22	27-Jul-22
Wellhead Facility and Flowline		294	0%	$341,243.13	10-Aug-22	31-May-23
Civil, Structure & Architecture		276	0%	$156,971.84	10-Aug-22	13-May-23
Civil Work		123	0%	$89,473.95	10-Aug-22	11-Dec-22
P03-E	Right of Way	40	0%	$67,105.46	10-Aug-22	19-Sep-22
P03-E	Steel Works(Wellhead Facilities)	30	0%	$15,210.57	12-Nov-22	11-Dec-22
P03-E	Out Door Post Works For Wellhead Post (Fundation, Fencin	10	0%	$4,473.70	19-Sep-22	29-Sep-22
P03-E	Well Pad Fencing	45	0%	$2,684.22	29-Sep-22	13-Nov-22
Buildings		261	0%	$51,800.71	25-Aug-22	13-May-23
Construction of Switchgear		261	0%	$14,504.20	25-Aug-22	13-May-23
Structure		44	0%	$5,801.68	12-Oct-22	25-Nov-22
P03	Steel Material Supply	25	0%	$2,900.84	12-Oct-22	06-Nov-22
P03	Shop Fabrication of Steel Structure	25	0%	$1,160.34	19-Oct-22	13-Nov-22
P03	Structural Installation	18	0%	$1,160.34	03-Nov-22	20-Nov-22
P03	Structural Painting	5	0%	$580.17	20-Nov-22	25-Nov-22
Foundation		48	0%	$4,496.30	25-Aug-22	12-Oct-22
P03	Excavation & Soil Transfer (Removing of Vegetal Soil)	19	0%	$899.26	25-Aug-22	13-Sep-22
P03	Levelling	6	0%	$89.93	13-Sep-22	19-Sep-22
P03	Lean Concrete	2	0%	$449.63	19-Sep-22	21-Sep-22
P03	Reinforced Work	9	0%	$899.26	21-Sep-22	30-Sep-22
P03	Formwork	4	0%	$359.70	30-Sep-22	04-Oct-22
P03	Main Concrete Pouring	5	0%	$1,753.56	04-Oct-22	09-Oct-22
P03	Backfilling & Compaction	4	0%	$44.96	09-Oct-22	12-Oct-22
Architectural		173	0%	$4,206.22	21-Nov-22	13-May-23
P03	Wall Execution	19	0%	$2,055.58	21-Nov-22	10-Dec-22
P03	Roof Covering	9	0%	$500.54	10-Dec-22	19-Dec-22
P03	Roof Execution (Block Joist, Concrete Pouring)	9	0%	$638.50	25-Apr-23	03-May-23
P03	Building Walkway (around Building)	10	0%	$216.20	03-May-23	13-May-23
P03	Joinery (Cornice, Faï?½ade, Plaster)	6	0%	$795.40	03-May-23	09-May-23
Construction of Guard House		131	0%	$37,296.51	14-Oct-22	22-Feb-23
Foundation		40	0%	$11,561.92	14-Oct-22	23-Nov-22
P03	Excavation & Soil Transfer (Removing of Vegetal Soil)	10	0%	$2,312.38	14-Oct-22	24-Oct-22
P03	Levelling	6	0%	$231.24	24-Oct-22	30-Oct-22
P03	Lean Concrete	2	0%	$1,156.19	30-Oct-22	01-Nov-22
P03	Reinforced Work	9	0%	$2,312.38	01-Nov-22	10-Nov-22
P03	Formwork	4	0%	$924.95	10-Nov-22	14-Nov-22
P03	Main Concrete Pouring	5	0%	$4,509.15	14-Nov-22	19-Nov-22
P03	Backfilling & Compaction	4	0%	$115.62	19-Nov-22	23-Nov-22
Architectural		50	0%	$10,815.99	03-Jan-23	22-Feb-23
P03	Wall Execution	15	0%	$5,285.77	03-Jan-23	18-Jan-23
P03	Roof Covering	9	0%	$1,287.10	18-Jan-23	27-Jan-23
P03	Roof Execution (Block Joist, Concrete Pouring)	9	0%	$1,641.87	27-Jan-23	04-Feb-23
P03	Building Walkway (around Building)	18	0%	$555.94	04-Feb-23	22-Feb-23
P03	Joinery (Cornice, Faï?½ade, Plaster)	15	0%	$2,045.30	04-Feb-23	19-Feb-23



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Structure		41	0%	$14,918.60	23-Nov-22	03-Jan-23
P03	Steel Material Supply	15	0%	$7,459.30	23-Nov-22	08-Dec-22
P03	Shop Fabrication of Steel Structure	15	0%	$2,983.72	03-Dec-22	18-Dec-22
P03	Structural Installation	15	0%	$2,983.72	13-Dec-22	28-Dec-22
P03	Structural Painting	6	0%	$1,491.86	28-Dec-22	03-Jan-23
Shelters		80	0%	$15,697.18	19-Sep-22	08-Dec-22
Diesel Generator Shelter		80	0%	$12,871.69	19-Sep-22	08-Dec-22
P03-	Fabrication	35	0%	$9,010.18	19-Sep-22	24-Oct-22
P03-	Installation	25	0%	$3,861.51	13-Nov-22	08-Dec-22
Fire Fighting Shelter		30	0%	$2,825.49	24-Sep-22	23-Oct-22
P03-	Fabrication	20	0%	$1,977.85	29-Sep-22	18-Oct-22
P03-	Installation	30	0%	$847.65	24-Sep-22	23-Oct-22
Flowline		84	0%	$92,135.64	10-Nov-22	01-Feb-23
P03-EF	Construction of Pipe Support	25	0%	$13,820.35	10-Nov-22	04-Dec-22
P03-EF	Installation of Pipe Supports	25	0%	$13,820.35	16-Nov-22	11-Dec-22
6" Flowline Installation		59	0%	$59,888.17	25-Nov-22	22-Jan-23
P03-E	COLD CUT	10	0%	$10,779.87	25-Nov-22	04-Dec-22
P03-E	Material Handeling	30	0%	$14,972.04	05-Dec-22	03-Jan-23
P03-E	Fit-Up & Welding	35	0%	$23,955.27	05-Dec-22	08-Jan-23
P03-E	Bending	9	0%	$6,587.70	09-Jan-23	17-Jan-23
P03-E	NDT	5	0%	$3,593.29	17-Jan-23	22-Jan-23
Hydrostatic Test		10	0%	$4,606.78	22-Jan-23	01-Feb-23
P03-E	6" Pigging and Hydrostatic Test	10	0%	$4,606.78	22-Jan-23	01-Feb-23
Piping		25	0%	$27,299.45	18-Apr-23	13-May-23
P03-EF	Sweep Bend Installation	7	0%	$9,554.81	18-Apr-23	25-Apr-23
P03-EF	Construction of Spools (Fit up, Welding, NDT…)	7	0%	$15,014.70	25-Apr-23	02-May-23
P03-EF	Valves, Fitting and Spools Installation and Hydrotest	6	0%	$1,364.97	02-May-23	08-May-23
P03-EF	Painting	5	0%	$1,364.97	08-May-23	13-May-23
Mechanical		15	0%	$10,237.29	18-Apr-23	03-May-23
P03-EF	Fuel Oil Storage Drum	15	0%	$5,118.65	18-Apr-23	03-May-23
P03-EF	Potable Water Tank	15	0%	$5,118.65	18-Apr-23	03-May-23
Instrument Works		15	0%	$10,237.29	10-May-23	24-May-23
P03-EF	Devices Installation and Piping Connecton	15	0%	$10,237.29	10-May-23	24-May-23
Electrical		37	0%	$37,536.74	18-Apr-23	24-May-23
P03-EF	Over Head line	10	0%	$31,906.23	18-Apr-23	28-Apr-23
P03-EF	Wellhead Electrical Equipment	15	0%	$3,190.62	10-May-23	24-May-23
P03-EF	Outdoor Post (Wellhead Post)	15	0%	$2,439.89	18-Apr-23	03-May-23
Pre-commissioning		7	0%	$6,824.86	25-May-23	31-May-23
P03-EF	Pre-commissioning	7	0%	$3,412.43	25-May-23	31-May-23
P03-EF	Ready for Comm.Certificate(RFCC)	5	0%	$3,412.43	27-May-23	31-May-23
Job Site HSE Supervision (Surface)		310	0%	$1,605.85	23-Jun-22	29-Apr-23
P03-EP	Job Site HSE Supervision (Surface)	310	0%	$1,605.85	23-Jun-22	29-Apr-23
Commissioning, Startup & Handover		78	0%	$10,438.03	13-Apr-23	29-Jun-23
Commissioning		34	0%	$3,131.41	13-Apr-23	17-May-23
P03-EF	Materials & Utilities Ready for Commissioning	4	0%	$156.57	13-May-23	17-May-23
P03-EF	Receiving Facilities Ready for Commissioning	3	0%	$156.57	04-May-23	07-May-23
P03-EF	Permits Obtained for Commissioning	10	0%	$156.57	25-Apr-23	05-May-23
P03-EF	Integrated Commissioning	3	0%	$2,505.13	22-Apr-23	25-Apr-23
P03-EF	Ready for Startup Certificate (RFSU)	15	0%	$156.57	13-Apr-23	28-Apr-23
Handover		63	0%	$3,131.41	28-Apr-23	29-Jun-23




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P03-EF	Compiling & Submitting Final Documentation	20	0%	$939.42	28-Apr-23	18-May-23
P03-EF	Training of Operator's Personnel	3	0%	$1,252.56	06-May-23	08-May-23
P03-EF	Provisional Acceptance Certificate (PAC)	15	0%	$939.42	15-Jun-23	29-Jun-23
Startup & Performance Test		15	0%	$4,175.21	19-Apr-23	04-May-23
P03-EF	Startup & Performance Test Run	4	0%	$3,340.17	22-Apr-23	25-Apr-23
P03-EF	Start of Production (SOP)	15	0%	$835.04	19-Apr-23	04-May-23
Package 04-New Well # W035 (Bangestan)		594	7.55%	$562,828.00	24-Jul-21 A	03-Nov-23
ENGINEERING		523	24.9%	$8,125.00	24-Jul-21 A	25-Aug-23
Basic Design Endorsement		30	100%	$406.25	31-Jul-21 A	20-Mar-22
P04-EP	Endorsement Report For Basic Design & Scope of Work	30	100%	$406.25	31-Jul-21 A	20-Mar-22
Value Engineering		75	45%	$243.75	01-Feb-22	02-Jul-22
P04-EP	Value Engineering Study Report	44	60%	$182.81	01-Feb-22	02-May-22
P04-EP	HAZID Report For WHF & Flowlines	44	0%	$60.94	20-May-22	02-Jul-22
Detail Design		449	32.4%	$4,468.75	24-Jul-21 A	27-Jan-23
Process		137	59.77%	$446.88	27-Jul-21 A	01-Jun-22
Basis/Criteria		54	86.99%	$89.38	27-Jul-21 A	12-May-22
P04-E	Process Design Criteria	39	100%	$31.24	27-Jul-21 A	20-Mar-22
P04-E	Process Basis Of Design	54	80%	$58.14	27-Jul-21 A	12-May-22
Drawing/Diagram		93	67.67%	$111.72	30-Oct-21	07-May-22
P04-E	Symbol & Legend For PFD and P&ID	44	80%	$6.12	30-Oct-21	02-May-22
P04-E	Process Flow Diagram - W035	44	60%	$68.86	02-Nov-21	02-May-22
P04-E	P&ID - W035	49	80%	$36.73	01-Nov-21	07-May-22
Philosophy		74	11.01%	$67.03	21-Nov-21	01-Jun-22
P04-E	Drainage Philosophy	44	0%	$2.65	19-Apr-22	01-Jun-22
P04-E	Control Philosophy	44	0%	$18.37	19-Apr-22	01-Jun-22
P04-E	Flare,Blow Down And Relief Philosophy	44	0%	$18.37	19-Apr-22	01-Jun-22
P04-E	Isolation Philosophy	44	60%	$12.31	21-Nov-21	02-May-22
P04-E	ESD Philosophy	44	0%	$15.34	19-Apr-22	01-Jun-22
Data Sheet		5	0%	$44.69	08-May-22	12-May-22
P04-E	Process Data Sheets For Instrument Devices - W035	5	0%	$44.69	08-May-22	12-May-22
Report		44	80%	$89.38	30-Oct-21	07-May-22
P04-E	Flowline Hydraulic Calculation Report	44	80%	$89.38	30-Oct-21	07-May-22
List		107	77.99%	$44.69	08-Nov-21	07-May-22
P04-E	Line List - W035	44	80%	$40.22	08-Nov-21	07-May-22
P04-E	Consumption List	44	60%	$4.47	23-Feb-22	02-May-22
Piping		284	10.38%	$893.75	24-Jul-21 A	27-Jan-23
Basis/Criteria		39	100%	$1.79	24-Jul-21 A	20-Mar-22
P04-E	Piping Design Criteria	39	100%	$1.79	24-Jul-21 A	20-Mar-22
Specification		49	73.45%	$35.84	24-Jul-21 A	07-May-22
P04-E	Specification For Color Coding and Marking	39	60%	$2.09	09-Aug-21	01-May-22
P04-E	Specification For Transportation, Handling, Storage of pipes	30	80%	$2.28	12-Dec-21	18-Apr-22
P04-E	Specification For Metallic Pipes	39	80%	$2.09	24-Jul-21 A	01-May-22
P04-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$2.09	24-Jul-21 A	24-Mar-22
P04-E	Specification For Painting	39	100%	$2.09	24-Jul-21 A	27-Mar-22
P04-E	Specification For Lining (Internal Protection of Equipment by F	39	60%	$2.51	09-Aug-21	04-May-22
P04-E	Specification For Material Requirements in Sour service	39	60%	$2.09	09-Aug-21	04-May-22
P04-E	Specification For Manual Valves	39	60%	$2.09	09-Aug-21	04-May-22
P04-E	Specification For Plant Piping Systems Pressure Testing	39	60%	$2.09	09-Aug-21	04-May-22
P04-E	Specification For Welding of Plant Piping System	39	60%	$2.09	09-Aug-21	04-May-22
P04-E	Specification For Flexibility Analysis	39	60%	$2.28	09-Aug-21	04-May-22

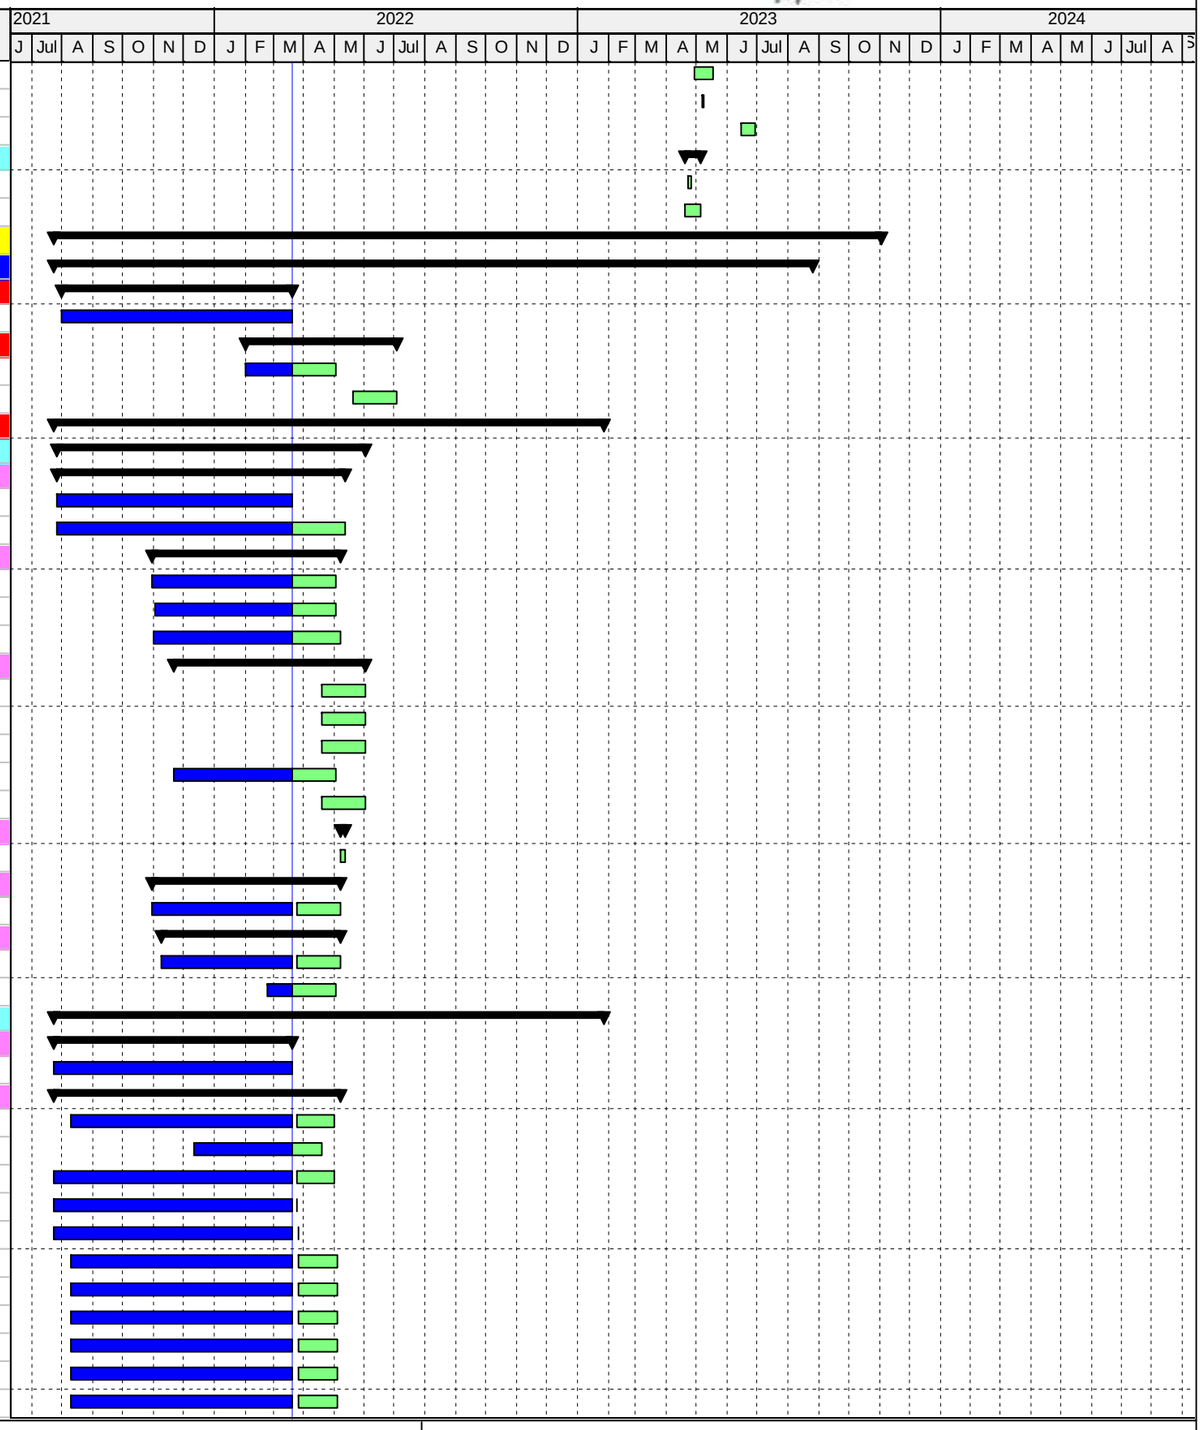


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P04-E	Specification For Coating Of Underground Piping	39	100%	$3.58	24-Jul-21 A	30-Mar-22
P04-E	Specification For Pipe Support	39	60%	$2.79	09-Aug-21	07-May-22
P04-E	Specification For Piping Construction, Fabrication & Erection	30	60%	$3.59	09-Aug-21	18-Apr-22
P04-E	Specification For Piping Cleaning and Flushing	39	100%	$2.09	24-Aug-21	30-Mar-22
Data Sheets		39	60%	$1.79	27-Dec-21	12-May-22
P04-E	Data Sheets For Stone Trap	39	60%	$1.79	27-Dec-21	12-May-22
Procedure/Plan		99	90.32%	$2.68	24-Jul-21 A	09-Aug-22
P04-E	3D-Model (PDMS) Review Procedure	39	100%	$2.41	24-Jul-21 A	03-Apr-22
P04-E	Piping Hydrostatic Test Diagram - Sub Surface	44	0%	$0.27	27-Jun-22	09-Aug-22
Drawing/Diagram		284	18.01%	$206.19	08-Nov-21	27-Jan-23
P04-E	Standard Pipe Support Drawings	14	100%	$6.21	19-Feb-22	20-Mar-22
P04-E	Piping Assembly Drawing	45	0%	$20.95	13-May-22	26-Jun-22
P04-E	Piping Hydrostatic Test Diagram - Sub Surface	44	0%	$3.36	27-Jun-22	09-Aug-22
P04-E	Plot Plan Drawing - W035	50	0%	$62.06	08-May-22	26-Jun-22
P04-E	Piping Plan - W035	44	0%	$37.24	01-Nov-22	14-Dec-22
P04-E	Isometric Drawings - W035	44	0%	$24.83	15-Dec-22	27-Jan-23
P04-E	Material Flow Diagram - W035	39	60%	$51.55	08-Nov-21	02-May-22
Report		88	5.36%	$448.22	28-Nov-21	17-Sep-22
P04-E	PDMS Model Review Report (60%) - W035	44	0%	$244.50	22-Jun-22	04-Aug-22
P04-E	PDMS Model Review Report (90%) - W035	44	0%	$163.64	05-Aug-22	17-Sep-22
P04-E	Piping Corrosion Study & Material Selection Report	44	60%	$40.07	28-Nov-21	16-May-22
List		177	0%	$35.84	08-May-22	31-Oct-22
P04-E	Piping Support List - W035	44	0%	$17.92	18-Sep-22	31-Oct-22
P04-E	Critical Line List - W035	39	0%	$17.92	08-May-22	15-Jun-22
MTO		7	0%	$161.41	18-Sep-22	24-Sep-22
P04-E	MTO For Pipes - W035	7	0%	$26.91	18-Sep-22	24-Sep-22
P04-E	MTO For Fittings - W035	7	0%	$26.89	18-Sep-22	24-Sep-22
P04-E	MTO For Flanges - W035	7	0%	$26.89	18-Sep-22	24-Sep-22
P04-E	MTO For Manual Valves - W035	7	0%	$26.91	18-Sep-22	24-Sep-22
P04-E	MTO For Gaskets - W035	7	0%	$26.91	18-Sep-22	24-Sep-22
P04-E	MTO For Bolt & Nuts - W035	7	0%	$26.91	18-Sep-22	24-Sep-22
Pipeline & Flow line		237	39.44%	$134.06	24-Jul-21 A	11-Nov-22
Basis/Criteria		39	100%	$0.94	28-Aug-21	20-Mar-22
P04-E	Pipeline Design Criteria	39	100%	$0.94	28-Aug-21	20-Mar-22
Specification		49	85.9%	$13.07	24-Jul-21 A	07-May-22
P04-E	Specification For Line Pipes	39	100%	$1.03	24-Jul-21 A	24-Mar-22
P04-E	Specification For Pipeline Cold Bending	39	80%	$0.91	28-Aug-21	01-May-22
P04-E	Specification For Barred Tee	39	80%	$0.91	28-Aug-21	01-May-22
P04-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$0.91	24-Jul-21 A	24-Mar-22
P04-E	Specification For Pipeline Valves	39	80%	$0.91	28-Aug-21	01-May-22
P04-E	Specification For Pipeline Coating	39	100%	$0.91	24-Jul-21 A	24-Mar-22
P04-E	Specification For Pipeline Flushing, Cleaning And Hydrostatic	39	100%	$1.02	24-Jul-21 A	27-Mar-22
P04-E	Specification For Welding of Transportation Pipeline	39	80%	$0.91	12-Dec-21	04-May-22
P04-E	Specification For Pipeline Stress Analysis	39	80%	$0.91	24-Jul-21 A	04-May-22
P04-E	Specification For Pipeline Insulation Joint	39	100%	$0.91	24-Jul-21 A	27-Mar-22
P04-E	Specification For Pipeline Construction	39	80%	$0.91	25-Jan-22	04-May-22
P04-E	Specification For Anchor Flanges	39	80%	$1.02	28-Aug-21	07-May-22
P04-E	Specification For Pigs	39	80%	$0.91	28-Aug-21	07-May-22
P04-E	Specification For Pipeline Cleaning and Flushing	44	60%	$0.91	24-Jul-21 A	02-May-22

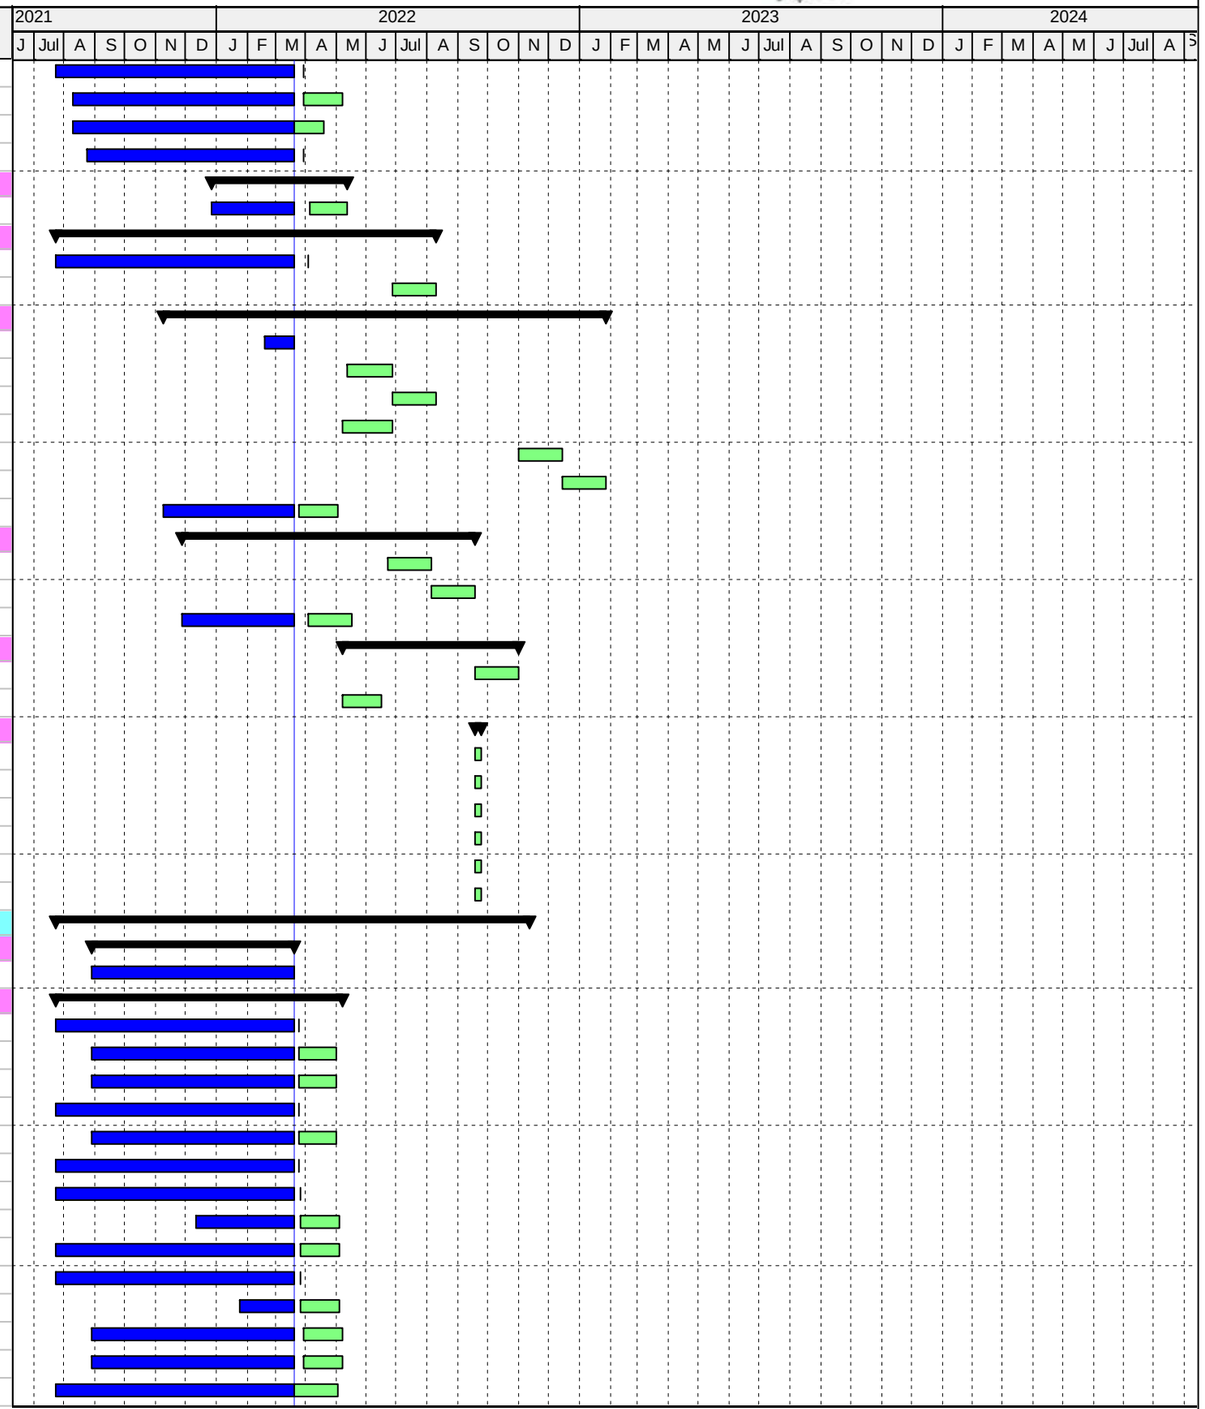


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Drawings		84	21.55%	$77.01	27-Jul-21 A	12-May-22
P04-E	Pipeline Standard Support Drawings	14	100%	$2.57	27-Jul-21 A	20-Mar-22
P04-E	Standard Drawing For Above Ground Pipeline Construction F	44	80%	$2.24	27-Nov-21	12-May-22
P04-E	Standard Drawing For Under Ground Pipeline Construction F	44	100%	$2.24	04-Dec-21	30-Mar-22
P04-E	Pipeline Standard Drawing For Anchor Support	44	60%	$2.24	22-Dec-21	12-May-22
P04-E	Standard Drawing For A/G Pipeline Road Crossing	44	60%	$2.24	05-Dec-21	12-May-22
P04-E	Standard Drawing For Existing Pipeline Crossing	44	60%	$2.24	18-Dec-21	12-May-22
P04-E	Pipeline Standard Drawing For Irish Crossing	44	60%	$2.12	04-Dec-21	12-May-22
P04-E	Pipeline Standard Drawing For Water - Way Crossing	44	60%	$2.12	22-Nov-21	12-May-22
P04-E	Pipeline Standard Drawing For Pig Signaller Concrete Pit	44	60%	$2.12	27-Nov-21	12-May-22
P04-E	Pipeline Standard Drawing For H-Pipe Support	44	100%	$2.12	27-Nov-21	30-Mar-22
P04-E	Flowline Transversal Drawings - W035	44	0%	$50.02	20-Mar-22	02-May-22
P04-E	Pipeline Hydrostatic Test Diagram - Sub Surface	44	0%	$4.74	20-Mar-22	02-May-22
Procedure/Plan		44	0%	$0.00	09-Apr-22	22-May-22
P04-E	Pipeline Hydrostatic Test Diagram - Sub Surface	44	0%	$0.00	09-Apr-22	22-May-22
List		36	0%	$14.71	07-Oct-22	11-Nov-22
P04-E	Road Crossing Location List	36	0%	$14.71	07-Oct-22	11-Nov-22
Report		44	80%	$21.34	27-Oct-21	22-May-22
P04-E	Pipeline Corrosion Study & Material Selection Report	44	80%	$21.34	27-Oct-21	22-May-22
MTO		7	100%	$7.00	22-Aug-21	19-May-22
P04-E	MTO For Line Pipes (Flowlines) - W035	7	100%	$7.00	22-Aug-21	19-May-22
Control & Instrumentation		278	78.5%	$357.50	26-Jul-21 A	18-Sep-22
Basis/Criteria		44	94.56%	$15.84	14-Aug-21	29-Apr-22
P04-E	Fire & Gas Detection Design Criteria	38	100%	$13.68	14-Aug-21	27-Mar-22
P04-E	Instrument & Control System Design Criteria	38	60%	$2.16	03-Jan-22	29-Apr-22
Specification		42	86.9%	$81.33	26-Jul-21 A	26-Apr-22
P04-E	Specification For WHCP/HPU	38	80%	$53.29	08-Aug-21	26-Apr-22
P04-E	Specification For Instrumentation	39	100%	$28.04	26-Jul-21 A	23-Mar-22
Data Sheets		120	80%	$20.34	22-Aug-21	24-May-22
P04-E	Data Sheets For WHCP/HPU - Wellheads	49	80%	$10.04	22-Aug-21	07-May-22
P04-E	Data Sheets For Pressure Gauge - Wellheads	42	80%	$5.15	07-Dec-21	24-May-22
P04-E	Data Sheets For Temperature Gauge - Wellheads	42	80%	$5.15	07-Dec-21	24-May-22
Drawing/Diagram		112	26.69%	$83.58	22-Aug-21	17-Sep-22
P04-E	Instrument Hook-up Diagram - Wellheads	42	80%	$13.23	14-Nov-21	12-May-22
P04-E	WHCP Hydraulic \Peneumatic Diagrams - Wellheads	42	100%	$11.73	22-Aug-21	19-Apr-22
P04-E	Instrument Location Layout Drawing - W035	44	0%	$58.63	05-Aug-22	17-Sep-22
List		7	100%	$43.40	10-Nov-21	13-May-22
P04-E	Instrument Index For New Wells & Manifold Extension	7	100%	$43.40	10-Nov-21	13-May-22
MTO		135	100%	$113.01	14-Nov-21	18-Sep-22
P04-E	MTO For Instrument Tube and Fitting - W035	7	100%	$56.50	14-Nov-21	13-May-22
P04-E	MTO For Instrument Cable Tray - W035	7	100%	$56.50	14-Nov-21	18-Sep-22
Safety		158	51.46%	$134.06	24-Jul-21 A	27-Sep-22
Basis/Criteria		44	100%	$13.41	29-Aug-21	19-Apr-22
P04-E	Active Fire Protection and Safety Concept	44	100%	$13.41	29-Aug-21	19-Apr-22
Specification		47	88.24%	$26.81	24-Jul-21 A	09-May-22
P04-E	Specification For Fire Fighting Equipment	44	100%	$4.73	29-Aug-21	24-Mar-22
P04-E	Specification For Hazardous Area Classification	44	100%	$4.73	24-Jul-21 A	24-Mar-22
P04-E	Specification For Fire Water System	44	80%	$6.31	24-Jul-21 A	09-May-22
P04-E	Specification For Environmental Job	44	60%	$4.73	11-Aug-21	06-May-22
P04-E	Specification For Total Flooding System	44	100%	$6.31	24-Jul-21 A	27-Mar-22

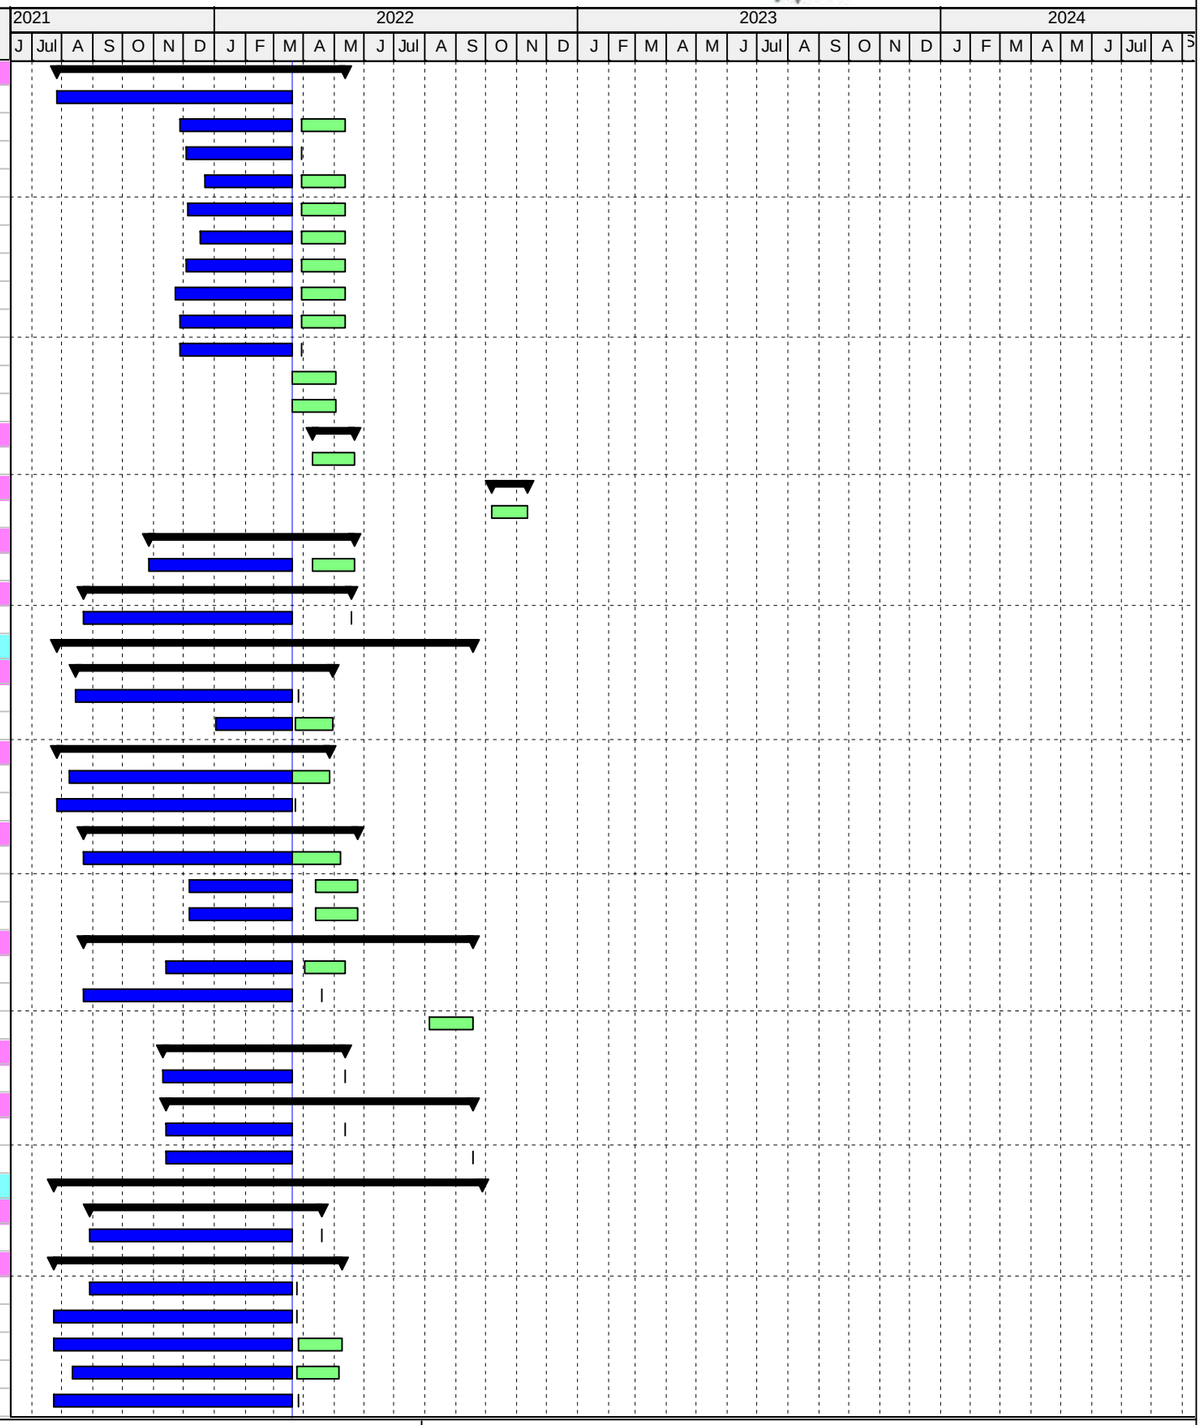


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Data Sheets		47	100%	$13.41	08-Dec-21	27-Mar-22
P04-E	Data Sheets For Fire Fighting Equipment	44	100%	$4.47	08-Dec-21	24-Mar-22
P04-E	Data Sheets For Safety Equipment	44	100%	$4.47	08-Dec-21	27-Mar-22
P04-E	Data Sheets For Safety Sign	44	100%	$4.47	08-Dec-21	27-Mar-22
Drawing/Diagram		143	14.45%	$53.63	29-Aug-21	22-Sep-22
P04-E	Typical Installation Detail for Safety & Fire Fighting Equipment	14	100%	$3.87	29-Dec-21	27-Mar-22
P04-E	Symbol & Legend For Safety & Firefighting Systems	44	100%	$3.87	29-Aug-21	27-Mar-22
P04-E	Hazardous Area Classification Layout - W035	44	0%	$15.30	03-May-22	15-Jun-22
P04-E	Safety & Fire Fighting Equipment Location Layout - W035	44	0%	$15.30	27-Jun-22	09-Aug-22
P04-E	Escape Route & Safety Sign Layout - W035	44	0%	$15.29	10-Aug-22	22-Sep-22
List		44	80%	$13.41	09-Nov-21	02-May-22
P04-E	Hazard Source List - W035	44	80%	$13.41	09-Nov-21	02-May-22
MTO		49	0%	$13.41	10-Aug-22	27-Sep-22
P04-E	MTO For Fire Fighting & Safety Equipment - W035	7	0%	$6.70	10-Aug-22	16-Aug-22
P04-E	MTO For Safety Sign - W035	5	0%	$6.70	23-Sep-22	27-Sep-22
Architecture		84	60%	$134.06	18-Dec-21	01-Jun-22
Basis/Criteria		74	60%	$26.81	08-Feb-22	01-Jun-22
P04-E	Architectural Design Criteria	74	60%	$26.81	08-Feb-22	01-Jun-22
Drawing/Diagram		84	60%	$107.25	18-Dec-21	02-May-22
P04-E	Architectural Drawing For WHCP/HPU Shelter of Well Pads -	44	60%	$77.50	26-Feb-22	02-May-22
P04-E	Standard Drawing for Architectural Details	44	60%	$29.75	18-Dec-21	02-May-22
Civil		449	38.55%	$804.38	01-Aug-21	25-Dec-22
Basis/Criteria		90	20%	$2.98	13-Feb-22	22-May-22
P04-E	Civil Design Criteria	64	60%	$0.99	13-Feb-22	22-May-22
P04-E	Design Criteria for Sewerage & Drainage	44	0%	$0.99	24-Mar-22	06-May-22
P04-E	Design Criteria for Road and Paving	44	0%	$0.99	27-Mar-22	09-May-22
Specification		94	72.14%	$15.04	09-Aug-21	06-Jun-22
P04-E	Specification For Civil Works	79	0%	$1.50	20-Mar-22	06-Jun-22
P04-E	Specification For Road & Paving	64	80%	$3.01	09-Aug-21	22-May-22
P04-E	Specification For Fence & Gate	64	100%	$3.01	18-Sep-21	20-Mar-22
P04-E	Specification For Earth Work	64	80%	$3.01	09-Aug-21	22-May-22
P04-E	Specification For Sewerage & Drainage	64	100%	$3.01	09-Aug-21	20-Mar-22
P04-E	Specification For Geological & Geotechnical Survey	44	0%	$1.50	20-Mar-22	02-May-22
Drawing/Diagram		331	42.03%	$641.89	01-Aug-21	03-Oct-22
P04-E	Standard Drawing For Civil Works	64	0%	$10.59	30-Mar-22	01-Jun-22
P04-E	Standard Drawing For Slope Protection Details	64	100%	$10.59	22-Aug-21	30-Mar-22
P04-E	Standard Drawing For Roads	64	80%	$10.59	22-Aug-21	01-Jun-22
P04-E	Standard Drawing For Electrical Cable Trench	64	100%	$10.59	22-Aug-21	30-Mar-22
P04-E	Standard Drawing For Manholes	64	80%	$10.59	22-Aug-21	01-Jun-22
P04-E	Standard Drawing For Catch Basins	64	80%	$10.59	22-Aug-21	05-Jun-22
P04-E	Standard Drawing For Sewerage & Drainage Details	64	60%	$10.59	02-Feb-22	05-Jun-22
P04-E	Standard Drawing For Civil Underground Crossings	38	60%	$18.04	07-Feb-22	10-May-22
P04-E	Standard Drawing For Fence & Gate Details	64	100%	$10.59	18-Sep-21	03-Apr-22
P04-E	Standard Drawing For Concrete Continues Weight	38	100%	$17.65	01-Aug-21	20-Mar-22
P04-E	Standard Drawing For Major Floodway Crossing	38	0%	$17.65	03-Apr-22	10-May-22
P04-E	Standard Drawing For Culvert & Details	38	100%	$17.65	25-Sep-21	03-Apr-22
P04-E	Standard Drawing For Valve Box	38	100%	$17.65	12-Jan-22	03-Apr-22
P04-E	Standard Drawing For Fire Hydrant Pit	38	60%	$17.65	13-Mar-22	10-May-22
P04-E	Standard Drawing For Cable Pull Pit	64	0%	$10.59	03-Apr-22	05-Jun-22

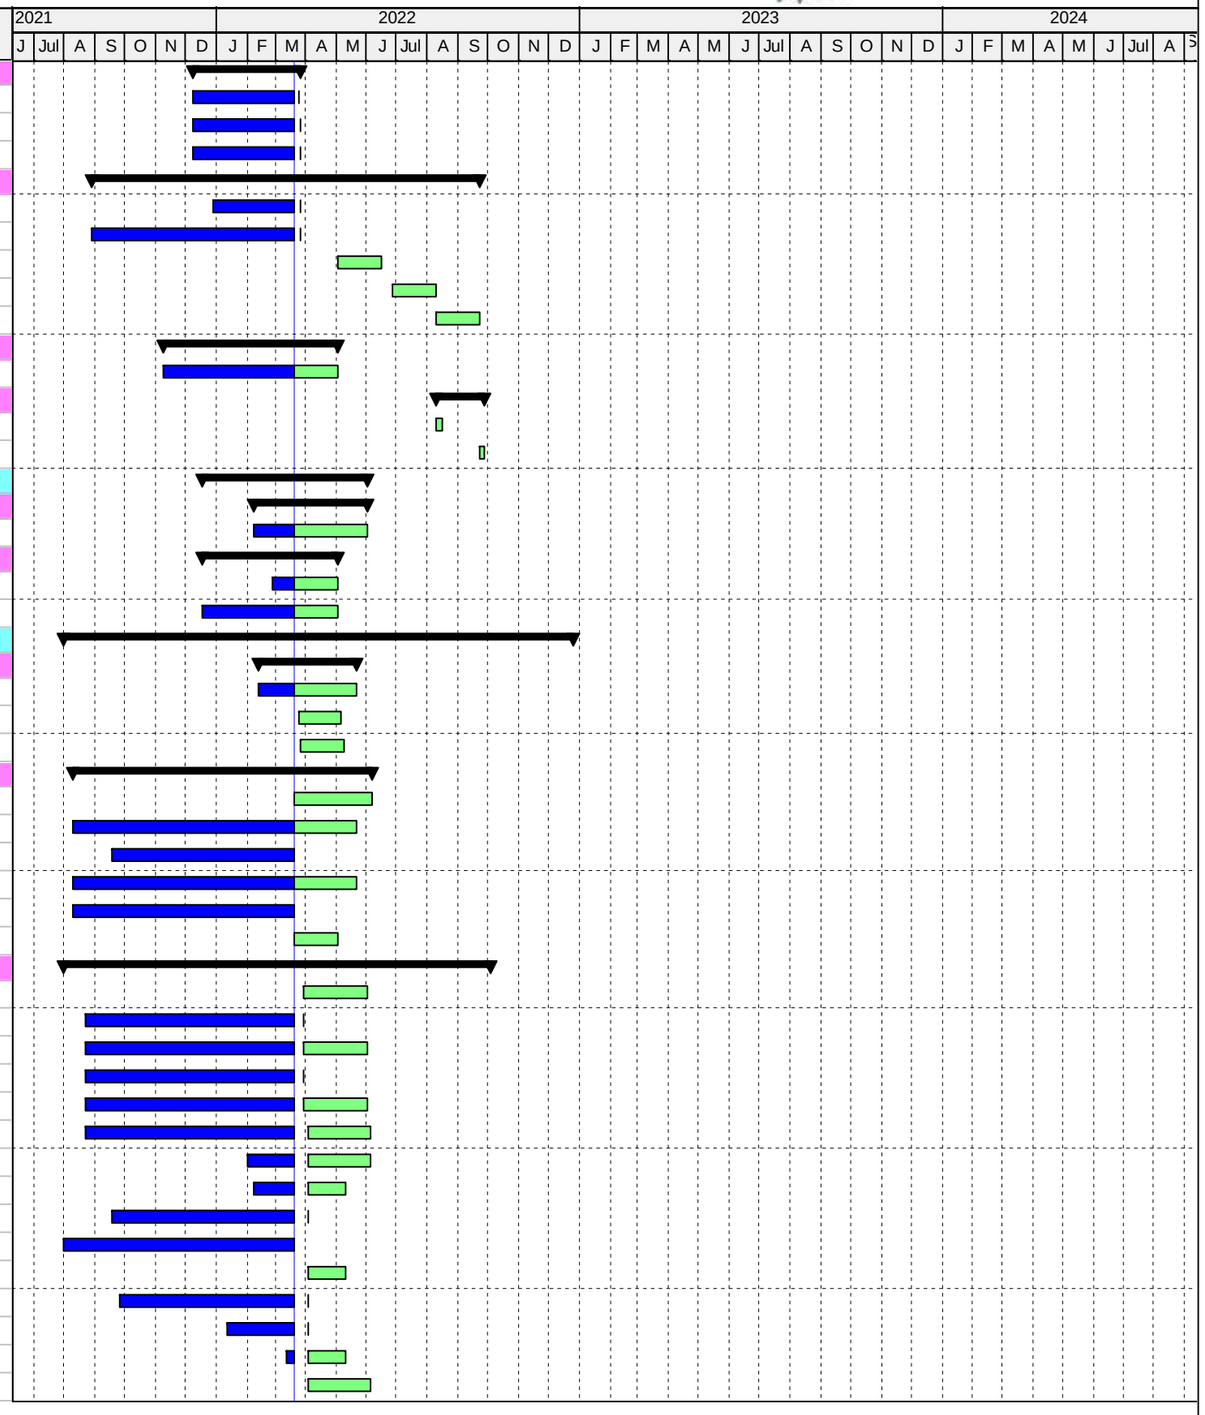


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P04-E	Standard Drawing For Pavings	38	60%	$17.65	08-Jan-22	10-May-22
P04-E	Standard Drawing For Earth Pit	38	60%	$17.65	13-Feb-22	10-May-22
P04-E	Standard Detail For Pipe Bedding	64	100%	$10.59	22-Aug-21	03-Apr-22
P04-E	Standard Details of Miscellaneous Items	64	60%	$10.59	06-Mar-22	05-Jun-22
P04-E	BINAK Oil Field Project Overall Well Location/Facilities Layout	54	0%	$8.02	20-Mar-22	12-May-22
P04-E	General Civil Layout -W035	64	0%	$141.02	12-Jun-22	14-Aug-22
P04-E	Civil and Structural drawings -W035	64	0%	$141.02	31-Jul-22	02-Oct-22
P04-E	Rough Grading Plans -W035	30	100%	$93.72	15-Dec-21	03-Oct-22
Calculation		252	40%	$72.23	05-Dec-21	25-Dec-22
P04-E	Calculation Note For Heli Pad, Well Pad & Diesel Storage Pac	38	0%	$36.12	03-Oct-22	09-Nov-22
P04-E	Calculation Note For Flood Control	39	80%	$36.12	05-Dec-21	25-Dec-22
MTO		7	0%	$72.23	03-Oct-22	10-Oct-22
P04-E	MTO For Civil Works - W035	7	0%	$72.23	03-Oct-22	10-Oct-22
Structure		108	33.66%	$491.56	08-Aug-21	26-May-22
Basis/Criteria		64	0%	$5.36	20-Mar-22	22-May-22
P04-E	Structural Design Criteria	64	0%	$1.79	20-Mar-22	22-May-22
P04-E	Design Criteria For Steel Structure	44	0%	$1.79	20-Mar-22	02-May-22
P04-E	Design Criteria For Load & Forces	44	0%	$1.79	20-Mar-22	02-May-22
Specification		98	79.14%	$40.95	14-Aug-21	26-May-22
P04-E	Specification For Concrete Work	64	80%	$7.38	14-Aug-21	26-May-22
P04-E	Specification for Fabrication of Steel Structures	64	100%	$9.53	24-Jan-22	24-Mar-22
P04-E	Specification For Grouting	64	100%	$7.38	14-Aug-21	24-Mar-22
P04-E	Specification for Erection of Steel Structures	64	100%	$9.59	24-Jan-22	24-Mar-22
P04-E	Specification For Steel Structural Works	37	0%	$7.07	20-Mar-22	25-Apr-22
Drawing/Diagram		108	41.97%	$317.01	08-Aug-21	12-May-22
P04-E	Standard Drawing For Fire Proofing	64	100%	$7.96	08-Aug-21	03-Apr-22
P04-E	Standard Drawing For Anchor Bolts	64	100%	$7.96	15-Dec-21	03-Apr-22
P04-E	Standard Drawing For Steel Stairs	64	100%	$7.96	18-Dec-21	03-Apr-22
P04-E	Standard Drawing For Operating Platform	38	100%	$9.35	27-Dec-21	30-Mar-22
P04-E	Standard Drawing For Handrail	38	100%	$13.31	18-Dec-21	30-Mar-22
P04-E	Standard Drawing For Insert Plates in Concrete	38	100%	$13.31	08-Aug-21	30-Mar-22
P04-E	Standard Details For Ladder & Safety Cage	64	100%	$7.96	15-Dec-21	03-Apr-22
P04-E	Standard Drawing For Lighting pole foundation Plan & Details	38	60%	$13.31	29-Jan-22	06-May-22
P04-E	General Notes - Steel Structures	38	100%	$9.35	25-Jan-22	30-Mar-22
P04-E	General Notes - Reinforced Concrete Structures	38	100%	$13.31	20-Dec-21	30-Mar-22
P04-E	Standard Drawing For Structural Built-up Sections	44	80%	$13.31	04-Dec-21	12-May-22
P04-E	Standard Drawing For Steel Flooring, Grating and Chequere	44	100%	$13.31	05-Jan-22	30-Mar-22
P04-E	Concrete Reinforcement Shape Code	44	0%	$13.31	30-Mar-22	12-May-22
P04-E	Standard Drawing For Septic Tank	44	80%	$13.31	22-Jan-22	12-May-22
P04-E	Platform Structure Drawing - W035	44	0%	$159.96	20-Mar-22	02-May-22
MTO		7	0%	$128.25	03-May-22	09-May-22
P04-E	MTO For Structural Works - W035	7	0%	$128.25	03-May-22	09-May-22
General		241	12.06%	$1,072.50	11-Aug-21	16-Nov-22
Risk Assessment		44	100%	$53.63	05-Sep-21	20-Mar-22
Procedure/Plan		44	100%	$53.63	05-Sep-21	20-Mar-22
P04-	HAZID Study Procedure	44	100%	$53.63	05-Sep-21	20-Mar-22
Survey (Topography) & Geotechnic		181	7.06%	$911.63	11-Aug-21	16-Nov-22
Geotechnic		181	8%	$804.38	11-Aug-21	16-Nov-22
Procedure/Plan		44	100%	$64.35	11-Aug-21	19-Apr-22

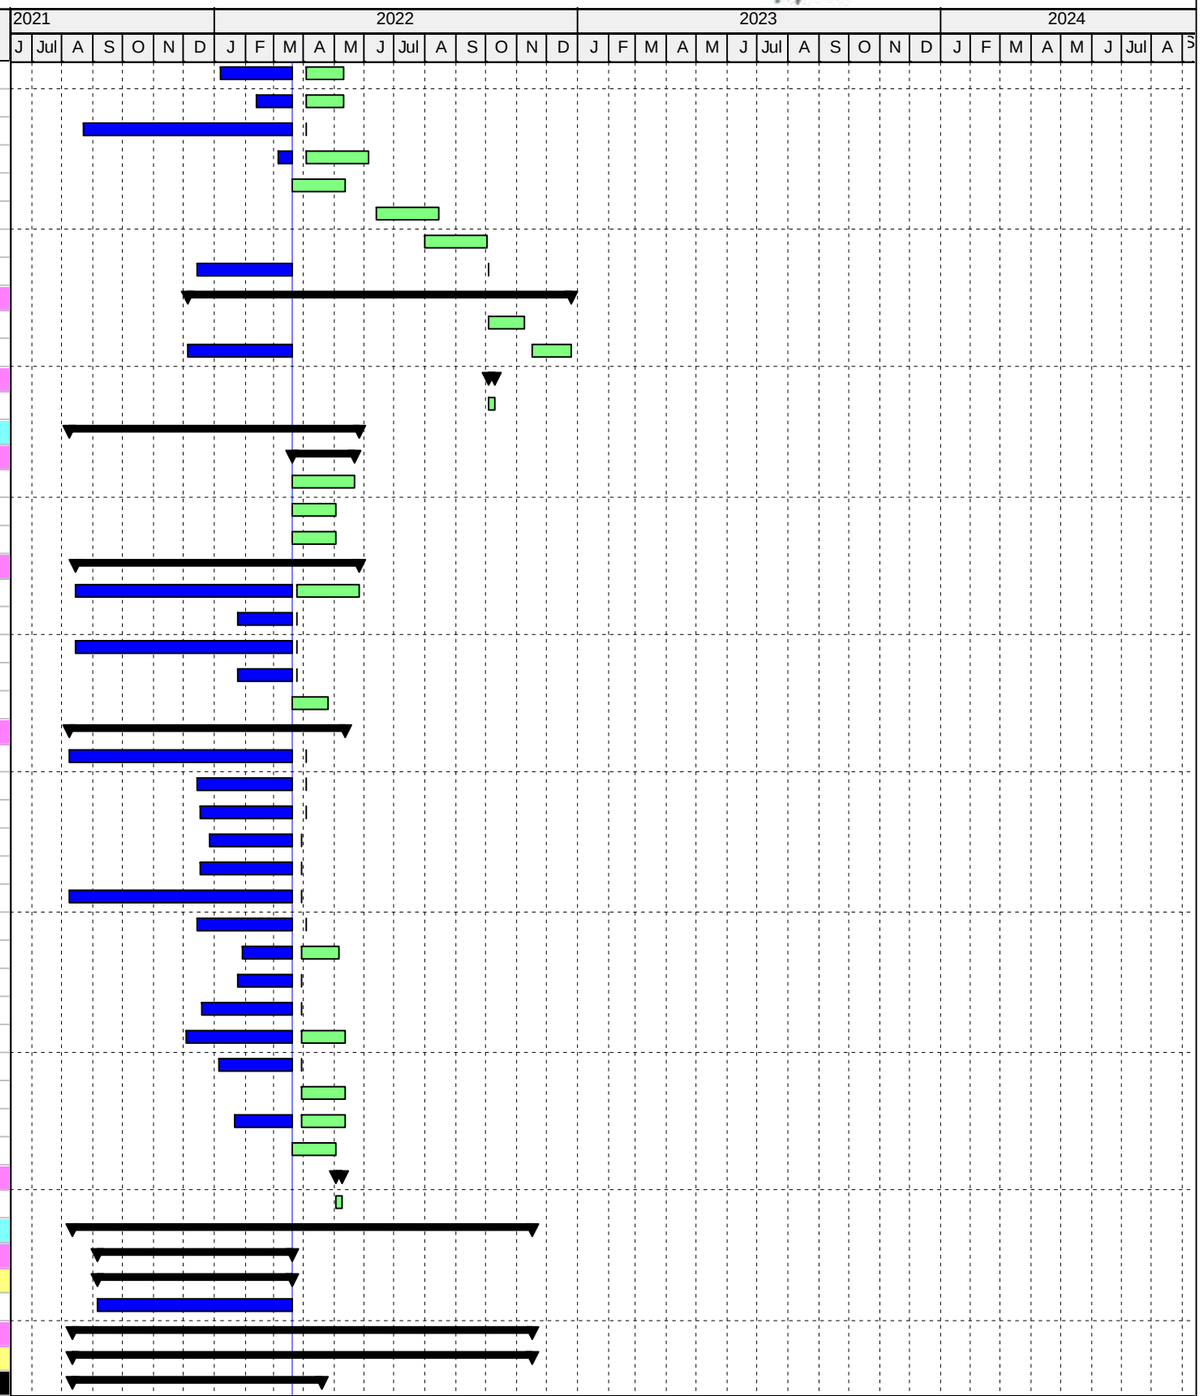


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P04	Geotechnical Investigation Plan for Well Pads	44	100%	$64.35	11-Aug-21	19-Apr-22
Report		44	0%	$740.03	03-Oct-22	16-Nov-22
P04	Geotechnical Investigation Report - W035	44	0%	$740.03	03-Oct-22	16-Nov-22
Survey		46	0%	$107.25	22-Aug-22	06-Oct-22
Drawing/Diagram		46	0%	$107.25	22-Aug-22	06-Oct-22
P04	Flowline Plan & Profile Drawings - W035	46	0%	$107.25	22-Aug-22	06-Oct-22
QC/QA		116	10.59%	$107.25	20-Sep-21	13-Jul-22
QC Management		116	39.14%	$8.72	08-Dec-21	13-Jul-22
P04-	Project Audit Procedure	44	0%	$0.44	20-Mar-22	02-May-22
P04-	Specification For Final Data Book (FDB) Requirements	44	0%	$0.44	20-Mar-22	02-May-22
P04-	Non Conformance Control Procedure	36	0%	$0.44	03-May-22	07-Jun-22
P04-	Corrective Action Procedure	36	0%	$0.44	08-Jun-22	13-Jul-22
P04-	Material Reciving, Storage, Handling Procedure	39	60%	$0.44	20-Feb-22	27-Apr-22
P04-	Packing, Marking, Transportation Procedure	39	0%	$0.44	20-Mar-22	27-Apr-22
P04-	Criticality Assessment Procedure	39	0%	$1.74	20-Mar-22	27-Apr-22
P04-	Project Quality Plan	44	80%	$3.92	08-Dec-21	02-May-22
P04-	Technical Query Procedure	44	0%	$0.44	30-Mar-22	12-May-22
QC General Document		55	8.57%	$12.73	28-Nov-21	16-May-22
P04-	Quality Control Plan (QCP)	39	60%	$1.82	28-Nov-21	27-Apr-22
P04-	Specification for Welding Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P04-	Heat Treatment Procedure (Pre Heating , PWHT)	44	0%	$1.82	03-Apr-22	16-May-22
P04-	Welder Performance Qualification Test (WQT) Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P04-	NDT Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P04-	Surface Preparation and Coating/Painting Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P04-	Control of Inspection Measuring and Test Equipment Procedu	44	0%	$1.81	03-Apr-22	16-May-22
QC Discipline Document		81	7.99%	$85.80	20-Sep-21	16-May-22
Piping		51	0%	$21.45	27-Mar-22	16-May-22
P04	ITP For Piping Works	44	0%	$2.15	27-Mar-22	09-May-22
P04	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$2.41	03-Apr-22	16-May-22
P04	PIPING WPS (Welding Procedure Specification)	44	0%	$2.41	03-Apr-22	16-May-22
P04	PIPING PQR (Procedure Qualification Record)	44	0%	$2.41	03-Apr-22	16-May-22
P04	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$2.41	03-Apr-22	16-May-22
P04	PIPING WPS (Preliminary Welding Procedure Specification) f	44	0%	$2.41	03-Apr-22	16-May-22
P04	PIPING PQR (Procedure Qualification Record) for Repair We	44	0%	$2.41	03-Apr-22	16-May-22
P04	Field Joint Coating Procedure For Pipeline	44	0%	$2.41	03-Apr-22	16-May-22
P04	Pressure Test Procedure	44	0%	$2.41	03-Apr-22	16-May-22
Telecomm.		44	0%	$4.29	27-Mar-22	09-May-22
P04	ITP For Telecommunication Installation	44	0%	$4.29	27-Mar-22	09-May-22
Safety		44	0%	$4.29	27-Mar-22	09-May-22
P04	ITP For Safety Installation	44	0%	$4.29	27-Mar-22	09-May-22
Architectural		44	0%	$4.29	27-Mar-22	09-May-22
P04	ITP For Architectural Works	44	0%	$4.29	27-Mar-22	09-May-22
Mechanical		44	0%	$4.29	27-Mar-22	09-May-22
P04	ITP For Mechanical Installation	44	0%	$4.29	27-Mar-22	09-May-22
Structure		51	0%	$17.16	27-Mar-22	16-May-22
P04	ITP For Steel Structural Works	44	0%	$1.72	27-Mar-22	09-May-22
P04	Steel Structure WPS (Welding Procedure Specification)	44	0%	$2.57	03-Apr-22	16-May-22
P04	Steel Structure PQR (Procedure Qualification Record)	44	0%	$2.57	03-Apr-22	16-May-22
P04	Steel Structure WPS (Welding Procedure Specification) For F	44	0%	$2.57	03-Apr-22	16-May-22

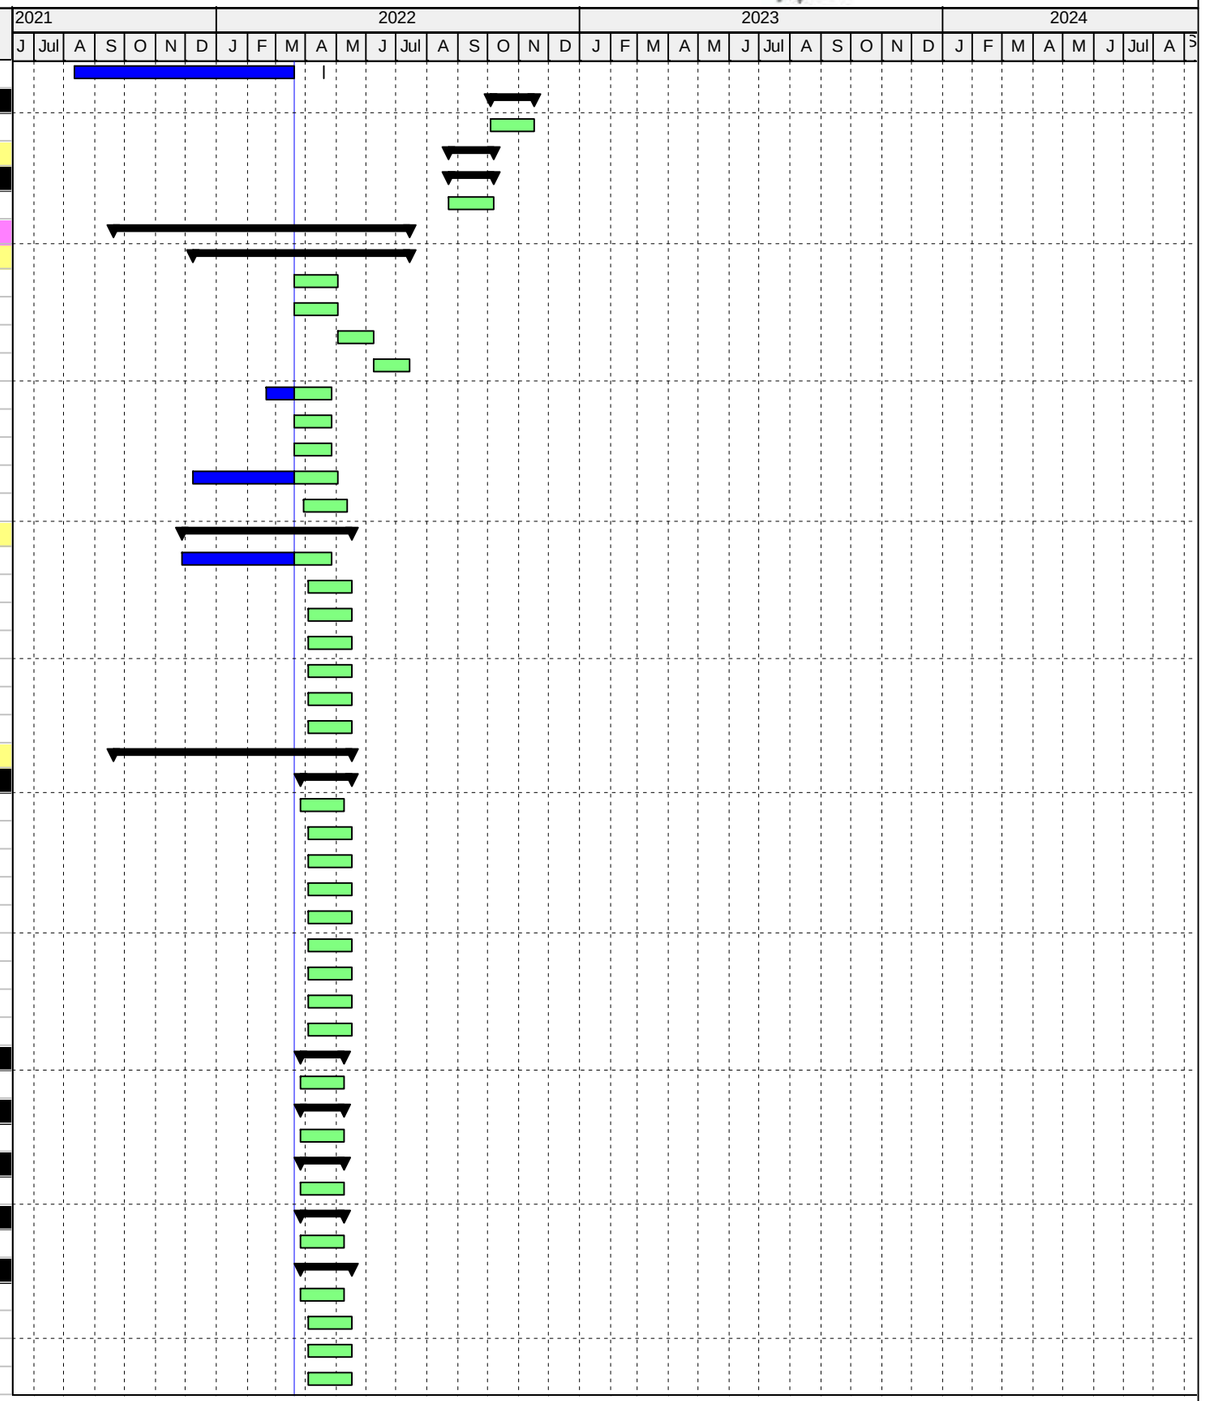

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P04	Steel Structure PQR (Procedure Qualification Record) For R	44	0%	$2.57	03-Apr-22	16-May-22
P04	Weld Map For Steel Structures	44	0%	$2.57	03-Apr-22	16-May-22
P04	NDT Plan For steel Structures	44	0%	$2.57	03-Apr-22	16-May-22
Instrumentation		44	0%	$4.29	27-Mar-22	09-May-22
P04	ITP For I&C Installation	44	0%	$4.29	27-Mar-22	09-May-22
Pipeline		74	15%	$17.16	16-Jan-22	16-May-22
P04	ITP For Pipeline	44	60%	$1.72	16-Jan-22	09-May-22
P04	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	60%	$2.57	23-Feb-22	16-May-22
P04	PIPELINE WPS (Welding Procedure Specification)	44	0%	$2.57	03-Apr-22	16-May-22
P04	PIPELINE PQR (Procedure Qualification Record)	44	0%	$2.57	03-Apr-22	16-May-22
P04	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	0%	$2.57	03-Apr-22	16-May-22
P04	PIPELINE WPS (Preliminary Welding Procedure Specificatior	44	0%	$2.57	03-Apr-22	16-May-22
P04	PIPELINE PQR (Procedure Qualification Record) for Repair \	44	0%	$2.57	03-Apr-22	16-May-22
Civil		44	100%	$4.29	20-Sep-21	27-Mar-22
P04	ITP For Civil Works	44	100%	$4.29	20-Sep-21	27-Mar-22
Electrical		44	0%	$4.29	27-Mar-22	09-May-22
P04	ITP For Electrical Installation	44	0%	$4.29	27-Mar-22	09-May-22
Procurement Engineering		294	7.26%	$812.50	15-Nov-21	29-Dec-22
Piping		96	0%	$211.25	25-Sep-22	29-Dec-22
Pipes		59	0%	$23.49	25-Sep-22	22-Nov-22
P04-E	PMR For Pipes - W035	10	0%	$2.35	25-Sep-22	04-Oct-22
P04-E	TBE For Pipes - W035	30	0%	$3.52	02-Oct-22	31-Oct-22
P04-E	VDR For Pipes - W035	7	0%	$17.62	16-Nov-22	22-Nov-22
Fittings		59	0%	$23.47	25-Sep-22	22-Nov-22
P04-E	PMR For Fittings - W035	10	0%	$2.35	25-Sep-22	04-Oct-22
P04-E	TBE For Fitting - W035	30	0%	$3.52	02-Oct-22	31-Oct-22
P04-E	VDR For Fitting - W035	7	0%	$17.60	16-Nov-22	22-Nov-22
Flanges		59	0%	$23.47	25-Sep-22	22-Nov-22
P04-E	PMR For Flanges - W035	10	0%	$2.35	25-Sep-22	04-Oct-22
P04-E	TBE For Flanges - W035	30	0%	$3.52	02-Oct-22	31-Oct-22
P04-E	VDR For Flanges - W035	7	0%	$17.60	16-Nov-22	22-Nov-22
Manual Valves		59	0%	$23.47	25-Sep-22	22-Nov-22
P04-E	PMR For Manual Valves - W035	10	0%	$2.35	25-Sep-22	04-Oct-22
P04-E	TBE For Manual Valves - W035	30	0%	$3.52	02-Oct-22	31-Oct-22
P04-E	VDR For Manual Valves - W035	7	0%	$17.60	16-Nov-22	22-Nov-22
Gaskets		59	0%	$23.47	25-Sep-22	22-Nov-22
P04-E	PMR For Gaskets - W035	10	0%	$2.35	25-Sep-22	04-Oct-22
P04-E	TBE For Gaskets - W035	30	0%	$3.52	02-Oct-22	31-Oct-22
P04-E	VDR For Gaskets - W035	7	0%	$17.60	16-Nov-22	22-Nov-22
Bolt & Nuts		59	0%	$23.47	25-Sep-22	22-Nov-22
P04-E	PMR For Bolt/Nuts - W035	10	0%	$2.35	25-Sep-22	04-Oct-22
P04-E	TBE For Bolt/Nuts - W035	30	0%	$3.52	02-Oct-22	31-Oct-22
P04-E	VDR For Bolt/Nuts - W035	7	0%	$17.60	16-Nov-22	22-Nov-22
Sampling Connection		59	0%	$23.47	01-Nov-22	29-Dec-22
P04-E	PMR For Sampling Connection Set - W035	10	0%	$2.35	01-Nov-22	10-Nov-22
P04-E	TBE For Sampling Connection Set - W035	30	0%	$3.52	08-Nov-22	07-Dec-22
P04-E	VDR For Sampling Connection Set - W035	7	0%	$17.60	23-Dec-22	29-Dec-22
Stone Trap		59	0%	$23.47	01-Nov-22	29-Dec-22
P04-E	PMR For Stone Trap - W035	10	0%	$2.35	01-Nov-22	10-Nov-22



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P04-E	TBE For Stone Trap - W035	30	0%	$3.52	08-Nov-22	07-Dec-22
P04-E	VDR For Stone Trap - W035	7	0%	$17.60	23-Dec-22	29-Dec-22
Pipe Support		34	0%	$23.47	01-Nov-22	04-Dec-22
P04-E	PMR For Pipe Support - W035	5	0%	$2.35	01-Nov-22	05-Nov-22
P04-E	TBE For Pipe Support - W035	5	0%	$3.52	08-Nov-22	12-Nov-22
P04-E	VDR For Pipe Support - W035	7	0%	$17.60	28-Nov-22	04-Dec-22
Pipeline		74	7.5%	$47.13	19-Feb-22	01-Jul-22
Line Pipe		74	15%	$23.56	19-Feb-22	19-Jun-22
P04-E	PMR For Line Pipes - W035	10	0%	$2.36	19-May-22	28-May-22
P04-E	TBE For Line Pipes - W035	30	100%	$3.53	19-Feb-22	26-May-22
P04-E	VDR For Line Pipes - W035	7	0%	$17.67	13-Jun-22	19-Jun-22
Flow Line Support		34	0%	$23.56	29-May-22	01-Jul-22
P04-E	PMR For Flowline Support - W035	5	0%	$2.36	29-May-22	02-Jun-22
P04-E	TBE For Flowline Support - W035	5	0%	$3.53	05-Jun-22	09-Jun-22
P04-E	VDR For Flowline Support - W035	7	0%	$17.67	25-Jun-22	01-Jul-22
Control & Instrumentation		291	20.58%	$269.75	15-Nov-21	29-Oct-22
WHCP/HPU		37	24.98%	$95.22	15-Nov-21	29-Jun-22
P04-E	PMR For WHCP/HPU - W035	10	100%	$9.52	15-Nov-21	19-Apr-22
P04-E	TBE/TBA For WHCP/HPU - W035	30	100%	$14.28	01-Dec-21	19-Apr-22
P04-E	VDR/TBA For WHCP/HPU - W035	7	0%	$71.42	23-Jun-22	29-Jun-22
Field Instrumentations		114	10%	$79.33	13-Dec-21	23-Jul-22
P04-E	PMR For Field Instrumentations - W035	10	100%	$7.93	13-Dec-21	13-May-22
P04-E	TBE/TBA For Field Instrumentations - W035	30	0%	$11.90	13-May-22	11-Jun-22
P04-E	VDR/TBA For Field Instrumentations - W035	7	0%	$59.50	17-Jul-22	23-Jul-22
Instrument Bulk Items		128	24.99%	$95.19	16-Jan-22	29-Oct-22
P04-E	PMR For Instrument Bulk Items - W035	10	100%	$9.52	16-Jan-22	18-Sep-22
P04-E	TBE/TBA For Instrument Bulk Items - W035	30	100%	$14.28	02-Feb-22	18-Sep-22
P04-E	VDR/TBA For Instrument Bulk Items - W035	7	0%	$71.40	23-Oct-22	29-Oct-22
Safety & Fire Fighting		121	0%	$190.13	17-Aug-22	15-Dec-22
Fire Fighting and Safety Equipment		79	0%	$102.99	17-Aug-22	03-Nov-22
P04-E	PMR For Fire Fighting and Safety Equipment - W035	10	0%	$10.30	17-Aug-22	26-Aug-22
P04-E	TBE For Fire Fighting and Safety Equipment - W035	30	0%	$15.45	24-Aug-22	22-Sep-22
P04-E	VDR For Fire Fighting and Safety Equipment - W035	7	0%	$77.24	28-Oct-22	03-Nov-22
Safety Sign		79	0%	$87.13	28-Sep-22	15-Dec-22
P04-E	PMR For Fire Safety Sign - W035	10	0%	$8.71	28-Sep-22	07-Oct-22
P04-E	TBE For Fire Safety Sign - W035	30	0%	$13.07	05-Oct-22	03-Nov-22
P04-E	VDR For Fire Safety Sign - W035	7	0%	$65.35	09-Dec-22	15-Dec-22
Structure		42	0%	$47.13	10-May-22	20-Jun-22
Steel Structure Items		42	0%	$23.56	10-May-22	20-Jun-22
P04-E	PMR For Steel Structure Items - W035	10	0%	$2.36	10-May-22	19-May-22
P04-E	TBE For Steel Structure Items - W035	30	0%	$3.53	17-May-22	15-Jun-22
P04-E	VDR For Steel Structure Items - W035	5	0%	$17.67	16-Jun-22	20-Jun-22
Anchor Bolts		42	0%	$23.56	10-May-22	20-Jun-22
P04-E	PMR For Anchor Bolts - W035	10	0%	$2.36	10-May-22	19-May-22
P04-E	TBE For Anchor Bolts - W035	30	0%	$3.53	17-May-22	15-Jun-22
P04-E	VDR For Anchor Bolts - W035	5	0%	$17.67	16-Jun-22	20-Jun-22
Civil		17	0%	$47.13	15-Aug-22	31-Aug-22
Geomembrane		17	0%	$23.56	15-Aug-22	31-Aug-22
P04-E	PMR For Geomembrane - W035	5	0%	$2.36	15-Aug-22	19-Aug-22
P04-E	TBE For Geomembrane - W035	5	0%	$3.53	22-Aug-22	26-Aug-22




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P04-E	VDR For Geomembrane - W035	5	0%	$17.67	27-Aug-22	31-Aug-22
Geotextile		17	0%	$23.56	15-Aug-22	31-Aug-22
P04-E	PMR For Geotextile - W035	5	0%	$2.36	15-Aug-22	19-Aug-22
P04-E	TBE For Geotextile - W035	5	0%	$3.53	22-Aug-22	26-Aug-22
P04-E	VDR For Geotextile - W035	5	0%	$17.67	27-Aug-22	31-Aug-22
Commissioning Engineering		450	0%	$162.50	20-Mar-22	12-Jun-23
Procedure/Plan		450	0%	$162.50	20-Mar-22	12-Jun-23
P04-EF	Operability Review	5	0%	$32.50	14-May-23	18-May-23
P04-EF	Pre-Commissioning, Commissioning & Startup Procedure - W	44	0%	$97.50	20-Mar-22	02-May-22
P04-EF	Operating Manual - W035	30	0%	$32.50	14-May-23	12-Jun-23
Field Engineering		336	0%	$1,218.75	03-Sep-22	05-Aug-23
P04-EP	Technical/Site Queries	44	0%	$609.38	03-Sep-22	17-Oct-22
P04-EP	As-Built Document Booklets - W035	10	0%	$609.38	26-Jul-23	05-Aug-23
Engineering Final Documentation		20	0%	$812.50	05-Aug-23	25-Aug-23
P04-EP	Final Engineering Dossier - W035	20	0%	$812.50	05-Aug-23	25-Aug-23
PROCUREMENT		390	0%	$324,211.00	01-Feb-22	13-May-23
Wellhead Facility and Flowline		390	0%	$215,243.68	01-Feb-22	13-May-23
Piping		194	0%	$27,572.72	01-Nov-22	13-May-23
Pipes - W035		184	0%	$5,514.54	01-Nov-22	03-May-23
P04-E	Tendering & Selection	10	0%	$220.58	01-Nov-22	10-Nov-22
P04-E	Contract Effectiveness / PO	5	0%	$330.87	11-Nov-22	15-Nov-22
P04-E	Manufacturing / Fabrication / Supply	150	0%	$2,757.27	16-Nov-22	14-Apr-23
P04-E	Final Inspection	7	0%	$551.45	15-Apr-23	21-Apr-23
P04-E	Delivery On Site	7	0%	$1,378.64	22-Apr-23	28-Apr-23
P04-E	Submitting Vendor Data Book	5	0%	$275.73	29-Apr-23	03-May-23
Fittings - W035		184	0%	$2,067.95	01-Nov-22	03-May-23
P04-E	Tendering & Selection	10	0%	$82.72	01-Nov-22	10-Nov-22
P04-E	Contract Effectiveness / PO	5	0%	$124.08	11-Nov-22	15-Nov-22
P04-E	Manufacturing / Fabrication / Supply	150	0%	$1,033.98	16-Nov-22	14-Apr-23
P04-E	Final Inspection	7	0%	$206.80	15-Apr-23	21-Apr-23
P04-E	Delivery On Site	7	0%	$516.99	22-Apr-23	28-Apr-23
P04-E	Submitting Vendor Data Book	5	0%	$103.40	29-Apr-23	03-May-23
Flanges - W035		184	0%	$2,067.95	01-Nov-22	03-May-23
P04-E	Tendering & Selection	10	0%	$82.72	01-Nov-22	10-Nov-22
P04-E	Contract Effectiveness / PO	5	0%	$124.08	11-Nov-22	15-Nov-22
P04-E	Manufacturing / Fabrication / Supply	150	0%	$1,033.98	16-Nov-22	14-Apr-23
P04-E	Final Inspection	7	0%	$206.80	15-Apr-23	21-Apr-23
P04-E	Delivery On Site	7	0%	$516.99	22-Apr-23	28-Apr-23
P04-E	Submitting Vendor Data Book	5	0%	$103.40	29-Apr-23	03-May-23
Manual Valves - W035		194	0%	$9,650.45	01-Nov-22	13-May-23
P04-E	Tendering & Selection	10	0%	$386.02	01-Nov-22	10-Nov-22
P04-E	Contract Effectiveness / PO	5	0%	$579.03	11-Nov-22	15-Nov-22
P04-E	Manufacturing / Fabrication / Supply	160	0%	$4,825.23	16-Nov-22	24-Apr-23
P04-E	Final Inspection	7	0%	$965.05	25-Apr-23	01-May-23
P04-E	Delivery On Site	7	0%	$1,930.09	02-May-23	08-May-23
P04-E	Submitting Vendor Data Book	5	0%	$482.52	09-May-23	13-May-23
P04-E	Delivering Spare Parts	5	0%	$482.52	09-May-23	13-May-23
Gaskets - W035		184	0%	$827.18	01-Nov-22	03-May-23
P04-E	Tendering & Selection	10	0%	$33.09	01-Nov-22	10-Nov-22

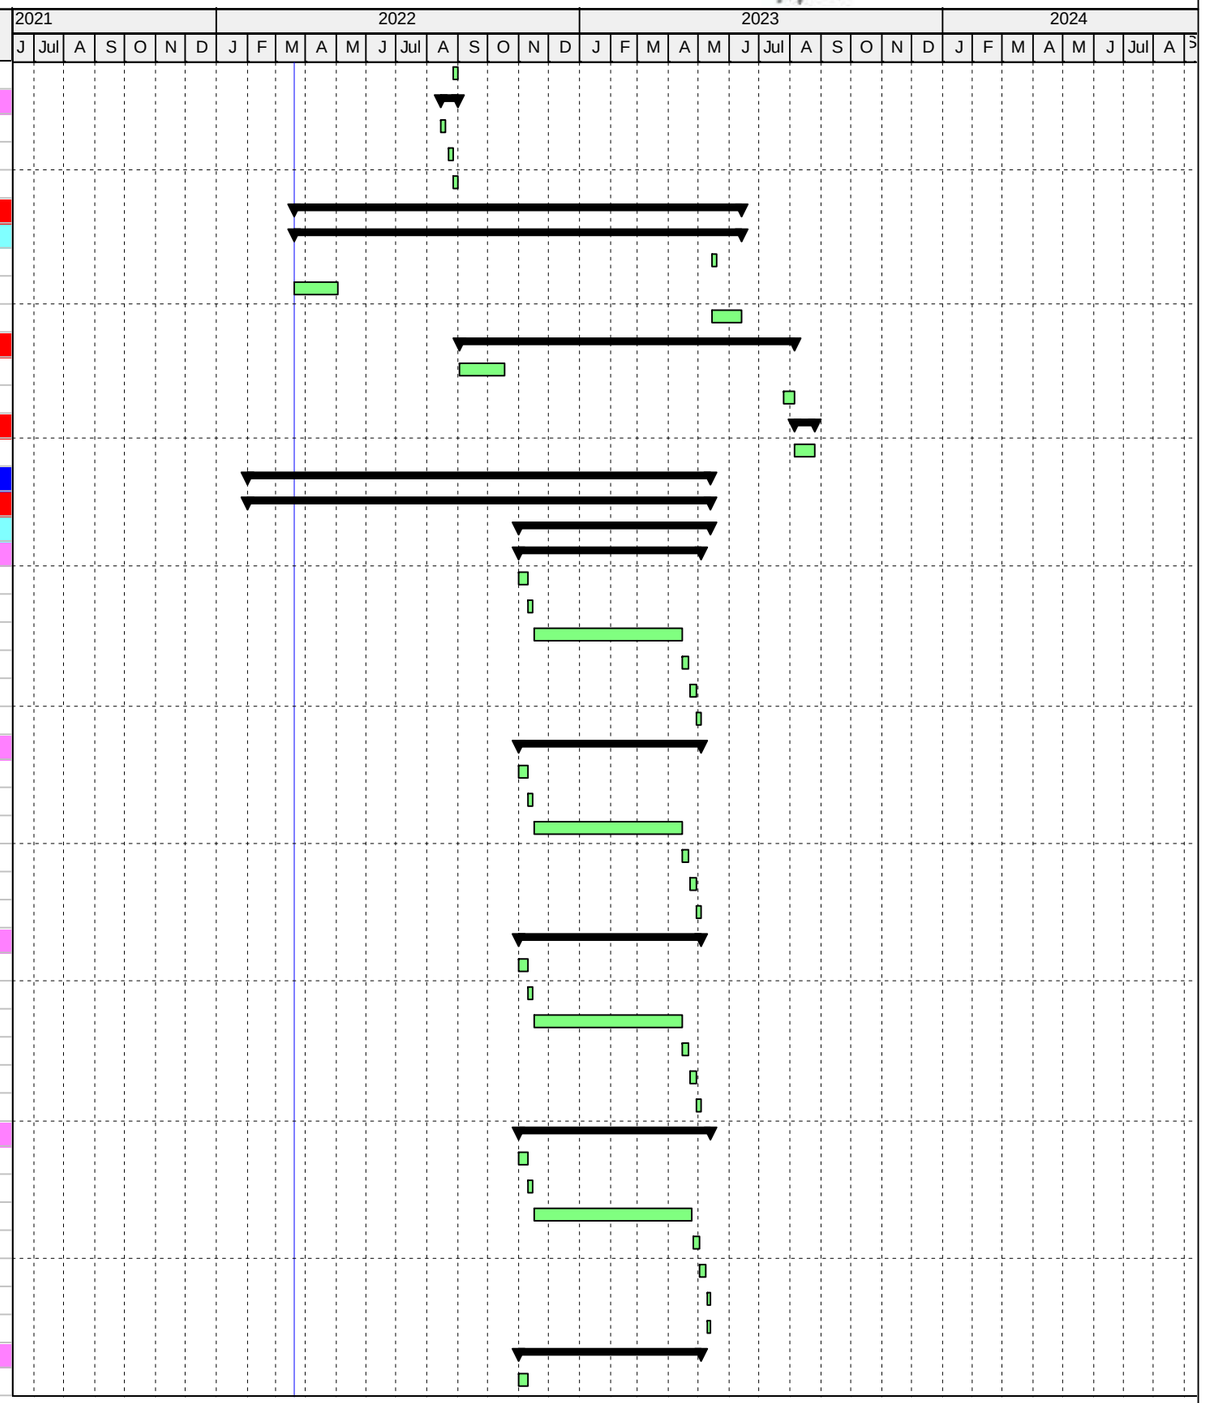


Actual Level of Effort | Remaining Work | Milestone

Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P04-E	Contract Effectiveness / PO	5	0%	$49.63	11-Nov-22	15-Nov-22
P04-E	Manufacturing / Fabrication / Supply	150	0%	$413.59	16-Nov-22	14-Apr-23
P04-E	Final Inspection	7	0%	$82.72	15-Apr-23	21-Apr-23
P04-E	Delivery On Site	7	0%	$206.80	22-Apr-23	28-Apr-23
P04-E	Submitting Vendor Data Book	5	0%	$41.36	29-Apr-23	03-May-23
Bolt/Nuts - W035		144	0%	$551.45	01-Nov-22	24-Mar-23
P04-E	Tendering & Selection	10	0%	$22.06	01-Nov-22	10-Nov-22
P04-E	Contract Effectiveness / PO	5	0%	$33.09	11-Nov-22	15-Nov-22
P04-E	Manufacturing / Fabrication / Supply	110	0%	$275.73	16-Nov-22	05-Mar-23
P04-E	Final Inspection	7	0%	$55.15	06-Mar-23	12-Mar-23
P04-E	Delivery On Site	7	0%	$137.86	13-Mar-23	19-Mar-23
P04-E	Submitting Vendor Data Book	5	0%	$27.57	20-Mar-23	24-Mar-23
Sampling Connection Set - W035		94	0%	$1,378.64	08-Dec-22	11-Mar-23
P04-E	Tendering & Selection	10	0%	$55.15	08-Dec-22	17-Dec-22
P04-E	Contract Effectiveness / PO	5	0%	$82.72	18-Dec-22	22-Dec-22
P04-E	Manufacturing / Fabrication / Supply	60	0%	$689.32	23-Dec-22	20-Feb-23
P04-E	Final Inspection	7	0%	$137.86	21-Feb-23	27-Feb-23
P04-E	Delivery On Site	7	0%	$344.66	28-Feb-23	06-Mar-23
P04-E	Submitting Vendor Data Book	5	0%	$68.93	07-Mar-23	11-Mar-23
Stone Trap - W035		94	0%	$4,135.91	08-Dec-22	11-Mar-23
P04-E	Tendering & Selection	10	0%	$165.44	08-Dec-22	17-Dec-22
P04-E	Contract Effectiveness / PO	5	0%	$248.15	18-Dec-22	22-Dec-22
P04-E	Manufacturing / Fabrication / Supply	60	0%	$2,067.95	23-Dec-22	20-Feb-23
P04-E	Final Inspection	7	0%	$413.59	21-Feb-23	27-Feb-23
P04-E	Delivery On Site	7	0%	$1,033.98	28-Feb-23	06-Mar-23
P04-E	Submitting Vendor Data Book	5	0%	$206.80	07-Mar-23	11-Mar-23
Pipe Support - W035		94	0%	$1,378.64	13-Nov-22	14-Feb-23
P04-E	Tendering & Selection	10	0%	$55.15	13-Nov-22	22-Nov-22
P04-E	Contract Effectiveness / PO	5	0%	$82.72	23-Nov-22	27-Nov-22
P04-E	Manufacturing / Fabrication / Supply	60	0%	$689.32	28-Nov-22	26-Jan-23
P04-E	Final Inspection	7	0%	$137.86	27-Jan-23	02-Feb-23
P04-E	Delivery On Site	7	0%	$344.66	03-Feb-23	09-Feb-23
P04-E	Submitting Vendor Data Book	5	0%	$68.93	10-Feb-23	14-Feb-23
Pipeline		184	0%	$161,066.85	29-May-22	28-Nov-22
Line Pipes - W035		184	0%	$136,906.82	29-May-22	28-Nov-22
P04-E	Tendering & Selection	10	0%	$5,476.27	29-May-22	07-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$8,214.41	08-Jun-22	12-Jun-22
P04-E	Manufacturing / Fabrication / Supply	150	0%	$68,453.41	13-Jun-22	09-Nov-22
P04-E	Final Inspection	7	0%	$13,690.68	10-Nov-22	16-Nov-22
P04-E	Delivery On Site	7	0%	$34,226.71	17-Nov-22	23-Nov-22
P04-E	Submitting Vendor Data Book	5	0%	$6,845.34	24-Nov-22	28-Nov-22
Flow Line Support - W035		154	0%	$24,160.03	10-Jun-22	10-Nov-22
P04-E	Tendering & Selection	10	0%	$966.40	10-Jun-22	19-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$1,449.60	20-Jun-22	24-Jun-22
P04-E	Manufacturing / Fabrication / Supply	120	0%	$12,080.01	25-Jun-22	22-Oct-22
P04-E	Final Inspection	7	0%	$2,416.00	23-Oct-22	29-Oct-22
P04-E	Delivery On Site	7	0%	$6,040.01	30-Oct-22	05-Nov-22
P04-E	Submitting Vendor Data Book	5	0%	$1,208.00	06-Nov-22	10-Nov-22
Control & Instrumentation		271	0%	$25,420.28	01-Feb-22	14-Jan-23

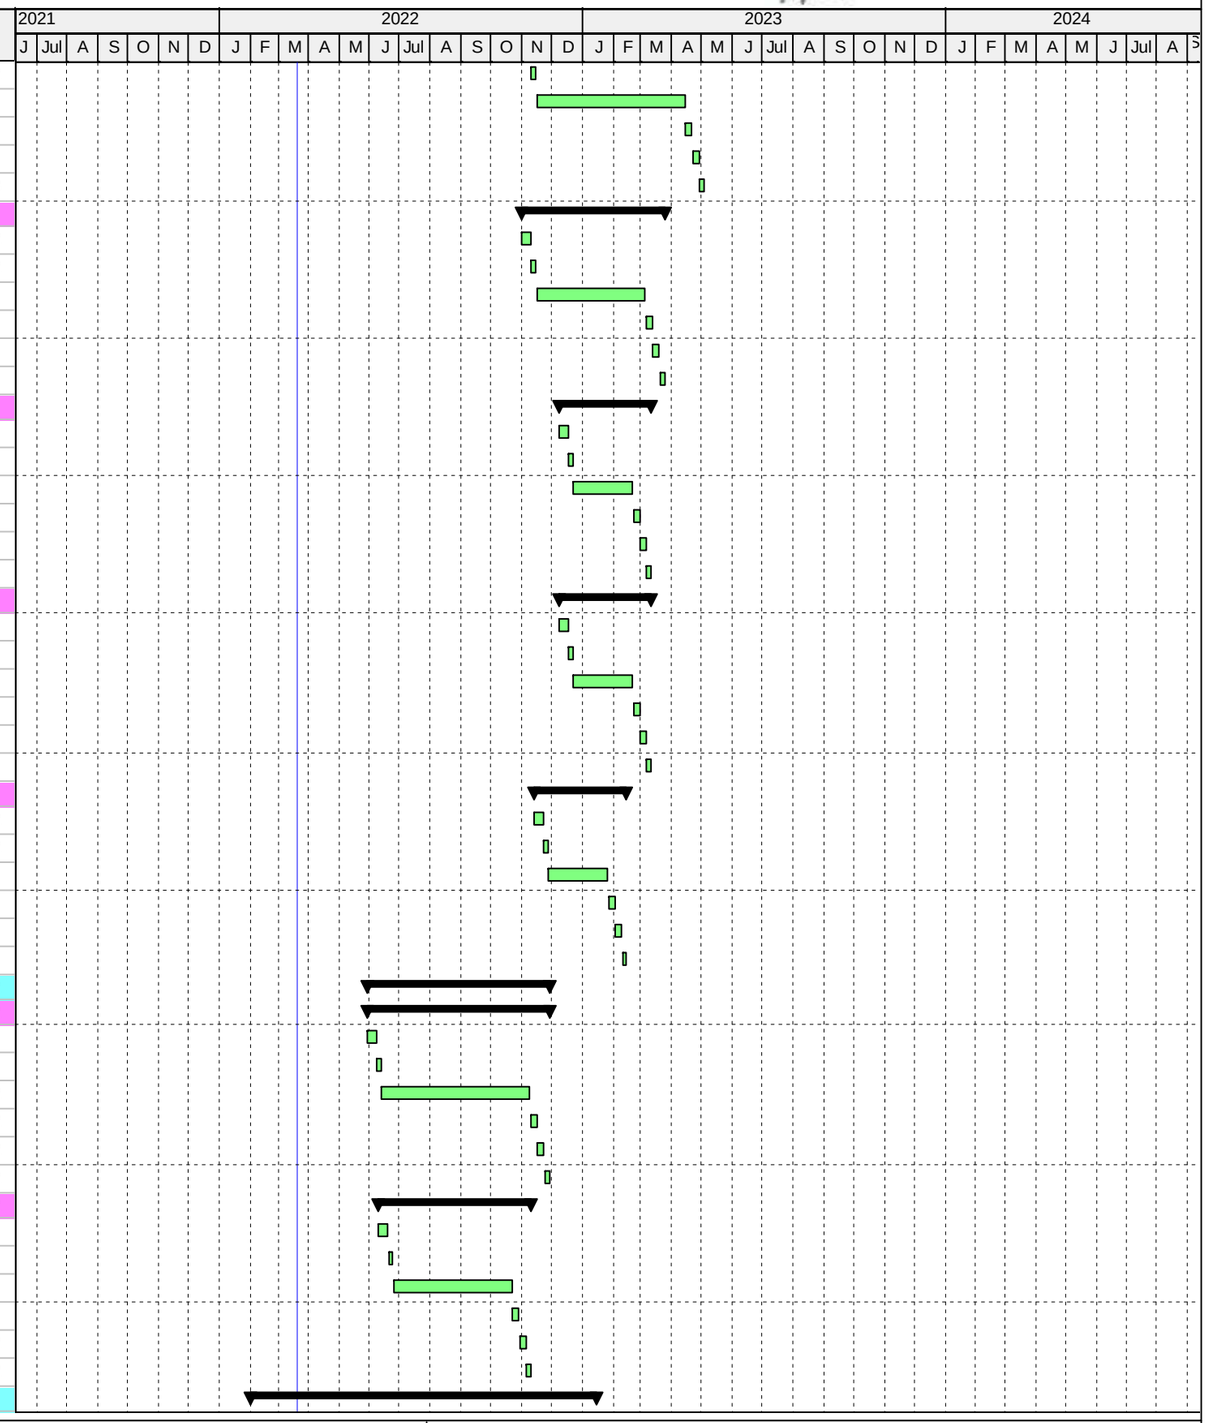


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
WHCP/HPU - W035		234	0%	$23,895.06	01-Feb-22	08-Dec-22
P04-E	Tendering & Selection	15	0%	$955.80	01-Feb-22	17-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$1,433.70	18-Jun-22	22-Jun-22
P04-E	Manufacturing / Fabrication / Supply	140	0%	$11,947.53	23-Jun-22	09-Nov-22
P04-E	Final Inspection	12	0%	$2,389.51	10-Nov-22	21-Nov-22
P04-E	Delivery On Site	7	0%	$4,779.01	22-Nov-22	28-Nov-22
P04-E	Submitting Vendor Data Book	5	0%	$1,194.75	29-Nov-22	03-Dec-22
P04-E	Delivering Spare Parts	5	0%	$1,194.75	04-Dec-22	08-Dec-22
Field Instrumentations - W035		144	0%	$1,271.01	12-Jun-22	02-Nov-22
P04-E	Tendering & Selection	30	0%	$50.84	12-Jun-22	11-Jul-22
P04-E	Contract Effectiveness / PO	5	0%	$76.26	12-Jul-22	16-Jul-22
P04-E	Manufacturing / Fabrication / Supply	80	0%	$635.51	17-Jul-22	04-Oct-22
P04-E	Final Inspection	12	0%	$127.10	05-Oct-22	16-Oct-22
P04-E	Delivery On Site	7	0%	$254.20	17-Oct-22	23-Oct-22
P04-E	Submitting Vendor Data Book	5	0%	$63.55	24-Oct-22	28-Oct-22
P04-E	Delivering Spare Parts	5	0%	$63.55	29-Oct-22	02-Nov-22
Instrument Tube and Fitting - W035		119	0%	$203.36	18-Sep-22	14-Jan-23
P04-E	Tendering & Selection	30	0%	$8.13	18-Sep-22	17-Oct-22
P04-E	Contract Effectiveness / PO	5	0%	$12.20	18-Oct-22	22-Oct-22
P04-E	Manufacturing / Fabrication / Supply	60	0%	$101.68	23-Oct-22	21-Dec-22
P04-E	Final Inspection	12	0%	$20.34	22-Dec-22	02-Jan-23
P04-E	Delivery On Site	7	0%	$50.84	03-Jan-23	09-Jan-23
P04-E	Submitting Vendor Data Book	5	0%	$10.17	10-Jan-23	14-Jan-23
Instrument Cable Tray - W035		119	0%	$50.84	13-May-22	08-Sep-22
P04-E	Tendering & Selection	30	0%	$2.03	13-May-22	11-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$3.05	12-Jun-22	16-Jun-22
P04-E	Manufacturing / Fabrication / Supply	60	0%	$25.42	17-Jun-22	15-Aug-22
P04-E	Final Inspection	12	0%	$5.08	16-Aug-22	27-Aug-22
P04-E	Delivery On Site	7	0%	$12.71	28-Aug-22	03-Sep-22
P04-E	Submitting Vendor Data Book	5	0%	$2.54	04-Sep-22	08-Sep-22
Safety & Fire Fighting		121	0%	$1,183.84	23-Sep-22	21-Jan-23
Fire Fighting and Safety Equipment - W035		79	0%	$947.07	23-Sep-22	10-Dec-22
P04-E	Tendering & Selection	30	0%	$37.88	23-Sep-22	22-Oct-22
P04-E	Contract Effectiveness / PO	5	0%	$56.82	23-Oct-22	27-Oct-22
P04-E	Manufacturing / Fabrication / Supply	20	0%	$473.54	28-Oct-22	16-Nov-22
P04-E	Final Inspection	12	0%	$94.71	17-Nov-22	28-Nov-22
P04-E	Delivery On Site	7	0%	$236.77	29-Nov-22	05-Dec-22
P04-E	Submitting Vendor Data Book	5	0%	$47.35	06-Dec-22	10-Dec-22
Fire Safety Sign - W035		79	0%	$236.77	04-Nov-22	21-Jan-23
P04-E	Tendering & Selection	30	0%	$9.47	04-Nov-22	03-Dec-22
P04-E	Contract Effectiveness / PO	5	0%	$14.21	04-Dec-22	08-Dec-22
P04-E	Manufacturing / Fabrication / Supply	20	0%	$118.38	09-Dec-22	28-Dec-22
P04-E	Final Inspection	12	0%	$23.68	29-Dec-22	09-Jan-23
P04-E	Delivery On Site	7	0%	$59.19	10-Jan-23	16-Jan-23
P04-E	Submitting Vendor Data Book	5	0%	$11.84	17-Jan-23	21-Jan-23
Extension of Binak B/C Manifold		318	0%	$108,967.32	13-May-22	26-Mar-23
Mechanical		154	0%	$3,748.48	13-May-22	13-Oct-22
Pumps - Extension of Binak B/C Manifold		154	0%	$3,748.48	13-May-22	13-Oct-22
P04-E	Tendering & Selection	15	0%	$149.94	13-May-22	27-May-22

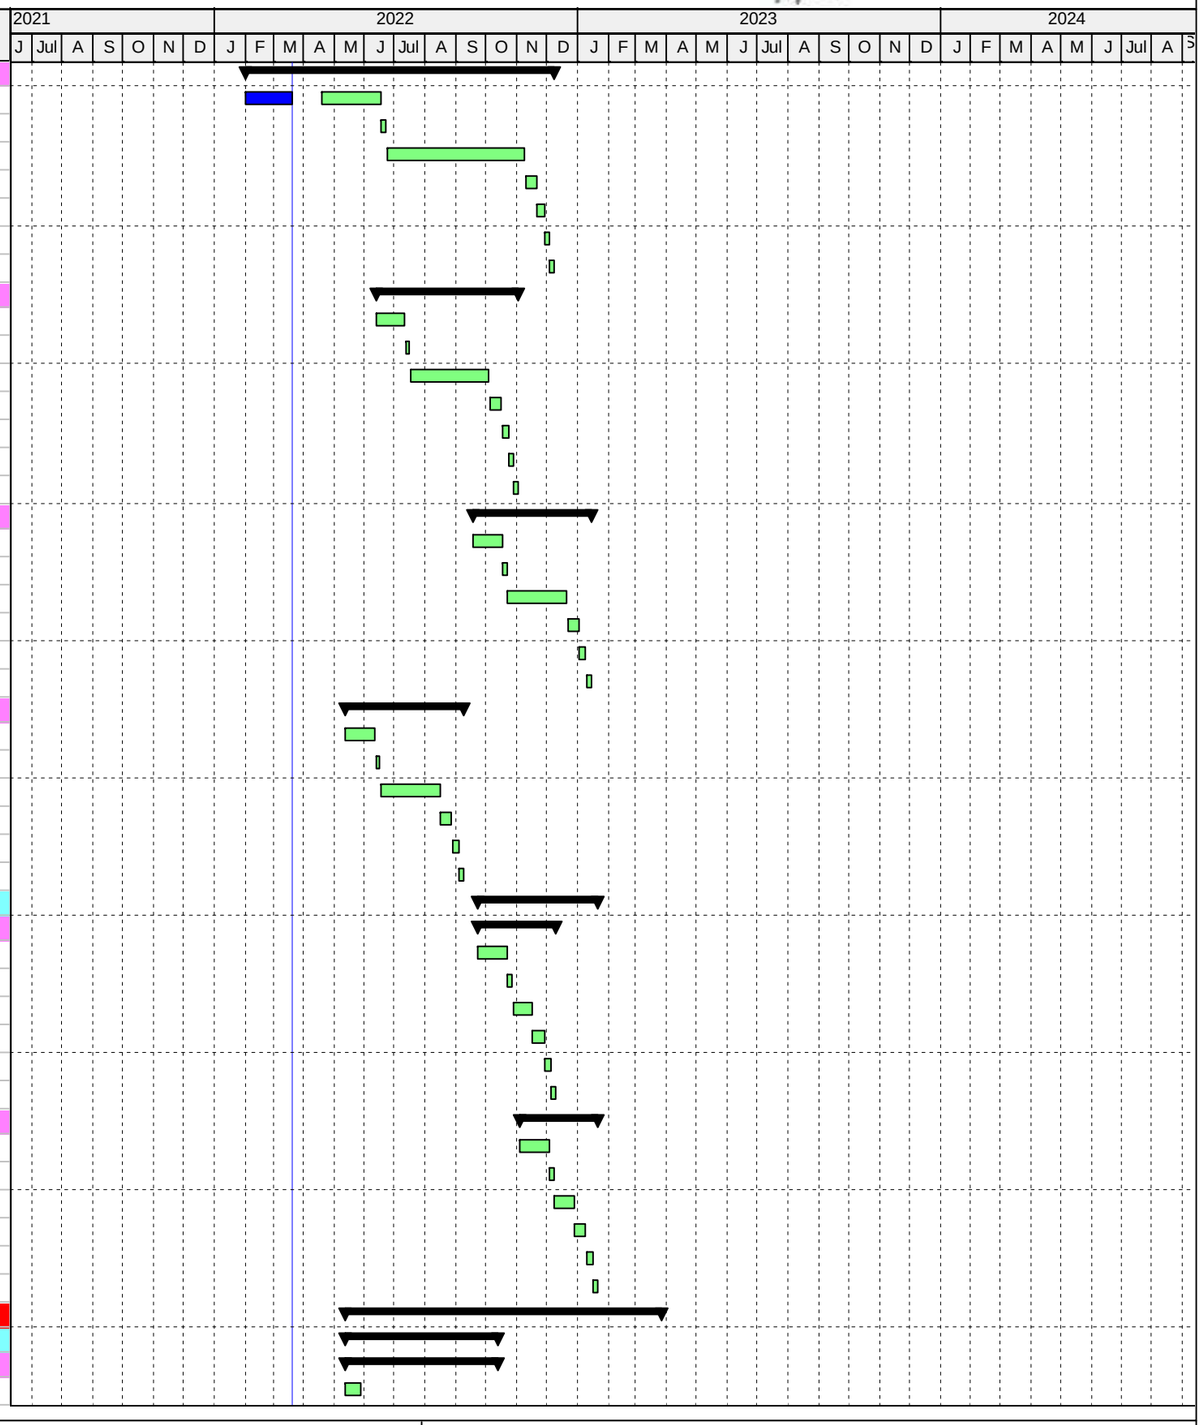


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P04-E	Contract Effectiveness / PO	5	0%	$224.91	28-May-22	01-Jun-22
P04-E	Manufacturing / Fabrication / Supply	110	0%	$1,874.24	02-Jun-22	19-Sep-22
P04-E	Final Inspection	7	0%	$374.85	20-Sep-22	26-Sep-22
P04-E	Delivery On Site	7	0%	$749.70	27-Sep-22	03-Oct-22
P04-E	Submitting Vendor Data Book	5	0%	$187.42	04-Oct-22	08-Oct-22
P04-E	Delivering Spare Parts	5	0%	$187.42	09-Oct-22	13-Oct-22
Piping		301	0%	$23,776.67	16-May-22	12-Mar-23
Pipes - Extension of Binak B/C Manifold		114	0%	$9,700.88	05-Oct-22	26-Jan-23
P04-E	Tendering & Selection	10	0%	$388.04	05-Oct-22	14-Oct-22
P04-E	Contract Effectiveness / PO	5	0%	$582.05	15-Oct-22	19-Oct-22
P04-E	Manufacturing / Fabrication / Supply	80	0%	$4,850.44	20-Oct-22	07-Jan-23
P04-E	Final Inspection	7	0%	$970.09	08-Jan-23	14-Jan-23
P04-E	Delivery On Site	7	0%	$2,425.22	15-Jan-23	21-Jan-23
P04-E	Submitting Vendor Data Book	5	0%	$485.04	22-Jan-23	26-Jan-23
Fittings - Extension of Binak B/C Manifold		124	0%	$1,283.94	04-Nov-22	07-Mar-23
P04-E	Tendering & Selection	10	0%	$51.36	04-Nov-22	13-Nov-22
P04-E	Contract Effectiveness / PO	5	0%	$77.04	14-Nov-22	18-Nov-22
P04-E	Manufacturing / Fabrication / Supply	90	0%	$641.97	19-Nov-22	16-Feb-23
P04-E	Final Inspection	7	0%	$128.39	17-Feb-23	23-Feb-23
P04-E	Delivery On Site	7	0%	$320.99	24-Feb-23	02-Mar-23
P04-E	Submitting Vendor Data Book	5	0%	$64.20	03-Mar-23	07-Mar-23
Flanges - Extension of Binak B/C Manifold		124	0%	$1,283.94	04-Nov-22	07-Mar-23
P04-E	Tendering & Selection	10	0%	$51.36	04-Nov-22	13-Nov-22
P04-E	Contract Effectiveness / PO	5	0%	$77.04	14-Nov-22	18-Nov-22
P04-E	Manufacturing / Fabrication / Supply	90	0%	$641.97	19-Nov-22	16-Feb-23
P04-E	Final Inspection	7	0%	$128.39	17-Feb-23	23-Feb-23
P04-E	Delivery On Site	7	0%	$320.99	24-Feb-23	02-Mar-23
P04-E	Submitting Vendor Data Book	5	0%	$64.20	03-Mar-23	07-Mar-23
Manual Valves - Extension of Binak B/C Manifold		129	0%	$5,706.40	04-Nov-22	12-Mar-23
P04-E	Tendering & Selection	10	0%	$228.26	04-Nov-22	13-Nov-22
P04-E	Contract Effectiveness / PO	5	0%	$342.38	14-Nov-22	18-Nov-22
P04-E	Manufacturing / Fabrication / Supply	90	0%	$2,853.20	19-Nov-22	16-Feb-23
P04-E	Final Inspection	7	0%	$570.64	17-Feb-23	23-Feb-23
P04-E	Delivery On Site	7	0%	$1,141.28	24-Feb-23	02-Mar-23
P04-E	Submitting Vendor Data Book	5	0%	$285.32	03-Mar-23	07-Mar-23
P04-E	Delivering Spare Parts	5	0%	$285.32	08-Mar-23	12-Mar-23
Gaskets - Extension of Binak B/C Manifold		124	0%	$1,545.48	04-Nov-22	07-Mar-23
P04-E	Tendering & Selection	10	0%	$61.82	04-Nov-22	13-Nov-22
P04-E	Contract Effectiveness / PO	5	0%	$92.73	14-Nov-22	18-Nov-22
P04-E	Manufacturing / Fabrication / Supply	90	0%	$772.74	19-Nov-22	16-Feb-23
P04-E	Final Inspection	7	0%	$154.55	17-Feb-23	23-Feb-23
P04-E	Delivery On Site	7	0%	$386.37	24-Feb-23	02-Mar-23
P04-E	Submitting Vendor Data Book	5	0%	$77.27	03-Mar-23	07-Mar-23
Bolt/Nuts - Extension of Binak B/C Manifold		114	0%	$2,377.67	04-Nov-22	25-Feb-23
P04-E	Tendering & Selection	10	0%	$95.11	04-Nov-22	13-Nov-22
P04-E	Contract Effectiveness / PO	5	0%	$142.66	14-Nov-22	18-Nov-22
P04-E	Manufacturing / Fabrication / Supply	80	0%	$1,188.83	19-Nov-22	06-Feb-23
P04-E	Final Inspection	7	0%	$237.77	07-Feb-23	13-Feb-23
P04-E	Delivery On Site	7	0%	$594.42	14-Feb-23	20-Feb-23

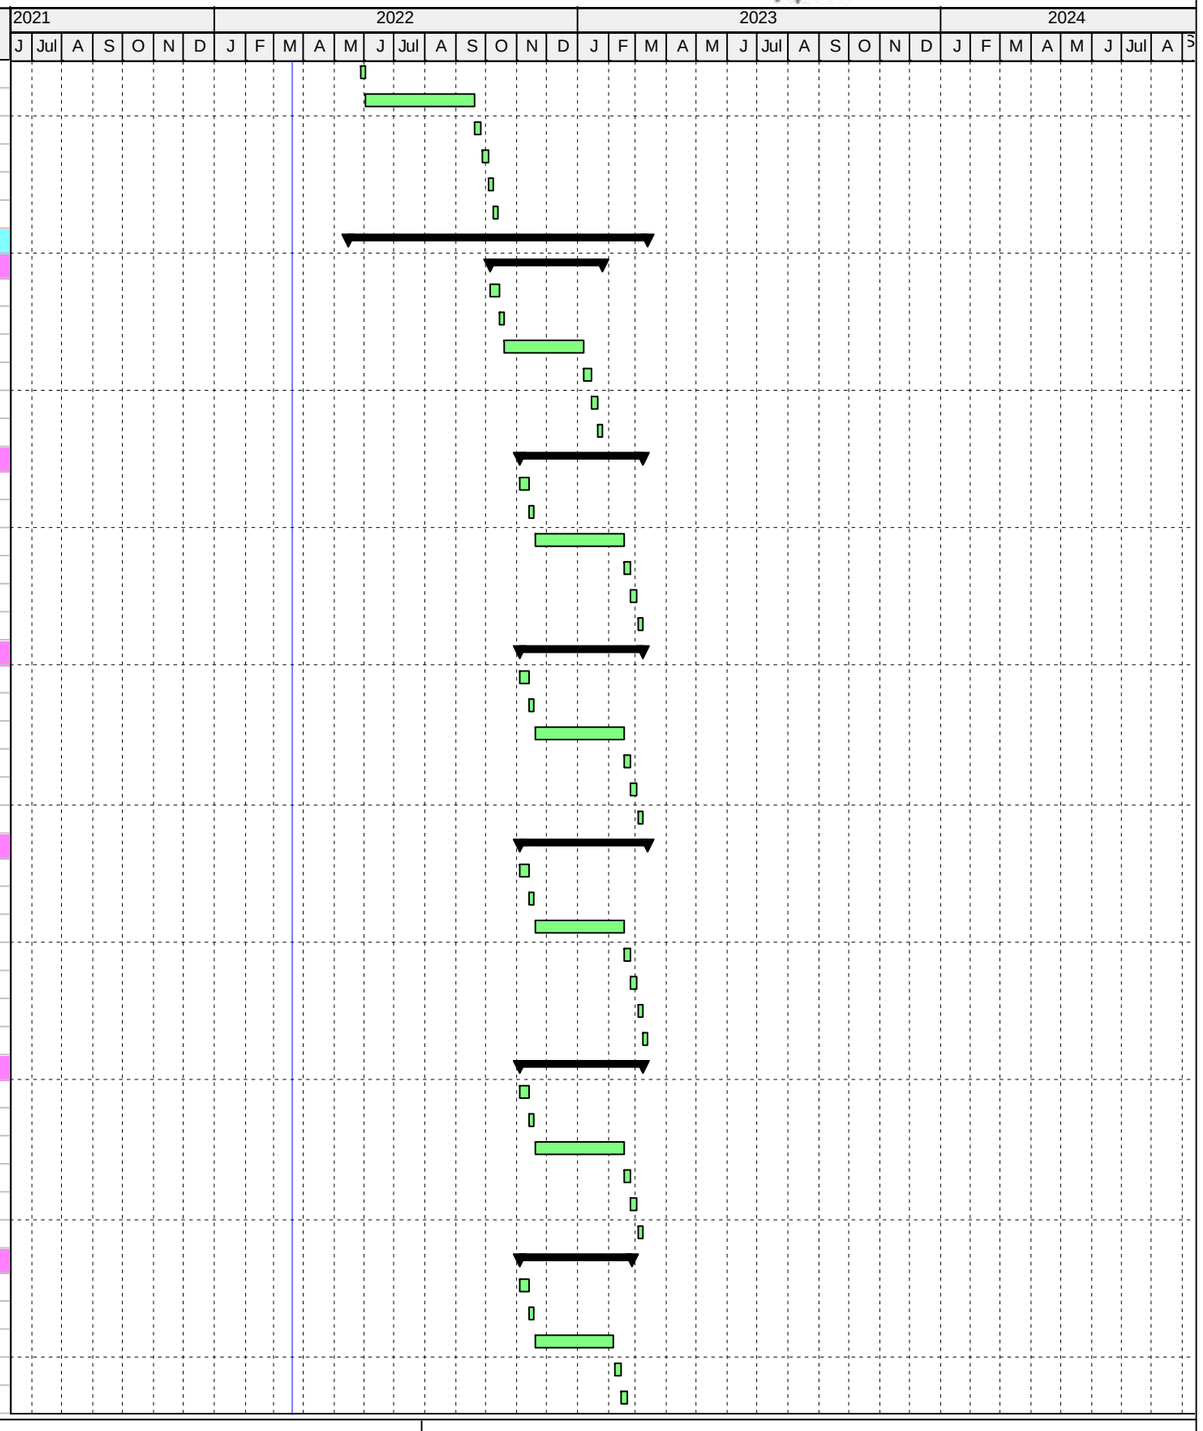


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P04-E	Submitting Vendor Data Book	5	0%	$118.88	21-Feb-23	25-Feb-23
Sampling Connection Set - Extension of Binak B/C Manifold		94	0%	$1,283.94	16-May-22	17-Aug-22
P04-E	Tendering & Selection	10	0%	$51.36	16-May-22	25-May-22
P04-E	Contract Effectiveness / PO	5	0%	$77.04	26-May-22	30-May-22
P04-E	Manufacturing / Fabrication / Supply	60	0%	$641.97	31-May-22	29-Jul-22
P04-E	Final Inspection	7	0%	$128.39	30-Jul-22	05-Aug-22
P04-E	Delivery On Site	7	0%	$320.99	06-Aug-22	12-Aug-22
P04-E	Submitting Vendor Data Book	5	0%	$64.20	13-Aug-22	17-Aug-22
Stone Trap - Extension of Binak B/C Manifold		94	0%	$594.42	07-Oct-22	08-Jan-23
P04-E	Tendering & Selection	10	0%	$23.78	07-Oct-22	16-Oct-22
P04-E	Contract Effectiveness / PO	5	0%	$35.67	17-Oct-22	21-Oct-22
P04-E	Manufacturing / Fabrication / Supply	60	0%	$297.21	22-Oct-22	20-Dec-22
P04-E	Final Inspection	7	0%	$59.44	21-Dec-22	27-Dec-22
P04-E	Delivery On Site	7	0%	$148.60	28-Dec-22	03-Jan-23
P04-E	Submitting Vendor Data Book	5	0%	$29.72	04-Jan-23	08-Jan-23
Control & Instrumentation		317	0%	$60,040.99	14-May-22	26-Mar-23
DCS System - Extension of Binak B/C Manifold		174	0%	$24,616.81	21-May-22	10-Nov-22
P04-E	Tendering & Selection	20	0%	$984.67	21-May-22	09-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$1,477.01	10-Jun-22	14-Jun-22
P04-E	Manufacturing / Fabrication / Supply	120	0%	$12,308.40	15-Jun-22	12-Oct-22
P04-E	Final Inspection	12	0%	$2,461.68	13-Oct-22	24-Oct-22
P04-E	Delivery On Site	7	0%	$4,923.36	25-Oct-22	31-Oct-22
P04-E	Submitting Vendor Data Book	5	0%	$1,230.84	01-Nov-22	05-Nov-22
P04-E	Delivering Spare Parts	5	0%	$1,230.84	06-Nov-22	10-Nov-22
ESD System - Extension of Binak B/C Manifold		169	0%	$17,411.89	05-Jun-22	20-Nov-22
P04-E	Tendering & Selection	20	0%	$696.48	05-Jun-22	24-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$1,044.71	25-Jun-22	29-Jun-22
P04-E	Manufacturing / Fabrication / Supply	120	0%	$8,705.94	30-Jun-22	27-Oct-22
P04-E	Final Inspection	7	0%	$1,741.19	28-Oct-22	03-Nov-22
P04-E	Delivery On Site	7	0%	$3,482.38	04-Nov-22	10-Nov-22
P04-E	Submitting Vendor Data Book	5	0%	$870.59	11-Nov-22	15-Nov-22
P04-E	Delivering Spare Parts	5	0%	$870.59	16-Nov-22	20-Nov-22
F&G System - Extension of Binak B/C Manifold		169	0%	$12,008.20	05-Jun-22	20-Nov-22
P04-E	Tendering & Selection	20	0%	$480.33	05-Jun-22	24-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$720.49	25-Jun-22	29-Jun-22
P04-E	Manufacturing / Fabrication / Supply	120	0%	$6,004.10	30-Jun-22	27-Oct-22
P04-E	Final Inspection	7	0%	$1,200.82	28-Oct-22	03-Nov-22
P04-E	Delivery On Site	7	0%	$2,401.64	04-Nov-22	10-Nov-22
P04-E	Submitting Vendor Data Book	5	0%	$600.41	11-Nov-22	15-Nov-22
P04-E	Delivering Spare Parts	5	0%	$600.41	16-Nov-22	20-Nov-22
ON/OFF & Shutdown Valves - Extension of Binak B/C Manifold		149	0%	$660.45	02-Jun-22	28-Oct-22
P04-E	Tendering & Selection	20	0%	$26.42	02-Jun-22	21-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$39.63	22-Jun-22	26-Jun-22
P04-E	Manufacturing / Fabrication / Supply	100	0%	$330.23	27-Jun-22	04-Oct-22
P04-E	Final Inspection	7	0%	$66.05	05-Oct-22	11-Oct-22
P04-E	Delivery On Site	7	0%	$132.09	12-Oct-22	18-Oct-22
P04-E	Submitting Vendor Data Book	5	0%	$33.02	19-Oct-22	23-Oct-22
P04-E	Delivering Spare Parts	5	0%	$33.02	24-Oct-22	28-Oct-22
Control Valves		144	0%	$660.45	04-Jul-22	24-Nov-22

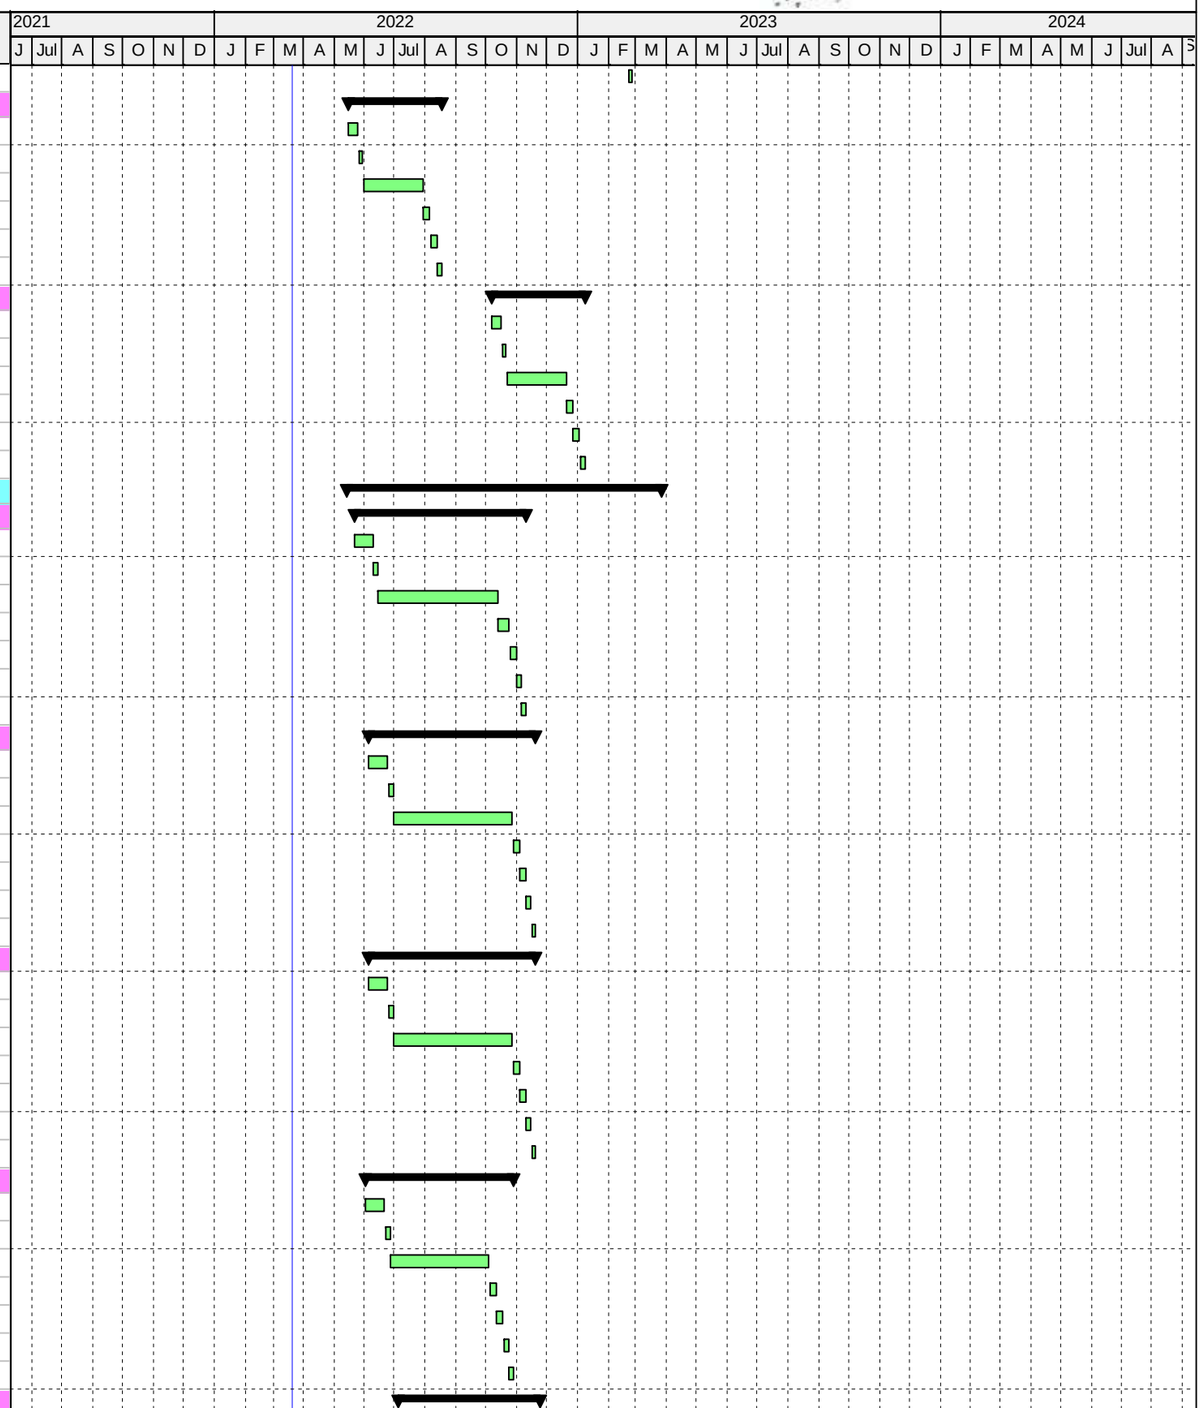


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P04-E	Tendering & Selection	15	0%	$26.42	04-Jul-22	18-Jul-22
P04-E	Contract Effectiveness / PO	5	0%	$39.63	19-Jul-22	23-Jul-22
P04-E	Manufacturing / Fabrication / Supply	100	0%	$330.23	24-Jul-22	31-Oct-22
P04-E	Final Inspection	7	0%	$66.05	01-Nov-22	07-Nov-22
P04-E	Delivery On Site	7	0%	$132.09	08-Nov-22	14-Nov-22
P04-E	Submitting Vendor Data Book	5	0%	$33.02	15-Nov-22	19-Nov-22
P04-E	Delivering Spare Parts	5	0%	$33.02	20-Nov-22	24-Nov-22
Pressure Safety Valves (PSV)		144	0%	$660.45	15-Jul-22	05-Dec-22
P04-E	Tendering & Selection	15	0%	$26.42	15-Jul-22	29-Jul-22
P04-E	Contract Effectiveness / PO	5	0%	$39.63	30-Jul-22	03-Aug-22
P04-E	Manufacturing / Fabrication / Supply	100	0%	$330.23	04-Aug-22	11-Nov-22
P04-E	Final Inspection	7	0%	$66.05	12-Nov-22	18-Nov-22
P04-E	Delivery On Site	7	0%	$132.09	19-Nov-22	25-Nov-22
P04-E	Submitting Vendor Data Book	5	0%	$33.02	26-Nov-22	30-Nov-22
P04-E	Delivering Spare Parts	5	0%	$33.02	01-Dec-22	05-Dec-22
F&G Devices		154	0%	$570.39	04-Aug-22	04-Jan-23
P04-E	Tendering & Selection	15	0%	$22.82	04-Aug-22	18-Aug-22
P04-E	Contract Effectiveness / PO	5	0%	$34.22	19-Aug-22	23-Aug-22
P04-E	Manufacturing / Fabrication / Supply	110	0%	$285.19	24-Aug-22	11-Dec-22
P04-E	Final Inspection	7	0%	$57.04	12-Dec-22	18-Dec-22
P04-E	Delivery On Site	7	0%	$114.08	19-Dec-22	25-Dec-22
P04-E	Submitting Vendor Data Book	5	0%	$28.52	26-Dec-22	30-Dec-22
P04-E	Delivering Spare Parts	5	0%	$28.52	31-Dec-22	04-Jan-23
Orifice and Restriction Orifice Plate		159	0%	$246.17	25-May-22	30-Oct-22
P04-E	Tendering & Selection	15	0%	$9.85	25-May-22	08-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$14.77	09-Jun-22	13-Jun-22
P04-E	Manufacturing / Fabrication / Supply	110	0%	$123.08	14-Jun-22	01-Oct-22
P04-E	Final Inspection	12	0%	$24.62	02-Oct-22	13-Oct-22
P04-E	Delivery On Site	7	0%	$49.23	14-Oct-22	20-Oct-22
P04-E	Submitting Vendor Data Book	5	0%	$12.31	21-Oct-22	25-Oct-22
P04-E	Delivering Spare Parts	5	0%	$12.31	26-Oct-22	30-Oct-22
Corrosion Coupon/Probe		159	0%	$246.17	21-May-22	26-Oct-22
P04-E	Tendering & Selection	15	0%	$9.85	21-May-22	04-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$14.77	05-Jun-22	09-Jun-22
P04-E	Manufacturing / Fabrication / Supply	110	0%	$123.08	10-Jun-22	27-Sep-22
P04-E	Final Inspection	12	0%	$24.62	28-Sep-22	09-Oct-22
P04-E	Delivery On Site	7	0%	$49.23	10-Oct-22	16-Oct-22
P04-E	Submitting Vendor Data Book	5	0%	$12.31	17-Oct-22	21-Oct-22
P04-E	Delivering Spare Parts	5	0%	$12.31	22-Oct-22	26-Oct-22
Pressure Transmitter		159	0%	$330.23	03-Jul-22	08-Dec-22
P04-E	Tendering & Selection	15	0%	$13.21	03-Jul-22	17-Jul-22
P04-E	Contract Effectiveness / PO	5	0%	$19.81	18-Jul-22	22-Jul-22
P04-E	Manufacturing / Fabrication / Supply	110	0%	$165.11	23-Jul-22	09-Nov-22
P04-E	Final Inspection	12	0%	$33.02	10-Nov-22	21-Nov-22
P04-E	Delivery On Site	7	0%	$66.05	22-Nov-22	28-Nov-22
P04-E	Submitting Vendor Data Book	5	0%	$16.51	29-Nov-22	03-Dec-22
P04-E	Delivering Spare Parts	5	0%	$16.51	04-Dec-22	08-Dec-22
Flow Transmitter/ Diff. Pressure Transmitter		159	0%	$330.23	14-May-22	19-Oct-22
P04-E	Tendering & Selection	15	0%	$13.21	14-May-22	28-May-22

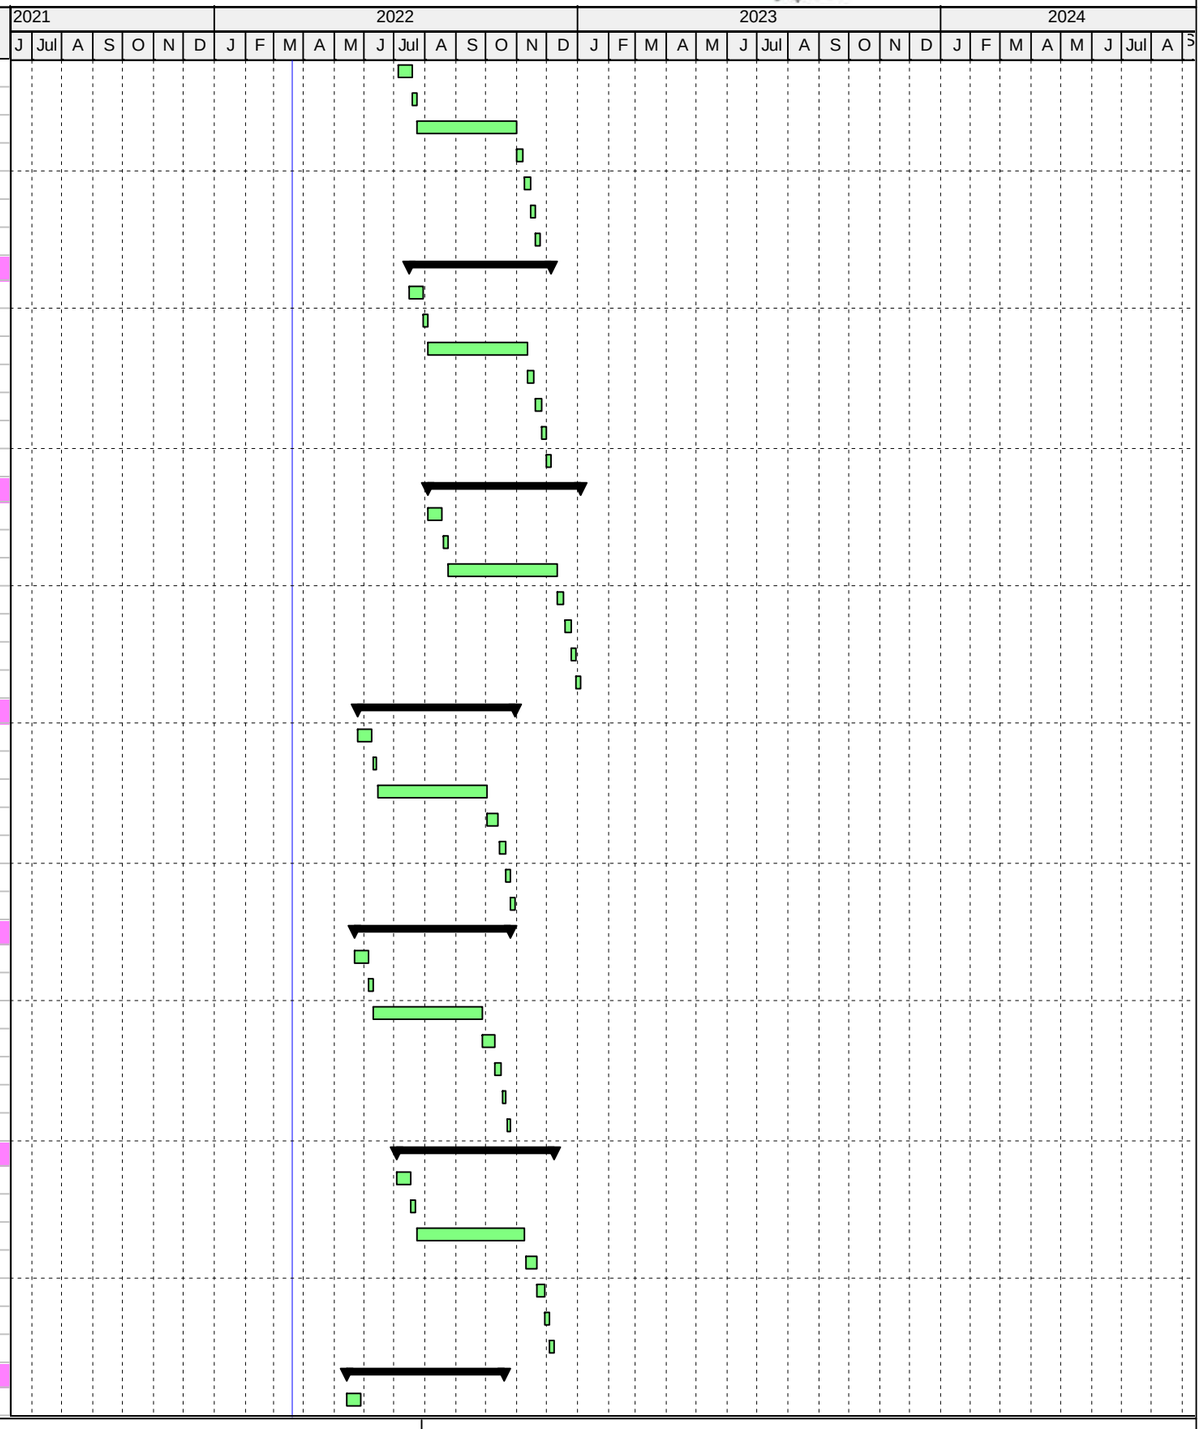


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P04-E	Contract Effectiveness / PO	5	0%	$19.81	29-May-22	02-Jun-22
P04-E	Manufacturing / Fabrication / Supply	110	0%	$165.11	03-Jun-22	20-Sep-22
P04-E	Final Inspection	12	0%	$33.02	21-Sep-22	02-Oct-22
P04-E	Delivery On Site	7	0%	$66.05	03-Oct-22	09-Oct-22
P04-E	Submitting Vendor Data Book	5	0%	$16.51	10-Oct-22	14-Oct-22
P04-E	Delivering Spare Parts	5	0%	$16.51	15-Oct-22	19-Oct-22
Instrument/F&G Cable		129	0%	$408.28	08-Nov-22	16-Mar-23
P04-E	Tendering & Selection	15	0%	$16.33	08-Nov-22	22-Nov-22
P04-E	Contract Effectiveness / PO	5	0%	$24.50	23-Nov-22	27-Nov-22
P04-E	Manufacturing / Fabrication / Supply	90	0%	$204.14	28-Nov-22	25-Feb-23
P04-E	Final Inspection	7	0%	$40.83	26-Feb-23	04-Mar-23
P04-E	Delivery On Site	7	0%	$102.07	05-Mar-23	11-Mar-23
P04-E	Submitting Vendor Data Book	5	0%	$20.41	12-Mar-23	16-Mar-23
Instrument/F&G Junction box and Gland		144	0%	$330.23	03-Nov-22	26-Mar-23
P04-E	Tendering & Selection	15	0%	$13.21	03-Nov-22	17-Nov-22
P04-E	Contract Effectiveness / PO	5	0%	$19.81	18-Nov-22	22-Nov-22
P04-E	Manufacturing / Fabrication / Supply	100	0%	$165.11	23-Nov-22	02-Mar-23
P04-E	Final Inspection	12	0%	$33.02	03-Mar-23	14-Mar-23
P04-E	Delivery On Site	7	0%	$82.56	15-Mar-23	21-Mar-23
P04-E	Submitting Vendor Data Book	5	0%	$16.51	22-Mar-23	26-Mar-23
Instrument Installation Accessories		139	0%	$246.17	30-Sep-22	15-Feb-23
P04-E	Tendering & Selection	15	0%	$9.85	30-Sep-22	14-Oct-22
P04-E	Contract Effectiveness / PO	5	0%	$14.77	15-Oct-22	19-Oct-22
P04-E	Manufacturing / Fabrication / Supply	100	0%	$123.08	20-Oct-22	27-Jan-23
P04-E	Final Inspection	7	0%	$24.62	28-Jan-23	03-Feb-23
P04-E	Delivery On Site	7	0%	$61.54	04-Feb-23	10-Feb-23
P04-E	Submitting Vendor Data Book	5	0%	$12.31	11-Feb-23	15-Feb-23
Differential Pressure/Pressure Gauge		149	0%	$330.23	14-May-22	09-Oct-22
P04-E	Tendering & Selection	15	0%	$13.21	14-May-22	28-May-22
P04-E	Contract Effectiveness / PO	5	0%	$19.81	29-May-22	02-Jun-22
P04-E	Manufacturing / Fabrication / Supply	100	0%	$165.11	03-Jun-22	10-Sep-22
P04-E	Final Inspection	12	0%	$33.02	11-Sep-22	22-Sep-22
P04-E	Delivery On Site	7	0%	$66.05	23-Sep-22	29-Sep-22
P04-E	Submitting Vendor Data Book	5	0%	$16.51	30-Sep-22	04-Oct-22
P04-E	Delivering Spare Parts	5	0%	$16.51	05-Oct-22	09-Oct-22
Temperature Gauge		149	0%	$330.23	07-Jun-22	02-Nov-22
P04-E	Tendering & Selection	15	0%	$13.21	07-Jun-22	21-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$19.81	22-Jun-22	26-Jun-22
P04-E	Manufacturing / Fabrication / Supply	100	0%	$165.11	27-Jun-22	04-Oct-22
P04-E	Final Inspection	12	0%	$33.02	05-Oct-22	16-Oct-22
P04-E	Delivery On Site	7	0%	$66.05	17-Oct-22	23-Oct-22
P04-E	Submitting Vendor Data Book	5	0%	$16.51	24-Oct-22	28-Oct-22
P04-E	Delivering Spare Parts	5	0%	$16.51	29-Oct-22	02-Nov-22
Instrument Tube and Fitting		129	0%	$408.28	07-Jun-22	13-Oct-22
P04-E	Tendering & Selection	10	0%	$16.33	07-Jun-22	16-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$24.50	17-Jun-22	21-Jun-22
P04-E	Manufacturing / Fabrication / Supply	90	0%	$204.14	22-Jun-22	19-Sep-22
P04-E	Final Inspection	12	0%	$40.83	20-Sep-22	01-Oct-22
P04-E	Delivery On Site	7	0%	$102.07	02-Oct-22	08-Oct-22

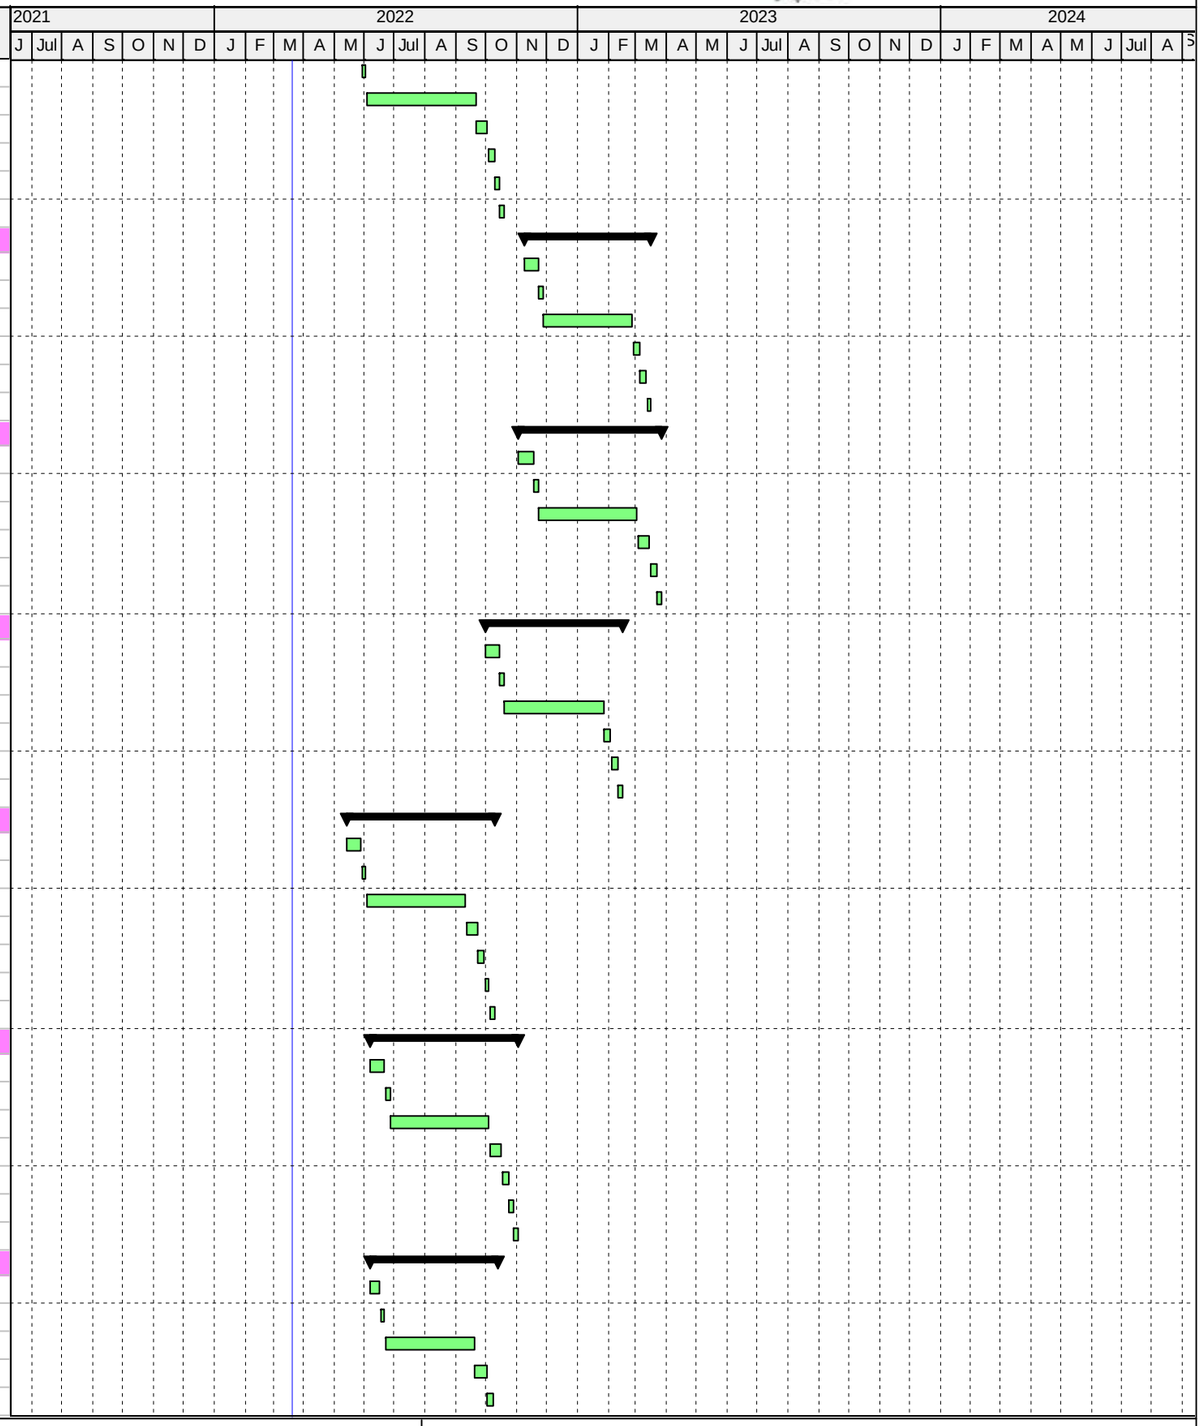


Actual Level of Effort | Remaining Work | Milestone

Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P04-E	Submitting Vendor Data Book	5	0%	$20.41	09-Oct-22	13-Oct-22
Instrument Cable Tray		134	0%	$246.17	30-Sep-22	10-Feb-23
P04-E	Tendering & Selection	15	0%	$9.85	30-Sep-22	14-Oct-22
P04-E	Contract Effectiveness / PO	5	0%	$14.77	15-Oct-22	19-Oct-22
P04-E	Manufacturing / Fabrication / Supply	90	0%	$123.08	20-Oct-22	17-Jan-23
P04-E	Final Inspection	12	0%	$24.62	18-Jan-23	29-Jan-23
P04-E	Delivery On Site	7	0%	$61.54	30-Jan-23	05-Feb-23
P04-E	Submitting Vendor Data Book	5	0%	$12.31	06-Feb-23	10-Feb-23
Safety & Fire Fighting		121	0%	$1,187.74	03-Sep-22	01-Jan-23
Fire Fighting and Safety Equipment - Extension of Binak B/C Ma		79	0%	$884.99	03-Sep-22	20-Nov-22
P04-E	Tendering & Selection	30	0%	$35.40	03-Sep-22	02-Oct-22
P04-E	Contract Effectiveness / PO	5	0%	$53.10	03-Oct-22	07-Oct-22
P04-E	Manufacturing / Fabrication / Supply	20	0%	$442.49	08-Oct-22	27-Oct-22
P04-E	Final Inspection	12	0%	$88.50	28-Oct-22	08-Nov-22
P04-E	Delivery On Site	7	0%	$221.25	09-Nov-22	15-Nov-22
P04-E	Submitting Vendor Data Book	5	0%	$44.25	16-Nov-22	20-Nov-22
Fire Safety Sign - Extension of Binak B/C Manifold		79	0%	$302.76	15-Oct-22	01-Jan-23
P04-E	Tendering & Selection	30	0%	$12.11	15-Oct-22	13-Nov-22
P04-E	Contract Effectiveness / PO	5	0%	$18.17	14-Nov-22	18-Nov-22
P04-E	Manufacturing / Fabrication / Supply	20	0%	$151.38	19-Nov-22	08-Dec-22
P04-E	Final Inspection	12	0%	$30.28	09-Dec-22	20-Dec-22
P04-E	Delivery On Site	7	0%	$75.69	21-Dec-22	27-Dec-22
P04-E	Submitting Vendor Data Book	5	0%	$15.14	28-Dec-22	01-Jan-23
Electrical		284	0%	$20,213.44	05-Jun-22	15-Mar-23
UPS System - Extension of Binak B/C Manifold		144	0%	$8,107.61	12-Sep-22	02-Feb-23
P04-E	Tendering & Selection	15	0%	$324.30	12-Sep-22	26-Sep-22
P04-E	Contract Effectiveness / PO	5	0%	$486.46	27-Sep-22	01-Oct-22
P04-E	Manufacturing / Fabrication / Supply	100	0%	$4,053.80	02-Oct-22	09-Jan-23
P04-E	Final Inspection	7	0%	$810.76	10-Jan-23	16-Jan-23
P04-E	Delivery On Site	7	0%	$1,621.52	17-Jan-23	23-Jan-23
P04-E	Submitting Vendor Data Book	5	0%	$405.38	24-Jan-23	28-Jan-23
P04-E	Delivering Spare Parts	5	0%	$405.38	29-Jan-23	02-Feb-23
LV Switchgear & MCC - Extension of Binak B/C Manifold		154	0%	$3,244.26	05-Jun-22	05-Nov-22
P04-E	Tendering & Selection	15	0%	$129.77	05-Jun-22	19-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$194.66	20-Jun-22	24-Jun-22
P04-E	Manufacturing / Fabrication / Supply	110	0%	$1,622.13	25-Jun-22	12-Oct-22
P04-E	Final Inspection	7	0%	$324.43	13-Oct-22	19-Oct-22
P04-E	Delivery On Site	7	0%	$648.85	20-Oct-22	26-Oct-22
P04-E	Submitting Vendor Data Book	5	0%	$162.21	27-Oct-22	31-Oct-22
P04-E	Delivering Spare Parts	5	0%	$162.21	01-Nov-22	05-Nov-22
DC Charger - Extension of Binak B/C Manifold		154	0%	$5,403.05	05-Jun-22	05-Nov-22
P04-E	Tendering & Selection	15	0%	$216.12	05-Jun-22	19-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$324.18	20-Jun-22	24-Jun-22
P04-E	Manufacturing / Fabrication / Supply	110	0%	$2,701.53	25-Jun-22	12-Oct-22
P04-E	Final Inspection	7	0%	$540.31	13-Oct-22	19-Oct-22
P04-E	Delivery On Site	7	0%	$1,080.61	20-Oct-22	26-Oct-22
P04-E	Submitting Vendor Data Book	5	0%	$270.15	27-Oct-22	31-Oct-22
P04-E	Delivering Spare Parts	5	0%	$270.15	01-Nov-22	05-Nov-22
Earthing & Lightning System - Extension of Binak B/C Manifold		154	0%	$539.70	07-Jun-22	07-Nov-22

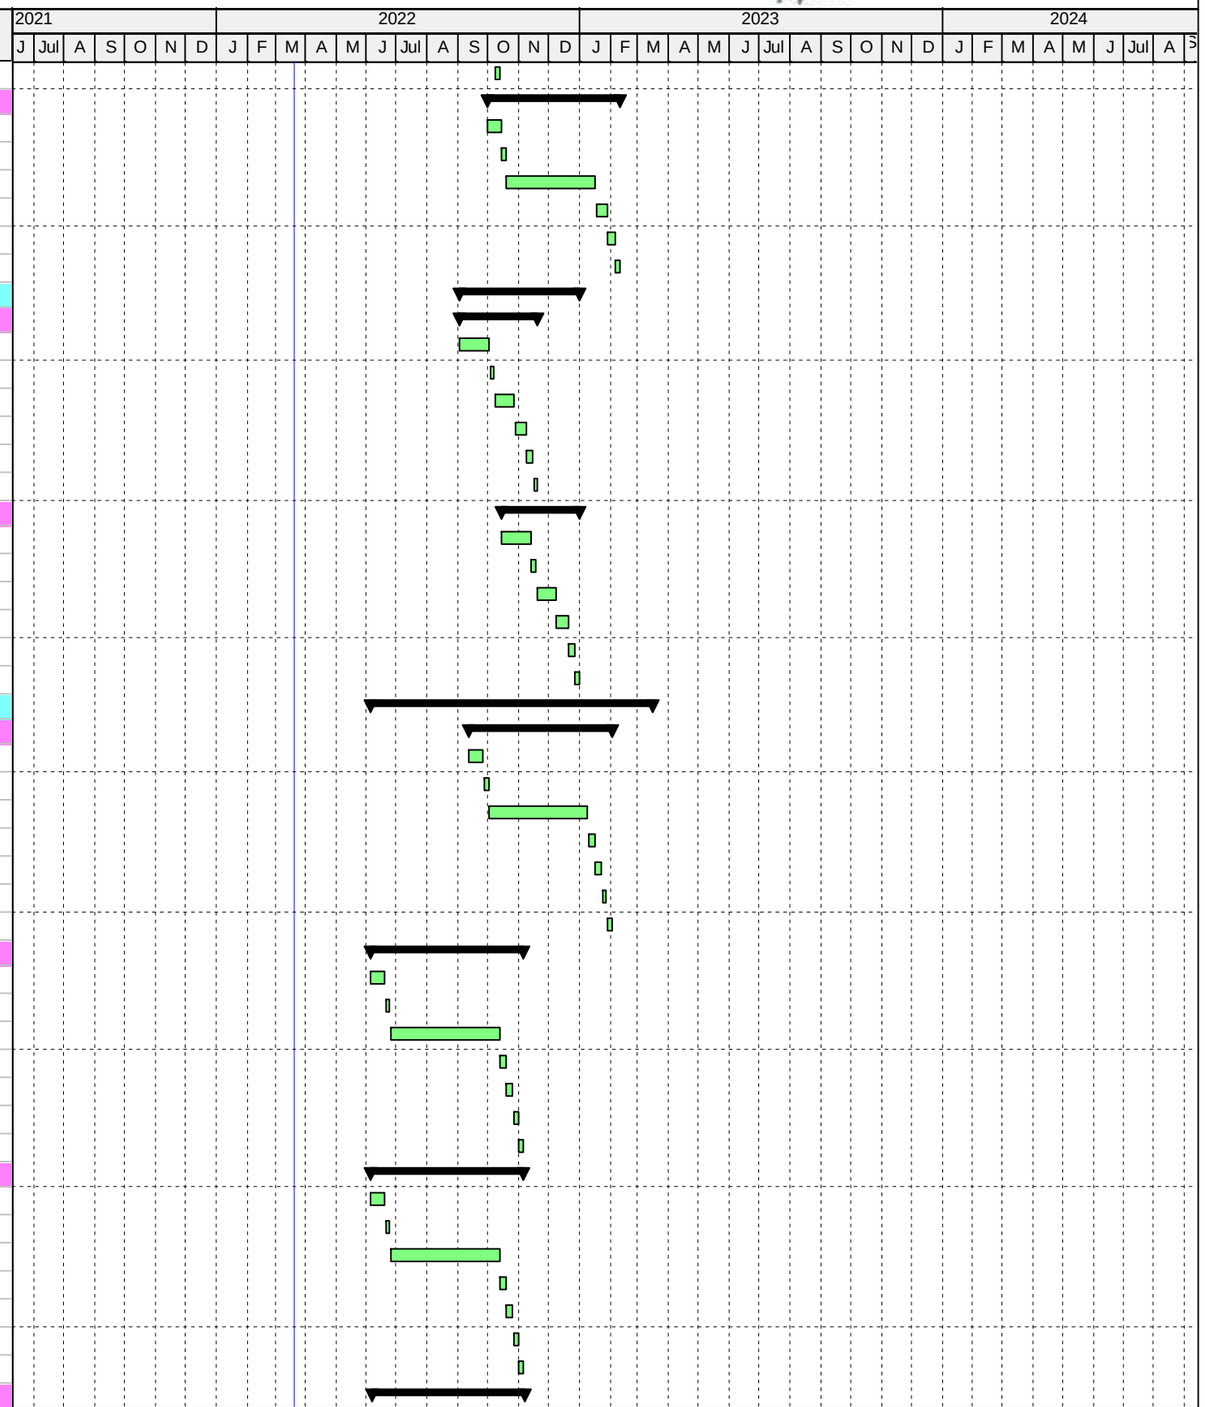


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P04-E	Tendering & Selection	15	0%	$21.59	07-Jun-22	21-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$32.38	22-Jun-22	26-Jun-22
P04-E	Manufacturing / Fabrication / Supply	110	0%	$269.85	27-Jun-22	14-Oct-22
P04-E	Final Inspection	7	0%	$53.97	15-Oct-22	21-Oct-22
P04-E	Delivering Spare Parts	7	0%	$107.94	22-Oct-22	28-Oct-22
P04-E	Submitting Vendor Data Book	5	0%	$26.98	29-Oct-22	02-Nov-22
P04-E	Delivery On Site	5	0%	$26.98	03-Nov-22	07-Nov-22
Power & Control Cables - Extension of Binak B/C Manifold		99	0%	$1,081.42	07-Dec-22	15-Mar-23
P04-E	Tendering & Selection	15	0%	$43.26	07-Dec-22	21-Dec-22
P04-E	Contract Effectiveness / PO	5	0%	$64.89	22-Dec-22	26-Dec-22
P04-E	Manufacturing / Fabrication / Supply	60	0%	$540.71	27-Dec-22	24-Feb-23
P04-E	Final Inspection	7	0%	$108.14	25-Feb-23	03-Mar-23
P04-E	Delivery On Site	7	0%	$270.35	04-Mar-23	10-Mar-23
P04-E	Submitting Vendor Data Book	5	0%	$54.07	11-Mar-23	15-Mar-23
Tray/Ladder and Accessories		97	0%	$735.77	01-Aug-22	05-Nov-22
P04-E	Tendering & Selection	15	0%	$29.43	01-Aug-22	15-Aug-22
P04-E	Contract Effectiveness / PO	5	0%	$44.15	16-Aug-22	20-Aug-22
P04-E	Manufacturing / Fabrication / Supply	60	0%	$367.88	21-Aug-22	19-Oct-22
P04-E	Final Inspection	7	0%	$73.58	20-Oct-22	26-Oct-22
P04-E	Delivery On Site	5	0%	$183.94	27-Oct-22	31-Oct-22
P04-E	Submitting Vendor Data Book	5	0%	$36.79	01-Nov-22	05-Nov-22
Electrical Bulk Items		154	0%	$1,101.63	07-Jun-22	07-Nov-22
P04-E	Tendering & Selection	15	0%	$44.07	07-Jun-22	21-Jun-22
P04-E	Contract Effectiveness / PO	5	0%	$66.10	22-Jun-22	26-Jun-22
P04-E	Manufacturing / Fabrication / Supply	110	0%	$550.82	27-Jun-22	14-Oct-22
P04-E	Final Inspection	12	0%	$110.16	15-Oct-22	26-Oct-22
P04-E	Delivery On Site	7	0%	$275.41	27-Oct-22	02-Nov-22
P04-E	Submitting Vendor Data Book	5	0%	$55.08	03-Nov-22	07-Nov-22
Construction		437	17.57%	$230,492.00	12-Sep-21	03-Nov-23
Wellpad and Access Road		187	24.4%	$165,954.24	12-Sep-21	07-Dec-22
Access Road		177	24%	$33,190.85	12-Sep-21	07-Dec-22
Wellpad Access Road		177	30%	$26,552.68	12-Sep-21	07-Dec-22
P04-E	Access Road Preparation	20	80%	$7,965.80	12-Sep-21	03-Sep-22
P04-E	Filling and Compaction	20	40%	$3,982.90	12-Sep-21	23-Sep-22
P04-E	Sub-Base Layer	10	0%	$6,638.17	23-Sep-22	03-Oct-22
Construction of Culvert and Bridge		105	0%	$7,965.80	24-Aug-22	07-Dec-22
bridge		65	0%	$3,186.32	03-Oct-22	07-Dec-22
P04	Excavation	19	0%	$318.63	03-Oct-22	21-Oct-22
P04	lean concrete	2	0%	$254.91	21-Oct-22	23-Oct-22
P04	wall	10	0%	$573.54	23-Oct-22	02-Nov-22
P04	reinforcement	10	0%	$637.26	02-Nov-22	12-Nov-22
P04	form working	10	0%	$318.63	12-Nov-22	22-Nov-22
P04	concrete pouring	5	0%	$955.90	22-Nov-22	27-Nov-22
P04	protect stone	3	0%	$63.73	27-Nov-22	30-Nov-22
P04	Backfill	6	0%	$63.73	30-Nov-22	07-Dec-22
culverts		13	0%	$4,779.48	24-Aug-22	05-Sep-22
P04	pipeway culvert	5	0%	$1,911.79	24-Aug-22	29-Aug-22
P04	pipeway	4	0%	$1,433.84	29-Aug-22	01-Sep-22
P04	pipeline culvert	4	0%	$1,433.84	01-Sep-22	05-Sep-22

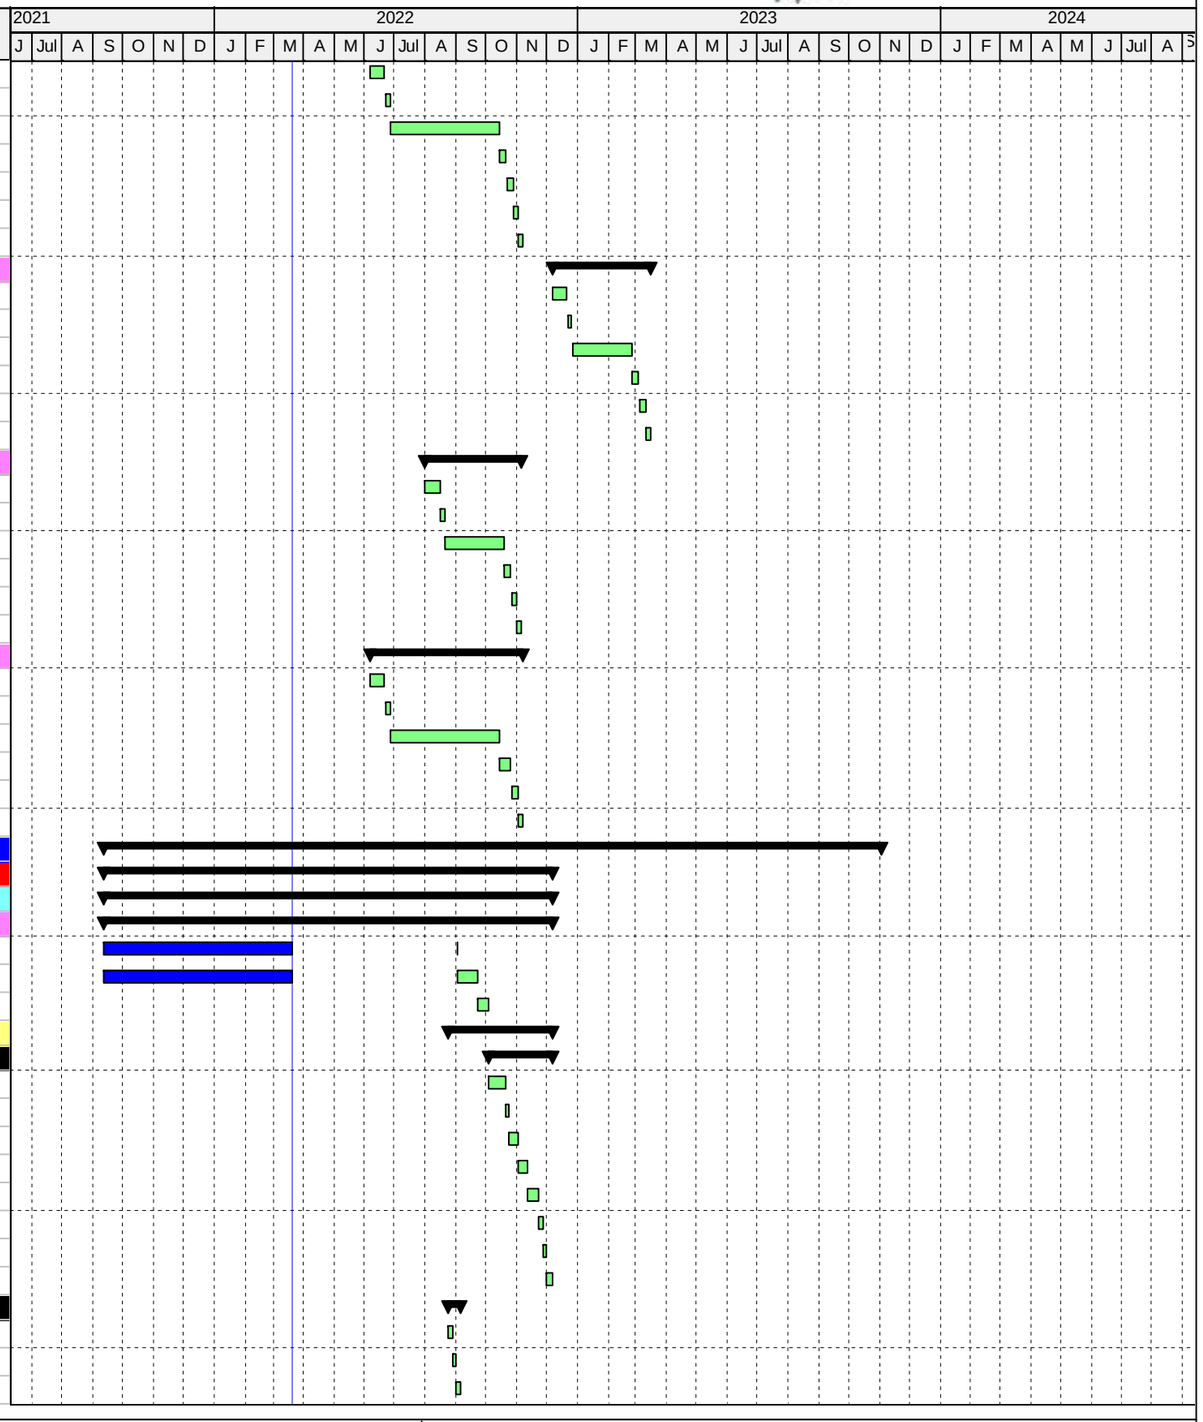


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Burn Pit Access Road		31	0%	$6,638.17	03-Sep-22	04-Oct-22
P04-E	ROW Preparation	15	0%	$3,650.99	03-Sep-22	18-Sep-22
P04-E	Filling and Compaction	10	0%	$1,327.63	18-Sep-22	28-Sep-22
P04-E	Sub-Base Layer	6	0%	$1,659.54	28-Sep-22	04-Oct-22
Wellpad		177	24.5%	$132,763.39	23-Nov-21	02-Dec-22
Water Supply		30	0%	$9,293.44	03-Sep-22	03-Oct-22
P04-E	Water Supply	30	0%	$9,293.44	03-Sep-22	03-Oct-22
Site Preparation		15	70%	$46,467.19	23-Nov-21	25-Oct-22
P04-E	Site Preparation W035	15	70%	$46,467.19	23-Nov-21	25-Oct-22
Civil Work		39	0%	$39,829.02	12-Oct-22	20-Nov-22
P04-E	Excavation and Soil Removal (Cellar)	20	0%	$25,888.86	12-Oct-22	01-Nov-22
P04-E	Installation of Conductor Pipe	15	0%	$1,991.45	12-Oct-22	27-Oct-22
P04-E	Form Work (Above Cellar)	9	0%	$1,991.45	01-Nov-22	10-Nov-22
P04-E	Armed Concrete	10	0%	$9,957.25	10-Nov-22	20-Nov-22
Surface Preparation		19	0%	$1,327.63	25-Oct-22	12-Nov-22
P04-E	Gravel Paving	19	0%	$1,327.63	25-Oct-22	12-Nov-22
Mud Channel		38	0%	$7,965.80	25-Oct-22	02-Dec-22
P04-E	Excavation	15	0%	$796.58	04-Nov-22	19-Nov-22
P04-E	Soil Removal, Filling and Compaction of Mud Pit Area	10	0%	$1,194.87	25-Oct-22	04-Nov-22
P04-E	Construction of Mud Pit's Walls	7	0%	$2,788.03	19-Nov-22	26-Nov-22
P04-E	Installation sealling Layer	5	0%	$2,389.74	25-Oct-22	30-Oct-22
P04-E	Backfill	6	0%	$796.58	26-Nov-22	02-Dec-22
Mud Pit		18	0%	$13,276.34	27-Oct-22	14-Nov-22
P04-E	Soil Removal, Filling and Compaction of Mud Pit Area	10	0%	$4,646.72	27-Oct-22	06-Nov-22
P04-E	Construction of Mud Pit's Walls	15	0%	$2,655.27	30-Oct-22	14-Nov-22
P04-E	Installation sealling Layer	10	0%	$5,974.35	04-Nov-22	14-Nov-22
SepticTank		25	0%	$5,310.54	01-Nov-22	26-Nov-22
P04-E	Excavation & Soil Transfer	7	0%	$1,593.16	01-Nov-22	08-Nov-22
P04-E	Levelling	3	0%	$26.55	08-Nov-22	11-Nov-22
P04-E	Tank Supply	10	0%	$3,027.01	11-Nov-22	21-Nov-22
P04-E	Tank Execution	3	0%	$504.50	21-Nov-22	24-Nov-22
P04-E	Backfilling & Compaction	3	0%	$159.32	24-Nov-22	26-Nov-22
Burn Pit		30	0%	$6,638.17	18-Sep-22	18-Oct-22
P04-E	Soil Removal, Triming ,Filling and Compaction of Burn Pit Are	20	0%	$5,310.54	18-Sep-22	08-Oct-22
P04-E	Construction & Installation of Support	15	0%	$331.91	28-Sep-22	13-Oct-22
P04-E	Welding, Installation and Testing	15	0%	$995.73	03-Oct-22	18-Oct-22
Gasoil Pad		11	0%	$2,655.27	25-Oct-22	05-Nov-22
P04-E	Excavation	5	0%	$531.05	25-Oct-22	30-Oct-22
P04-E	lean concrete	2	0%	$796.58	30-Oct-22	01-Nov-22
P04-E	Form work	4	0%	$265.53	29-Oct-22	02-Nov-22
P04-E	Armed Concrete	3	0%	$1,062.11	02-Nov-22	05-Nov-22
Wellhead Facility and Flowline		242	0%	$59,005.95	07-Dec-22	05-Aug-23
Civil		135	0%	$21,242.14	07-Dec-22	21-Apr-23
P04-EF	Right of Way	45	0%	$15,931.61	07-Dec-22	21-Jan-23
P04-EF	Steel Works(Wellhead Facilities)	30	0%	$3,611.16	21-Jan-23	20-Feb-23
P04-EF	Construction & Installation of Shelter for Wellhead Control Pa	15	0%	$1,062.11	20-Feb-23	07-Mar-23
P04-EF	Well Pad Fencing	45	0%	$637.26	07-Mar-23	21-Apr-23
Flowline		101	0%	$25,372.56	21-Jan-23	02-May-23
P04-EF	Construction of Pipe Support	25	0%	$3,805.88	21-Jan-23	15-Feb-23

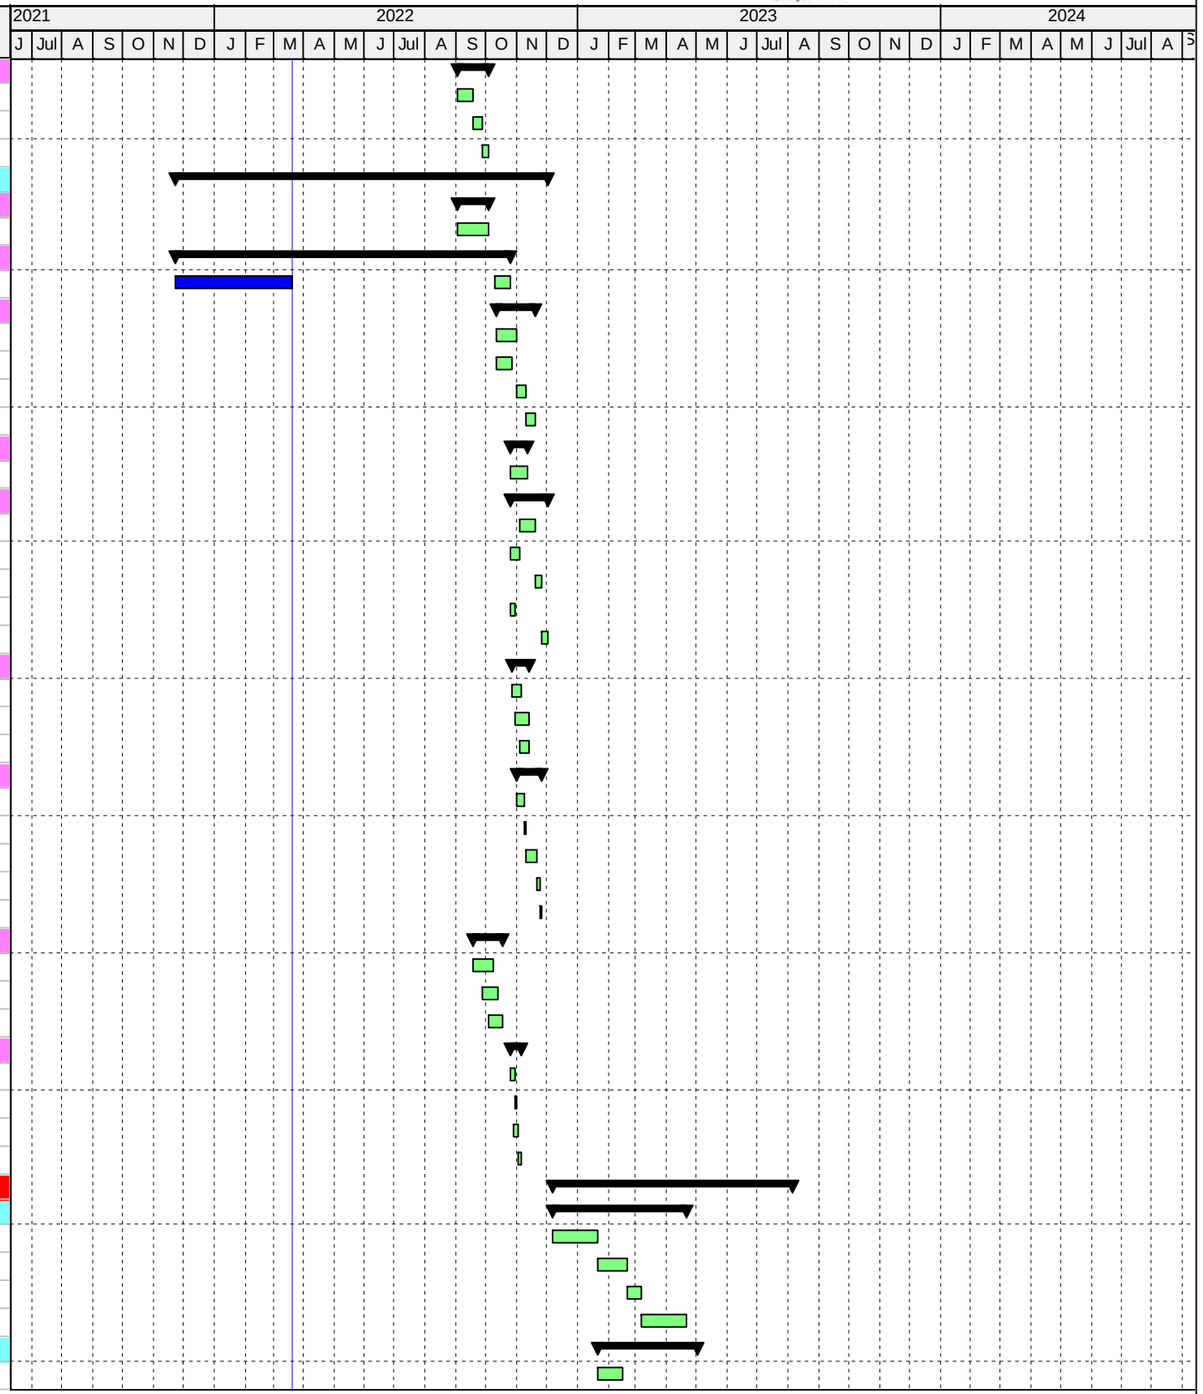


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P04-EF	Installation of Pipe Supports	25	0%	$3,805.88	27-Jan-23	21-Feb-23
6" Flowline Installation		80	0%	$16,492.16	06-Feb-23	27-Apr-23
P04-E	COLD CUT	25	0%	$824.61	06-Feb-23	03-Mar-23
P04-E	Material Handeling	30	0%	$1,979.06	21-Feb-23	23-Mar-23
P04-E	Fit-Up & Welding	40	0%	$10,884.83	26-Feb-23	07-Apr-23
P04-E	Bending	20	0%	$1,731.68	28-Mar-23	17-Apr-23
P04-E	NDT	20	0%	$1,071.99	07-Apr-23	27-Apr-23
Hydrostatic Test		5	0%	$1,268.63	27-Apr-23	02-May-23
P04-E	6" Pigging and Hydrostatic Test	5	0%	$1,268.63	27-Apr-23	02-May-23
Piping		20	0%	$6,490.65	01-Jul-23	21-Jul-23
P04-EF	Sweep Bend Installation	10	0%	$324.53	01-Jul-23	11-Jul-23
P04-EF	Construction of Spools (Fit up, Welding, NDT…)	15	0%	$2,271.73	01-Jul-23	16-Jul-23
P04-EF	Valves, Fitting and Spools Installation and Hydrotest	5	0%	$3,569.86	13-Jul-23	18-Jul-23
P04-EF	Painting	5	0%	$324.53	16-Jul-23	21-Jul-23
Instrument Works		30	0%	$4,720.48	26-Jun-23	26-Jul-23
P04-EF	Wellhead Control Panel Installation	15	0%	$2,360.24	26-Jun-23	11-Jul-23
P04-EF	Devices Installation and Piping Connecton	15	0%	$2,360.24	11-Jul-23	26-Jul-23
Pre-commissioning		11	0%	$1,180.12	26-Jul-23	05-Aug-23
P04-EF	Pre-commissioning	10	0%	$1,062.11	26-Jul-23	05-Aug-23
P04-EF	Ready for Comm.Certificate(RFCC)	7	0%	$118.01	29-Jul-23	05-Aug-23
Helipad		51	0%	$2,074.43	03-Sep-22	23-Oct-22
P04-EP	Excavation & Soil Transfer	19	0%	$207.44	03-Sep-22	21-Sep-22
P04-EP	Levelling	13	0%	$248.93	15-Sep-22	28-Sep-22
P04-EP	Lean Concrete	2	0%	$311.16	28-Sep-22	30-Sep-22
P04-EP	Reinforced Work	5	0%	$311.16	30-Sep-22	05-Oct-22
P04-EP	Form Work	6	0%	$311.16	05-Oct-22	11-Oct-22
P04-EP	Main Concrete Pouring	5	0%	$414.89	11-Oct-22	16-Oct-22
P04-EP	Backfilling & Compaction	5	0%	$228.19	16-Oct-22	21-Oct-22
P04-EP	Paint Marking	3	0%	$41.49	21-Oct-22	23-Oct-22
Job Site HSE Supervision (Surface)		310	0%	$460.98	03-Sep-22	10-Jul-23
P04-EP	Job Site HSE Supervision (Surface)	310	0%	$460.98	03-Sep-22	10-Jul-23
Commissioning, Startup & Handover		90	0%	$2,996.40	05-Aug-23	03-Nov-23
Commissioning		34	0%	$898.92	05-Aug-23	08-Sep-23
P04-EF	Materials & Utilities Ready for Commissioning	3	0%	$44.95	05-Aug-23	08-Aug-23
P04-EF	Receiving Facilities Ready for Commissioning	3	0%	$44.95	08-Aug-23	11-Aug-23
P04-EF	Permits Obtained for Commissioning	10	0%	$44.95	11-Aug-23	21-Aug-23
P04-EF	Integrated Commissioning	3	0%	$719.14	21-Aug-23	24-Aug-23
P04-EF	Ready for Startup Certificate (RFSU)	15	0%	$44.95	24-Aug-23	08-Sep-23
Handover		38	0%	$898.92	26-Sep-23	03-Nov-23
P04-EF	Compiling & Submitting Final Documentation	20	0%	$269.68	26-Sep-23	16-Oct-23
P04-EF	Training of Operator's Personnel	3	0%	$359.57	16-Oct-23	19-Oct-23
P04-EF	Provisional Acceptance Certificate (PAC)	15	0%	$269.68	19-Oct-23	03-Nov-23
Startup & Performance Test		18	0%	$1,198.56	08-Sep-23	26-Sep-23
P04-EF	Startup & Performance Test Run	3	0%	$958.85	08-Sep-23	11-Sep-23
P04-EF	Start of Production (SOP)	15	0%	$239.71	11-Sep-23	26-Sep-23
Package 05-New Well # W008N		693	2.03%	$249,326.00	24-Jul-21 A	10-Feb-24
ENGINEERING		619	23.31%	$8,125.00	24-Jul-21 A	28-Nov-23
Basic Design Endorsement		30	100%	$406.25	31-Jul-21 A	20-Mar-22
P05-EP	Endorsement Report For Basic Design & Scope of Work	30	100%	$406.25	31-Jul-21 A	20-Mar-22

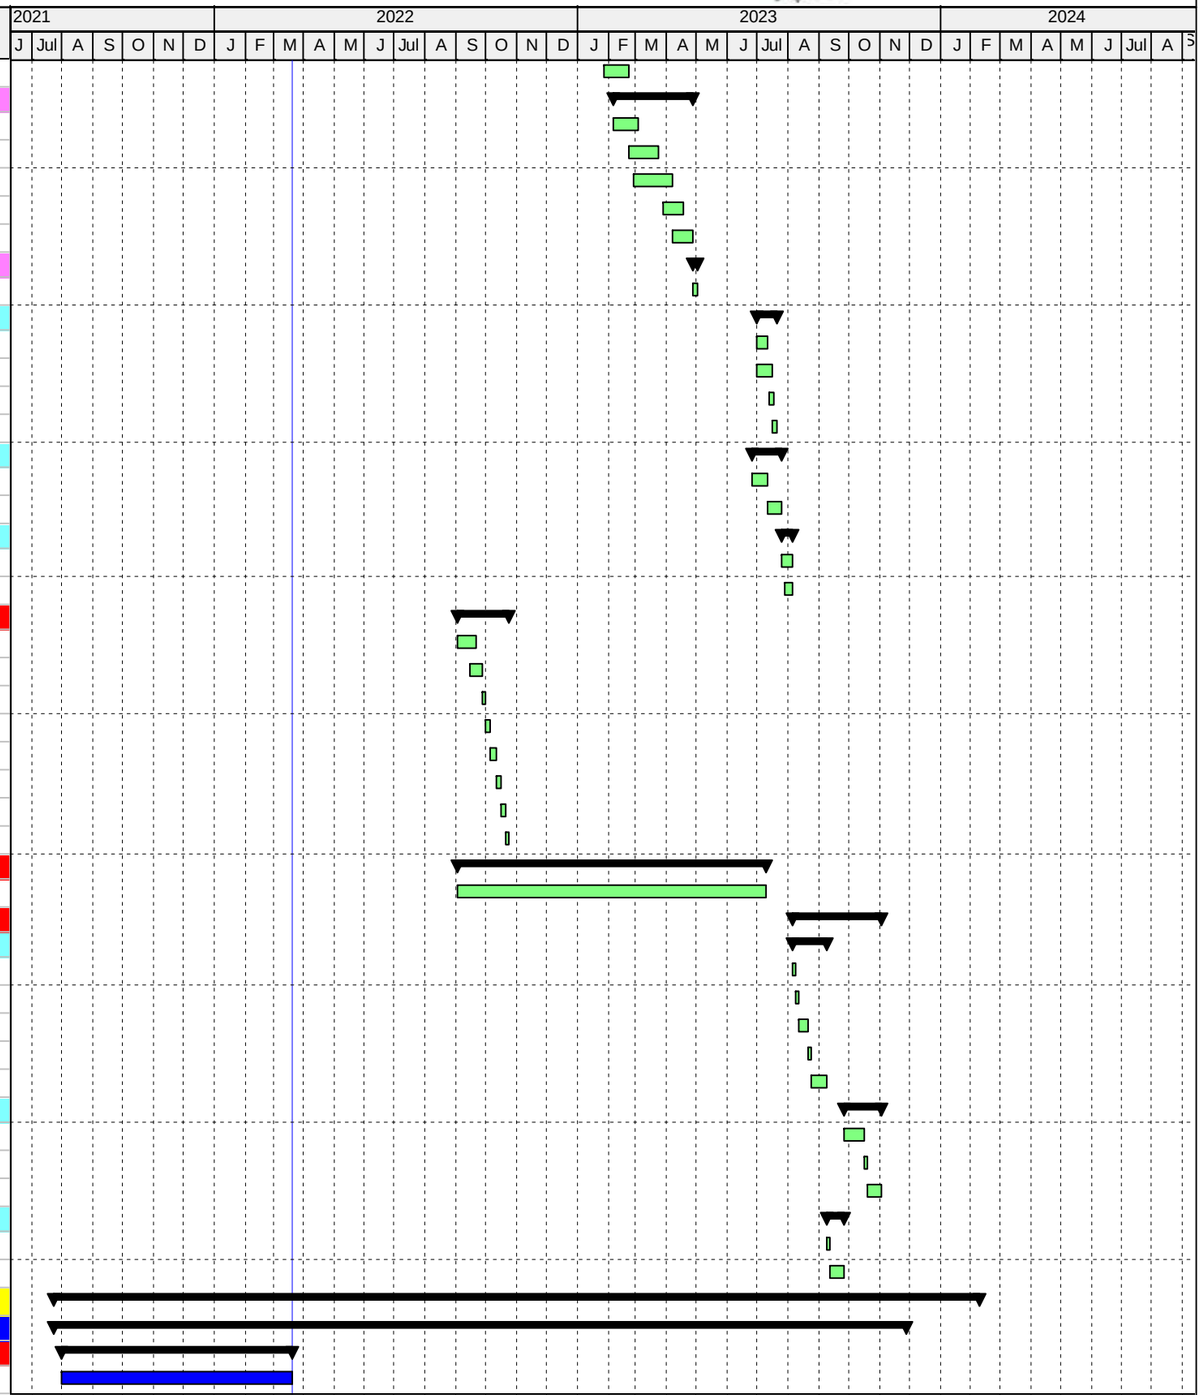


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Value Engineering		75	22.5%	$243.75	01-Feb-22	02-Jul-22
P05-EP	Value Engineering Study Report	44	60%	$91.41	01-Feb-22	02-May-22
P05-EP	HAZID Report For WHF & Flowlines	44	0%	$152.34	20-May-22	02-Jul-22
Detail Design		449	30.75%	$4,468.75	24-Jul-21 A	12-Mar-23
Process		142	59.82%	$446.88	27-Jul-21 A	17-Jun-22
Basis/Criteria		54	86.99%	$89.38	27-Jul-21 A	12-May-22
P05-E	Process Design Criteria	39	100%	$31.24	27-Jul-21 A	20-Mar-22
P05-E	Process Basis Of Design	54	80%	$58.14	27-Jul-21 A	12-May-22
Drawing/Diagram		98	67.67%	$111.72	30-Oct-21	12-May-22
P05-E	Symbol & Legend For PFD and P&ID	44	80%	$6.12	30-Oct-21	02-May-22
P05-E	Process Flow Diagram - W008N	44	60%	$68.86	02-Nov-21	02-May-22
P05-E	P&ID - W008N	54	80%	$36.73	01-Nov-21	12-May-22
Philosophy		74	11.01%	$67.03	21-Nov-21	01-Jun-22
P05-E	Drainage Philosophy	44	0%	$2.65	19-Apr-22	01-Jun-22
P05-E	Control Philosophy	44	0%	$18.37	19-Apr-22	01-Jun-22
P05-E	Flare,Blow Down And Relief Philosophy	44	0%	$18.37	19-Apr-22	01-Jun-22
P05-E	Isolation Philosophy	44	60%	$12.31	21-Nov-21	02-May-22
P05-E	ESD Philosophy	44	0%	$15.34	19-Apr-22	01-Jun-22
Data Sheet		36	0%	$44.69	13-May-22	17-Jun-22
P05-E	Process Data Sheets For Instrument Devices - W008N	36	0%	$44.69	13-May-22	17-Jun-22
Report		44	80%	$89.38	30-Oct-21	12-May-22
P05-E	Flowline Hydraulic Calculation Report	44	80%	$89.38	30-Oct-21	12-May-22
List		112	78.46%	$44.69	08-Nov-21	12-May-22
P05-E	Line List - W008N	44	80%	$41.25	08-Nov-21	12-May-22
P05-E	Consumption List	44	60%	$3.44	23-Feb-22	02-May-22
Piping		328	10.27%	$893.75	24-Jul-21 A	12-Mar-23
Basis/Criteria		39	100%	$1.79	24-Jul-21 A	20-Mar-22
P05-E	Piping Design Criteria	39	100%	$1.79	24-Jul-21 A	20-Mar-22
Specification		49	73.45%	$35.84	24-Jul-21 A	07-May-22
P05-E	Specification For Color Coding and Marking	39	60%	$2.09	09-Aug-21	01-May-22
P05-E	Specification For Transportation, Handling, Storage of pipes	30	80%	$2.28	12-Dec-21	18-Apr-22
P05-E	Specification For Metallic Pipes	39	80%	$2.09	24-Jul-21 A	01-May-22
P05-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$2.09	24-Jul-21 A	24-Mar-22
P05-E	Specification For Painting	39	100%	$2.09	24-Jul-21 A	27-Mar-22
P05-E	Specification For Lining (Internal Protection of Equipment by F	39	60%	$2.51	09-Aug-21	04-May-22
P05-E	Specification For Material Requirements in Sour service	39	60%	$2.09	09-Aug-21	04-May-22
P05-E	Specification For Manual Valves	39	60%	$2.09	09-Aug-21	04-May-22
P05-E	Specification For Plant Piping Systems Pressure Testing	39	60%	$2.09	09-Aug-21	04-May-22
P05-E	Specification For Welding of Plant Piping System	39	60%	$2.09	09-Aug-21	04-May-22
P05-E	Specification For Flexibility Analysis	39	60%	$2.28	09-Aug-21	04-May-22
P05-E	Specification For Coating Of Underground Piping	39	100%	$3.59	24-Jul-21 A	30-Mar-22
P05-E	Specification For Pipe Support	39	60%	$2.79	09-Aug-21	07-May-22
P05-E	Specification For Piping Construction, Fabrication & Erection	45	60%	$3.58	09-Aug-21	03-May-22
P05-E	Specification For Piping Cleaning and Flushing	39	100%	$2.09	24-Aug-21	30-Mar-22
Procedure/Plan		108	50%	$1.79	24-Jul-21 A	18-Aug-22
P05-E	3D-Model (PDMS) Review Procedure	39	100%	$0.89	24-Jul-21 A	03-Apr-22
P05-E	Piping Hydrostatic Test Diagram - Sub Surface	44	0%	$0.89	06-Jul-22	18-Aug-22
Drawing/Diagram		328	18.01%	$206.19	08-Nov-21	12-Mar-23
P05-E	Standard Pipe Support Drawings	14	100%	$6.21	19-Feb-22	20-Mar-22

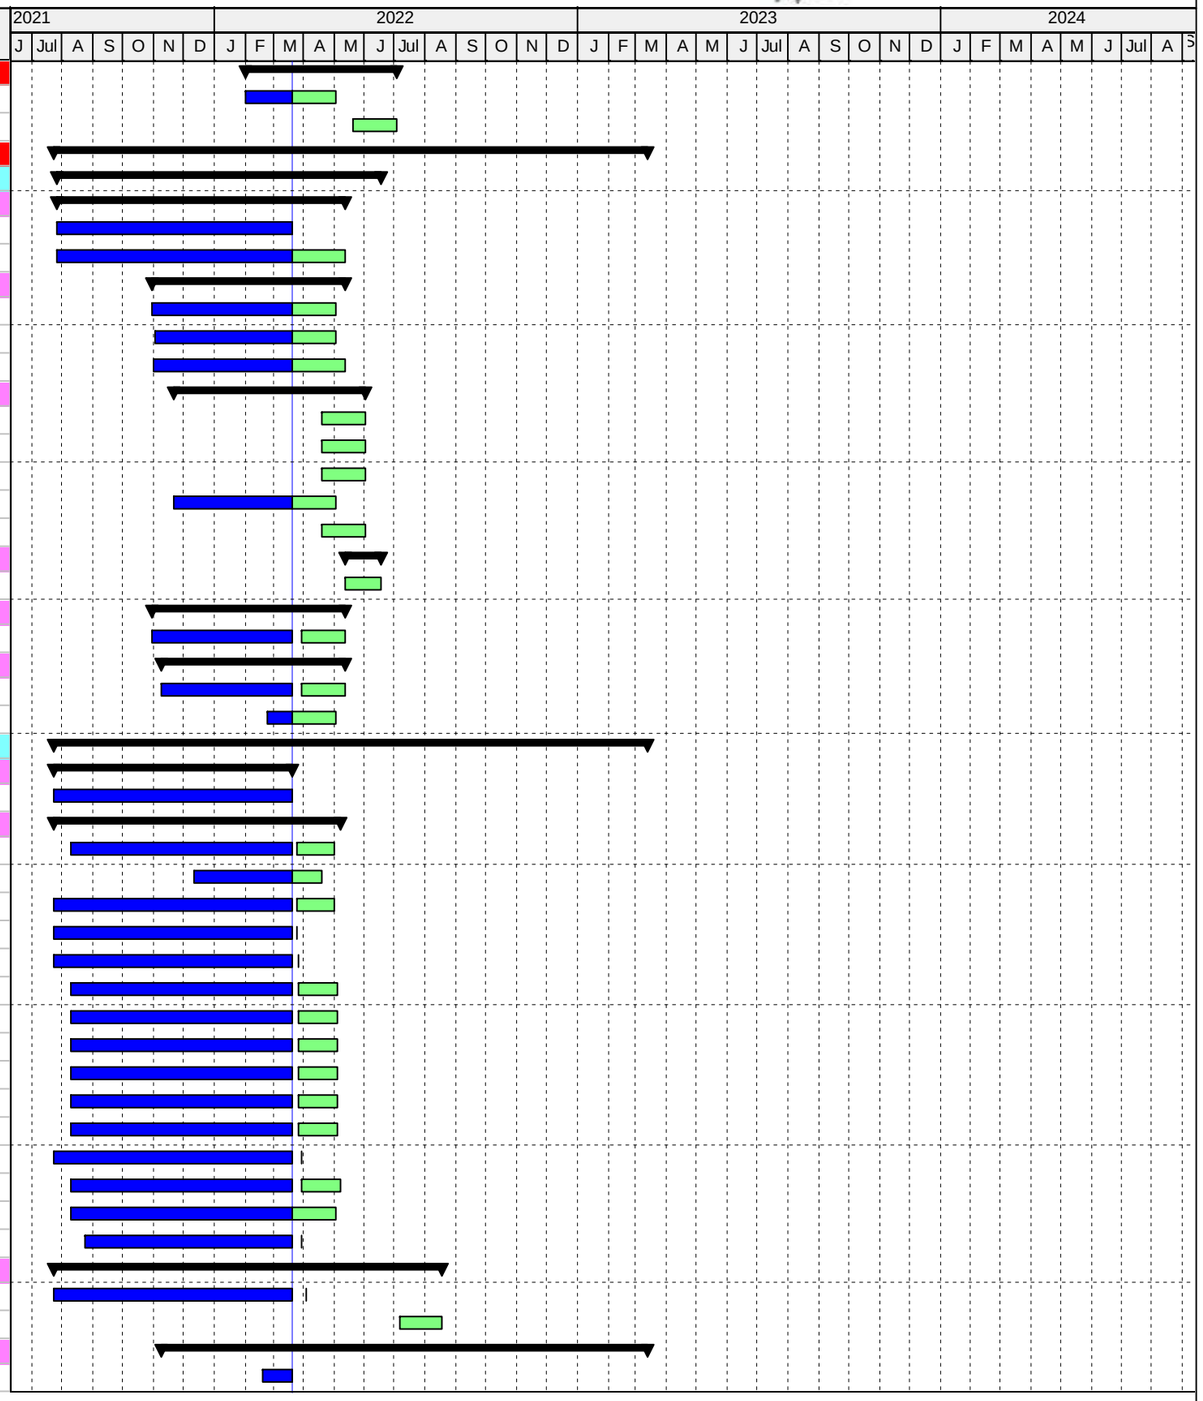


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05-E	Piping Assembly Drawing	54	0%	$20.95	13-May-22	05-Jul-22
P05-E	Piping Hydrostatic Test Diagram - Sub Surface	44	0%	$3.36	06-Jul-22	18-Aug-22
P05-E	Plot Plan Drawing - W008N	64	0%	$62.06	13-May-22	15-Jul-22
P05-E	Piping Plan - W008N	44	0%	$37.24	15-Dec-22	27-Jan-23
P05-E	Isometric Drawings - W008N	44	0%	$24.83	28-Jan-23	12-Mar-23
P05-E	Material Flow Diagram - W008N	39	60%	$51.55	08-Nov-21	12-May-22
Data Sheets		39	60%	$2.68	27-Dec-21	12-May-22
P05-E	Data Sheets For Stone Trap	39	60%	$2.68	27-Dec-21	12-May-22
Report		132	5.36%	$448.22	28-Nov-21	31-Oct-22
P05-E	PDMS Model Review Report (60%) - W008N	44	0%	$244.50	22-Jun-22	04-Aug-22
P05-E	PDMS Model Review Report (90%) - W008N	44	0%	$163.64	18-Sep-22	31-Oct-22
P05-E	Piping Corrosion Study & Material Selection Report	44	60%	$40.07	28-Nov-21	16-May-22
List		216	0%	$35.84	13-May-22	14-Dec-22
P05-E	Piping Support List - W008N	44	0%	$17.92	01-Nov-22	14-Dec-22
P05-E	Critical Line List - W008N	39	0%	$17.92	13-May-22	20-Jun-22
MTO		7	0%	$161.41	01-Nov-22	07-Nov-22
P05-E	MTO For Pipes - W008N	7	0%	$26.89	01-Nov-22	07-Nov-22
P05-E	MTO For Fittings - W008N	7	0%	$26.89	01-Nov-22	07-Nov-22
P05-E	MTO For Flanges - W008N	7	0%	$26.91	01-Nov-22	07-Nov-22
P05-E	MTO For Manual Valves - W008N	7	0%	$26.91	01-Nov-22	07-Nov-22
P05-E	MTO For Gaskets - W008N	7	0%	$26.91	01-Nov-22	07-Nov-22
P05-E	MTO For Bolt & Nuts - W008N	7	0%	$26.91	01-Nov-22	07-Nov-22
Pipeline & Flow line		182	39.45%	$134.06	24-Jul-21 A	22-May-22
Basis/Criteria		39	100%	$0.94	28-Aug-21	20-Mar-22
P05-E	Pipeline Design Criteria	39	100%	$0.94	28-Aug-21	20-Mar-22
Specification		49	85.88%	$13.07	24-Jul-21 A	07-May-22
P05-E	Specification For Line Pipes	39	100%	$1.02	24-Jul-21 A	24-Mar-22
P05-E	Specification For Pipeline Cold Bending	39	80%	$0.91	28-Aug-21	01-May-22
P05-E	Specification For Barred Tee	39	80%	$0.91	28-Aug-21	01-May-22
P05-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$0.91	24-Jul-21 A	24-Mar-22
P05-E	Specification For Pipeline Valves	39	80%	$0.91	28-Aug-21	01-May-22
P05-E	Specification For Pipeline Coating	39	100%	$0.91	24-Jul-21 A	24-Mar-22
P05-E	Specification For Pipeline Flushing, Cleaning And Hydrostatic	39	100%	$1.02	24-Jul-21 A	27-Mar-22
P05-E	Specification For Welding of Transportation Pipeline	39	80%	$0.91	12-Dec-21	04-May-22
P05-E	Specification For Pipeline Stress Analysis	39	80%	$0.91	24-Jul-21 A	04-May-22
P05-E	Specification For Pipeline Insulation Joint	39	100%	$0.91	24-Jul-21 A	27-Mar-22
P05-E	Specification For Pipeline Construction	39	80%	$0.91	25-Jan-22	04-May-22
P05-E	Specification For Anchor Flanges	39	80%	$1.02	28-Aug-21	07-May-22
P05-E	Specification For Pigs	39	80%	$0.91	28-Aug-21	07-May-22
P05-E	Specification For Pipeline Cleaning and Flushing	44	60%	$0.91	24-Jul-21 A	02-May-22
Drawings		84	21.55%	$77.01	27-Jul-21 A	12-May-22
P05-E	Pipeline Standard Support Drawings	14	100%	$2.57	27-Jul-21 A	20-Mar-22
P05-E	Standard Drawing For Above Ground Pipeline Construction F	44	80%	$2.24	27-Nov-21	12-May-22
P05-E	Standard Drawing For Under Ground Pipeline Construction F	44	100%	$2.24	04-Dec-21	30-Mar-22
P05-E	Pipeline Standard Drawing For Anchor Support	44	60%	$2.24	22-Dec-21	12-May-22
P05-E	Standard Drawing For A/G Pipeline Road Crossing	44	60%	$2.24	05-Dec-21	12-May-22
P05-E	Standard Drawing For Existing Pipeline Crossing	44	60%	$2.24	18-Dec-21	12-May-22
P05-E	Pipeline Standard Drawing For Irish Crossing	44	60%	$2.12	04-Dec-21	12-May-22
P05-E	Pipeline Standard Drawing For Water - Way Crossing	44	60%	$2.12	22-Nov-21	12-May-22

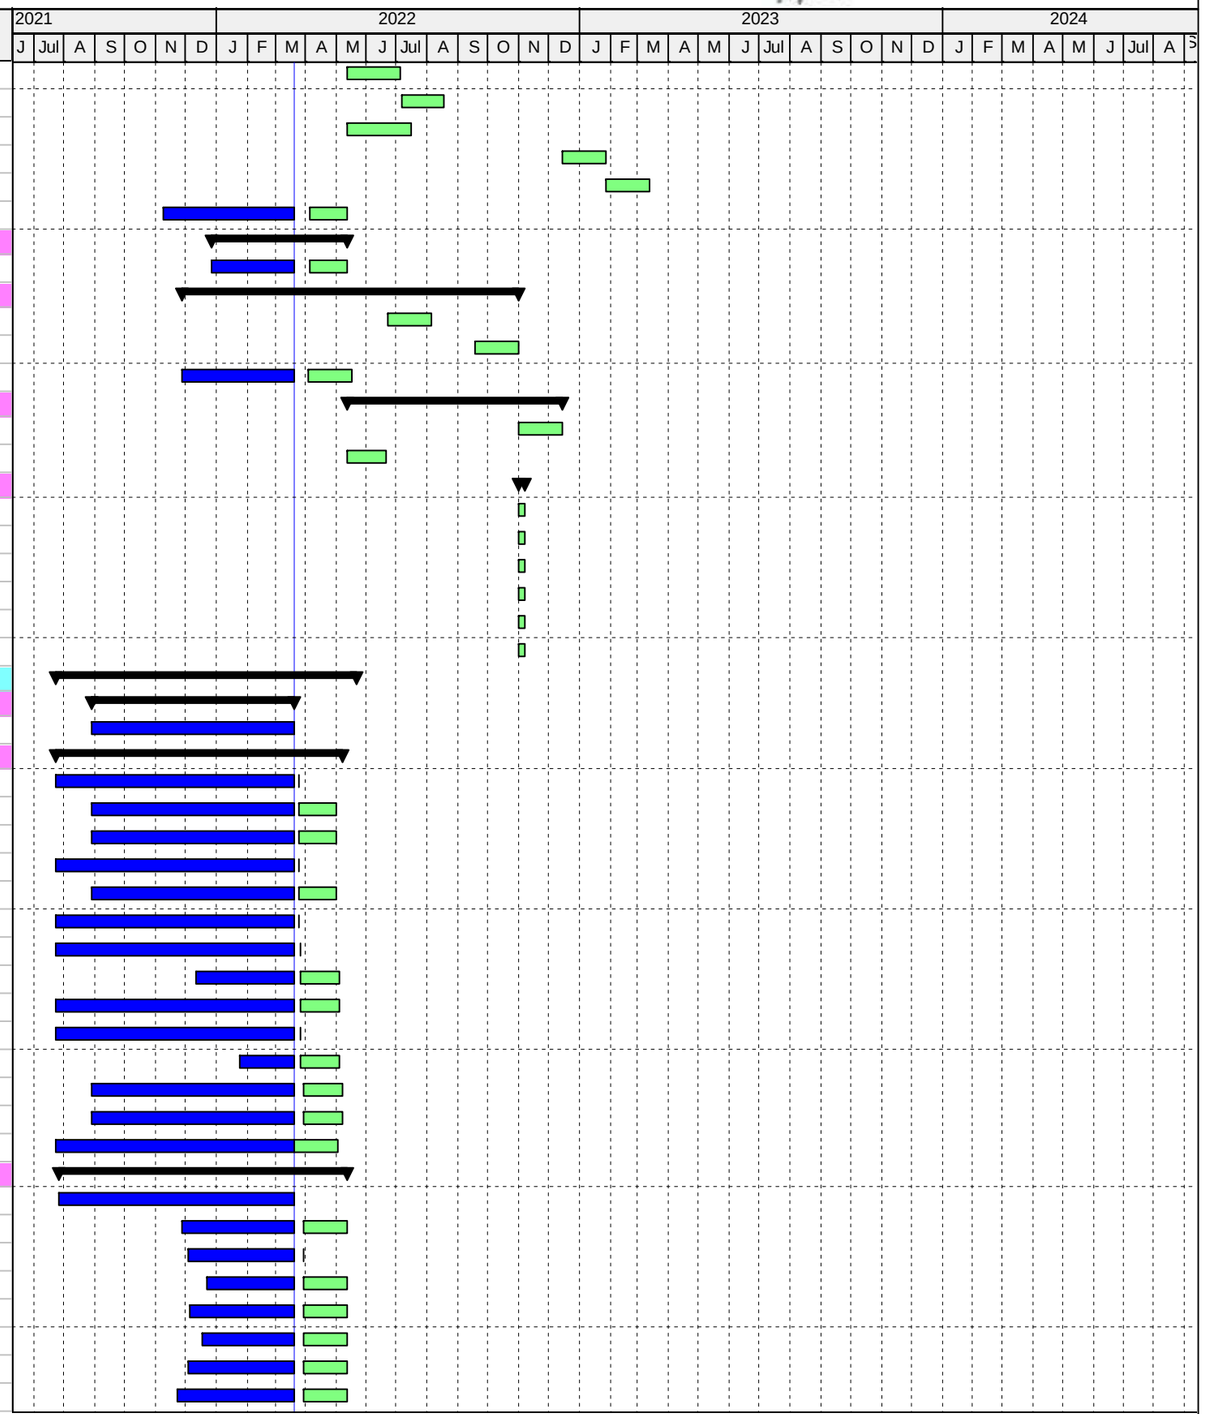


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05-E	Pipeline Standard Drawing For Pig Signaller Concrete Pit	44	60%	$2.12	27-Nov-21	12-May-22
P05-E	Pipeline Standard Drawing For H-Pipe Support	44	100%	$2.12	27-Nov-21	30-Mar-22
P05-E	Flowline Transversal Drawings - W008N	44	0%	$50.02	20-Mar-22	02-May-22
P05-E	Pipeline Hydrostatic Test Diagram - Sub Surface	44	0%	$4.74	20-Mar-22	02-May-22
Procedure/Plan		44	0%	$0.00	09-Apr-22	22-May-22
P05-E	Pipeline Hydrostatic Test Diagram - Sub Surface	44	0%	$0.00	09-Apr-22	22-May-22
List		44	0%	$14.71	20-Mar-22	02-May-22
P05-E	Road Crossing Location List	44	0%	$14.71	20-Mar-22	02-May-22
Report		44	80%	$21.34	27-Oct-21	22-May-22
P05-E	Pipeline Corrosion Study & Material Selection Report	44	80%	$21.34	27-Oct-21	22-May-22
MTO		7	100%	$7.00	22-Aug-21	04-May-22
P05-E	MTO For Line Pipes (Flowlines) - W008N	7	100%	$7.00	22-Aug-21	04-May-22
Control & Instrumentation		278	78.5%	$357.50	26-Jul-21 A	18-Sep-22
Basis/Criteria		44	94.56%	$15.84	14-Aug-21	29-Apr-22
P05-E	Fire & Gas Detection Design Criteria	38	100%	$13.68	14-Aug-21	27-Mar-22
P05-E	Instrument & Control System Design Criteria	38	60%	$2.16	03-Jan-22	29-Apr-22
Specification		42	86.9%	$81.33	26-Jul-21 A	26-Apr-22
P05-E	Specification For WHCP/HPU	38	80%	$53.29	08-Aug-21	26-Apr-22
P05-E	Specification For Instrumentation	39	100%	$28.04	26-Jul-21 A	23-Mar-22
Data Sheets		120	80%	$20.34	22-Aug-21	24-May-22
P05-E	Data Sheets For WHCP/HPU - Wellheads	49	80%	$10.04	22-Aug-21	07-May-22
P05-E	Data Sheets For Pressure Gauge - Wellheads	42	80%	$5.15	07-Dec-21	24-May-22
P05-E	Data Sheets For Temperature Gauge - Wellheads	42	80%	$5.15	07-Dec-21	24-May-22
Drawing/Diagram		112	26.69%	$83.58	22-Aug-21	17-Sep-22
P05-E	Instrument Hook-up Diagram - Wellheads	42	80%	$13.23	14-Nov-21	12-May-22
P05-E	WHCP Hydraulic \Peneumatic Diagrams - Wellheads	42	100%	$11.73	22-Aug-21	19-Apr-22
P05-E	Instrument Location Layout Drawing - W008N	44	0%	$58.63	05-Aug-22	17-Sep-22
List		7	100%	$43.40	10-Nov-21	13-May-22
P05-E	Instrument Index For New Wells & Manifold Extension	7	100%	$43.40	10-Nov-21	13-May-22
MTO		135	100%	$113.01	14-Nov-21	18-Sep-22
P05-E	MTO For Instrument Tube and Fitting - W008N	7	100%	$56.50	14-Nov-21	13-May-22
P05-E	MTO For Instrument Cable Tray - W008N	7	100%	$56.50	14-Nov-21	18-Sep-22
Safety		177	51.46%	$134.06	24-Jul-21 A	16-Oct-22
Basis/Criteria		44	100%	$13.41	29-Aug-21	19-Apr-22
P05-E	Active Fire Protection and Safety Concept	44	100%	$13.41	29-Aug-21	19-Apr-22
Specification		47	88.24%	$26.81	24-Jul-21 A	09-May-22
P05-E	Specification For Fire Fighting Equipment	44	100%	$4.73	29-Aug-21	24-Mar-22
P05-E	Specification For Hazardous Area Classification	44	100%	$4.73	24-Jul-21 A	24-Mar-22
P05-E	Specification For Fire Water System	44	80%	$6.31	24-Jul-21 A	09-May-22
P05-E	Specification For Environmental Job	44	60%	$4.73	11-Aug-21	06-May-22
P05-E	Specification For Total Flooding System	44	100%	$6.31	24-Jul-21 A	27-Mar-22
Data Sheets		47	100%	$13.41	08-Dec-21	27-Mar-22
P05-E	Data Sheets For Fire Fighting Equipment	44	100%	$4.47	08-Dec-21	24-Mar-22
P05-E	Data Sheets For Safety Equipment	44	100%	$4.47	08-Dec-21	27-Mar-22
P05-E	Data Sheets For Safety Sign	44	100%	$4.47	08-Dec-21	27-Mar-22
Drawing/Diagram		162	14.45%	$53.63	29-Aug-21	11-Oct-22
P05-E	Typical Installation Detail for Safety & Fire Fighting Equipment	14	100%	$3.87	29-Dec-21	27-Mar-22
P05-E	Symbol & Legend For Safety & Firefighting Systems	44	100%	$3.87	29-Aug-21	27-Mar-22
P05-E	Hazardous Area Classification Layout - W008N	44	0%	$15.29	03-May-22	15-Jun-22
P05-E	Safety & Fire Fighting Equipment Location Layout - W008N	44	0%	$15.30	16-Jul-22	28-Aug-22

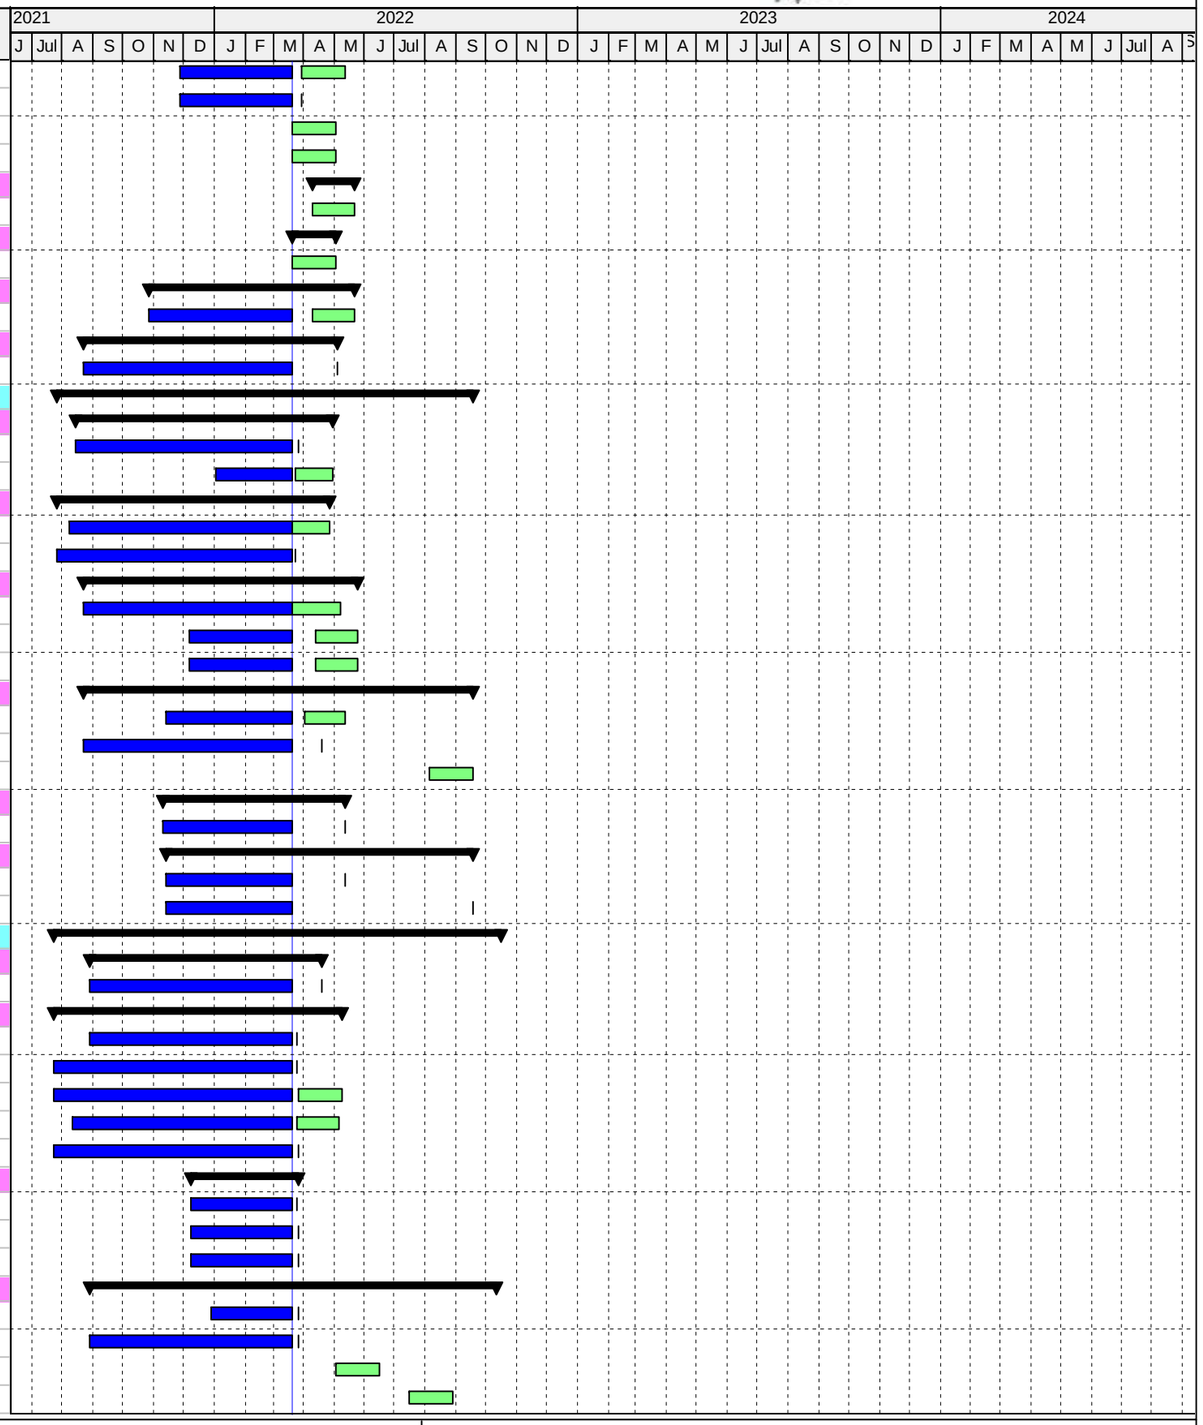


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05-E	Escape Route & Safety Sign Layout - W008N	44	0%	$15.30	29-Aug-22	11-Oct-22
List		44	80%	$13.41	09-Nov-21	02-May-22
P05-E	Hazard Source List - W008N	44	80%	$13.41	09-Nov-21	02-May-22
MTO		49	0%	$13.41	29-Aug-22	16-Oct-22
P05-E	MTO For Fire Fighting & Safety Equipment - W008N	7	0%	$6.70	29-Aug-22	04-Sep-22
P05-E	MTO For Safety Sign - W008N	5	0%	$6.70	12-Oct-22	16-Oct-22
Architecture		84	60%	$134.06	18-Dec-21	01-Jun-22
Basis/Criteria		74	60%	$26.81	08-Feb-22	01-Jun-22
P05-E	Architectural Design Criteria	74	60%	$26.81	08-Feb-22	01-Jun-22
Drawing/Diagram		84	60%	$107.25	18-Dec-21	02-May-22
P05-E	Architectural Drawing For WHCP/HPU Shelter of Well Pads -	44	60%	$77.50	26-Feb-22	02-May-22
P05-E	Standard Drawing for Architectural Details	44	60%	$29.75	18-Dec-21	02-May-22
Civil		449	29.3%	$804.38	01-Aug-21	04-Feb-23
Basis/Criteria		90	20%	$2.98	13-Feb-22	22-May-22
P05-E	Civil Design Criteria	64	60%	$0.99	13-Feb-22	22-May-22
P05-E	Design Criteria for Sewerage & Drainage	44	0%	$0.99	24-Mar-22	06-May-22
P05-E	Design Criteria for Road and Paving	44	0%	$0.99	27-Mar-22	09-May-22
Specification		94	72.14%	$15.04	09-Aug-21	06-Jun-22
P05-E	Specification For Civil Works	79	0%	$1.50	20-Mar-22	06-Jun-22
P05-E	Specification For Road & Paving	64	80%	$3.01	09-Aug-21	22-May-22
P05-E	Specification For Fence & Gate	64	100%	$3.01	18-Sep-21	20-Mar-22
P05-E	Specification For Earth Work	64	80%	$3.01	09-Aug-21	22-May-22
P05-E	Specification For Sewerage & Drainage	64	100%	$3.01	09-Aug-21	20-Mar-22
P05-E	Specification For Geological & Geotechnical Survey	44	0%	$1.50	20-Mar-22	02-May-22
Calculation		188	40%	$152.67	05-Dec-21	25-Dec-22
P05-E	Calculation Note For Heli Pad, Well Pad & Diesel Storage Pac	4	0%	$76.34	06-Dec-22	09-Dec-22
P05-E	Calculation Note For Flood Control	39	80%	$76.34	05-Dec-21	25-Dec-22
Drawing/Diagram		315	29.06%	$561.45	01-Aug-21	28-Jan-23
P05-E	Standard Drawing For Civil Works	64	0%	$9.83	30-Mar-22	01-Jun-22
P05-E	Standard Drawing For Slope Protection Details	64	100%	$9.83	22-Aug-21	30-Mar-22
P05-E	Standard Drawing For Roads	64	80%	$9.83	22-Aug-21	01-Jun-22
P05-E	Standard Drawing For Electrical Cable Trench	64	100%	$9.83	22-Aug-21	30-Mar-22
P05-E	Standard Drawing For Manholes	64	80%	$9.83	22-Aug-21	01-Jun-22
P05-E	Standard Drawing For Catch Basins	64	80%	$9.83	22-Aug-21	05-Jun-22
P05-E	Standard Drawing For Sewerage & Drainage Details	64	60%	$9.83	02-Feb-22	05-Jun-22
P05-E	Standard Drawing For Civil Underground Crossings	38	60%	$16.73	07-Feb-22	10-May-22
P05-E	Standard Drawing For Fence & Gate Details	64	100%	$9.83	18-Sep-21	03-Apr-22
P05-E	Standard Drawing For Concrete Continues Weight	33	100%	$16.34	01-Aug-21	20-Mar-22
P05-E	Standard Drawing For Major Floodway Crossing	38	0%	$16.34	03-Apr-22	10-May-22
P05-E	Standard Drawing For Culvert & Details	38	100%	$16.34	25-Sep-21	03-Apr-22
P05-E	Standard Drawing For Valve Box	38	100%	$16.34	12-Jan-22	03-Apr-22
P05-E	Standard Drawing For Fire Hydrant Pit	38	60%	$16.34	13-Mar-22	10-May-22
P05-E	Standard Drawing For Cable Pull Pit	64	0%	$9.83	03-Apr-22	05-Jun-22
P05-E	Standard Drawing For Pavings	38	60%	$16.34	08-Jan-22	10-May-22
P05-E	Standard Drawing For Earth Pit	38	60%	$16.34	13-Feb-22	10-May-22
P05-E	Standard Detail For Pipe Bedding	64	100%	$9.83	22-Aug-21	03-Apr-22
P05-E	Standard Details of Miscellaneous Items	64	60%	$9.83	06-Mar-22	05-Jun-22
P05-E	BINAK Oil Field Project Overall Well Location/Facilities Layou	54	0%	$7.41	20-Mar-22	12-May-22
P05-E	General Civil Layout -W008N	79	0%	$117.91	16-Jul-22	02-Oct-22

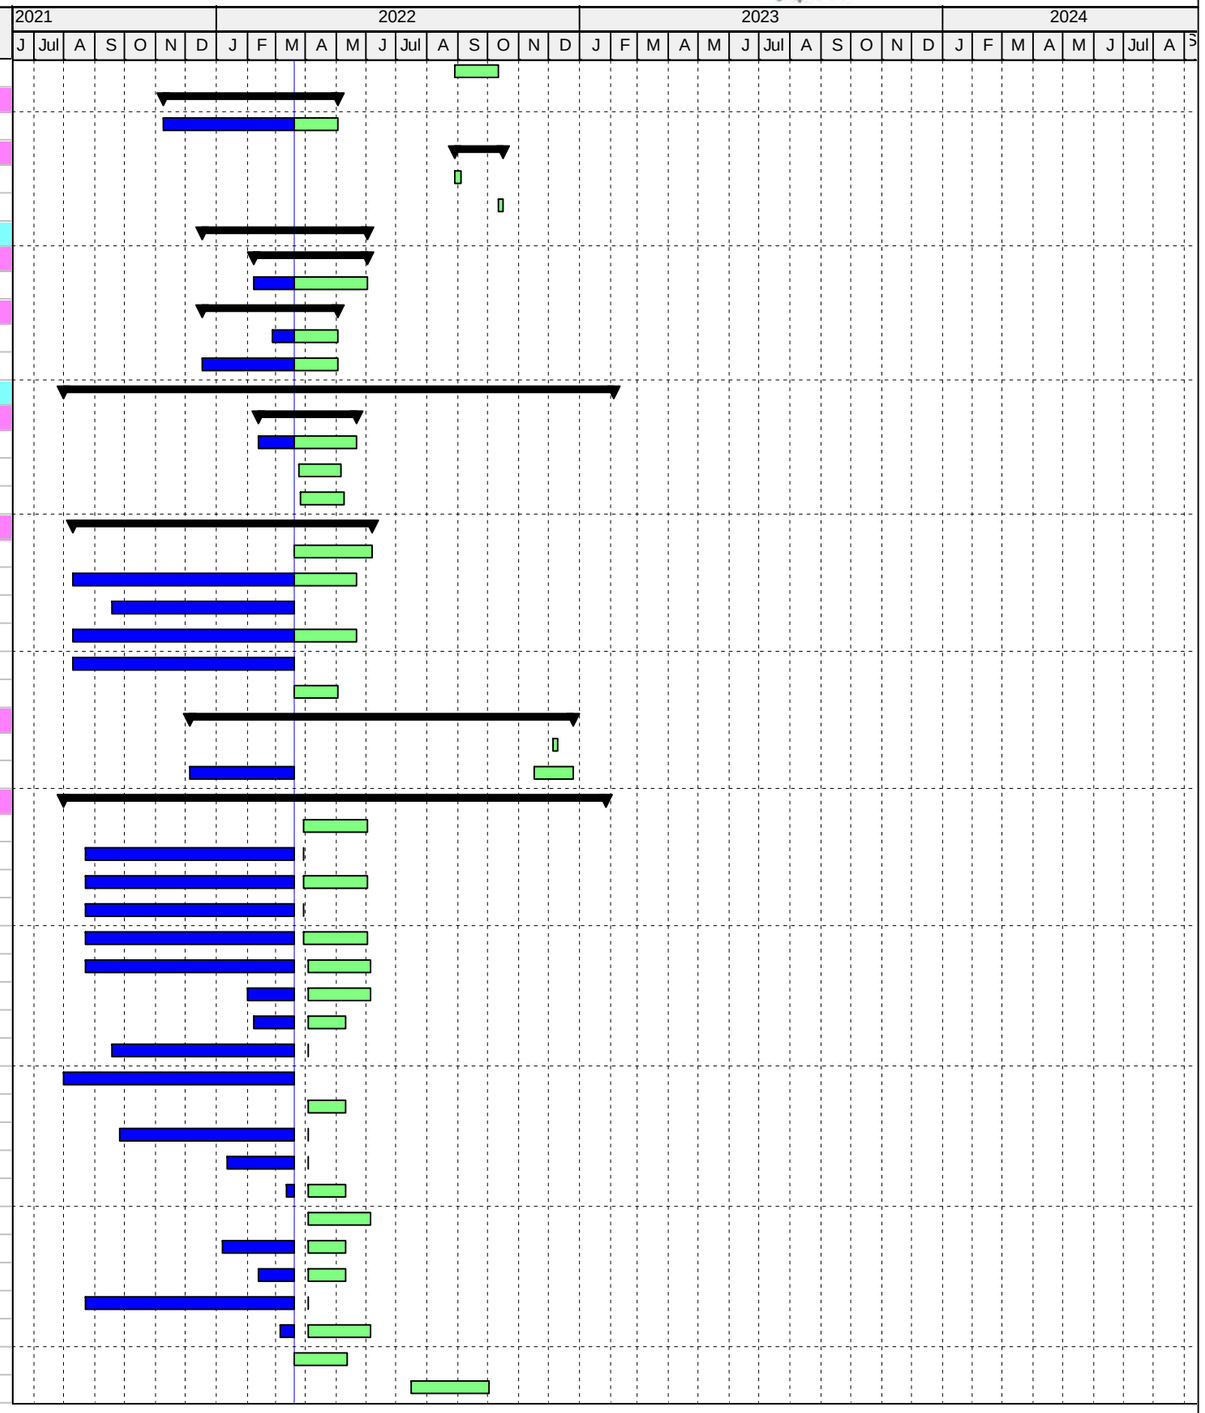


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05-E	Civil and Structural drawings -W008N	64	0%	$117.91	03-Oct-22	05-Dec-22
P05-E	Rough Grading Plans -W008N	54	0%	$79.05	06-Dec-22	28-Jan-23
MTO		7	0%	$72.23	29-Jan-23	04-Feb-23
P05-E	MTO For Civil Works	7	0%	$72.23	29-Jan-23	04-Feb-23
Structure		189	33.97%	$491.56	08-Aug-21	24-Sep-22
Basis/Criteria		64	0%	$5.36	20-Mar-22	22-May-22
P05-E	Structural Design Criteria	64	0%	$1.79	20-Mar-22	22-May-22
P05-E	Design Criteria For Steel Structure	44	0%	$1.79	20-Mar-22	02-May-22
P05-E	Design Criteria For Load & Forces	44	0%	$1.79	20-Mar-22	02-May-22
Specification		94	82.86%	$40.95	14-Aug-21	26-May-22
P05-E	Specification For Concrete Work	64	80%	$6.06	14-Aug-21	26-May-22
P05-E	Specification For Storage Tank Foundation	64	100%	$15.17	23-Nov-21	24-Mar-22
P05-E	Specification for Fabrication of Steel Structures	37	100%	$7.84	24-Jan-22	20-Mar-22
P05-E	Specification For Grouting	64	100%	$6.06	14-Aug-21	24-Mar-22
P05-E	Specification For Steel Structural Works	64	0%	$5.81	24-Mar-22	26-May-22
Drawing/Diagram		172	41.97%	$317.01	08-Aug-21	17-Sep-22
P05-E	Standard Drawing For Fire Proofing	64	100%	$7.96	08-Aug-21	03-Apr-22
P05-E	Standard Drawing For Anchor Bolts	64	100%	$7.96	15-Dec-21	03-Apr-22
P05-E	Standard Drawing For Steel Stairs	64	100%	$7.96	18-Dec-21	03-Apr-22
P05-E	Standard Drawing For Operating Platform	38	100%	$9.35	27-Dec-21	30-Mar-22
P05-E	Standard Drawing For Handrail	38	100%	$13.31	18-Dec-21	30-Mar-22
P05-E	Standard Drawing For Insert Plates in Concrete	38	100%	$13.31	08-Aug-21	30-Mar-22
P05-E	Standard Details For Ladder & Safety Cage	64	100%	$7.96	15-Dec-21	03-Apr-22
P05-E	Standard Drawing For Lighting pole foundation Plan & Details	38	60%	$13.31	29-Jan-22	06-May-22
P05-E	General Notes - Steel Structures	38	100%	$9.35	25-Jan-22	30-Mar-22
P05-E	General Notes - Reinforced Concrete Structures	38	100%	$13.31	20-Dec-21	30-Mar-22
P05-E	Standard Drawing For Structural Built-up Sections	44	80%	$13.31	04-Dec-21	12-May-22
P05-E	Standard Drawing For Steel Flooring, Grating and Chequere	44	100%	$13.31	05-Jan-22	30-Mar-22
P05-E	Concrete Reinforcement Shape Code	44	0%	$13.31	30-Mar-22	12-May-22
P05-E	Standard Drawing For Septic Tank	44	80%	$13.31	22-Jan-22	12-May-22
P05-E	Platform Structure Drawing - W008N	44	0%	$159.96	05-Aug-22	17-Sep-22
MTO		7	0%	$128.25	18-Sep-22	24-Sep-22
P05-E	MTO For Structural Works - W008N	7	0%	$128.25	18-Sep-22	24-Sep-22
General		201	12.06%	$1,072.50	11-Aug-21	06-Oct-22
Risk Assessment		44	100%	$53.63	05-Sep-21	20-Mar-22
Procedure/Plan		44	100%	$53.63	05-Sep-21	20-Mar-22
P05-	HAZID Study Procedure	44	100%	$53.63	05-Sep-21	20-Mar-22
Survey (Topography) & Geotechnic		171	7.06%	$911.63	11-Aug-21	06-Oct-22
Geotechnic		74	8%	$804.38	11-Aug-21	01-Jun-22
Procedure/Plan		44	100%	$64.35	11-Aug-21	19-Apr-22
P05	Geotechnical Investigation Plan for Well Pads	44	100%	$64.35	11-Aug-21	19-Apr-22
Report		44	0%	$740.03	19-Apr-22	01-Jun-22
P05	Geotechnical Investigation Report - W008N	44	0%	$740.03	19-Apr-22	01-Jun-22
Survey		46	0%	$107.25	22-Aug-22	06-Oct-22
Drawing/Diagram		46	0%	$107.25	22-Aug-22	06-Oct-22
P05	Flowline Plan & Profile Drawings - W008N	46	0%	$107.25	22-Aug-22	06-Oct-22
QC/QA		116	10.59%	$107.25	20-Sep-21	13-Jul-22
QC Management		116	39.14%	$8.72	08-Dec-21	13-Jul-22
P05-	Project Audit Procedure	44	0%	$0.44	20-Mar-22	02-May-22
P05-	Specification For Final Data Book (FDB) Requirements	44	0%	$0.44	20-Mar-22	02-May-22

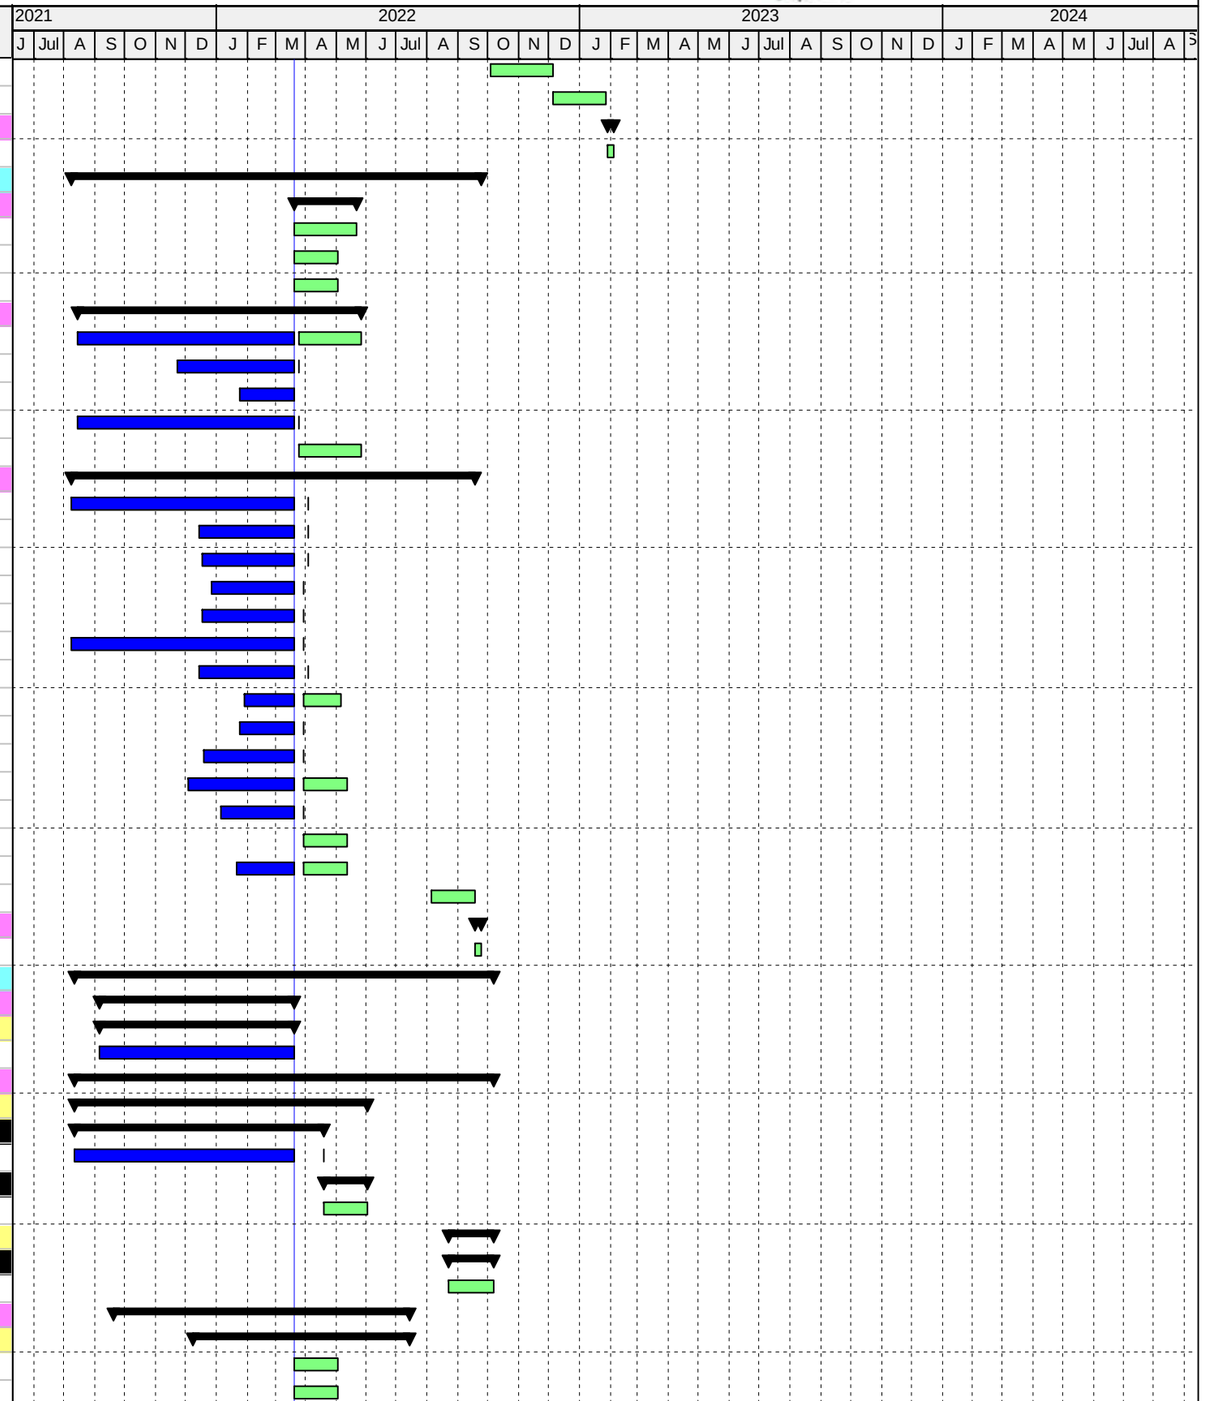


Actual Level of Effort Remaining Work Milestone
Actual Work Critical Remaining Work summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05-	Non Conformance Control Procedure	36	0%	$0.44	03-May-22	07-Jun-22
P05-	Corrective Action Procedure	36	0%	$0.44	08-Jun-22	13-Jul-22
P05-	Material Reciving, Storage, Handling Procedure	39	60%	$0.44	20-Feb-22	27-Apr-22
P05-	Packing, Marking, Transportation Procedure	39	0%	$0.44	20-Mar-22	27-Apr-22
P05-	Criticality Assessment Procedure	39	0%	$1.74	20-Mar-22	27-Apr-22
P05-	Project Quality Plan	44	80%	$3.92	08-Dec-21	02-May-22
P05-	Technical Query Procedure	44	0%	$0.44	30-Mar-22	12-May-22
QC General Document		55	8.57%	$12.73	28-Nov-21	16-May-22
P05-	Quality Control Plan (QCP)	39	60%	$1.82	28-Nov-21	27-Apr-22
P05-	Specification for Welding Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P05-	Heat Treatment Procedure (Pre Heating , PWHT)	44	0%	$1.82	03-Apr-22	16-May-22
P05-	Welder Performance Qualification Test (WQT) Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P05-	NDT Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P05-	Surface Preparation and Coating/Painting Procedure	44	0%	$1.82	03-Apr-22	16-May-22
P05-	Control of Inspection Measuring and Test Equipment Procedu	44	0%	$1.81	03-Apr-22	16-May-22
QC Discipline Document		81	7.99%	$85.80	20-Sep-21	16-May-22
Piping		51	0%	$21.45	27-Mar-22	16-May-22
P05	ITP For Piping Works	44	0%	$2.15	27-Mar-22	09-May-22
P05	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$2.41	03-Apr-22	16-May-22
P05	PIPING WPS (Welding Procedure Specification)	44	0%	$2.41	03-Apr-22	16-May-22
P05	PIPING PQR (Procedure Qualification Record)	44	0%	$2.41	03-Apr-22	16-May-22
P05	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$2.41	03-Apr-22	16-May-22
P05	PIPING WPS (Preliminary Welding Procedure Specification) f	44	0%	$2.41	03-Apr-22	16-May-22
P05	PIPING PQR (Procedure Qualification Record) for Repair We	44	0%	$2.41	03-Apr-22	16-May-22
P05	Field Joint Coating Procedure For Pipeline	44	0%	$2.41	03-Apr-22	16-May-22
P05	Pressure Test Procedure	44	0%	$2.41	03-Apr-22	16-May-22
Telecomm.		44	0%	$4.29	27-Mar-22	09-May-22
P05	ITP For Telecommunication Installation	44	0%	$4.29	27-Mar-22	09-May-22
Safety		44	0%	$4.29	27-Mar-22	09-May-22
P05	ITP For Safety Installation	44	0%	$4.29	27-Mar-22	09-May-22
Architectural		44	0%	$4.29	27-Mar-22	09-May-22
P05	ITP For Architectural Works	44	0%	$4.29	27-Mar-22	09-May-22
Mechanical		44	0%	$4.29	27-Mar-22	09-May-22
P05	ITP For Mechanical Installation	44	0%	$4.29	27-Mar-22	09-May-22
Structure		51	0%	$17.16	27-Mar-22	16-May-22
P05	ITP For Steel Structural Works	44	0%	$1.72	27-Mar-22	09-May-22
P05	Steel Structure WPS (Welding Procedure Specification)	44	0%	$2.57	03-Apr-22	16-May-22
P05	Steel Structure PQR (Procedure Qualification Record)	44	0%	$2.57	03-Apr-22	16-May-22
P05	Steel Structure WPS (Welding Procedure Specification) For F	44	0%	$2.57	03-Apr-22	16-May-22
P05	Steel Structure PQR (Procedure Qualification Record) For Re	44	0%	$2.57	03-Apr-22	16-May-22
P05	Weld Map For Steel Structures	44	0%	$2.57	03-Apr-22	16-May-22
P05	NDT Plan For steel Structures	44	0%	$2.57	03-Apr-22	16-May-22
Instrumentation		44	0%	$4.29	27-Mar-22	09-May-22
P05	ITP For I&C Installation	44	0%	$4.29	27-Mar-22	09-May-22
Pipeline		74	15%	$17.16	16-Jan-22	16-May-22
P05	ITP For Pipeline	44	60%	$1.72	16-Jan-22	09-May-22
P05	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	60%	$2.57	23-Feb-22	16-May-22
P05	PIPELINE WPS (Welding Procedure Specification)	44	0%	$2.57	03-Apr-22	16-May-22
P05	PIPELINE PQR (Procedure Qualification Record)	44	0%	$2.57	03-Apr-22	16-May-22

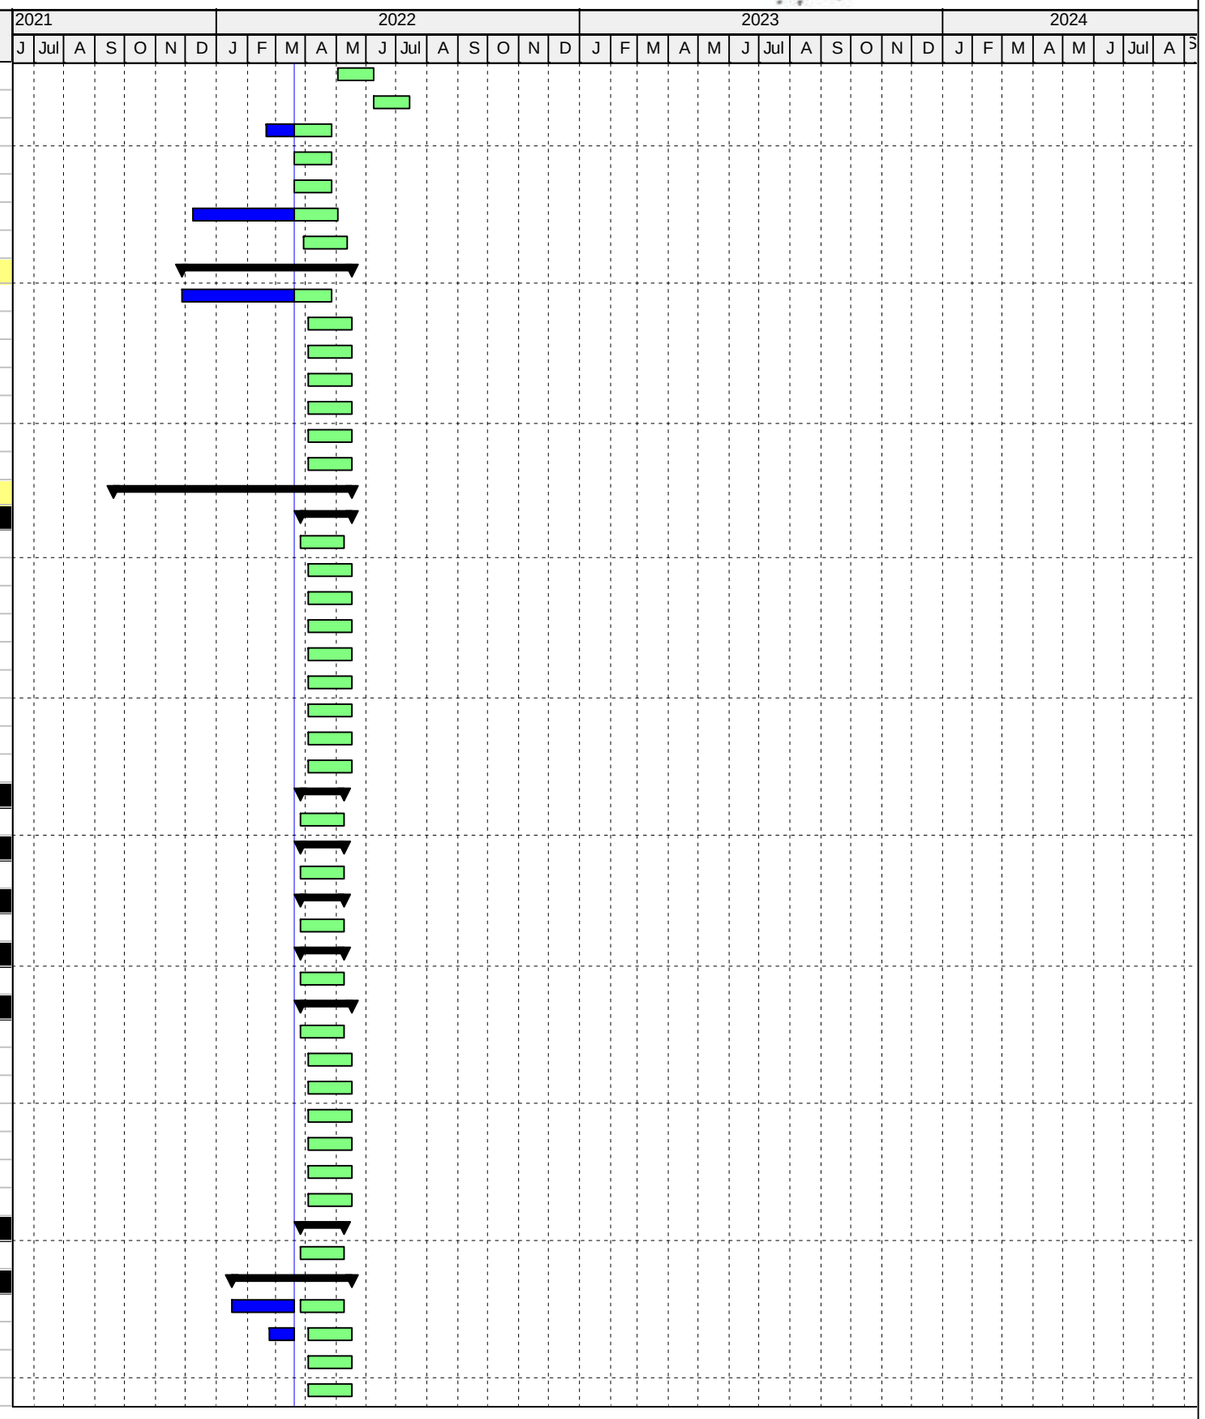


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	0%	$2.57	03-Apr-22	16-May-22
P05	PIPELINE WPS (Preliminary Welding Procedure Specificatior	44	0%	$2.57	03-Apr-22	16-May-22
P05	PIPELINE PQR (Procedure Qualification Record) for Repair \	44	0%	$2.57	03-Apr-22	16-May-22
Civil		44	100%	$4.29	20-Sep-21	27-Mar-22
P05	ITP For Civil Works	44	100%	$4.29	20-Sep-21	27-Mar-22
Electrical		44	0%	$4.29	27-Mar-22	09-May-22
P05	ITP For Electrical Installation	44	0%	$4.29	27-Mar-22	09-May-22
Procurement Engineering		301	7.26%	$812.50	15-Nov-21	25-Jan-23
Piping		219	0%	$211.25	21-Jun-22	25-Jan-23
Pipes		79	0%	$23.49	08-Nov-22	25-Jan-23
P05-E	PMR For Pipes - W008N	10	0%	$2.35	08-Nov-22	17-Nov-22
P05-E	TBE For Pipes - W008N	30	0%	$3.52	15-Nov-22	14-Dec-22
P05-E	VDR For Pipes - W008N	7	0%	$17.62	19-Jan-23	25-Jan-23
Fittings		79	0%	$23.47	08-Nov-22	25-Jan-23
P05-E	PMR For Fittings - W008N	10	0%	$2.35	08-Nov-22	17-Nov-22
P05-E	TBE For Fitting - W008N	30	0%	$3.52	15-Nov-22	14-Dec-22
P05-E	VDR For Fitting - W008N	7	0%	$17.60	19-Jan-23	25-Jan-23
Flanges		79	0%	$23.47	08-Nov-22	25-Jan-23
P05-E	PMR For Flanges - W008N	10	0%	$2.35	08-Nov-22	17-Nov-22
P05-E	TBE For Flanges - W008N	30	0%	$3.52	15-Nov-22	14-Dec-22
P05-E	VDR For Flanges - W008N	7	0%	$17.60	19-Jan-23	25-Jan-23
Manual Valves		69	0%	$23.47	08-Nov-22	15-Jan-23
P05-E	PMR For Manual Valves - W008N	10	0%	$2.35	08-Nov-22	17-Nov-22
P05-E	TBE For Manual Valves - W008N	30	0%	$3.52	15-Nov-22	14-Dec-22
P05-E	VDR For Manual Valves - W008N	7	0%	$17.60	09-Jan-23	15-Jan-23
Gaskets		79	0%	$23.47	08-Nov-22	25-Jan-23
P05-E	PMR For Gaskets - W008N	10	0%	$2.35	08-Nov-22	17-Nov-22
P05-E	TBE For Gaskets - W008N	30	0%	$3.52	15-Nov-22	14-Dec-22
P05-E	VDR For Gaskets - W008N	7	0%	$17.60	19-Jan-23	25-Jan-23
Bolt & Nuts		79	0%	$23.47	08-Nov-22	25-Jan-23
P05-E	PMR For Bolt/Nuts - W008N	10	0%	$2.35	08-Nov-22	17-Nov-22
P05-E	TBE For Bolt/Nuts - W008N	30	0%	$3.52	15-Nov-22	14-Dec-22
P05-E	VDR For Bolt/Nuts - W008N	7	0%	$17.60	19-Jan-23	25-Jan-23
Sampling Connection		79	0%	$23.47	21-Jun-22	07-Sep-22
P05-E	PMR For Sampling Connection Set - W008N	10	0%	$2.35	21-Jun-22	30-Jun-22
P05-E	TBE For Sampling Connection Set - W008N	30	0%	$3.52	28-Jun-22	27-Jul-22
P05-E	VDR For Sampling Connection Set - W008N	7	0%	$17.60	01-Sep-22	07-Sep-22
Stone Trap		79	0%	$23.47	05-Aug-22	22-Oct-22
P05-E	PMR For Stone Trap - W008N	10	0%	$2.35	05-Aug-22	14-Aug-22
P05-E	TBE For Stone Trap - W008N	30	0%	$3.52	12-Aug-22	10-Sep-22
P05-E	VDR For Stone Trap - W008N	7	0%	$17.60	16-Oct-22	22-Oct-22
Pipe Support		54	0%	$23.47	01-Nov-22	24-Dec-22
P05-E	PMR For Pipe Support - W008N	5	0%	$2.35	01-Nov-22	05-Nov-22
P05-E	TBE For Pipe Support - W008N	5	0%	$3.52	08-Nov-22	12-Nov-22
P05-E	VDR For Pipe Support - W008N	7	0%	$17.60	18-Dec-22	24-Dec-22
Pipeline		75	7.5%	$47.13	19-Feb-22	01-Jul-22
Line Pipe		74	15%	$23.56	19-Feb-22	01-Jul-22
P05-E	PMR For Line Pipes - W008N	10	0%	$2.36	04-May-22	13-May-22
P05-E	TBE For Line Pipes - W008N	30	100%	$3.53	19-Feb-22	21-May-22
P05-E	VDR For Line Pipes - W008N	7	0%	$17.67	25-Jun-22	01-Jul-22

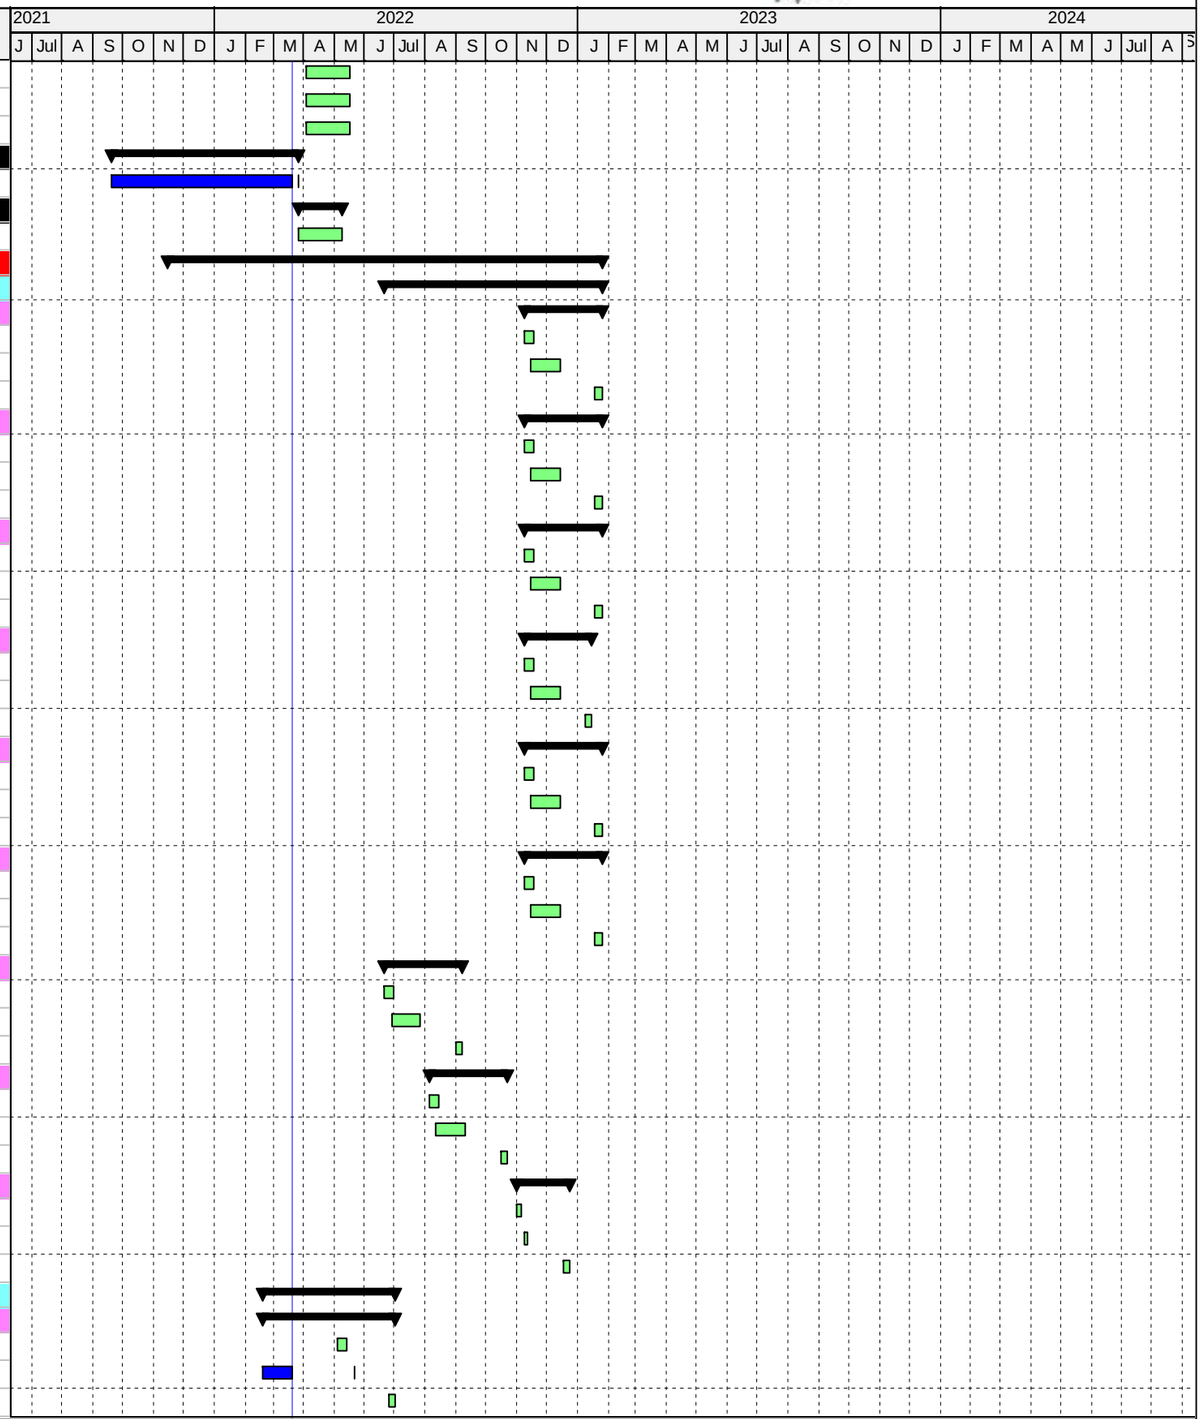


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Flow Line Support		54	0%	$23.56	03-May-22	25-Jun-22
P05-E	PMR For Flowline Support - W008N	5	0%	$2.36	03-May-22	07-May-22
P05-E	TBE For Flowline Support - W008N	5	0%	$3.53	10-May-22	14-May-22
P05-E	VDR For Flowline Support - W008N	7	0%	$17.67	19-Jun-22	25-Jun-22
Control & Instrumentation		291	20.58%	$269.75	15-Nov-21	29-Oct-22
WHCP/HPU		37	24.98%	$95.22	15-Nov-21	29-Jun-22
P05-E	PMR For WHCP/HPU - W008N	10	100%	$9.52	15-Nov-21	19-Apr-22
P05-E	TBE/TBA For WHCP/HPU - W008N	30	100%	$14.28	01-Dec-21	19-Apr-22
P05-E	VDR/TBA For WHCP/HPU - W008N	7	0%	$71.42	23-Jun-22	29-Jun-22
Field Instrumentations		114	10%	$79.33	13-Dec-21	23-Jul-22
P05-E	PMR For Field Instrumentations - W008N	10	100%	$7.93	13-Dec-21	13-May-22
P05-E	TBE/TBA For Field Instrumentations - W008N	30	0%	$11.90	13-May-22	11-Jun-22
P05-E	VDR/TBA For Field Instrumentations - W008N	7	0%	$59.50	17-Jul-22	23-Jul-22
Instrument Bulk Items		128	24.99%	$95.19	16-Jan-22	29-Oct-22
P05-E	PMR For Instrument Bulk Items - W008N	10	100%	$9.52	16-Jan-22	18-Sep-22
P05-E	TBE/TBA For Instrument Bulk Items	30	100%	$14.28	02-Feb-22	18-Sep-22
P05-E	VDR/TBA For Instrument Bulk Items	7	0%	$71.40	23-Oct-22	29-Oct-22
Safety & Fire Fighting		121	0%	$190.13	05-Sep-22	03-Jan-23
Fire Fighting and Safety Equipment		79	0%	$102.99	05-Sep-22	22-Nov-22
P05-E	PMR For Fire Fighting and Safety Equipment - W008N	10	0%	$10.30	05-Sep-22	14-Sep-22
P05-E	TBE For Fire Fighting and Safety Equipment - W008N	30	0%	$15.45	12-Sep-22	11-Oct-22
P05-E	VDR For Fire Fighting and Safety Equipment - W008N	7	0%	$77.24	16-Nov-22	22-Nov-22
Safety Sign		79	0%	$87.13	17-Oct-22	03-Jan-23
P05-E	PMR For Fire Safety Sign - W008N	10	0%	$8.71	17-Oct-22	26-Oct-22
P05-E	TBE For Fire Safety Sign - W008N	30	0%	$13.07	24-Oct-22	22-Nov-22
P05-E	VDR For Fire Safety Sign - W008N	7	0%	$65.35	28-Dec-22	03-Jan-23
Structure		42	0%	$47.13	25-Sep-22	05-Nov-22
Steel Structure Items		42	0%	$23.56	25-Sep-22	05-Nov-22
P05-E	PMR For Steel Structure Items - W008N	10	0%	$2.36	25-Sep-22	04-Oct-22
P05-E	TBE For Steel Structure Items - W008N	30	0%	$3.53	02-Oct-22	31-Oct-22
P05-E	VDR For Steel Structure Items - W008N	5	0%	$17.67	01-Nov-22	05-Nov-22
Anchor Bolts		42	0%	$23.56	25-Sep-22	05-Nov-22
P05-E	PMR For Anchor Bolts - W008N	10	0%	$2.36	25-Sep-22	04-Oct-22
P05-E	TBE For Anchor Bolts - W008N	30	0%	$3.53	02-Oct-22	31-Oct-22
P05-E	VDR For Anchor Bolts - W008N	5	0%	$17.67	01-Nov-22	05-Nov-22
Civil		17	0%	$47.13	03-Oct-22	19-Oct-22
Geomembrane		17	0%	$23.56	03-Oct-22	19-Oct-22
P05-E	PMR For Geomembrane - W008N	5	0%	$2.36	03-Oct-22	07-Oct-22
P05-E	TBE For Geomembrane - W008N	5	0%	$3.53	10-Oct-22	14-Oct-22
P05-E	VDR For Geomembrane - W008N	5	0%	$17.67	15-Oct-22	19-Oct-22
Geotextile		17	0%	$23.56	03-Oct-22	19-Oct-22
P05-E	PMR For Geotextile - W008N	5	0%	$2.36	03-Oct-22	07-Oct-22
P05-E	TBE For Geotextile - W008N	5	0%	$3.53	10-Oct-22	14-Oct-22
P05-E	VDR For Geotextile - W008N	5	0%	$17.67	15-Oct-22	19-Oct-22
Commissioning Engineering		599	0%	$162.50	20-Mar-22	08-Nov-23
P05-EP	Operability Review	5	0%	$32.50	20-Mar-22	24-Mar-22
P05-EP	Pre-Commissioning, Commissioning & Startup Procedure - W	44	0%	$97.50	20-Mar-22	02-May-22
P05-EP	Operating Manual - W008N	40	0%	$32.50	30-Sep-23	08-Nov-23
Field Engineering		359	0%	$1,218.75	25-Nov-22	18-Nov-23
P05-EP	Technical/Site Queries	30	0%	$609.38	25-Nov-22	24-Dec-22

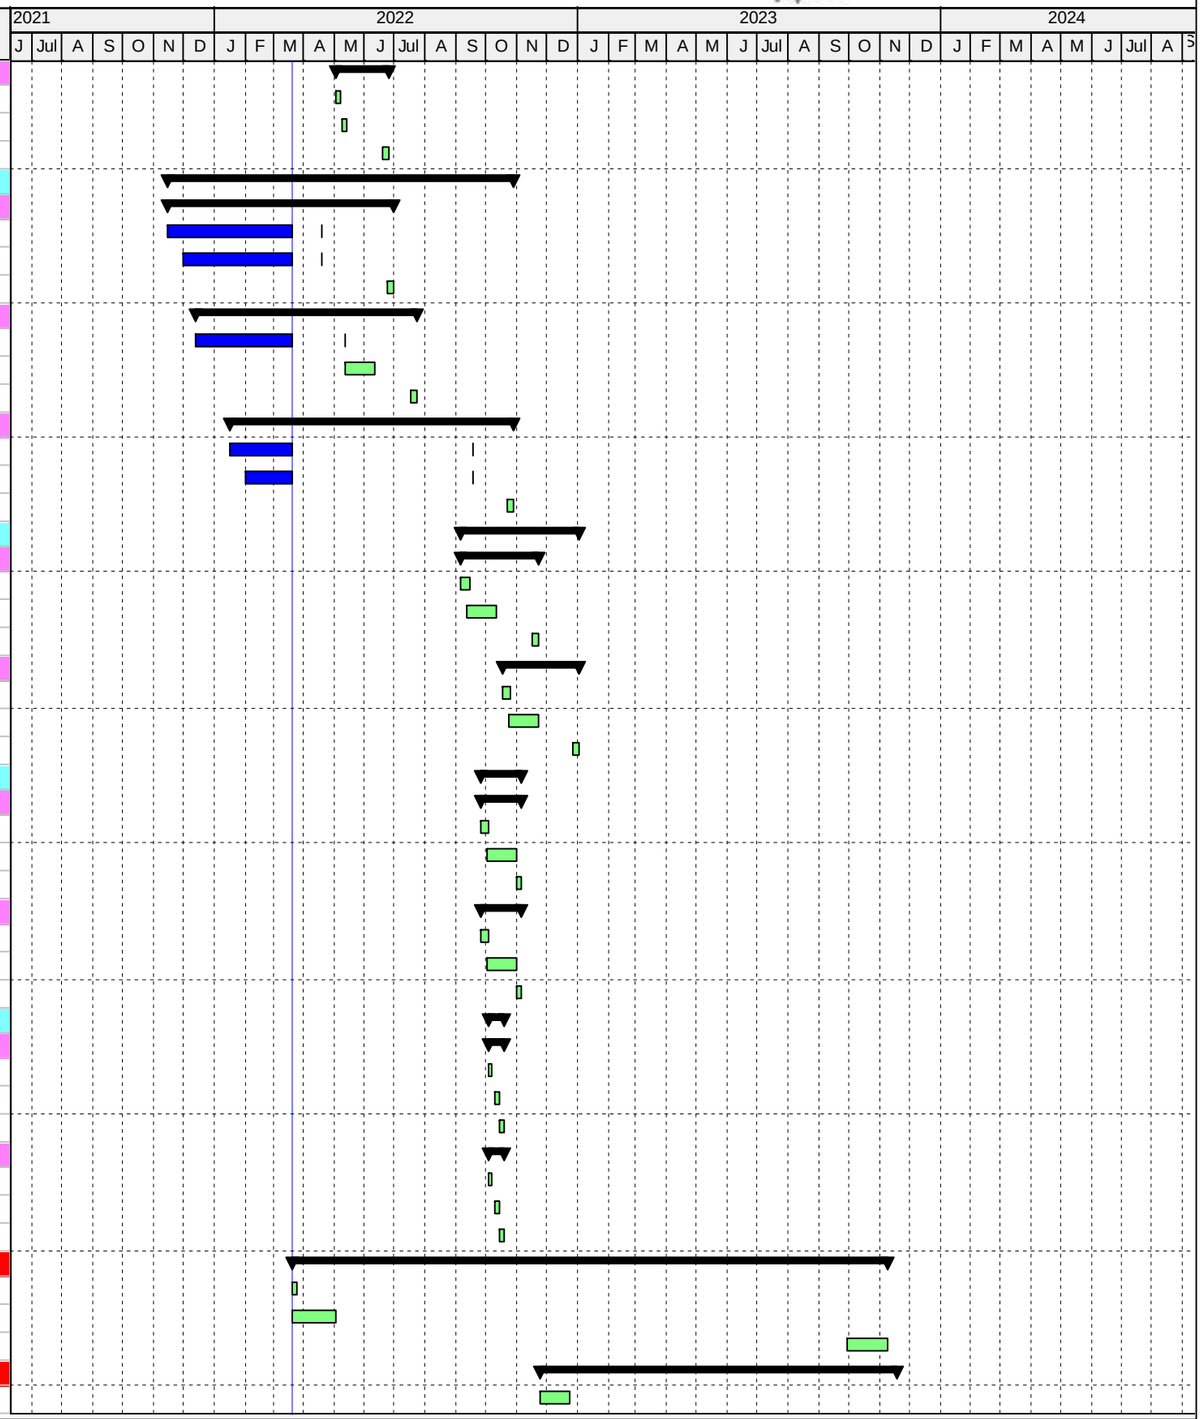


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05-EP	As-Built Document Booklets - W008N	10	0%	$609.38	09-Nov-23	18-Nov-23
Engineering Final Documentation		10	0%	$812.50	19-Nov-23	28-Nov-23
P05-EP	Final Engineering Dossier - W008N	10	0%	$812.50	19-Nov-23	28-Nov-23
PROCUREMENT		534	0%	$100,063.00	01-Feb-22	04-Oct-23
Wellhead Facility and Flowline		534	0%	$59,997.77	01-Feb-22	04-Oct-23
Piping		434	0%	$9,779.64	28-Jul-22	04-Oct-23
Pipes - W008N		269	0%	$1,955.93	15-Dec-22	09-Sep-23
P05-E	Tendering & Selection	30	0%	$78.24	15-Dec-22	13-Jan-23
P05-E	Contract Effectiveness / PO	5	0%	$117.36	14-Jan-23	18-Jan-23
P05-E	Manufacturing / Fabrication / Supply	210	0%	$977.96	19-Jan-23	16-Aug-23
P05-E	Final Inspection	12	0%	$195.59	17-Aug-23	28-Aug-23
P05-E	Delivery On Site	7	0%	$488.98	29-Aug-23	04-Sep-23
P05-E	Submitting Vendor Data Book	5	0%	$97.80	05-Sep-23	09-Sep-23
Fittings - W008N		269	0%	$733.47	15-Dec-22	09-Sep-23
P05-E	Tendering & Selection	30	0%	$29.34	15-Dec-22	13-Jan-23
P05-E	Contract Effectiveness / PO	5	0%	$44.01	14-Jan-23	18-Jan-23
P05-E	Manufacturing / Fabrication / Supply	210	0%	$366.74	19-Jan-23	16-Aug-23
P05-E	Final Inspection	12	0%	$73.35	17-Aug-23	28-Aug-23
P05-E	Delivery On Site	7	0%	$183.37	29-Aug-23	04-Sep-23
P05-E	Submitting Vendor Data Book	5	0%	$36.67	05-Sep-23	09-Sep-23
Flanges - W008N		269	0%	$733.47	15-Dec-22	09-Sep-23
P05-E	Tendering & Selection	30	0%	$29.34	15-Dec-22	13-Jan-23
P05-E	Contract Effectiveness / PO	5	0%	$44.01	14-Jan-23	18-Jan-23
P05-E	Manufacturing / Fabrication / Supply	210	0%	$366.74	19-Jan-23	16-Aug-23
P05-E	Final Inspection	12	0%	$73.35	17-Aug-23	28-Aug-23
P05-E	Delivery On Site	7	0%	$183.37	29-Aug-23	04-Sep-23
P05-E	Submitting Vendor Data Book	5	0%	$36.67	05-Sep-23	09-Sep-23
Manual Valves - W008N		294	0%	$3,422.87	15-Dec-22	04-Oct-23
P05-E	Tendering & Selection	20	0%	$136.91	15-Dec-22	03-Jan-23
P05-E	Contract Effectiveness / PO	5	0%	$205.37	04-Jan-23	08-Jan-23
P05-E	Manufacturing / Fabrication / Supply	240	0%	$1,711.44	09-Jan-23	05-Sep-23
P05-E	Final Inspection	12	0%	$342.29	06-Sep-23	17-Sep-23
P05-E	Delivery On Site	7	0%	$684.57	18-Sep-23	24-Sep-23
P05-E	Submitting Vendor Data Book	5	0%	$171.14	25-Sep-23	29-Sep-23
P05-E	Delivering Spare Parts	5	0%	$171.14	30-Sep-23	04-Oct-23
Gaskets - W008N		269	0%	$293.39	15-Dec-22	09-Sep-23
P05-E	Tendering & Selection	30	0%	$11.74	15-Dec-22	13-Jan-23
P05-E	Contract Effectiveness / PO	5	0%	$17.60	14-Jan-23	18-Jan-23
P05-E	Manufacturing / Fabrication / Supply	210	0%	$146.69	19-Jan-23	16-Aug-23
P05-E	Final Inspection	12	0%	$29.34	17-Aug-23	28-Aug-23
P05-E	Delivery On Site	7	0%	$73.35	29-Aug-23	04-Sep-23
P05-E	Submitting Vendor Data Book	5	0%	$14.67	05-Sep-23	09-Sep-23
Bolt/Nuts - W008N		179	0%	$195.59	15-Dec-22	11-Jun-23
P05-E	Tendering & Selection	30	0%	$7.82	15-Dec-22	13-Jan-23
P05-E	Contract Effectiveness / PO	5	0%	$11.74	14-Jan-23	18-Jan-23
P05-E	Manufacturing / Fabrication / Supply	120	0%	$97.80	19-Jan-23	18-May-23
P05-E	Final Inspection	12	0%	$19.56	19-May-23	30-May-23
P05-E	Delivery On Site	7	0%	$48.90	31-May-23	06-Jun-23
P05-E	Submitting Vendor Data Book	5	0%	$9.78	07-Jun-23	11-Jun-23

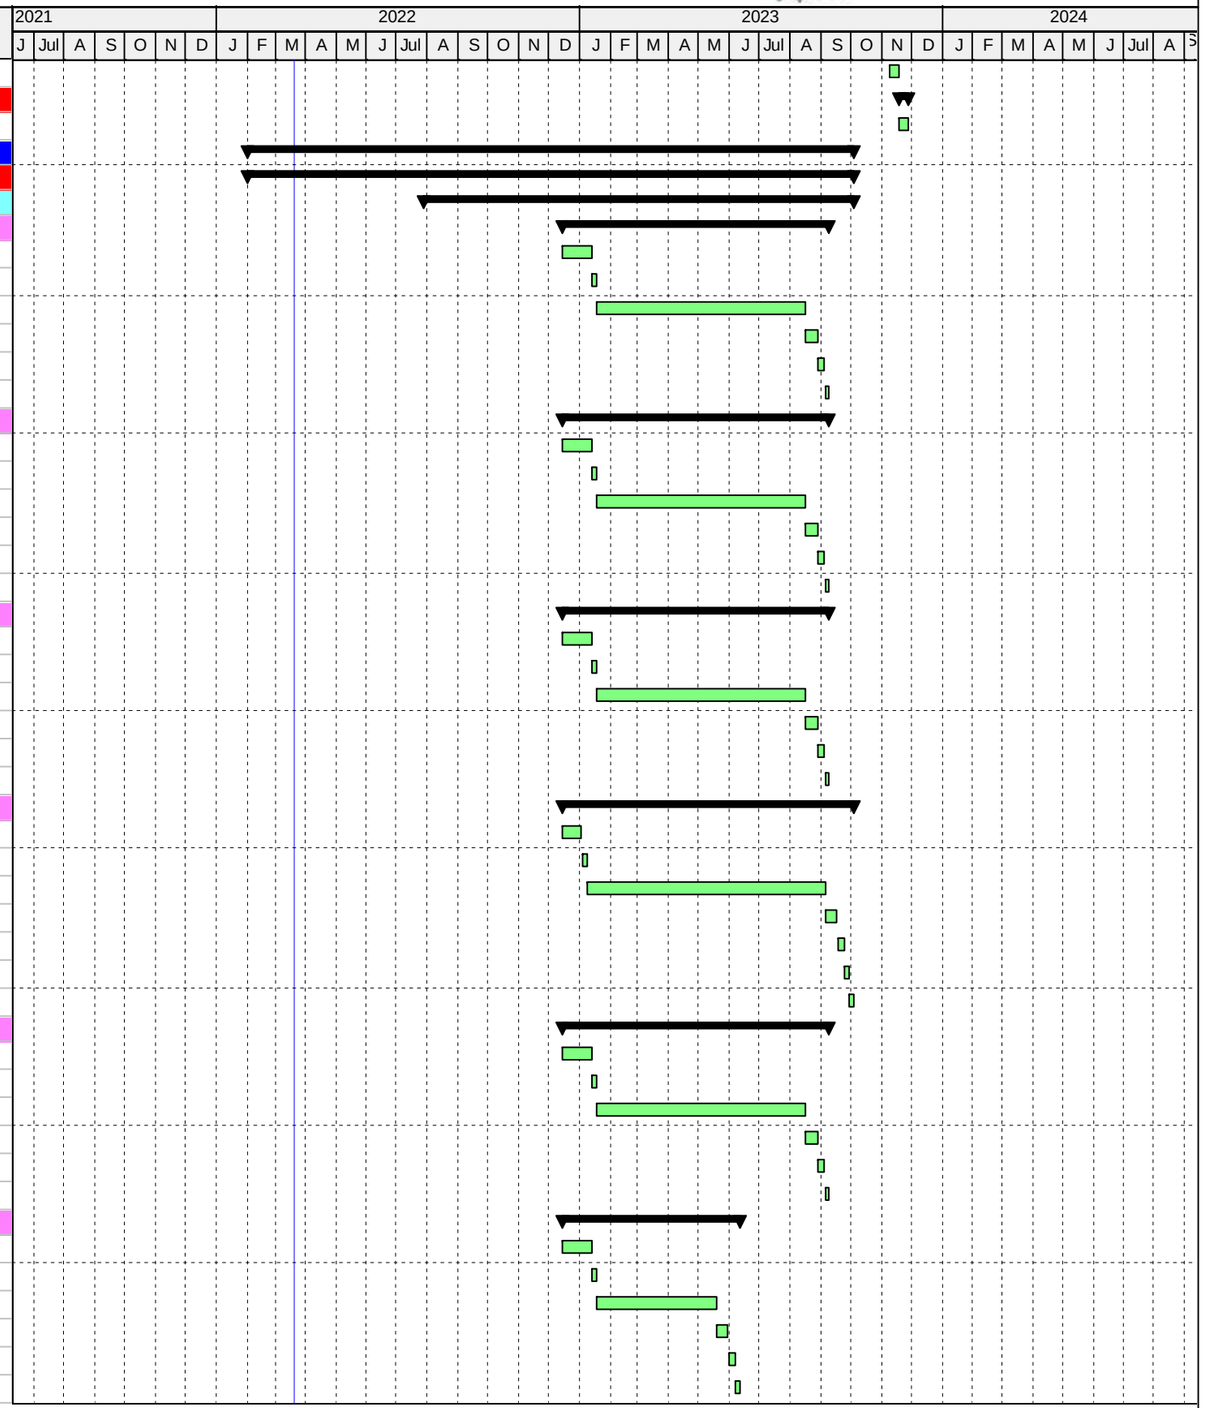


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Sampling Connection Set - W008N		119	0%	$488.98	28-Jul-22	23-Nov-22
P05-E	Tendering & Selection	30	0%	$19.56	28-Jul-22	26-Aug-22
P05-E	Contract Effectiveness / PO	5	0%	$29.34	27-Aug-22	31-Aug-22
P05-E	Manufacturing / Fabrication / Supply	60	0%	$244.49	01-Sep-22	30-Oct-22
P05-E	Final Inspection	12	0%	$48.90	31-Oct-22	11-Nov-22
P05-E	Delivery On Site	7	0%	$122.25	12-Nov-22	18-Nov-22
P05-E	Submitting Vendor Data Book	5	0%	$24.45	19-Nov-22	23-Nov-22
Stone Trap - W008N		119	0%	$1,466.95	11-Sep-22	07-Jan-23
P05-E	Tendering & Selection	30	0%	$58.68	11-Sep-22	10-Oct-22
P05-E	Contract Effectiveness / PO	5	0%	$88.02	11-Oct-22	15-Oct-22
P05-E	Manufacturing / Fabrication / Supply	60	0%	$733.47	16-Oct-22	14-Dec-22
P05-E	Final Inspection	12	0%	$146.69	15-Dec-22	26-Dec-22
P05-E	Delivery On Site	7	0%	$366.74	27-Dec-22	02-Jan-23
P05-E	Submitting Vendor Data Book	5	0%	$73.35	03-Jan-23	07-Jan-23
Pipe Support - W008N		119	0%	$488.98	13-Nov-22	11-Mar-23
P05-E	Tendering & Selection	30	0%	$19.56	13-Nov-22	12-Dec-22
P05-E	Contract Effectiveness / PO	5	0%	$29.34	13-Dec-22	17-Dec-22
P05-E	Manufacturing / Fabrication / Supply	60	0%	$244.49	18-Dec-22	15-Feb-23
P05-E	Final Inspection	12	0%	$48.90	16-Feb-23	27-Feb-23
P05-E	Delivery On Site	7	0%	$122.25	28-Feb-23	06-Mar-23
P05-E	Submitting Vendor Data Book	5	0%	$24.45	07-Mar-23	11-Mar-23
Pipeline		275	0%	$43,678.38	15-May-22	13-Feb-23
Line Pipes - W008N		269	0%	$37,126.62	21-May-22	13-Feb-23
P05-E	Tendering & Selection	30	0%	$1,485.06	21-May-22	19-Jun-22
P05-E	Contract Effectiveness / PO	5	0%	$2,227.60	20-Jun-22	24-Jun-22
P05-E	Manufacturing / Fabrication / Supply	210	0%	$18,563.31	25-Jun-22	20-Jan-23
P05-E	Final Inspection	12	0%	$3,712.66	21-Jan-23	01-Feb-23
P05-E	Delivery On Site	7	0%	$9,281.66	02-Feb-23	08-Feb-23
P05-E	Submitting Vendor Data Book	5	0%	$1,856.33	09-Feb-23	13-Feb-23
Flow Line Support - W008N		239	0%	$6,551.76	15-May-22	08-Jan-23
P05-E	Tendering & Selection	30	0%	$262.07	15-May-22	13-Jun-22
P05-E	Contract Effectiveness / PO	5	0%	$393.11	14-Jun-22	18-Jun-22
P05-E	Manufacturing / Fabrication / Supply	180	0%	$3,275.88	19-Jun-22	15-Dec-22
P05-E	Final Inspection	12	0%	$655.18	16-Dec-22	27-Dec-22
P05-E	Delivery On Site	7	0%	$1,637.94	28-Dec-22	03-Jan-23
P05-E	Submitting Vendor Data Book	5	0%	$327.59	04-Jan-23	08-Jan-23
Control & Instrumentation		301	0%	$6,107.77	01-Feb-22	13-Feb-23
Field Instrumentations - W008N		184	0%	$305.39	12-Jun-22	12-Dec-22
P05-E	Tendering & Selection	30	0%	$12.22	12-Jun-22	11-Jul-22
P05-E	Contract Effectiveness / PO	5	0%	$18.32	12-Jul-22	16-Jul-22
P05-E	Manufacturing / Fabrication / Supply	120	0%	$152.69	17-Jul-22	13-Nov-22
P05-E	Final Inspection	12	0%	$30.54	14-Nov-22	25-Nov-22
P05-E	Delivery On Site	7	0%	$61.08	26-Nov-22	02-Dec-22
P05-E	Submitting Vendor Data Book	5	0%	$15.27	03-Dec-22	07-Dec-22
P05-E	Delivering Spare Parts	5	0%	$15.27	08-Dec-22	12-Dec-22
WHCP/HPU - W008N		274	0%	$5,741.31	01-Feb-22	17-Jan-23
P05-E	Tendering & Selection	15	0%	$229.65	01-Feb-22	17-Jun-22
P05-E	Contract Effectiveness / PO	5	0%	$344.48	18-Jun-22	22-Jun-22
P05-E	Manufacturing / Fabrication / Supply	180	0%	$2,870.65	23-Jun-22	19-Dec-22

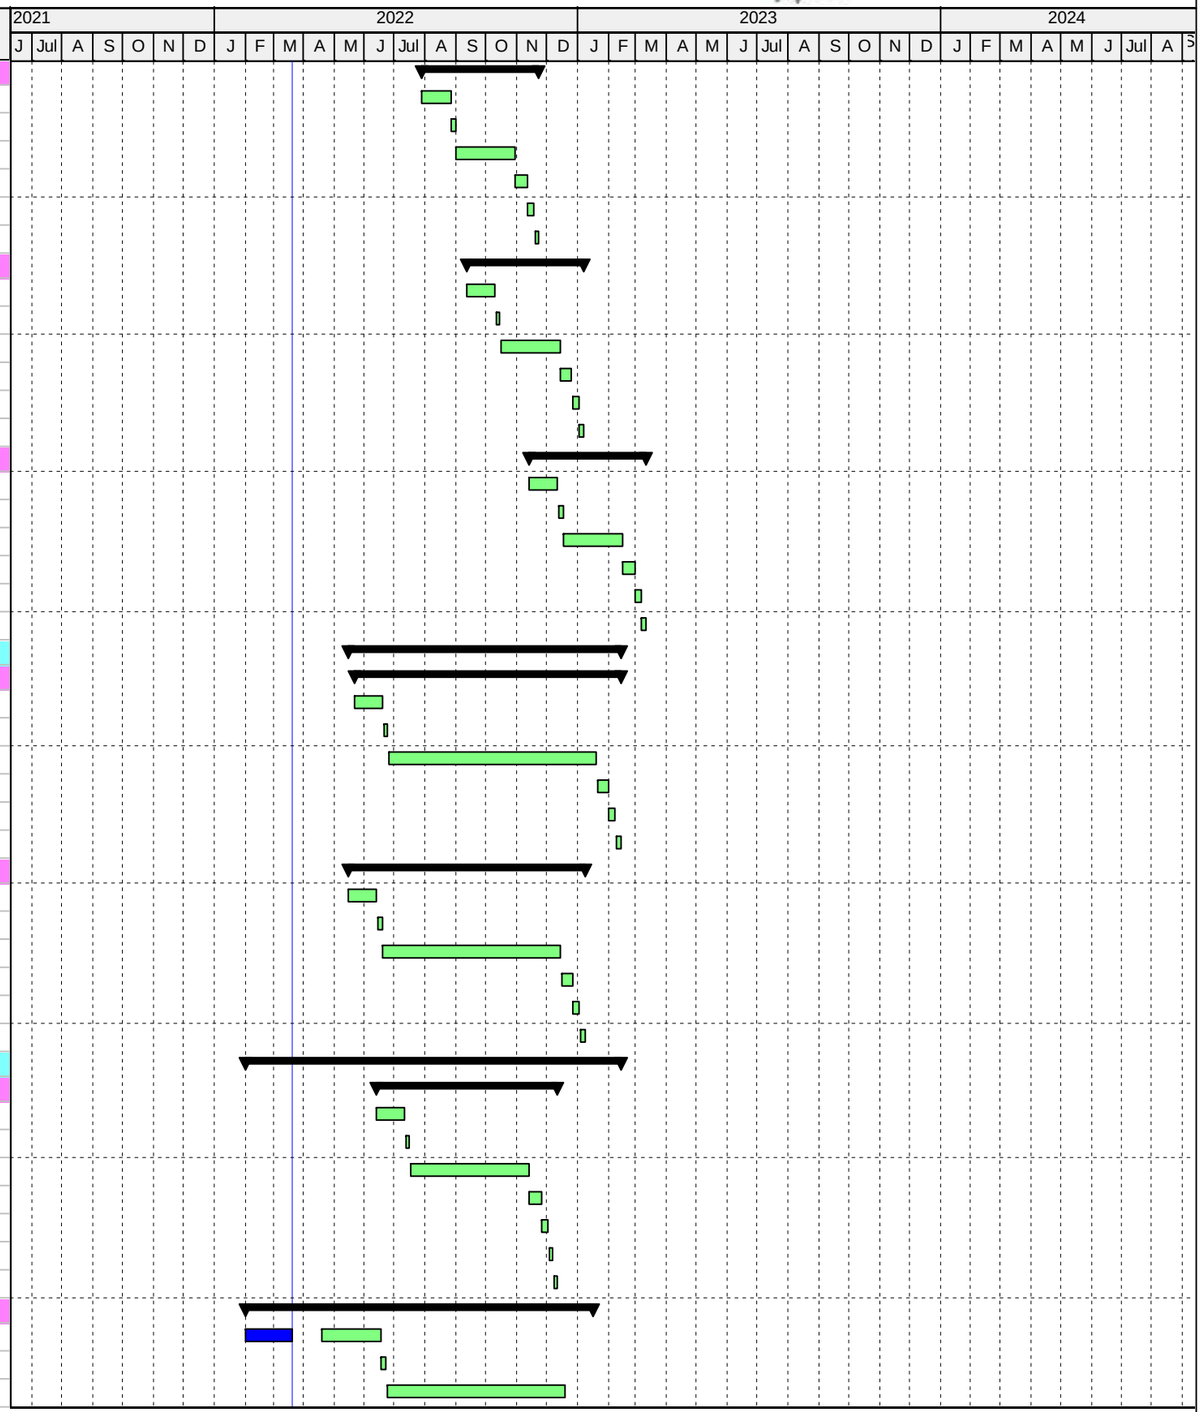


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05-E	Final Inspection	12	0%	$574.13	20-Dec-22	31-Dec-22
P05-E	Delivery On Site	7	0%	$1,148.26	01-Jan-23	07-Jan-23
P05-E	Submitting Vendor Data Book	5	0%	$287.07	08-Jan-23	12-Jan-23
P05-E	Delivering Spare Parts	5	0%	$287.07	13-Jan-23	17-Jan-23
Instrument Tube and Fitting - W008N		149	0%	$48.86	18-Sep-22	13-Feb-23
P05-E	Tendering & Selection	30	0%	$1.95	18-Sep-22	17-Oct-22
P05-E	Contract Effectiveness / PO	5	0%	$2.93	18-Oct-22	22-Oct-22
P05-E	Manufacturing / Fabrication / Supply	90	0%	$24.43	23-Oct-22	20-Jan-23
P05-E	Final Inspection	12	0%	$4.89	21-Jan-23	01-Feb-23
P05-E	Delivery On Site	7	0%	$12.22	02-Feb-23	08-Feb-23
P05-E	Submitting Vendor Data Book	5	0%	$2.44	09-Feb-23	13-Feb-23
Instrument Cable Tray - W008N		149	0%	$12.22	18-Sep-22	13-Feb-23
P05-E	Tendering & Selection	30	0%	$0.49	18-Sep-22	17-Oct-22
P05-E	Contract Effectiveness / PO	5	0%	$0.73	18-Oct-22	22-Oct-22
P05-E	Manufacturing / Fabrication / Supply	90	0%	$6.11	23-Oct-22	20-Jan-23
P05-E	Final Inspection	12	0%	$1.22	21-Jan-23	01-Feb-23
P05-E	Delivery On Site	7	0%	$3.05	02-Feb-23	08-Feb-23
P05-E	Submitting Vendor Data Book	5	0%	$0.61	09-Feb-23	13-Feb-23
Safety & Fire Fighting		121	0%	$431.98	12-Oct-22	09-Feb-23
Fire Safety Sign - W008N		79	0%	$86.40	23-Nov-22	09-Feb-23
P05-E	Tendering & Selection	30	0%	$3.46	23-Nov-22	22-Dec-22
P05-E	Contract Effectiveness / PO	5	0%	$5.18	23-Dec-22	27-Dec-22
P05-E	Manufacturing / Fabrication / Supply	20	0%	$43.20	28-Dec-22	16-Jan-23
P05-E	Final Inspection	12	0%	$8.64	17-Jan-23	28-Jan-23
P05-E	Delivery On Site	7	0%	$21.60	29-Jan-23	04-Feb-23
P05-E	Submitting Vendor Data Book	5	0%	$4.32	05-Feb-23	09-Feb-23
Fire Fighting and Safety Equipment - W008N		79	0%	$345.59	12-Oct-22	29-Dec-22
P05-E	Tendering & Selection	30	0%	$13.82	12-Oct-22	10-Nov-22
P05-E	Contract Effectiveness / PO	5	0%	$20.74	11-Nov-22	15-Nov-22
P05-E	Manufacturing / Fabrication / Supply	20	0%	$172.79	16-Nov-22	05-Dec-22
P05-E	Final Inspection	12	0%	$34.56	06-Dec-22	17-Dec-22
P05-E	Delivery On Site	7	0%	$86.40	18-Dec-22	24-Dec-22
P05-E	Submitting Vendor Data Book	5	0%	$17.28	25-Dec-22	29-Dec-22
Extension of Binak B/C Manifold		318	0%	$40,065.23	13-May-22	26-Mar-23
Mechanical		154	0%	$1,378.24	13-May-22	13-Oct-22
Pumps - Extension of Binak B/C Manifold		154	0%	$1,378.24	13-May-22	13-Oct-22
P05-E	Tendering & Selection	15	0%	$55.13	13-May-22	27-May-22
P05-E	Contract Effectiveness / PO	5	0%	$82.69	28-May-22	01-Jun-22
P05-E	Manufacturing / Fabrication / Supply	110	0%	$689.12	02-Jun-22	19-Sep-22
P05-E	Final Inspection	7	0%	$137.82	20-Sep-22	26-Sep-22
P05-E	Delivery On Site	7	0%	$275.65	27-Sep-22	03-Oct-22
P05-E	Submitting Vendor Data Book	5	0%	$68.91	04-Oct-22	08-Oct-22
P05-E	Delivering Spare Parts	5	0%	$68.91	09-Oct-22	13-Oct-22
Piping		301	0%	$8,742.23	16-May-22	12-Mar-23
Pipes - Extension of Binak B/C Manifold		114	0%	$3,566.83	05-Oct-22	26-Jan-23
P05-E	Tendering & Selection	10	0%	$142.67	05-Oct-22	14-Oct-22
P05-E	Contract Effectiveness / PO	5	0%	$214.01	15-Oct-22	19-Oct-22
P05-E	Manufacturing / Fabrication / Supply	80	0%	$1,783.42	20-Oct-22	07-Jan-23
P05-E	Final Inspection	7	0%	$356.68	08-Jan-23	14-Jan-23

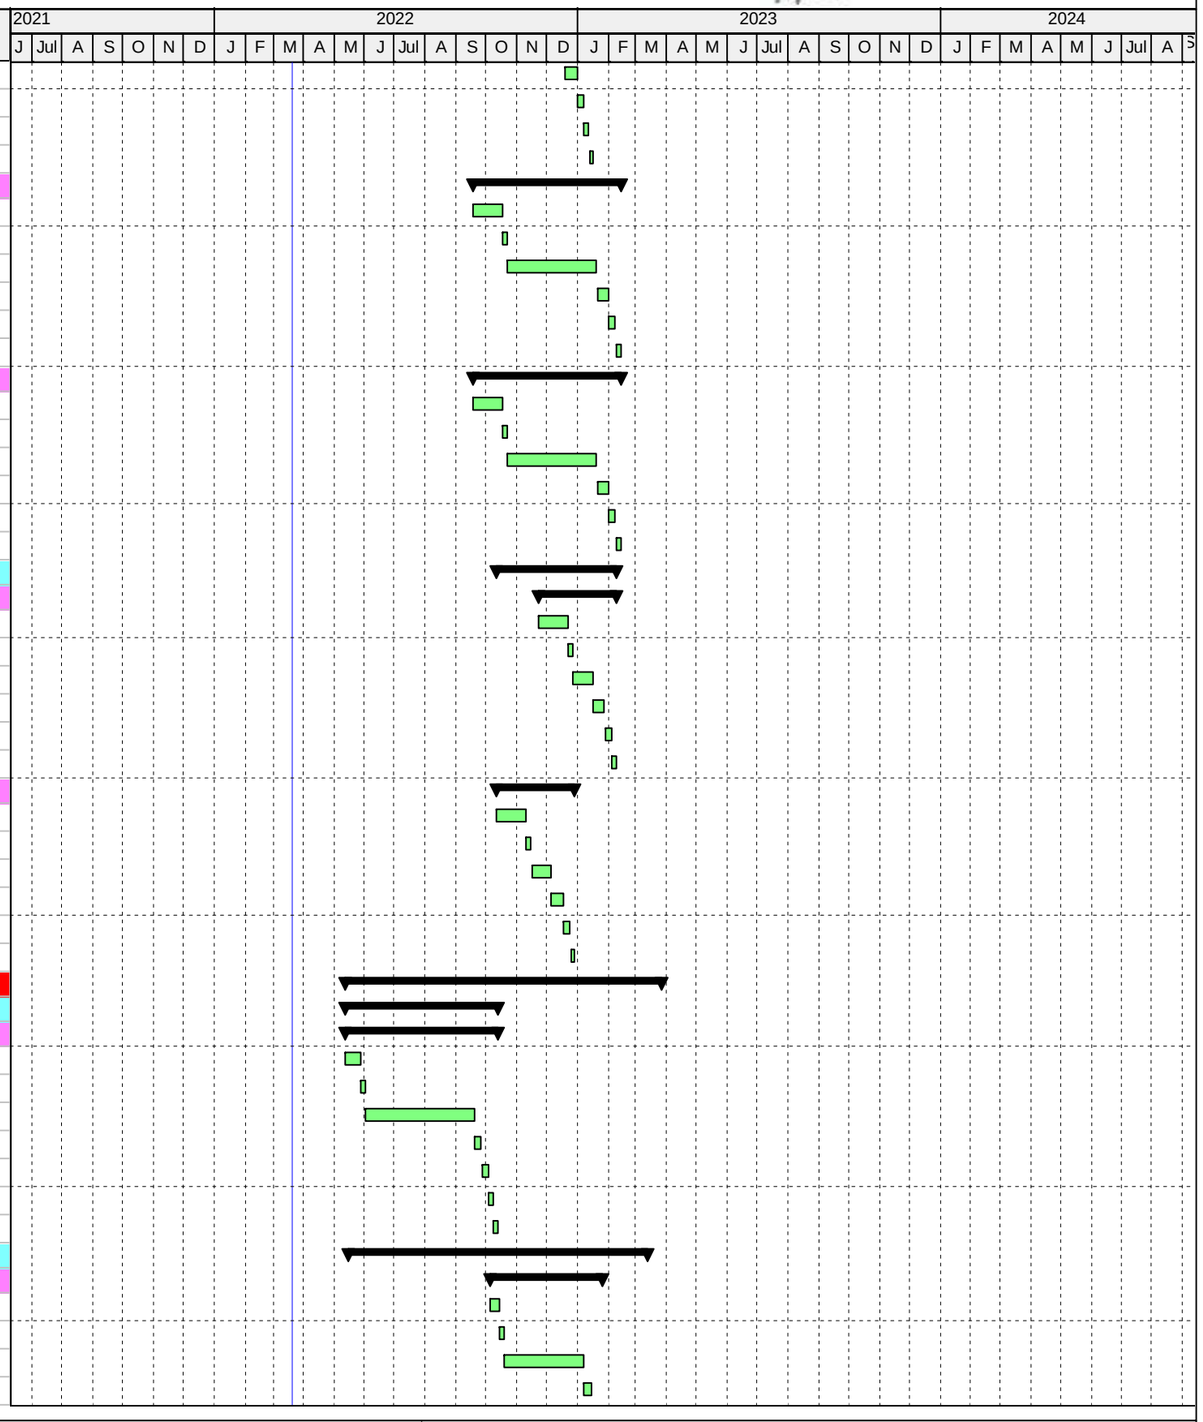


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05-E	Delivery On Site	7	0%	$891.71	15-Jan-23	21-Jan-23
P05-E	Submitting Vendor Data Book	5	0%	$178.34	22-Jan-23	26-Jan-23
Fittings - Extension of Binak B/C Manifold		124	0%	$472.08	04-Nov-22	07-Mar-23
P05-E	Tendering & Selection	10	0%	$18.88	04-Nov-22	13-Nov-22
P05-E	Contract Effectiveness / PO	5	0%	$28.32	14-Nov-22	18-Nov-22
P05-E	Manufacturing / Fabrication / Supply	90	0%	$236.04	19-Nov-22	16-Feb-23
P05-E	Final Inspection	7	0%	$47.21	17-Feb-23	23-Feb-23
P05-E	Delivery On Site	7	0%	$118.02	24-Feb-23	02-Mar-23
P05-E	Submitting Vendor Data Book	5	0%	$23.60	03-Mar-23	07-Mar-23
Flanges - Extension of Binak B/C Manifold		124	0%	$472.08	04-Nov-22	07-Mar-23
P05-E	Tendering & Selection	10	0%	$18.88	04-Nov-22	13-Nov-22
P05-E	Contract Effectiveness / PO	5	0%	$28.32	14-Nov-22	18-Nov-22
P05-E	Manufacturing / Fabrication / Supply	90	0%	$236.04	19-Nov-22	16-Feb-23
P05-E	Final Inspection	7	0%	$47.21	17-Feb-23	23-Feb-23
P05-E	Delivery On Site	7	0%	$118.02	24-Feb-23	02-Mar-23
P05-E	Submitting Vendor Data Book	5	0%	$23.60	03-Mar-23	07-Mar-23
Manual Valves - Extension of Binak B/C Manifold		129	0%	$2,098.14	04-Nov-22	12-Mar-23
P05-E	Tendering & Selection	10	0%	$83.93	04-Nov-22	13-Nov-22
P05-E	Contract Effectiveness / PO	5	0%	$125.89	14-Nov-22	18-Nov-22
P05-E	Manufacturing / Fabrication / Supply	90	0%	$1,049.07	19-Nov-22	16-Feb-23
P05-E	Final Inspection	7	0%	$209.81	17-Feb-23	23-Feb-23
P05-E	Delivery On Site	7	0%	$419.63	24-Feb-23	02-Mar-23
P05-E	Submitting Vendor Data Book	5	0%	$104.91	03-Mar-23	07-Mar-23
P05-E	Delivering Spare Parts	5	0%	$104.91	08-Mar-23	12-Mar-23
Gaskets - Extension of Binak B/C Manifold		124	0%	$568.25	04-Nov-22	07-Mar-23
P05-E	Tendering & Selection	10	0%	$22.73	04-Nov-22	13-Nov-22
P05-E	Contract Effectiveness / PO	5	0%	$34.09	14-Nov-22	18-Nov-22
P05-E	Manufacturing / Fabrication / Supply	90	0%	$284.12	19-Nov-22	16-Feb-23
P05-E	Final Inspection	7	0%	$56.82	17-Feb-23	23-Feb-23
P05-E	Delivery On Site	7	0%	$142.06	24-Feb-23	02-Mar-23
P05-E	Submitting Vendor Data Book	5	0%	$28.41	03-Mar-23	07-Mar-23
Bolt/Nuts - Extension of Binak B/C Manifold		114	0%	$874.22	04-Nov-22	25-Feb-23
P05-E	Tendering & Selection	10	0%	$34.97	04-Nov-22	13-Nov-22
P05-E	Contract Effectiveness / PO	5	0%	$52.45	14-Nov-22	18-Nov-22
P05-E	Manufacturing / Fabrication / Supply	80	0%	$437.11	19-Nov-22	06-Feb-23
P05-E	Final Inspection	7	0%	$87.42	07-Feb-23	13-Feb-23
P05-E	Delivery On Site	7	0%	$218.56	14-Feb-23	20-Feb-23
P05-E	Submitting Vendor Data Book	5	0%	$43.71	21-Feb-23	25-Feb-23
Sampling Connection Set - Extension of Binak B/C Manifold		94	0%	$472.08	16-May-22	17-Aug-22
P05-E	Tendering & Selection	10	0%	$18.88	16-May-22	25-May-22
P05-E	Contract Effectiveness / PO	5	0%	$28.32	26-May-22	30-May-22
P05-E	Manufacturing / Fabrication / Supply	60	0%	$236.04	31-May-22	29-Jul-22
P05-E	Final Inspection	7	0%	$47.21	30-Jul-22	05-Aug-22
P05-E	Delivery On Site	7	0%	$118.02	06-Aug-22	12-Aug-22
P05-E	Submitting Vendor Data Book	5	0%	$23.60	13-Aug-22	17-Aug-22
Pipe Support - Extension of Binak B/C Manifold		94	0%	$218.56	07-Oct-22	08-Jan-23
P05-E	Tendering & Selection	10	0%	$8.74	07-Oct-22	16-Oct-22
P05-E	Contract Effectiveness / PO	5	0%	$13.11	17-Oct-22	21-Oct-22
P05-E	Manufacturing / Fabrication / Supply	60	0%	$109.28	22-Oct-22	20-Dec-22

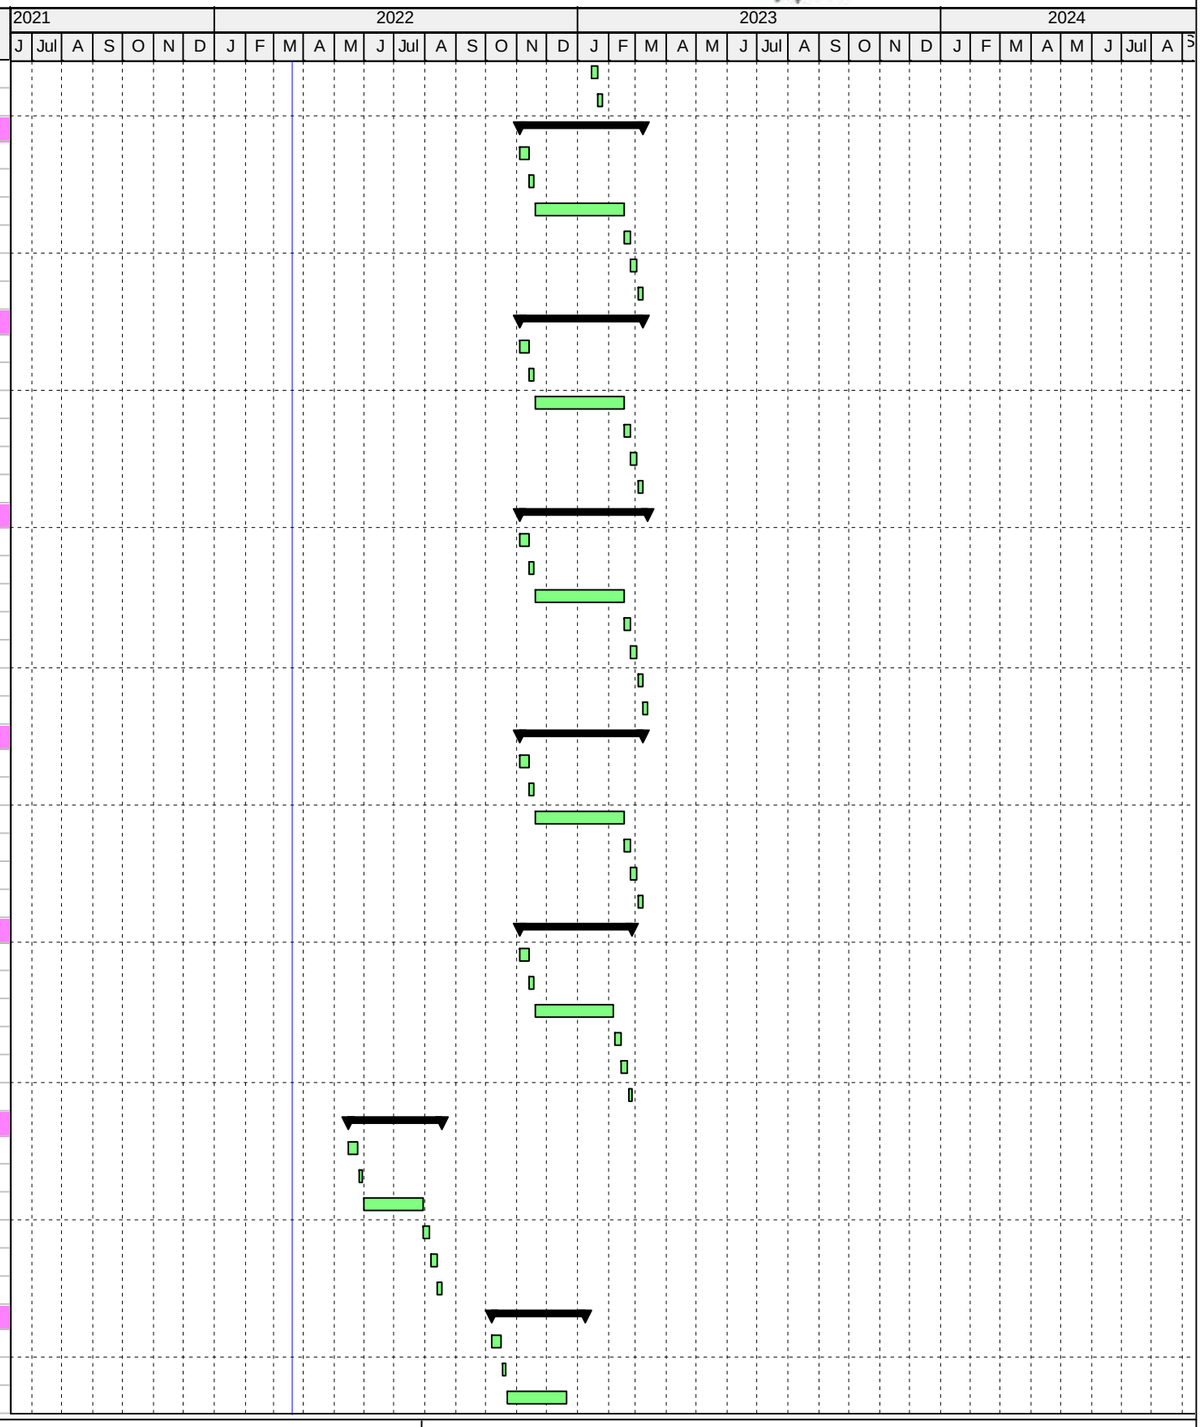

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05-E	Final Inspection	7	0%	$21.86	21-Dec-22	27-Dec-22
P05-E	Delivery On Site	7	0%	$54.64	28-Dec-22	03-Jan-23
P05-E	Submitting Vendor Data Book	5	0%	$10.93	04-Jan-23	08-Jan-23
Control & Instrumentation		317	0%	$22,075.94	14-May-22	26-Mar-23
DCS System - Extension of Binak B/C Manifold		169	0%	$9,051.14	21-May-22	05-Nov-22
P05-E	Tendering & Selection	20	0%	$362.05	21-May-22	09-Jun-22
P05-E	Contract Effectiveness / PO	5	0%	$543.07	10-Jun-22	14-Jun-22
P05-E	Manufacturing / Fabrication / Supply	120	0%	$4,525.57	15-Jun-22	12-Oct-22
P05-E	Final Inspection	7	0%	$905.11	13-Oct-22	19-Oct-22
P05-E	Delivery On Site	7	0%	$1,810.23	20-Oct-22	26-Oct-22
P05-E	Submitting Vendor Data Book	5	0%	$452.56	27-Oct-22	31-Oct-22
P05-E	Delivering Spare Parts	5	0%	$452.56	01-Nov-22	05-Nov-22
ESD System - Extension of Binak B/C Manifold		169	0%	$6,402.02	05-Jun-22	20-Nov-22
P05-E	Tendering & Selection	20	0%	$256.08	05-Jun-22	24-Jun-22
P05-E	Contract Effectiveness / PO	5	0%	$384.12	25-Jun-22	29-Jun-22
P05-E	Manufacturing / Fabrication / Supply	120	0%	$3,201.01	30-Jun-22	27-Oct-22
P05-E	Final Inspection	7	0%	$640.20	28-Oct-22	03-Nov-22
P05-E	Delivery On Site	7	0%	$1,280.40	04-Nov-22	10-Nov-22
P05-E	Submitting Vendor Data Book	5	0%	$320.10	11-Nov-22	15-Nov-22
P05-E	Delivering Spare Parts	5	0%	$320.10	16-Nov-22	20-Nov-22
F&G System - Extension of Binak B/C Manifold		169	0%	$4,415.19	05-Jun-22	20-Nov-22
P05-E	Tendering & Selection	20	0%	$176.61	05-Jun-22	24-Jun-22
P05-E	Contract Effectiveness / PO	5	0%	$264.91	25-Jun-22	29-Jun-22
P05-E	Manufacturing / Fabrication / Supply	120	0%	$2,207.59	30-Jun-22	27-Oct-22
P05-E	Final Inspection	7	0%	$441.52	28-Oct-22	03-Nov-22
P05-E	Delivery On Site	7	0%	$883.04	04-Nov-22	10-Nov-22
P05-E	Submitting Vendor Data Book	5	0%	$220.76	11-Nov-22	15-Nov-22
P05-E	Delivering Spare Parts	5	0%	$220.76	16-Nov-22	20-Nov-22
ON/OFF & Shutdown Valves - Extension of Binak B/C Manifold		154	0%	$242.84	02-Jun-22	02-Nov-22
P05-E	Tendering & Selection	20	0%	$9.71	02-Jun-22	21-Jun-22
P05-E	Contract Effectiveness / PO	5	0%	$14.57	22-Jun-22	26-Jun-22
P05-E	Manufacturing / Fabrication / Supply	100	0%	$121.42	27-Jun-22	04-Oct-22
P05-E	Final Inspection	12	0%	$24.28	05-Oct-22	16-Oct-22
P05-E	Delivery On Site	7	0%	$48.57	17-Oct-22	23-Oct-22
P05-E	Submitting Vendor Data Book	5	0%	$12.14	24-Oct-22	28-Oct-22
P05-E	Delivering Spare Parts	5	0%	$12.14	29-Oct-22	02-Nov-22
Control Valves		144	0%	$242.84	04-Jul-22	24-Nov-22
P05-E	Tendering & Selection	15	0%	$9.71	04-Jul-22	18-Jul-22
P05-E	Contract Effectiveness / PO	5	0%	$14.57	19-Jul-22	23-Jul-22
P05-E	Manufacturing / Fabrication / Supply	100	0%	$121.42	24-Jul-22	31-Oct-22
P05-E	Final Inspection	7	0%	$24.28	01-Nov-22	07-Nov-22
P05-E	Delivery On Site	7	0%	$48.57	08-Nov-22	14-Nov-22
P05-E	Submitting Vendor Data Book	5	0%	$12.14	15-Nov-22	19-Nov-22
P05-E	Delivering Spare Parts	5	0%	$12.14	20-Nov-22	24-Nov-22
Pressure Safety Valves (PSV)		144	0%	$242.84	15-Jul-22	05-Dec-22
P05-E	Tendering & Selection	15	0%	$9.71	15-Jul-22	29-Jul-22
P05-E	Contract Effectiveness / PO	5	0%	$14.57	30-Jul-22	03-Aug-22
P05-E	Manufacturing / Fabrication / Supply	100	0%	$121.42	04-Aug-22	11-Nov-22
P05-E	Final Inspection	7	0%	$24.28	12-Nov-22	18-Nov-22

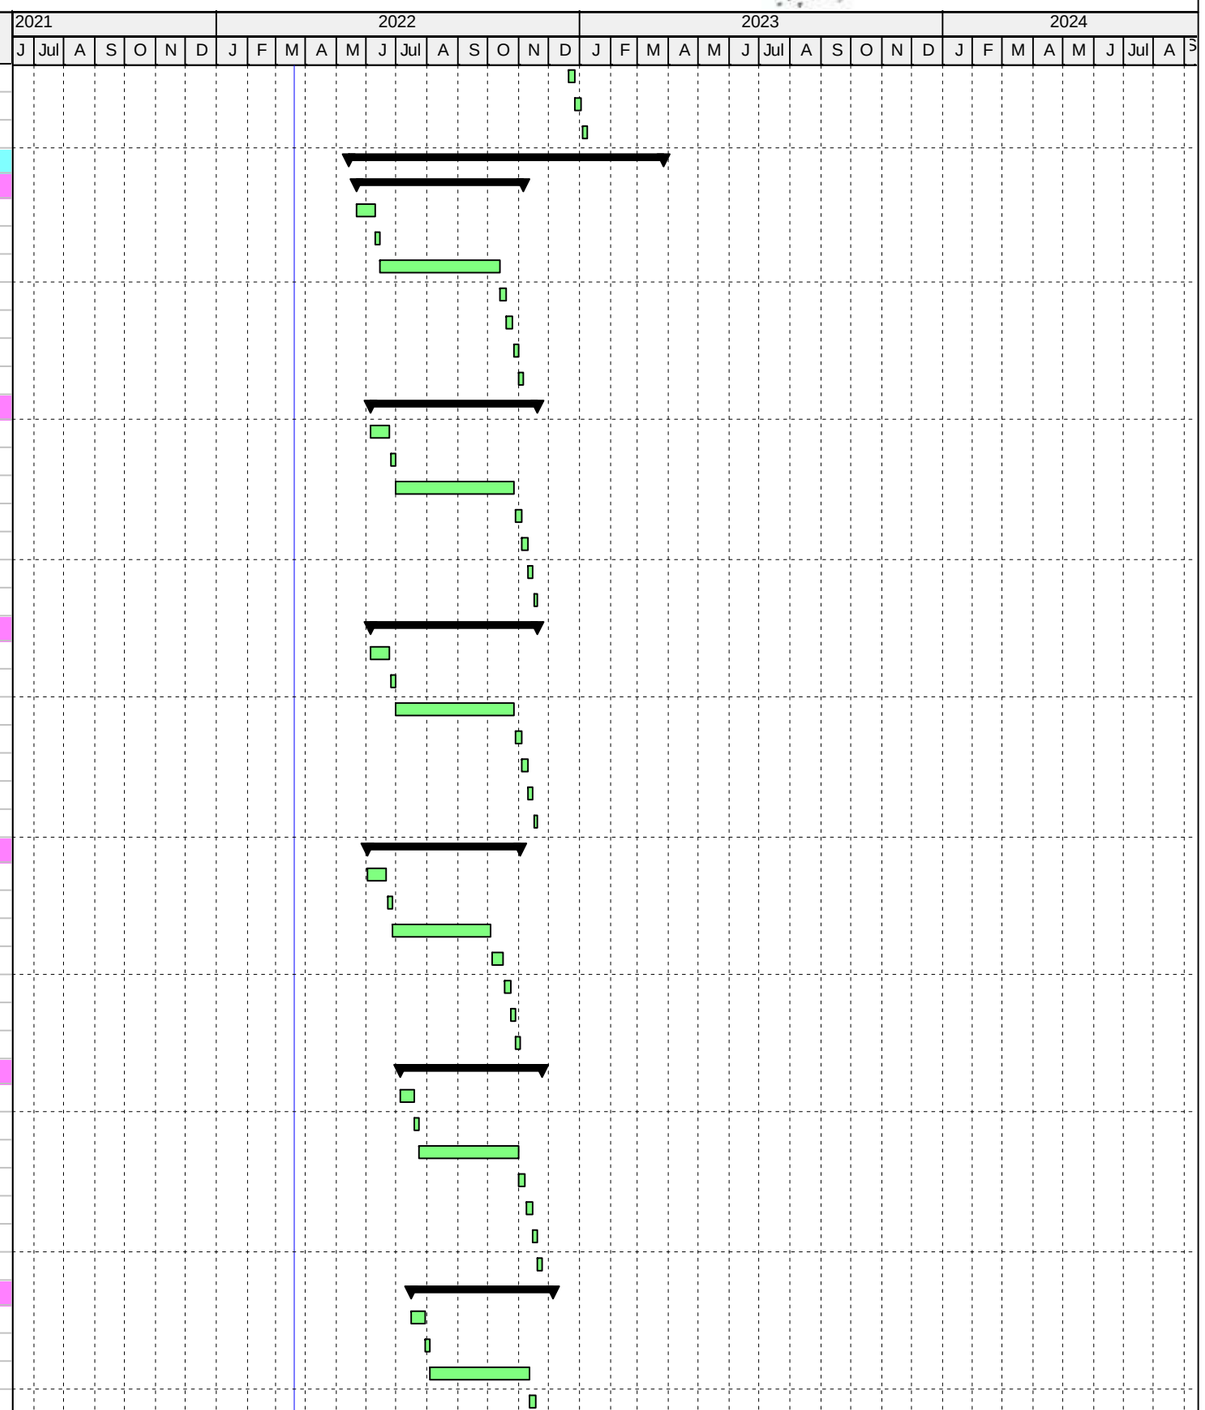


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05-E	Delivery On Site	7	0%	$48.57	19-Nov-22	25-Nov-22
P05-E	Submitting Vendor Data Book	5	0%	$12.14	26-Nov-22	30-Nov-22
P05-E	Delivering Spare Parts	5	0%	$12.14	01-Dec-22	05-Dec-22
F&G Devices		154	0%	$209.72	04-Aug-22	04-Jan-23
P05-E	Tendering & Selection	15	0%	$8.39	04-Aug-22	18-Aug-22
P05-E	Contract Effectiveness / PO	5	0%	$12.58	19-Aug-22	23-Aug-22
P05-E	Manufacturing / Fabrication / Supply	110	0%	$104.86	24-Aug-22	11-Dec-22
P05-E	Final Inspection	7	0%	$20.97	12-Dec-22	18-Dec-22
P05-E	Delivery On Site	7	0%	$41.94	19-Dec-22	25-Dec-22
P05-E	Submitting Vendor Data Book	5	0%	$10.49	26-Dec-22	30-Dec-22
P05-E	Delivering Spare Parts	5	0%	$10.49	31-Dec-22	04-Jan-23
Orifice and Restriction Orifice Plate		159	0%	$90.51	25-May-22	30-Oct-22
P05-E	Tendering & Selection	15	0%	$3.62	25-May-22	08-Jun-22
P05-E	Contract Effectiveness / PO	5	0%	$5.43	09-Jun-22	13-Jun-22
P05-E	Manufacturing / Fabrication / Supply	110	0%	$45.26	14-Jun-22	01-Oct-22
P05-E	Final Inspection	12	0%	$9.05	02-Oct-22	13-Oct-22
P05-E	Delivery On Site	7	0%	$18.10	14-Oct-22	20-Oct-22
P05-E	Submitting Vendor Data Book	5	0%	$4.53	21-Oct-22	25-Oct-22
P05-E	Delivering Spare Parts	5	0%	$4.53	26-Oct-22	30-Oct-22
Corrosion Coupon/Probe		159	0%	$90.51	21-May-22	26-Oct-22
P05-E	Tendering & Selection	15	0%	$3.62	21-May-22	04-Jun-22
P05-E	Contract Effectiveness / PO	5	0%	$5.43	05-Jun-22	09-Jun-22
P05-E	Manufacturing / Fabrication / Supply	110	0%	$45.26	10-Jun-22	27-Sep-22
P05-E	Final Inspection	12	0%	$9.05	28-Sep-22	09-Oct-22
P05-E	Delivery On Site	7	0%	$18.10	10-Oct-22	16-Oct-22
P05-E	Submitting Vendor Data Book	5	0%	$4.53	17-Oct-22	21-Oct-22
P05-E	Delivering Spare Parts	5	0%	$4.53	22-Oct-22	26-Oct-22
Pressure Transmitter		149	0%	$121.42	03-Jul-22	28-Nov-22
P05-E	Tendering & Selection	15	0%	$4.86	03-Jul-22	17-Jul-22
P05-E	Contract Effectiveness / PO	5	0%	$7.29	18-Jul-22	22-Jul-22
P05-E	Manufacturing / Fabrication / Supply	100	0%	$60.71	23-Jul-22	30-Oct-22
P05-E	Final Inspection	12	0%	$12.14	31-Oct-22	11-Nov-22
P05-E	Delivery On Site	7	0%	$24.28	12-Nov-22	18-Nov-22
P05-E	Submitting Vendor Data Book	5	0%	$6.07	19-Nov-22	23-Nov-22
P05-E	Delivering Spare Parts	5	0%	$6.07	24-Nov-22	28-Nov-22
Flow Transmitter/ Diff. Pressure Transmitter		159	0%	$121.42	14-May-22	19-Oct-22
P05-E	Tendering & Selection	15	0%	$4.86	14-May-22	28-May-22
P05-E	Contract Effectiveness / PO	5	0%	$7.29	29-May-22	02-Jun-22
P05-E	Manufacturing / Fabrication / Supply	110	0%	$60.71	03-Jun-22	20-Sep-22
P05-E	Final Inspection	12	0%	$12.14	21-Sep-22	02-Oct-22
P05-E	Delivery On Site	7	0%	$24.28	03-Oct-22	09-Oct-22
P05-E	Submitting Vendor Data Book	5	0%	$6.07	10-Oct-22	14-Oct-22
P05-E	Delivering Spare Parts	5	0%	$6.07	15-Oct-22	19-Oct-22
Instrument/F&G Cable		129	0%	$150.12	08-Nov-22	16-Mar-23
P05-E	Tendering & Selection	15	0%	$6.00	08-Nov-22	22-Nov-22
P05-E	Contract Effectiveness / PO	5	0%	$9.01	23-Nov-22	27-Nov-22
P05-E	Manufacturing / Fabrication / Supply	90	0%	$75.06	28-Nov-22	25-Feb-23
P05-E	Final Inspection	7	0%	$15.01	26-Feb-23	04-Mar-23
P05-E	Delivery On Site	7	0%	$37.53	05-Mar-23	11-Mar-23

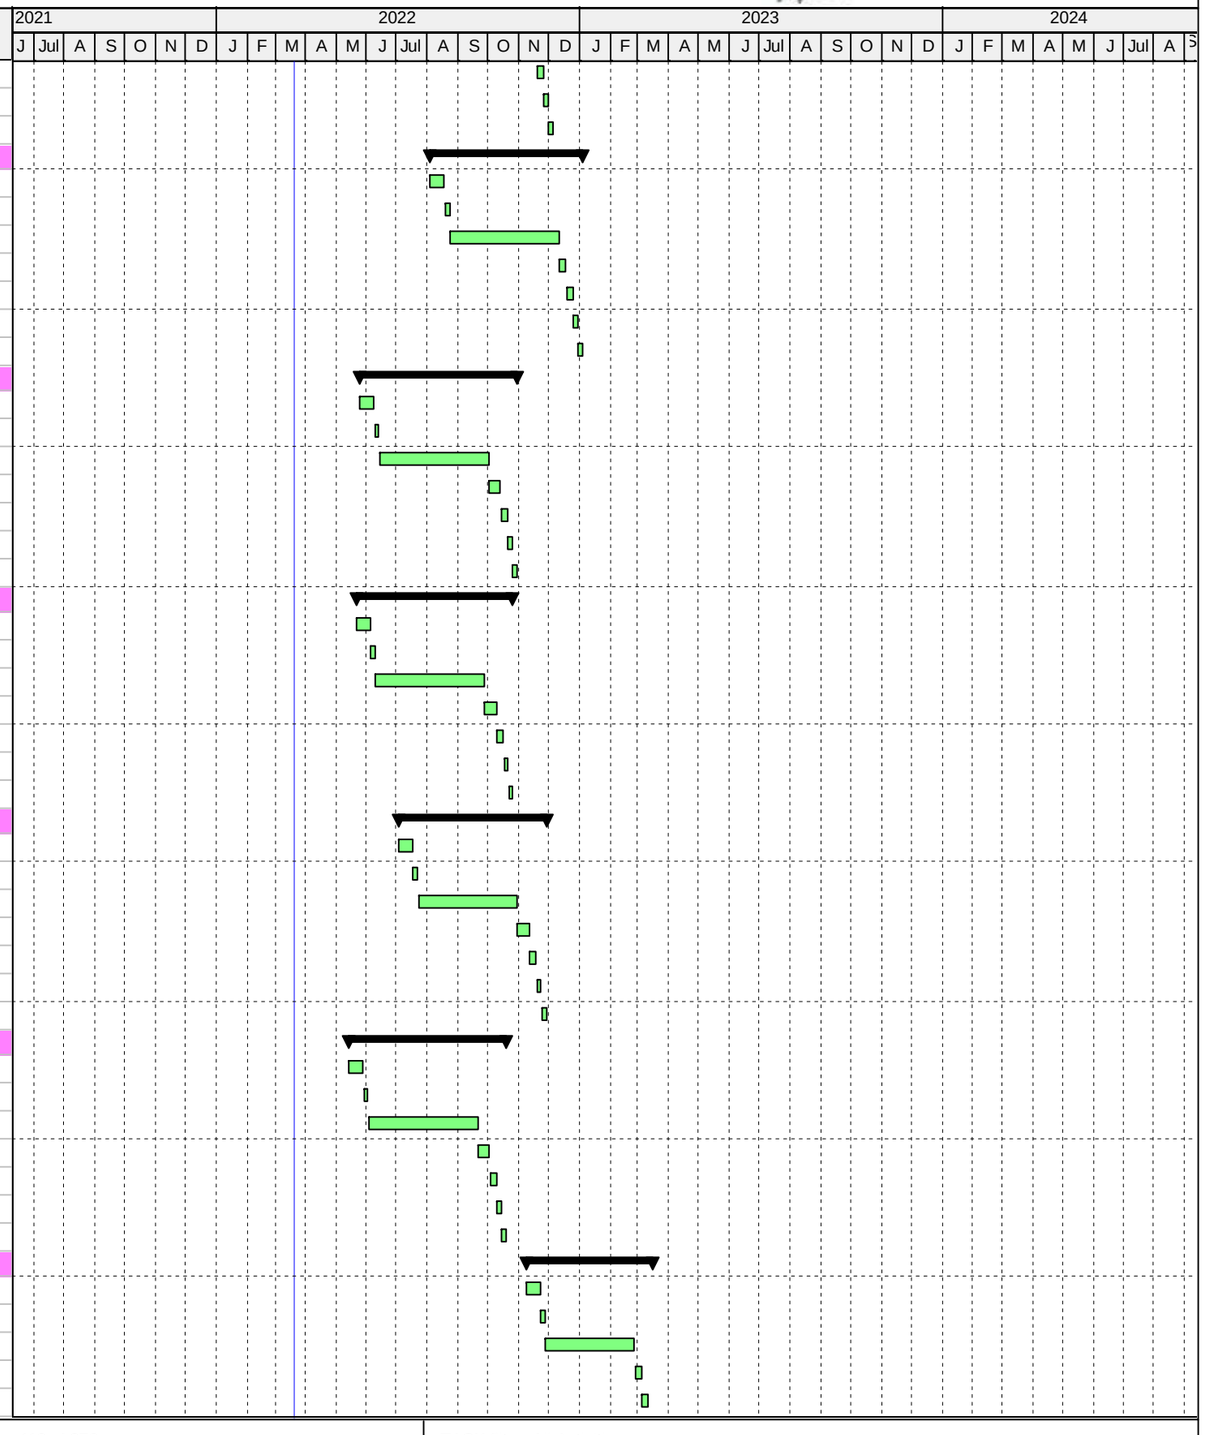


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05-E	Submitting Vendor Data Book	5	0%	$7.51	12-Mar-23	16-Mar-23
Instrument/F&G Junction box and Gland		144	0%	$121.42	03-Nov-22	26-Mar-23
P05-E	Tendering & Selection	15	0%	$4.86	03-Nov-22	17-Nov-22
P05-E	Contract Effectiveness / PO	5	0%	$7.29	18-Nov-22	22-Nov-22
P05-E	Manufacturing / Fabrication / Supply	100	0%	$60.71	23-Nov-22	02-Mar-23
P05-E	Final Inspection	12	0%	$12.14	03-Mar-23	14-Mar-23
P05-E	Delivery On Site	7	0%	$30.35	15-Mar-23	21-Mar-23
P05-E	Submitting Vendor Data Book	5	0%	$6.07	22-Mar-23	26-Mar-23
Instrument Installation Accessories		139	0%	$90.51	30-Sep-22	15-Feb-23
P05-E	Tendering & Selection	15	0%	$3.62	30-Sep-22	14-Oct-22
P05-E	Contract Effectiveness / PO	5	0%	$5.43	15-Oct-22	19-Oct-22
P05-E	Manufacturing / Fabrication / Supply	100	0%	$45.26	20-Oct-22	27-Jan-23
P05-E	Final Inspection	7	0%	$9.05	28-Jan-23	03-Feb-23
P05-E	Delivery On Site	7	0%	$22.63	04-Feb-23	10-Feb-23
P05-E	Submitting Vendor Data Book	5	0%	$4.53	11-Feb-23	15-Feb-23
Differential Pressure/Pressure Gauge		149	0%	$121.42	14-May-22	09-Oct-22
P05-E	Tendering & Selection	15	0%	$4.86	14-May-22	28-May-22
P05-E	Contract Effectiveness / PO	5	0%	$7.29	29-May-22	02-Jun-22
P05-E	Manufacturing / Fabrication / Supply	100	0%	$60.71	03-Jun-22	10-Sep-22
P05-E	Final Inspection	12	0%	$12.14	11-Sep-22	22-Sep-22
P05-E	Delivery On Site	7	0%	$24.28	23-Sep-22	29-Sep-22
P05-E	Submitting Vendor Data Book	5	0%	$6.07	30-Sep-22	04-Oct-22
P05-E	Delivering Spare Parts	5	0%	$6.07	05-Oct-22	09-Oct-22
Temperature Gauge		149	0%	$121.42	07-Jun-22	02-Nov-22
P05-E	Tendering & Selection	15	0%	$4.86	07-Jun-22	21-Jun-22
P05-E	Contract Effectiveness / PO	5	0%	$7.29	22-Jun-22	26-Jun-22
P05-E	Manufacturing / Fabrication / Supply	100	0%	$60.71	27-Jun-22	04-Oct-22
P05-E	Final Inspection	12	0%	$12.14	05-Oct-22	16-Oct-22
P05-E	Delivery On Site	7	0%	$24.28	17-Oct-22	23-Oct-22
P05-E	Submitting Vendor Data Book	5	0%	$6.07	24-Oct-22	28-Oct-22
P05-E	Delivering Spare Parts	5	0%	$6.07	29-Oct-22	02-Nov-22
Instrument Tube and Fitting		129	0%	$150.12	07-Jul-22	12-Nov-22
P05-E	Tendering & Selection	10	0%	$6.00	07-Jul-22	16-Jul-22
P05-E	Contract Effectiveness / PO	5	0%	$9.01	17-Jul-22	21-Jul-22
P05-E	Manufacturing / Fabrication / Supply	90	0%	$75.06	22-Jul-22	19-Oct-22
P05-E	Final Inspection	12	0%	$15.01	20-Oct-22	31-Oct-22
P05-E	Delivery On Site	7	0%	$37.53	01-Nov-22	07-Nov-22
P05-E	Submitting Vendor Data Book	5	0%	$7.51	08-Nov-22	12-Nov-22
Instrument Cable Tray		134	0%	$90.51	30-Sep-22	10-Feb-23
P05-E	Tendering & Selection	15	0%	$3.62	30-Sep-22	14-Oct-22
P05-E	Contract Effectiveness / PO	5	0%	$5.43	15-Oct-22	19-Oct-22
P05-E	Manufacturing / Fabrication / Supply	90	0%	$45.26	20-Oct-22	17-Jan-23
P05-E	Final Inspection	12	0%	$9.05	18-Jan-23	29-Jan-23
P05-E	Delivery On Site	7	0%	$22.63	30-Jan-23	05-Feb-23
P05-E	Submitting Vendor Data Book	5	0%	$4.53	06-Feb-23	10-Feb-23
Safety & Fire Fighting		121	0%	$436.71	03-Sep-22	01-Jan-23
Fire Fighting and Safety Equipment - Extension of Binak B/C Ma		79	0%	$325.39	03-Sep-22	20-Nov-22
P05-E	Tendering & Selection	30	0%	$13.02	03-Sep-22	02-Oct-22
P05-E	Contract Effectiveness / PO	5	0%	$19.52	03-Oct-22	07-Oct-22

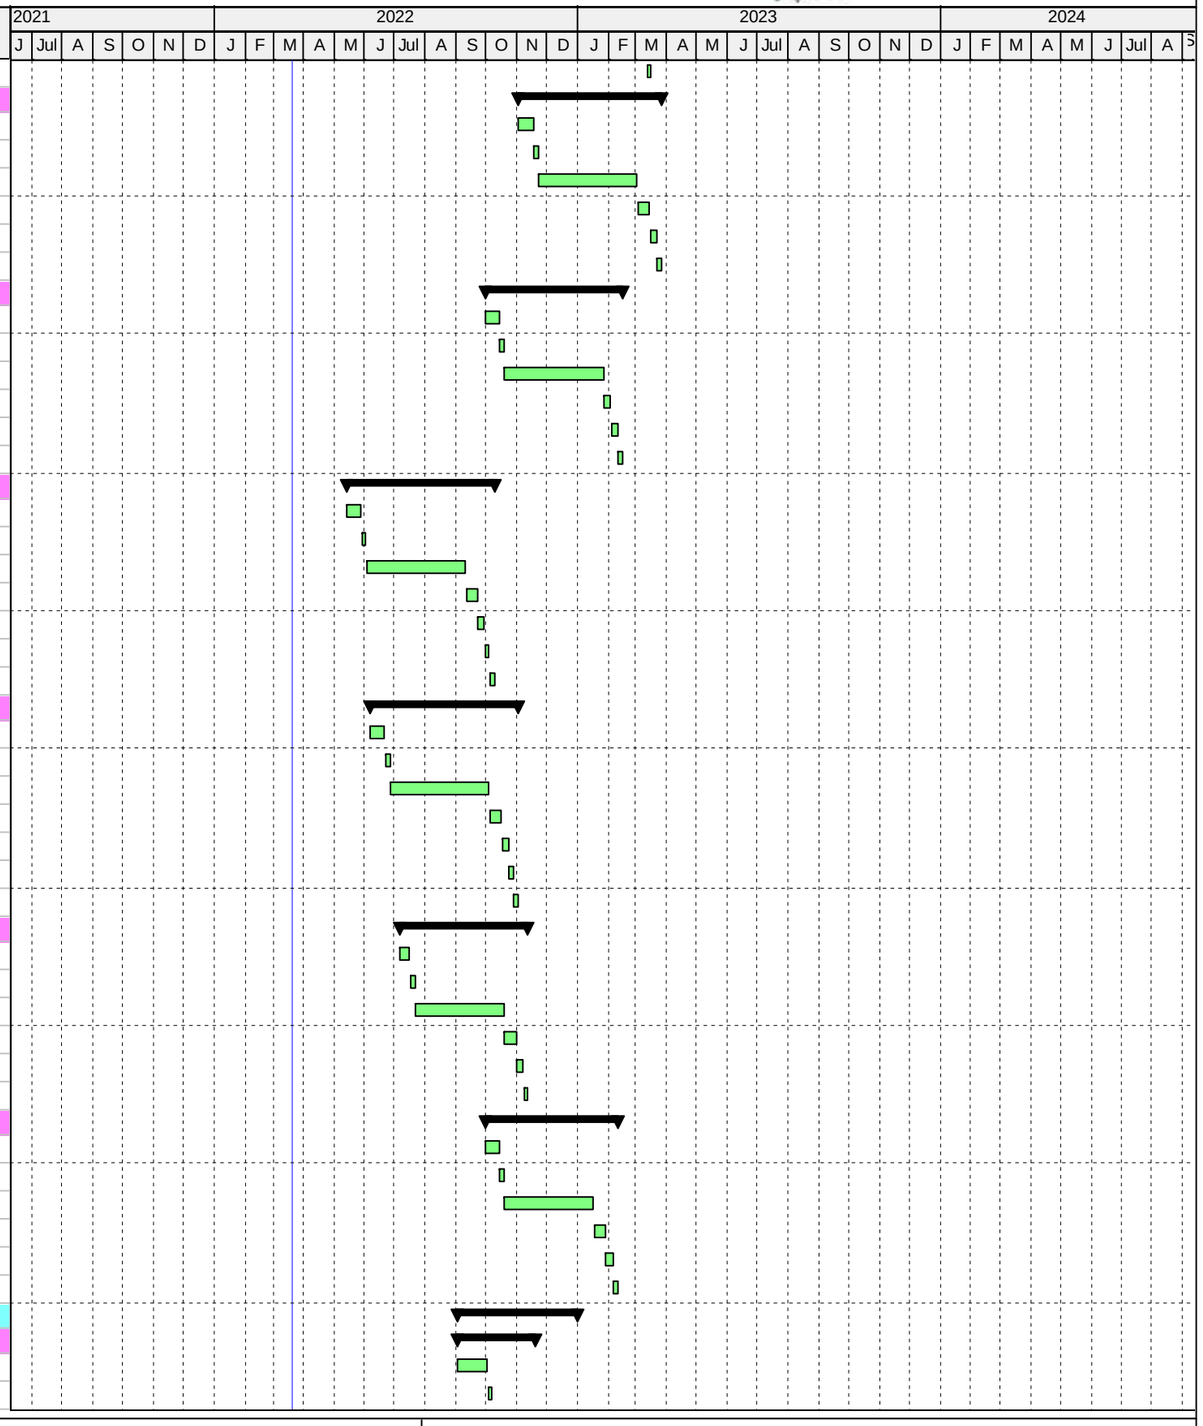


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05-E	Manufacturing / Fabrication / Supply	20	0%	$162.70	08-Oct-22	27-Oct-22
P05-E	Final Inspection	12	0%	$32.54	28-Oct-22	08-Nov-22
P05-E	Delivery On Site	7	0%	$81.35	09-Nov-22	15-Nov-22
P05-E	Submitting Vendor Data Book	5	0%	$16.27	16-Nov-22	20-Nov-22
Fire Safety Sign - Extension of Binak B/C Manifold		79	0%	$111.32	15-Oct-22	01-Jan-23
P05-E	Tendering & Selection	30	0%	$4.45	15-Oct-22	13-Nov-22
P05-E	Contract Effectiveness / PO	5	0%	$6.68	14-Nov-22	18-Nov-22
P05-E	Manufacturing / Fabrication / Supply	20	0%	$55.66	19-Nov-22	08-Dec-22
P05-E	Final Inspection	12	0%	$11.13	09-Dec-22	20-Dec-22
P05-E	Delivery On Site	7	0%	$27.83	21-Dec-22	27-Dec-22
P05-E	Submitting Vendor Data Book	5	0%	$5.57	28-Dec-22	01-Jan-23
Electrical		284	0%	$7,432.10	05-Jun-22	15-Mar-23
UPS System - Extension of Binak B/C Manifold		144	0%	$2,981.02	12-Sep-22	02-Feb-23
P05-E	Tendering & Selection	15	0%	$119.24	12-Sep-22	26-Sep-22
P05-E	Contract Effectiveness / PO	5	0%	$178.86	27-Sep-22	01-Oct-22
P05-E	Manufacturing / Fabrication / Supply	100	0%	$1,490.51	02-Oct-22	09-Jan-23
P05-E	Final Inspection	7	0%	$298.10	10-Jan-23	16-Jan-23
P05-E	Delivery On Site	7	0%	$596.20	17-Jan-23	23-Jan-23
P05-E	Submitting Vendor Data Book	5	0%	$149.05	24-Jan-23	28-Jan-23
P05-E	Delivering Spare Parts	5	0%	$149.05	29-Jan-23	02-Feb-23
LV Switchgear & MCC - Extension of Binak B/C Manifold		154	0%	$1,192.85	05-Jun-22	05-Nov-22
P05-E	Tendering & Selection	15	0%	$47.71	05-Jun-22	19-Jun-22
P05-E	Contract Effectiveness / PO	5	0%	$71.57	20-Jun-22	24-Jun-22
P05-E	Manufacturing / Fabrication / Supply	100	0%	$596.43	25-Jun-22	02-Oct-22
P05-E	Final Inspection	7	0%	$119.29	13-Oct-22	19-Oct-22
P05-E	Delivery On Site	7	0%	$238.57	20-Oct-22	26-Oct-22
P05-E	Submitting Vendor Data Book	5	0%	$59.64	27-Oct-22	31-Oct-22
P05-E	Delivering Spare Parts	5	0%	$59.64	01-Nov-22	05-Nov-22
DC Charger - Extension of Binak B/C Manifold		154	0%	$1,986.60	05-Jun-22	05-Nov-22
P05-E	Tendering & Selection	15	0%	$79.46	05-Jun-22	19-Jun-22
P05-E	Contract Effectiveness / PO	5	0%	$119.20	20-Jun-22	24-Jun-22
P05-E	Manufacturing / Fabrication / Supply	110	0%	$993.30	25-Jun-22	12-Oct-22
P05-E	Final Inspection	7	0%	$198.66	13-Oct-22	19-Oct-22
P05-E	Delivery On Site	7	0%	$397.32	20-Oct-22	26-Oct-22
P05-E	Submitting Vendor Data Book	5	0%	$99.33	27-Oct-22	31-Oct-22
P05-E	Delivering Spare Parts	5	0%	$99.33	01-Nov-22	05-Nov-22
Earthing & Lightning System		149	0%	$198.44	11-Sep-22	06-Feb-23
P05-E	Tendering & Selection	15	0%	$7.94	11-Sep-22	25-Sep-22
P05-E	Contract Effectiveness / PO	5	0%	$11.91	26-Sep-22	30-Sep-22
P05-E	Manufacturing / Fabrication / Supply	110	0%	$99.22	01-Oct-22	18-Jan-23
P05-E	Final Inspection	7	0%	$19.84	19-Jan-23	25-Jan-23
P05-E	Delivery On Site	7	0%	$39.69	26-Jan-23	01-Feb-23
P05-E	Submitting Vendor Data Book	5	0%	$9.92	02-Feb-23	06-Feb-23
P05-E	Delivering Spare Parts	5	0%	$9.92	02-Feb-23	06-Feb-23
Power & Control Cables - Extension of Binak B/C Manifold		99	0%	$397.62	07-Dec-22	15-Mar-23
P05-E	Tendering & Selection	15	0%	$15.90	07-Dec-22	21-Dec-22
P05-E	Contract Effectiveness / PO	5	0%	$23.86	22-Dec-22	26-Dec-22
P05-E	Manufacturing / Fabrication / Supply	60	0%	$198.81	27-Dec-22	24-Feb-23
P05-E	Final Inspection	7	0%	$39.76	25-Feb-23	03-Mar-23

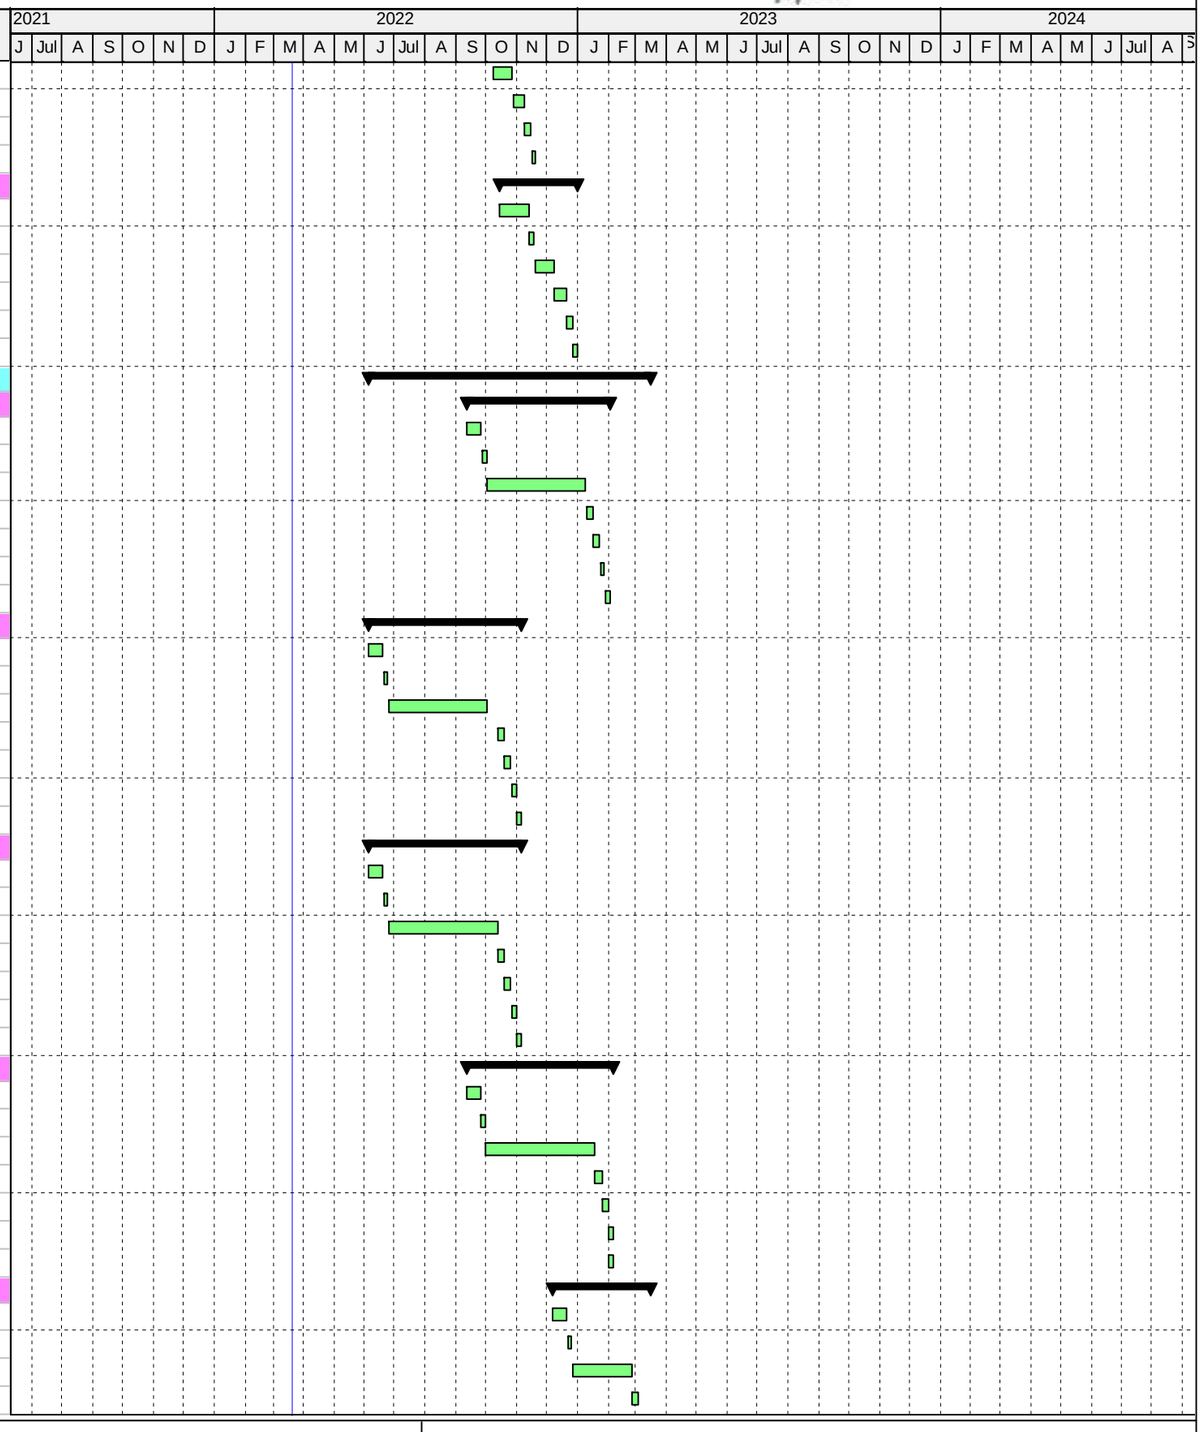


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05-E	Delivery On Site	7	0%	$99.40	04-Mar-23	10-Mar-23
P05-E	Submitting Vendor Data Book	5	0%	$19.88	11-Mar-23	15-Mar-23
Tray/Ladder and Accessories - Extension of Binak B/C Manifold		154	0%	$270.53	07-Jun-22	07-Nov-22
P05-E	Tendering & Selection	15	0%	$10.82	07-Jun-22	21-Jun-22
P05-E	Contract Effectiveness / PO	5	0%	$16.23	22-Jun-22	26-Jun-22
P05-E	Manufacturing / Fabrication / Supply	60	0%	$135.26	27-Jun-22	25-Aug-22
P05-E	Final Inspection	7	0%	$27.05	15-Oct-22	21-Oct-22
P05-E	Delivery On Site	7	0%	$67.63	27-Oct-22	02-Nov-22
P05-E	Submitting Vendor Data Book	5	0%	$13.53	03-Nov-22	07-Nov-22
Electrical Bulk Items		154	0%	$405.05	07-Jun-22	07-Nov-22
P05-E	Tendering & Selection	15	0%	$16.20	07-Jun-22	21-Jun-22
P05-E	Contract Effectiveness / PO	5	0%	$24.30	22-Jun-22	26-Jun-22
P05-E	Manufacturing / Fabrication / Supply	110	0%	$202.52	27-Jun-22	14-Oct-22
P05-E	Final Inspection	12	0%	$40.50	15-Oct-22	26-Oct-22
P05-E	Delivery On Site	7	0%	$101.26	27-Oct-22	02-Nov-22
P05-E	Submitting Vendor Data Book	5	0%	$20.25	03-Nov-22	07-Nov-22
Construction		443	2.24%	$141,138.00	02-Dec-21	10-Feb-24
Wellpad and Access Road		162	3.12%	$101,337.08	02-Dec-21	05-May-23
Access Road		97	15.6%	$20,267.42	02-Dec-21	01-Mar-23
Wellpad Access Road		97	19.5%	$16,213.93	02-Dec-21	01-Mar-23
P05-E	Access Road Preparation W008N	30	65%	$4,864.18	02-Dec-21	24-Dec-22
P05-E	Filling and Compaction	20	0%	$2,432.09	21-Jan-23	09-Feb-23
P05-E	Sub-Base Layer	10	0%	$4,053.48	10-Feb-23	19-Feb-23
Construction of Culvert and Bridge		67	0%	$4,864.18	25-Dec-22	01-Mar-23
bridge		67	0%	$1,945.67	25-Dec-22	01-Mar-23
P05	Excavation	15	0%	$194.57	25-Dec-22	08-Jan-23
P05	lean concrete	2	0%	$155.65	09-Jan-23	10-Jan-23
P05	wall	10	0%	$350.22	11-Jan-23	20-Jan-23
P05	reinforcement	10	0%	$389.13	21-Jan-23	30-Jan-23
P05	form working	10	0%	$194.57	31-Jan-23	09-Feb-23
P05	concrete pouring	5	0%	$583.70	10-Feb-23	14-Feb-23
P05	protect stone	10	0%	$38.91	15-Feb-23	24-Feb-23
P05	Backfill	5	0%	$38.91	25-Feb-23	01-Mar-23
culverts		27	0%	$2,918.51	25-Dec-22	20-Jan-23
P05	pipeway culvert	7	0%	$1,167.40	25-Dec-22	31-Dec-22
P05	pipeway	10	0%	$875.55	01-Jan-23	10-Jan-23
P05	pipeline culvert	10	0%	$875.55	11-Jan-23	20-Jan-23
Burn Pit Access Road		36	0%	$4,053.48	25-Dec-22	30-Jan-23
P05-E	ROW Preparation	20	0%	$2,229.42	25-Dec-22	13-Jan-23
P05-E	Filling and Compaction	10	0%	$810.70	14-Jan-23	23-Jan-23
P05-E	Sub-Base Layer	6	0%	$1,013.37	24-Jan-23	30-Jan-23
Wellpad		162	0%	$81,069.67	25-Nov-22	05-May-23
Water Supply		25	0%	$5,674.88	25-Nov-22	19-Dec-22
P05-E	Water Supply	25	0%	$5,674.88	25-Nov-22	19-Dec-22
Burn Pit		48	0%	$4,053.48	24-Jan-23	12-Mar-23
P05-E	Soil Removal, Triming ,Filling and Compaction of Burn Pit Are	30	0%	$3,242.79	24-Jan-23	22-Feb-23
P05-E	Construction & Installation of Support	10	0%	$202.67	23-Feb-23	04-Mar-23
P05-E	Welding, Installation and Testing	10	0%	$608.02	02-Mar-23	12-Mar-23
Site Preparation		30	0%	$28,374.38	10-Feb-23	11-Mar-23

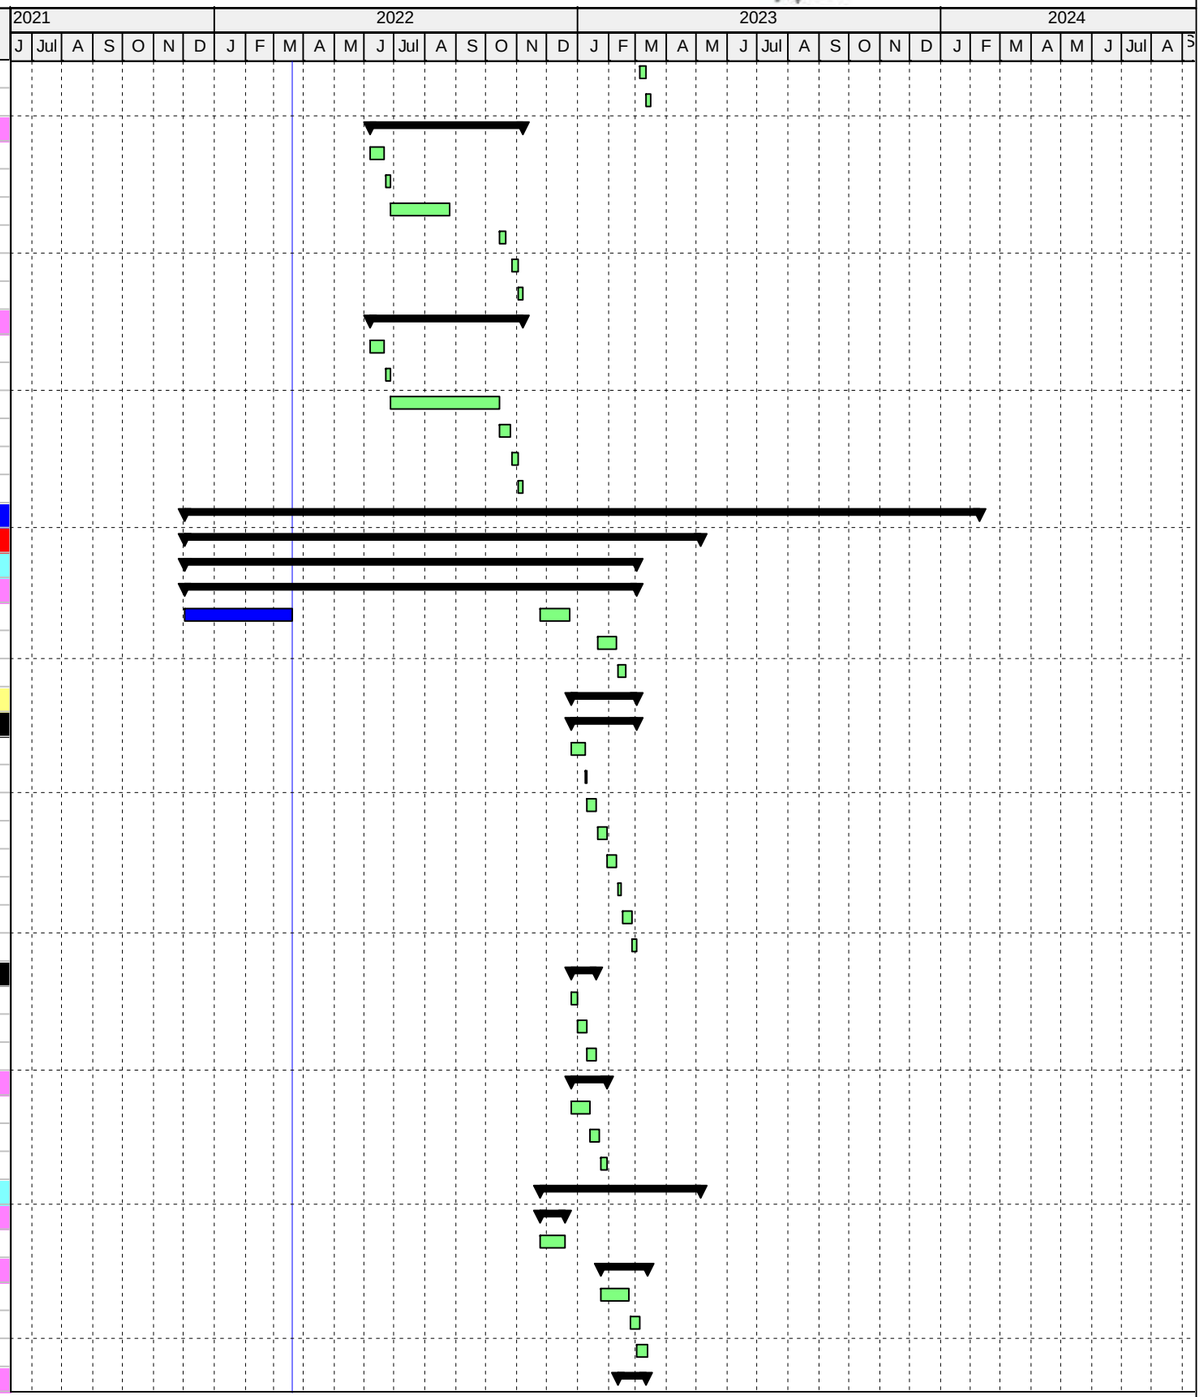

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05-E	Site Preparation W008N	30	0%	$28,374.38	10-Feb-23	11-Mar-23
Civil Work		33	0%	$24,320.90	12-Mar-23	13-Apr-23
P05-E	Excavation and Soil Removal (Cellar)	15	0%	$15,808.59	12-Mar-23	26-Mar-23
P05-E	Installation of Conductor Pipe	10	0%	$1,216.05	12-Mar-23	21-Mar-23
P05-E	Form Work (Above Cellar)	9	0%	$1,216.05	27-Mar-23	04-Apr-23
P05-E	Armed Concrete	9	0%	$6,080.23	04-Apr-23	13-Apr-23
Surface Preparation		19	0%	$810.70	12-Mar-23	30-Mar-23
P05-E	Gravel Paving	19	0%	$810.70	12-Mar-23	30-Mar-23
Mud Channel		55	0%	$4,864.18	12-Mar-23	05-May-23
P05-E	Excavation	20	0%	$486.42	22-Mar-23	10-Apr-23
P05-E	Soil Removal, Filling and Compaction of Mud Pit Area	25	0%	$729.63	12-Mar-23	05-Apr-23
P05-E	Construction of Mud Pit's Walls	25	0%	$1,702.46	01-Apr-23	25-Apr-23
P05-E	Installation sealling Layer	15	0%	$1,459.25	12-Mar-23	26-Mar-23
P05-E	Backfill	10	0%	$486.42	26-Apr-23	05-May-23
Mud Pit		25	0%	$8,106.97	27-Mar-23	20-Apr-23
P05-E	Soil Removal, Filling and Compaction of Mud Pit Area	15	0%	$2,837.44	27-Mar-23	10-Apr-23
P05-E	Construction of Mud Pit's Walls	12	0%	$1,621.39	29-Mar-23	10-Apr-23
P05-E	Installation sealling Layer	10	0%	$3,648.14	10-Apr-23	20-Apr-23
SepticTank		27	0%	$3,242.79	27-Mar-23	23-Apr-23
P05-E	Excavation & Soil Transfer	4	0%	$972.84	27-Mar-23	30-Mar-23
P05-E	Levelling	3	0%	$16.21	30-Mar-23	02-Apr-23
P05-E	Tank Supply	19	0%	$1,848.39	27-Mar-23	14-Apr-23
P05-E	Tank Execution	3	0%	$308.06	14-Apr-23	17-Apr-23
P05-E	Backfilling & Compaction	6	0%	$97.28	17-Apr-23	23-Apr-23
Gasoil Pad		16	0%	$1,621.39	12-Mar-23	27-Mar-23
P05-E	Excavation	5	0%	$324.28	12-Mar-23	16-Mar-23
P05-E	lean concrete	2	0%	$486.42	17-Mar-23	18-Mar-23
P05-E	Form work	4	0%	$162.14	19-Mar-23	22-Mar-23
P05-E	Armed Concrete	5	0%	$648.56	22-Mar-23	27-Mar-23
Wellhead Facility and Flowline		194	0%	$35,284.50	06-May-23	15-Nov-23
Civil		103	0%	$12,349.58	06-May-23	16-Aug-23
P05-EF	Right of Way	13	0%	$9,262.18	06-May-23	18-May-23
P05-EF	Steel Works(Wellhead Facilities)	30	0%	$2,099.43	19-May-23	17-Jun-23
P05-EF	Construction & Installation of Shelter for Wellhead Control Pa	15	0%	$617.48	18-Jun-23	02-Jul-23
P05-EF	Well Pad Fencing	45	0%	$370.49	03-Jul-23	16-Aug-23
Flowline		116	0%	$14,819.49	19-May-23	12-Sep-23
P05-EF	Fabrication of Pipe Support	30	0%	$2,222.92	19-May-23	17-Jun-23
P05-EF	Installation of Pipe Supports	30	0%	$2,222.92	30-May-23	29-Jun-23
6" Flowline Installation		81	0%	$9,632.67	18-Jun-23	07-Sep-23
P05-E	COLD CUT	26	0%	$481.63	18-Jun-23	14-Jul-23
P05-E	Material Handeling	35	0%	$1,155.92	14-Jul-23	18-Aug-23
P05-E	Fit-Up & Welding	40	0%	$6,357.56	14-Jul-23	23-Aug-23
P05-E	Bending	10	0%	$1,011.43	23-Aug-23	02-Sep-23
P05-E	NDT	5	0%	$626.12	02-Sep-23	07-Sep-23
Hydrostatic Test		5	0%	$740.97	07-Sep-23	12-Sep-23
P05-E	6" Pigging and Hydrostatic Test	5	0%	$740.97	07-Sep-23	12-Sep-23
Piping		34	0%	$4,234.14	20-Sep-23	23-Oct-23
P05-EF	Sweep Bend Installation	10	0%	$211.71	20-Sep-23	29-Sep-23
P05-EF	Construction of Spools (Fit up, Welding, NDT…)	15	0%	$1,481.95	30-Sep-23	14-Oct-23



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P05-EF	Valves, Fitting and Spools Installation and Hydrotest	7	0%	$2,328.78	15-Oct-23	21-Oct-23
P05-EF	Painting	5	0%	$211.71	19-Oct-23	23-Oct-23
Instrument Works		20	0%	$3,175.61	20-Sep-23	09-Oct-23
P05-EF	Wellhead Control Panel Installation	10	0%	$1,746.58	20-Sep-23	29-Sep-23
P05-EF	Devices Installation and Piping Connecton	10	0%	$1,429.02	30-Sep-23	09-Oct-23
Pre-commissioning		7	0%	$705.69	09-Nov-23	15-Nov-23
P05-EF	Pre-commissioning	7	0%	$635.12	09-Nov-23	15-Nov-23
P05-EF	Ready for Comm.Certificate(RFCC)	5	0%	$70.57	09-Nov-23	14-Nov-23
Helipad		44	0%	$2,399.35	12-Mar-23	25-Apr-23
P05-EP	Excavation & Soil Transfer	10	0%	$239.93	12-Mar-23	21-Mar-23
P05-EP	Levelling	5	0%	$287.92	22-Mar-23	26-Mar-23
P05-EP	Lean Concrete	3	0%	$359.90	27-Mar-23	29-Mar-23
P05-EP	Reinforced Work	6	0%	$359.90	30-Mar-23	05-Apr-23
P05-EP	Form Work	10	0%	$359.90	05-Apr-23	15-Apr-23
P05-EP	Main Concrete Pouring	5	0%	$479.87	15-Apr-23	20-Apr-23
P05-EP	Backfilling & Compaction	3	0%	$263.93	20-Apr-23	22-Apr-23
P05-EP	Paint Marking	3	0%	$47.99	22-Apr-23	25-Apr-23
Job Site HSE Supervision (Surface)		350	0%	$282.28	25-Nov-22	09-Nov-23
P05-EP	Job Site HSE Supervision (Surface)	350	0%	$282.28	25-Nov-22	09-Nov-23
Commissioning, Startup & Handover		88	0%	$1,834.79	14-Nov-23	10-Feb-24
Commissioning		33	0%	$550.44	14-Nov-23	17-Dec-23
P05-EF	Materials & Utilities Ready for Commissioning	3	0%	$27.52	14-Nov-23	17-Nov-23
P05-EF	Receiving Facilities Ready for Commissioning	3	0%	$27.52	17-Nov-23	20-Nov-23
P05-EF	Permits Obtained for Commissioning	10	0%	$27.52	20-Nov-23	30-Nov-23
P05-EF	Integrated Commissioning	3	0%	$440.35	30-Nov-23	02-Dec-23
P05-EF	Ready for Startup Certificate (RFSU)	15	0%	$27.52	02-Dec-23	17-Dec-23
Startup & Performance Test		18	0%	$733.92	17-Dec-23	04-Jan-24
P05-EF	Startup & Performance Test Run	3	0%	$587.13	17-Dec-23	20-Dec-23
P05-EF	Start of Production (SOP)	15	0%	$146.78	20-Dec-23	04-Jan-24
Handover		37	0%	$550.44	04-Jan-24	10-Feb-24
P05-EF	Compiling & Submitting Final Documentation	20	0%	$165.13	04-Jan-24	24-Jan-24
P05-EF	Training of Operator's Personnel	2	0%	$220.18	24-Jan-24	26-Jan-24
P05-EF	Provisional Acceptance Certificate (PAC)	15	0%	$165.13	26-Jan-24	10-Feb-24
Package 06-New Well # W007S/Manifold Extension (Bangestan)		729	0.51%	$848,245.00	24-Jul-21 A	17-Mar-24
ENGINEERING		645	15.48%	$27,722.00	24-Jul-21 A	24-Dec-23
Basic Design Endorsement		30	100%	$1,386.10	31-Jul-21 A	20-Mar-22
P06-EP	Endorsement Report For Basic Design & Scope of Work	30	100%	$1,386.10	31-Jul-21 A	20-Mar-22
Value Engineering		75	4.31%	$831.66	01-Feb-22	02-Jul-22
P06-EP	Value Engineering Study Report	44	60%	$59.80	01-Feb-22	02-May-22
P06-EP	HAZID Report For WHF & Flowlines	44	0%	$99.72	20-May-22	02-Jul-22
P06-EP	HAZOP Report For Binak B/C Manifold Extension	44	0%	$598.30	20-May-22	02-Jul-22
P06-EP	SIL Report For Binak B/C Manifold Extension	44	0%	$73.85	20-May-22	02-Jul-22
Detail Design		475	18.64%	$15,247.10	24-Jul-21 A	29-Mar-23
Process		149	45.42%	$1,524.71	27-Jul-21 A	07-Jul-22
Basis/Criteria		40	86.99%	$152.47	27-Jul-21 A	28-Apr-22
P06-E	Process Design Criteria	35	100%	$53.29	27-Jul-21 A	20-Mar-22
P06-E	Process Basis Of Design	40	80%	$99.18	27-Jul-21 A	28-Apr-22
Description		44	0%	$152.47	20-Mar-22	02-May-22
P06-E	Process Description - Extension of Binak B/C Manifold	44	0%	$152.47	20-Mar-22	02-May-22
Calculation		44	60%	$152.47	23-Feb-22	02-May-22




Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Calculation book for (CV,PSV,Pump & Line sizing) - Extension	44	60%	$152.47	23-Feb-22	02-May-22
Drawing/Diagram		75	61.39%	$381.18	26-Oct-21	07-Jun-22
P06-E	Symbol & Legend For PFD and P&ID	40	80%	$6.06	30-Oct-21	28-Apr-22
P06-E	ESD Block Diagram - Extension of Binak B/C Manifold	40	0%	$30.38	29-Apr-22	07-Jun-22
P06-E	Process Flow Diagram - Extension of Binak B/C Manifold	40	60%	$67.58	01-Nov-21	28-Apr-22
P06-E	P&ID - Extension of Binak B/C Manifold	30	80%	$43.26	26-Oct-21	28-Apr-22
P06-E	Cause & Effect Diagram - Extension of Binak B/C Manifold	40	0%	$24.28	29-Apr-22	07-Jun-22
P06-E	Process Flow Diagram - W007S	40	60%	$68.35	02-Nov-21	28-Apr-22
P06-E	P&ID for Potable Water Tank - W007S	30	80%	$36.44	01-Nov-21	28-Apr-22
P06-E	P&ID for Diesel Oil Drum- W007S	30	80%	$68.35	16-Nov-21	18-Apr-22
P06-E	P&ID for Potable Water Tank - W007S	30	80%	$36.48	16-Nov-21	18-Apr-22
Philosophy		74	11.01%	$152.47	21-Nov-21	01-Jun-22
P06-E	Drainage Philosophy	44	0%	$6.04	19-Apr-22	01-Jun-22
P06-E	Control Philosophy	44	0%	$41.78	19-Apr-22	01-Jun-22
P06-E	Flare,Blow Down And Relief Philosophy	44	0%	$41.78	19-Apr-22	01-Jun-22
P06-E	Isolation Philosophy	44	60%	$27.99	21-Nov-21	02-May-22
P06-E	ESD Philosophy	44	0%	$34.89	19-Apr-22	01-Jun-22
Data Sheet		70	0%	$152.47	29-Apr-22	07-Jul-22
P06-E	Process Data Sheets For Instrument Devices - W007S & Exte	36	0%	$51.84	29-Apr-22	03-Jun-22
P06-E	Process Data Sheets For Fuel Oil Storage Drum of Well Pads	35	0%	$50.32	29-May-22	02-Jul-22
P06-E	Process Data Sheets For Potable Water Tank of Well Pads	35	0%	$50.32	03-Jun-22	07-Jul-22
List		115	22.66%	$152.47	08-Nov-21	08-May-22
P06-E	Line List - W007S & Manifold Extension	40	0%	$54.22	30-Mar-22	08-May-22
P06-E	Tie-In List - Extension of Binak B/C Manifold	40	0%	$54.22	20-Mar-22	28-Apr-22
P06-E	Line List - W007S	40	80%	$40.66	08-Nov-21	08-May-22
P06-E	Consumption List	40	60%	$3.37	23-Feb-22	02-May-22
Report		44	80%	$228.71	30-Oct-21	02-May-22
P06-E	Flowline Hydraulic Calculation Report	44	80%	$228.71	30-Oct-21	02-May-22
Mechanical		100	65.52%	$152.47	28-Jul-21 A	26-Jun-22
Basis/Criteria		54	60%	$5.26	28-Jul-21 A	12-May-22
P06-E	Mechanical Design Criteria	54	60%	$5.26	28-Jul-21 A	12-May-22
Specification		99	60%	$47.33	28-Jul-21 A	26-Jun-22
P06-E	Specification For Positive Displacement Rotary Pumps	44	60%	$35.50	21-Feb-22	02-May-22
P06-E	Specification For Pressure Vessels	54	60%	$5.92	28-Jul-21 A	01-Jun-22
P06-E	Specification For Atmospheric Above Ground Welded Steel Ta	79	60%	$5.92	28-Jul-21 A	26-Jun-22
Data Sheets		60	60%	$78.86	16-Jan-22	02-Jun-22
Rotary Equipment		60	60%	$78.86	16-Jan-22	02-Jun-22
P06-	Data Sheets For Fuel Oil Storage Drum of Well Pads	35	60%	$8.54	16-Jan-22	02-May-22
P06-	Data Sheets For Potable Water Tank of Well Pads	50	60%	$10.05	09-Feb-22	02-Jun-22
P06-	Data Sheets For Oil Sump Pump - Extension of Binak B/C Ma	50	60%	$60.27	14-Mar-22	28-May-22
Drawing/Diagram		34	100%	$21.03	28-Jul-21 A	09-Apr-22
P06-E	Standard Detail Drawing For Pressure Vessels and Heat Exch	14	100%	$10.51	28-Jul-21 A	09-Apr-22
P06-E	Standard Detail Drawing For Storage Tanks	14	100%	$10.51	28-Jul-21 A	09-Apr-22
HVAC/Plumbing		402	5.54%	$304.94	24-Jul-21 A	29-Mar-23
Basis/Criteria		64	100%	$3.60	24-Jul-21 A	14-May-22
P06-E	HVAC & Plumbing Design Criteria	64	100%	$3.60	24-Jul-21 A	14-May-22
Specification		64	100%	$5.73	24-Jul-21 A	27-Mar-22
P06-E	Specification For HVAC Equipment	64	100%	$3.44	24-Jul-21 A	27-Mar-22
P06-E	Specification For Duct Work & Pipe Work	64	100%	$2.29	24-Jul-21 A	27-Mar-22
Drawing/Diagram-1		48	87.87%	$8.63	24-Jul-21 A	16-May-22

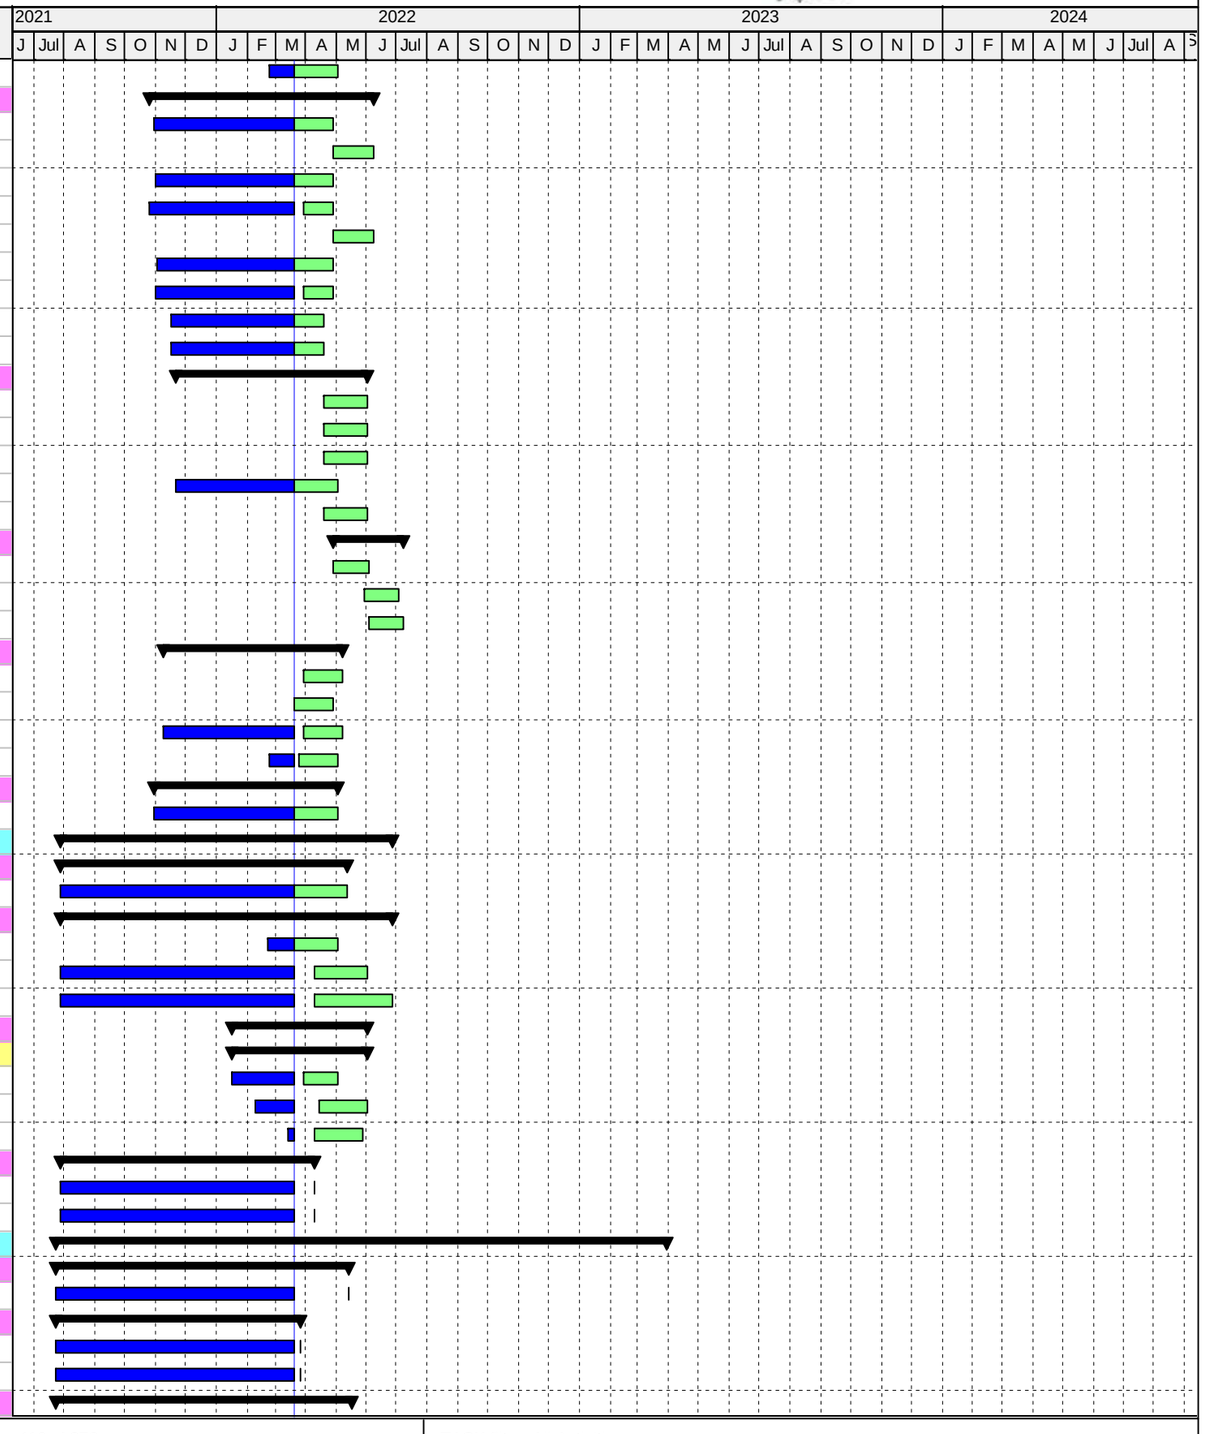


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Standard Drawing For HVAC & Plumbing	14	100%	$6.00	24-Jul-21 A	30-Mar-22
P06-E	Symbol & Legend For HVAC & Plumbing	48	60%	$2.63	22-Aug-21	16-May-22
Calculation		195	0%	$57.39	13-May-22	23-Nov-22
P06-E	HVAC Calculation Note For Switchgear Building - W007S	62	0%	$28.70	13-May-22	13-Jul-22
P06-E	HVAC Calculation Note For Security Building - W007S	62	0%	$28.70	23-Sep-22	23-Nov-22
Drawing/Diagram		257	0%	$172.20	13-May-22	24-Jan-23
P06-E	HVAC System Layout For Switchgear Building - W007S	62	0%	$43.05	14-Jul-22	13-Sep-22
P06-E	HVAC System Layout For Security Building - W007S	62	0%	$43.05	24-Nov-22	24-Jan-23
P06-E	Plumbing & Sewage Piping Layout For Switchgear Building - \	64	0%	$43.05	13-May-22	15-Jul-22
P06-E	Plumbing & Sewage Piping Layout For Security Building - W	64	0%	$43.05	23-Sep-22	25-Nov-22
Data Sheets		64	0%	$28.70	25-Jan-23	29-Mar-23
P06-E	Data Sheets For Main HVAC Equipment - W007S	64	0%	$28.70	25-Jan-23	29-Mar-23
MTO		7	0%	$28.70	25-Jan-23	31-Jan-23
P06-E	MTO For Building HVAC & Plumbing Systems - W007S	7	0%	$28.70	25-Jan-23	31-Jan-23
Piping		445	3.32%	$3,049.42	24-Jul-21 A	17-Dec-22
Basis/Criteria		39	100%	$0.30	24-Jul-21 A	20-Mar-22
P06-E	Piping Design Criteria	39	100%	$0.30	24-Jul-21 A	20-Mar-22
Specification		441	65.76%	$10.37	24-Jul-21 A	06-Jul-22
P06-E	Piping Material Specification	64	60%	$4.95	28-Nov-21	06-Jul-22
P06-E	Specification For Color Coding and Marking	39	60%	$0.32	09-Aug-21	01-May-22
P06-E	Specification For Transportation, Handling, Storage of pipes	39	80%	$0.32	12-Dec-21	01-May-22
P06-E	Specification For the Design of Piping in Mechanical Packages	39	60%	$0.32	09-Aug-21	01-May-22
P06-E	Specification For Metallic Pipes	39	80%	$0.32	24-Jul-21 A	01-May-22
P06-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$0.32	24-Jul-21 A	24-Mar-22
P06-E	Specification For Painting	39	100%	$0.32	24-Jul-21 A	27-Mar-22
P06-E	Specification For Lining (Internal Protection of Equipment by F	39	60%	$0.32	09-Aug-21	04-May-22
P06-E	Specification For Material Requirements in Sour service	39	60%	$0.32	09-Aug-21	04-May-22
P06-E	Specification For Manual Valves	39	60%	$0.32	09-Aug-21	04-May-22
P06-E	Specification For Plant Piping Systems Pressure Testing	39	60%	$0.32	09-Aug-21	04-May-22
P06-E	Specification For Welding of Plant Piping System	39	60%	$0.32	09-Aug-21	04-May-22
P06-E	Specification For Flexibility Analysis	39	60%	$0.32	09-Aug-21	04-May-22
P06-E	Specification For Coating Of Underground Piping	39	100%	$0.32	24-Jul-21 A	30-Mar-22
P06-E	Specification For Pipe Support	39	60%	$0.32	09-Aug-21	07-May-22
P06-E	Specification For Piping Construction, Fabrication & Erection	39	60%	$0.32	09-Aug-21	07-May-22
P06-E	Specification For Piping Design & Plant Layout	39	60%	$0.32	09-Aug-21	07-May-22
P06-E	Specification For Insulation	39	100%	$0.32	24-Aug-21	30-Mar-22
P06-E	Specification For Piping Cleaning and Flushing	39	0%	$0.05	24-Aug-21	30-Mar-22
Data Sheets		39	60%	$0.91	27-Dec-21	12-May-22
P06-E	Data Sheets For Stone Trap	39	60%	$0.91	27-Dec-21	12-May-22
Procedure/Plan		125	50%	$0.61	24-Jul-21 A	04-Sep-22
P06-E	3D-Model (PDMS) Review Procedure	39	100%	$0.30	24-Jul-21 A	03-Apr-22
P06-E	Piping Hydrostatic Test Diagram - Sub Surface	44	0%	$0.30	23-Jul-22	04-Sep-22
Drawing/Diagram		243	36.31%	$138.75	08-Nov-21	17-Dec-22
P06-E	Standard Pipe Support Drawings	14	100%	$0.07	19-Feb-22	20-Mar-22
P06-E	Piping Assembly Drawing	45	0%	$9.95	08-Jun-22	22-Jul-22
P06-E	Piping Hydrostatic Test Diagram - Sub Surface	44	0%	$0.67	23-Jul-22	04-Sep-22
P06-E	Plot Plan Drawing - Extension of Binak B/C Manifold	39	60%	$69.37	15-Jan-22	27-Apr-22
P06-E	Piping Plan Drawing - Extension of Binak B/C Manifold	44	0%	$4.18	04-Nov-22	17-Dec-22
P06-E	Isometric Drawings - Extension of Binak B/C Manifold	39	0%	$4.18	09-Nov-22	17-Dec-22

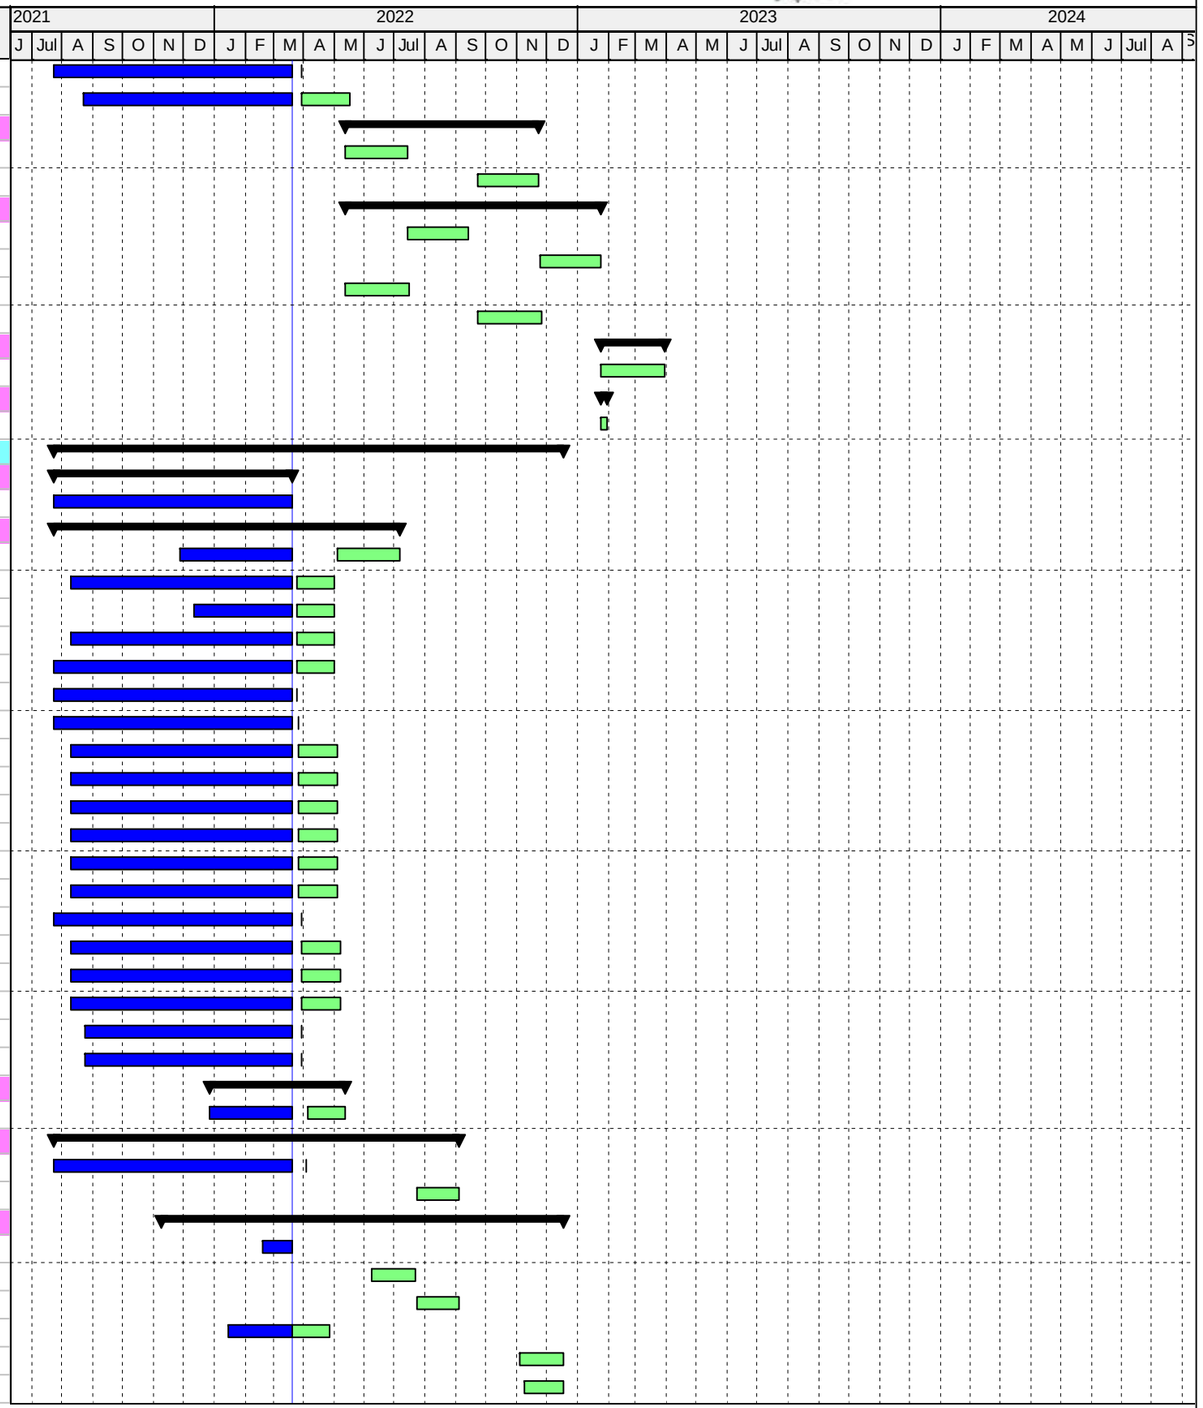


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Plot Plan Drawing - W007S	39	0%	$4.18	29-Apr-22	06-Jun-22
P06-E	Piping Plan - W007S	37	0%	$6.67	25-Sep-22	31-Oct-22
P06-E	Isometric Drawings - W007S	36	0%	$10.57	30-Sep-22	04-Nov-22
P06-E	Material Flow Diagram - W007S	39	60%	$14.46	08-Nov-21	12-May-22
P06-E	Material Flow Diagram - Extension of Binak B/C Manifold	39	0%	$14.46	13-May-22	20-Jun-22
Calculation		44	60%	$59.77	28-Nov-21	21-Jun-22
P06-E	Piping Wall Thickness Calculation	44	60%	$59.77	28-Nov-21	21-Jun-22
Report		200	0.29%	$2,439.54	28-Nov-21	24-Nov-22
P06-E	PDMS Model Review Report (30%) - Extension of Binak B/C	35	0%	$622.57	09-May-22	12-Jun-22
P06-E	PDMS Model Review Report (60%) - Extension of Binak B/C	40	0%	$957.27	23-Jul-22	31-Aug-22
P06-E	PDMS Model Review Report (90%) - Extension of Binak B/C	40	0%	$622.57	01-Sep-22	10-Oct-22
P06-E	PDMS Model Review Report (30%) - W007S	45	0%	$48.06	09-May-22	22-Jun-22
P06-E	PDMS Model Review Report (60%) - W007S	40	0%	$71.72	23-Jun-22	01-Aug-22
P06-E	PDMS Model Review Report (90%) - W007S	40	0%	$48.06	02-Aug-22	10-Sep-22
P06-E	Stress Analysis Calculations Report For Manifold area	45	0%	$57.57	11-Oct-22	24-Nov-22
P06-E	Piping Corrosion Study & Material Selection Report	45	60%	$11.71	28-Nov-21	17-May-22
List		179	0%	$94.23	09-May-22	03-Nov-22
P06-E	Critical Line List - Extension of Binak B/C Manifold	37	0%	$9.12	09-May-22	14-Jun-22
P06-E	Piping Tie-In List - Extension of Binak B/C Manifold	37	0%	$30.40	09-May-22	14-Jun-22
P06-E	Piping Support List - Extension of Binak B/C Manifold	64	0%	$30.40	01-Sep-22	03-Nov-22
P06-E	Piping Support List - W007S	54	0%	$12.16	02-Aug-22	24-Sep-22
P06-E	Critical Line List - W007S	39	0%	$12.16	09-May-22	16-Jun-22
MTO		37	0%	$304.94	11-Sep-22	17-Oct-22
P06-E	MTO For Pipes - Manifold & W007S	7	0%	$50.80	11-Sep-22	17-Sep-22
P06-E	MTO For Fittings - Manifold & W007S	7	0%	$50.80	11-Oct-22	17-Oct-22
P06-E	MTO For Flanges - Manifold & W007S	7	0%	$50.83	11-Oct-22	17-Oct-22
P06-E	MTO For Manual Valves - Manifold & W007S	7	0%	$50.83	11-Oct-22	17-Oct-22
P06-E	MTO For Gaskets - Manifold & W007S	7	0%	$50.83	11-Oct-22	17-Oct-22
P06-E	MTO For Bolt & Nuts - Manifold & W007S	7	0%	$50.83	11-Oct-22	17-Oct-22
Pipeline & Flow line		182	43.07%	$457.41	24-Jul-21 A	23-May-22
Basis/Criteria		39	100%	$3.20	28-Aug-21	20-Mar-22
P06-E	Pipeline Design Criteria	39	100%	$3.20	28-Aug-21	20-Mar-22
Specification		49	81.46%	$44.60	24-Jul-21 A	07-May-22
P06-E	Specification For Line Pipes	39	100%	$0.86	24-Jul-21 A	24-Mar-22
P06-E	Specification For Pipeline Cold Bending	39	80%	$0.76	28-Aug-21	01-May-22
P06-E	Specification For Barred Tee	39	80%	$0.76	28-Aug-21	01-May-22
P06-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$0.76	24-Jul-21 A	24-Mar-22
P06-E	Specification For Pipeline Valves	39	80%	$0.76	28-Aug-21	01-May-22
P06-E	Specification For Pipeline Coating	39	100%	$0.76	24-Jul-21 A	24-Mar-22
P06-E	Specification For Pipeline Flushing, Cleaning And Hydrostatic	39	100%	$0.86	24-Jul-21 A	27-Mar-22
P06-E	Specification For Welding of Transportation Pipeline	39	80%	$0.76	12-Dec-21	04-May-22
P06-E	Specification For Pipeline Stress Analysis	39	80%	$0.76	24-Jul-21 A	04-May-22
P06-E	Specification For Pipeline Insulation Joint	39	100%	$0.76	24-Jul-21 A	27-Mar-22
P06-E	Specification For Pipeline Construction	39	80%	$0.76	25-Jan-22	04-May-22
P06-E	Specification For Anchor Flanges	39	80%	$0.86	28-Aug-21	07-May-22
P06-E	Specification For Pigs	39	80%	$0.76	28-Aug-21	07-May-22
P06-E	Pipeline Material Specification	44	80%	$33.64	27-Oct-21	02-May-22
P06-E	Specification For Pipeline Cleaning and Flushing	39	60%	$0.76	24-Jul-21 A	07-May-22
Drawing/Diagram		95	24.68%	$243.71	27-Jul-21 A	23-May-22

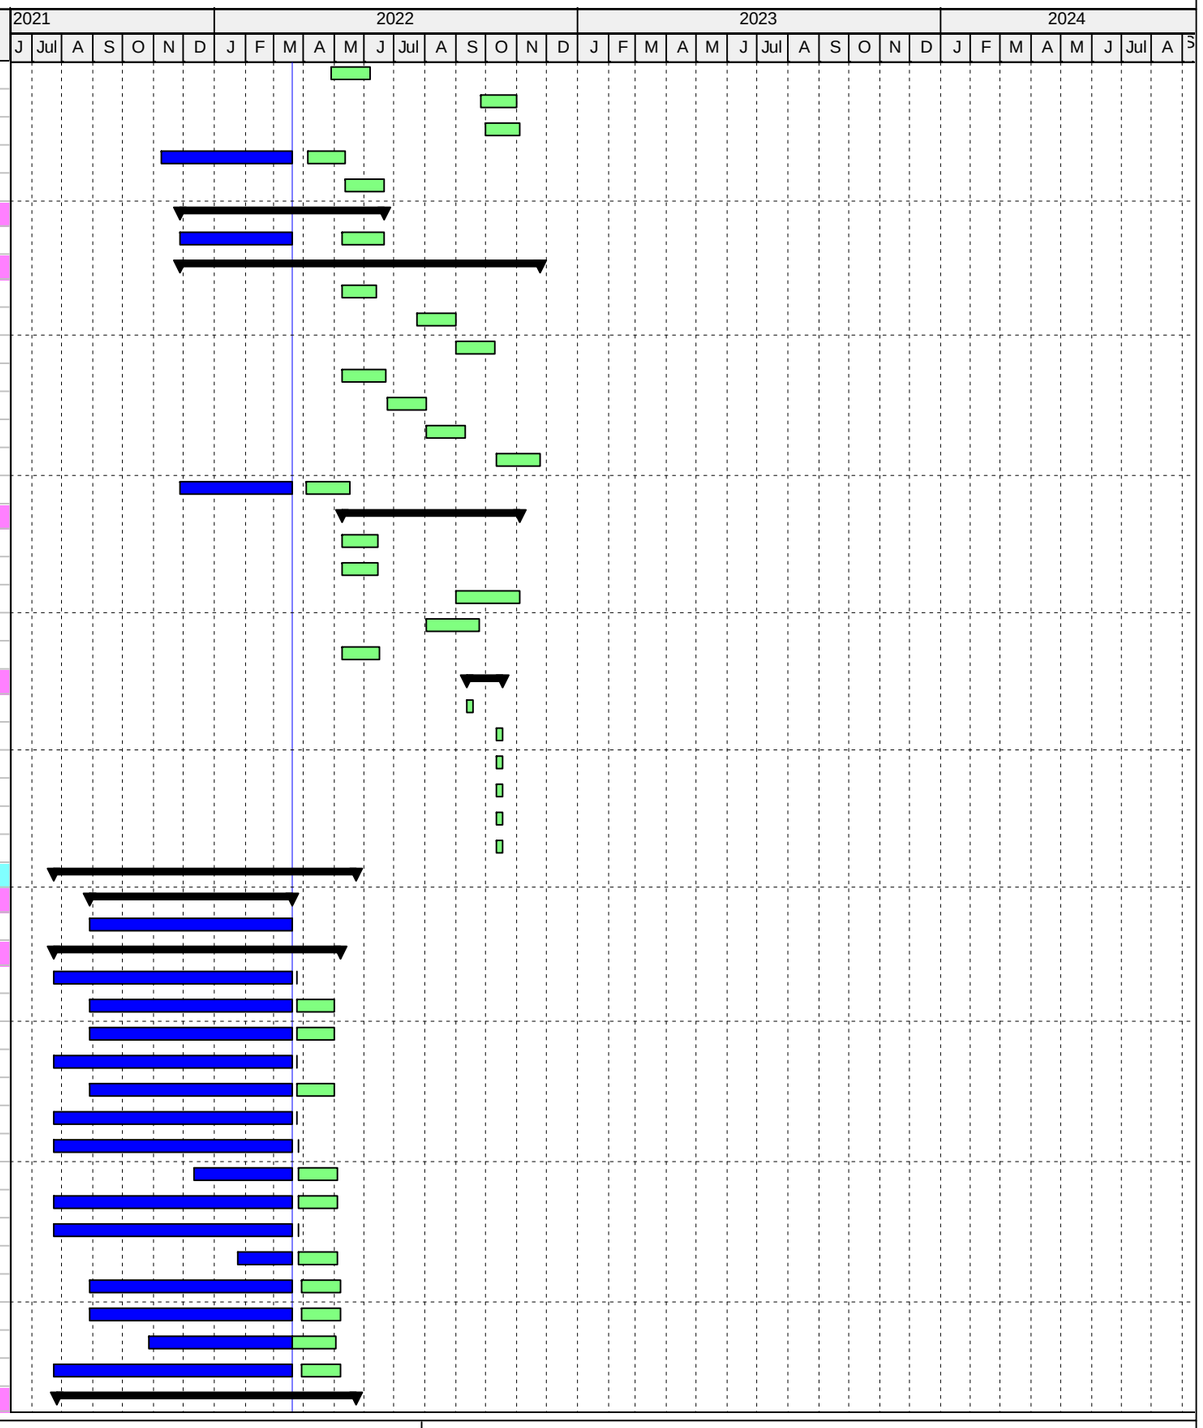


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Pipeline Standard Drawing For Vent Valve Pre-cast Concrete	44	60%	$5.87	27-Nov-21	12-May-22
P06-E	Pipeline Standard Drawing For Slab Bridge And Set-On-Weig	44	60%	$5.87	21-Dec-21	12-May-22
P06-E	Pipeline Standard Drawing For River Crossing	44	60%	$5.87	15-Dec-21	12-May-22
P06-E	Pipeline Standard Support Drawings	14	100%	$7.60	27-Jul-21 A	20-Mar-22
P06-E	Pipeline Standard Drawing For Line Marker Post and Cathodi	45	80%	$5.48	18-Sep-21	23-May-22
P06-E	Standard Drawing For Above Ground Pipeline Construction F	44	80%	$5.56	27-Nov-21	12-May-22
P06-E	Standard Drawing For Under Ground Pipeline Construction F	44	100%	$5.56	04-Dec-21	30-Mar-22
P06-E	Pipeline Standard Drawing For Anchor Support	44	60%	$5.56	22-Dec-21	12-May-22
P06-E	Standard Drawing For A/G Pipeline Road Crossing	44	60%	$5.56	05-Dec-21	12-May-22
P06-E	Standard Drawing For Existing Pipeline Crossing	44	60%	$5.56	18-Dec-21	12-May-22
P06-E	Pipeline Standard Drawing For Irish Crossing	44	60%	$6.29	04-Dec-21	12-May-22
P06-E	Pipeline Standard Drawing For Water - Way Crossing	44	60%	$6.29	22-Nov-21	12-May-22
P06-E	Pipeline Standard Drawing For Pig Signaller Concrete Pit	44	60%	$6.29	27-Nov-21	12-May-22
P06-E	Pipeline Standard Drawing For H-Pipe Support	44	100%	$6.29	27-Nov-21	30-Mar-22
P06-E	Flowline Transversal Drawings - W007S	44	0%	$148.59	20-Mar-22	02-May-22
P06-E	Pipeline Hydrostatic Test Diagram - Sub Surface	44	0%	$11.48	20-Mar-22	02-May-22
Procedure/Plan		44	0%	$9.24	09-Apr-22	22-May-22
P06-E	Pipeline Hydrostatic Test Diagram - Sub Surface	44	0%	$9.24	09-Apr-22	22-May-22
Calculation		44	80%	$18.94	27-Oct-21	22-May-22
P06-E	Pipeline Wall Thickness Calculation	44	80%	$18.94	27-Oct-21	22-May-22
List		44	0%	$41.03	20-Mar-22	02-May-22
P06-E	Road Crossing Location List	44	0%	$41.03	20-Mar-22	02-May-22
Report		44	80%	$72.82	27-Oct-21	22-May-22
P06-E	Pipeline Corrosion Study & Material Selection Report	44	80%	$72.82	27-Oct-21	22-May-22
MTO		7	100%	$23.88	22-Aug-21	20-Mar-22
P06-E	MTO For Line Pipes (Flowlines) - W007S	7	100%	$23.88	22-Aug-21	20-Mar-22
Control & Instrumentation		381	26.66%	$1,524.71	24-Jul-21 A	19-Jan-23
Basis/Criteria		44	94.59%	$7.01	14-Aug-21	29-Apr-22
P06-E	Fire & Gas Detection Design Criteria	38	100%	$6.06	14-Aug-21	27-Mar-22
P06-E	Instrument & Control System Design Criteria	38	60%	$0.96	03-Jan-22	29-Apr-22
Specification		46	79.48%	$36.14	24-Jul-21 A	04-May-22
P06-E	Specification For WHCP/HPU	38	80%	$1.80	08-Aug-21	26-Apr-22
P06-E	Specification For Instrumentation	39	100%	$0.94	26-Jul-21 A	23-Mar-22
P06-E	Specification For Control System	39	80%	$2.52	28-Jul-21 A	30-Apr-22
P06-E	Specification For ESD System	39	80%	$2.52	28-Jul-21 A	30-Apr-22
P06-E	Specification For Instrument and Control of Package Unit Sys	39	60%	$1.89	04-Aug-21	30-Apr-22
P06-E	Specification For Control Valves	39	80%	$2.52	24-Jul-21 A	30-Apr-22
P06-E	Specification For On-off /Shut Down Valves(ESDV/MOV)	39	80%	$2.52	24-Jul-21 A	30-Apr-22
P06-E	Specification For Pressure Safety Valves(PSV)	39	100%	$2.52	24-Jul-21 A	27-Mar-22
P06-E	Specification For Fire & Gas Sensor and Devices	39	80%	$2.52	26-Jul-21 A	04-May-22
P06-E	Specification For Instrument/F&G Cables	39	60%	$2.52	04-Aug-21	04-May-22
P06-E	Specification For Control Panels and System Cabinets	39	60%	$2.52	24-Jul-21 A	04-May-22
P06-E	Specification For Fire & Gas System	39	100%	$2.52	28-Jul-21 A	20-Mar-22
P06-E	Specification For LBV	37	80%	$8.83	10-Aug-21	25-Apr-22
Data Sheets		175	42.94%	$376.60	22-Aug-21	12-Jul-22
P06-E	Data Sheets For WHCP/HPU - Wellheads	35	80%	$7.95	22-Aug-21	26-Apr-22
P06-E	Data Sheets For Pressure Gauge - Wellheads	35	80%	$4.03	07-Dec-21	28-Apr-22
P06-E	Data Sheets For Temperature Gauge - Wellheads	35	80%	$4.03	07-Dec-21	28-Apr-22
P06-E	Data Sheets For Temperature Gauge - Extension of Binak B/	35	80%	$20.37	07-Dec-21	28-Apr-22

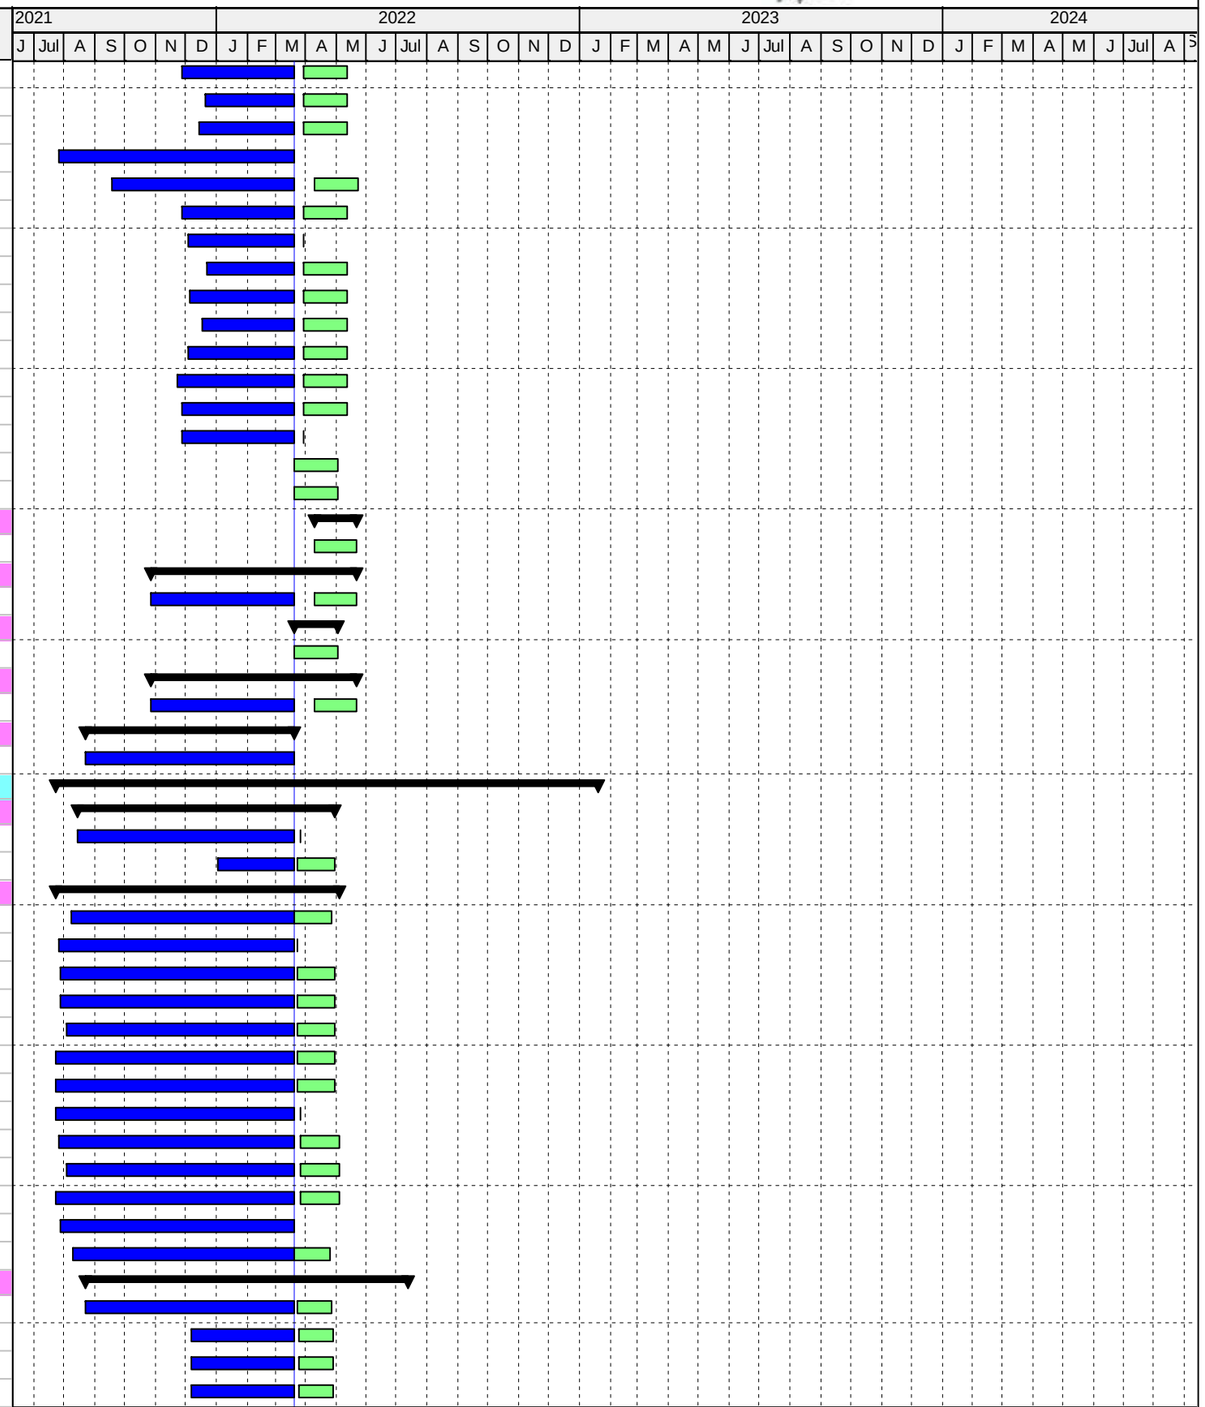


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Data Sheets For Pressure & Diff. Pressure Gauge - Extensio	35	80%	$20.37	07-Dec-21	28-Apr-22
P06-E	Data Sheets For Pressure Transmitter - Extension of Binak B/	35	80%	$20.37	07-Dec-21	28-Apr-22
P06-E	Data Sheets For Pressure & Safety Relief Valves - Extension	35	0%	$39.73	09-May-22	12-Jun-22
P06-E	Data Sheets For ON/OFF & Shutdown Valves - Extension of	35	60%	$39.73	09-Mar-22	30-Apr-22
P06-E	Data Sheets For Control/Regulator valves - Extension of Bina	35	60%	$39.73	07-Mar-22	12-Jun-22
P06-E	Data Sheets For Flow Transmitter/Diff. Pressure Transmitter	35	80%	$20.37	07-Dec-21	28-Apr-22
P06-E	Data Sheets For Orifice Plate/Restriction Orifice - Extension o	35	0%	$39.73	29-Mar-22	02-May-22
P06-E	Data Sheets For Corrosion Coupon/ Probe - Extension of Bin	35	60%	$39.73	09-Mar-22	28-Apr-22
P06-E	Data Sheets For F&G Devices - Extension of Binak B/C Mani	35	0%	$39.73	08-Jun-22	12-Jul-22
P06-E	Data Sheets For Pressure Switch and Differential Pressure S	35	0%	$20.37	29-Apr-22	02-Jun-22
P06-E	Data sheet for Level Transmitter - W007S & Manifold	35	60%	$20.34	01-Jan-22	26-Apr-22
Drawing/Diagram		276	13.69%	$676.82	22-Aug-21	19-Jan-23
P06-E	Instrument Hook-up Diagram - Wellheads	42	80%	$6.23	14-Nov-21	12-May-22
P06-E	WHCP Hydraulic \Peneumatic Diagrams - Wellheads	42	100%	$5.55	22-Aug-21	19-Apr-22
P06-E	Typical Instrument Installation Drawing - Extension of Binak B/	35	100%	$32.62	09-Mar-22	31-Mar-22
P06-E	Block Diagram Configuration For Control/ESD/F&G System -	37	80%	$27.48	01-Sep-21	02-May-22
P06-E	Instrument Earthing Typical Diagram - Extension of Binak B/C	55	100%	$27.48	01-Jan-22	30-Apr-22
P06-E	Instrument Hook-up Diagram - Extension of Binak B/C Manifo	40	0%	$37.23	29-Apr-22	07-Jun-22
P06-E	ESD Level Hierarchy - Extension of Binak B/C Manifold	38	0%	$27.48	29-Apr-22	05-Jun-22
P06-E	ESD System Loop Diagram - Extension of Binak B/C Manifold	42	0%	$37.23	10-Oct-22	20-Nov-22
P06-E	Control System Loop Diagram - Extension of Binak B/C Manif	42	0%	$37.23	10-Oct-22	20-Nov-22
P06-E	F&G System Loop Diagram - Extension of Binak B/C Manifold	42	0%	$37.23	10-Oct-22	20-Nov-22
P06-E	Instrument Air Piping and Air Header Diagram - Extension of I	40	0%	$27.48	01-Sep-22	10-Oct-22
P06-E	Instrument & F&G Junction Box Termination Diagram - Exten	42	0%	$37.23	18-Jul-22	28-Aug-22
P06-E	F&G Cause and Effect Diagram - Extension of Binak B/C Mar	39	0%	$27.48	18-Jul-22	25-Aug-22
P06-E	Control System Logic Diagram - Extension of Binak B/C Manif	42	0%	$32.62	29-Apr-22	09-Jun-22
P06-E	ESD Logic Diagram - Extension of Binak B/C Manifold	42	0%	$32.62	29-Apr-22	09-Jun-22
P06-E	Control Room Layout & Arrangement Drawing - Extension of	38	0%	$22.88	24-Nov-22	31-Dec-22
P06-E	Control Room Cable Route Layout - Extension of Binak B/C M	42	0%	$37.23	13-Oct-22	23-Nov-22
P06-E	Instrument Location Layout - Extension of Binak B/C Manifold	42	0%	$37.23	01-Sep-22	12-Oct-22
P06-E	Instrument/F&G Cable Trench/Route Layout Drawing - Exten	42	0%	$37.23	29-Aug-22	09-Oct-22
P06-E	F&G Location Layout - Extension of Binak B/C Manifold	40	0%	$32.62	29-Apr-22	07-Jun-22
P06-E	Instrument Location Layout Drawing - W007S	37	0%	$27.48	02-Aug-22	07-Sep-22
P06-E	Wiring Diagram; Interposing Relay Panel (IRP) - Extension of	44	0%	$49.00	07-Dec-22	19-Jan-23
List		350	38.67%	$302.20	03-Nov-21	31-Dec-22
P06-E	I/O List For Control System - Extension of Binak B/C Manifold	40	80%	$12.30	03-Nov-21	28-Apr-22
P06-E	I/O List For ESD Systems - Extension of Binak B/C Manifold	40	80%	$87.76	03-Nov-21	28-Apr-22
P06-E	I/O List For F&G Systems - Extension of Binak B/C Manifold	40	0%	$12.30	08-Jun-22	17-Jul-22
P06-E	Panels & Junction Box List - Extension of Binak B/C Manifold	37	0%	$43.18	29-Aug-22	04-Oct-22
P06-E	Set Point & Alarm List - Extension of Binak B/C Manifold	38	0%	$18.49	29-Apr-22	05-Jun-22
P06-E	I&C Power Consumption Summary - Extension of Binak B/C M	38	60%	$35.96	28-Feb-22	31-Dec-22
P06-E	F&G Detector List - Extension of Binak B/C Manifold	39	0%	$18.49	08-Jun-22	16-Jul-22
P06-E	Instrument /F&G Cable List - Extension of Binak B/C Manifold	42	0%	$58.48	29-Aug-22	09-Oct-22
P06-E	Instrument Index For New Wells & Manifold Extension	7	100%	$15.23	10-Nov-21	13-May-22
MTO		131	0%	$125.94	08-Jun-22	16-Oct-22
P06-E	MTO for Bulk Item and Installation Accessories - W007S & Ma	7	0%	$25.19	01-Sep-22	07-Sep-22
P06-E	MTO For Instrument/F&G Cable - W007S & Manifold	7	0%	$25.19	10-Oct-22	16-Oct-22
P06-E	MTO For Instrument/F&G Junction box and Gland - W007S &	7	0%	$25.19	05-Oct-22	11-Oct-22

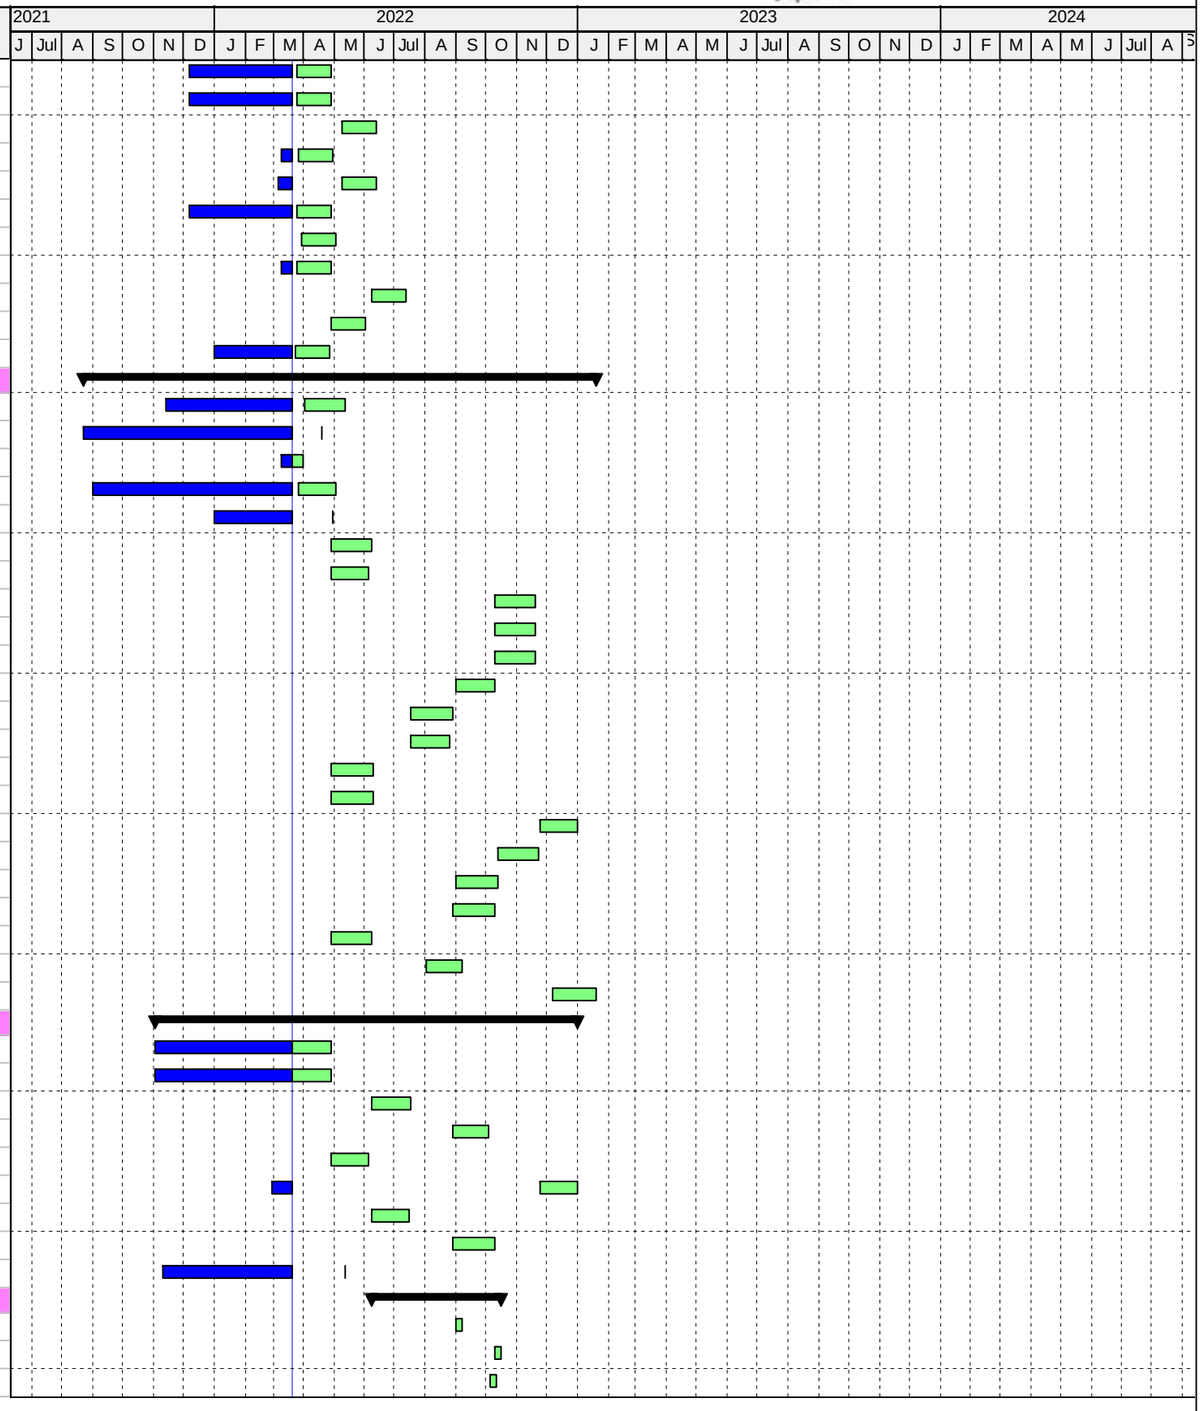


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	MTO For Instrument Tube and Fitting - W007S & Manifold	7	0%	$25.19	08-Jun-22	14-Jun-22
P06-E	MTO For Instrument Cable Tray/Ladder - W007S & Manifold	7	0%	$25.19	01-Sep-22	07-Sep-22
Safety		138	50.85%	$381.18	24-Jul-21 A	07-Sep-22
Basis/Criteria		44	100%	$38.12	29-Aug-21	19-Apr-22
P06-E	Active Fire Protection and Safety Concept	44	100%	$38.12	29-Aug-21	19-Apr-22
Specification		47	94.82%	$76.24	24-Jul-21 A	06-May-22
P06-E	Specification For Fire Fighting Equipment	44	100%	$5.92	29-Aug-21	24-Mar-22
P06-E	Specification For Hazardous Area Classification	44	100%	$5.92	24-Jul-21 A	24-Mar-22
P06-E	Specification For Fire Water System	44	80%	$7.90	24-Jul-21 A	06-May-22
P06-E	Specification For Environmental Job	44	60%	$5.92	11-Aug-21	06-May-22
P06-E	Specification For Total Flooding System	44	100%	$7.90	24-Jul-21 A	27-Mar-22
P06-E	Specification For Safety Equipment	44	100%	$9.48	29-Aug-21	27-Mar-22
P06-E	Specification For passive Fire protection	44	100%	$23.70	24-Jul-21 A	27-Mar-22
P06-E	Specification For Safety Signs	44	100%	$9.48	24-Jul-21 A	27-Mar-22
Drawing/Diagram		128	16.99%	$152.47	29-Aug-21	02-Sep-22
P06-E	Typical Installation Detail for Safety & Fire Fighting Equipment	14	100%	$5.93	29-Dec-21	27-Mar-22
P06-E	Symbol & Legend For Safety & Firefighting Systems	44	100%	$5.93	29-Aug-21	27-Mar-22
P06-E	Hazardous Area Classification Layout - Extension of Binak B/C	44	60%	$23.43	12-Mar-22	02-May-22
P06-E	Safety & Fire Fighting Equipment Location Layout - Extension	44	0%	$23.43	28-Apr-22	10-Jun-22
P06-E	Escape Route & Safety Sign Layout - Extension of Binak B/C	44	0%	$23.43	11-Jun-22	24-Jul-22
P06-E	Hazardous Area Classification Layout - W007S	44	0%	$23.43	03-May-22	15-Jun-22
P06-E	Safety & Fire Fighting Equipment Location Layout - W007S	44	0%	$23.43	07-Jun-22	20-Jul-22
P06-E	Escape Route & Safety Sign Layout - W007S	44	0%	$23.43	21-Jul-22	02-Sep-22
Data Sheets		47	70.93%	$38.12	21-Sep-21	09-May-22
P06-E	Material Safety Data Sheets	44	60%	$27.72	21-Sep-21	09-May-22
P06-E	Data Sheets For Fire Fighting Equipment	44	100%	$3.46	08-Dec-21	24-Mar-22
P06-E	Data Sheets For Safety Equipment	44	100%	$3.46	08-Dec-21	27-Mar-22
P06-E	Data Sheets For Safety Sign	44	100%	$3.46	08-Dec-21	27-Mar-22
List		69	80%	$38.12	09-Nov-21	02-May-22
P06-E	Hazard Source List - Extension of Binak B/C Manifold	44	80%	$19.06	09-Nov-21	02-May-22
P06-E	Hazard Source List - W007S	44	80%	$19.06	09-Nov-21	02-May-22
MTO		49	0%	$38.12	21-Jul-22	07-Sep-22
P06-E	MTO For Fire Fighting & Safety Equipment - Manifold & W00	7	0%	$19.06	21-Jul-22	27-Jul-22
P06-E	MTO For Safety Sign - W007S	5	0%	$19.06	03-Sep-22	07-Sep-22
Electrical		232	21.65%	$1,524.71	24-Jul-21 A	06-Dec-22
Basis/Criteria		54	100%	$4.12	03-Aug-21	20-Mar-22
P06-E	Electrical System Design Criteria	54	100%	$4.12	03-Aug-21	20-Mar-22
Specification		55	100%	$49.55	24-Jul-21 A	30-Mar-22
P06-E	Specification For LV Switchgear & Motor Control Centers	49	100%	$2.57	24-Jul-21 A	24-Mar-22
P06-E	Specification For MV Switchgear	49	100%	$2.94	24-Jul-21 A	24-Mar-22
P06-E	Specification For UPS System	49	100%	$2.94	04-Aug-21	24-Mar-22
P06-E	Specification For Transformers	49	100%	$2.94	24-Jul-21 A	24-Mar-22
P06-E	Specification For DC Charger	49	100%	$2.94	04-Aug-21	24-Mar-22
P06-E	Specification For Earthing & Lightning System	49	100%	$1.87	28-Jul-21 A	24-Mar-22
P06-E	Specification For Lighting & Small Power System	49	100%	$2.57	28-Jul-21 A	27-Mar-22
P06-E	Specification For Bulk Materials	49	100%	$2.57	24-Jul-21 A	27-Mar-22
P06-E	Specification For Diesel Generator	49	100%	$2.94	28-Jul-21 A	27-Mar-22
P06-E	Specification For LV Induction Motors	49	100%	$2.70	24-Jul-21 A	27-Mar-22
P06-E	Specification For Electrical Requirements of Packaged Units	49	100%	$2.94	28-Jul-21 A	27-Mar-22

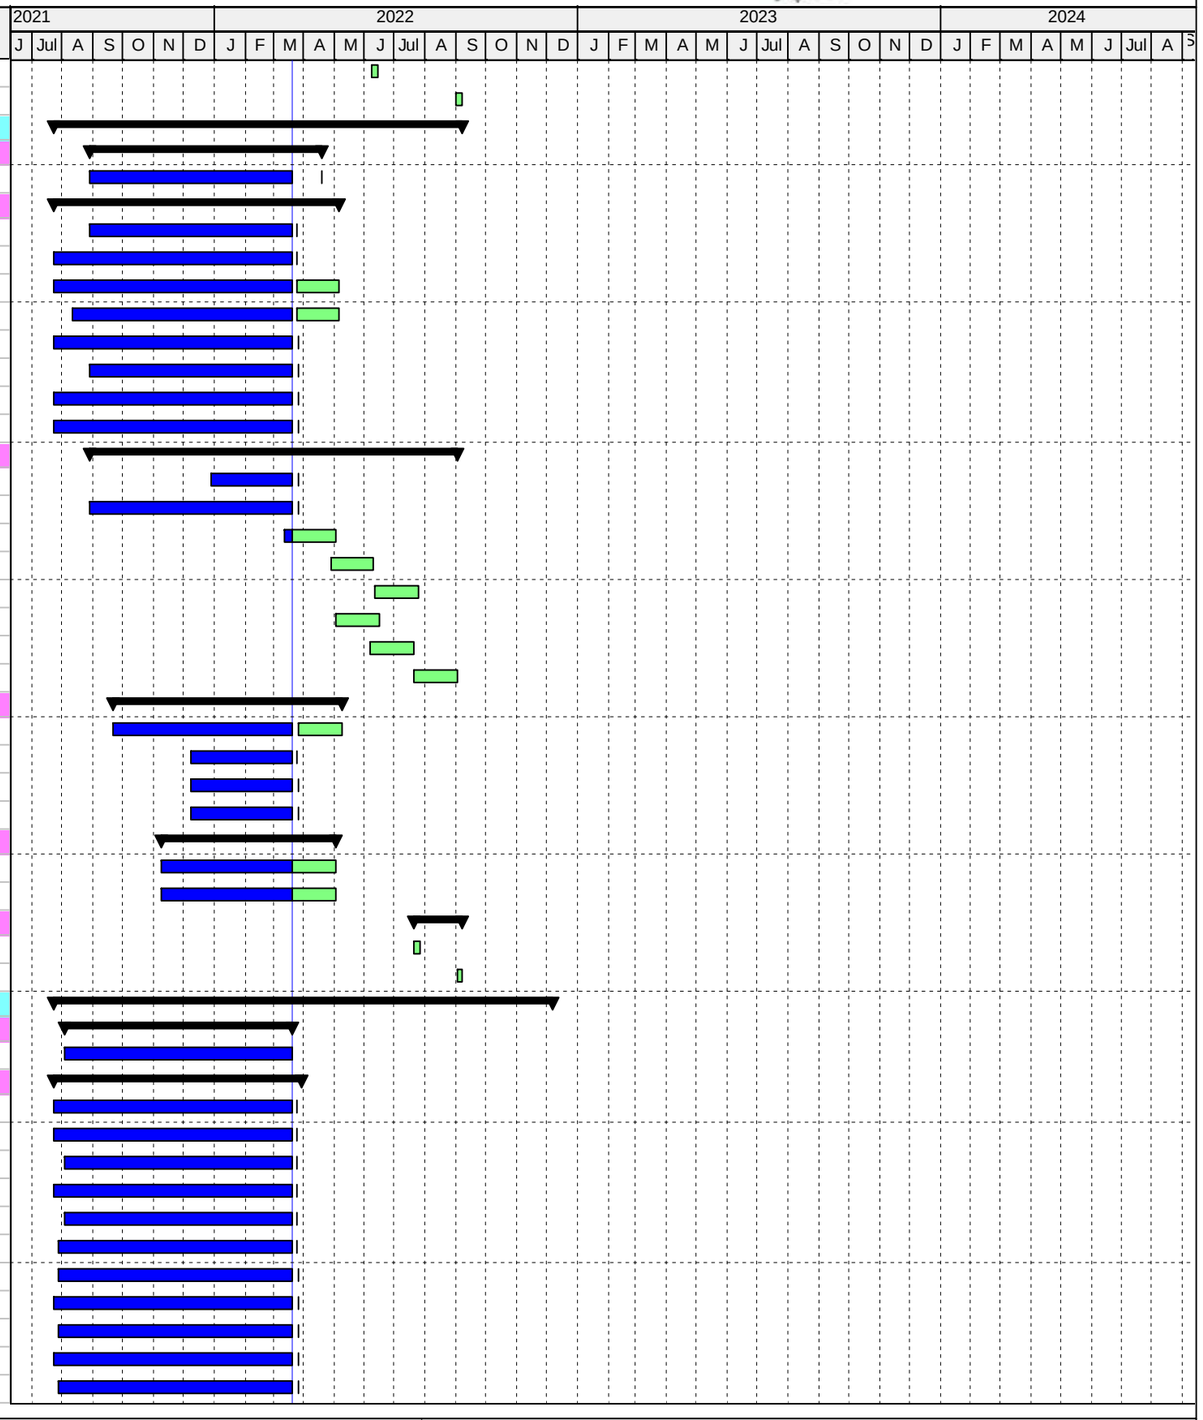


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Specification For Capacitor Bank	49	100%	$2.94	24-Jul-21 A	27-Mar-22
P06-E	Specification For Distribution & Lighting Panels	49	100%	$2.94	28-Jul-21 A	30-Mar-22
P06-E	Specification For Power & Control Cables	49	100%	$2.57	24-Jul-21 A	30-Mar-22
P06-E	Specification For Cathodic Protection System	49	100%	$2.57	31-Jul-21 A	30-Mar-22
P06-E	Specification For MV Induction Motors	49	100%	$2.70	24-Jul-21 A	30-Mar-22
P06-E	Specification For NGR	49	100%	$2.94	24-Jul-21 A	30-Mar-22
P06-E	Specification For Overhead Transmission Lines	49	100%	$2.94	28-Jul-21 A	30-Mar-22
Calculation		223	40.7%	$81.42	11-Oct-21 A	16-Jul-22
P06-E	Calculation Note For Lighting System of Well Pads Switchgea	64	0%	$6.01	27-Apr-22	29-Jun-22
P06-E	Calculation Note For Lighting System of Well Pads Security B	64	0%	$6.01	27-Apr-22	29-Jun-22
P06-E	Calculation Note For Lighting System of Well Pads Area	74	0%	$8.02	27-Apr-22	09-Jul-22
P06-E	Calculation Note For Cable Sizing of Well Pads	74	80%	$8.02	02-Nov-21	11-Jun-22
P06-E	Calculation Note For UPS System of Well Pads	74	0%	$8.02	04-May-22	16-Jul-22
P06-E	Calculation Note For Earthing & Lightning System of Well Pac	74	0%	$8.02	19-Apr-22	01-Jul-22
P06-E	Calculation Note For Diesel Generator Sizing of Well Pads	64	60%	$6.01	26-Jan-22	27-May-22
P06-E	Calculation Note For DC Charger of Well Pads	74	80%	$8.02	26-Jan-22	06-Jun-22
P06-E	Calculation Note For LV Capacitor Bank of Well Pads	44	60%	$9.76	29-Jan-22	17-May-22
P06-E	Calculation Note For 11 KV Over Head Line Sag and Tension	44	80%	$6.77	13-Oct-21	17-May-22
P06-E	Calculation Note For 33 KV Over Head Line Sag and Tension	44	80%	$6.77	11-Oct-21 A	17-May-22
Drawing/Diagram		232	18.59%	$871.98	09-Aug-21	06-Dec-22
P06-E	Electrical Legend and Symbols	45	100%	$1.83	09-Aug-21	30-Mar-22
P06-E	Typical Installation Details & Notes For Earthing and Lightning	30	100%	$5.58	25-Aug-21	30-Mar-22
P06-E	Typical Installation Details & Notes For Lighting System	30	100%	$4.97	25-Aug-21	30-Mar-22
P06-E	Typical Installation Details & Notes For Power System	30	100%	$1.66	25-Aug-21	30-Mar-22
P06-E	Installation Details & Notes For Cathodic Protection Systems	60	100%	$1.66	25-Aug-21	30-Mar-22
P06-E	Typical Installation Details For Over Head Line Equipment	30	100%	$3.75	22-Aug-21	19-Apr-22
P06-E	Installation Detail & Notes for Connection OHL to Gantries for	45	60%	$15.09	06-Mar-22	03-May-22
P06-E	Electrical Typical Schematic Diagrams For LV Panels of Well F	30	100%	$9.24	30-Aug-21	20-Mar-22
P06-E	Control Logic Diagram For LV Incomers of Well Pads	60	80%	$7.41	30-Aug-21	18-May-22
P06-E	Earthing Layout For Electrical Tower (Gantry) of Well Pads	40	0%	$5.58	16-Jul-22	24-Aug-22
P06-E	Cable Route Layout For Electrical Tower (Gantry) of Well Pac	50	0%	$7.41	16-Jul-22	03-Sep-22
P06-E	Overall Single Line Diagram of Well Pads	50	60%	$9.24	02-Mar-22	08-May-22
P06-E	Single Line Diagram For LV Switchgear of Well Pads	50	60%	$7.41	08-Feb-22	08-May-22
P06-E	Single Line Diagram For LV Power Distribution Panel of Well	50	0%	$7.41	04-May-22	22-Jun-22
P06-E	Single Line Diagram For DC Charger of Well Pads	50	80%	$7.41	06-Feb-22	23-May-22
P06-E	Single Line Diagram For Capacitor Banks of Well Pads	50	60%	$7.41	02-Feb-22	23-May-22
P06-E	Interconnection Wiring Diagram of Well Pads	40	0%	$11.16	04-May-22	12-Jun-22
P06-E	Area Lighting & Small Power Layout of Well Pads of Well Pad	50	0%	$7.41	16-Jul-22	03-Sep-22
P06-E	Lighting & Small Power Layout For Switchgear Building of We	40	0%	$5.58	13-May-22	21-Jun-22
P06-E	Lighting & Small Power Layout For Security Building of Well P	40	0%	$5.58	23-Sep-22	01-Nov-22
P06-E	Area Electrical Cable Route & Section Layout of Well Pads	50	0%	$9.24	16-Jul-22	03-Sep-22
P06-E	Electrical Cable Route & Section Layout For Switchgear Buildi	60	0%	$15.09	16-Jul-22	13-Sep-22
P06-E	Electrical Equipment Arrangement Layout For Switchgear Buil	50	0%	$13.17	13-May-22	01-Jul-22
P06-E	Earthing & Lightning Layout for well pads	50	0%	$5.32	29-May-22	17-Jul-22
P06-E	Earthing Layout - Extension of Binak B/C Manifold	50	0%	$74.29	07-Jun-22	26-Jul-22
P06-E	LV Switchgear/MCC Expansion SLD - Extension of Binak B/C	40	0%	$48.05	04-May-22	12-Jun-22
P06-E	UPS Single Line Diagram - Extension of Binak B/C Manifold	40	60%	$81.70	26-Mar-22	03-May-22
P06-E	DC Charger Single Line Diagram - Extension of Binak B/C Ma	40	60%	$81.70	26-Mar-22	03-May-22

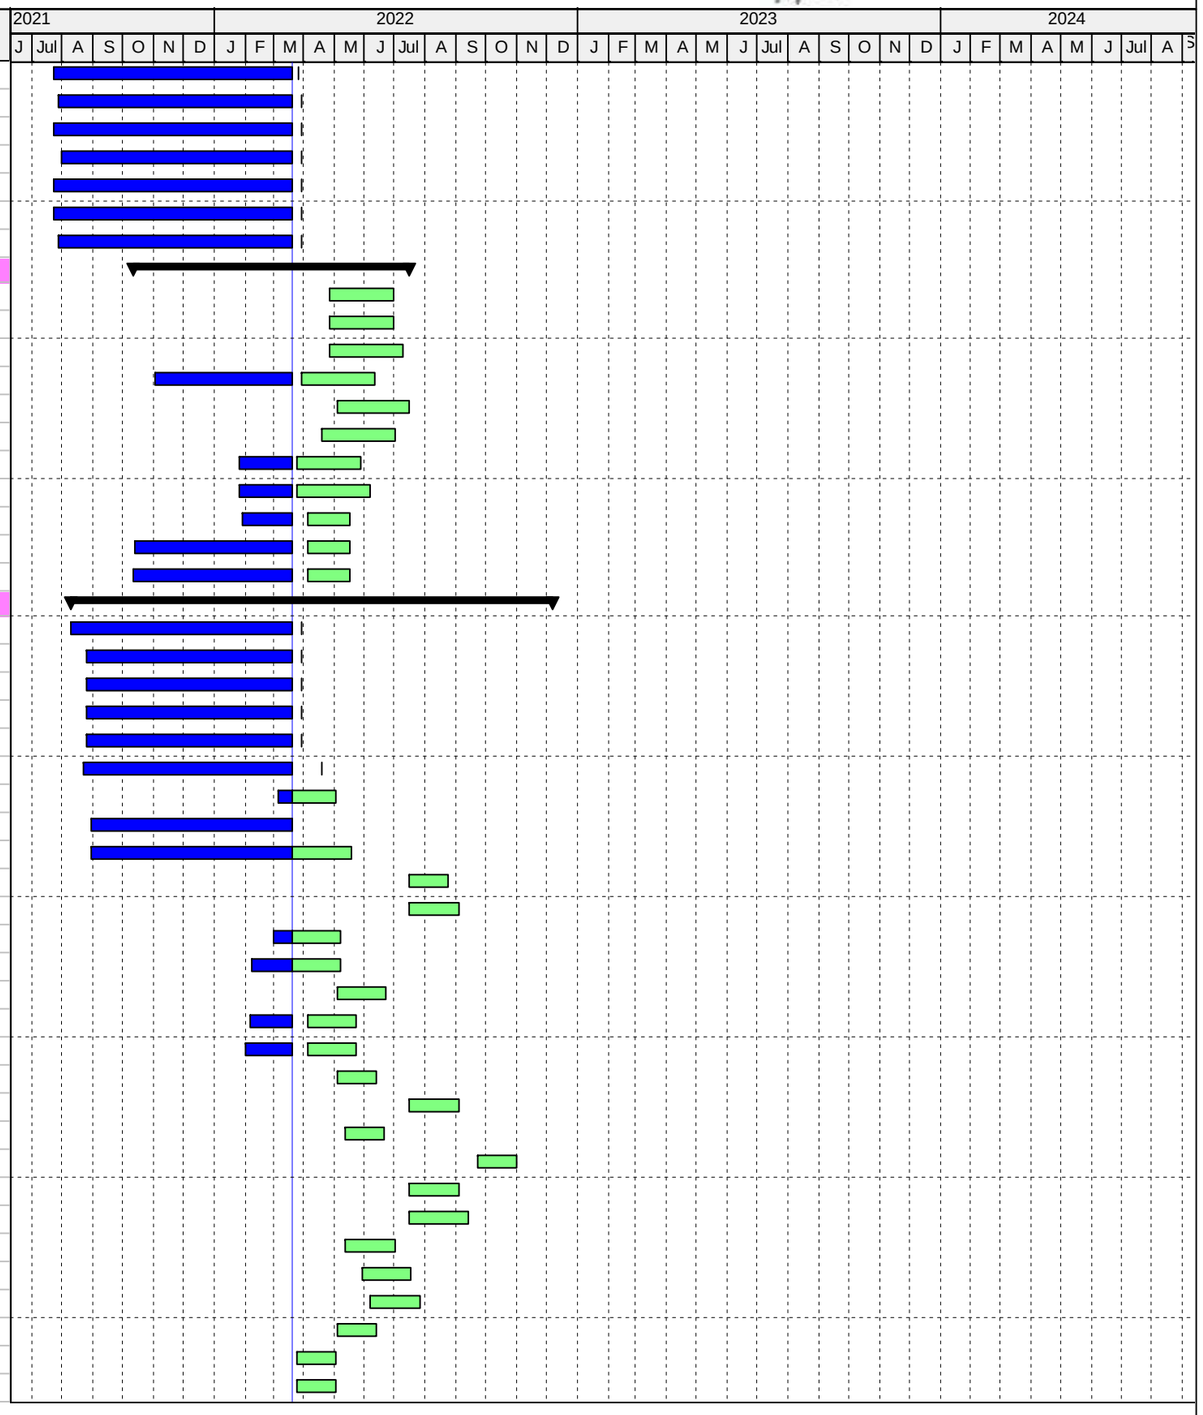


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Interconnection Wiring Diagram - Extension of Binak B/C Mar	40	0%	$150.33	28-Oct-22	06-Dec-22
P06-E	Area Electrical Cable Route & Section Layout - Extension of B	40	0%	$89.12	16-Jul-22	24-Aug-22
P06-E	Electrical Equipment Arrangement Layout In Switchgear Buildi	40	0%	$89.12	04-May-22	12-Jun-22
P06-E	Earthing & Lightning Layout - Extension of Binak B/C Manifold	40	0%	$44.56	07-Jun-22	16-Jul-22
P06-E	11KV Over Head Line Study Report	35	0%	$18.75	01-Aug-22	04-Sep-22
P06-E	33KV Over Head Line Study Report	35	0%	$18.75	08-Jul-22	11-Aug-22
List		108	26.14%	$131.13	25-Jan-22	27-Oct-22
P06-E	Electrical Load List of Well Pads	45	80%	$14.80	25-Jan-22	03-May-22
P06-E	Electrical Power & Control Cable List of Well Pads	79	0%	$8.31	10-Aug-22	27-Oct-22
P06-E	Cable Drum Schedule and Cutting List of Well Pads	74	0%	$8.31	10-Aug-22	22-Oct-22
P06-E	Electrical Load List - Extension of Binak B/C Manifold	45	60%	$37.38	07-Mar-22	03-May-22
P06-E	Electrical Power & Control Cable List - Extension of Binak B/C	74	0%	$62.31	10-Aug-22	22-Oct-22
Data Sheets		214	67.99%	$69.07	12-Sep-21	17-Jul-22
P06-E	Data Sheets For UPS of Well Pads	45	0%	$5.93	04-May-22	17-Jun-22
P06-E	Data Sheets For DC Charger of Well Pads	45	80%	$5.93	29-Jan-22	08-May-22
P06-E	Data Sheets For Diesel Generator of Well Pads	45	60%	$5.93	20-Sep-21	08-May-22
P06-E	Data Sheets For LV Capacitor Bank of Well Pads	45	80%	$5.93	12-Sep-21	03-May-22
P06-E	Data Sheets For LV Switchgear of Well Pads	45	60%	$5.93	19-Feb-22	08-May-22
P06-E	Data Sheets For Power & Control Cables of Well Pads	45	80%	$5.93	13-Sep-21	13-May-22
P06-E	Data Sheets For Power Transformers of Well Pads	45	80%	$5.93	15-Sep-21	03-May-22
P06-E	Data Sheets For Distribution & Lighting Panels of Well Pads	45	60%	$5.93	12-Sep-21	17-Jul-22
P06-E	Data Sheets For 11 KV Over Head Line Equipment	45	80%	$10.83	10-Nov-21	17-Jul-22
P06-E	Data Sheets For 33 KV Over Head Line Equipment	45	80%	$10.83	10-Nov-21	17-Jul-22
Report		133	0%	$137.99	04-May-22	13-Sep-22
P06-E	Electrical Network (Load Flow, Motor Starting & Short Circuit)	54	0%	$39.49	04-May-22	26-Jun-22
P06-E	Relay Coordination & Setting Study Report of Well Pads	54	0%	$39.49	27-Jun-22	19-Aug-22
P06-E	11KV Over Head Line Study Report	44	0%	$29.50	01-Aug-22	13-Sep-22
P06-E	33KV Over Head Line Study Report	44	0%	$29.50	08-Jul-22	20-Aug-22
MTO		184	0%	$179.46	04-May-22	03-Nov-22
P06-E	MTO For Earthing & Lightning Systems - Manifold & W007S	7	0%	$27.60	27-Jul-22	02-Aug-22
P06-E	MTO For Lighting & Small Powers - Manifold & W007S	7	0%	$27.60	18-Oct-22	24-Oct-22
P06-E	MTO For Power & Control Cables - Manifold & W007S	7	0%	$27.60	28-Oct-22	03-Nov-22
P06-E	MTO For Tray/Ladder and Accessories - Manifold & W007S	7	0%	$27.60	23-Jun-22	29-Jun-22
P06-E	MTO For Electrical Bulk Items - Manifold & W007S	7	0%	$27.60	04-May-22	10-May-22
P06-E	MTO For Transmission Over Head Line - W007S	7	0%	$41.45	04-May-22	10-May-22
Architecture		277	16.71%	$381.18	18-Dec-21	29-Sep-22
Basis/Criteria		74	60%	$77.00	08-Feb-22	01-Jun-22
P06-E	Architectural Design Criteria	74	60%	$77.00	08-Feb-22	01-Jun-22
Specification		44	0%	$96.29	20-Mar-22	02-May-22
P06-E	Buildings General Specification	44	0%	$96.29	20-Mar-22	02-May-22
Drawing/Diagram		247	18.94%	$92.40	18-Dec-21	22-Sep-22
P06-E	Architectural Drawing For Diesel Generator Shelter of Well P	25	0%	$21.08	23-May-22	16-Jun-22
P06-E	Architectural Drawing For WHCP/HPU Shelter of Well Pads -	44	0%	$21.08	19-Apr-22	01-Jun-22
P06-E	Architectural Drawing For Switchgear Building of Well Pads -	44	60%	$21.08	18-May-22	12-May-22
P06-E	Architectural Drawing For Security Building of Well Pads - WC	44	0%	$21.08	10-Aug-22	22-Sep-22
P06-E	Standard Drawing for Architectural Details	44	60%	$8.09	18-Dec-21	02-May-22
MTO		7	0%	$115.50	23-Sep-22	29-Sep-22
P06-E	MTO For Architectural Works - W007S	7	0%	$115.50	23-Sep-22	29-Sep-22
Civil		449	17.74%	$1,372.24	01-Aug-21	25-Dec-22

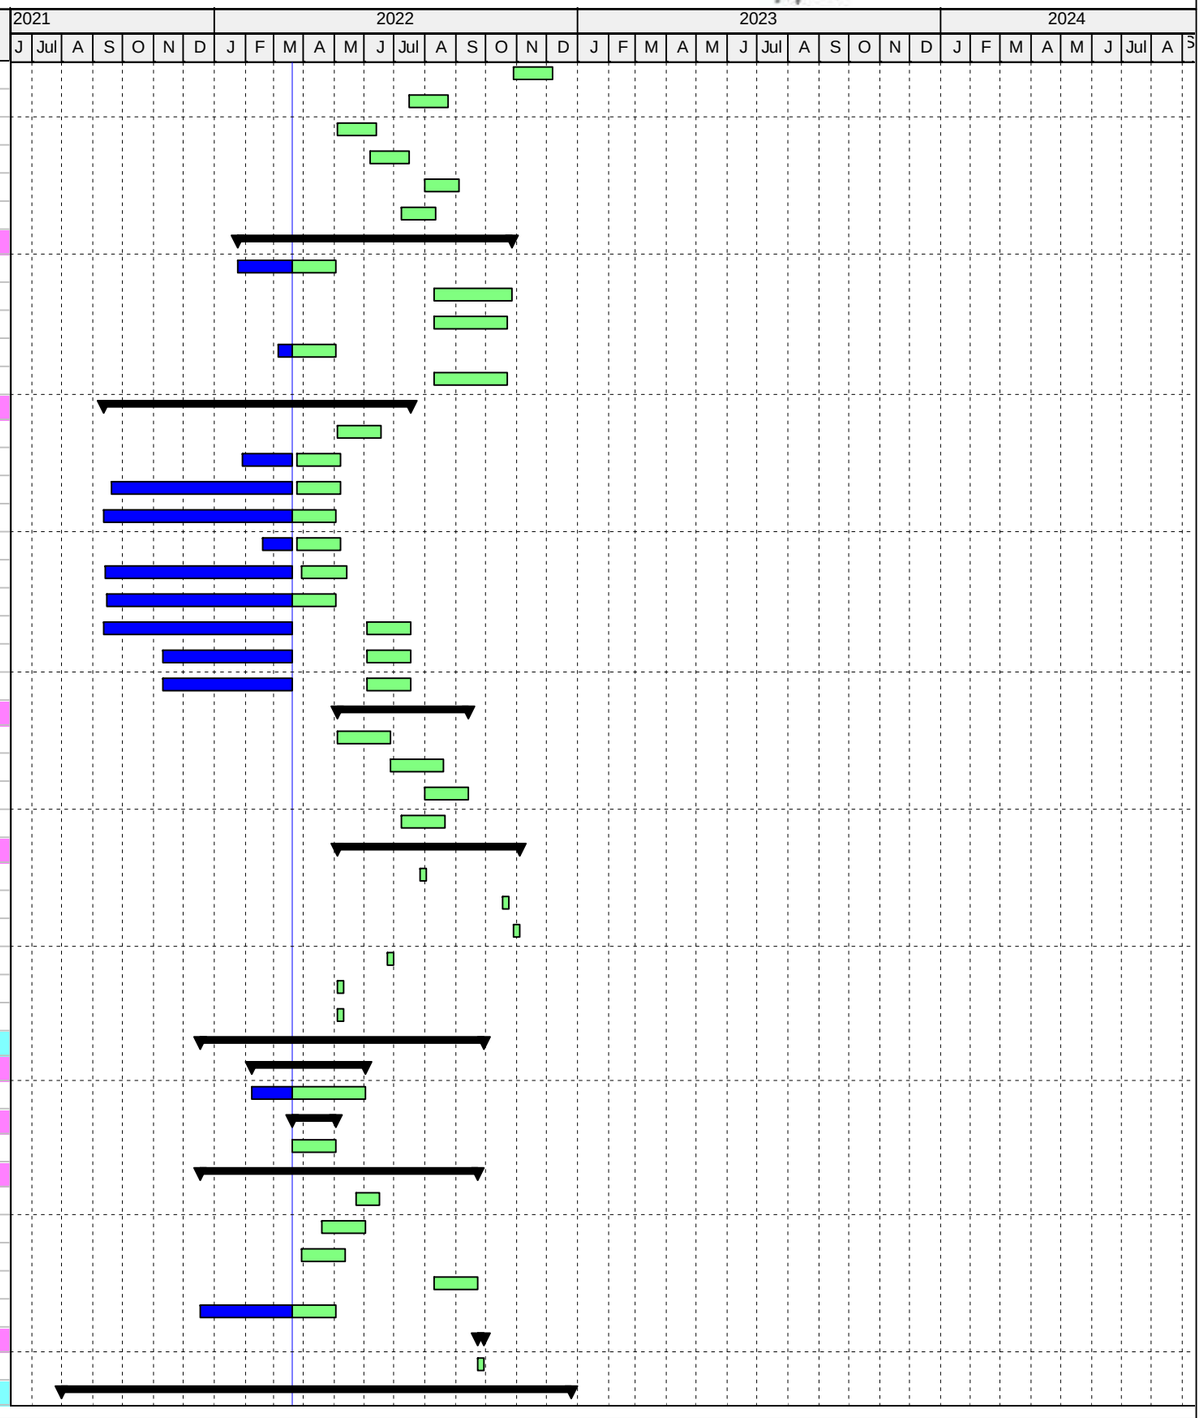


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Basis/Criteria		90	20%	$4.80	13-Feb-22	22-May-22
P06-E	Civil Design Criteria	64	60%	$1.60	13-Feb-22	22-May-22
P06-E	Design Criteria for Sewerage & Drainage	44	0%	$1.60	24-Mar-22	06-May-22
P06-E	Design Criteria for Road and Paving	44	0%	$1.60	27-Mar-22	09-May-22
Specification		94	72%	$24.15	09-Aug-21	06-Jun-22
P06-E	Specification For Civil Works	79	0%	$2.42	20-Mar-22	06-Jun-22
P06-E	Specification For Road & Paving	64	80%	$4.83	09-Aug-21	22-May-22
P06-E	Specification For Fence & Gate	64	100%	$4.83	18-Sep-21	20-Mar-22
P06-E	Specification For Earth Work	64	80%	$4.83	09-Aug-21	22-May-22
P06-E	Specification For Sewerage & Drainage	64	100%	$4.83	09-Aug-21	20-Mar-22
P06-E	Specification For Geological & Geotechnical Survey	44	0%	$2.42	20-Mar-22	02-May-22
Drawing/Diagram		167	17.13%	$1,026.02	01-Aug-21	02-Sep-22
P06-E	Standard Drawing For Civil Works	64	0%	$10.57	30-Mar-22	01-Jun-22
P06-E	Standard Drawing For Slope Protection Details	64	100%	$10.57	22-Aug-21	30-Mar-22
P06-E	Standard Drawing For Roads	64	80%	$10.57	22-Aug-21	01-Jun-22
P06-E	Standard Drawing For Electrical Cable Trench	64	100%	$10.57	22-Aug-21	30-Mar-22
P06-E	Standard Drawing For Manholes	64	80%	$10.57	22-Aug-21	01-Jun-22
P06-E	Standard Drawing For Catch Basins	64	80%	$10.57	22-Aug-21	05-Jun-22
P06-E	Standard Drawing For Sewerage & Drainage Details	64	60%	$10.57	02-Feb-22	05-Jun-22
P06-E	Standard Drawing For Civil Underground Crossings	38	60%	$17.96	07-Feb-22	10-May-22
P06-E	Standard Drawing For Fence & Gate Details	64	100%	$10.57	18-Sep-21	03-Apr-22
P06-E	Standard Drawing For Concrete Continues Weight	38	100%	$17.65	01-Aug-21	20-Mar-22
P06-E	Standard Drawing For Major Floodway Crossing	38	0%	$17.65	03-Apr-22	10-May-22
P06-E	Standard Drawing For Culvert & Details	38	100%	$17.65	25-Sep-21	03-Apr-22
P06-E	Standard Drawing For Valve Box	38	100%	$17.65	12-Jan-22	03-Apr-22
P06-E	Standard Drawing For Fire Hydrant Pit	38	60%	$17.65	13-Mar-22	10-May-22
P06-E	Standard Drawing For Cable Pull Pit	64	0%	$10.57	03-Apr-22	05-Jun-22
P06-E	Standard Drawing For Pavings	38	60%	$17.65	08-Jan-22	10-May-22
P06-E	Standard Drawing For Earth Pit	38	60%	$17.65	13-Feb-22	10-May-22
P06-E	Standard Detail For Pipe Bedding	64	100%	$10.57	22-Aug-21	03-Apr-22
P06-E	Standard Details of Miscellaneous Items	64	60%	$10.57	06-Mar-22	05-Jun-22
P06-E	BINAK Oil Field Project Overall Well Location/Facilities Layou	54	0%	$8.00	20-Mar-22	12-May-22
P06-E	General Civil Layout - W007S	64	0%	$267.59	28-Apr-22	30-Jun-22
P06-E	Civil and Structural drawings - W007S	64	0%	$267.59	01-Jul-22	02-Sep-22
P06-E	Rough Grading Plans -W007S	54	0%	$225.11	13-May-22	05-Jul-22
Calculation		282	40%	$123.23	05-Dec-21	25-Dec-22
P06-E	Calculation Note For Heli Pad, Well Pad & Diesel Storage Pa	38	0%	$61.61	03-Sep-22	10-Oct-22
P06-E	Calculation Note For Flood Control	39	80%	$61.61	05-Dec-21	25-Dec-22
Report		54	0%	$81.92	20-Mar-22	12-May-22
P06-E	Site Visit Report (Civil Work) - W007S & Manifold Extension	54	0%	$81.92	20-Mar-22	12-May-22
MTO		7	0%	$112.11	01-Jul-22	07-Jul-22
P06-E	MTO For Civil Works - W007S	7	0%	$112.11	01-Jul-22	07-Jul-22
Structure		238	8.51%	$1,524.71	08-Aug-21	12-Nov-22
Basis/Criteria		64	0%	$16.62	20-Mar-22	22-May-22
P06-E	Structural Design Criteria	64	0%	$5.54	20-Mar-22	22-May-22
P06-E	Design Criteria For Steel Structure	44	0%	$5.54	20-Mar-22	02-May-22
P06-E	Design Criteria For Load & Forces	44	0%	$5.54	20-Mar-22	02-May-22
Specification		98	84.92%	$127.01	14-Aug-21	26-May-22
P06-E	Specification For Concrete Work	64	80%	$12.29	14-Aug-21	26-May-22

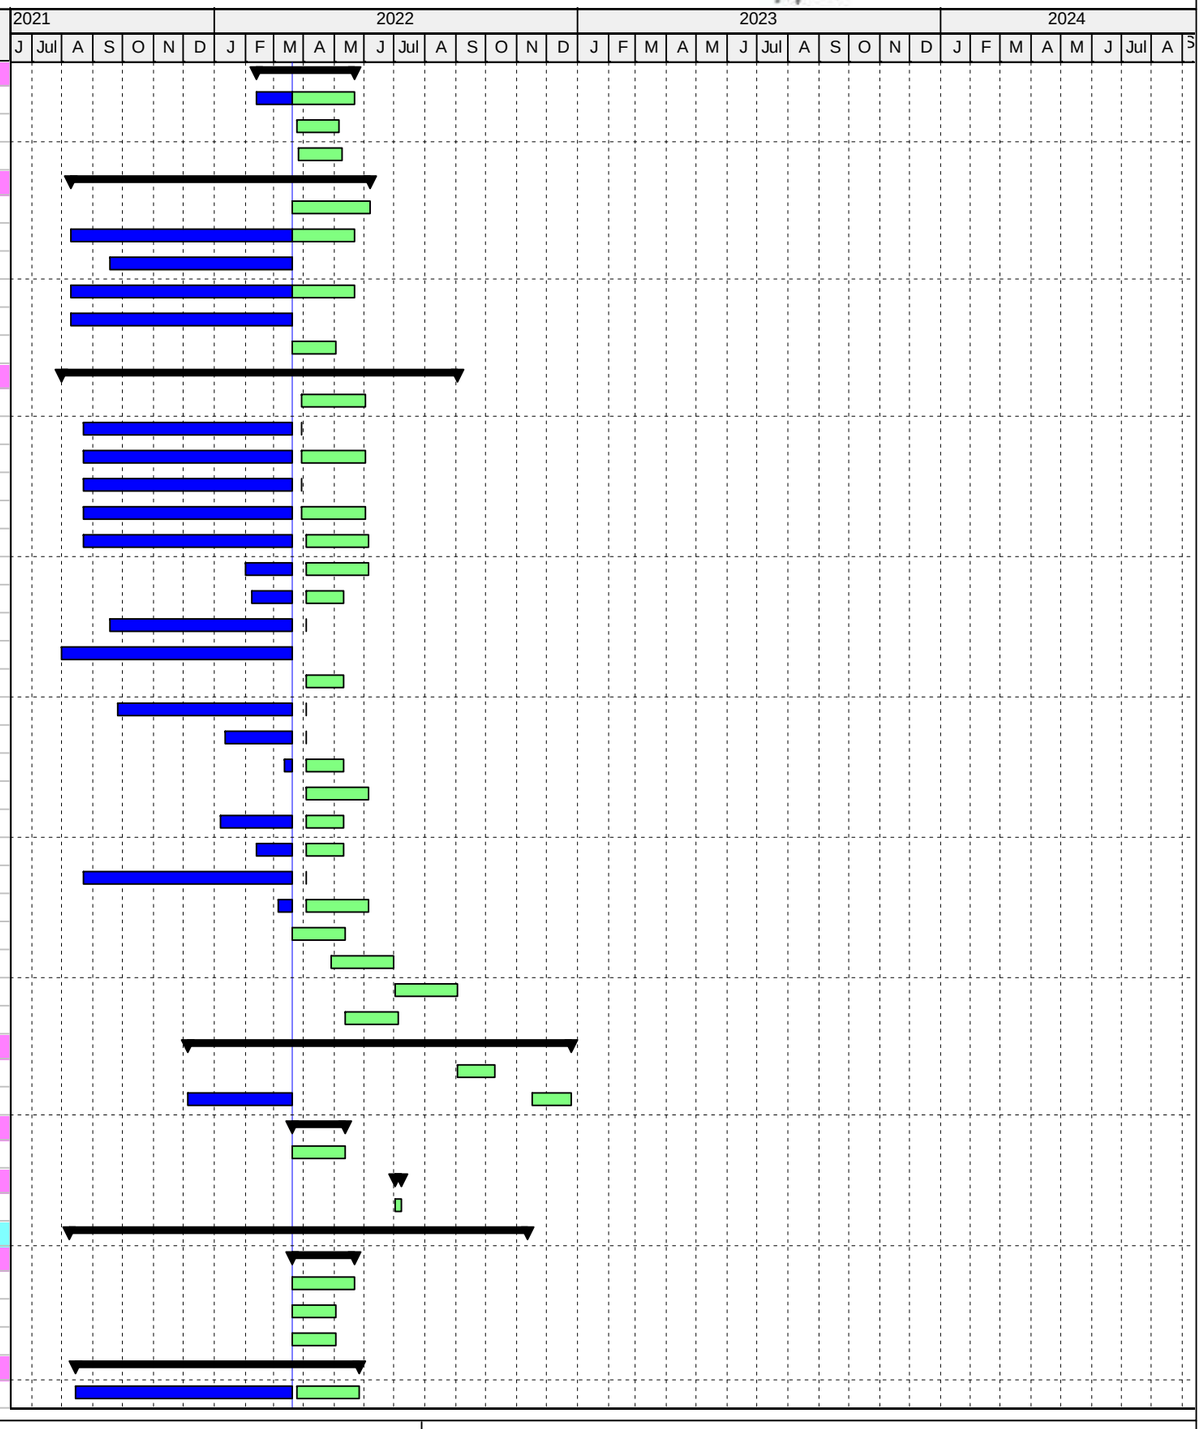


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Specification For Storage Tank Foundation	38	100%	$30.75	23-Nov-21	24-Mar-22
P06-E	Specification for Fabrication of Steel Structures	64	100%	$15.89	24-Jan-22	24-Mar-22
P06-E	Specification For Grouting	64	100%	$12.29	14-Aug-21	24-Mar-22
P06-E	Specification for Erection of Steel Structures	64	100%	$15.99	24-Jan-22	24-Mar-22
P06-E	Specification for Fireproofing	64	100%	$15.71	18-Sep-21	24-Mar-22
P06-E	Specification for Design of Blast Resistant Buildings	64	60%	$12.29	12-Dec-21	26-May-22
P06-E	Specification For Steel Structural Works	37	0%	$11.79	20-Mar-22	25-Apr-22
Drawing/Diagram		221	2.23%	$983.29	08-Aug-21	05-Nov-22
P06-E	Standard Drawing For Fire Proofing	64	100%	$1.38	08-Aug-21	03-Apr-22
P06-E	Standard Drawing For Anchor Bolts	64	100%	$1.38	15-Dec-21	03-Apr-22
P06-E	Standard Drawing For Steel Stairs	64	100%	$1.38	18-Dec-21	03-Apr-22
P06-E	Standard Drawing For Operating Platform	38	100%	$1.57	27-Dec-21	30-Mar-22
P06-E	Standard Drawing For Handrail	38	100%	$2.16	18-Dec-21	30-Mar-22
P06-E	Standard Drawing For Insert Plates in Concrete	38	100%	$2.16	08-Aug-21	30-Mar-22
P06-E	Standard Details For Ladder & Safety Cage	64	100%	$1.38	15-Dec-21	03-Apr-22
P06-E	Standard Drawing For Lighting pole foundation Plan & Details	38	60%	$2.16	29-Jan-22	06-May-22
P06-E	General Notes - Steel Structures	38	100%	$1.47	25-Jan-22	30-Mar-22
P06-E	General Notes - Reinforced Concrete Structures	38	100%	$2.16	20-Dec-21	30-Mar-22
P06-E	Standard Drawing For Structural Built-up Sections	44	80%	$2.16	04-Dec-21	12-May-22
P06-E	Standard Drawing For Steel Flooring, Grating and Chequere	44	100%	$2.16	05-Jan-22	30-Mar-22
P06-E	Concrete Reinforcement Shape Code	44	0%	$2.16	30-Mar-22	12-May-22
P06-E	Standard Drawing For Septic Tank	44	80%	$2.16	22-Jan-22	12-May-22
P06-E	Pipe Supports Foundation Drawing For Extension of Binak B/	66	0%	$73.35	28-Apr-22	02-Jul-22
P06-E	Pipe Supports Structure Drawing For Extension of Binak B/C	64	0%	$73.35	28-Apr-22	30-Jun-22
P06-E	Access Platforms Structure Plan & Details For Extension of Bi	66	0%	$59.00	28-Apr-22	02-Jul-22
P06-E	Access Platforms Foundation Drawing For Extension of Binak	44	0%	$59.00	28-Apr-22	10-Jun-22
P06-E	Fuel Oil Storage Drum Detail Drawing For Well Pads - W007S	44	0%	$59.00	04-May-22	16-Jun-22
P06-E	Foundation Drawing For Security Building For Well Pads - W	44	0%	$59.00	23-Sep-22	05-Nov-22
P06-E	Structural Drawing For Security Building For Well Pads - W0(	44	0%	$59.00	23-Sep-22	05-Nov-22
P06-E	Foundation Drawing For Switchgear Building For Well Pads -	44	0%	$59.00	13-May-22	25-Jun-22
P06-E	Structural Drawing For Switchgear Building For Well Pads - V	44	0%	$59.00	13-May-22	25-Jun-22
P06-E	Foundation Drawing For Potable Water Tank For Well Pads	44	0%	$59.00	09-May-22	21-Jun-22
P06-E	Foundation Drawing For Diesel Generator Shelter For Well F	44	0%	$59.00	18-Aug-22	30-Sep-22
P06-E	Structural Drawing For Diesel Generator Shelter For Well Pa	44	0%	$59.00	18-Aug-22	30-Sep-22
P06-E	Platform Structure Drawing - W007S	44	0%	$43.76	23-Jun-22	05-Aug-22
P06-E	Foundation Drawing For Oil Pump	44	0%	$59.00	28-May-22	10-Jul-22
P06-E	Sump Pit Structural Drawing for Oil Pump	44	0%	$59.00	13-Jun-22	26-Jul-22
P06-E	Foundation Drawing For Transmission Line Tower - W007S	44	0%	$59.00	06-Aug-22	18-Sep-22
MTO		7	0%	$397.80	06-Nov-22	12-Nov-22
P06-E	MTO For Structural Works - W007S & Manifold Extension	7	0%	$397.80	06-Nov-22	12-Nov-22
General		201	12.06%	$3,049.42	11-Aug-21	06-Oct-22
Risk Assessment		44	100%	$152.47	05-Sep-21	20-Mar-22
Procedure/Plan		44	100%	$152.47	05-Sep-21	20-Mar-22
P06-	HAZOP Study Procedure	44	100%	$53.04	25-Oct-21	20-Mar-22
P06-	HAZID Study Procedure	44	100%	$19.88	05-Sep-21	20-Mar-22
P06-	SIL Study Procedure	44	100%	$79.54	25-Oct-21	20-Mar-22
Survey (Topography) & Geotechnic		201	7.06%	$2,592.01	11-Aug-21	06-Oct-22
Geotechnic		104	8%	$2,287.07	11-Aug-21	02-May-22
Procedure/Plan		44	100%	$182.97	11-Aug-21	19-Apr-22

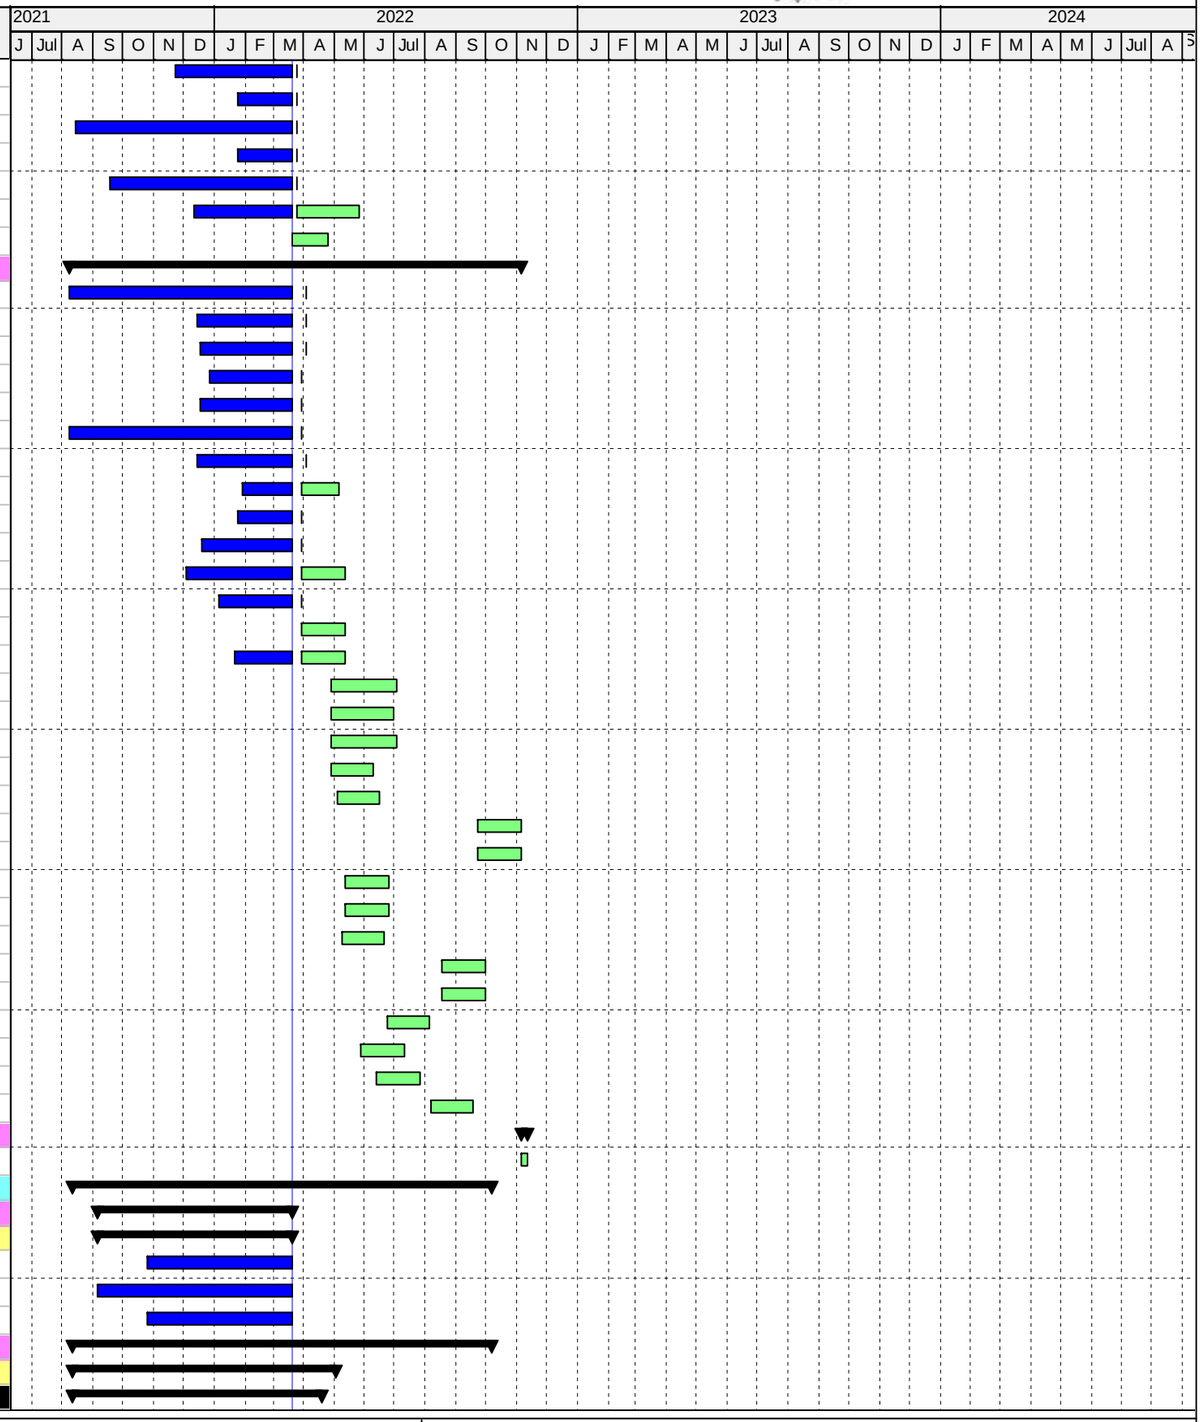


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06	Geotechnical Investigation Plan for Well Pads	44	100%	$182.97	11-Aug-21	19-Apr-22
Report		44	0%	$2,104.10	20-Mar-22	02-May-22
P06	Geotechnical Investigation Report - W007S	44	0%	$2,104.10	20-Mar-22	02-May-22
Survey		93	0%	$304.94	06-Jul-22	06-Oct-22
Drawing/Diagram		93	0%	$304.94	06-Jul-22	06-Oct-22
P06	Flowline Plan & Profile Drawings - W007S	46	0%	$152.47	22-Aug-22	06-Oct-22
P06	Over Head Line Plan and Profile - W007S	39	0%	$152.47	06-Jul-22	13-Aug-22
QC/QA		116	10.59%	$304.94	20-Sep-21	13-Jul-22
QC Management		116	39%	$24.79	08-Dec-21	13-Jul-22
P06-	Project Audit Procedure	44	0%	$1.24	20-Mar-22	02-May-22
P06-	Specification For Final Data Book (FDB) Requirements	44	0%	$1.24	20-Mar-22	02-May-22
P06-	Non Conformance Control Procedure	36	0%	$1.24	03-May-22	07-Jun-22
P06-	Corrective Action Procedure	36	0%	$1.24	08-Jun-22	13-Jul-22
P06-	Material Reciving, Storage, Handling Procedure	39	60%	$1.24	20-Feb-22	27-Apr-22
P06-	Packing, Marking, Transportation Procedure	39	0%	$1.24	20-Mar-22	27-Apr-22
P06-	Criticality Assessment Procedure	39	0%	$4.96	20-Mar-22	27-Apr-22
P06-	Project Quality Plan	44	80%	$11.16	08-Dec-21	02-May-22
P06-	Technical Query Procedure	44	0%	$1.24	30-Mar-22	12-May-22
QC General Document		55	8.58%	$36.20	28-Nov-21	16-May-22
P06-	Quality Control Plan (QCP)	39	60%	$5.18	28-Nov-21	27-Apr-22
P06-	Specification for Welding Procedure	44	0%	$5.18	03-Apr-22	16-May-22
P06-	Heat Treatment Procedure (Pre Heating , PWHT)	44	0%	$5.18	03-Apr-22	16-May-22
P06-	Welder Performance Qualification Test (WQT) Procedure	44	0%	$5.18	03-Apr-22	16-May-22
P06-	NDT Procedure	44	0%	$5.18	03-Apr-22	16-May-22
P06-	Surface Preparation and Coating/Painting Procedure	44	0%	$5.18	03-Apr-22	16-May-22
P06-	Control of Inspection Measuring and Test Equipment Procedu	44	0%	$5.14	03-Apr-22	16-May-22
QC Discipline Document		81	8%	$243.95	20-Sep-21	16-May-22
Piping		51	0%	$60.99	27-Mar-22	16-May-22
P06	ITP For Piping Works	44	0%	$6.10	27-Mar-22	09-May-22
P06	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$6.86	03-Apr-22	16-May-22
P06	PIPING WPS (Welding Procedure Specification)	44	0%	$6.86	03-Apr-22	16-May-22
P06	PIPING PQR (Procedure Qualification Record)	44	0%	$6.86	03-Apr-22	16-May-22
P06	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$6.86	03-Apr-22	16-May-22
P06	PIPING WPS (Preliminary Welding Procedure Specification) f	44	0%	$6.86	03-Apr-22	16-May-22
P06	PIPING PQR (Procedure Qualification Record) for Repair We	44	0%	$6.86	03-Apr-22	16-May-22
P06	Field Joint Coating Procedure For Pipeline	44	0%	$6.86	03-Apr-22	16-May-22
P06	Pressure Test Procedure	44	0%	$6.86	03-Apr-22	16-May-22
Telecomm.		44	0%	$12.20	27-Mar-22	09-May-22
P06	ITP For Telecommunication Installation	44	0%	$12.20	27-Mar-22	09-May-22
Safety		44	0%	$12.20	27-Mar-22	09-May-22
P06	ITP For Safety Installation	44	0%	$12.20	27-Mar-22	09-May-22
Architectural		44	0%	$12.20	27-Mar-22	09-May-22
P06	ITP For Architectural Works	44	0%	$12.20	27-Mar-22	09-May-22
Mechanical		44	0%	$12.20	27-Mar-22	09-May-22
P06	ITP For Mechanical Installation	44	0%	$12.20	27-Mar-22	09-May-22
Structure		51	0%	$48.79	27-Mar-22	16-May-22
P06	ITP For Steel Structural Works	44	0%	$4.88	27-Mar-22	09-May-22
P06	Steel Structure WPS (Welding Procedure Specification)	44	0%	$7.32	03-Apr-22	16-May-22
P06	Steel Structure PQR (Procedure Qualification Record)	44	0%	$7.32	03-Apr-22	16-May-22

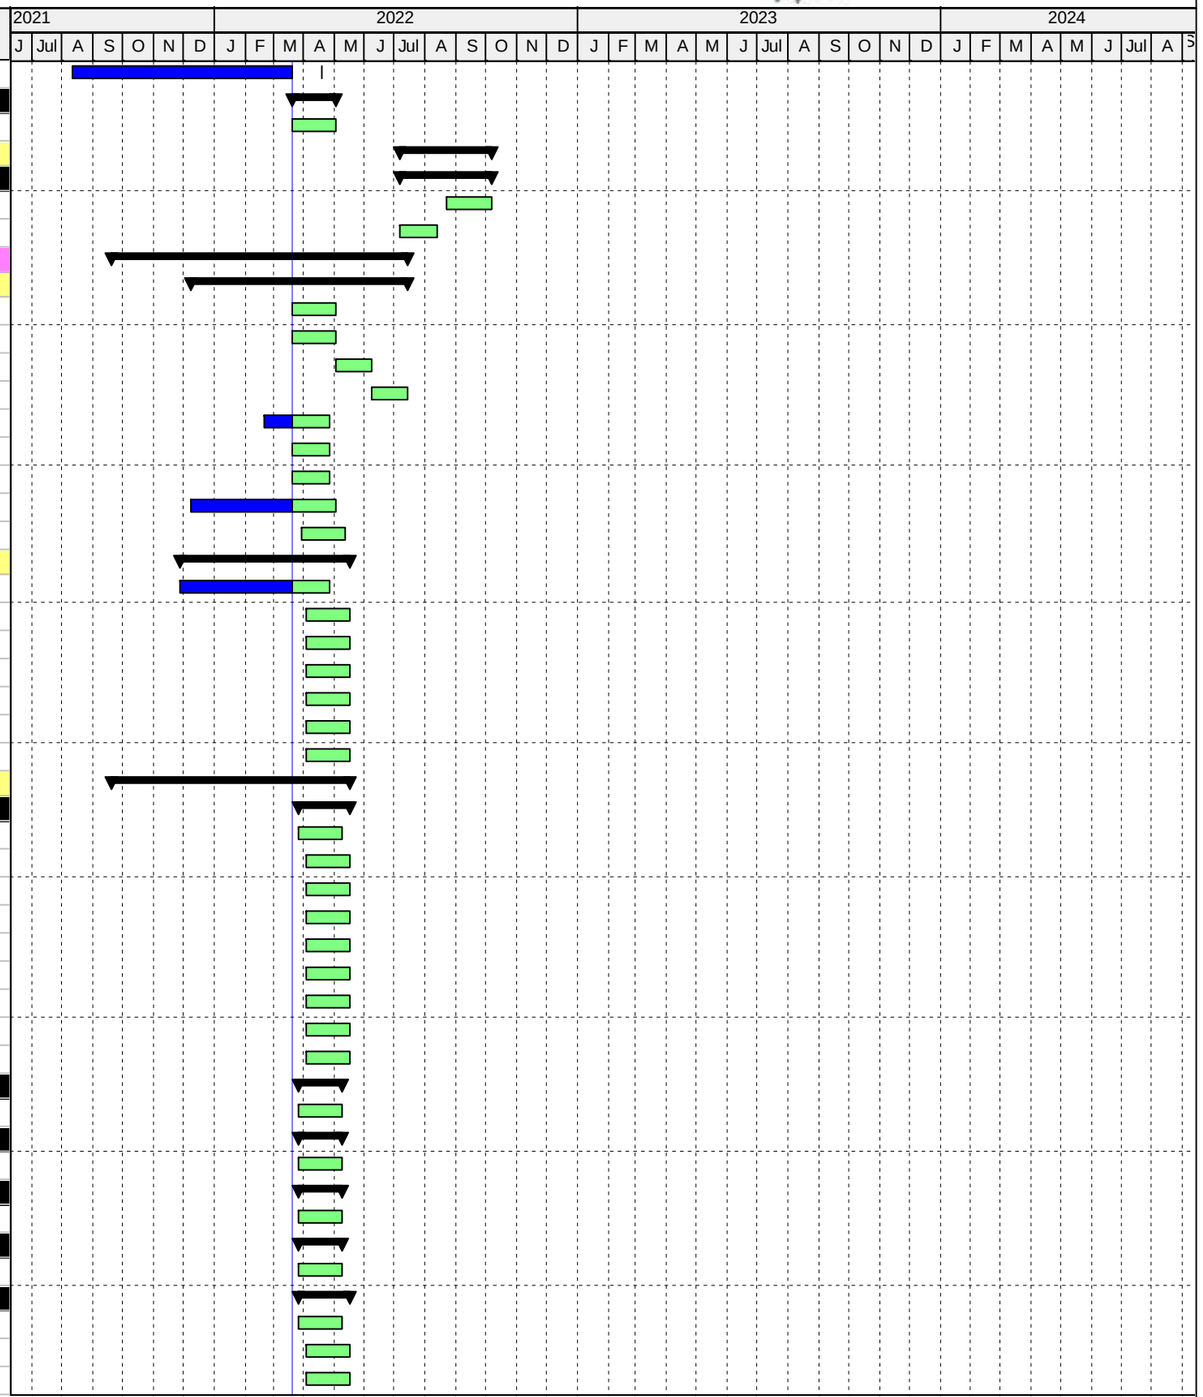

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06	Steel Structure WPS (Welding Procedure Specification) For F	44	0%	$7.32	03-Apr-22	16-May-22
P06	Steel Structure PQR (Procedure Qualification Record) For Re	44	0%	$7.32	03-Apr-22	16-May-22
P06	Weld Map For Steel Structures	44	0%	$7.32	03-Apr-22	16-May-22
P06	NDT Plan For steel Structures	44	0%	$7.32	03-Apr-22	16-May-22
Instrumentation		44	0%	$12.20	27-Mar-22	09-May-22
P06	ITP For I&C Installation	44	0%	$12.20	27-Mar-22	09-May-22
Pipeline		74	15%	$48.79	16-Jan-22	16-May-22
P06	ITP For Pipeline	44	60%	$4.88	16-Jan-22	09-May-22
P06	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	60%	$7.32	23-Feb-22	16-May-22
P06	PIPELINE WPS (Welding Procedure Specification)	44	0%	$7.32	03-Apr-22	16-May-22
P06	PIPELINE PQR (Procedure Qualification Record)	44	0%	$7.32	03-Apr-22	16-May-22
P06	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	0%	$7.32	03-Apr-22	16-May-22
P06	PIPELINE WPS (Preliminary Welding Procedure Specificatior	44	0%	$7.32	03-Apr-22	16-May-22
P06	PIPELINE PQR (Procedure Qualification Record) for Repair \	44	0%	$7.32	03-Apr-22	16-May-22
Civil		44	100%	$12.20	20-Sep-21	27-Mar-22
P06	ITP For Civil Works	44	100%	$12.20	20-Sep-21	27-Mar-22
Electrical		44	0%	$12.20	27-Mar-22	09-May-22
P06	ITP For Electrical Installation	44	0%	$12.20	27-Mar-22	09-May-22
Procurement Engineering		454	0.98%	$2,772.20	16-Jan-22	16-Jun-23
Mechanical		175	0%	$325.18	03-May-22	24-Oct-22
Potable Tank		109	0%	$117.75	08-Jul-22	24-Oct-22
P06-E	PMR For Potable Tanks - W007S	15	0%	$11.77	08-Jul-22	22-Jul-22
P06-E	TBE For Potable Tanks - W007S	30	0%	$17.66	15-Jul-22	13-Aug-22
P06-E	VDR For Potable Tanks - W007S	7	0%	$88.31	18-Oct-22	24-Oct-22
Pump		32	0%	$89.68	03-May-22	03-Jun-22
P06-E	PMR For Pumps - Extension of Binak B/C Manifold	10	0%	$8.97	03-May-22	12-May-22
P06-E	TBE For Pumps - Extension of Binak B/C Manifold	20	0%	$13.45	10-May-22	29-May-22
P06-E	VDR For Pumps - Extension of Binak B/C Manifold	7	0%	$67.26	28-May-22	03-Jun-22
Drum		109	0%	$117.75	03-Jul-22	19-Oct-22
P06-E	PMR For Drums - W007S	10	0%	$11.77	03-Jul-22	12-Jul-22
P06-E	TBE For Drums - W007S	30	0%	$17.66	10-Jul-22	08-Aug-22
P06-E	VDR For Drums - W007S	7	0%	$88.31	13-Oct-22	19-Oct-22
HVAC		79	0%	$106.45	30-Mar-23	16-Jun-23
Main HVAC Equipment		79	0%	$106.45	30-Mar-23	16-Jun-23
P06-E	PMR For Main HVAC Equipment - W007S	10	0%	$10.65	30-Mar-23	08-Apr-23
P06-E	TBE For Main HVAC Equipment - W007S	30	0%	$15.97	06-Apr-23	05-May-23
P06-E	VDR For Main HVAC Equipment - W007S	7	0%	$79.84	10-Jun-23	16-Jun-23
Piping		232	0%	$261.14	29-Apr-22	16-Dec-22
Pipes		60	0%	$29.04	18-Sep-22	16-Nov-22
P06-E	PMR For Pipes - W007S	5	0%	$2.90	18-Sep-22	22-Sep-22
P06-E	TBE For Pipes - W007S	10	0%	$4.36	25-Sep-22	04-Oct-22
P06-E	VDR For Pipes - W007S	7	0%	$21.78	10-Nov-22	16-Nov-22
Stone Trap		59	0%	$29.01	13-May-22	10-Jul-22
P06-E	PMR For Stone Trap - W007S	7	0%	$2.90	13-May-22	19-May-22
P06-E	TBE For Stone Trap - W007S	10	0%	$4.35	20-May-22	29-May-22
P06-E	VDR For Stone Trap - W007S	7	0%	$21.76	04-Jul-22	10-Jul-22
Bolt & Nuts		59	0%	$29.01	18-Oct-22	15-Dec-22
P06-E	PMR For Bolt/Nuts - W007S	7	0%	$2.90	18-Oct-22	24-Oct-22
P06-E	TBE For Bolt/Nuts - W007S	10	0%	$4.35	25-Oct-22	03-Nov-22
P06-E	VDR For Bolt/Nuts - W007S	7	0%	$21.76	09-Dec-22	15-Dec-22




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Flanges		60	0%	$29.01	18-Oct-22	16-Dec-22
P06-E	PMR For Flanges - W007S	7	0%	$2.90	18-Oct-22	24-Oct-22
P06-E	TBE For Flanges - W007S	10	0%	$4.35	25-Oct-22	03-Nov-22
P06-E	VDR For Flanges - W007S	7	0%	$21.76	10-Dec-22	16-Dec-22
Sampling Connection		59	0%	$29.01	29-Apr-22	26-Jun-22
P06-E	PMR For Sampling Connection Set - W007S	7	0%	$2.90	29-Apr-22	05-May-22
P06-E	TBE For Sampling Connection - W007S	10	0%	$4.35	06-May-22	15-May-22
P06-E	VDR For Sampling Connection - W007S	7	0%	$21.76	20-Jun-22	26-Jun-22
Manual Valves		49	0%	$29.01	18-Oct-22	05-Dec-22
P06-E	PMR For Manual Valves - W007S	7	0%	$2.90	18-Oct-22	24-Oct-22
P06-E	TBE For Manual Valves - W007S	10	0%	$4.35	25-Oct-22	03-Nov-22
P06-E	VDR For Manual Valves - W007S	7	0%	$21.76	29-Nov-22	05-Dec-22
Gaskets		60	0%	$29.01	18-Oct-22	16-Dec-22
P06-E	PMR For Gaskets - W007S	7	0%	$2.90	18-Oct-22	24-Oct-22
P06-E	TBE For Gaskets - W007S	10	0%	$4.35	25-Oct-22	03-Nov-22
P06-E	VDR For Gaskets - W007S	7	0%	$21.76	10-Dec-22	16-Dec-22
Fittings		60	0%	$29.01	18-Oct-22	16-Dec-22
P06-E	PMR For Fittings - W007S	7	0%	$2.90	18-Oct-22	24-Oct-22
P06-E	TBE For Fitting - W007S	10	0%	$4.35	25-Oct-22	03-Nov-22
P06-E	VDR For Fitting - W007S	7	0%	$21.76	10-Dec-22	16-Dec-22
Pipe Support		54	0%	$29.01	25-Sep-22	17-Nov-22
P06-E	PMR For Pipe Support - W007S	5	0%	$2.90	25-Sep-22	29-Sep-22
P06-E	TBE For Pipe Support - W007S	5	0%	$4.35	02-Oct-22	06-Oct-22
P06-E	VDR For Pipe Support - W007S	7	0%	$21.76	11-Nov-22	17-Nov-22
Pipeline		111	7.51%	$33.27	19-Feb-22	30-Jun-22
Line Pipe		67	15.03%	$16.63	19-Feb-22	30-Jun-22
P06-E	PMR For Line Pipes - W007S	10	0%	$1.66	03-May-22	12-May-22
P06-E	TBE For Line Pipes - W007S	30	100%	$2.49	19-Feb-22	20-May-22
P06-E	VDR For Line Pipes - W007S	7	0%	$12.47	24-Jun-22	30-Jun-22
Flow Line Support		103	0%	$16.63	20-Mar-22	30-Jun-22
P06-E	PMR For Flowline Support - W007S	5	0%	$1.66	20-Mar-22	24-Mar-22
P06-E	TBE For Flowline Support - W007S	5	0%	$2.49	27-Mar-22	31-Mar-22
P06-E	VDR For Flowline Support - W007S	7	0%	$12.47	24-Jun-22	30-Jun-22
Control & Instrumentation		229	2.31%	$1,066.47	16-Jan-22	11-Dec-22
Instrument Tube and Fitting		94	0%	$44.79	15-Jun-22	16-Sep-22
P06-E	PMR For Instrument Tube and Fitting - Manifold & W007S	10	0%	$4.48	15-Jun-22	24-Jun-22
P06-E	TBE/TBA For Instrument Tube and Fitting - Manifold & W007S	15	0%	$6.72	22-Jun-22	06-Jul-22
P06-E	VDR/TBA For Instrument Tube and Fitting - Manifold & W007S	7	0%	$33.59	10-Sep-22	16-Sep-22
Instrument Cable Tray		94	0%	$44.79	08-Sep-22	10-Dec-22
P06-E	PMR For Instrument Cable Tray/Ladder - Manifold & W007S	10	0%	$4.48	08-Sep-22	17-Sep-22
P06-E	TBE/TBA For Instrument Cable Tray/Ladder - Manifold & W0	15	0%	$6.72	15-Sep-22	29-Sep-22
P06-E	VDR/TBA For Instrument Cable Tray/Ladder - Manifold & WC	7	0%	$33.59	04-Dec-22	10-Dec-22
Differential Pressure/Pressure Gauge		227	10.01%	$44.79	16-Jan-22	11-Dec-22
P06-E	PMR For Differential Pressure/Pressure Gauge - Manifold & \	10	100%	$4.48	16-Jan-22	29-Apr-22
P06-E	TBE/TBA For Differential Pressure/Pressure Gauge - Manifol	15	0%	$6.72	29-Apr-22	13-May-22
P06-E	VDR/TBA For Differential Pressure/Pressure Gauge - Manifol	7	0%	$33.59	05-Dec-22	11-Dec-22
Instrument/F&G Junction box and Gland		29	0%	$44.79	12-Oct-22	09-Nov-22
P06-E	PMR For Instrument/F&G Junction box and Gland - Extensio	10	0%	$4.48	12-Oct-22	21-Oct-22
P06-E	TBE/TBA For Instrument/F&G Junction box and Gland - Exte	15	0%	$6.72	19-Oct-22	02-Nov-22

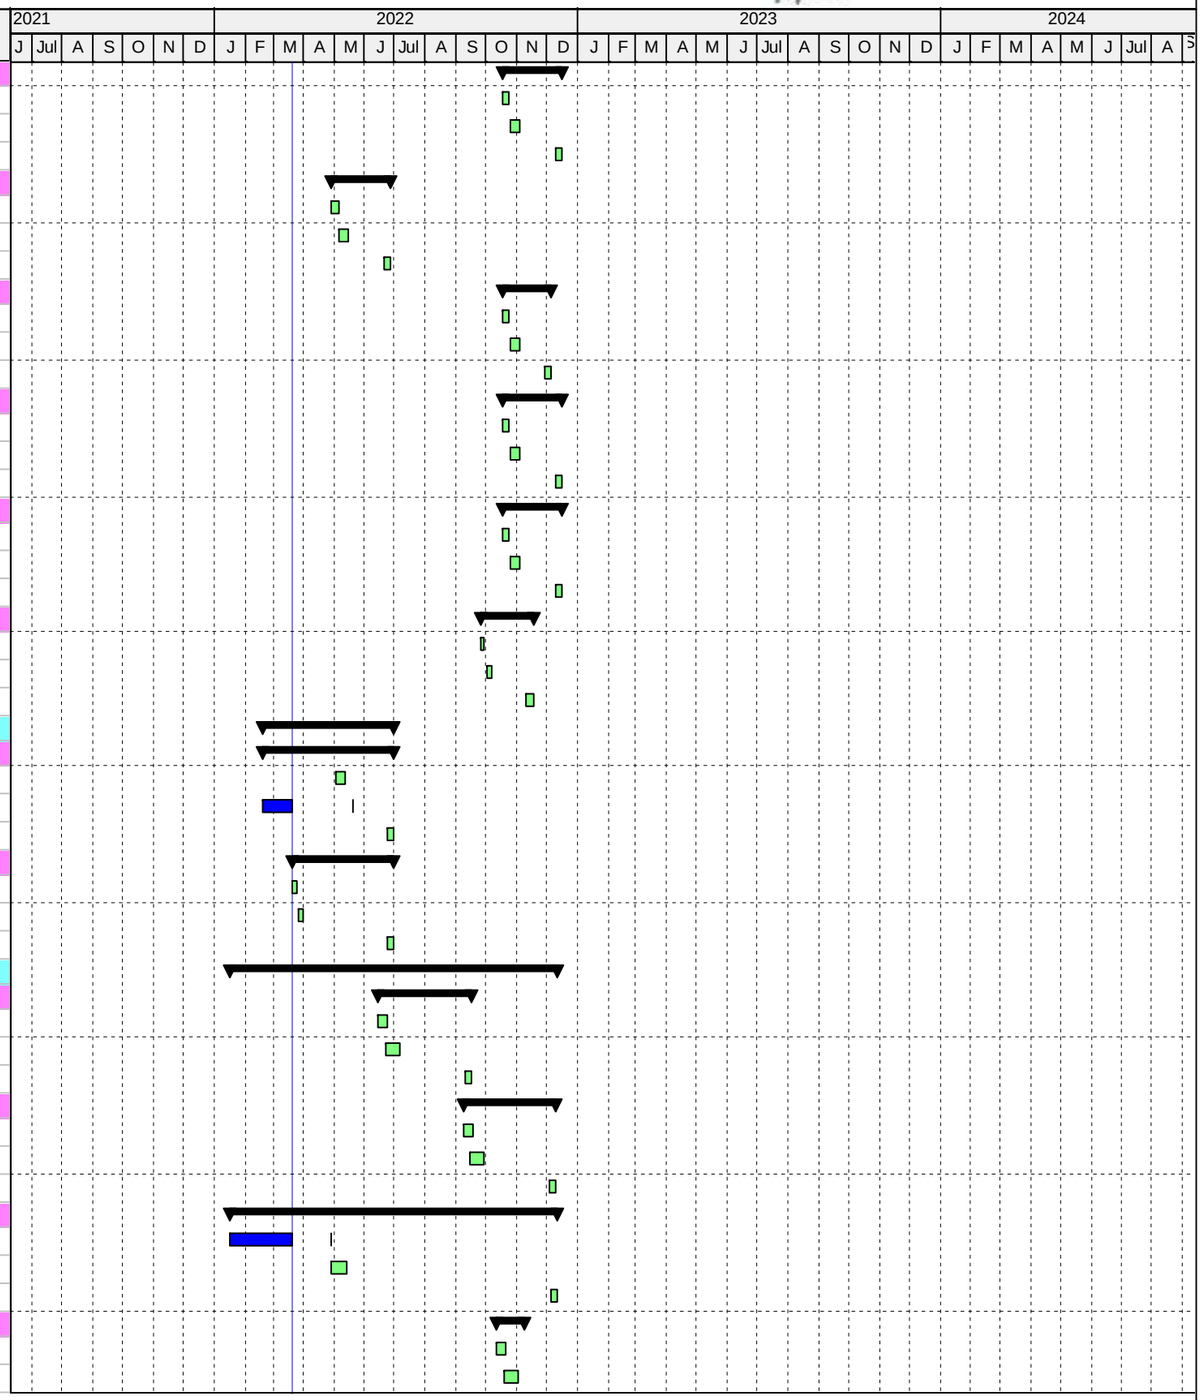


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	VDR/TBA For Instrument/F&G Junction box and Gland - Exte	7	0%	$33.59	03-Nov-22	09-Nov-22
Instrument Installation Accessories		29	0%	$44.79	08-Sep-22	06-Oct-22
P06-E	PMR For Bulk Item and Installation Accessories - Extension of	10	0%	$4.48	08-Sep-22	17-Sep-22
P06-E	TBE/TBA For Bulk Item and Installation Accessories - Extensic	15	0%	$6.72	15-Sep-22	29-Sep-22
P06-E	VDR/TBA For Bulk Item and Installation Accessories - Extensi	7	0%	$33.59	30-Sep-22	06-Oct-22
Temperature Gauge		128	10.01%	$44.79	16-Jan-22	17-Aug-22
P06-E	PMR For Temperature Gauge - Manifold & W007S	10	100%	$4.48	16-Jan-22	23-May-22
P06-E	TBE/TBA For Temperature Gauge - Manifold & W007S	15	0%	$6.72	23-May-22	06-Jun-22
P06-E	VDR/TBA For Temperature Gauge - Manifold & W007S	7	0%	$33.59	11-Aug-22	17-Aug-22
Pressure Transmitter		75	10.01%	$44.79	16-Jan-22	24-Jun-22
P06-E	PMR For Pressure Transmitter/Pressure Switch - Extension o	10	100%	$4.48	16-Jan-22	03-Jun-22
P06-E	TBE/TBA For Pressure Transmitter/Pressure Switch - Extensi	15	0%	$6.72	03-Jun-22	17-Jun-22
P06-E	VDR/TBA For Pressure Transmitter/Pressure Switch - Extens	7	0%	$33.59	18-Jun-22	24-Jun-22
Flow Transmitter/ Diff. Pressure Transmitter - Extension of Binal		110	10.01%	$44.79	16-Jan-22	20-May-22
P06-E	PMR For Flow Transmitter/ Diff. Pressure Transmitter - Exter	10	100%	$4.48	16-Jan-22	29-Apr-22
P06-E	TBE/TBA For Flow Transmitter/ Diff. Pressure Transmitter - E	15	0%	$6.72	29-Apr-22	13-May-22
P06-E	VDR/TBA For Flow Transmitter/ Diff. Pressure Transmitter - E	7	0%	$33.59	14-May-22	20-May-22
Corrosion Coupon/Probe		74	0%	$44.79	29-Apr-22	11-Jul-22
P06-E	PMR For Corrosion Coupon/Probe - Extension of Binak B/C M	10	0%	$4.48	29-Apr-22	08-May-22
P06-E	TBE/TBA For Corrosion Coupon/Probe - Extension of Binak E	15	0%	$6.72	06-May-22	20-May-22
P06-E	VDR/TBA For Corrosion Coupon/Probe - Extension of Binak I	7	0%	$33.59	05-Jul-22	11-Jul-22
Instrument/F&G Cable		29	0%	$44.79	17-Oct-22	14-Nov-22
P06-E	PMR For Instrument/F&G Cable - Extension of Binak B/C Ma	10	0%	$4.48	17-Oct-22	26-Oct-22
P06-E	TBE/TBA For Instrument/F&G Cable - Extension of Binak B/C	15	0%	$6.72	24-Oct-22	07-Nov-22
P06-E	VDR/TBA For Instrument/F&G Cable - Extension of Binak B/C	7	0%	$33.59	08-Nov-22	14-Nov-22
Orifice and Restriction Orifice Plate		29	0%	$44.79	03-May-22	31-May-22
P06-E	PMR For Orifice and Restriction Orifice Plate - Extension of B	10	0%	$4.48	03-May-22	12-May-22
P06-E	TBE/TBA For Orifice and Restriction Orifice Plate - Extension	15	0%	$6.72	10-May-22	24-May-22
P06-E	VDR/TBA For Orifice and Restriction Orifice Plate - Extension	7	0%	$33.59	25-May-22	31-May-22
Control Valves		108	9.99%	$67.61	14-Mar-22	05-Jul-22
P06-E	PMR For Control Valves - Extension of Binak B/C Manifold	10	100%	$6.76	14-Mar-22	13-Jun-22
P06-E	TBE/TBA For Control Valves - Extension of Binak B/C Manifol	15	0%	$10.14	14-Jun-22	28-Jun-22
P06-E	VDR/TBA For Control Valves - Extension of Binak B/C Manifo	7	0%	$50.71	29-Jun-22	05-Jul-22
Pressure Safety Valves (PSV)		29	0%	$67.61	13-Jun-22	11-Jul-22
P06-E	PMR For Pressure Safety Valves (PSV) - Extension of Binak I	10	0%	$6.76	13-Jun-22	22-Jun-22
P06-E	TBE/TBA For Pressure Safety Valves (PSV) - Extension of Bi	15	0%	$10.14	20-Jun-22	04-Jul-22
P06-E	VDR/TBA For Pressure Safety Valves (PSV) - Extension of Bi	7	0%	$50.71	05-Jul-22	11-Jul-22
F&G Devices		29	0%	$67.61	13-Jul-22	10-Aug-22
P06-E	PMR For F&G Detector - Extension of Binak B/C Manifold	10	0%	$6.76	13-Jul-22	22-Jul-22
P06-E	TBE/TBA For F&G Detector - Extension of Binak B/C Manifol	15	0%	$10.14	20-Jul-22	03-Aug-22
P06-E	VDR/TBA For F&G Detector - Extension of Binak B/C Manifol	7	0%	$50.71	04-Aug-22	10-Aug-22
Control System/Console/Furniture		54	0%	$86.28	29-Apr-22	21-Jun-22
P06-E	PMR For Control System/Console/Furniture - Extension of Bi	10	0%	$8.63	29-Apr-22	08-May-22
P06-E	TBE/TBA For Control System/Console/Furniture - Extension c	15	0%	$12.94	06-May-22	20-May-22
P06-E	VDR/TBA For Control System/Console/Furniture - Extension	7	0%	$64.71	15-Jun-22	21-Jun-22
ON/OFF & Shutdown Valves		64	0%	$67.29	01-May-22	03-Jul-22
P06-E	PMR For ON/OFF & Shutdown Valves - Extension of Binak B	10	0%	$6.73	01-May-22	10-May-22
P06-E	TBE/TBA For ON/OFF & Shutdown Valves - Extension of Bin	15	0%	$10.09	08-May-22	22-May-22
P06-E	VDR/TBA For ON/OFF & Shutdown Valves - Extension of Bir	7	0%	$50.47	27-Jun-22	03-Jul-22

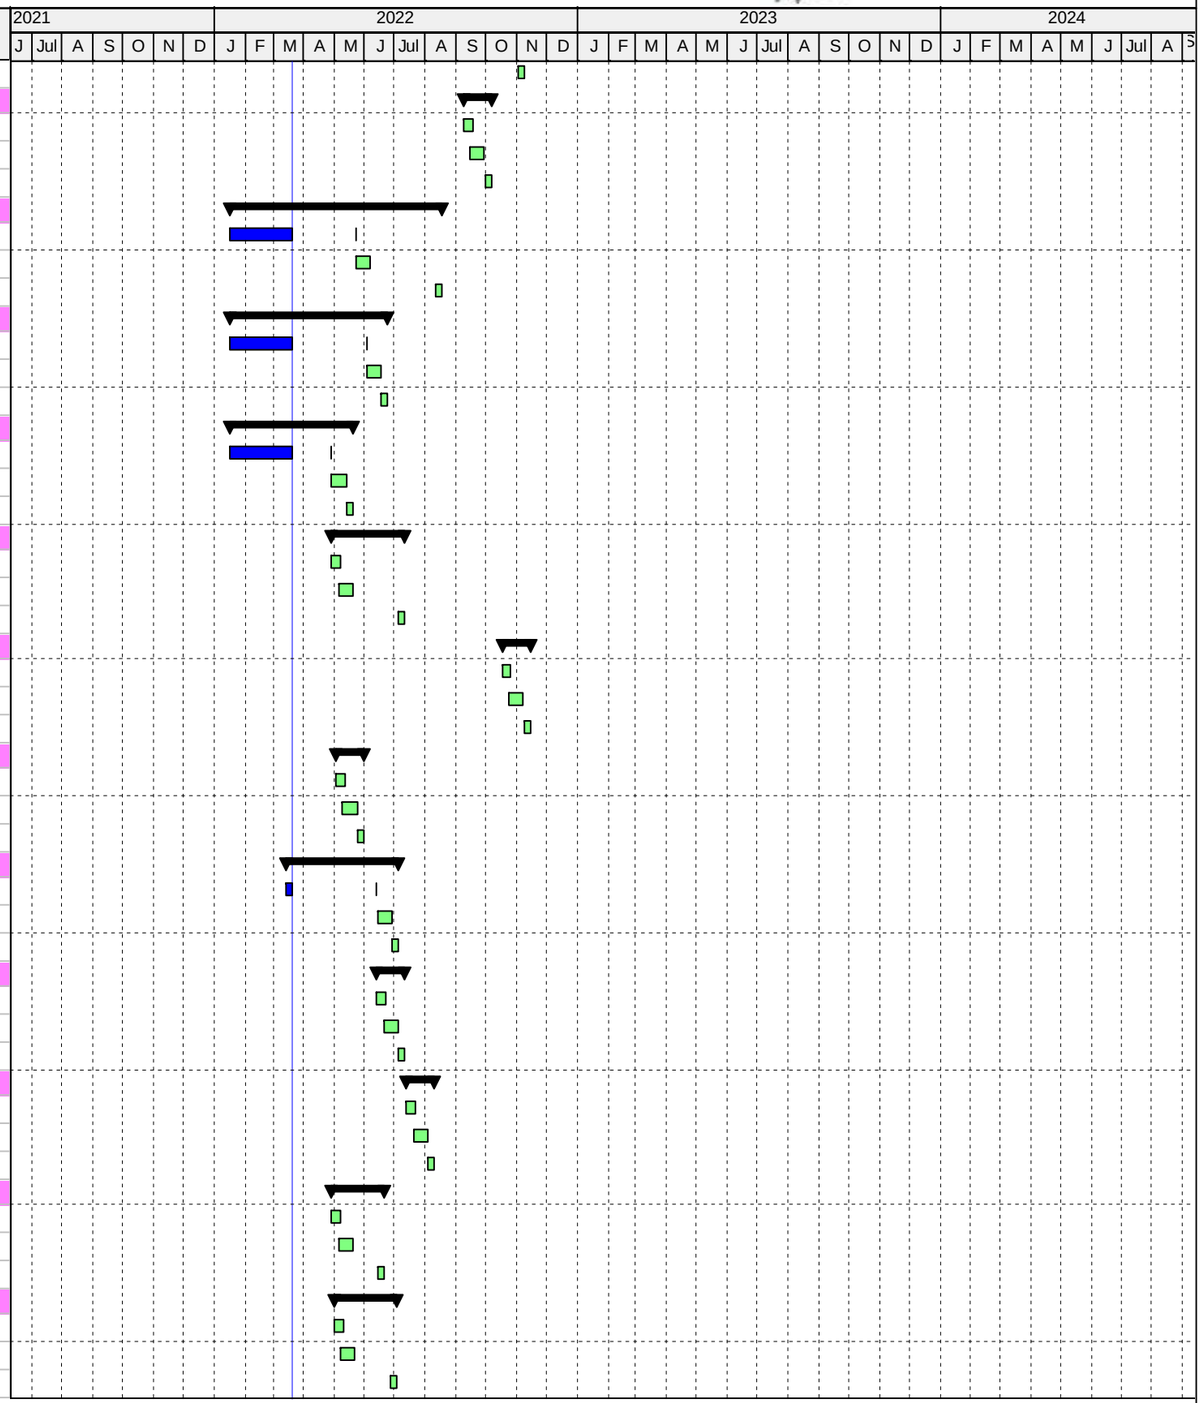


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
ESD System		69	0%	$86.28	29-Apr-22	06-Jul-22
P06-E	PMR For ESD System - Extension of Binak B/C Manifold	10	0%	$8.63	29-Apr-22	08-May-22
P06-E	TBE/TBA For ESD System - Extension of Binak B/C Manifold	30	0%	$12.94	06-May-22	04-Jun-22
P06-E	VDR/TBA For ESD System - Extension of Binak B/C Manifold	7	0%	$64.71	30-Jun-22	06-Jul-22
F&G System		69	0%	$86.28	29-Apr-22	06-Jul-22
P06-E	PMR For F&G System - Extension of Binak B/C Manifold	10	0%	$8.63	29-Apr-22	08-May-22
P06-E	TBE/TBA For F&G System - Extension of Binak B/C Manifold	30	0%	$12.94	06-May-22	04-Jun-22
P06-E	VDR/TBA For F&G System - Extension of Binak B/C Manifold	7	0%	$64.71	30-Jun-22	06-Jul-22
Level Transmitter		124	0%	$44.79	27-Apr-22	28-Aug-22
P06-E	PMR For Level Transmitter - W007S & Manifold	10	0%	$4.48	27-Apr-22	06-May-22
P06-E	TBE For Level Transmitter - W007S & Manifold	30	0%	$6.72	04-May-22	02-Jun-22
P06-E	VDR For Level Transmitter - W007S & Manifold	7	0%	$33.59	22-Aug-22	28-Aug-22
Safety & Fire Fighting		121	0%	$129.46	28-Jul-22	25-Nov-22
Fire Fighting and Safety Equipment		79	0%	$96.46	28-Jul-22	14-Oct-22
P06-E	PMR For Fire Fighting and Safety Equipment - Manifold & W(	10	0%	$9.65	28-Jul-22	06-Aug-22
P06-E	TBE For Fire Fighting and Safety Equipment - Manifold & W0	30	0%	$14.47	04-Aug-22	02-Sep-22
P06-E	VDR For Fire Fighting and Safety Equipment - Manifold & W(	7	0%	$72.35	08-Oct-22	14-Oct-22
Safety Sign		79	0%	$33.00	08-Sep-22	25-Nov-22
P06-E	PMR For Fire Safety Sign - Manifold & W007S	10	0%	$3.30	08-Sep-22	17-Sep-22
P06-E	TBE For Fire Safety Sign - Manifold & W007S	30	0%	$4.95	15-Sep-22	14-Oct-22
P06-E	VDR For Fire Safety Sign - Manifold & W007S	7	0%	$24.75	19-Nov-22	25-Nov-22
Electrical		263	0%	$766.79	09-May-22	26-Jan-23
Tray/Ladder and Accessories		64	0%	$58.97	30-Jun-22	01-Sep-22
P06-E	PMR For Tray/Ladder and Accessories - Manifold & W007S	10	0%	$5.90	30-Jun-22	09-Jul-22
P06-E	TBE For Tray/Ladder and Accessories - Manifold & W007S	15	0%	$8.84	07-Jul-22	21-Jul-22
P06-E	VDR For Tray/Ladder and Accessories - Manifold & W007S	7	0%	$44.22	26-Aug-22	01-Sep-22
DC Charger		59	0%	$58.97	09-May-22	06-Jul-22
P06-E	PMR For DC Charger - Manifold & W007S	10	0%	$5.90	09-May-22	18-May-22
P06-E	TBE For DC Charger - Manifold & W007S	15	0%	$8.84	16-May-22	30-May-22
P06-E	VDR For DC Charger - Manifold & W007S	7	0%	$44.22	30-Jun-22	06-Jul-22
Earthing & Lightning System		94	0%	$58.97	15-Aug-22	16-Nov-22
P06-E	PMR For Earthing & Lightning System - Manifold & W007S	10	0%	$5.90	15-Aug-22	24-Aug-22
P06-E	TBE For Earthing & Lightning System - Manifold & W007S	15	0%	$8.84	22-Aug-22	05-Sep-22
P06-E	VDR For Earthing & Lightning System - Manifold & W007S	7	0%	$44.22	10-Nov-22	16-Nov-22
UPS System		124	0%	$58.97	11-Aug-22	12-Dec-22
P06-E	PMR For UPS System - Manifold & W007S	10	0%	$5.90	11-Aug-22	20-Aug-22
P06-E	TBE For UPS System - Manifold & W007S	15	0%	$8.84	18-Aug-22	01-Sep-22
P06-E	VDR For UPS System - Manifold & W007S	7	0%	$44.22	06-Dec-22	12-Dec-22
Transmission Over Head Line Equipment		94	0%	$59.04	11-May-22	12-Aug-22
P06-E	PMR For Transmission Over head Line Equipment - W007S	10	0%	$5.90	11-May-22	20-May-22
P06-E	TBE For Transmission Over head Line Equipment - W007S	15	0%	$8.86	18-May-22	01-Jun-22
P06-E	VDR For Transmission Over head Line Equipment - W007S	7	0%	$44.28	06-Aug-22	12-Aug-22
Lighting and Small Power Equipment		94	0%	$59.04	25-Oct-22	26-Jan-23
P06-E	PMR For Lighting and Small Power Equipment - W007S	10	0%	$5.90	25-Oct-22	03-Nov-22
P06-E	TBE For Lighting and Small Power Equipment - W007S	15	0%	$8.86	01-Nov-22	15-Nov-22
P06-E	VDR For Lighting and Small Power Equipment - W007S	7	0%	$44.28	20-Jan-23	26-Jan-23
Capacitor Bank		65	0%	$59.04	18-May-22	21-Jul-22
P06-E	PMR For Capacitor Bank - W007S	10	0%	$5.90	18-May-22	27-May-22
P06-E	TBE For Capacitor Bank - W007S	15	0%	$8.86	25-May-22	08-Jun-22

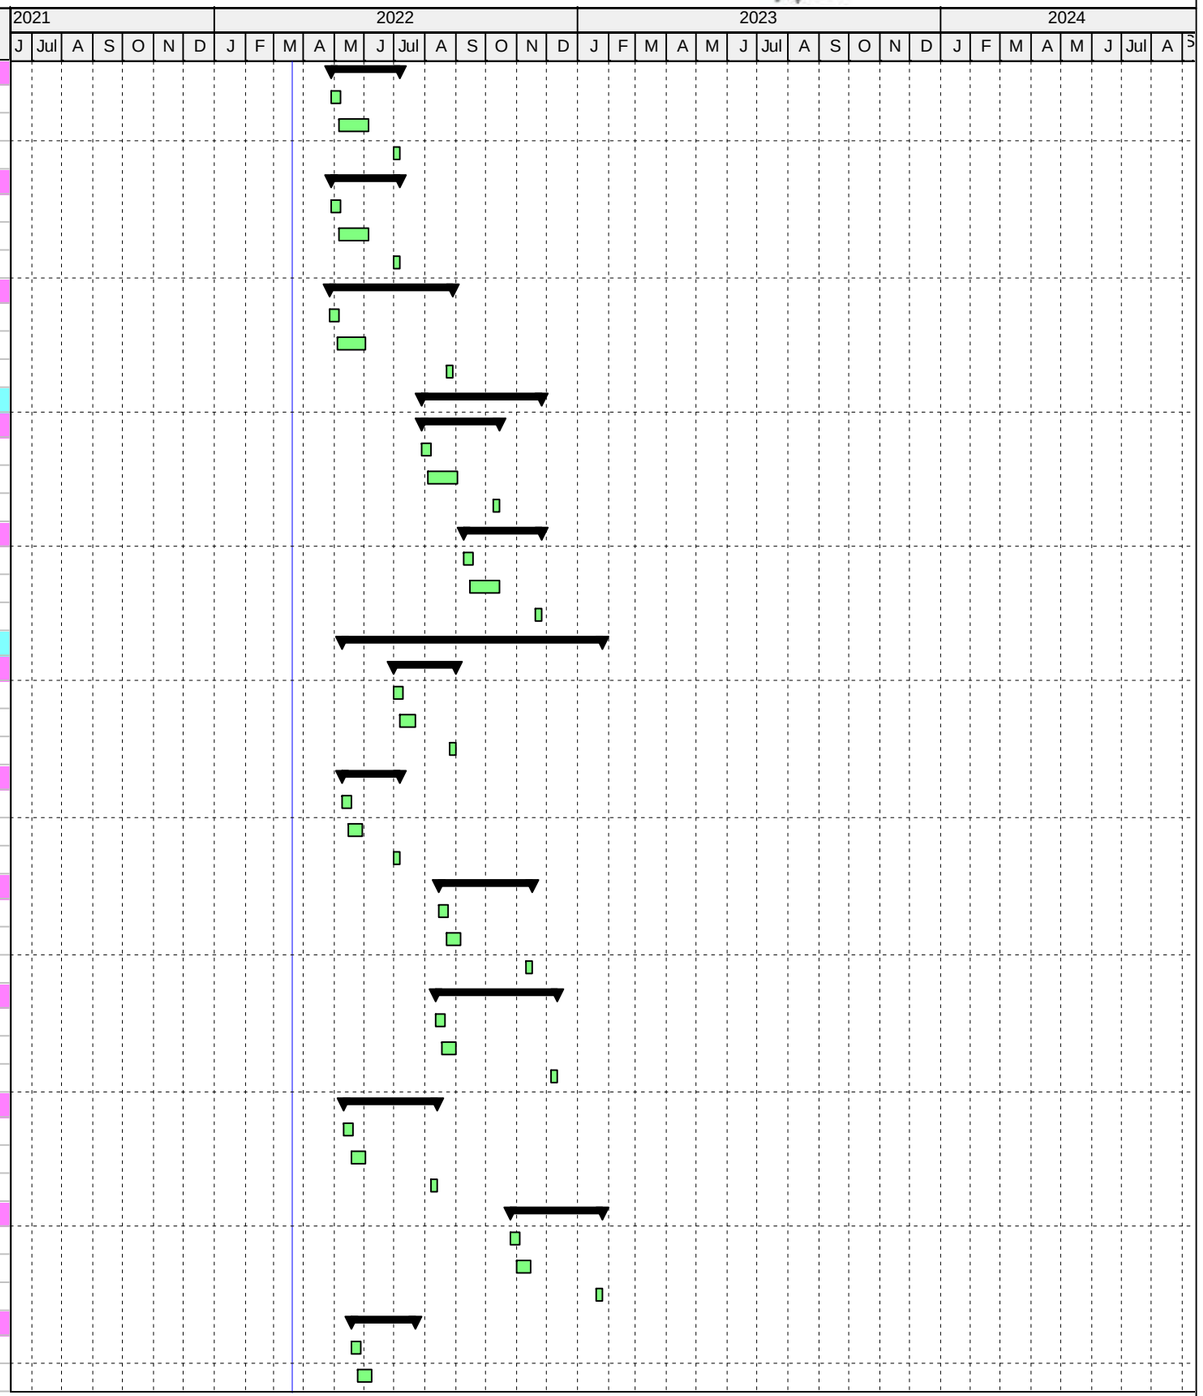


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	VDR For Capacitor Bank - W007S	8	0%	$44.28	14-Jul-22	21-Jul-22
Lighting & Distribution Main Panels		94	0%	$58.97	01-Aug-22	02-Nov-22
P06-E	PMR For Lighting & Distribution Main Panels - W007S	10	0%	$5.90	01-Aug-22	10-Aug-22
P06-E	TBE For Lighting & Distribution Main Panels - W007S	15	0%	$8.84	08-Aug-22	22-Aug-22
P06-E	VDR For Lighting & Distribution Main Panels - W007S	7	0%	$44.22	27-Oct-22	02-Nov-22
Transformers		94	0%	$58.97	18-May-22	19-Aug-22
P06-E	PMR For Transformers - W007S	10	0%	$5.90	18-May-22	27-May-22
P06-E	TBE For Transformers - W007S	15	0%	$8.84	25-May-22	08-Jun-22
P06-E	VDR For Transformers - W007S	7	0%	$44.22	13-Aug-22	19-Aug-22
Power & Control Cables		65	0%	$58.97	04-Nov-22	07-Jan-23
P06-E	PMR For Power & Control Cables - Manifold & W007S	10	0%	$5.90	04-Nov-22	13-Nov-22
P06-E	TBE For Power & Control Cables - Manifold & W007S	16	0%	$8.84	11-Nov-22	26-Nov-22
P06-E	VDR For Power & Control Cables - Manifold & W007S	7	0%	$44.22	01-Jan-23	07-Jan-23
Electrical Bulk Items		64	0%	$58.97	11-May-22	13-Jul-22
P06-E	PMR For Electrical Bulk Items - Manifold & W007S	10	0%	$5.90	11-May-22	20-May-22
P06-E	TBE For Electrical Bulk Items - Manifold & W007S	15	0%	$8.84	18-May-22	01-Jun-22
P06-E	VDR For Electrical Bulk Items - Manifold & W007S	7	0%	$44.22	07-Jul-22	13-Jul-22
LV Switchgear & MCC		94	0%	$58.97	09-May-22	10-Aug-22
P06-E	PMR For LV Switchgear & MCC - Manifold & W007S	10	0%	$5.90	09-May-22	18-May-22
P06-E	TBE For LV Switchgear & MCC - Manifold & W007S	15	0%	$8.84	16-May-22	30-May-22
P06-E	VDR For LV Switchgear & MCC - Manifold & W007S	7	0%	$44.22	04-Aug-22	10-Aug-22
Emergency Diesel Generator		94	0%	$58.97	23-May-22	24-Aug-22
P06-E	PMR For Emergency Diesel Generator - W007S	10	0%	$5.90	23-May-22	01-Jun-22
P06-E	TBE For Emergency Diesel Generator - W007S	15	0%	$8.84	30-May-22	13-Jun-22
P06-E	VDR For Emergency Diesel Generator - W007S	7	0%	$44.22	18-Aug-22	24-Aug-22
Structure		42	0%	$50.18	13-Nov-22	24-Dec-22
Steel Structure Items		32	0%	$16.73	13-Nov-22	14-Dec-22
P06-E	PMR For Steel Structure Items - W007S/Manifold Extension	7	0%	$1.67	13-Nov-22	19-Nov-22
P06-E	TBE For Steel Structure Items - W007S/Manifold Extension	20	0%	$2.51	20-Nov-22	09-Dec-22
P06-E	VDR For Steel Structure Items - W007S/Manifold Extension	5	0%	$12.55	10-Dec-22	14-Dec-22
Anchor Bolts		42	0%	$16.72	13-Nov-22	24-Dec-22
P06-E	PMR For Anchor Bolts - W007S/Manifold Extension	10	0%	$1.67	13-Nov-22	22-Nov-22
P06-E	TBE For Anchor Bolts - W007S/Manifold Extension	30	0%	$2.51	20-Nov-22	19-Dec-22
P06-E	VDR For Anchor Bolts - W007S/Manifold Extension	5	0%	$12.54	20-Dec-22	24-Dec-22
Blast Proof Doors		42	0%	$16.72	13-Nov-22	24-Dec-22
P06-E	PMR For Blast Proof Doors - W007S/Manifold Extension	10	0%	$1.67	13-Nov-22	22-Nov-22
P06-E	TBE For Blast Proof Doors - W007S/Manifold Extension	30	0%	$2.51	20-Nov-22	19-Dec-22
P06-E	VDR For Blast Proof Doors - W007S/Manifold Extension	5	0%	$12.54	20-Dec-22	24-Dec-22
Civil		17	0%	$33.27	01-Jul-22	17-Jul-22
Geomembrane		17	0%	$16.63	01-Jul-22	17-Jul-22
P06-E	PMR For Geomembrane - W007S	5	0%	$1.66	01-Jul-22	05-Jul-22
P06-E	TBE For Geomembrane - W007S	5	0%	$2.49	08-Jul-22	12-Jul-22
P06-E	VDR For Geomembrane - W007S	5	0%	$12.47	13-Jul-22	17-Jul-22
Geotextile		17	0%	$16.63	01-Jul-22	17-Jul-22
P06-E	PMR For Geotextile - W007S	5	0%	$1.66	01-Jul-22	05-Jul-22
P06-E	TBE For Geotextile - W007S	5	0%	$2.49	08-Jul-22	12-Jul-22
P06-E	VDR For Geotextile - W007S	5	0%	$12.47	13-Jul-22	17-Jul-22
Commissioning Engineering		626	0%	$554.44	20-Mar-22	05-Dec-23
P06-EP	Operability Review	5	0%	$110.89	01-Dec-23	05-Dec-23

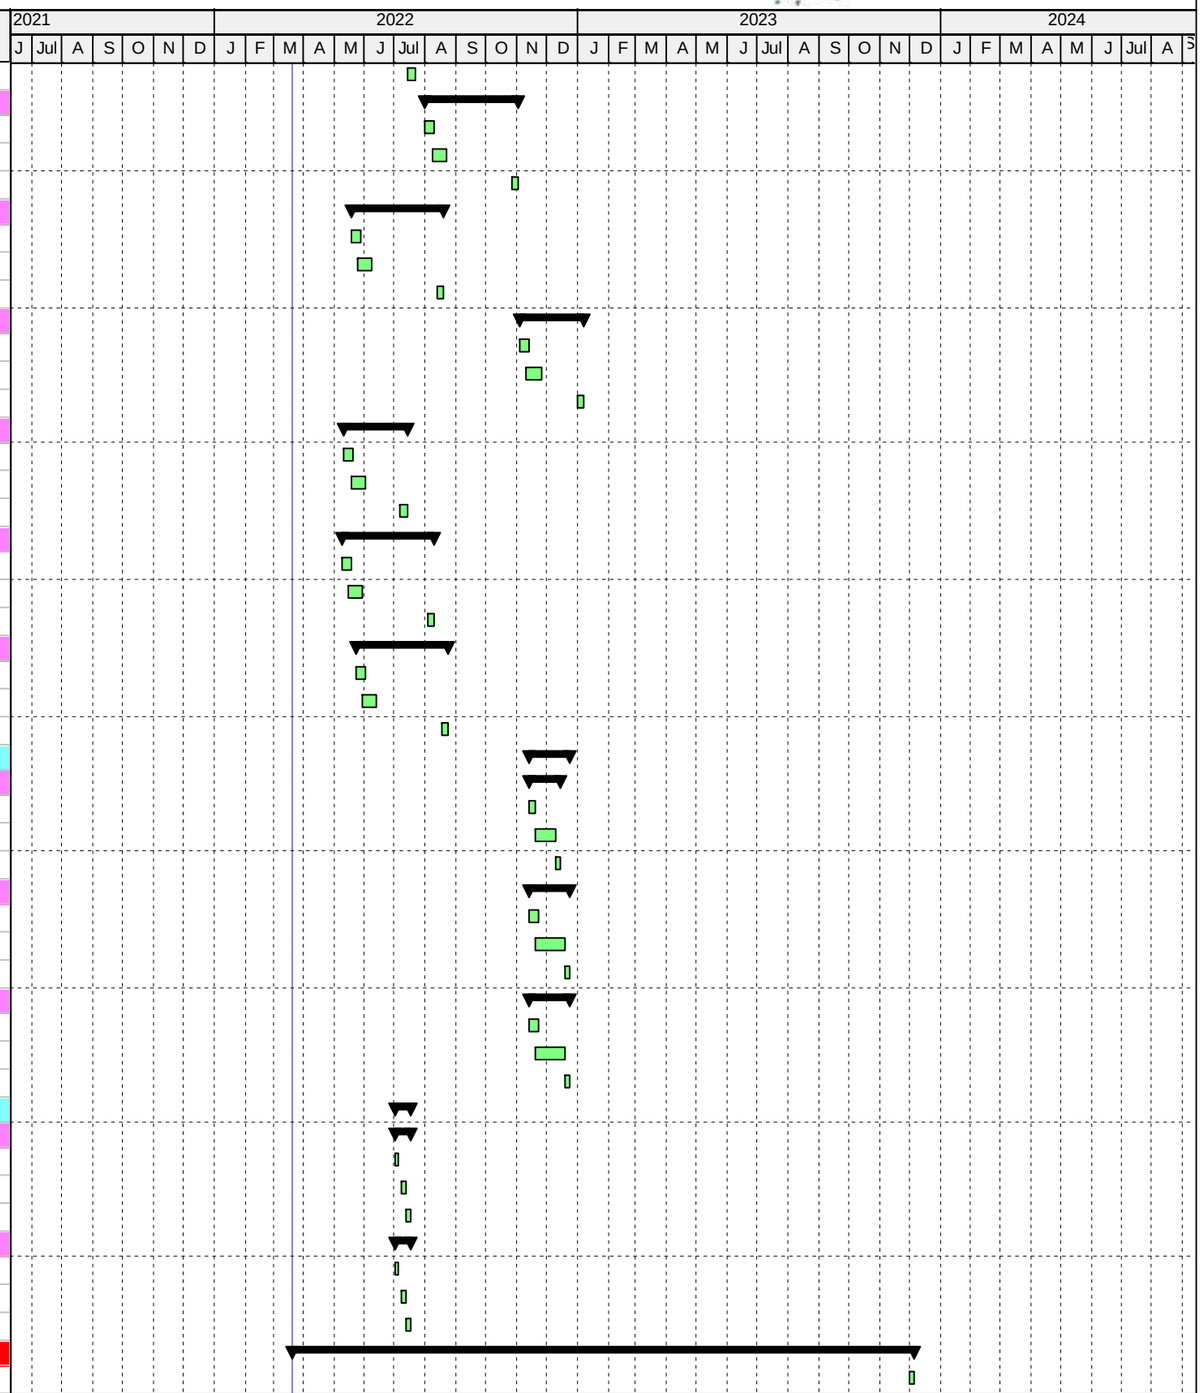


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-EP	Pre-Commissioning, Commissioning & Startup Procedure - M	44	0%	$332.66	20-Mar-22	02-May-22
P06-EP	Operating Manual - Manifold & W007S	30	0%	$110.89	01-Nov-23	30-Nov-23
Field Engineering		640	0%	$4,158.30	20-Mar-22	19-Dec-23
P06-EP	Technical/Site Queries	44	0%	$2,079.15	26-Jul-22	07-Sep-22
P06-EP	As-Built Document Booklets - (Manifold &) W007S	10	0%	$2,079.15	10-Dec-23	19-Dec-23
P06-EP	As-Built Document Booklets - Manifold	0	0%	$0.00		20-Mar-22
Engineering Final Documentation		250	0%	$2,772.20	19-Apr-23	24-Dec-23
P06-EP	Final Engineering Dossier - (Manifold &)W007S	10	0%	$2,772.20	15-Dec-23	24-Dec-23
P06-EP	Final Engineering Dossier - Manifold	0	0%	$0.00		19-Apr-23
PROCUREMENT		579	0%	$536,451.00	01-Apr-22	31-Oct-23
Wellhead Facility and Flowline		579	0%	$371,975.12	01-Apr-22	31-Oct-23
Mechanical		339	0%	$20,458.63	09-Aug-22	13-Jul-23
Elevated Tanks - W007S		309	0%	$8,183.45	14-Aug-22	18-Jun-23
P06-E	Tendering & Selection	60	0%	$327.34	14-Aug-22	12-Oct-22
P06-E	Contract Effectiveness / PO	5	0%	$491.01	13-Oct-22	17-Oct-22
P06-E	Manufacturing / Fabrication / Supply	220	0%	$4,091.73	18-Oct-22	25-May-23
P06-E	Final Inspection	12	0%	$818.35	26-May-23	06-Jun-23
P06-E	Delivery On Site	7	0%	$1,636.69	07-Jun-23	13-Jun-23
P06-E	Submitting Vendor Data Book	5	0%	$409.17	14-Jun-23	18-Jun-23
P06-E	Delivering Spare Parts	5	0%	$409.17	14-Jun-23	18-Jun-23
Drums - W007S		339	0%	$12,275.18	09-Aug-22	13-Jul-23
P06-E	Tendering & Selection	60	0%	$491.01	09-Aug-22	07-Oct-22
P06-E	Contract Effectiveness / PO	5	0%	$736.51	08-Oct-22	12-Oct-22
P06-E	Manufacturing / Fabrication / Supply	250	0%	$6,137.59	13-Oct-22	19-Jun-23
P06-E	Final Inspection	12	0%	$1,227.52	20-Jun-23	01-Jul-23
P06-E	Delivery On Site	7	0%	$2,455.04	02-Jul-23	08-Jul-23
P06-E	Submitting Vendor Data Book	5	0%	$613.76	09-Jul-23	13-Jul-23
P06-E	Delivering Spare Parts	5	0%	$613.76	09-Jul-23	13-Jul-23
HVAC		179	0%	$3,719.75	06-May-23	31-Oct-23
Main HVAC Equipment - W007S		179	0%	$3,719.75	06-May-23	31-Oct-23
P06-E	Tendering & Selection	30	0%	$148.79	06-May-23	04-Jun-23
P06-E	Contract Effectiveness / PO	5	0%	$223.19	05-Jun-23	09-Jun-23
P06-E	Manufacturing / Fabrication / Supply	120	0%	$1,859.88	10-Jun-23	07-Oct-23
P06-E	Final Inspection	12	0%	$371.98	08-Oct-23	19-Oct-23
P06-E	Delivery On Site	7	0%	$929.94	20-Oct-23	26-Oct-23
P06-E	Submitting Vendor Data Book	5	0%	$185.99	27-Oct-23	31-Oct-23
Piping		442	0%	$44,748.61	16-May-22	31-Jul-23
Pipes - W007S		270	0%	$8,949.72	05-Oct-22	01-Jul-23
P06-E	Tendering & Selection	31	0%	$357.99	05-Oct-22	04-Nov-22
P06-E	Contract Effectiveness / PO	5	0%	$536.98	05-Nov-22	09-Nov-22
P06-E	Manufacturing / Fabrication / Supply	210	0%	$4,474.86	10-Nov-22	07-Jun-23
P06-E	Final Inspection	12	0%	$894.97	08-Jun-23	19-Jun-23
P06-E	Delivery On Site	7	0%	$2,237.43	20-Jun-23	26-Jun-23
P06-E	Submitting Vendor Data Book	5	0%	$447.49	27-Jun-23	01-Jul-23
Fittings - W007S		240	0%	$3,356.15	04-Nov-22	01-Jul-23
P06-E	Tendering & Selection	31	0%	$134.25	04-Nov-22	04-Dec-22
P06-E	Contract Effectiveness / PO	5	0%	$201.37	05-Dec-22	09-Dec-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$1,678.07	10-Dec-22	07-Jun-23
P06-E	Final Inspection	12	0%	$335.61	08-Jun-23	19-Jun-23

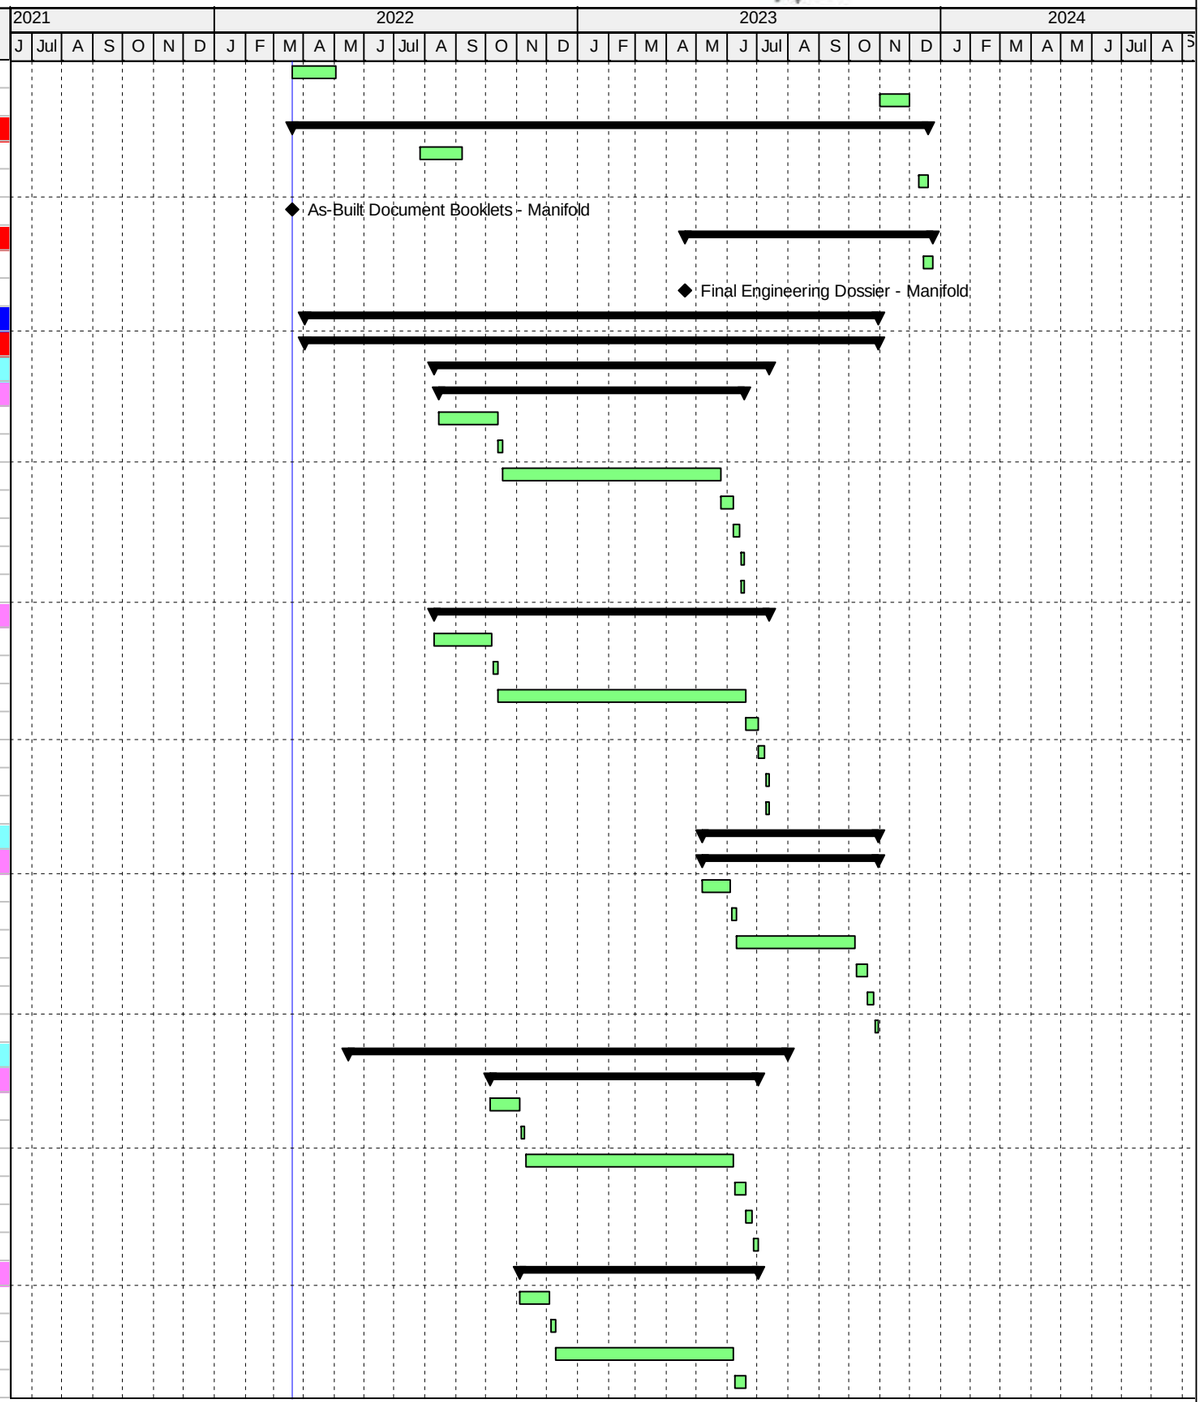


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Delivery On Site	7	0%	$839.04	20-Jun-23	26-Jun-23
P06-E	Submitting Vendor Data Book	5	0%	$167.81	27-Jun-23	01-Jul-23
Flanges - W007S		240	0%	$3,356.15	04-Nov-22	01-Jul-23
P06-E	Tendering & Selection	31	0%	$134.25	04-Nov-22	04-Dec-22
P06-E	Contract Effectiveness / PO	5	0%	$201.37	05-Dec-22	09-Dec-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$1,678.07	10-Dec-22	07-Jun-23
P06-E	Final Inspection	12	0%	$335.61	08-Jun-23	19-Jun-23
P06-E	Delivery On Site	7	0%	$839.04	20-Jun-23	26-Jun-23
P06-E	Submitting Vendor Data Book	5	0%	$167.81	27-Jun-23	01-Jul-23
Manual Valves - W007S		244	0%	$15,662.01	25-Oct-22	25-Jun-23
P06-E	Tendering & Selection	30	0%	$626.48	25-Oct-22	23-Nov-22
P06-E	Contract Effectiveness / PO	5	0%	$939.72	24-Nov-22	28-Nov-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$7,831.01	29-Nov-22	27-May-23
P06-E	Final Inspection	12	0%	$1,566.20	28-May-23	08-Jun-23
P06-E	Delivery On Site	7	0%	$3,132.40	09-Jun-23	15-Jun-23
P06-E	Submitting Vendor Data Book	5	0%	$783.10	16-Jun-23	20-Jun-23
P06-E	Delivering Spare Parts	5	0%	$783.10	21-Jun-23	25-Jun-23
Gaskets - W007S		270	0%	$1,342.46	04-Nov-22	31-Jul-23
P06-E	Tendering & Selection	31	0%	$53.70	04-Nov-22	04-Dec-22
P06-E	Contract Effectiveness / PO	5	0%	$80.55	05-Dec-22	09-Dec-22
P06-E	Manufacturing / Fabrication / Supply	210	0%	$671.23	10-Dec-22	07-Jul-23
P06-E	Final Inspection	12	0%	$134.25	08-Jul-23	19-Jul-23
P06-E	Delivery On Site	7	0%	$335.61	20-Jul-23	26-Jul-23
P06-E	Submitting Vendor Data Book	5	0%	$67.12	27-Jul-23	31-Jul-23
Bolt/Nuts - W007S		179	0%	$894.97	04-Nov-22	01-May-23
P06-E	Tendering & Selection	30	0%	$35.80	04-Nov-22	03-Dec-22
P06-E	Contract Effectiveness / PO	5	0%	$53.70	04-Dec-22	08-Dec-22
P06-E	Manufacturing / Fabrication / Supply	120	0%	$447.49	09-Dec-22	07-Apr-23
P06-E	Final Inspection	12	0%	$89.50	08-Apr-23	19-Apr-23
P06-E	Delivery On Site	7	0%	$223.74	20-Apr-23	26-Apr-23
P06-E	Submitting Vendor Data Book	5	0%	$44.75	27-Apr-23	01-May-23
Sampling Connection Set - W007S		119	0%	$2,237.43	16-May-22	11-Sep-22
P06-E	Tendering & Selection	30	0%	$89.50	16-May-22	14-Jun-22
P06-E	Contract Effectiveness / PO	5	0%	$134.25	15-Jun-22	19-Jun-22
P06-E	Manufacturing / Fabrication / Supply	60	0%	$1,118.72	20-Jun-22	18-Aug-22
P06-E	Final Inspection	12	0%	$223.74	19-Aug-22	30-Aug-22
P06-E	Delivery On Site	7	0%	$559.36	31-Aug-22	06-Sep-22
P06-E	Submitting Vendor Data Book	5	0%	$111.87	07-Sep-22	11-Sep-22
Stone Trap - W007S		119	0%	$6,712.29	30-May-22	25-Sep-22
P06-E	Tendering & Selection	30	0%	$268.49	30-May-22	28-Jun-22
P06-E	Contract Effectiveness / PO	5	0%	$402.74	29-Jun-22	03-Jul-22
P06-E	Manufacturing / Fabrication / Supply	60	0%	$3,356.15	04-Jul-22	01-Sep-22
P06-E	Final Inspection	12	0%	$671.23	02-Sep-22	13-Sep-22
P06-E	Delivery On Site	7	0%	$1,678.07	14-Sep-22	20-Sep-22
P06-E	Submitting Vendor Data Book	5	0%	$335.61	21-Sep-22	25-Sep-22
Pipe Support - W007S		119	0%	$2,237.43	07-Oct-22	02-Feb-23
P06-E	Tendering & Selection	30	0%	$89.50	07-Oct-22	05-Nov-22
P06-E	Contract Effectiveness / PO	5	0%	$134.25	06-Nov-22	10-Nov-22
P06-E	Manufacturing / Fabrication / Supply	60	0%	$1,118.72	11-Nov-22	09-Jan-23

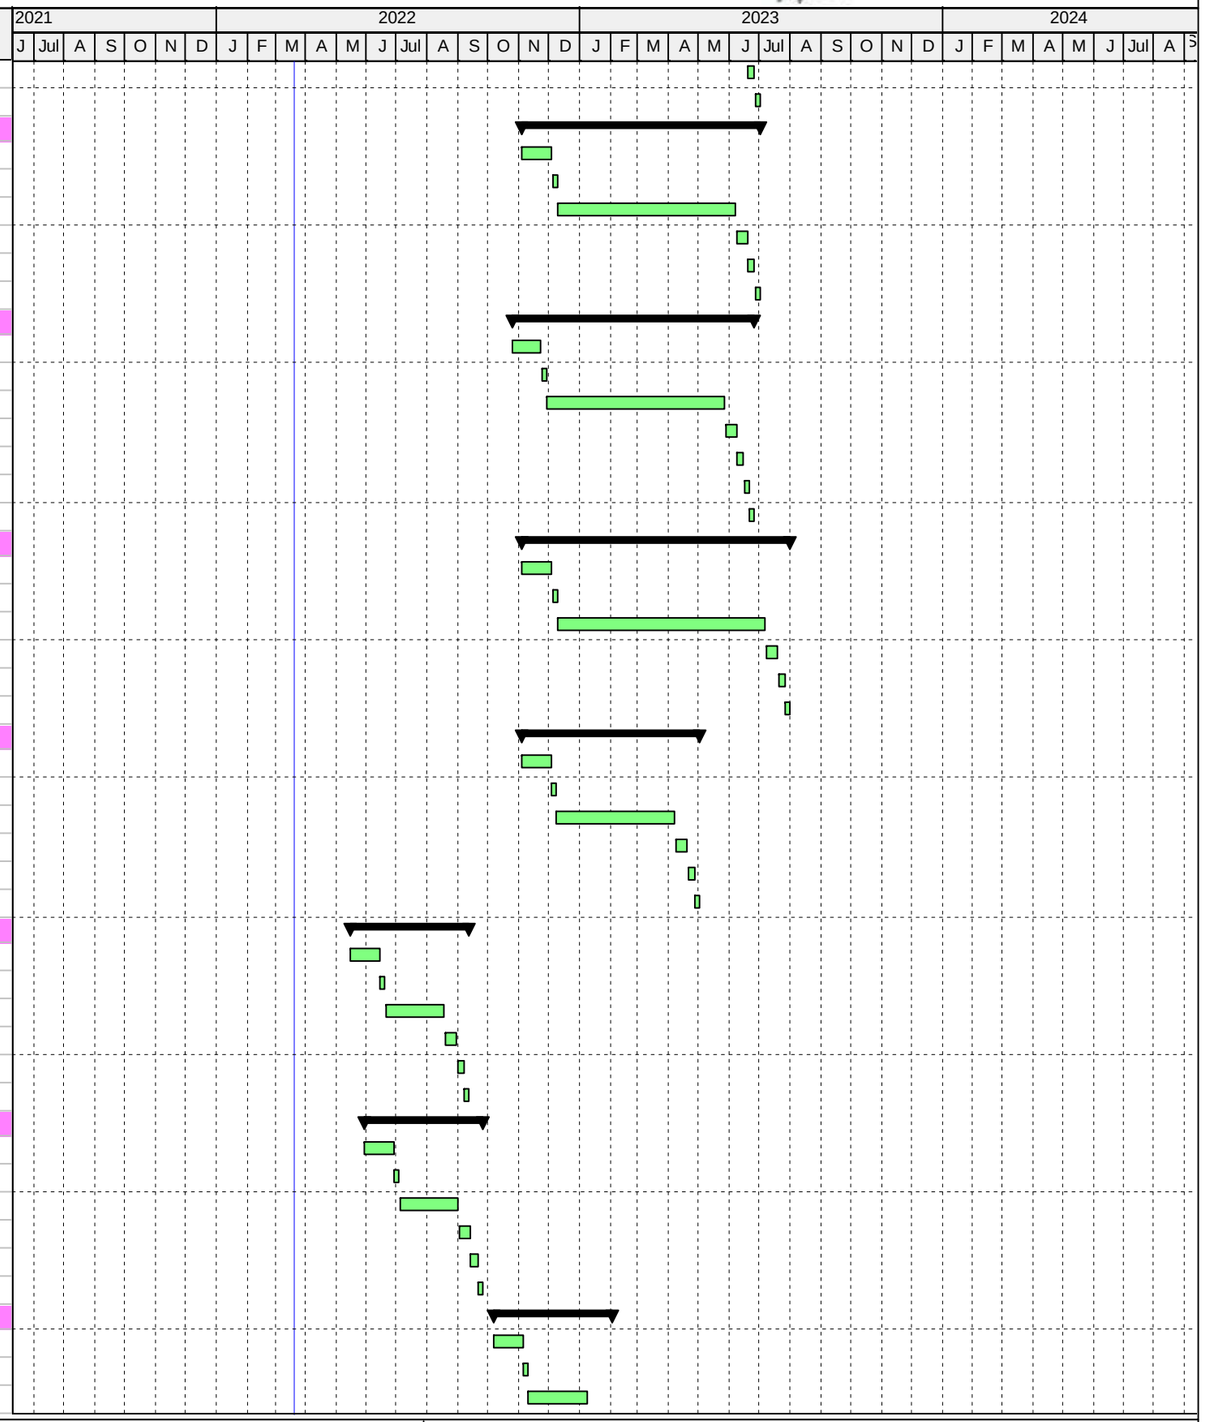


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Final Inspection	12	0%	$223.74	10-Jan-23	21-Jan-23
P06-E	Delivery On Site	7	0%	$559.36	22-Jan-23	28-Jan-23
P06-E	Submitting Vendor Data Book	5	0%	$111.87	29-Jan-23	02-Feb-23
Pipeline		288	0%	$115,126.30	01-Apr-22	13-Jan-23
Line Pipes - W007S		239	0%	$97,857.36	20-May-22	13-Jan-23
P06-E	Tendering & Selection	30	0%	$3,914.29	20-May-22	18-Jun-22
P06-E	Contract Effectiveness / PO	5	0%	$5,871.44	19-Jun-22	23-Jun-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$48,928.68	24-Jun-22	20-Dec-22
P06-E	Final Inspection	12	0%	$9,785.74	21-Dec-22	01-Jan-23
P06-E	Delivery On Site	7	0%	$24,464.34	02-Jan-23	08-Jan-23
P06-E	Submitting Vendor Data Book	5	0%	$4,892.87	09-Jan-23	13-Jan-23
Flow Line Support - W007S		239	0%	$17,268.95	01-Apr-22	25-Nov-22
P06-E	Tendering & Selection	30	0%	$690.76	01-Apr-22	30-Apr-22
P06-E	Contract Effectiveness / PO	5	0%	$1,036.14	01-May-22	05-May-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$8,634.47	06-May-22	01-Nov-22
P06-E	Final Inspection	12	0%	$1,726.89	02-Nov-22	13-Nov-22
P06-E	Delivery On Site	7	0%	$4,317.24	14-Nov-22	20-Nov-22
P06-E	Submitting Vendor Data Book	5	0%	$863.45	21-Nov-22	25-Nov-22
Control & Instrumentation		422	0%	$11,903.20	14-May-22	09-Jul-23
Control System/Console/Furniture		274	0%	$962.97	21-May-22	18-Feb-23
P06-E	Tendering & Selection	60	0%	$38.52	21-May-22	19-Jul-22
P06-E	Contract Effectiveness / PO	5	0%	$57.78	20-Jul-22	24-Jul-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$481.48	25-Jul-22	20-Jan-23
P06-E	Final Inspection	12	0%	$96.30	21-Jan-23	01-Feb-23
P06-E	Delivery On Site	7	0%	$192.59	02-Feb-23	08-Feb-23
P06-E	Submitting Vendor Data Book	5	0%	$48.15	09-Feb-23	13-Feb-23
P06-E	Delivering Spare Parts	5	0%	$48.15	14-Feb-23	18-Feb-23
ESD System		274	0%	$962.97	05-Jun-22	05-Mar-23
P06-E	Tendering & Selection	60	0%	$38.52	05-Jun-22	03-Aug-22
P06-E	Contract Effectiveness / PO	5	0%	$57.78	04-Aug-22	08-Aug-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$481.48	09-Aug-22	04-Feb-23
P06-E	Final Inspection	12	0%	$96.30	05-Feb-23	16-Feb-23
P06-E	Delivery On Site	7	0%	$192.59	17-Feb-23	23-Feb-23
P06-E	Submitting Vendor Data Book	5	0%	$48.15	24-Feb-23	28-Feb-23
P06-E	Delivering Spare Parts	5	0%	$48.15	01-Mar-23	05-Mar-23
F&G System		274	0%	$962.97	05-Jun-22	05-Mar-23
P06-E	Tendering & Selection	60	0%	$38.52	05-Jun-22	03-Aug-22
P06-E	Contract Effectiveness / PO	5	0%	$57.78	04-Aug-22	08-Aug-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$481.48	09-Aug-22	04-Feb-23
P06-E	Final Inspection	12	0%	$96.30	05-Feb-23	16-Feb-23
P06-E	Delivery On Site	7	0%	$192.59	17-Feb-23	23-Feb-23
P06-E	Submitting Vendor Data Book	5	0%	$48.15	24-Feb-23	28-Feb-23
P06-E	Delivering Spare Parts	5	0%	$48.15	01-Mar-23	05-Mar-23
Pneumatic On/Off & Shutdown Valves		274	0%	$754.66	23-May-22	20-Feb-23
P06-E	Tendering & Selection	60	0%	$30.19	23-May-22	21-Jul-22
P06-E	Contract Effectiveness / PO	5	0%	$45.28	22-Jul-22	26-Jul-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$377.33	27-Jul-22	22-Jan-23
P06-E	Final Inspection	12	0%	$75.47	23-Jan-23	03-Feb-23
P06-E	Delivery On Site	7	0%	$150.93	04-Feb-23	10-Feb-23

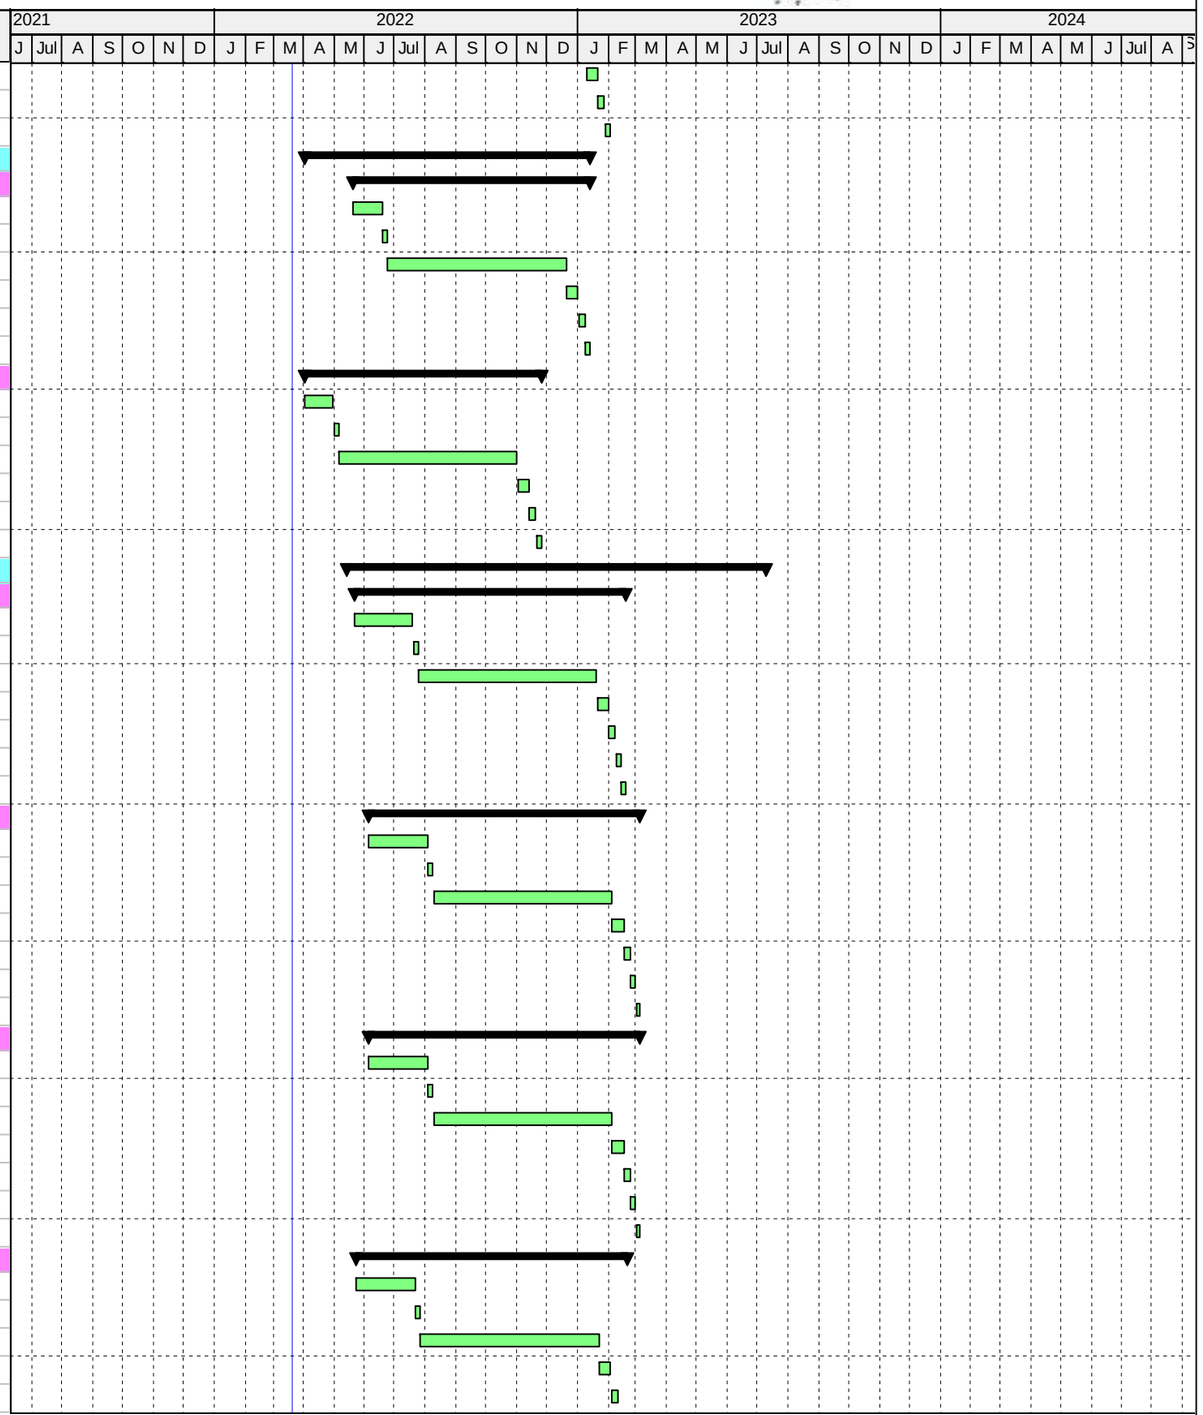

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Submitting Vendor Data Book	5	0%	$37.73	11-Feb-23	15-Feb-23
P06-E	Delivering Spare Parts	5	0%	$37.73	16-Feb-23	20-Feb-23
Control Valves		274	0%	$754.66	29-Jun-22	29-Mar-23
P06-E	Tendering & Selection	60	0%	$30.19	29-Jun-22	27-Aug-22
P06-E	Contract Effectiveness / PO	5	0%	$45.28	28-Aug-22	01-Sep-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$377.33	02-Sep-22	28-Feb-23
P06-E	Final Inspection	12	0%	$75.47	01-Mar-23	12-Mar-23
P06-E	Delivery On Site	7	0%	$150.93	13-Mar-23	19-Mar-23
P06-E	Submitting Vendor Data Book	5	0%	$37.73	20-Mar-23	24-Mar-23
P06-E	Delivering Spare Parts	5	0%	$37.73	25-Mar-23	29-Mar-23
Pressure Safety Valves (PSV)		274	0%	$754.66	05-Jul-22	04-Apr-23
P06-E	Tendering & Selection	60	0%	$30.19	05-Jul-22	02-Sep-22
P06-E	Contract Effectiveness / PO	5	0%	$45.28	03-Sep-22	07-Sep-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$377.33	08-Sep-22	06-Mar-23
P06-E	Final Inspection	12	0%	$75.47	07-Mar-23	18-Mar-23
P06-E	Delivery On Site	7	0%	$150.93	19-Mar-23	25-Mar-23
P06-E	Submitting Vendor Data Book	5	0%	$37.73	26-Mar-23	30-Mar-23
P06-E	Delivering Spare Parts	5	0%	$37.73	31-Mar-23	04-Apr-23
F&G Devices		274	0%	$753.47	04-Aug-22	04-May-23
P06-E	Tendering & Selection	60	0%	$30.14	04-Aug-22	02-Oct-22
P06-E	Contract Effectiveness / PO	5	0%	$45.21	03-Oct-22	07-Oct-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$376.74	08-Oct-22	05-Apr-23
P06-E	Final Inspection	12	0%	$75.35	06-Apr-23	17-Apr-23
P06-E	Delivery On Site	7	0%	$150.69	18-Apr-23	24-Apr-23
P06-E	Submitting Vendor Data Book	5	0%	$37.67	25-Apr-23	29-Apr-23
P06-E	Delivering Spare Parts	5	0%	$37.67	30-Apr-23	04-May-23
Orifice and Restriction Orifice Plate		274	0%	$545.17	25-May-22	22-Feb-23
P06-E	Tendering & Selection	60	0%	$21.81	25-May-22	23-Jul-22
P06-E	Contract Effectiveness / PO	5	0%	$32.71	24-Jul-22	28-Jul-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$272.58	29-Jul-22	24-Jan-23
P06-E	Final Inspection	12	0%	$54.52	25-Jan-23	05-Feb-23
P06-E	Delivery On Site	7	0%	$109.03	06-Feb-23	12-Feb-23
P06-E	Submitting Vendor Data Book	5	0%	$27.26	13-Feb-23	17-Feb-23
P06-E	Delivering Spare Parts	5	0%	$27.26	18-Feb-23	22-Feb-23
Corrosion Coupon/Probe		274	0%	$545.17	21-May-22	18-Feb-23
P06-E	Tendering & Selection	60	0%	$21.81	21-May-22	19-Jul-22
P06-E	Contract Effectiveness / PO	5	0%	$32.71	20-Jul-22	24-Jul-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$272.58	25-Jul-22	20-Jan-23
P06-E	Final Inspection	12	0%	$54.52	21-Jan-23	01-Feb-23
P06-E	Delivery On Site	7	0%	$109.03	02-Feb-23	08-Feb-23
P06-E	Submitting Vendor Data Book	5	0%	$27.26	09-Feb-23	13-Feb-23
P06-E	Delivering Spare Parts	5	0%	$27.26	14-Feb-23	18-Feb-23
Pressure Transmitter		274	0%	$545.17	18-Jun-22	18-Mar-23
P06-E	Tendering & Selection	60	0%	$21.81	18-Jun-22	16-Aug-22
P06-E	Contract Effectiveness / PO	5	0%	$32.71	17-Aug-22	21-Aug-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$272.58	22-Aug-22	17-Feb-23
P06-E	Final Inspection	12	0%	$54.52	18-Feb-23	01-Mar-23
P06-E	Delivery On Site	7	0%	$109.03	02-Mar-23	08-Mar-23
P06-E	Submitting Vendor Data Book	5	0%	$27.26	09-Mar-23	13-Mar-23




Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Delivering Spare Parts	5	0%	$27.26	14-Mar-23	18-Mar-23
Flow Transmitter/ Diff. Pressure Transmitter		234	0%	$545.17	24-Jul-22	14-Mar-23
P06-E	Tendering & Selection	60	0%	$21.81	24-Jul-22	21-Sep-22
P06-E	Contract Effectiveness / PO	5	0%	$32.71	22-Sep-22	26-Sep-22
P06-E	Manufacturing / Fabrication / Supply	140	0%	$272.58	27-Sep-22	13-Feb-23
P06-E	Final Inspection	12	0%	$54.52	14-Feb-23	25-Feb-23
P06-E	Delivery On Site	7	0%	$109.03	26-Feb-23	04-Mar-23
P06-E	Submitting Vendor Data Book	5	0%	$27.26	05-Mar-23	09-Mar-23
P06-E	Delivering Spare Parts	5	0%	$27.26	10-Mar-23	14-Mar-23
Instrument/F&G Cable		229	0%	$545.17	08-Nov-22	24-Jun-23
P06-E	Tendering & Selection	60	0%	$21.81	08-Nov-22	06-Jan-23
P06-E	Contract Effectiveness / PO	5	0%	$32.71	07-Jan-23	11-Jan-23
P06-E	Manufacturing / Fabrication / Supply	140	0%	$272.58	12-Jan-23	31-May-23
P06-E	Final Inspection	12	0%	$54.52	01-Jun-23	12-Jun-23
P06-E	Delivery On Site	7	0%	$136.29	13-Jun-23	19-Jun-23
P06-E	Submitting Vendor Data Book	5	0%	$27.26	20-Jun-23	24-Jun-23
Instrument/F&G Junction box and Gland		239	0%	$545.17	13-Nov-22	09-Jul-23
P06-E	Tendering & Selection	30	0%	$21.81	13-Nov-22	12-Dec-22
P06-E	Contract Effectiveness / PO	5	0%	$32.71	13-Dec-22	17-Dec-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$272.58	18-Dec-22	15-Jun-23
P06-E	Final Inspection	12	0%	$54.52	16-Jun-23	27-Jun-23
P06-E	Delivery On Site	7	0%	$136.29	28-Jun-23	04-Jul-23
P06-E	Submitting Vendor Data Book	5	0%	$27.26	05-Jul-23	09-Jul-23
Instrument Installation Accessories		229	0%	$545.17	30-Sep-22	16-May-23
P06-E	Tendering & Selection	60	0%	$21.81	30-Sep-22	28-Nov-22
P06-E	Contract Effectiveness / PO	5	0%	$32.71	29-Nov-22	03-Dec-22
P06-E	Manufacturing / Fabrication / Supply	140	0%	$272.58	04-Dec-22	22-Apr-23
P06-E	Final Inspection	12	0%	$54.52	23-Apr-23	04-May-23
P06-E	Delivery On Site	7	0%	$136.29	05-May-23	11-May-23
P06-E	Submitting Vendor Data Book	5	0%	$27.26	12-May-23	16-May-23
Differential Pressure/Pressure Gauge		234	0%	$545.17	14-May-22	02-Jan-23
P06-E	Tendering & Selection	60	0%	$21.81	14-May-22	12-Jul-22
P06-E	Contract Effectiveness / PO	5	0%	$32.71	13-Jul-22	17-Jul-22
P06-E	Manufacturing / Fabrication / Supply	140	0%	$272.58	18-Jul-22	04-Dec-22
P06-E	Final Inspection	12	0%	$54.52	05-Dec-22	16-Dec-22
P06-E	Delivery On Site	7	0%	$109.03	17-Dec-22	23-Dec-22
P06-E	Submitting Vendor Data Book	5	0%	$27.26	24-Dec-22	28-Dec-22
P06-E	Delivering Spare Parts	5	0%	$27.26	29-Dec-22	02-Jan-23
Temperature Gauge - Manifold & W007S		234	0%	$545.17	07-Jun-22	26-Jan-23
P06-E	Tendering & Selection	60	0%	$21.81	07-Jun-22	05-Aug-22
P06-E	Contract Effectiveness / PO	5	0%	$32.71	06-Aug-22	10-Aug-22
P06-E	Manufacturing / Fabrication / Supply	140	0%	$272.58	11-Aug-22	28-Dec-22
P06-E	Final Inspection	12	0%	$54.52	29-Dec-22	09-Jan-23
P06-E	Delivery On Site	7	0%	$109.03	10-Jan-23	16-Jan-23
P06-E	Submitting Vendor Data Book	5	0%	$27.26	17-Jan-23	21-Jan-23
P06-E	Delivering Spare Parts	5	0%	$27.26	22-Jan-23	26-Jan-23
Instrument Cable Tray/Ladder - Manifold & W007S		229	0%	$545.17	30-Sep-22	16-May-23
P06-E	Tendering & Selection	60	0%	$21.81	30-Sep-22	28-Nov-22
P06-E	Contract Effectiveness / PO	5	0%	$32.71	29-Nov-22	03-Dec-22

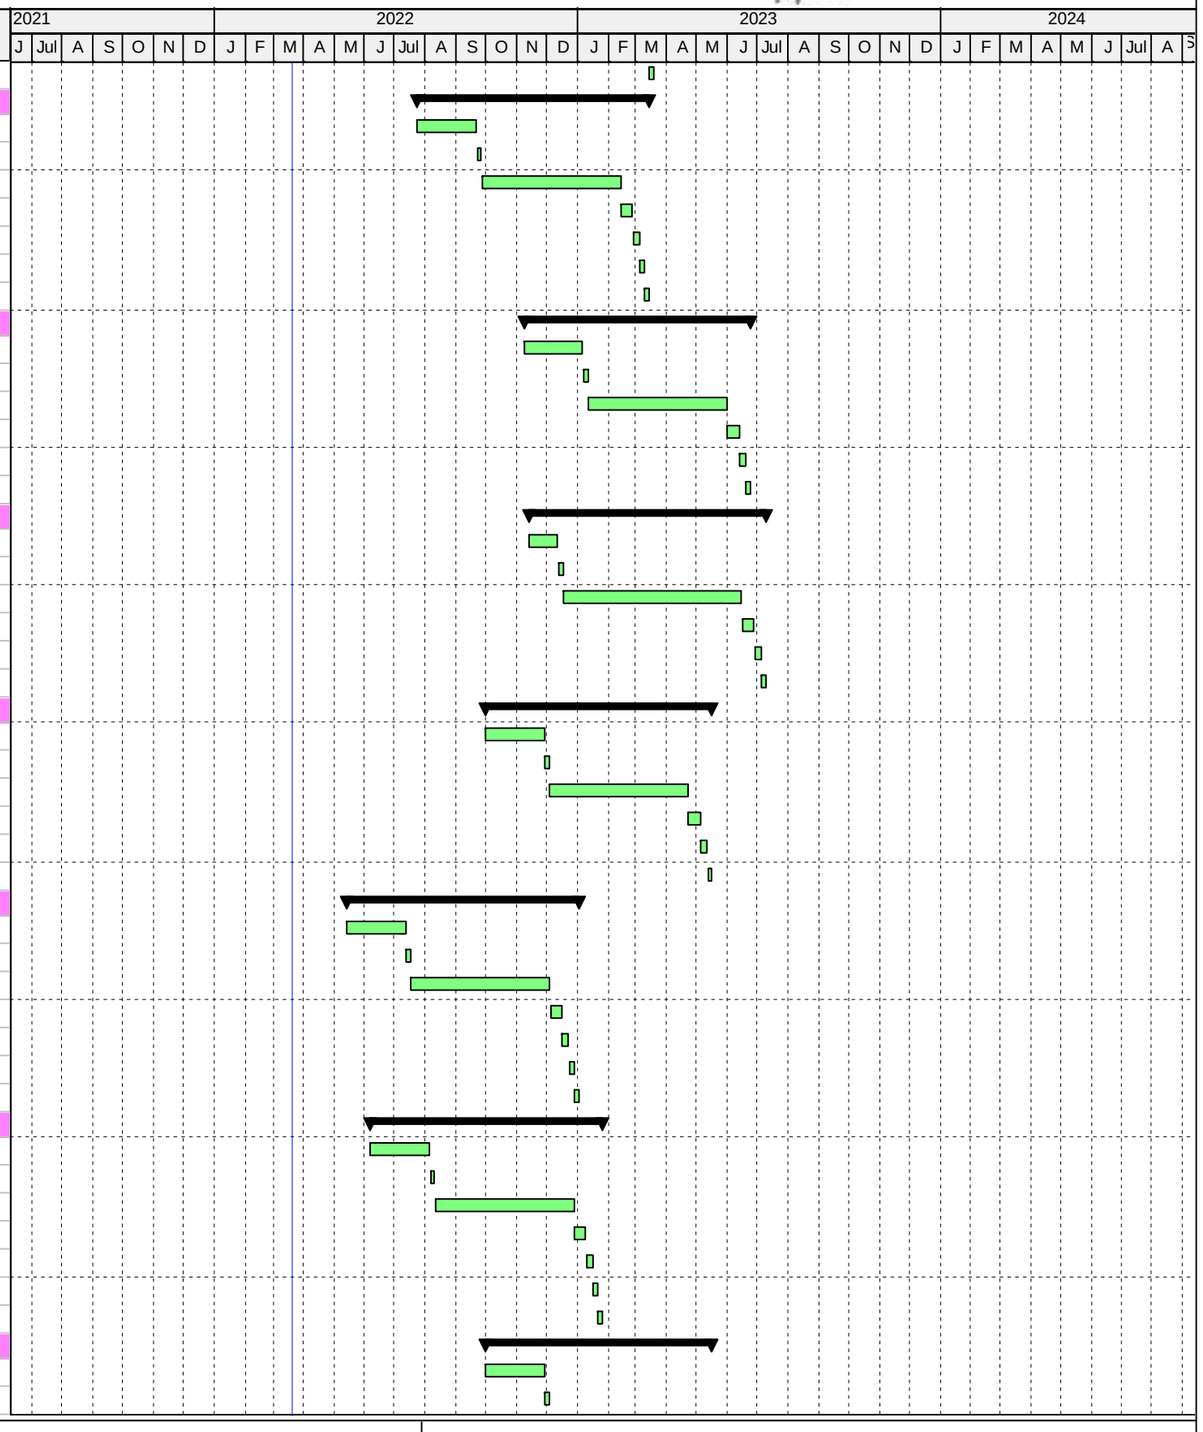


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Manufacturing / Fabrication / Supply	140	0%	$272.58	04-Dec-22	22-Apr-23
P06-E	Final Inspection	12	0%	$54.52	23-Apr-23	04-May-23
P06-E	Delivery On Site	7	0%	$136.29	05-May-23	11-May-23
P06-E	Submitting Vendor Data Book	5	0%	$27.26	12-May-23	16-May-23
Instrument Tube and Fitting - Manifold & W007S		229	0%	$545.17	07-Jul-22	20-Feb-23
P06-E	Tendering & Selection	60	0%	$21.81	07-Jul-22	04-Sep-22
P06-E	Contract Effectiveness / PO	5	0%	$32.71	05-Sep-22	09-Sep-22
P06-E	Manufacturing / Fabrication / Supply	140	0%	$272.58	10-Sep-22	27-Jan-23
P06-E	Final Inspection	12	0%	$54.52	28-Jan-23	08-Feb-23
P06-E	Delivery On Site	7	0%	$136.29	09-Feb-23	15-Feb-23
P06-E	Submitting Vendor Data Book	5	0%	$27.26	16-Feb-23	20-Feb-23
Safety & Fire Fighting		121	0%	$1,785.48	03-Sep-22	01-Jan-23
Fire Safety Sign - Manifold & W007S		79	0%	$357.10	15-Oct-22	01-Jan-23
P06-E	Tendering & Selection	30	0%	$14.28	15-Oct-22	13-Nov-22
P06-E	Contract Effectiveness / PO	5	0%	$21.43	14-Nov-22	18-Nov-22
P06-E	Manufacturing / Fabrication / Supply	20	0%	$178.55	19-Nov-22	08-Dec-22
P06-E	Final Inspection	12	0%	$35.71	09-Dec-22	20-Dec-22
P06-E	Delivery On Site	7	0%	$89.27	21-Dec-22	27-Dec-22
P06-E	Submitting Vendor Data Book	5	0%	$17.85	28-Dec-22	01-Jan-23
Fire Fighting and Safety Equipment - Manifold & W007S		79	0%	$1,428.38	03-Sep-22	20-Nov-22
P06-E	Tendering & Selection	30	0%	$57.14	03-Sep-22	02-Oct-22
P06-E	Contract Effectiveness / PO	5	0%	$85.70	03-Oct-22	07-Oct-22
P06-E	Manufacturing / Fabrication / Supply	20	0%	$714.19	08-Oct-22	27-Oct-22
P06-E	Final Inspection	12	0%	$142.84	28-Oct-22	08-Nov-22
P06-E	Delivery On Site	7	0%	$357.10	09-Nov-22	15-Nov-22
P06-E	Submitting Vendor Data Book	5	0%	$71.42	16-Nov-22	20-Nov-22
Electrical		404	0%	$174,233.15	31-May-22	08-Jul-23
LV Switchgear & MCC - Manifold & W007S		259	0%	$16,900.62	31-May-22	13-Feb-23
P06-E	Tendering & Selection	60	0%	$676.02	31-May-22	29-Jul-22
P06-E	Contract Effectiveness / PO	5	0%	$1,014.04	30-Jul-22	03-Aug-22
P06-E	Manufacturing / Fabrication / Supply	150	0%	$8,450.31	04-Aug-22	31-Dec-22
P06-E	Final Inspection	12	0%	$1,690.06	01-Jan-23	12-Jan-23
P06-E	Delivery On Site	7	0%	$3,380.12	13-Jan-23	19-Jan-23
P06-E	Submitting Vendor Data Book	20	0%	$845.03	20-Jan-23	08-Feb-23
P06-E	Delivering Spare Parts	5	0%	$845.03	09-Feb-23	13-Feb-23
Tray/Ladder and Accessories - Manifold & W007S		179	0%	$1,393.87	22-Jul-22	16-Jan-23
P06-E	Tendering & Selection	30	0%	$55.75	22-Jul-22	20-Aug-22
P06-E	Contract Effectiveness / PO	5	0%	$83.63	21-Aug-22	25-Aug-22
P06-E	Manufacturing / Fabrication / Supply	120	0%	$696.93	26-Aug-22	23-Dec-22
P06-E	Final Inspection	12	0%	$139.39	24-Dec-22	04-Jan-23
P06-E	Delivery On Site	7	0%	$348.47	05-Jan-23	11-Jan-23
P06-E	Submitting Vendor Data Book	5	0%	$69.69	12-Jan-23	16-Jan-23
DC Charger - Manifold & W007S		254	0%	$10,802.46	31-May-22	08-Feb-23
P06-E	Tendering & Selection	25	0%	$432.10	31-May-22	24-Jun-22
P06-E	Contract Effectiveness / PO	5	0%	$648.15	25-Jun-22	29-Jun-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$5,401.23	30-Jun-22	26-Dec-22
P06-E	Final Inspection	12	0%	$1,080.25	27-Dec-22	07-Jan-23
P06-E	Delivery On Site	7	0%	$2,160.49	08-Jan-23	14-Jan-23
P06-E	Submitting Vendor Data Book	20	0%	$540.12	15-Jan-23	03-Feb-23

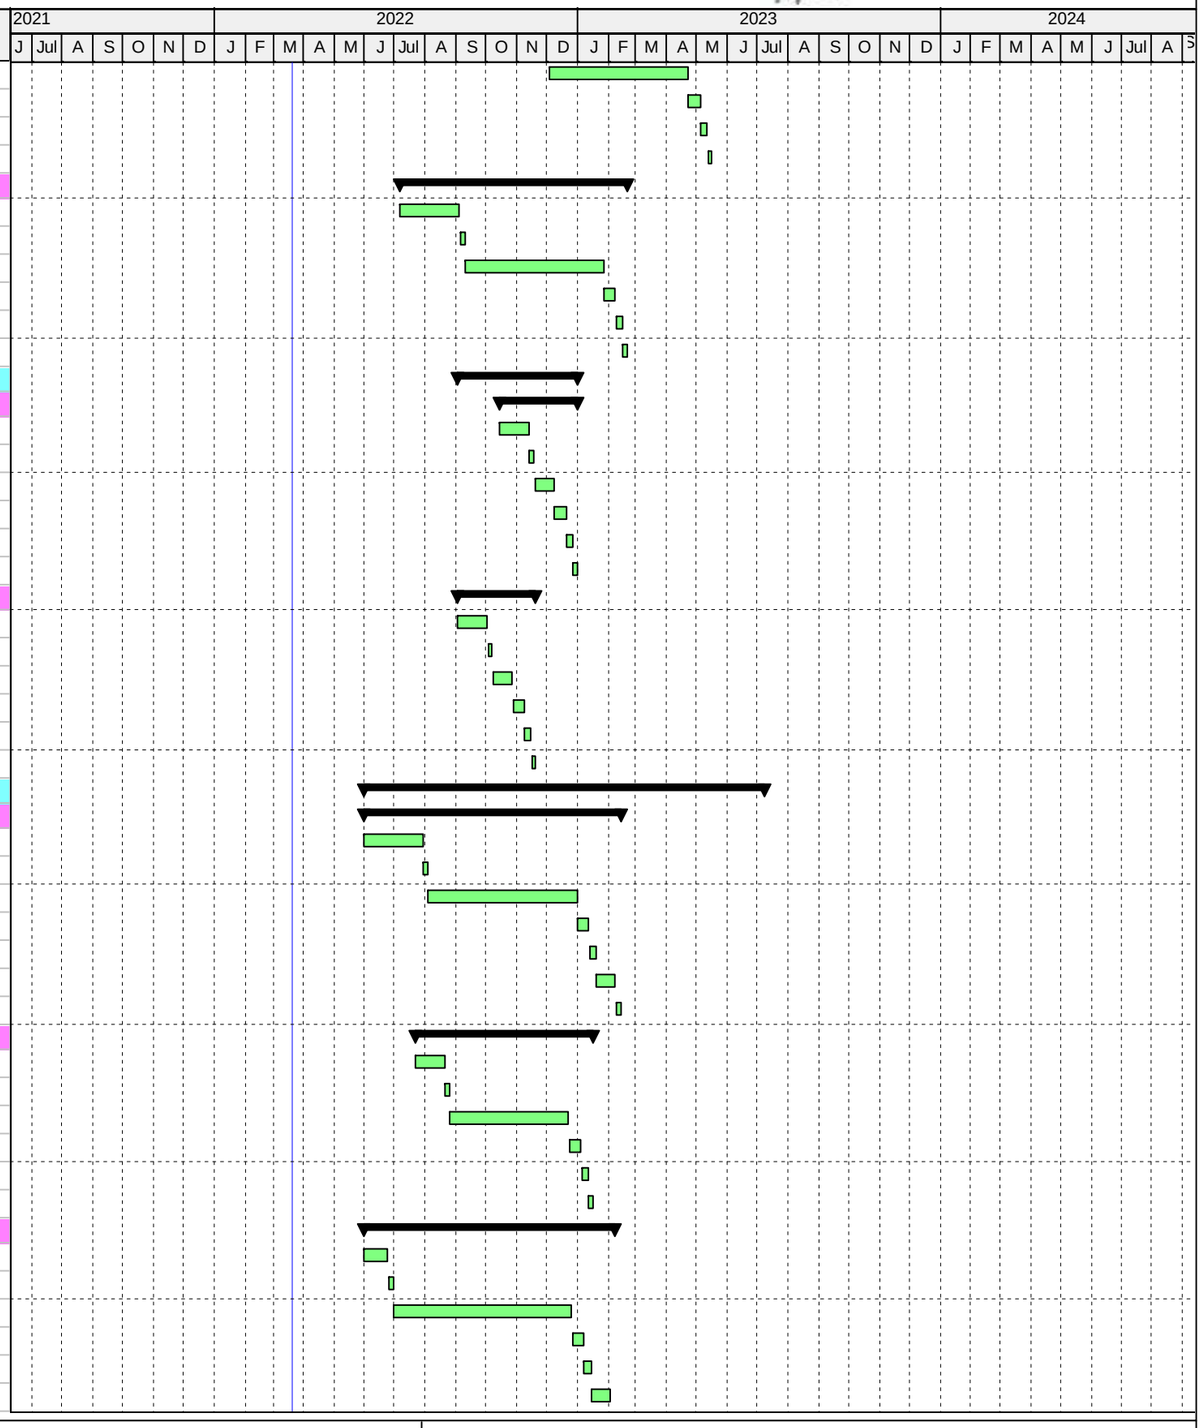


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Delivering Spare Parts	5	0%	$540.12	04-Feb-23	08-Feb-23
Electrical Bulk Items - Manifold & W007S		149	0%	$1,393.87	02-Jun-22	28-Oct-22
P06-E	Tendering & Selection	30	0%	$55.75	02-Jun-22	01-Jul-22
P06-E	Contract Effectiveness / PO	5	0%	$83.63	02-Jul-22	06-Jul-22
P06-E	Manufacturing / Fabrication / Supply	90	0%	$696.93	07-Jul-22	04-Oct-22
P06-E	Final Inspection	12	0%	$139.39	05-Oct-22	16-Oct-22
P06-E	Delivery On Site	7	0%	$348.47	17-Oct-22	23-Oct-22
P06-E	Submitting Vendor Data Book	5	0%	$69.69	24-Oct-22	28-Oct-22
Earthing & Lightning System - Manifold & W007S		154	0%	$6,324.66	06-Sep-22	06-Feb-23
P06-E	Tendering & Selection	60	0%	$252.99	06-Sep-22	04-Nov-22
P06-E	Contract Effectiveness / PO	5	0%	$379.48	05-Nov-22	09-Nov-22
P06-E	Manufacturing / Fabrication / Supply	60	0%	$3,162.33	10-Nov-22	08-Jan-23
P06-E	Final Inspection	12	0%	$632.47	09-Jan-23	20-Jan-23
P06-E	Delivery On Site	7	0%	$1,264.93	21-Jan-23	27-Jan-23
P06-E	Submitting Vendor Data Book	5	0%	$316.23	28-Jan-23	01-Feb-23
P06-E	Delivering Spare Parts	5	0%	$316.23	02-Feb-23	06-Feb-23
UPS System - Manifold & W007S		274	0%	$10,384.30	02-Oct-22	02-Jul-23
P06-E	Tendering & Selection	60	0%	$415.37	02-Oct-22	30-Nov-22
P06-E	Contract Effectiveness / PO	5	0%	$623.06	01-Dec-22	05-Dec-22
P06-E	Manufacturing / Fabrication / Supply	180	0%	$5,192.15	06-Dec-22	03-Jun-23
P06-E	Final Inspection	12	0%	$1,038.43	04-Jun-23	15-Jun-23
P06-E	Delivery On Site	7	0%	$2,076.86	16-Jun-23	22-Jun-23
P06-E	Submitting Vendor Data Book	5	0%	$519.21	23-Jun-23	27-Jun-23
P06-E	Delivering Spare Parts	5	0%	$519.21	28-Jun-23	02-Jul-23
Transformers - W007S		319	0%	$19,514.11	09-Jun-22	23-Apr-23
P06-E	Tendering & Selection	60	0%	$780.56	09-Jun-22	07-Aug-22
P06-E	Contract Effectiveness / PO	5	0%	$1,170.85	08-Aug-22	12-Aug-22
P06-E	Manufacturing / Fabrication / Supply	210	0%	$9,757.06	13-Aug-22	10-Mar-23
P06-E	Final Inspection	12	0%	$1,951.41	11-Mar-23	22-Mar-23
P06-E	Delivery On Site	7	0%	$3,902.82	23-Mar-23	29-Mar-23
P06-E	Submitting Vendor Data Book	20	0%	$975.71	30-Mar-23	18-Apr-23
P06-E	Delivering Spare Parts	5	0%	$975.71	19-Apr-23	23-Apr-23
Capacitor Bank - W007S		214	0%	$3,258.16	09-Jun-22	08-Jan-23
P06-E	Tendering & Selection	30	0%	$130.33	09-Jun-22	08-Jul-22
P06-E	Contract Effectiveness / PO	5	0%	$195.49	09-Jul-22	13-Jul-22
P06-E	Manufacturing / Fabrication / Supply	150	0%	$1,629.08	14-Jul-22	10-Dec-22
P06-E	Final Inspection	12	0%	$325.82	11-Dec-22	22-Dec-22
P06-E	Delivery On Site	7	0%	$651.63	23-Dec-22	29-Dec-22
P06-E	Submitting Vendor Data Book	5	0%	$162.91	30-Dec-22	03-Jan-23
P06-E	Delivering Spare Parts	5	0%	$162.91	04-Jan-23	08-Jan-23
Emergency Diesel Generator - W007S		244	0%	$16,935.46	14-Jun-22	12-Feb-23
P06-E	Tendering & Selection	60	0%	$677.42	14-Jun-22	12-Aug-22
P06-E	Contract Effectiveness / PO	5	0%	$1,016.13	13-Aug-22	17-Aug-22
P06-E	Manufacturing / Fabrication / Supply	135	0%	$8,467.73	18-Aug-22	30-Dec-22
P06-E	Final Inspection	12	0%	$1,693.55	31-Dec-22	11-Jan-23
P06-E	Delivery On Site	7	0%	$3,387.09	12-Jan-23	18-Jan-23
P06-E	Submitting Vendor Data Book	20	0%	$846.77	19-Jan-23	07-Feb-23
P06-E	Delivering Spare Parts	5	0%	$846.77	08-Feb-23	12-Feb-23
Transmission Over head Line Equipment - W007S		179	0%	$65,894.98	02-Jun-22	27-Nov-22

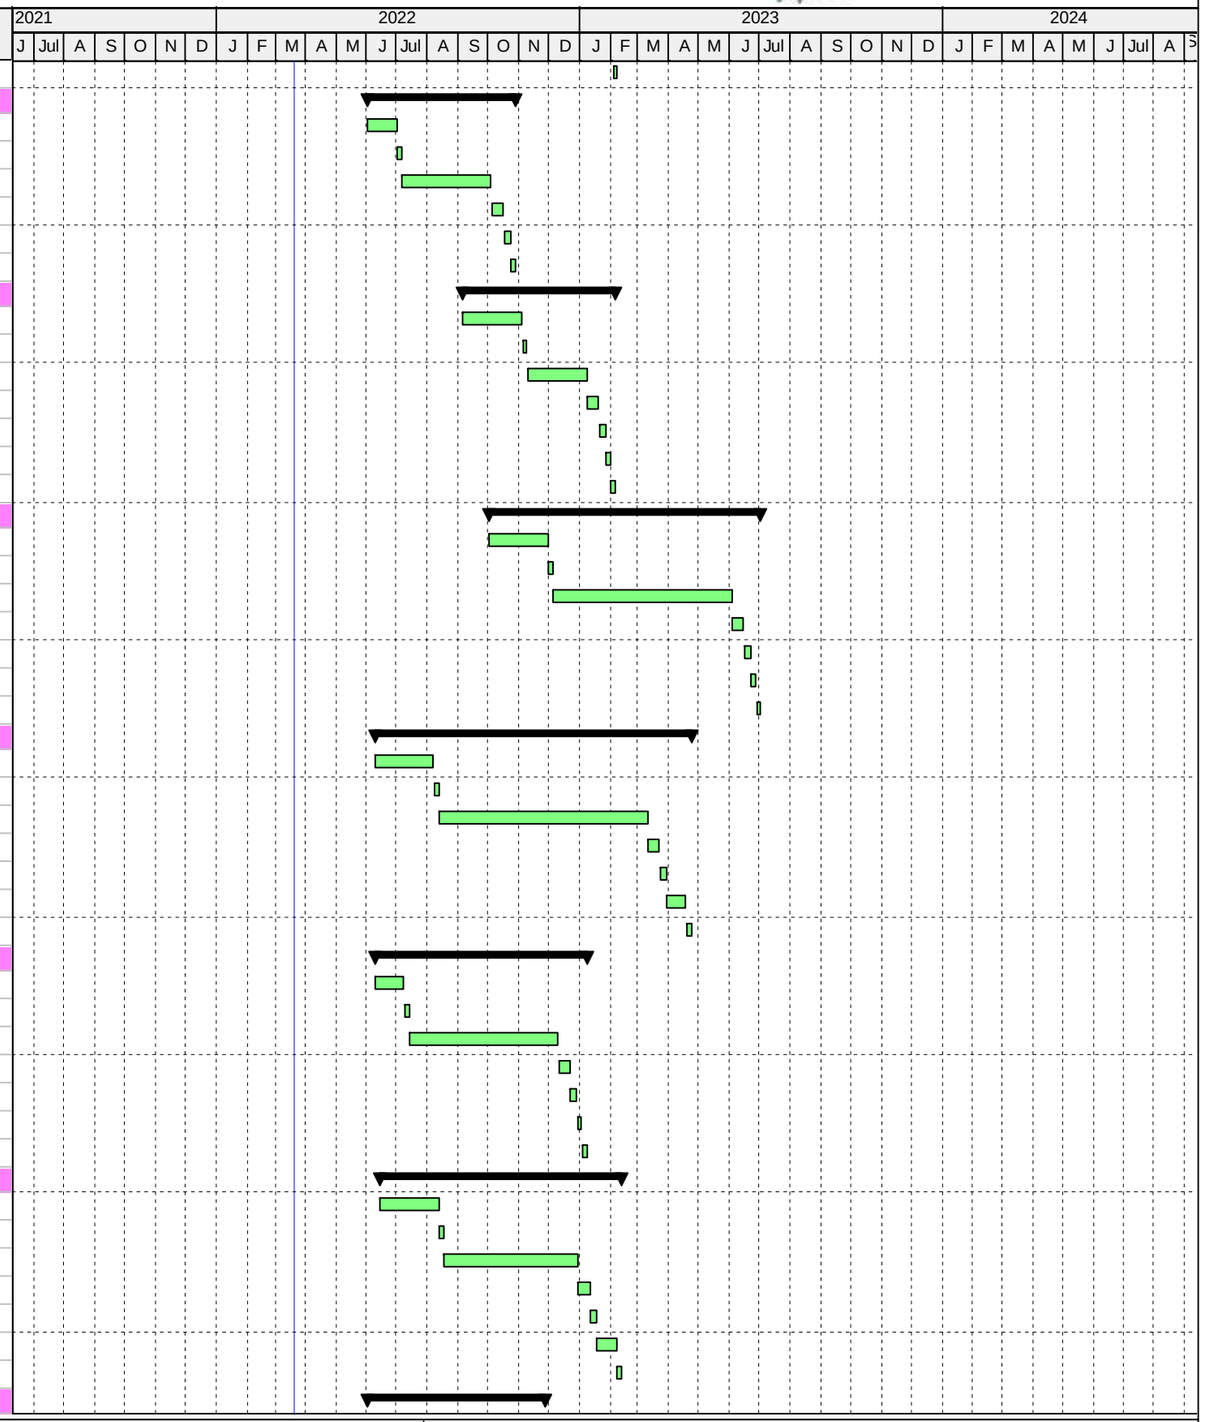

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Tendering & Selection	60	0%	$2,635.80	02-Jun-22	31-Jul-22
P06-E	Contract Effectiveness / PO	5	0%	$3,953.70	01-Aug-22	05-Aug-22
P06-E	Manufacturing / Fabrication / Supply	90	0%	$32,947.49	06-Aug-22	03-Nov-22
P06-E	Final Inspection	12	0%	$6,589.50	04-Nov-22	15-Nov-22
P06-E	Delivery On Site	7	0%	$16,473.74	16-Nov-22	22-Nov-22
P06-E	Submitting Vendor Data Book	5	0%	$3,294.75	23-Nov-22	27-Nov-22
Lighting & Distribution Main Panels - W007S		214	0%	$3,902.82	23-Aug-22	24-Mar-23
P06-E	Tendering & Selection	60	0%	$156.11	23-Aug-22	21-Oct-22
P06-E	Contract Effectiveness / PO	5	0%	$234.17	22-Oct-22	26-Oct-22
P06-E	Manufacturing / Fabrication / Supply	120	0%	$1,951.41	27-Oct-22	23-Feb-23
P06-E	Final Inspection	12	0%	$390.28	24-Feb-23	07-Mar-23
P06-E	Delivery On Site	7	0%	$780.56	08-Mar-23	14-Mar-23
P06-E	Submitting Vendor Data Book	5	0%	$195.14	15-Mar-23	19-Mar-23
P06-E	Delivering Spare Parts	5	0%	$195.14	20-Mar-23	24-Mar-23
Lighting and Small Power Equipment - W007S		179	0%	$7,945.03	16-Nov-22	13-May-23
P06-E	Tendering & Selection	60	0%	$317.80	16-Nov-22	14-Jan-23
P06-E	Contract Effectiveness / PO	5	0%	$476.70	15-Jan-23	19-Jan-23
P06-E	Manufacturing / Fabrication / Supply	85	0%	$3,972.52	20-Jan-23	14-Apr-23
P06-E	Final Inspection	12	0%	$794.50	15-Apr-23	26-Apr-23
P06-E	Delivery On Site	7	0%	$1,589.01	27-Apr-23	03-May-23
P06-E	Submitting Vendor Data Book	5	0%	$397.25	04-May-23	08-May-23
P06-E	Delivering Spare Parts	5	0%	$397.25	09-May-23	13-May-23
Power & Control Cables - Manifold & W007S		224	0%	$9,582.82	27-Nov-22	08-Jul-23
P06-E	Tendering & Selection	30	0%	$383.31	27-Nov-22	26-Dec-22
P06-E	Contract Effectiveness / PO	5	0%	$574.97	27-Dec-22	31-Dec-22
P06-E	Manufacturing / Fabrication / Supply	165	0%	$4,791.41	01-Jan-23	14-Jun-23
P06-E	Final Inspection	12	0%	$958.28	15-Jun-23	26-Jun-23
P06-E	Delivery On Site	7	0%	$2,395.71	27-Jun-23	03-Jul-23
P06-E	Submitting Vendor Data Book	5	0%	$479.14	04-Jul-23	08-Jul-23
Extension of Binak B/C Manifold		318	0%	$164,475.88	13-May-22	26-Mar-23
Mechanical		134	0%	$5,657.97	13-May-22	23-Sep-22
Pumps - Extension of Binak B/C Manifold		134	0%	$5,657.97	13-May-22	23-Sep-22
P06-E	Tendering & Selection	10	0%	$226.32	13-May-22	22-May-22
P06-E	Contract Effectiveness / PO	5	0%	$339.48	23-May-22	27-May-22
P06-E	Manufacturing / Fabrication / Supply	100	0%	$2,828.99	28-May-22	04-Sep-22
P06-E	Final Inspection	7	0%	$565.80	05-Sep-22	11-Sep-22
P06-E	Delivery On Site	7	0%	$1,131.59	12-Sep-22	18-Sep-22
P06-E	Submitting Vendor Data Book	5	0%	$282.90	19-Sep-22	23-Sep-22
P06-E	Delivering Spare Parts	5	0%	$282.90	19-Sep-22	23-Sep-22
Piping		291	0%	$35,888.64	16-May-22	02-Mar-23
Pipes - Extension of Binak B/C Manifold		96	0%	$14,642.56	05-Oct-22	08-Jan-23
P06-E	Tendering & Selection	7	0%	$585.70	05-Oct-22	11-Oct-22
P06-E	Contract Effectiveness / PO	5	0%	$878.55	12-Oct-22	16-Oct-22
P06-E	Manufacturing / Fabrication / Supply	70	0%	$7,321.28	12-Oct-22	20-Dec-22
P06-E	Final Inspection	7	0%	$1,464.26	21-Dec-22	27-Dec-22
P06-E	Delivery On Site	7	0%	$3,660.64	28-Dec-22	03-Jan-23
P06-E	Submitting Vendor Data Book	5	0%	$732.13	04-Jan-23	08-Jan-23
Fittings - Extension of Binak B/C Manifold		114	0%	$1,937.99	04-Nov-22	25-Feb-23
P06-E	Tendering & Selection	10	0%	$77.52	04-Nov-22	13-Nov-22




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Contract Effectiveness / PO	5	0%	$116.28	14-Nov-22	18-Nov-22
P06-E	Manufacturing / Fabrication / Supply	80	0%	$968.99	19-Nov-22	06-Feb-23
P06-E	Final Inspection	7	0%	$193.80	07-Feb-23	13-Feb-23
P06-E	Delivery On Site	7	0%	$484.50	14-Feb-23	20-Feb-23
P06-E	Submitting Vendor Data Book	5	0%	$96.90	21-Feb-23	25-Feb-23
Flanges - Extension of Binak B/C Manifold		114	0%	$1,937.99	04-Nov-22	25-Feb-23
P06-E	Tendering & Selection	10	0%	$77.52	04-Nov-22	13-Nov-22
P06-E	Contract Effectiveness / PO	5	0%	$116.28	14-Nov-22	18-Nov-22
P06-E	Manufacturing / Fabrication / Supply	80	0%	$968.99	19-Nov-22	06-Feb-23
P06-E	Final Inspection	7	0%	$193.80	07-Feb-23	13-Feb-23
P06-E	Delivery On Site	7	0%	$484.50	14-Feb-23	20-Feb-23
P06-E	Submitting Vendor Data Book	5	0%	$96.90	21-Feb-23	25-Feb-23
Manual Valves - Extension of Binak B/C Manifold		119	0%	$8,613.27	04-Nov-22	02-Mar-23
P06-E	Tendering & Selection	10	0%	$344.53	04-Nov-22	13-Nov-22
P06-E	Contract Effectiveness / PO	5	0%	$516.80	14-Nov-22	18-Nov-22
P06-E	Manufacturing / Fabrication / Supply	80	0%	$4,306.64	19-Nov-22	06-Feb-23
P06-E	Final Inspection	7	0%	$861.33	07-Feb-23	13-Feb-23
P06-E	Delivery On Site	7	0%	$1,722.65	14-Feb-23	20-Feb-23
P06-E	Submitting Vendor Data Book	5	0%	$430.66	21-Feb-23	25-Feb-23
P06-E	Delivering Spare Parts	5	0%	$430.66	26-Feb-23	02-Mar-23
Gaskets - Extension of Binak B/C Manifold		114	0%	$2,332.76	04-Nov-22	25-Feb-23
P06-E	Tendering & Selection	10	0%	$93.31	04-Nov-22	13-Nov-22
P06-E	Contract Effectiveness / PO	5	0%	$139.97	14-Nov-22	18-Nov-22
P06-E	Manufacturing / Fabrication / Supply	80	0%	$1,166.38	19-Nov-22	06-Feb-23
P06-E	Final Inspection	7	0%	$233.28	07-Feb-23	13-Feb-23
P06-E	Delivery On Site	7	0%	$583.19	14-Feb-23	20-Feb-23
P06-E	Submitting Vendor Data Book	5	0%	$116.64	21-Feb-23	25-Feb-23
Bolt/Nuts - Extension of Binak B/C Manifold		114	0%	$3,588.86	04-Nov-22	25-Feb-23
P06-E	Tendering & Selection	10	0%	$143.55	04-Nov-22	13-Nov-22
P06-E	Contract Effectiveness / PO	5	0%	$215.33	14-Nov-22	18-Nov-22
P06-E	Manufacturing / Fabrication / Supply	80	0%	$1,794.43	19-Nov-22	06-Feb-23
P06-E	Final Inspection	7	0%	$358.89	07-Feb-23	13-Feb-23
P06-E	Delivery On Site	7	0%	$897.22	14-Feb-23	20-Feb-23
P06-E	Submitting Vendor Data Book	5	0%	$179.44	21-Feb-23	25-Feb-23
Sampling Connection Set - Extension of Binak B/C Manifold		94	0%	$1,937.99	16-May-22	17-Aug-22
P06-E	Tendering & Selection	10	0%	$77.52	16-May-22	25-May-22
P06-E	Contract Effectiveness / PO	5	0%	$116.28	26-May-22	30-May-22
P06-E	Manufacturing / Fabrication / Supply	60	0%	$968.99	31-May-22	29-Jul-22
P06-E	Final Inspection	7	0%	$193.80	30-Jul-22	05-Aug-22
P06-E	Delivery On Site	7	0%	$484.50	06-Aug-22	12-Aug-22
P06-E	Submitting Vendor Data Book	5	0%	$96.90	13-Aug-22	17-Aug-22
Pipe Support - Extension of Binak B/C Manifold		94	0%	$897.22	07-Oct-22	08-Jan-23
P06-E	Tendering & Selection	10	0%	$35.89	07-Oct-22	16-Oct-22
P06-E	Contract Effectiveness / PO	5	0%	$53.83	17-Oct-22	21-Oct-22
P06-E	Manufacturing / Fabrication / Supply	60	0%	$448.61	22-Oct-22	20-Dec-22
P06-E	Final Inspection	7	0%	$89.72	21-Dec-22	27-Dec-22
P06-E	Delivery On Site	7	0%	$224.30	28-Dec-22	03-Jan-23
P06-E	Submitting Vendor Data Book	5	0%	$44.86	04-Jan-23	08-Jan-23
Control & Instrumentation		317	0%	$90,626.21	14-May-22	26-Mar-23

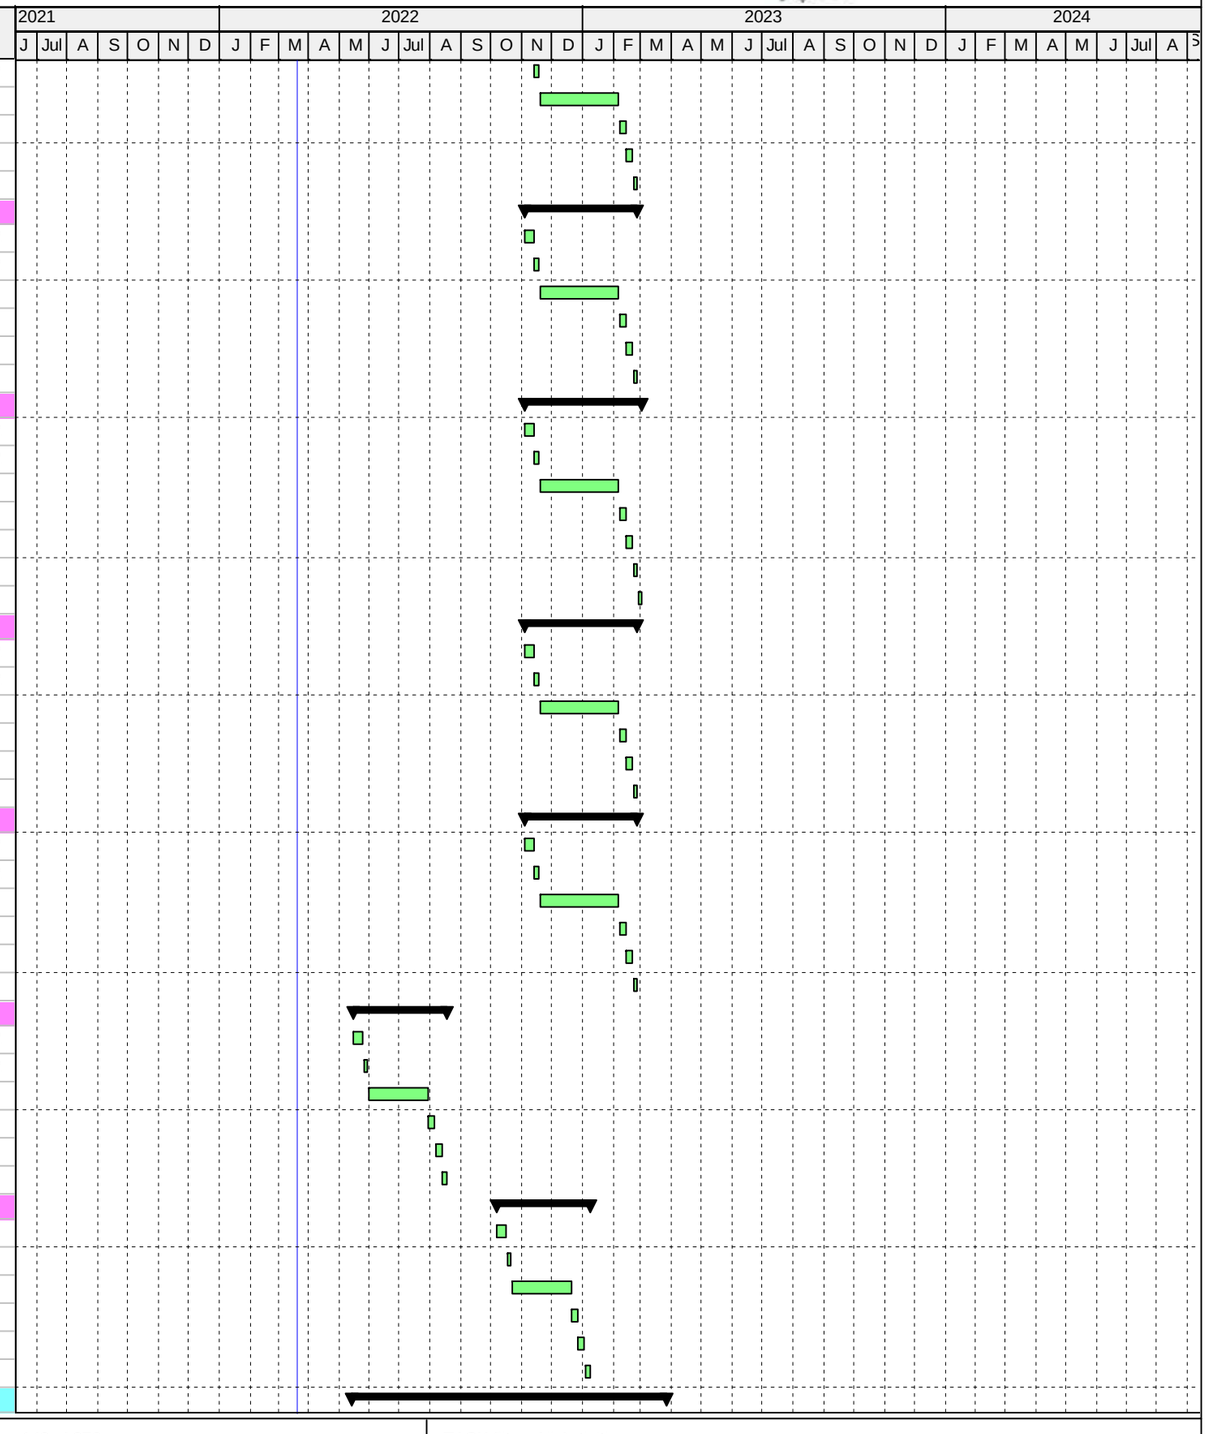


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
DCS System - Extension of Binak B/C Manifold		169	0%	$37,156.75	21-May-22	05-Nov-22
P06-E	Tendering & Selection	20	0%	$1,486.27	21-May-22	09-Jun-22
P06-E	Contract Effectiveness / PO	5	0%	$2,229.40	10-Jun-22	14-Jun-22
P06-E	Manufacturing / Fabrication / Supply	120	0%	$18,578.37	15-Jun-22	12-Oct-22
P06-E	Final Inspection	7	0%	$3,715.67	13-Oct-22	19-Oct-22
P06-E	Delivery On Site	7	0%	$7,431.35	20-Oct-22	26-Oct-22
P06-E	Submitting Vendor Data Book	5	0%	$1,857.84	27-Oct-22	31-Oct-22
P06-E	Delivering Spare Parts	5	0%	$1,857.84	01-Nov-22	05-Nov-22
F&G System - Extension of Binak B/C Manifold		169	0%	$18,125.24	05-Jun-22	20-Nov-22
P06-E	Tendering & Selection	20	0%	$725.01	05-Jun-22	24-Jun-22
P06-E	Contract Effectiveness / PO	5	0%	$1,087.51	25-Jun-22	29-Jun-22
P06-E	Manufacturing / Fabrication / Supply	120	0%	$9,062.62	30-Jun-22	27-Oct-22
P06-E	Final Inspection	7	0%	$1,812.52	28-Oct-22	03-Nov-22
P06-E	Delivery On Site	7	0%	$3,625.05	04-Nov-22	10-Nov-22
P06-E	Submitting Vendor Data Book	5	0%	$906.26	11-Nov-22	15-Nov-22
P06-E	Delivering Spare Parts	5	0%	$906.26	16-Nov-22	20-Nov-22
ESD System - Extension of Binak B/C Manifold		169	0%	$26,281.60	05-Jun-22	20-Nov-22
P06-E	Tendering & Selection	20	0%	$1,051.26	05-Jun-22	24-Jun-22
P06-E	Contract Effectiveness / PO	5	0%	$1,576.90	25-Jun-22	29-Jun-22
P06-E	Manufacturing / Fabrication / Supply	120	0%	$13,140.80	30-Jun-22	27-Oct-22
P06-E	Final Inspection	7	0%	$2,628.16	28-Oct-22	03-Nov-22
P06-E	Delivery On Site	7	0%	$5,256.32	04-Nov-22	10-Nov-22
P06-E	Submitting Vendor Data Book	5	0%	$1,314.08	11-Nov-22	15-Nov-22
P06-E	Delivering Spare Parts	5	0%	$1,314.08	16-Nov-22	20-Nov-22
ON/OFF & Shutdown Valves - Extension of Binak B/C Manifold		149	0%	$996.89	02-Jun-22	28-Oct-22
P06-E	Tendering & Selection	20	0%	$39.88	02-Jun-22	21-Jun-22
P06-E	Contract Effectiveness / PO	5	0%	$59.81	22-Jun-22	26-Jun-22
P06-E	Manufacturing / Fabrication / Supply	100	0%	$498.44	27-Jun-22	04-Oct-22
P06-E	Final Inspection	7	0%	$99.69	05-Oct-22	11-Oct-22
P06-E	Delivery On Site	7	0%	$199.38	12-Oct-22	18-Oct-22
P06-E	Submitting Vendor Data Book	5	0%	$49.84	19-Oct-22	23-Oct-22
P06-E	Delivering Spare Parts	5	0%	$49.84	24-Oct-22	28-Oct-22
Control Valves		144	0%	$996.89	04-Jul-22	24-Nov-22
P06-E	Tendering & Selection	15	0%	$39.88	04-Jul-22	18-Jul-22
P06-E	Contract Effectiveness / PO	5	0%	$59.81	19-Jul-22	23-Jul-22
P06-E	Manufacturing / Fabrication / Supply	100	0%	$498.44	24-Jul-22	31-Oct-22
P06-E	Final Inspection	7	0%	$99.69	01-Nov-22	07-Nov-22
P06-E	Delivery On Site	7	0%	$199.38	08-Nov-22	14-Nov-22
P06-E	Submitting Vendor Data Book	5	0%	$49.84	15-Nov-22	19-Nov-22
P06-E	Delivering Spare Parts	5	0%	$49.84	20-Nov-22	24-Nov-22
Pressure Safety Valves (PSV)		144	0%	$996.89	15-Jul-22	05-Dec-22
P06-E	Tendering & Selection	15	0%	$39.88	15-Jul-22	29-Jul-22
P06-E	Contract Effectiveness / PO	5	0%	$59.81	30-Jul-22	03-Aug-22
P06-E	Manufacturing / Fabrication / Supply	100	0%	$498.44	04-Aug-22	11-Nov-22
P06-E	Final Inspection	7	0%	$99.69	12-Nov-22	18-Nov-22
P06-E	Delivery On Site	7	0%	$199.38	19-Nov-22	25-Nov-22
P06-E	Submitting Vendor Data Book	5	0%	$49.84	26-Nov-22	30-Nov-22
P06-E	Delivering Spare Parts	5	0%	$49.84	01-Dec-22	05-Dec-22
F&G Devices		154	0%	$860.95	04-Aug-22	04-Jan-23

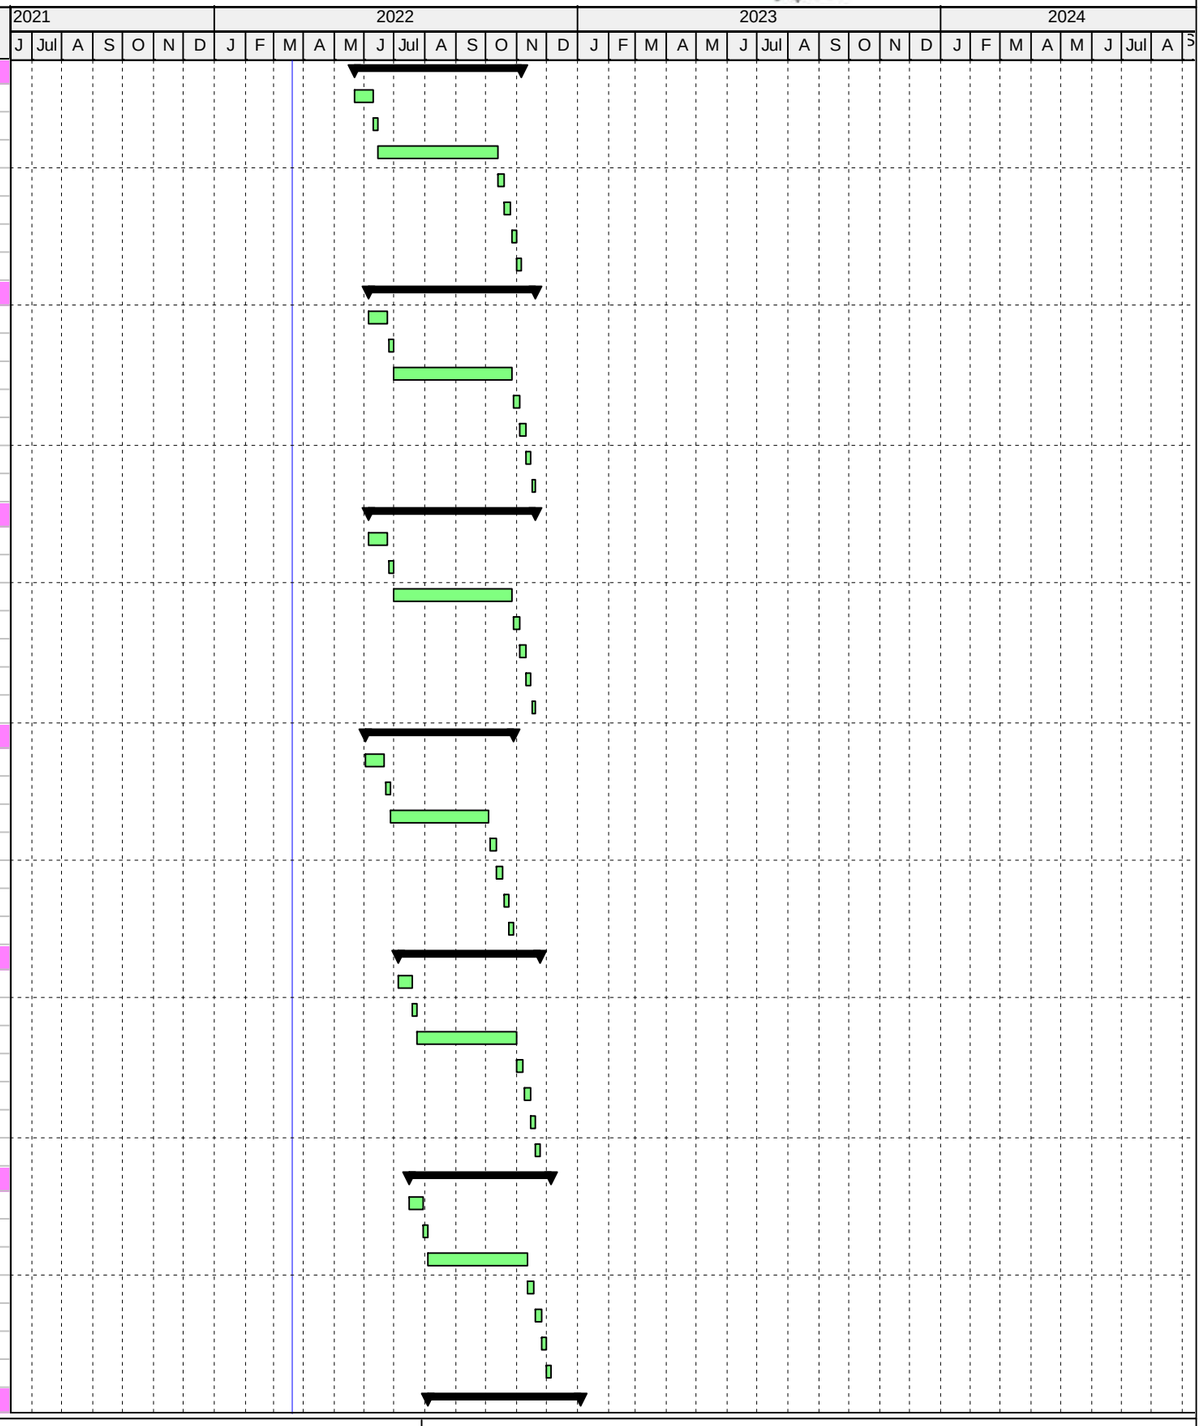


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Tendering & Selection	15	0%	$34.44	04-Aug-22	18-Aug-22
P06-E	Contract Effectiveness / PO	5	0%	$51.66	19-Aug-22	23-Aug-22
P06-E	Manufacturing / Fabrication / Supply	110	0%	$430.47	24-Aug-22	11-Dec-22
P06-E	Final Inspection	7	0%	$86.09	12-Dec-22	18-Dec-22
P06-E	Submitting Vendor Data Book	7	0%	$172.19	24-Dec-22	30-Dec-22
P06-E	Delivery On Site	5	0%	$43.05	19-Dec-22	23-Dec-22
P06-E	Delivering Spare Parts	5	0%	$43.05	31-Dec-22	04-Jan-23
Orifice and Restriction Orifice Plate		159	0%	$371.57	25-May-22	30-Oct-22
P06-E	Tendering & Selection	15	0%	$14.86	25-May-22	08-Jun-22
P06-E	Contract Effectiveness / PO	5	0%	$22.29	09-Jun-22	13-Jun-22
P06-E	Manufacturing / Fabrication / Supply	110	0%	$185.78	14-Jun-22	01-Oct-22
P06-E	Final Inspection	12	0%	$37.16	02-Oct-22	13-Oct-22
P06-E	Delivery On Site	7	0%	$74.31	14-Oct-22	20-Oct-22
P06-E	Submitting Vendor Data Book	5	0%	$18.58	21-Oct-22	25-Oct-22
P06-E	Delivering Spare Parts	5	0%	$18.58	26-Oct-22	30-Oct-22
Corrosion Coupon/Probe		159	0%	$371.57	21-May-22	26-Oct-22
P06-E	Tendering & Selection	15	0%	$14.86	21-May-22	04-Jun-22
P06-E	Contract Effectiveness / PO	5	0%	$22.29	05-Jun-22	09-Jun-22
P06-E	Manufacturing / Fabrication / Supply	110	0%	$185.78	10-Jun-22	27-Sep-22
P06-E	Final Inspection	12	0%	$37.16	28-Sep-22	09-Oct-22
P06-E	Delivery On Site	7	0%	$74.31	10-Oct-22	16-Oct-22
P06-E	Submitting Vendor Data Book	5	0%	$18.58	17-Oct-22	21-Oct-22
P06-E	Delivering Spare Parts	5	0%	$18.58	22-Oct-22	26-Oct-22
Pressure Transmitter		159	0%	$498.44	18-Jun-22	23-Nov-22
P06-E	Tendering & Selection	15	0%	$19.94	18-Jun-22	02-Jul-22
P06-E	Contract Effectiveness / PO	5	0%	$29.91	03-Jul-22	07-Jul-22
P06-E	Manufacturing / Fabrication / Supply	110	0%	$249.22	08-Jul-22	25-Oct-22
P06-E	Final Inspection	12	0%	$49.84	26-Oct-22	06-Nov-22
P06-E	Delivery On Site	7	0%	$99.69	07-Nov-22	13-Nov-22
P06-E	Submitting Vendor Data Book	5	0%	$24.92	14-Nov-22	18-Nov-22
P06-E	Delivering Spare Parts	5	0%	$24.92	19-Nov-22	23-Nov-22
Flow Transmitter/ Diff. Pressure Transmitter		159	0%	$498.44	14-May-22	19-Oct-22
P06-E	Tendering & Selection	15	0%	$19.94	14-May-22	28-May-22
P06-E	Contract Effectiveness / PO	5	0%	$29.91	29-May-22	02-Jun-22
P06-E	Manufacturing / Fabrication / Supply	110	0%	$249.22	03-Jun-22	20-Sep-22
P06-E	Final Inspection	12	0%	$49.84	21-Sep-22	02-Oct-22
P06-E	Delivery On Site	7	0%	$99.69	03-Oct-22	09-Oct-22
P06-E	Submitting Vendor Data Book	5	0%	$24.92	10-Oct-22	14-Oct-22
P06-E	Delivering Spare Parts	5	0%	$24.92	15-Oct-22	19-Oct-22
Instrument/F&G Cable		129	0%	$616.26	08-Nov-22	16-Mar-23
P06-E	Tendering & Selection	15	0%	$24.65	08-Nov-22	22-Nov-22
P06-E	Contract Effectiveness / PO	5	0%	$36.98	23-Nov-22	27-Nov-22
P06-E	Manufacturing / Fabrication / Supply	90	0%	$308.13	28-Nov-22	25-Feb-23
P06-E	Final Inspection	7	0%	$61.63	26-Feb-23	04-Mar-23
P06-E	Delivery On Site	7	0%	$154.06	05-Mar-23	11-Mar-23
P06-E	Submitting Vendor Data Book	5	0%	$30.81	12-Mar-23	16-Mar-23
Instrument/F&G Junction box and Gland		144	0%	$498.44	03-Nov-22	26-Mar-23
P06-E	Tendering & Selection	15	0%	$19.94	03-Nov-22	17-Nov-22
P06-E	Contract Effectiveness / PO	5	0%	$29.91	18-Nov-22	22-Nov-22

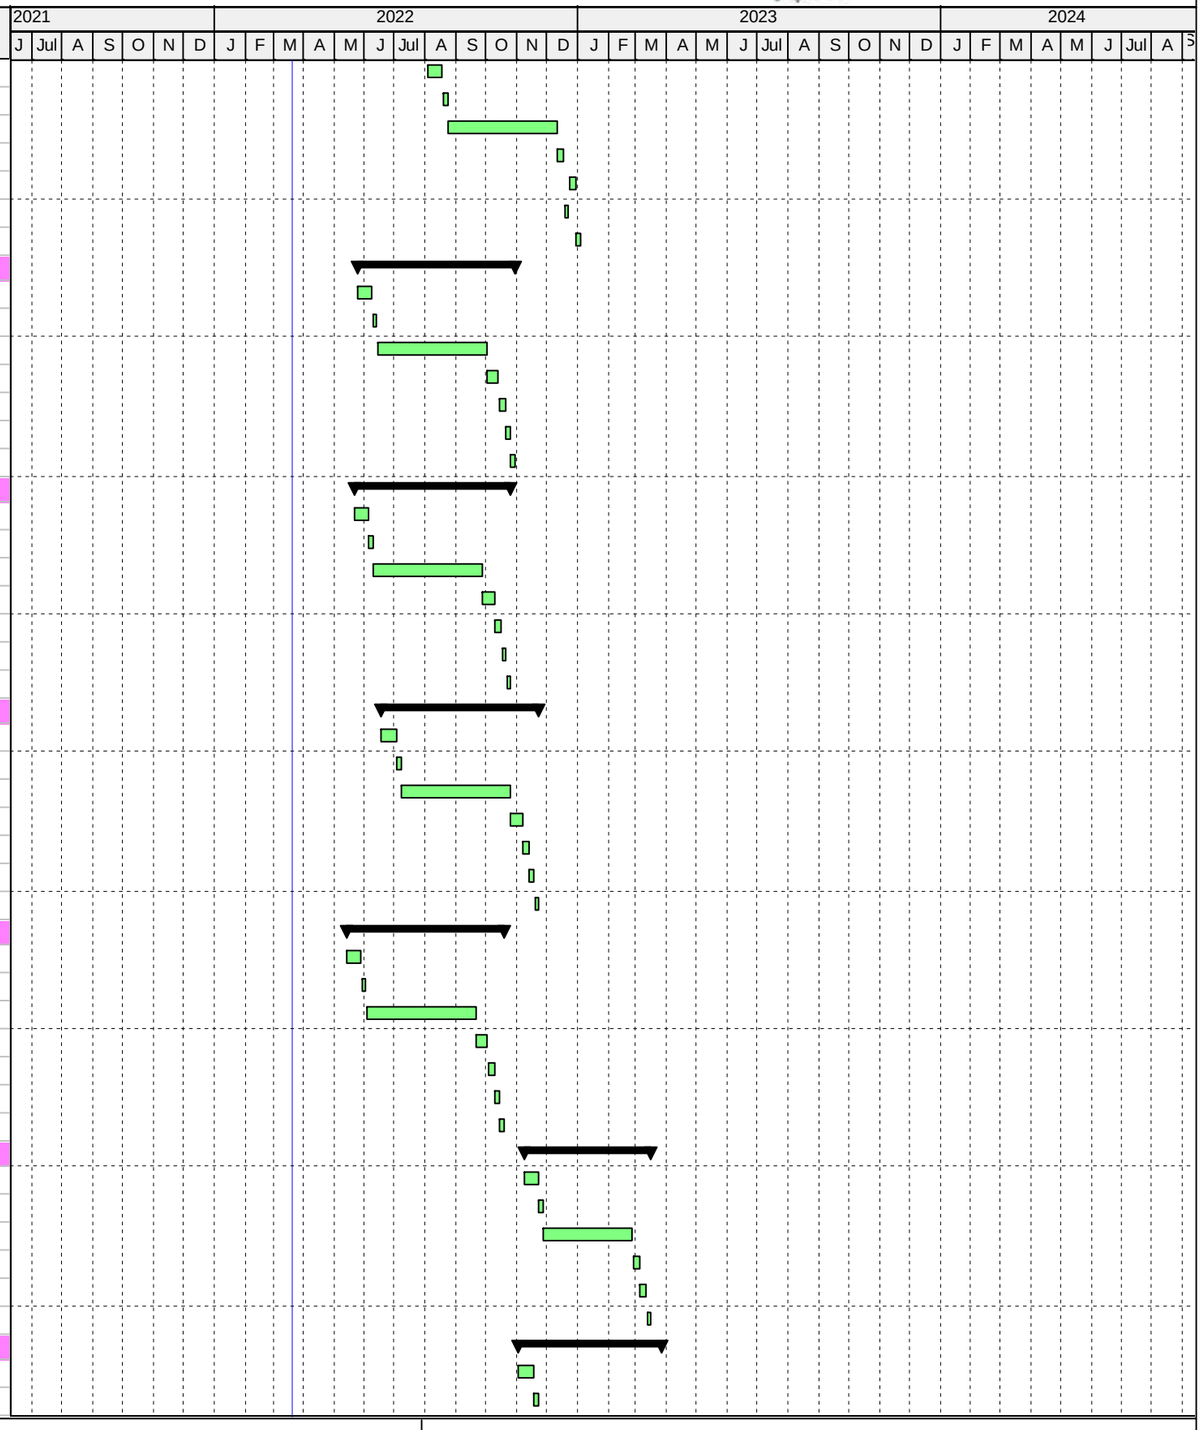


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Manufacturing / Fabrication / Supply	100	0%	$249.22	23-Nov-22	02-Mar-23
P06-E	Final Inspection	12	0%	$49.84	03-Mar-23	14-Mar-23
P06-E	Delivery On Site	7	0%	$124.61	15-Mar-23	21-Mar-23
P06-E	Submitting Vendor Data Book	5	0%	$24.92	22-Mar-23	26-Mar-23
Instrument Installation Accessories		139	0%	$371.57	30-Sep-22	15-Feb-23
P06-E	Tendering & Selection	15	0%	$14.86	30-Sep-22	14-Oct-22
P06-E	Contract Effectiveness / PO	5	0%	$22.29	15-Oct-22	19-Oct-22
P06-E	Manufacturing / Fabrication / Supply	100	0%	$185.78	20-Oct-22	27-Jan-23
P06-E	Final Inspection	7	0%	$37.16	28-Jan-23	03-Feb-23
P06-E	Delivery On Site	7	0%	$92.89	04-Feb-23	10-Feb-23
P06-E	Submitting Vendor Data Book	5	0%	$18.58	11-Feb-23	15-Feb-23
Differential Pressure/Pressure Gauge		149	0%	$498.44	14-May-22	09-Oct-22
P06-E	Tendering & Selection	15	0%	$19.94	14-May-22	28-May-22
P06-E	Contract Effectiveness / PO	5	0%	$29.91	29-May-22	02-Jun-22
P06-E	Manufacturing / Fabrication / Supply	100	0%	$249.22	03-Jun-22	10-Sep-22
P06-E	Final Inspection	12	0%	$49.84	11-Sep-22	22-Sep-22
P06-E	Delivery On Site	7	0%	$99.69	23-Sep-22	29-Sep-22
P06-E	Submitting Vendor Data Book	5	0%	$24.92	30-Sep-22	04-Oct-22
P06-E	Delivering Spare Parts	5	0%	$24.92	05-Oct-22	09-Oct-22
Temperature Gauge		149	0%	$498.44	07-Jun-22	02-Nov-22
P06-E	Tendering & Selection	15	0%	$19.94	07-Jun-22	21-Jun-22
P06-E	Contract Effectiveness / PO	5	0%	$29.91	22-Jun-22	26-Jun-22
P06-E	Manufacturing / Fabrication / Supply	100	0%	$249.22	27-Jun-22	04-Oct-22
P06-E	Final Inspection	12	0%	$49.84	05-Oct-22	16-Oct-22
P06-E	Delivery On Site	7	0%	$99.69	17-Oct-22	23-Oct-22
P06-E	Submitting Vendor Data Book	5	0%	$24.92	24-Oct-22	28-Oct-22
P06-E	Delivering Spare Parts	5	0%	$24.92	29-Oct-22	02-Nov-22
Instrument Tube and Fitting		129	0%	$616.26	07-Jul-22	12-Nov-22
P06-E	Tendering & Selection	10	0%	$24.65	07-Jul-22	16-Jul-22
P06-E	Contract Effectiveness / PO	5	0%	$36.98	17-Jul-22	21-Jul-22
P06-E	Manufacturing / Fabrication / Supply	90	0%	$308.13	22-Jul-22	19-Oct-22
P06-E	Final Inspection	12	0%	$61.63	20-Oct-22	31-Oct-22
P06-E	Delivery On Site	7	0%	$154.06	01-Nov-22	07-Nov-22
P06-E	Submitting Vendor Data Book	5	0%	$30.81	08-Nov-22	12-Nov-22
Instrument Cable Tray		134	0%	$371.57	30-Sep-22	10-Feb-23
P06-E	Tendering & Selection	15	0%	$14.86	30-Sep-22	14-Oct-22
P06-E	Contract Effectiveness / PO	5	0%	$22.29	15-Oct-22	19-Oct-22
P06-E	Manufacturing / Fabrication / Supply	90	0%	$185.78	20-Oct-22	17-Jan-23
P06-E	Final Inspection	12	0%	$37.16	18-Jan-23	29-Jan-23
P06-E	Delivery On Site	7	0%	$92.89	30-Jan-23	05-Feb-23
P06-E	Submitting Vendor Data Book	5	0%	$18.58	06-Feb-23	10-Feb-23
Safety & Fire Fighting		121	0%	$1,792.79	03-Sep-22	01-Jan-23
Fire Fighting and Safety Equipment - Extension of Binak B/C Ma		79	0%	$1,335.81	03-Sep-22	20-Nov-22
P06-E	Tendering & Selection	30	0%	$53.43	03-Sep-22	02-Oct-22
P06-E	Contract Effectiveness / PO	5	0%	$80.15	03-Oct-22	07-Oct-22
P06-E	Manufacturing / Fabrication / Supply	20	0%	$667.90	08-Oct-22	27-Oct-22
P06-E	Final Inspection	12	0%	$133.58	28-Oct-22	08-Nov-22
P06-E	Delivery On Site	7	0%	$333.95	09-Nov-22	15-Nov-22
P06-E	Submitting Vendor Data Book	5	0%	$66.79	16-Nov-22	20-Nov-22

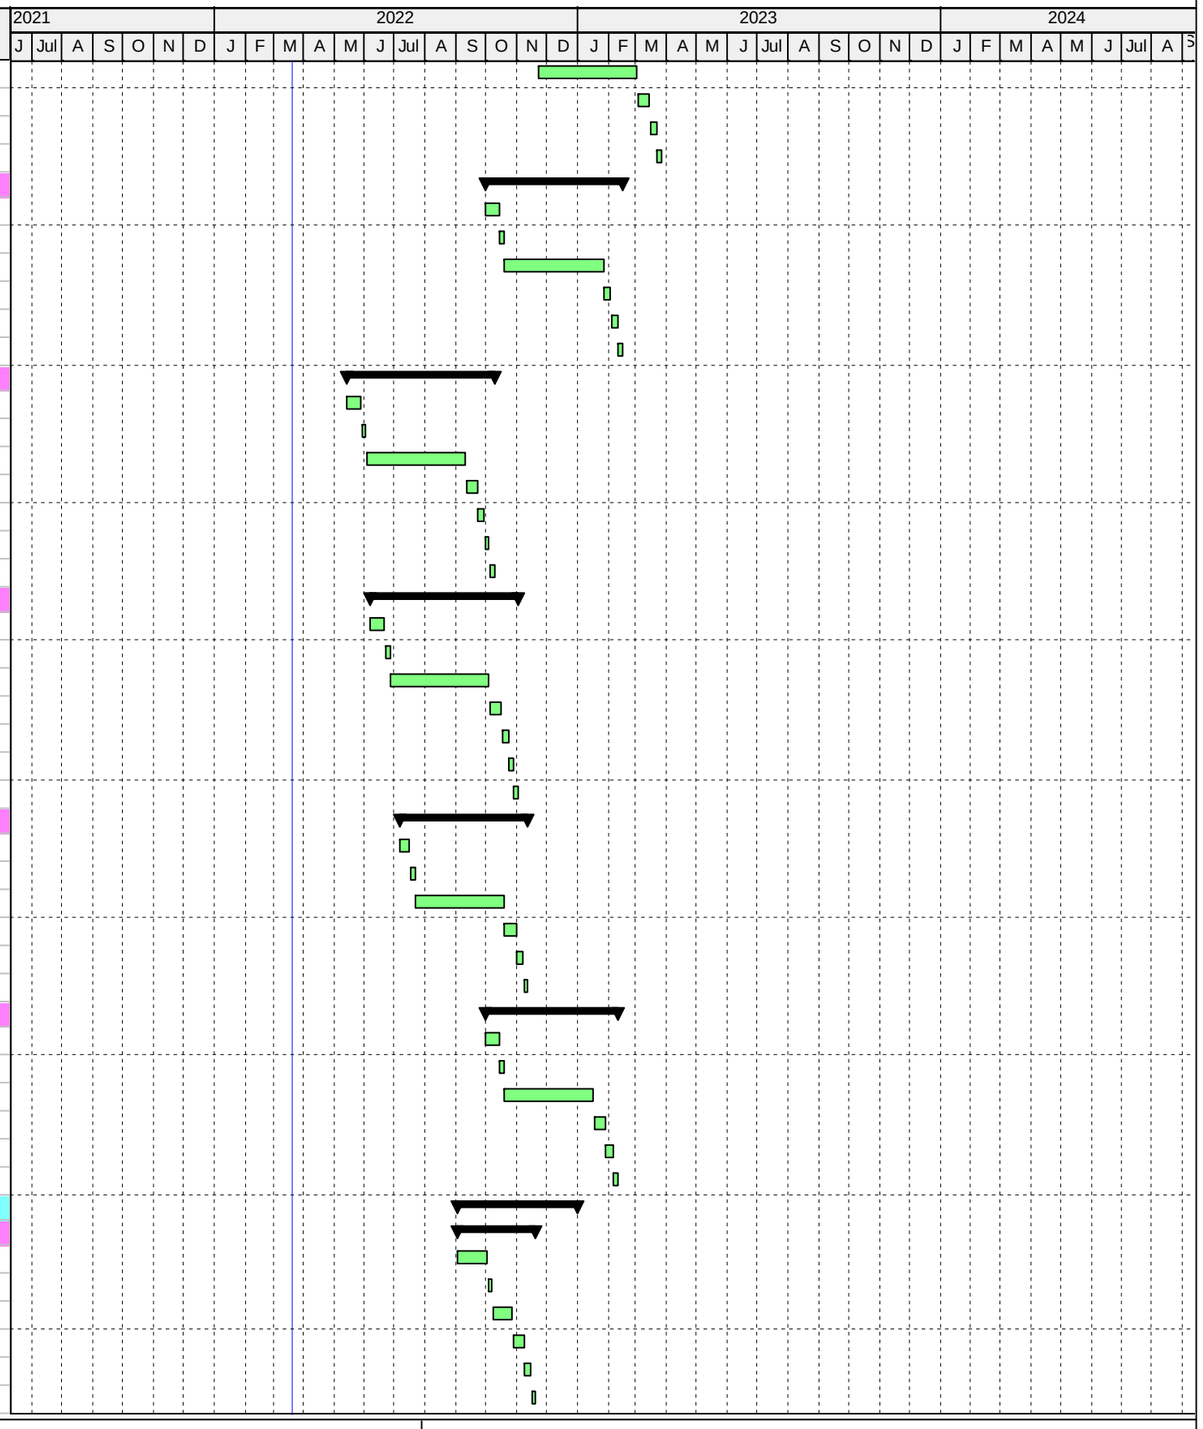


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Fire Safety Sign - Extension of Binak B/C Manifold		79	0%	$456.98	15-Oct-22	01-Jan-23
P06-E	Tendering & Selection	30	0%	$18.28	15-Oct-22	13-Nov-22
P06-E	Contract Effectiveness / PO	5	0%	$27.42	14-Nov-22	18-Nov-22
P06-E	Manufacturing / Fabrication / Supply	20	0%	$228.49	19-Nov-22	08-Dec-22
P06-E	Final Inspection	12	0%	$45.70	09-Dec-22	20-Dec-22
P06-E	Delivery On Site	7	0%	$114.25	21-Dec-22	27-Dec-22
P06-E	Submitting Vendor Data Book	5	0%	$22.85	28-Dec-22	01-Jan-23
Electrical		284	0%	$30,510.28	05-Jun-22	15-Mar-23
LV Switchgear & MCC - Extension of Binak B/C Manifold		154	0%	$4,896.90	05-Jun-22	05-Nov-22
P06-E	Tendering & Selection	15	0%	$195.88	05-Jun-22	19-Jun-22
P06-E	Contract Effectiveness / PO	5	0%	$293.81	20-Jun-22	24-Jun-22
P06-E	Manufacturing / Fabrication / Supply	110	0%	$2,448.45	25-Jun-22	12-Oct-22
P06-E	Final Inspection	7	0%	$489.69	13-Oct-22	19-Oct-22
P06-E	Delivery On Site	7	0%	$979.38	20-Oct-22	26-Oct-22
P06-E	Submitting Vendor Data Book	5	0%	$244.84	27-Oct-22	31-Oct-22
P06-E	Delivering Spare Parts	5	0%	$244.84	01-Nov-22	05-Nov-22
UPS System - Extension of Binak B/C Manifold		144	0%	$12,237.67	12-Sep-22	02-Feb-23
P06-E	Tendering & Selection	15	0%	$489.51	12-Sep-22	26-Sep-22
P06-E	Contract Effectiveness / PO	5	0%	$734.26	27-Sep-22	01-Oct-22
P06-E	Manufacturing / Fabrication / Supply	100	0%	$6,118.84	02-Oct-22	09-Jan-23
P06-E	Final Inspection	7	0%	$1,223.77	10-Jan-23	16-Jan-23
P06-E	Delivery On Site	7	0%	$2,447.53	17-Jan-23	23-Jan-23
P06-E	Submitting Vendor Data Book	5	0%	$611.88	24-Jan-23	28-Jan-23
P06-E	Delivering Spare Parts	5	0%	$611.88	29-Jan-23	02-Feb-23
DC Charger - Extension of Binak B/C Manifold		154	0%	$8,155.40	05-Jun-22	05-Nov-22
P06-E	Tendering & Selection	15	0%	$326.22	05-Jun-22	19-Jun-22
P06-E	Contract Effectiveness / PO	5	0%	$489.32	20-Jun-22	24-Jun-22
P06-E	Manufacturing / Fabrication / Supply	110	0%	$4,077.70	25-Jun-22	12-Oct-22
P06-E	Final Inspection	7	0%	$815.54	13-Oct-22	19-Oct-22
P06-E	Delivery On Site	7	0%	$1,631.08	20-Oct-22	26-Oct-22
P06-E	Submitting Vendor Data Book	5	0%	$407.77	27-Oct-22	31-Oct-22
P06-E	Delivering Spare Parts	5	0%	$407.77	01-Nov-22	05-Nov-22
Earthing & Lightning System		149	0%	$814.62	11-Sep-22	06-Feb-23
P06-E	Tendering & Selection	15	0%	$32.58	11-Sep-22	25-Sep-22
P06-E	Contract Effectiveness / PO	5	0%	$48.88	26-Sep-22	30-Sep-22
P06-E	Manufacturing / Fabrication / Supply	110	0%	$407.31	01-Oct-22	18-Jan-23
P06-E	Final Inspection	7	0%	$81.46	19-Jan-23	25-Jan-23
P06-E	Delivering Spare Parts	5	0%	$162.92	02-Feb-23	06-Feb-23
P06-E	Submitting Vendor Data Book	5	0%	$40.73	02-Feb-23	06-Feb-23
P06-E	Delivery On Site	7	0%	$40.73	26-Jan-23	01-Feb-23
Power & Control Cables - Extension of Binak B/C Manifold		99	0%	$1,632.30	07-Dec-22	15-Mar-23
P06-E	Tendering & Selection	15	0%	$65.29	07-Dec-22	21-Dec-22
P06-E	Contract Effectiveness / PO	5	0%	$97.94	22-Dec-22	26-Dec-22
P06-E	Manufacturing / Fabrication / Supply	60	0%	$816.15	27-Dec-22	24-Feb-23
P06-E	Final Inspection	7	0%	$163.23	25-Feb-23	03-Mar-23
P06-E	Delivery On Site	7	0%	$408.07	04-Mar-23	10-Mar-23
P06-E	Submitting Vendor Data Book	5	0%	$81.61	11-Mar-23	15-Mar-23
Tray/Ladder and Accessories		99	0%	$1,110.57	01-Aug-22	07-Nov-22
P06-E	Tendering & Selection	15	0%	$44.42	01-Aug-22	15-Aug-22

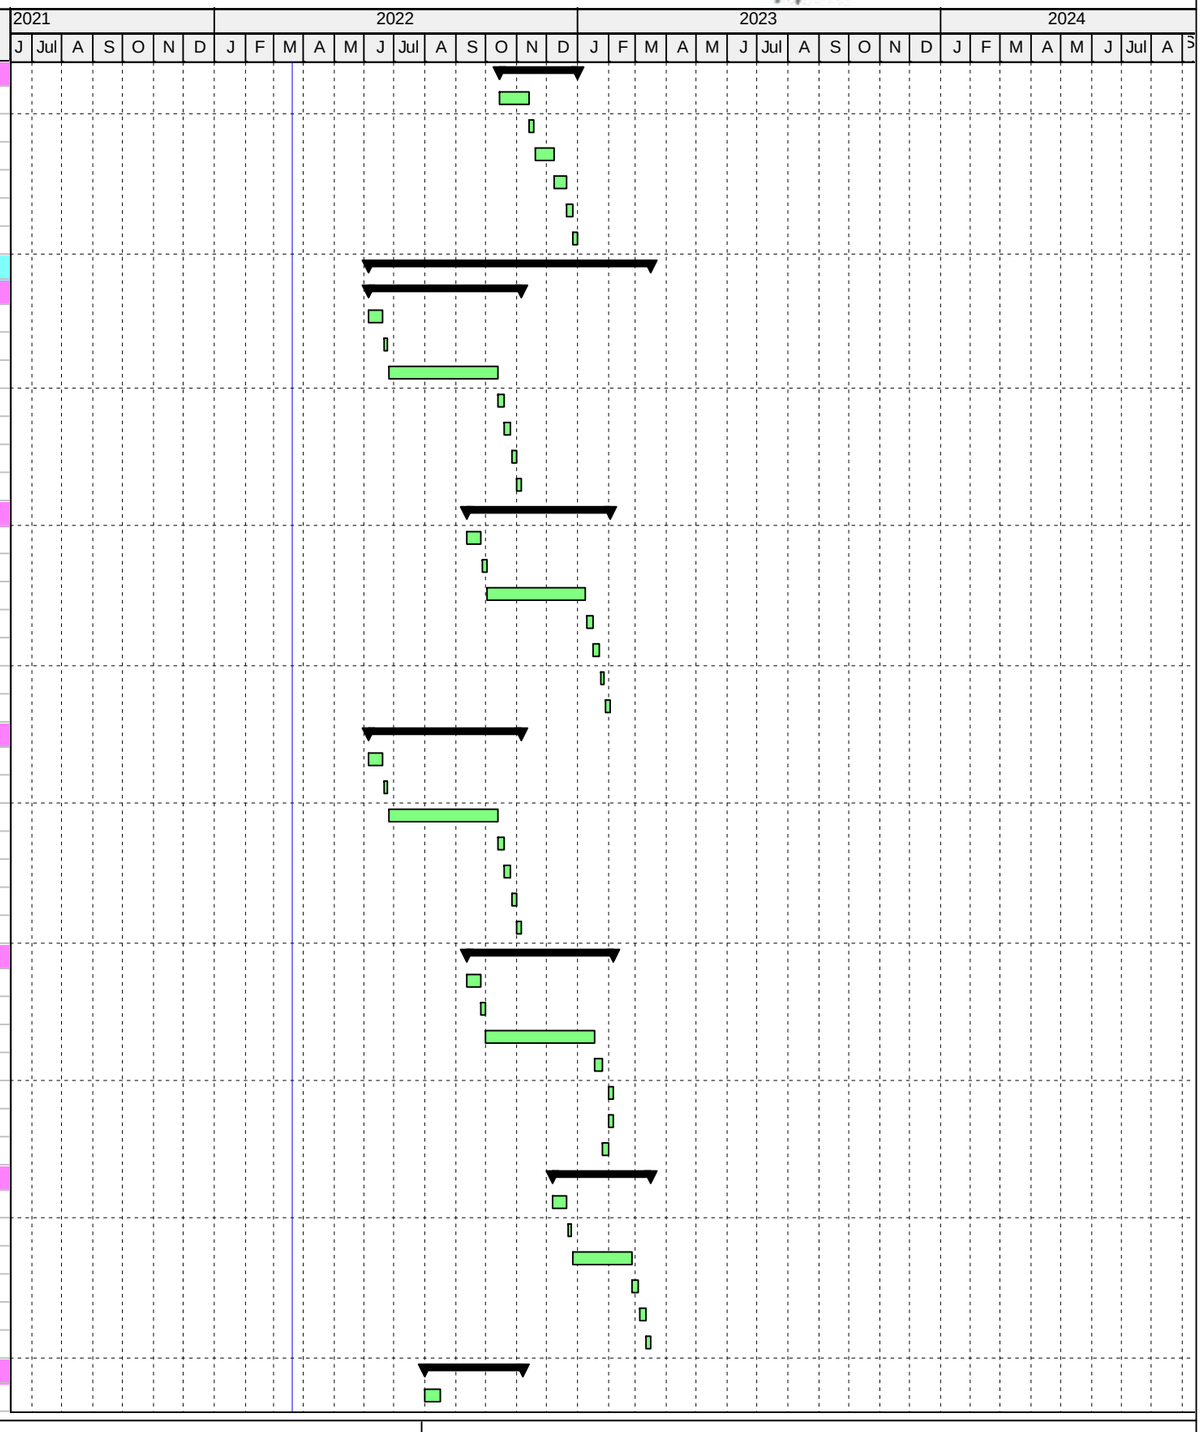

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	Contract Effectiveness / PO	5	0%	$66.63	16-Aug-22	20-Aug-22
P06-E	Manufacturing / Fabrication / Supply	60	0%	$555.29	21-Aug-22	19-Oct-22
P06-E	Final Inspection	7	0%	$111.06	20-Oct-22	26-Oct-22
P06-E	Delivery On Site	7	0%	$277.64	27-Oct-22	02-Nov-22
P06-E	Submitting Vendor Data Book	5	0%	$55.53	03-Nov-22	07-Nov-22
Electrical Bulk Items - Extension of Binak B/C Manifold		154	0%	$1,662.81	07-Jun-22	07-Nov-22
P06-E	Tendering & Selection	15	0%	$66.51	07-Jun-22	21-Jun-22
P06-E	Contract Effectiveness / PO	5	0%	$99.77	22-Jun-22	26-Jun-22
P06-E	Manufacturing / Fabrication / Supply	110	0%	$831.40	27-Jun-22	14-Oct-22
P06-E	Final Inspection	12	0%	$166.28	15-Oct-22	26-Oct-22
P06-E	Delivery On Site	7	0%	$415.70	27-Oct-22	02-Nov-22
P06-E	Submitting Vendor Data Book	5	0%	$83.14	03-Nov-22	07-Nov-22
Construction		601	0%	$284,072.00	26-Jul-22	17-Mar-24
Wellhead Facility and Flowline		601	0%	$230,098.32	26-Jul-22	17-Mar-24
Wellpad and Access Road		285	0%	$120,801.62	26-Jul-22	06-May-23
Access Road		166	0%	$24,160.32	26-Jul-22	07-Jan-23
Wellpad Access Road		166	0%	$15,704.21	26-Jul-22	07-Jan-23
P06-	Access Road Preparation	25	0%	$7,066.89	26-Jul-22	19-Aug-22
P06-	Filling and Compaction	35	0%	$3,140.84	19-Sep-22	23-Oct-22
P06-	Sub-Base Layer	45	0%	$2,355.63	24-Oct-22	07-Dec-22
Construction of Culvert and Bridge		141	0%	$3,140.84	20-Aug-22	07-Jan-23
bridge		76	0%	$1,413.38	24-Oct-22	07-Jan-23
P0	Excavation	8	0%	$141.34	24-Oct-22	31-Oct-22
P0	lean concrete	2	0%	$113.07	31-Oct-22	02-Nov-22
P0	wall	19	0%	$254.41	15-Nov-22	03-Dec-22
P0	reinforcement	13	0%	$282.68	02-Nov-22	14-Nov-22
P0	form working	25	0%	$141.34	03-Dec-22	28-Dec-22
P0	concrete pouring	3	0%	$339.21	28-Dec-22	31-Dec-22
P0	protect stone	5	0%	$70.67	31-Dec-22	05-Jan-23
P0	Backfill	3	0%	$70.67	05-Jan-23	07-Jan-23
culverts		30	0%	$1,727.46	20-Aug-22	18-Sep-22
P0	pipeway culvert	10	0%	$690.99	20-Aug-22	29-Aug-22
P0	pipeway	10	0%	$518.24	30-Aug-22	08-Sep-22
P0	pipeline culvert	10	0%	$518.24	09-Sep-22	18-Sep-22
Burn Pit Access Road		54	0%	$8,456.11	20-Aug-22	12-Oct-22
P06-	ROW Preparation	20	0%	$5,919.28	20-Aug-22	08-Sep-22
P06-	Filling and Compaction	15	0%	$1,691.22	09-Sep-22	23-Sep-22
P06-	Sub-Base Layer	19	0%	$845.61	24-Sep-22	12-Oct-22
Wellpad		285	0%	$96,641.29	26-Jul-22	06-May-23
Water Supply		30	0%	$6,764.89	26-Jul-22	24-Aug-22
P06-	Water Supply	30	0%	$6,764.89	26-Jul-22	24-Aug-22
Site Preparation		40	0%	$19,328.26	24-Oct-22	02-Dec-22
P06-	Site Preparation W007S	40	0%	$19,328.26	24-Oct-22	02-Dec-22
Civil Work		62	0%	$4,832.06	03-Dec-22	03-Feb-23
P06-	Excavation and Soil Removal (Cellar)	30	0%	$3,140.84	03-Dec-22	01-Jan-23
P06-	Installation of Conductor Pipe	30	0%	$241.60	04-Dec-22	02-Jan-23
P06-	Form Work (Above Cellar)	25	0%	$241.60	03-Jan-23	27-Jan-23
P06-	Armed Concrete	31	0%	$1,208.02	03-Jan-23	03-Feb-23
Surface Preparation		20	0%	$7,731.30	03-Dec-22	22-Dec-22
P06-	Gravel Paving	20	0%	$7,731.30	03-Dec-22	22-Dec-22




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Mud Channel		130	0%	$11,596.96	03-Dec-22	11-Apr-23
P06-	Excavation	40	0%	$1,159.70	02-Jan-23	10-Feb-23
P06-	Soil Removal, Filling and Compaction of Mud Pit Area	30	0%	$1,739.54	03-Dec-22	01-Jan-23
P06-	Construction of Mud Pit's Walls	60	0%	$4,058.93	11-Feb-23	11-Apr-23
P06-	Supply & Installation sealling Layer	15	0%	$3,479.09	03-Dec-22	17-Dec-22
P06-	Backfill	5	0%	$1,159.70	11-Feb-23	15-Feb-23
Mud Pit		155	0%	$31,891.63	03-Dec-22	06-May-23
P06-	Soil Removal, Filling and Compaction of Mud Pit Area	50	0%	$11,162.07	03-Dec-22	21-Jan-23
P06-	Construction of Mud Pit's Walls	35	0%	$6,378.33	03-Dec-22	06-Jan-23
P06-	Supply & Installation sealling Layer	25	0%	$14,351.23	12-Apr-23	06-May-23
SepticTank		68	0%	$3,865.65	20-Nov-22	26-Jan-23
P06-	Excavation & Soil Transfer	30	0%	$1,121.04	03-Dec-22	01-Jan-23
P06-	Levelling	13	0%	$154.63	02-Jan-23	14-Jan-23
P06-	Tank Supply	30	0%	$1,932.83	20-Nov-22	20-Dec-22
P06-	Tank Execution	6	0%	$386.57	14-Jan-23	20-Jan-23
P06-	Backfilling & Compaction	6	0%	$270.60	20-Jan-23	26-Jan-23
Burn Pit		50	0%	$7,731.30	03-Dec-22	21-Jan-23
P06-	Soil Removal, Triming ,Filling and Compaction of Burn Pit Are	25	0%	$6,185.04	03-Dec-22	27-Dec-22
P06-	Construction & Installation of Support	30	0%	$386.57	03-Dec-22	01-Jan-23
P06-	Welding, Installation and Testing	20	0%	$1,159.70	02-Jan-23	21-Jan-23
Gasoil Pad		27	0%	$2,899.24	03-Dec-22	29-Dec-22
P06-	Excavation	13	0%	$579.85	03-Dec-22	15-Dec-22
P06-	lean concrete	2	0%	$869.77	15-Dec-22	17-Dec-22
P06-	Form work	10	0%	$289.92	17-Dec-22	27-Dec-22
P06-	Armed Concrete	3	0%	$1,159.70	27-Dec-22	29-Dec-22
Helipad		86	0%	$2,300.98	03-Dec-22	26-Feb-23
P06-Ef	Excavation & Soil Transfer	30	0%	$230.10	03-Dec-22	01-Jan-23
P06-Ef	levelling	10	0%	$276.12	02-Jan-23	11-Jan-23
P06-Ef	Lean Concrete	3	0%	$345.15	12-Jan-23	14-Jan-23
P06-Ef	Reinforced Work	6	0%	$345.15	15-Jan-23	21-Jan-23
P06-Ef	Formwork	15	0%	$345.15	21-Jan-23	05-Feb-23
P06-Ef	Main Concrete Pouring	5	0%	$460.20	05-Feb-23	10-Feb-23
P06-Ef	Backfilling & Compaction	10	0%	$253.11	10-Feb-23	20-Feb-23
P06-Ef	Paint Marking	6	0%	$46.02	20-Feb-23	26-Feb-23
Wellhead Facility and Flowline		384	0%	$101,243.26	03-Dec-22	21-Dec-23
Civil, Structure & Architecture		362	0%	$47,584.33	03-Dec-22	29-Nov-23
Civil Work		207	0%	$20,937.11	07-May-23	29-Nov-23
P06-	Right of Way	10	0%	$7,327.99	07-May-23	16-May-23
P06-	Steel Works (Wellhead Facilities)	15	0%	$4,815.53	07-May-23	21-May-23
P06-	Well Pad Fencing	40	0%	$3,140.57	17-May-23	25-Jun-23
P06-	Out Door Post Works For Gantry (Fundation, Fencing ...)	10	0%	$2,512.45	15-Nov-23	24-Nov-23
P06-	Out Door Post Works For Wellhead Post (Fundation, Fencinç	10	0%	$3,140.57	20-Nov-23	29-Nov-23
Buildings		348	0%	$20,937.11	03-Dec-22	15-Nov-23
Construction of Guard House		157	0%	$5,862.39	03-Dec-22	08-May-23
Foundation		38	0%	$1,465.60	03-Dec-22	10-Jan-23
P0	Excavation & Soil Transfer (Removing of Vegetal Soil)	8	0%	$293.12	03-Dec-22	10-Dec-22
P0	Levelling	3	0%	$29.31	10-Dec-22	12-Dec-22
P0	Lean Concrete	2	0%	$146.56	13-Dec-22	14-Dec-22
P0	Reinforced Work	6	0%	$293.12	15-Dec-22	21-Dec-22

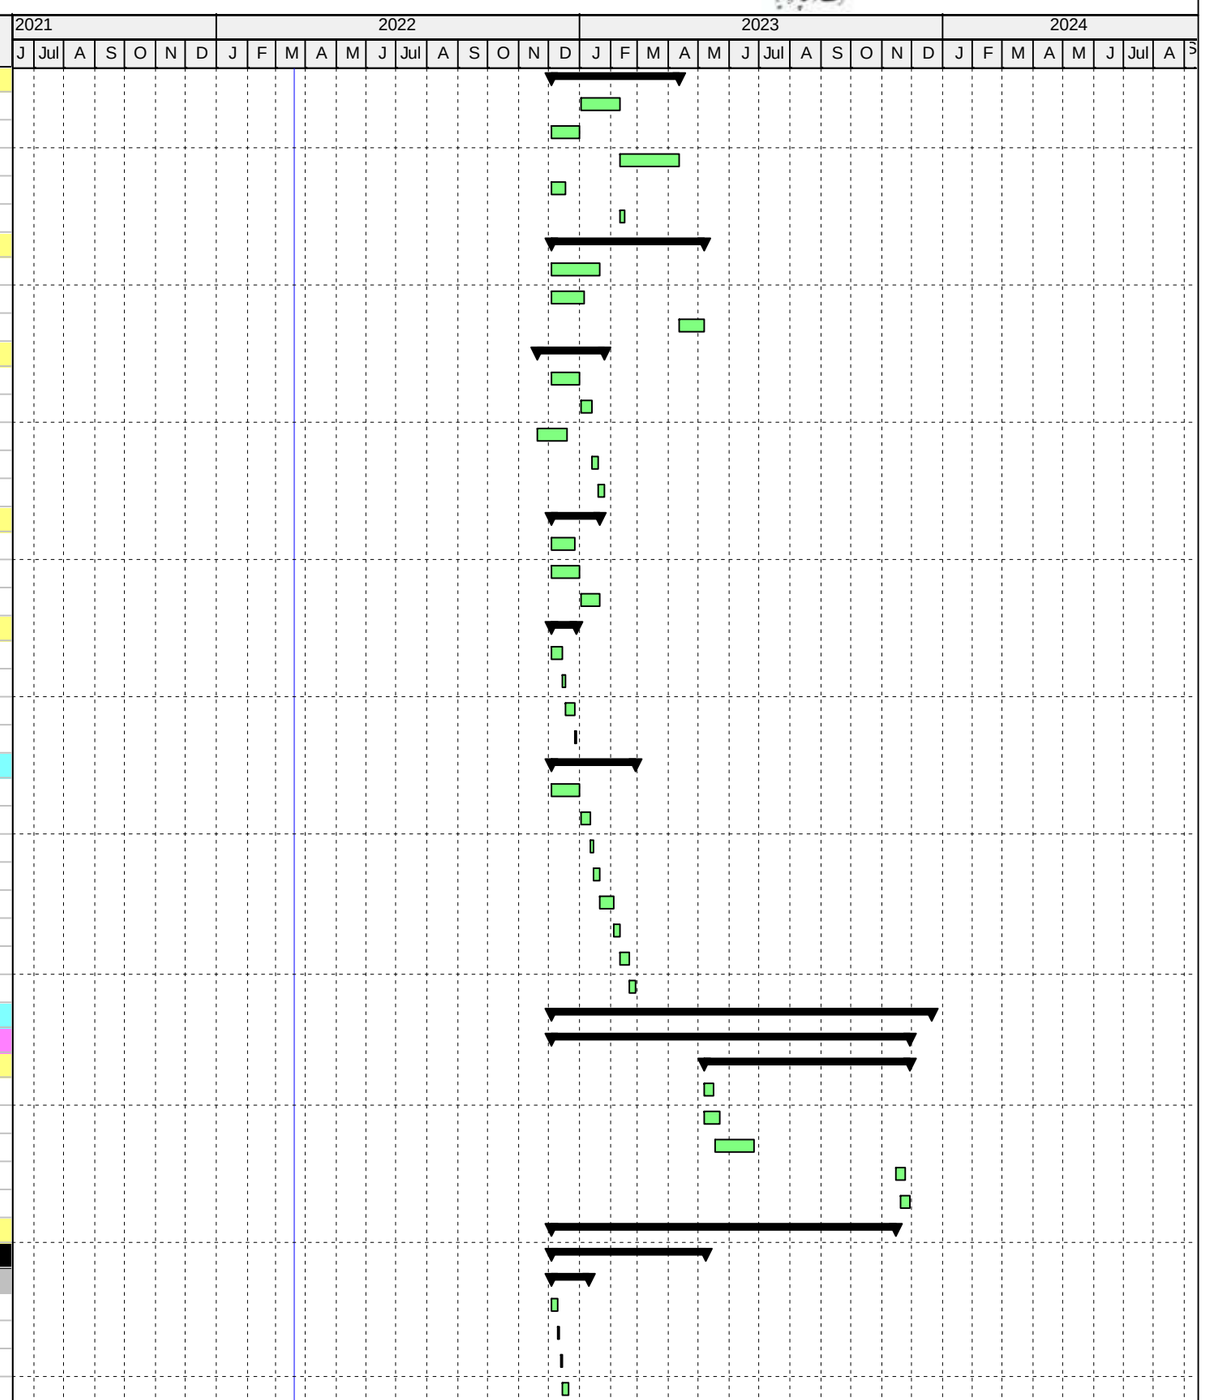


© Oracle Corporation

نگهداشت و افزایش تولید میدان نفتی بینک

بسته های کاری سطح الارض

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P0	Formwork	13	0%	$117.25	21-Dec-22	02-Jan-23
P0	Main Concrete Pouring	5	0%	$512.96	02-Jan-23	07-Jan-23
P0	Backfilling & Compaction	3	0%	$73.28	07-Jan-23	10-Jan-23
Structure		48	0%	$2,344.96	07-Jan-23	24-Feb-23
P0	Structural Installation	13	0%	$1,172.48	01-Feb-23	14-Feb-23
P0	Structural Painting	10	0%	$468.99	14-Feb-23	24-Feb-23
P0	Shop Fabrication of Steel Structure	15	0%	$468.99	17-Jan-23	01-Feb-23
P0	Steel Material Supply	20	0%	$234.50	07-Jan-23	27-Jan-23
Architectural		74	0%	$2,051.84	24-Feb-23	08-May-23
P0	Wall Execution	25	0%	$1,002.73	24-Feb-23	21-Mar-23
P0	Roof Covering	19	0%	$244.17	21-Mar-23	08-Apr-23
P0	Roof Execution (Block Joist, Concrete Pouring)	15	0%	$311.47	09-Apr-23	23-Apr-23
P0	Building Walkway (around Building)	15	0%	$105.46	24-Apr-23	08-May-23
P0	Joinery (Cornice, Façade, Plaster)	2	0%	$388.00	24-Apr-23	25-Apr-23
Construction of Switchgear		323	0%	$8,374.84	28-Dec-22	15-Nov-23
Foundation		34	0%	$2,093.71	28-Dec-22	31-Jan-23
P0	Excavation & Soil Transfer (Removing of Vegetal Soil)	6	0%	$418.74	28-Dec-22	03-Jan-23
P0	Levelling	3	0%	$41.87	03-Jan-23	05-Jan-23
P0	Lean Concrete	2	0%	$209.37	05-Jan-23	07-Jan-23
P0	Reinforced Work	10	0%	$418.74	07-Jan-23	17-Jan-23
P0	Formwork	6	0%	$167.50	17-Jan-23	23-Jan-23
P0	Main Concrete Pouring	5	0%	$816.55	23-Jan-23	28-Jan-23
P0	Backfilling & Compaction	3	0%	$20.94	28-Jan-23	31-Jan-23
Structure		65	0%	$3,349.94	28-Dec-22	02-Mar-23
P0	Steel Material Supply	15	0%	$1,674.97	28-Dec-22	11-Jan-23
P0	Shop Fabrication of Steel Structure	15	0%	$669.99	22-Jan-23	05-Feb-23
P0	Structural Installation	10	0%	$669.99	06-Feb-23	15-Feb-23
P0	Structural Painting	15	0%	$334.99	16-Feb-23	02-Mar-23
Architectural		273	0%	$2,931.19	16-Feb-23	15-Nov-23
P0	Wall Execution	10	0%	$1,432.47	16-Feb-23	25-Feb-23
P0	Roof Covering	8	0%	$348.81	26-Feb-23	05-Mar-23
P0	Roof Execution (Block Joist, Concrete Pouring)	7	0%	$444.96	27-Oct-23	02-Nov-23
P0	Building Walkway (around Building)	13	0%	$150.66	03-Nov-23	15-Nov-23
P0	Joinery (Cornice, Façade, Plaster)	10	0%	$554.29	03-Nov-23	12-Nov-23
Construction of Outdoor Post (new Gantry)		70	0%	$6,699.87	03-Dec-22	10-Feb-23
Foundation		45	0%	$1,674.97	03-Dec-22	16-Jan-23
P0	Excavation & Soil Transfer (Removing of Vegetal Soil)	10	0%	$334.99	03-Dec-22	12-Dec-22
P0	Levelling	6	0%	$33.50	13-Dec-22	19-Dec-22
P0	Lean Concrete	2	0%	$167.50	19-Dec-22	21-Dec-22
P0	Reinforced Work	9	0%	$334.99	21-Dec-22	29-Dec-22
P0	Formwork	10	0%	$134.00	30-Dec-22	08-Jan-23
P0	Main Concrete Pouring	5	0%	$653.24	09-Jan-23	13-Jan-23
P0	Backfilling & Compaction	3	0%	$16.75	14-Jan-23	16-Jan-23
Structure		70	0%	$4,019.92	03-Dec-22	10-Feb-23
P0	Steel Material Supply	25	0%	$2,009.96	03-Dec-22	27-Dec-22
P0	Shop Fabrication of Steel Structure	19	0%	$803.98	23-Dec-22	10-Jan-23
P0	Structural Installation	13	0%	$803.98	14-Jan-23	26-Jan-23
P0	Structural Painting	15	0%	$401.99	26-Jan-23	10-Feb-23
Civil Works(Paving,Gravel,Roads,Trench,Fence,...)		20	0%	$1,004.98	16-Jan-23	05-Feb-23

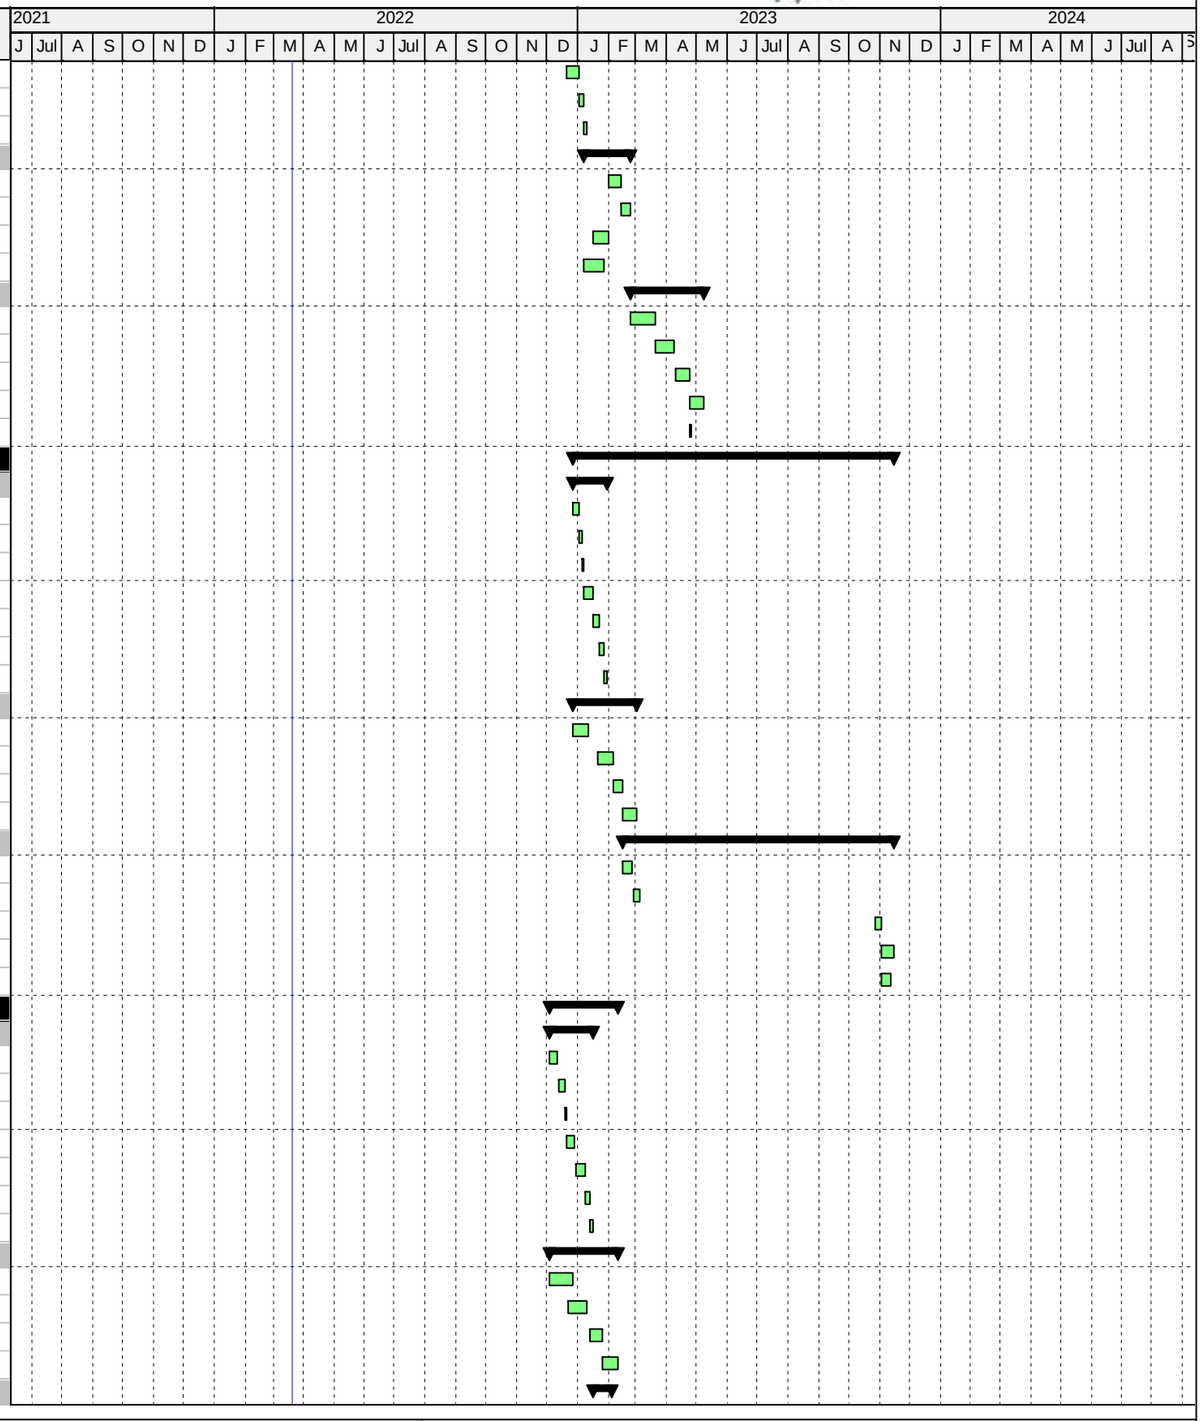


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P0	Civil Works	20	0%	$1,004.98	16-Jan-23	05-Feb-23
Shelters		60	0%	$5,710.12	22-May-23	20-Jul-23
Diesel Generator Shelter		48	0%	$4,282.59	22-May-23	08-Jul-23
P06	Fabrication	31	0%	$2,997.81	22-May-23	22-Jun-23
P06	Installation	31	0%	$1,284.78	07-Jun-23	08-Jul-23
Fire Fighting Shelter		41	0%	$1,427.53	09-Jun-23	20-Jul-23
P06	Fabrication	31	0%	$999.27	09-Jun-23	10-Jul-23
P06	Installation	13	0%	$428.26	08-Jul-23	20-Jul-23
Flowline		61	0%	$12,149.19	06-Oct-23	06-Dec-23
Construction of Pipe Support		7	0%	$1,822.38	20-Nov-23	26-Nov-23
P06-	Construction of Pipe Support	7	0%	$1,822.38	20-Nov-23	26-Nov-23
Installation of Pipe Supports		7	0%	$1,822.38	22-Nov-23	28-Nov-23
P06-	Installation of Pipe Supports	7	0%	$1,822.38	22-Nov-23	28-Nov-23
6" Flowline Installation		30	0%	$7,896.97	07-Nov-23	06-Dec-23
P06-	COLD CUT	15	0%	$394.85	20-Nov-23	04-Dec-23
P06-	Material Handeling	18	0%	$947.64	15-Nov-23	02-Dec-23
P06-	Fit-Up & Welding	22	0%	$5,212.00	15-Nov-23	06-Dec-23
P06-	Bending	15	0%	$829.18	17-Nov-23	01-Dec-23
P06-	NDT	15	0%	$513.30	07-Nov-23	21-Nov-23
Hydrostatic Test		25	0%	$607.46	06-Oct-23	31-Oct-23
P06-	6" Pigging and Hydrostatic Test	25	0%	$607.46	06-Oct-23	31-Oct-23
Piping		30	0%	$5,062.16	15-Nov-23	14-Dec-23
P06-E	Sweep Bend Installation	10	0%	$253.11	15-Nov-23	24-Nov-23
P06-E	Construction of Spools (Fit up, Welding, NDT…)	15	0%	$1,771.76	25-Nov-23	09-Dec-23
P06-E	Valves, Fitting and Spools Installation and Hydrotest	10	0%	$2,784.19	27-Nov-23	07-Dec-23
P06-E	Painting	10	0%	$253.11	05-Dec-23	14-Dec-23
Mechanical		10	0%	$6,074.60	20-Nov-23	29-Nov-23
P06-E	Fuel Oil Storage Drum	10	0%	$3,037.30	20-Nov-23	29-Nov-23
P06-E	Potable Water Tank	10	0%	$3,037.30	20-Nov-23	29-Nov-23
Instrument Works		15	0%	$5,062.16	15-Nov-23	29-Nov-23
P06-E	Devices Installation and Piping Connecton	15	0%	$5,062.16	15-Nov-23	29-Nov-23
Electrical		33	0%	$20,248.65	15-Nov-23	17-Dec-23
P06-E	Over Head line	10	0%	$10,934.27	07-Dec-23	17-Dec-23
P06-E	Wellhead Electrical Equipment	15	0%	$2,227.35	15-Nov-23	29-Nov-23
P06-E	Outdoor Post (new Gantry)	10	0%	$5,467.14	30-Nov-23	09-Dec-23
P06-E	Outdoor Post (Wellhead Post)	10	0%	$1,619.89	20-Nov-23	29-Nov-23
Pre-commissioning		7	0%	$5,062.16	15-Dec-23	21-Dec-23
P06-E	Pre-commissioning	7	0%	$4,555.95	15-Dec-23	21-Dec-23
P06-E	Ready for Comm. Certificate (RFCC)	4	0%	$506.22	17-Dec-23	20-Dec-23
Safety & Fire Fighting		10	0%	$2,300.98	20-Nov-23	29-Nov-23
P06-EF	Safety & Fire Fighting	10	0%	$2,300.98	20-Nov-23	29-Nov-23
Job Site HSE Supervision (Surface)		500	0%	$460.20	26-Jul-22	07-Dec-23
P06-EF	Job Site HSE Supervision (Surface)	500	0%	$460.20	26-Jul-22	07-Dec-23
Commissioning , Startup & Handover		87	0%	$2,991.28	22-Dec-23	17-Mar-24
Commissioning		32	0%	$897.38	22-Dec-23	22-Jan-24
P06-E	Materials & Utilities Ready for Commissioning	3	0%	$44.87	22-Dec-23	24-Dec-23
P06-E	Receiving Facilities Ready for Commissioning	2	0%	$44.87	25-Dec-23	26-Dec-23
P06-E	Permits Obtained for Commissioning	10	0%	$44.87	27-Dec-23	05-Jan-24
P06-E	Integrated Commissioning	2	0%	$717.91	06-Jan-24	07-Jan-24
P06-E	Ready for Startup Certificate (RFSU)	15	0%	$44.87	08-Jan-24	22-Jan-24

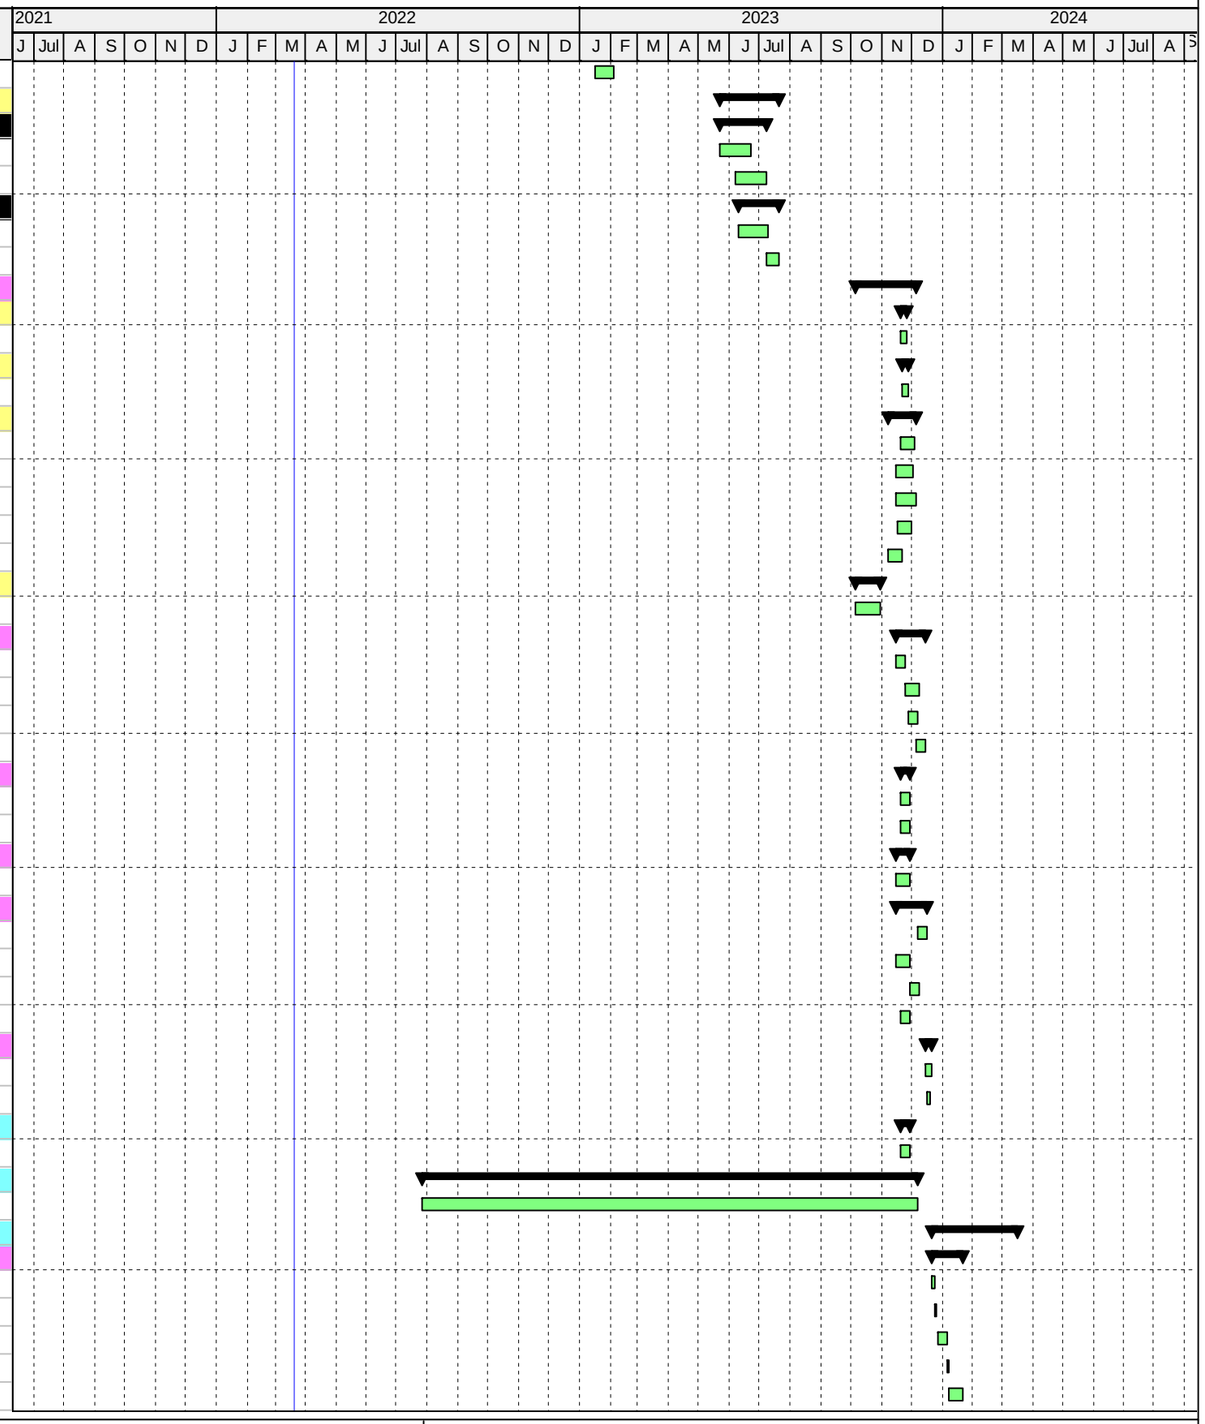


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Startup & Performance Test		18	0%	$1,196.51	23-Jan-24	09-Feb-24
P06-E	Startup & Performance Test Run	3	0%	$957.21	23-Jan-24	25-Jan-24
P06-E	Start of Production (SOP)	15	0%	$239.30	26-Jan-24	09-Feb-24
Handover		37	0%	$897.38	10-Feb-24	17-Mar-24
P06-E	Compiling & Submitting Final Documentation	20	0%	$269.22	10-Feb-24	29-Feb-24
P06-E	Training of Operator's Personnel	2	0%	$358.95	01-Mar-24	02-Mar-24
P06-E	Provisional Acceptance Certificate (PAC)	15	0%	$269.22	03-Mar-24	17-Mar-24
Manifold Extension		291	0%	$53,973.68	23-Sep-22	10-Jul-23
Civil, Structure & Architecture		86	0%	$10,794.74	23-Sep-22	18-Dec-22
P06-EI	Site Preparation	30	0%	$539.74	23-Sep-22	22-Oct-22
P06-EI	Fence & Gate & Civil Works & Roads	15	0%	$1,079.47	23-Oct-22	06-Nov-22
P06-EI	Foundation	20	0%	$4,857.63	07-Nov-22	26-Nov-22
P06-EI	Steel Works	30	0%	$4,317.89	18-Nov-22	18-Dec-22
Mechanic		20	0%	$2,158.95	13-Dec-22	02-Jan-23
P06-EI	Installation Pump	20	0%	$2,158.95	13-Dec-22	02-Jan-23
Piping		66	0%	$11,604.34	04-Jan-23	10-Mar-23
P06-EI	Pipe sleeper/Support	10	0%	$3,481.30	04-Jan-23	13-Jan-23
P06-EI	Material Handeling	10	0%	$2,320.87	21-Feb-23	02-Mar-23
P06-EI	Fit-Up & Welding	10	0%	$3,481.30	21-Feb-23	02-Mar-23
P06-EI	Hydrotest	10	0%	$1,160.43	01-Mar-23	10-Mar-23
P06-EI	NDT	7	0%	$1,160.43	26-Feb-23	04-Mar-23
Control & Instrumentation		160	0%	$25,907.37	01-Nov-22	09-Apr-23
Tray&Ladder		55	0%	$1,554.44	27-Nov-22	20-Jan-23
P06-E	Tray & Ladder	20	0%	$932.67	01-Jan-23	20-Jan-23
P06-E	support installation for cable trays	20	0%	$621.78	27-Nov-22	16-Dec-22
CONDUIT		15	0%	$518.15	16-Jan-23	30-Jan-23
P06-E	Conduit	15	0%	$518.15	16-Jan-23	30-Jan-23
Junction Boxes		21	0%	$2,590.74	17-Mar-23	07-Apr-23
P06-E	Digital (on/off)	15	0%	$1,968.96	17-Mar-23	31-Mar-23
P06-E	Analog	6	0%	$621.78	01-Apr-23	07-Apr-23
CABLING		26	0%	$5,699.62	26-Jan-23	21-Feb-23
P06-E	Cable Laying	10	0%	$2,849.81	26-Jan-23	04-Feb-23
P06-E	Cable Arragement	5	0%	$854.94	05-Feb-23	09-Feb-23
P06-E	Test after cabling(continuity Test)	4	0%	$284.98	10-Feb-23	13-Feb-23
P06-E	Cable Marking&Tag	4	0%	$569.96	13-Feb-23	17-Feb-23
P06-E	Connection & Glanding	4	0%	$1,139.92	17-Feb-23	21-Feb-23
DCS System		16	0%	$3,367.96	01-Nov-22	16-Nov-22
P06-E	marshaling cabinets	6	0%	$2,559.65	01-Nov-22	07-Nov-22
P06-E	operator desks	3	0%	$404.15	07-Nov-22	09-Nov-22
P06-E	engineering sations	3	0%	$269.44	09-Nov-22	12-Nov-22
P06-E	printers	2	0%	$67.36	12-Nov-22	14-Nov-22
P06-E	operator stations	3	0%	$67.36	14-Nov-22	16-Nov-22
ESD System		16	0%	$3,367.96	11-Mar-23	26-Mar-23
P06-E	marshaling cabinets	6	0%	$2,559.65	11-Mar-23	17-Mar-23
P06-E	operator desks	3	0%	$404.15	17-Mar-23	19-Mar-23
P06-E	engineering sations	3	0%	$269.44	19-Mar-23	22-Mar-23
P06-E	printers	2	0%	$67.36	22-Mar-23	24-Mar-23
P06-E	operator stations	3	0%	$67.36	24-Mar-23	26-Mar-23
F & G System		30	0%	$3,367.96	11-Mar-23	09-Apr-23

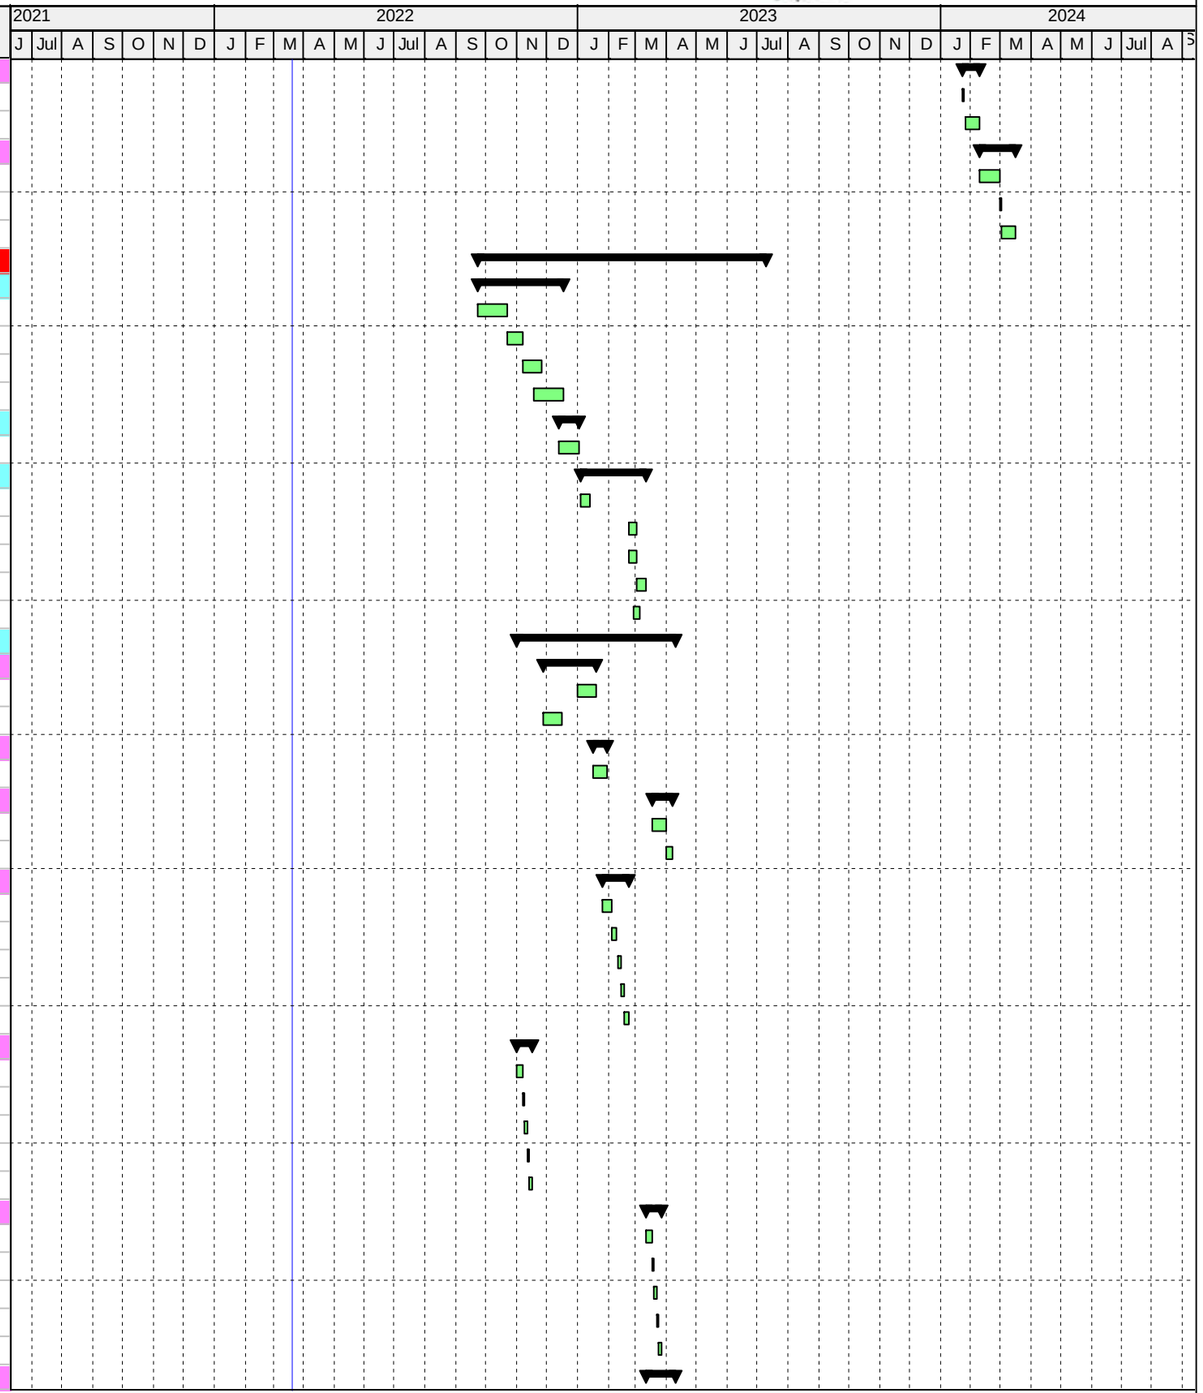

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P06-E	F & G system panel	7	0%	$1,347.18	11-Mar-23	17-Mar-23
P06-E	operator station & printer	4	0%	$505.19	18-Mar-23	21-Mar-23
P06-E	engineering station	4	0%	$505.19	21-Mar-23	25-Mar-23
P06-E	operator stations	4	0%	$235.76	25-Mar-23	29-Mar-23
P06-E	Gas detectors	4	0%	$336.80	29-Mar-23	01-Apr-23
P06-E	manual alarm call points (MAC)	4	0%	$168.40	02-Apr-23	05-Apr-23
P06-E	smoke detectors	4	0%	$269.44	05-Apr-23	09-Apr-23
FIELD INSTRUMENT		149	0%	$5,440.55	01-Nov-22	29-Mar-23
Calibration		19	0%	$1,251.33	11-Mar-23	29-Mar-23
P06-	Calibration	19	0%	$1,251.33	11-Mar-23	29-Mar-23
Installation		146	0%	$4,189.22	01-Nov-22	26-Mar-23
P06-	FE - FLOW ELEMENTS (ORIFICE PLATE & FLANGE) Orifi	10	0%	$544.60	11-Nov-22	20-Nov-22
P06-	CC - CORROSION COUPON	10	0%	$547.53	01-Nov-22	10-Nov-22
P06-	CP/CT - CORROSION PROBE / TRANSMITTER WITH DA	10	0%	$397.98	01-Nov-22	10-Nov-22
P06-	PG - PRESSURE GAUGE	10	0%	$418.92	01-Nov-22	10-Nov-22
P06-	PT - SMART PRESSURE TRANSMITTER	10	0%	$293.25	01-Nov-22	10-Nov-22
P06-	FT - SMART DIFF. (FLOW) PRESSURE TRANSMITTER	10	0%	$248.42	01-Nov-22	10-Nov-22
P06-	FCV & PCV (flow control valve -Pressure awitch valve)	10	0%	$523.65	01-Nov-22	10-Nov-22
P06-	On/Off Valve	10	0%	$502.71	17-Mar-23	26-Mar-23
P06-	PRESSURE SAFETY VALVE	10	0%	$502.71	17-Mar-23	26-Mar-23
P06-	TT - SMART TEMPERATURE TRANSMITTER	10	0%	$209.46	17-Mar-23	26-Mar-23
Job Site HSE Supervision (Surface)		160	0%	$107.95	23-Sep-22	01-Mar-23
P06-EI	Job Site HSE Supervision (Surface)	160	0%	$107.95	23-Sep-22	01-Mar-23
Mechanical Completion & Pre-commissioning		10	0%	$2,698.68	09-Apr-23	19-Apr-23
P06-EI	Mechanical Completion & Pre-commissioning	10	0%	$2,698.68	09-Apr-23	19-Apr-23
Commissioning, Startup & Handover		82	0%	$701.66	19-Apr-23	10-Jul-23
Startup & Performance Test		20	0%	$280.66	24-May-23	12-Jun-23
P06-E	Startup & Performance Test Run	5	0%	$224.53	24-May-23	28-May-23
P06-E	Start of Production (SOP)	15	0%	$56.13	29-May-23	12-Jun-23
Handover		28	0%	$210.50	13-Jun-23	10-Jul-23
P06-E	Training of Operator's Personnel	5	0%	$63.15	03-Jul-23	07-Jul-23
P06-E	Provisional Acceptance Certificate (PAC)	3	0%	$84.20	08-Jul-23	10-Jul-23
P06-E	Compiling & Submitting Final Documentation	20	0%	$63.15	13-Jun-23	02-Jul-23
Commissioning		35	0%	$210.50	19-Apr-23	23-May-23
P06-E	Materials & Utilities Ready for Commissioning	4	0%	$10.52	19-Apr-23	23-Apr-23
P06-E	Receiving Facilities Ready for Commissioning	3	0%	$10.52	23-Apr-23	26-Apr-23
P06-E	Permits Obtained for Commissioning	10	0%	$10.52	26-Apr-23	06-May-23
P06-E	Integrated Commissioning	3	0%	$168.40	06-May-23	08-May-23
P06-E	Ready for Startup Certificate (RFSU)	15	0%	$10.52	09-May-23	23-May-23
Package 07-Workover # 14		532	0.58%	$503,660.00	24-Jul-21 A	02-Sep-23
ENGINEERING		445	21.66%	$13,382.00	24-Jul-21 A	07-Jun-23
Basic Design Endorsement		30	100%	$669.10	31-Jul-21 A	20-Mar-22
P07-EP	Endorsement Report For Basic Design & Scope of Work	30	100%	$669.10	31-Jul-21 A	20-Mar-22
Value Engineering		44	60%	$401.46	01-Feb-22	20-Mar-22
P07-EP	Value Engineering Study Report	44	60%	$401.46	01-Feb-22	20-Mar-22
Detail Design		415	27.01%	$7,360.10	24-Jul-21 A	04-Feb-23
Process		79	65%	$350.34	15-Nov-21	22-Jun-22
Drawing/Diagram		35	80%	$245.24	15-Nov-21	23-Apr-22
P07-E	P&ID for Diesel Oil Drum- BK14	35	80%	$122.62	15-Nov-21	23-Apr-22
P07-E	P&ID for Potable Water Tank - BK14	35	80%	$122.62	15-Nov-21	23-Apr-22




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
List		44	60%	$52.55	27-Feb-22	02-May-22
P07-E	Line List - BK14	44	60%	$52.55	27-Feb-22	02-May-22
Data Sheet		60	0%	$52.55	24-Apr-22	22-Jun-22
P07-E	Process Data Sheets For Instrument Devices - BK14	30	0%	$17.87	24-Apr-22	23-May-22
P07-E	Process Data Sheets For Fuel Oil Storage Drum of Well Pads	30	0%	$17.34	24-May-22	22-Jun-22
P07-E	Process Data Sheets For Potable Water Tank of Well Pads	30	0%	$17.34	24-May-22	22-Jun-22
Mechanical		99	77.78%	$490.92	28-Jul-21 A	26-Jun-22
Basis/Criteria		54	60%	$54.54	28-Jul-21 A	12-May-22
P07-E	Mechanical Design Criteria	54	60%	$54.54	28-Jul-21 A	12-May-22
Specification		79	60%	$81.84	28-Jul-21 A	26-Jun-22
P07-E	Specification For Pressure Vessels	54	60%	$40.92	28-Jul-21 A	01-Jun-22
P07-E	Specification For Atmospheric Above Ground Welded Steel Ta	79	60%	$40.92	28-Jul-21 A	26-Jun-22
Data Sheets		45	60%	$136.38	16-Jan-22	18-May-22
P07-E	Data Sheets For Fuel Oil Storage Drum of Well Pads	35	60%	$68.19	16-Jan-22	13-May-22
P07-E	Data Sheets For Potable Water Tank of Well Pads	35	60%	$68.19	09-Feb-22	18-May-22
Drawing/Diagram		34	100%	$218.16	28-Jul-21 A	09-Apr-22
P07-E	Standard Detail Drawing For Pressure Vessels and Heat Exch	14	100%	$109.08	28-Jul-21 A	09-Apr-22
P07-E	Standard Detail Drawing For Storage Tanks	14	100%	$109.08	28-Jul-21 A	09-Apr-22
HVAC/Plumbing		378	5.17%	$420.26	24-Jul-21 A	04-Feb-23
Basis/Criteria		40	100%	$6.09	24-Jul-21 A	14-May-22
P07-E	HVAC & Plumbing Design Criteria	40	100%	$6.09	24-Jul-21 A	14-May-22
Specification		64	100%	$9.75	24-Jul-21 A	27-Mar-22
P07-E	Specification For HVAC Equipment	64	100%	$6.09	24-Jul-21 A	27-Mar-22
P07-E	Specification For Duct Work & Pipe Work	64	100%	$3.66	24-Jul-21 A	27-Mar-22
Calculation		178	0%	$97.46	03-May-22	27-Oct-22
P07-E	HVAC Calculation Note For Switchgear Building - BK14	35	0%	$48.73	03-May-22	06-Jun-22
P07-E	HVAC Calculation Note For Security Building - BK14	35	0%	$48.73	23-Sep-22	27-Oct-22
Data Sheets		35	0%	$48.71	02-Dec-22	05-Jan-23
P07-E	Data Sheets For Main HVAC Equipment - BK14	35	0%	$48.71	02-Dec-22	05-Jan-23
Drawing/Diagram		252	2.82%	$209.54	24-Jul-21 A	05-Jan-23
P07-E	Standard Drawing For HVAC & Plumbing	14	100%	$4.67	24-Jul-21 A	30-Mar-22
P07-E	Symbol & Legend For HVAC & Plumbing	48	60%	$2.03	22-Aug-21	16-May-22
P07-E	HVAC System Layout For Switchgear Building - BK14	35	0%	$50.71	07-Jun-22	11-Jul-22
P07-E	HVAC System Layout For Security Building - BK14	35	0%	$50.71	28-Oct-22	01-Dec-22
P07-E	Plumbing & Sewage Piping Layout For Switchgear Building - I	35	0%	$50.71	12-Jul-22	15-Aug-22
P07-E	Plumbing & Sewage Piping Layout For Security Building - Bk	35	0%	$50.71	02-Dec-22	05-Jan-23
MTO		30	0%	$48.71	06-Jan-23	04-Feb-23
P07-E	MTO For Building HVAC & Plumbing Systems - BK14	30	0%	$48.71	06-Jan-23	04-Feb-23
Piping		49	59.28%	$350.34	24-Jul-21 A	09-May-22
Basis/Criteria		39	100%	$7.01	24-Jul-21 A	20-Mar-22
P07-E	Piping Design Criteria	39	100%	$7.01	24-Jul-21 A	20-Mar-22
Specification		45	71.8%	$133.13	24-Jul-21 A	07-May-22
P07-E	Specification For Color Coding and Marking	39	60%	$9.71	09-Aug-21	01-May-22
P07-E	Specification For Transportation, Handling, Storage of pipes	39	80%	$10.58	12-Dec-21	01-May-22
P07-E	Specification For Metallic Pipes	39	80%	$9.71	24-Jul-21 A	01-May-22
P07-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$9.71	24-Jul-21 A	24-Mar-22
P07-E	Specification For Painting	39	100%	$9.71	24-Jul-21 A	27-Mar-22
P07-E	Specification For Lining (Internal Protection of Equipment by F	39	60%	$11.65	09-Aug-21	04-May-22
P07-E	Specification For Material Requirements in Sour service	39	60%	$9.71	09-Aug-21	04-May-22
P07-E	Specification For Manual Valves	39	60%	$9.71	09-Aug-21	04-May-22

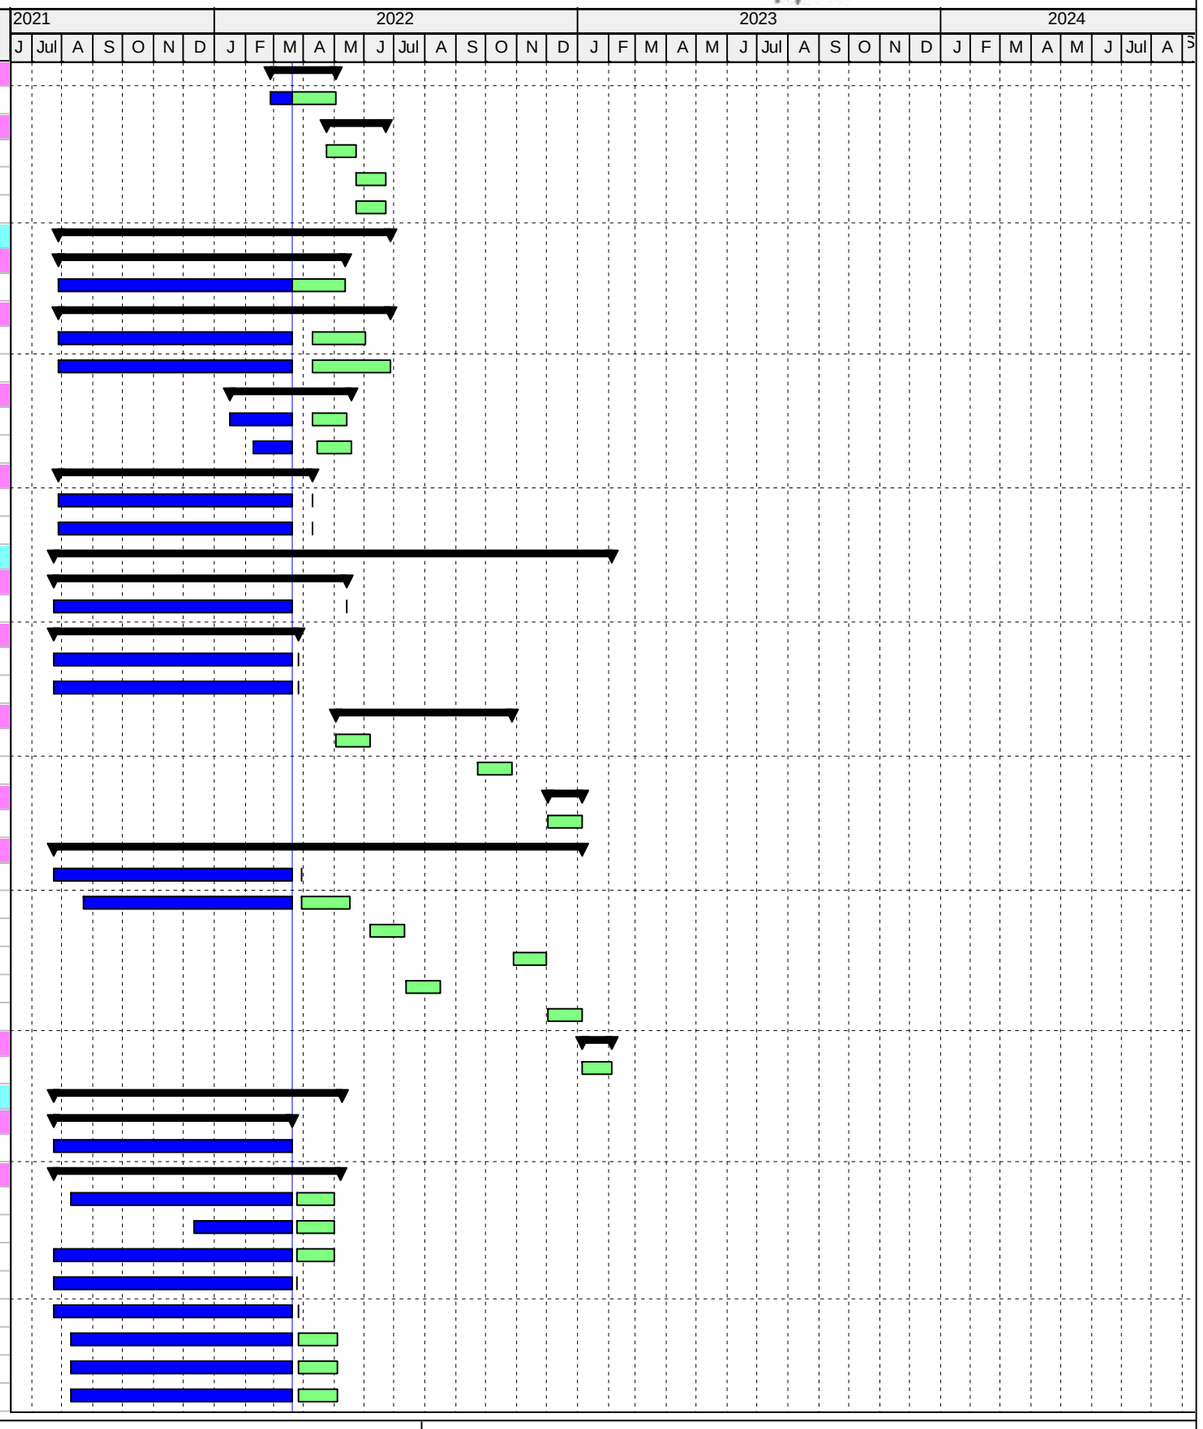


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P07-E	Specification For Plant Piping Systems Pressure Testing	39	60%	$9.71	09-Aug-21	04-May-22
P07-E	Specification For Welding of Plant Piping System	39	60%	$9.71	09-Aug-21	04-May-22
P07-E	Specification For Flexibility Analysis	39	60%	$10.58	09-Aug-21	04-May-22
P07-E	Specification For Pipe Support	39	60%	$12.97	09-Aug-21	07-May-22
P07-E	Specification For Piping Cleaning and Flushing	39	100%	$9.71	24-Aug-21	30-Mar-22
Drawing/Diagram		14	100%	$105.10	19-Feb-22	20-Mar-22
P07-E	Standard Pipe Support Drawings	14	100%	$105.10	19-Feb-22	20-Mar-22
MTO		7	0%	$105.10	03-May-22	09-May-22
P07-E	MTO For Pipes - BK14	7	0%	$105.10	03-May-22	09-May-22
Electrical		239	27.05%	$1,780.41	24-Jul-21 A	13-Nov-22
Basis/Criteria		54	100%	$10.15	03-Aug-21	20-Mar-22
P07-E	Electrical System Design Criteria	54	100%	$10.15	03-Aug-21	20-Mar-22
Specification		55	100%	$119.82	24-Jul-21 A	30-Mar-22
P07-E	Specification For LV Switchgear & Motor Control Centers	49	100%	$6.21	24-Jul-21 A	24-Mar-22
P07-E	Specification For MV Switchgear	49	100%	$7.12	24-Jul-21 A	24-Mar-22
P07-E	Specification For UPS System	49	100%	$7.12	04-Aug-21	24-Mar-22
P07-E	Specification For Transformers	49	100%	$7.12	24-Jul-21 A	24-Mar-22
P07-E	Specification For DC Charger	49	100%	$7.12	04-Aug-21	24-Mar-22
P07-E	Specification For Earthing & Lightning System	49	100%	$4.53	28-Jul-21 A	24-Mar-22
P07-E	Specification For Lighting & Small Power System	49	100%	$6.22	28-Jul-21 A	27-Mar-22
P07-E	Specification For Bulk Materials	49	100%	$6.22	24-Jul-21 A	27-Mar-22
P07-E	Specification For Diesel Generator	49	100%	$7.12	28-Jul-21 A	27-Mar-22
P07-E	Specification For LV Induction Motors	49	100%	$6.52	24-Jul-21 A	27-Mar-22
P07-E	Specification For Electrical Requirements of Packaged Units	49	100%	$7.12	28-Jul-21 A	27-Mar-22
P07-E	Specification For Capacitor Bank	49	100%	$7.12	24-Jul-21 A	27-Mar-22
P07-E	Specification For Distribution & Lighting Panels	49	100%	$7.12	28-Jul-21 A	30-Mar-22
P07-E	Specification For Power & Control Cables	49	100%	$6.22	24-Jul-21 A	30-Mar-22
P07-E	Specification For Cathodic Protection System	49	100%	$6.22	31-Jul-21 A	30-Mar-22
P07-E	Specification For MV Induction Motors	49	100%	$6.52	24-Jul-21 A	30-Mar-22
P07-E	Specification For NGR	49	100%	$7.12	24-Jul-21 A	30-Mar-22
P07-E	Specification For Overhead Transmission Lines	49	100%	$7.12	28-Jul-21 A	30-Mar-22
Calculation		204	40.68%	$196.38	11-Oct-21 A	28-May-22
P07-E	Calculation Note For Lighting System of Well Pads Switchgea	50	0%	$14.49	28-Mar-22	16-May-22
P07-E	Calculation Note For Lighting System of Well Pads Security B	50	0%	$14.49	28-Mar-22	16-May-22
P07-E	Calculation Note For Lighting System of Well Pads Area	55	0%	$19.34	28-Mar-22	21-May-22
P07-E	Calculation Note For Cable Sizing of Well Pads	55	80%	$19.34	02-Nov-21	23-May-22
P07-E	Calculation Note For UPS System of Well Pads	55	0%	$19.34	04-Apr-22	28-May-22
P07-E	Calculation Note For Earthing & Lightning System of Well Pac	55	0%	$19.34	20-Mar-22	13-May-22
P07-E	Calculation Note For Diesel Generator Sizing of Well Pads	55	60%	$14.49	26-Jan-22	18-May-22
P07-E	Calculation Note For DC Charger of Well Pads	55	80%	$19.34	26-Jan-22	18-May-22
P07-E	Calculation Note For LV Capacitor Bank of Well Pads	40	60%	$23.55	29-Jan-22	13-May-22
P07-E	Calculation Note For 11 KV Over Head Line Sag and Tension	40	80%	$16.32	13-Oct-21	13-May-22
P07-E	Calculation Note For 33 KV Over Head Line Sag and Tension	40	80%	$16.32	11-Oct-21 A	13-May-22
Data Sheets		169	67.99%	$166.47	12-Sep-21	12-Jul-22
P07-E	Data Sheets For UPS of Well Pads	30	0%	$14.28	13-Jun-22	12-Jul-22
P07-E	Data Sheets For DC Charger of Well Pads	30	80%	$14.28	29-Jan-22	23-Apr-22
P07-E	Data Sheets For Diesel Generator of Well Pads	30	60%	$14.28	20-Sep-21	23-Apr-22
P07-E	Data Sheets For LV Capacitor Bank of Well Pads	30	80%	$14.28	12-Sep-21	18-Apr-22
P07-E	Data Sheets For LV Switchgear of Well Pads	30	60%	$14.28	19-Feb-22	18-Apr-22

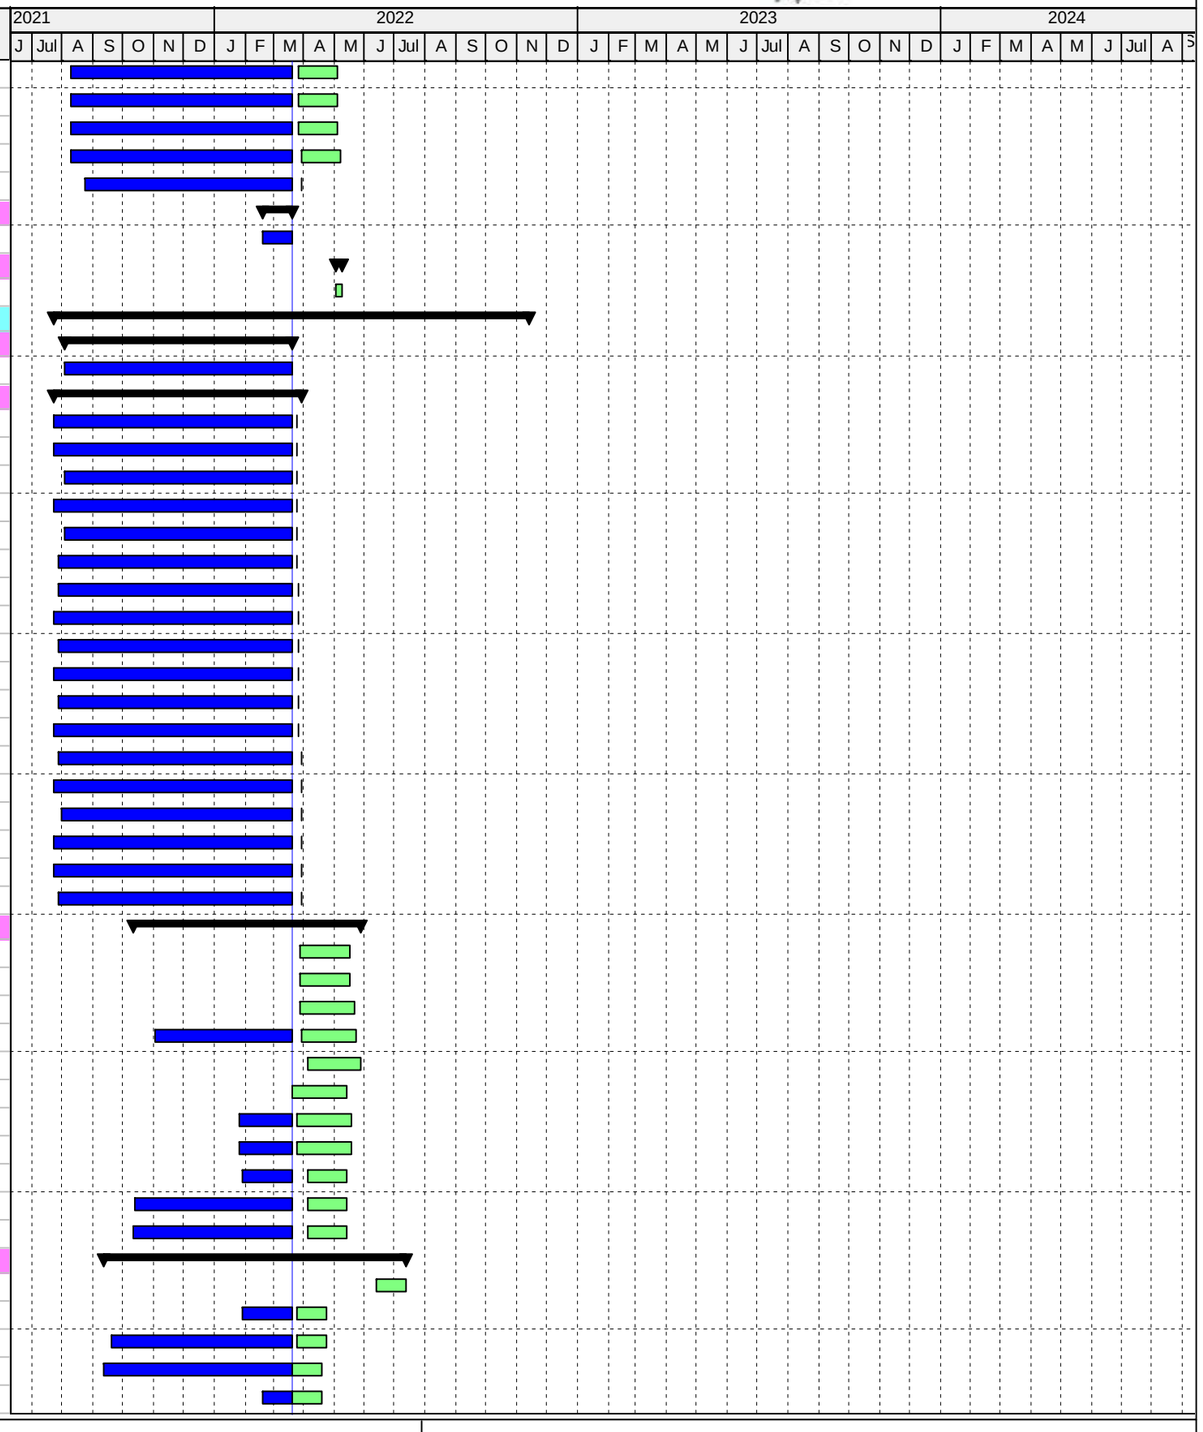


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P07-E	Data Sheets For Power & Control Cables of Well Pads	30	80%	$14.28	13-Sep-21	28-Apr-22
P07-E	Data Sheets For Power Transformers of Well Pads	30	80%	$14.28	15-Sep-21	18-Apr-22
P07-E	Data Sheets For Distribution & Lighting Panels of Well Pads	30	60%	$14.28	12-Sep-21	02-Jul-22
P07-E	Data Sheets For 11 KV Over Head Line Equipment	25	80%	$26.10	10-Nov-21	27-Jun-22
P07-E	Data Sheets For 33 KV Over Head Line Equipment	25	80%	$26.10	10-Nov-21	27-Jun-22
Drawing/Diagram		202	29.58%	$472.34	09-Aug-21	06-Nov-22
P07-E	Electrical Legend and Symbols	40	100%	$4.06	09-Aug-21	20-Mar-22
P07-E	Typical Installation Details & Notes For Earthing and Lightning	14	100%	$12.14	25-Aug-21	20-Mar-22
P07-E	Typical Installation Details & Notes For Lighting System	14	100%	$10.77	25-Aug-21	20-Mar-22
P07-E	Typical Installation Details & Notes For Power System	14	100%	$3.59	25-Aug-21	20-Mar-22
P07-E	Installation Details & Notes For Cathodic Protection Systems	50	100%	$3.64	25-Aug-21	20-Mar-22
P07-E	Typical Installation Details For Over Head Line Equipment	14	100%	$8.08	22-Aug-21	20-Mar-22
P07-E	Installation Detail & Notes for Connection OHL to Gantries for	45	60%	$32.88	06-Mar-22	03-May-22
P07-E	Electrical Typical Schematic Diagrams For LV Panels of Well F	14	100%	$20.22	30-Aug-21	20-Mar-22
P07-E	Control Logic Diagram For LV Incomers of Well Pads	45	80%	$16.20	30-Aug-21	03-May-22
P07-E	Earthing Layout For Electrical Tower (Gantry) of Well Pads	45	0%	$12.14	04-May-22	17-Jun-22
P07-E	Cable Route Layout For Electrical Tower (Gantry) of Well Pac	45	0%	$16.20	18-Jun-22	01-Aug-22
P07-E	Overall Single Line Diagram of Well Pads	45	60%	$20.22	02-Mar-22	03-May-22
P07-E	Single Line Diagram For LV Switchgear of Well Pads	45	60%	$16.20	08-Feb-22	03-May-22
P07-E	Single Line Diagram For LV Power Distribution Panel of Well	45	0%	$16.20	29-Apr-22	12-Jun-22
P07-E	Single Line Diagram For DC Charger of Well Pads	45	80%	$16.20	06-Feb-22	03-May-22
P07-E	Single Line Diagram For Capacitor Banks of Well Pads	45	60%	$16.20	02-Feb-22	03-May-22
P07-E	Interconnection Wiring Diagram of Well Pads	45	0%	$24.28	29-Apr-22	12-Jun-22
P07-E	Area Lighting & Small Power Layout of Well Pads of Well Pad	40	0%	$16.20	01-Jul-22	09-Aug-22
P07-E	Lighting & Small Power Layout For Switchgear Building of We	45	0%	$12.14	03-May-22	16-Jun-22
P07-E	Lighting & Small Power Layout For Security Building of Well P	45	0%	$12.14	23-Sep-22	06-Nov-22
P07-E	Area Electrical Cable Route & Section Layout of Well Pads	30	0%	$20.22	26-Jun-22	25-Jul-22
P07-E	Electrical Cable Route & Section Layout For Switchgear Build	30	0%	$39.63	26-Jun-22	25-Jul-22
P07-E	Electrical Equipment Arrangement Layout For Switchgear Buil	30	0%	$24.94	17-Jun-22	16-Jul-22
P07-E	Earthing & Lightning Layout for well pads	30	0%	$16.34	09-May-22	07-Jun-22
P07-E	11KV Over Head Line Study Report	44	0%	$40.76	12-Jul-22	24-Aug-22
P07-E	33KV Over Head Line Study Report	44	0%	$40.76	18-Jun-22	31-Jul-22
List		89	37.67%	$49.85	25-Jan-22	28-Sep-22
P07-E	Electrical Load List of Well Pads	40	80%	$23.48	25-Jan-22	28-Apr-22
P07-E	Electrical Power & Control Cable List of Well Pads	50	0%	$13.19	10-Aug-22	28-Sep-22
P07-E	Cable Drum Schedule and Cutting List of Well Pads	50	0%	$13.19	10-Aug-22	28-Sep-22
Report		133	0%	$332.76	04-May-22	13-Sep-22
P07-E	Electrical Network (Load Flow, Motor Starting & Short Circuit)	54	0%	$95.24	04-May-22	26-Jun-22
P07-E	Relay Coordination & Setting Study Report of Well Pads	54	0%	$95.24	27-Jun-22	19-Aug-22
P07-E	11KV Over Head Line Study Report	44	0%	$71.14	01-Aug-22	13-Sep-22
P07-E	33KV Over Head Line Study Report	44	0%	$71.14	08-Jul-22	20-Aug-22
MTO		176	0%	$432.64	22-May-22	13-Nov-22
P07-E	MTO For Transmission Over Head Line - BK14	7	0%	$99.94	28-Jun-22	04-Jul-22
P07-E	MTO For Lighting & Small Powers - BK14	7	0%	$66.54	22-May-22	28-May-22
P07-E	MTO For Power & Control Cables - BK14	7	0%	$66.54	29-Sep-22	05-Oct-22
P07-E	MTO For Tray/Ladder and Accessories - BK14	7	0%	$66.54	26-Jul-22	01-Aug-22
P07-E	MTO For Electrical Bulk Items - BK14	7	0%	$66.54	07-Nov-22	13-Nov-22
P07-E	MTO For Earthing & Lightning Systems - BK14	7	0%	$66.54	18-Jun-22	24-Jun-22

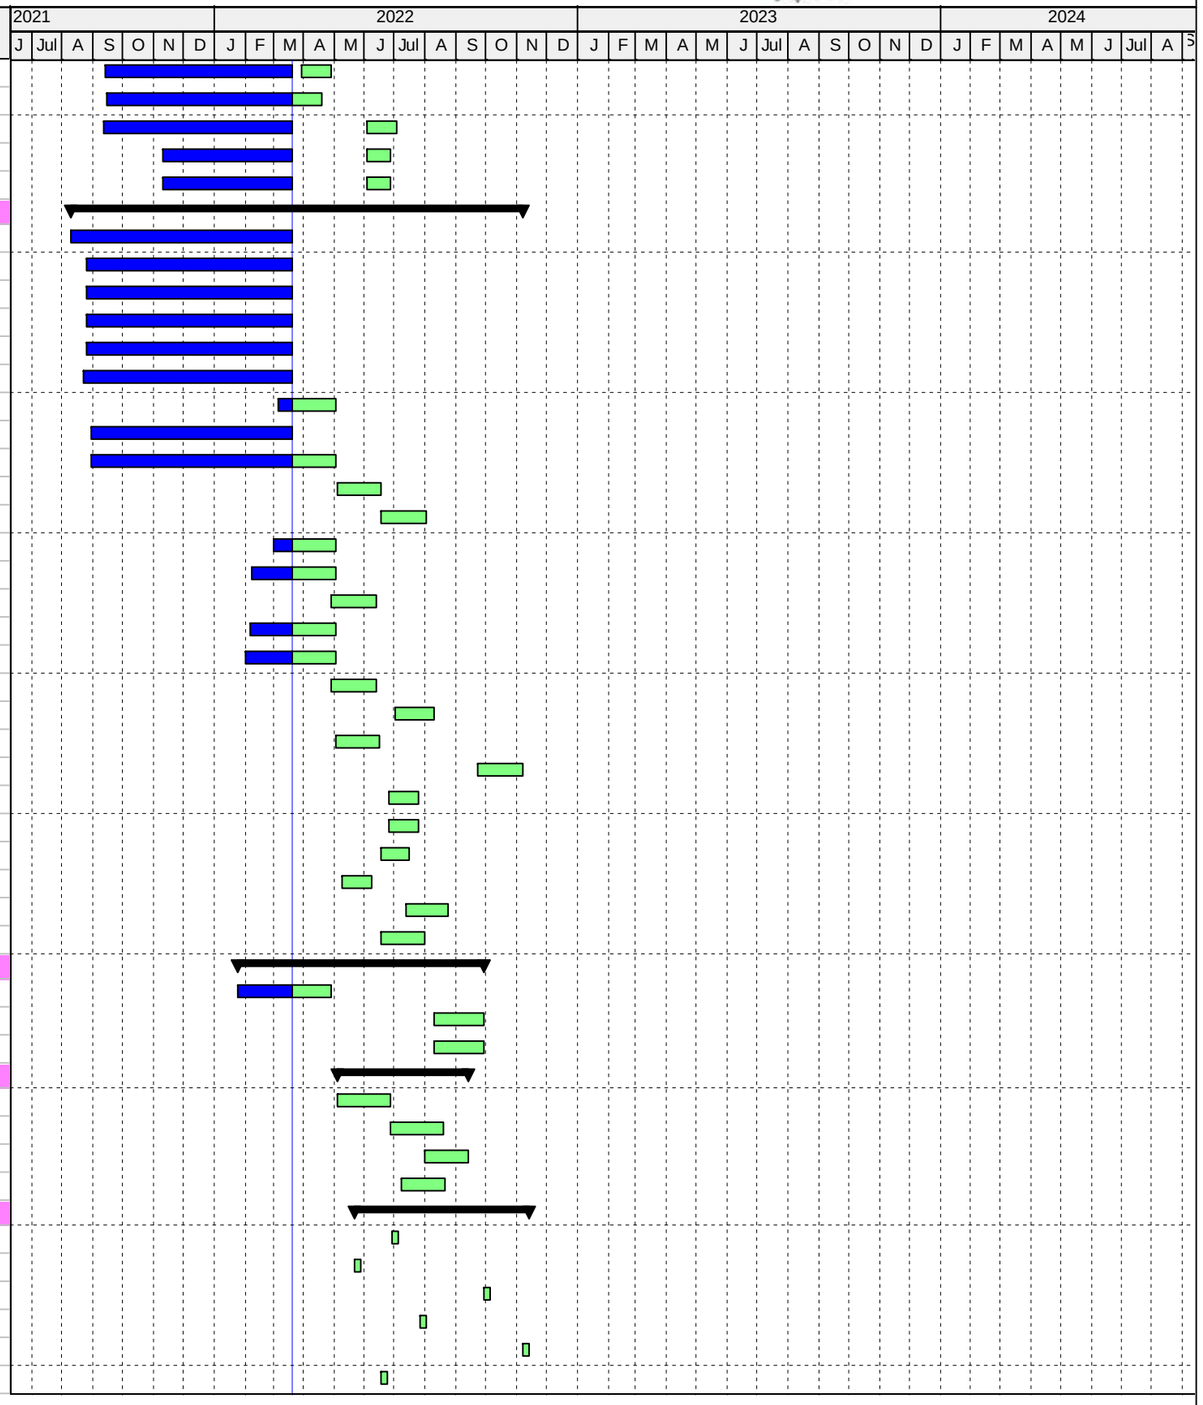


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Architecture		253	16.97%	$771.34	08-Feb-22	27-Oct-22
Basis/Criteria		74	60%	$155.89	08-Feb-22	01-Jun-22
P07-E	Architectural Design Criteria	74	60%	$155.89	08-Feb-22	01-Jun-22
Specification		44	0%	$194.76	20-Mar-22	02-May-22
P07-E	Buildings General Specification	44	0%	$194.76	20-Mar-22	02-May-22
Drawing/Diagram		218	20%	$186.97	24-Apr-22	22-Sep-22
P07-E	Architectural Drawing For Diesel Generator Shelter of Well P.	54	0%	$62.34	24-Apr-22	16-Jun-22
P07-E	Architectural Drawing For Switchgear Building of Well Pads -	44	60%	$62.32	18-May-22	02-May-22
P07-E	Architectural Drawing For Security Building of Well Pads - BK	44	0%	$62.32	10-Aug-22	22-Sep-22
MTO		35	0%	$233.72	23-Sep-22	27-Oct-22
P07-E	MTO For Architectural Works - BK14	35	0%	$233.72	23-Sep-22	27-Oct-22
Civil		129	25.57%	$739.69	01-Aug-21	27-Jul-22
Basis/Criteria		90	20%	$2.59	13-Feb-22	22-May-22
P07-E	Civil Design Criteria	64	60%	$0.86	13-Feb-22	22-May-22
P07-E	Design Criteria for Sewerage & Drainage	44	0%	$0.86	24-Mar-22	06-May-22
P07-E	Design Criteria for Road and Paving	44	0%	$0.86	27-Mar-22	09-May-22
Specification		94	72%	$13.24	09-Aug-21	06-Jun-22
P07-E	Specification For Civil Works	79	0%	$1.32	20-Mar-22	06-Jun-22
P07-E	Specification For Road & Paving	64	80%	$2.65	09-Aug-21	22-May-22
P07-E	Specification For Fence & Gate	64	100%	$2.65	18-Sep-21	20-Mar-22
P07-E	Specification For Earth Work	64	80%	$2.65	09-Aug-21	22-May-22
P07-E	Specification For Sewerage & Drainage	64	100%	$2.65	09-Aug-21	20-Mar-22
P07-E	Specification For Geological & Geotechnical Survey	44	0%	$1.32	20-Mar-22	02-May-22
Drawing/Diagram		108	18.08%	$563.94	01-Aug-21	05-Jun-22
P07-E	Standard Drawing For Civil Works	30	0%	$6.15	30-Mar-22	28-Apr-22
P07-E	Standard Drawing For Slope Protection Details	64	100%	$6.15	22-Aug-21	30-Mar-22
P07-E	Standard Drawing For Roads	64	80%	$6.15	22-Aug-21	01-Jun-22
P07-E	Standard Drawing For Electrical Cable Trench	64	100%	$6.15	22-Aug-21	30-Mar-22
P07-E	Standard Drawing For Manholes	64	80%	$6.15	22-Aug-21	01-Jun-22
P07-E	Standard Drawing For Catch Basins	64	80%	$6.15	22-Aug-21	05-Jun-22
P07-E	Standard Drawing For Sewerage & Drainage Details	30	60%	$6.15	02-Feb-22	05-Jun-22
P07-E	Standard Drawing For Civil Underground Crossings	38	60%	$10.43	07-Feb-22	10-May-22
P07-E	Standard Drawing For Fence & Gate Details	64	100%	$6.15	18-Sep-21	03-Apr-22
P07-E	Standard Drawing For Concrete Continues Weight	38	100%	$10.21	01-Aug-21	20-Mar-22
P07-E	Standard Drawing For Major Floodway Crossing	38	0%	$10.21	03-Apr-22	10-May-22
P07-E	Standard Drawing For Culvert & Details	38	100%	$10.21	25-Sep-21	03-Apr-22
P07-E	Standard Drawing For Valve Box	38	100%	$10.21	12-Jan-22	03-Apr-22
P07-E	Standard Drawing For Fire Hydrant Pit	38	60%	$10.21	13-Mar-22	10-May-22
P07-E	Standard Drawing For Pavings	38	60%	$10.21	08-Jan-22	10-May-22
P07-E	Standard Drawing For Earth Pit	38	60%	$10.21	13-Feb-22	10-May-22
P07-E	Standard Detail For Pipe Bedding	50	100%	$6.15	22-Aug-21	03-Apr-22
P07-E	Standard Details of Miscellaneous Items	50	60%	$6.15	06-Mar-22	22-May-22
P07-E	BINAK Oil Field Project Overall Well Location/Facilities Layou	30	0%	$4.62	20-Mar-22	18-Apr-22
P07-E	Civil and Structural drawings - BK14	30	0%	$130.66	24-Apr-22	24-May-22
P07-E	General Civil Layout - BK14	30	0%	$130.66	24-Apr-22	24-May-22
P07-E	Rough Grading Plans -BK14	30	0%	$154.63	24-Apr-22	24-May-22
Report		10	80%	$96.46	09-Nov-21	24-Apr-22
P07-E	Site Visit Report (Civil Work) - BK14	10	80%	$96.46	09-Nov-21	24-Apr-22
MTO		64	0%	$63.47	24-May-22	27-Jul-22

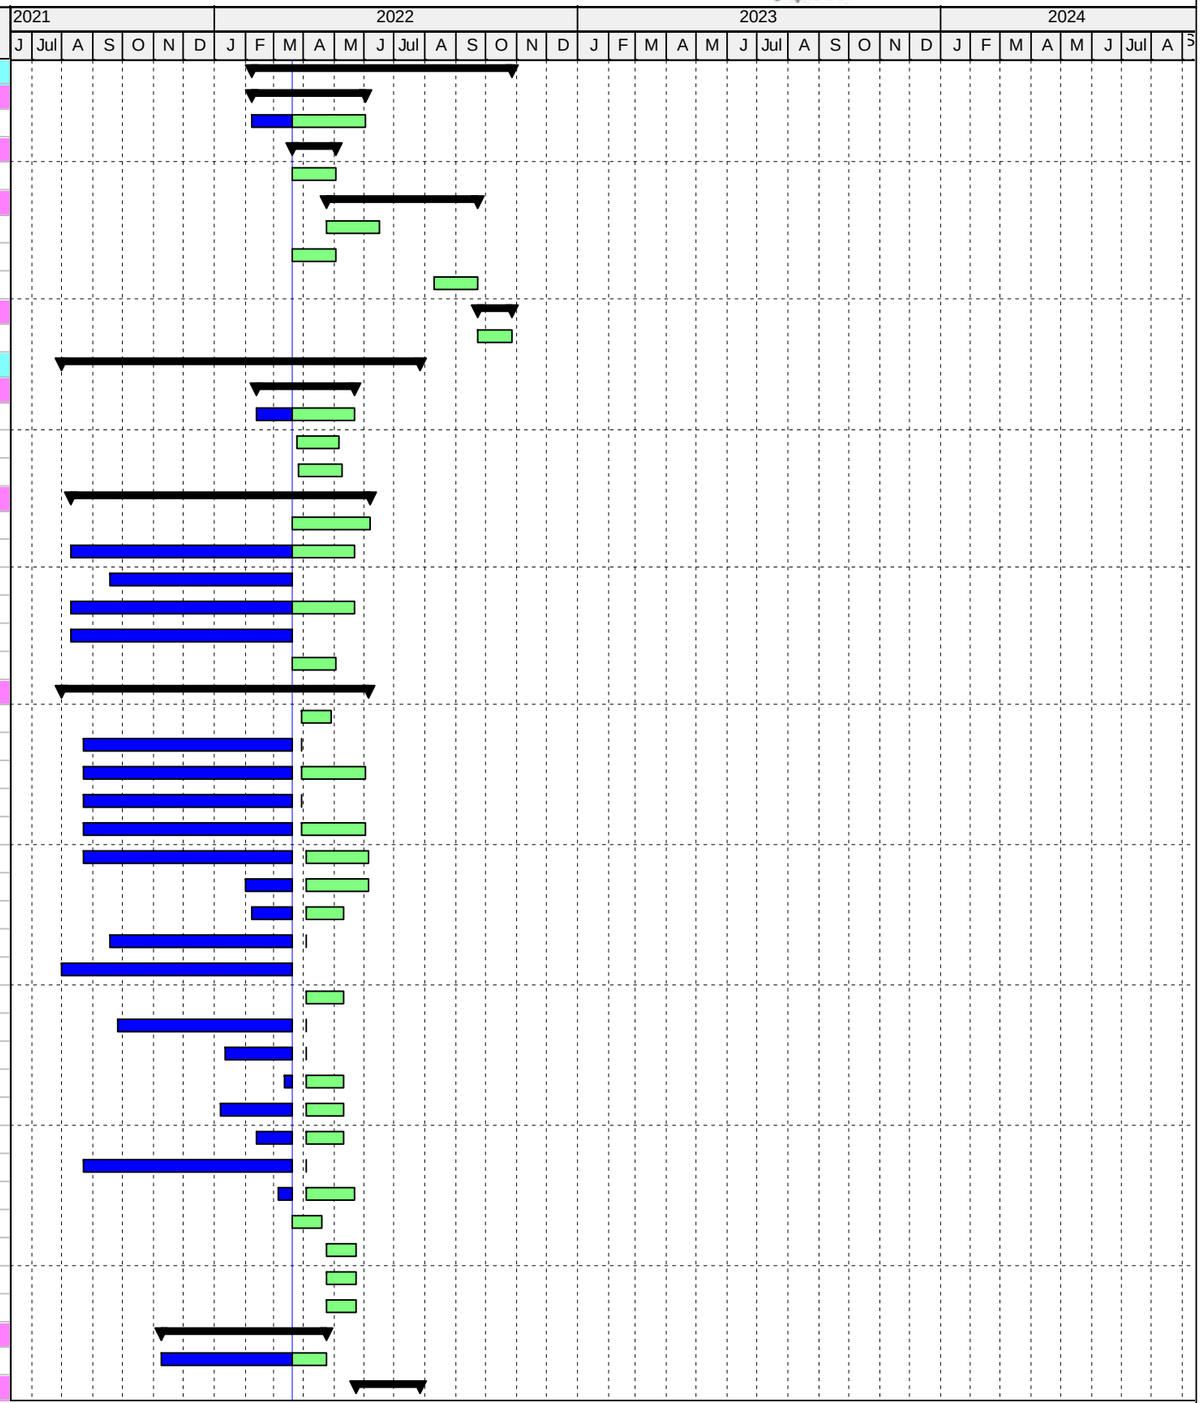


Actual Level of Effort | Remaining Work | Milestone

Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P07-E	MTO For Civil Works - BK14	64	0%	$63.47	24-May-22	27-Jul-22
Structure		184	15.19%	$981.10	08-Aug-21	19-Sep-22
Basis/Criteria		64	0%	$10.69	20-Mar-22	22-May-22
P07-E	Structural Design Criteria	64	0%	$3.57	20-Mar-22	22-May-22
P07-E	Design Criteria For Steel Structure	44	0%	$3.56	20-Mar-22	02-May-22
P07-E	Design Criteria For Load & Forces	44	0%	$3.56	20-Mar-22	02-May-22
Specification		98	98.97%	$81.73	14-Aug-21	26-May-22
P07-E	Specification For Concrete Work	64	80%	$1.19	14-Aug-21	26-May-22
P07-E	Specification For Storage Tank Foundation	38	100%	$30.97	23-Nov-21	24-Mar-22
P07-E	Specification for Fabrication of Steel Structures	64	100%	$0.61	24-Jan-22	24-Mar-22
P07-E	Specification For Grouting	64	100%	$23.98	14-Aug-21	24-Mar-22
P07-E	Specification for Erection of Steel Structures	64	100%	$0.80	24-Jan-22	24-Mar-22
P07-E	Specification for Fireproofing	64	100%	$23.57	18-Sep-21	24-Mar-22
P07-E	Specification For Steel Structural Works	37	0%	$0.60	20-Mar-22	25-Apr-22
Drawing/Diagram		167	10.78%	$632.71	08-Aug-21	12-Sep-22
P07-E	Standard Drawing For Fire Proofing	64	100%	$4.05	08-Aug-21	03-Apr-22
P07-E	Standard Drawing For Anchor Bolts	64	100%	$4.05	15-Dec-21	03-Apr-22
P07-E	Standard Drawing For Steel Stairs	64	100%	$4.05	18-Dec-21	03-Apr-22
P07-E	Standard Drawing For Operating Platform	38	100%	$4.81	27-Dec-21	30-Mar-22
P07-E	Standard Drawing For Handrail	38	100%	$6.83	18-Dec-21	30-Mar-22
P07-E	Standard Drawing For Insert Plates in Concrete	38	100%	$6.83	08-Aug-21	30-Mar-22
P07-E	Standard Details For Ladder & Safety Cage	64	100%	$4.05	15-Dec-21	03-Apr-22
P07-E	Standard Drawing For Lighting pole foundation Plan & Details	38	60%	$6.83	29-Jan-22	06-May-22
P07-E	General Notes - Steel Structures	38	100%	$4.81	25-Jan-22	30-Mar-22
P07-E	General Notes - Reinforced Concrete Structures	38	100%	$6.83	20-Dec-21	30-Mar-22
P07-E	Standard Drawing For Structural Built-up Sections	44	80%	$6.83	04-Dec-21	12-May-22
P07-E	Standard Drawing For Steel Flooring, Grating and Chequere	44	100%	$6.83	05-Jan-22	30-Mar-22
P07-E	Concrete Reinforcement Shape Code	44	0%	$6.83	30-Mar-22	12-May-22
P07-E	Standard Drawing For Septic Tank	44	80%	$6.83	22-Jan-22	12-May-22
P07-E	Fuel Oil Storage Drum Detail Drawing For Well Pads - BK-14	30	0%	$69.03	06-Aug-22	04-Sep-22
P07-E	Foundation Drawing For Security Building For Well Pads - Bk	44	0%	$69.03	03-May-22	15-Jun-22
P07-E	Structural Drawing For Security Building For Well Pads - BK-:	44	0%	$69.03	16-Jun-22	29-Jul-22
P07-E	Foundation Drawing For Switchgear Building For Well Pads -	44	0%	$69.03	03-May-22	15-Jun-22
P07-E	Structural Drawing For Switchgear Building For Well Pads - E	44	0%	$69.03	16-Jun-22	29-Jul-22
P07-E	Foundation Drawing For Potable Water Tank For Well Pads -	44	0%	$69.03	22-Jul-22	03-Sep-22
P07-E	Foundation Drawing For Diesel Generator Shelter For Well F	44	0%	$69.03	17-Jun-22	30-Jul-22
P07-E	Structural Drawing For Diesel Generator Shelter For Well Pa	44	0%	$69.03	31-Jul-22	12-Sep-22
MTO		7	0%	$255.97	13-Sep-22	19-Sep-22
P07-E	MTO For Structural Works - BK14	7	0%	$255.97	13-Sep-22	19-Sep-22
General		116	13.46%	$1,475.70	11-Aug-21	13-Jul-22
Geotechnic		104	8%	$1,180.56	11-Aug-21	02-May-22
Procedure/Plan		44	100%	$94.44	11-Aug-21	19-Apr-22
P07-	Geotechnical Investigation Plan for Well Pads	44	100%	$94.44	11-Aug-21	19-Apr-22
Report		44	0%	$1,086.12	20-Mar-22	02-May-22
P07-	Geotechnical Investigation Report - BK14	44	0%	$1,086.12	20-Mar-22	02-May-22
Survey		46	60%	$147.57	21-Feb-22	04-May-22
Drawing/Diagram		46	60%	$147.57	21-Feb-22	04-May-22
P07-	Over Head Line Plan and Profile - BK14	46	60%	$147.57	21-Feb-22	04-May-22
QC/QA		116	10.58%	$147.57	20-Sep-21	13-Jul-22

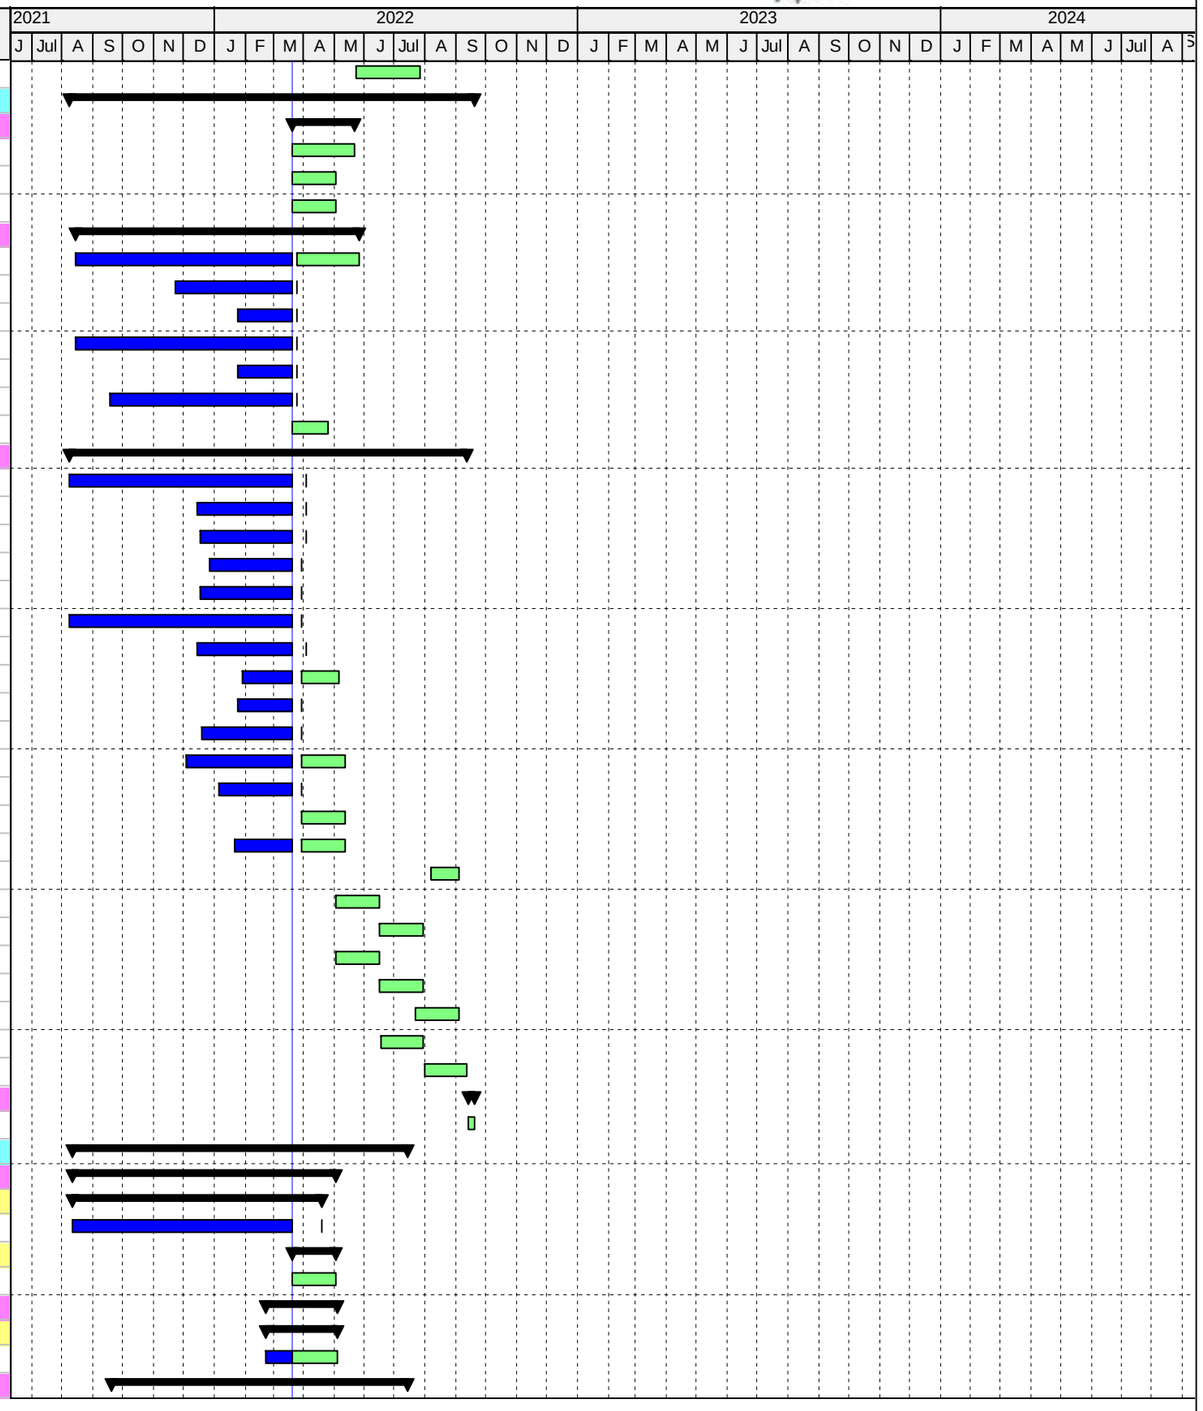


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
QC Management		116	38.9%	$12.00	08-Dec-21	13-Jul-22
P07-	Project Audit Procedure	44	0%	$0.60	20-Mar-22	02-May-22
P07-	Specification For Final Data Book (FDB) Requirements	44	0%	$0.60	20-Mar-22	02-May-22
P07-	Non Conformance Control Procedure	36	0%	$0.60	03-May-22	07-Jun-22
P07-	Corrective Action Procedure	36	0%	$0.60	08-Jun-22	13-Jul-22
P07-	Material Reciving, Storage, Handling Procedure	39	60%	$0.60	20-Feb-22	27-Apr-22
P07-	Packing, Marking, Transportation Procedure	39	0%	$0.60	20-Mar-22	27-Apr-22
P07-	Criticality Assessment Procedure	39	0%	$2.40	20-Mar-22	27-Apr-22
P07-	Project Quality Plan	44	80%	$5.40	08-Dec-21	02-May-22
P07-	Technical Query Procedure	44	0%	$0.60	30-Mar-22	12-May-22
QC General Document		55	8.57%	$17.52	28-Nov-21	16-May-22
P07-	Quality Control Plan (QCP)	39	60%	$2.50	28-Nov-21	27-Apr-22
P07-	Specification for Welding Procedure	44	0%	$2.50	03-Apr-22	16-May-22
P07-	Heat Treatment Procedure (Pre Heating , PWHT)	44	0%	$2.50	03-Apr-22	16-May-22
P07-	Welder Performance Qualification Test (WQT) Procedure	44	0%	$2.50	03-Apr-22	16-May-22
P07-	NDT Procedure	44	0%	$2.50	03-Apr-22	16-May-22
P07-	Surface Preparation and Coating/Painting Procedure	44	0%	$2.50	03-Apr-22	16-May-22
P07-	Control of Inspection Measuring and Test Equipment Procedu	44	0%	$2.49	03-Apr-22	16-May-22
QC Discipline Document		81	7.99%	$118.06	20-Sep-21	16-May-22
Piping		51	0%	$29.51	27-Mar-22	16-May-22
P07	ITP For Piping Works	44	0%	$2.95	27-Mar-22	09-May-22
P07	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$3.32	03-Apr-22	16-May-22
P07	PIPING WPS (Welding Procedure Specification)	44	0%	$3.32	03-Apr-22	16-May-22
P07	PIPING PQR (Procedure Qualification Record)	44	0%	$3.32	03-Apr-22	16-May-22
P07	PIPING PQR (Procedure Qualification Record)	44	0%	$3.32	03-Apr-22	16-May-22
P07	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$3.32	03-Apr-22	16-May-22
P07	PIPING WPS (Preliminary Welding Procedure Specification) f	44	0%	$3.32	03-Apr-22	16-May-22
P07	PIPING PQR (Procedure Qualification Record) for Repair W	44	0%	$3.32	03-Apr-22	16-May-22
P07	Field Joint Coating Procedure For Pipeline	44	0%	$3.32	03-Apr-22	16-May-22
P07	Pressure Test Procedure	44	0%	$3.32	03-Apr-22	16-May-22
Telecomm.		44	0%	$5.90	27-Mar-22	09-May-22
P07	ITP For Telecommunication Installation	44	0%	$5.90	27-Mar-22	09-May-22
Safety		44	0%	$5.90	27-Mar-22	09-May-22
P07	ITP For Safety Installation	44	0%	$5.90	27-Mar-22	09-May-22
Architectural		44	0%	$5.90	27-Mar-22	09-May-22
P07	ITP For Architectural Works	44	0%	$5.90	27-Mar-22	09-May-22
Mechanical		44	0%	$5.90	27-Mar-22	09-May-22
P07	ITP For Mechanical Installation	44	0%	$5.90	27-Mar-22	09-May-22
Structure		51	0%	$23.61	27-Mar-22	16-May-22
P07	ITP For Steel Structural Works	44	0%	$2.36	27-Mar-22	09-May-22
P07	Steel Structure WPS (Welding Procedure Specification)	44	0%	$3.54	03-Apr-22	16-May-22
P07	Steel Structure PQR (Procedure Qualification Record)	44	0%	$3.54	03-Apr-22	16-May-22
P07	Steel Structure WPS (Welding Procedure Specification) For F	44	0%	$3.54	03-Apr-22	16-May-22
P07	Steel Structure PQR (Procedure Qualification Record) For R	44	0%	$3.54	03-Apr-22	16-May-22
P07	Weld Map For Steel Structures	44	0%	$3.54	03-Apr-22	16-May-22
P07	NDT Plan For steel Structures	44	0%	$3.54	03-Apr-22	16-May-22
Instrumentation		44	0%	$5.90	27-Mar-22	09-May-22
P07	ITP For I&C Installation	44	0%	$5.90	27-Mar-22	09-May-22
Pipeline		74	15%	$23.61	16-Jan-22	16-May-22
P07	ITP For Pipeline	44	60%	$2.36	16-Jan-22	09-May-22

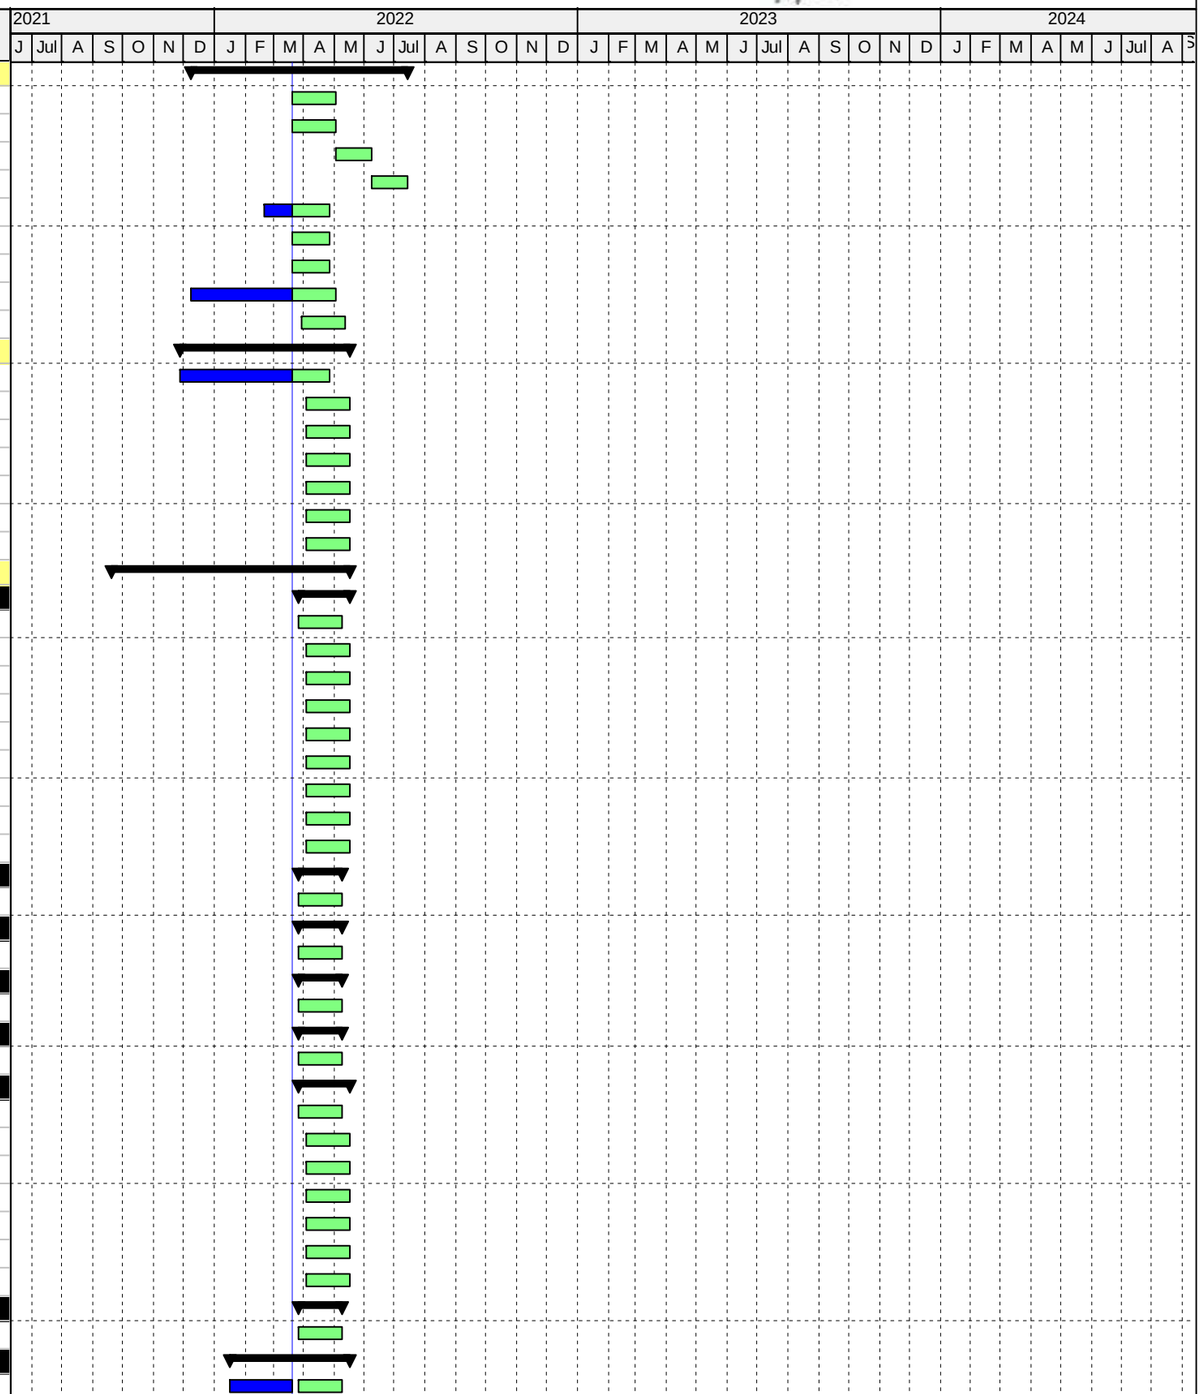

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P07	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	60%	$3.54	23-Feb-22	16-May-22
P07	PIPELINE WPS (Welding Procedure Specification)	44	0%	$3.54	03-Apr-22	16-May-22
P07	PIPELINE PQR (Procedure Qualification Record)	44	0%	$3.54	03-Apr-22	16-May-22
P07	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	0%	$3.54	03-Apr-22	16-May-22
P07	PIPELINE WPS (Preliminary Welding Procedure Specificatior	44	0%	$3.54	03-Apr-22	16-May-22
P07	PIPELINE PQR (Procedure Qualification Record) for Repair \	44	0%	$3.54	03-Apr-22	16-May-22
Civil		44	100%	$5.90	20-Sep-21	27-Mar-22
P07	ITP For Civil Works	44	100%	$5.90	20-Sep-21	27-Mar-22
Electrical		44	0%	$5.90	27-Mar-22	09-May-22
P07	ITP For Electrical Installation	44	0%	$5.90	27-Mar-22	09-May-22
Procurement Engineering		333	0%	$1,338.20	19-Apr-22	17-Mar-23
Mechanical		59	0%	$133.82	29-May-22	26-Jul-22
Drum		31	0%	$80.29	29-May-22	28-Jun-22
P07-E	PMR For Drum - BK14	7	0%	$8.03	29-May-22	04-Jun-22
P07-E	TBE For Drum - BK14	5	0%	$12.04	05-Jun-22	09-Jun-22
P07-E	VDR For Drum - BK14	7	0%	$60.22	22-Jun-22	28-Jun-22
Potable Tanks		34	0%	$53.53	23-Jun-22	26-Jul-22
P07-E	PMR For Potable Tanks - BK14	10	0%	$5.35	23-Jun-22	02-Jul-22
P07-E	TBE For Potable Tanks - BK14	5	0%	$8.03	03-Jul-22	07-Jul-22
P07-E	VDR For Potable Tanks - BK14	7	0%	$40.15	20-Jul-22	26-Jul-22
Structure		19	0%	$82.30	20-Sep-22	08-Oct-22
Steel Structure Items		13	0%	$27.44	20-Sep-22	02-Oct-22
P07-E	PMR For Steel Structure Items - BK14	3	0%	$2.74	20-Sep-22	22-Sep-22
P07-E	TBE For Steel Structure Items - BK14	3	0%	$4.12	27-Sep-22	29-Sep-22
P07-E	VDR For Steel Structure Items - BK14	3	0%	$20.58	30-Sep-22	02-Oct-22
Anchor Bolts		19	0%	$27.43	20-Sep-22	08-Oct-22
P07-E	PMR For Anchor Bolts - BK14	7	0%	$2.74	20-Sep-22	26-Sep-22
P07-E	TBE For Anchor Bolts - BK14	7	0%	$4.11	27-Sep-22	03-Oct-22
P07-E	VDR For Anchor Bolts - BK14	5	0%	$20.57	04-Oct-22	08-Oct-22
Blast Proof Doors		19	0%	$27.43	20-Sep-22	08-Oct-22
P07-E	PMR For Blast Proof Doors - BK14	7	0%	$2.74	20-Sep-22	26-Sep-22
P07-E	TBE For Blast Proof Doors - BK14	7	0%	$4.11	27-Sep-22	03-Oct-22
P07-E	VDR For Blast Proof Doors - BK14	5	0%	$20.57	04-Oct-22	08-Oct-22
Electrical		245	0%	$971.00	19-Apr-22	19-Dec-22
UPS System		54	0%	$73.31	13-Jul-22	04-Sep-22
P07-E	PMR For UPS System - BK14	7	0%	$7.33	13-Jul-22	19-Jul-22
P07-E	TBE For UPS System - BK14	20	0%	$11.00	20-Jul-22	08-Aug-22
P07-E	VDR For UPS System - BK14	7	0%	$54.98	29-Aug-22	04-Sep-22
Transformers		54	0%	$73.31	19-Apr-22	11-Jun-22
P07-E	PMR For Transformers - BK14	7	0%	$7.33	19-Apr-22	25-Apr-22
P07-E	TBE For Transformers - BK14	20	0%	$11.00	26-Apr-22	15-May-22
P07-E	VDR For Transformers - BK14	7	0%	$54.98	05-Jun-22	11-Jun-22
Transmission Over head Line		54	0%	$91.57	05-Jul-22	27-Aug-22
P07-E	PMR For Transmission Over head Line - BK14	7	0%	$9.16	05-Jul-22	11-Jul-22
P07-E	TBE For Transmission Over head Line - BK14	20	0%	$13.73	12-Jul-22	31-Jul-22
P07-E	VDR For Transmission Over head Line - BK14	7	0%	$68.67	21-Aug-22	27-Aug-22
LV Switchgear & MCC		54	0%	$73.31	19-Apr-22	11-Jun-22
P07-E	PMR For LV Switchgear & MCC - BK14	7	0%	$7.33	19-Apr-22	25-Apr-22
P07-E	TBE For LV Switchgear & MCC - BK14	20	0%	$11.00	26-Apr-22	15-May-22
P07-E	VDR For LV Switchgear & MCC - BK14	7	0%	$54.98	05-Jun-22	11-Jun-22




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Emergency Diesel Generator		39	0%	$73.31	24-Apr-22	01-Jun-22
P07-E	PMR For Emergency Diesel Generator - BK14	7	0%	$7.33	24-Apr-22	30-Apr-22
P07-E	TBE For Emergency Diesel Generator - BK14	15	0%	$11.00	01-May-22	15-May-22
P07-E	VDR For Emergency Diesel Generator - BK14	7	0%	$54.98	26-May-22	01-Jun-22
DC Charger		49	0%	$73.31	24-Apr-22	11-Jun-22
P07-E	PMR For DC Charger - BK14	7	0%	$7.33	24-Apr-22	30-Apr-22
P07-E	TBE For DC Charger - BK14	20	0%	$11.00	01-May-22	20-May-22
P07-E	VDR For DC Charger - BK14	7	0%	$54.98	05-Jun-22	11-Jun-22
Capacitor Bank		44	0%	$73.31	19-Apr-22	01-Jun-22
P07-E	PMR For Capacitor Bank - BK14	7	0%	$7.33	19-Apr-22	25-Apr-22
P07-E	TBE For Capacitor Bank - BK14	20	0%	$11.00	26-Apr-22	15-May-22
P07-E	VDR For Capacitor Bank - BK14	7	0%	$54.98	26-May-22	01-Jun-22
Lighting & Distribution Main Panels		54	0%	$73.31	03-Jul-22	25-Aug-22
P07-E	PMR For Lighting & Distribution Main Panels - BK14	7	0%	$7.33	03-Jul-22	09-Jul-22
P07-E	TBE For Lighting & Distribution Main Panels - BK14	20	0%	$11.00	10-Jul-22	29-Jul-22
P07-E	VDR For Lighting & Distribution Main Panels - BK14	7	0%	$54.98	19-Aug-22	25-Aug-22
Earthing & Lightning System		39	0%	$73.31	25-Jun-22	02-Aug-22
P07-E	PMR For Earthing & Lightning System - BK14	7	0%	$7.33	25-Jun-22	01-Jul-22
P07-E	TBE For Earthing & Lightning System - BK14	15	0%	$11.00	02-Jul-22	16-Jul-22
P07-E	VDR For Earthing & Lightning System - BK14	7	0%	$54.98	27-Jul-22	02-Aug-22
Lighting and Small Power Equipment		51	0%	$73.31	29-May-22	18-Jul-22
P07-E	PMR For Lighting and Small Power Equipment - BK14	7	0%	$7.33	29-May-22	04-Jun-22
P07-E	TBE For Lighting and Small Power Equipment - BK14	20	0%	$11.00	05-Jun-22	24-Jun-22
P07-E	VDR For Lighting and Small Power Equipment - BK14	7	0%	$54.98	12-Jul-22	18-Jul-22
Tray/Ladder and Accessories		44	0%	$73.21	02-Aug-22	14-Sep-22
P07-E	PMR For Tray/Ladder and Accessories - BK14	7	0%	$7.32	02-Aug-22	08-Aug-22
P07-E	TBE For Tray/Ladder and Accessories - BK14	20	0%	$10.98	09-Aug-22	28-Aug-22
P07-E	VDR For Tray/Ladder and Accessories - BK14	7	0%	$54.91	08-Sep-22	14-Sep-22
Power & Control Cables		54	0%	$73.21	06-Oct-22	28-Nov-22
P07-E	PMR For Power & Control Cables - BK14	7	0%	$7.32	06-Oct-22	12-Oct-22
P07-E	TBE For Power & Control Cables - BK14	20	0%	$10.98	13-Oct-22	01-Nov-22
P07-E	VDR For Power & Control Cables - BK14	7	0%	$54.91	22-Nov-22	28-Nov-22
Electrical Bulk Items		36	0%	$73.21	14-Nov-22	19-Dec-22
P07-E	PMR For Electrical Bulk Items - BK14	7	0%	$7.32	14-Nov-22	20-Nov-22
P07-E	TBE For Electrical Bulk Items - BK14	10	0%	$10.98	21-Nov-22	30-Nov-22
P07-E	VDR For Electrical Bulk Items - BK14	7	0%	$54.91	13-Dec-22	19-Dec-22
Piping		56	0%	$54.87	10-May-22	04-Jul-22
Pipe		56	0%	$27.43	10-May-22	04-Jul-22
P07-E	PMR For Pipes - BK14	7	0%	$2.74	10-May-22	16-May-22
P07-E	TBE For Pipes - BK14	25	0%	$4.11	17-May-22	10-Jun-22
P07-E	VDR For Pipes - BK14	7	0%	$20.57	28-Jun-22	04-Jul-22
Pipe Support		41	0%	$27.43	17-May-22	26-Jun-22
P07-E	PMR For Pipe Support - BK14	5	0%	$2.74	17-May-22	21-May-22
P07-E	TBE For Pipe Support - BK14	15	0%	$4.11	24-May-22	07-Jun-22
P07-E	VDR For Pipe Support - BK14	7	0%	$20.57	20-Jun-22	26-Jun-22
Civil		17	0%	$54.87	24-May-22	10-Jun-22
Geomembrane		17	0%	$27.43	24-May-22	10-Jun-22
P07-E	PMR For Geomembrane - BK14	7	0%	$2.74	24-May-22	31-May-22
P07-E	TBE For Geomembrane - BK14	5	0%	$4.11	31-May-22	05-Jun-22

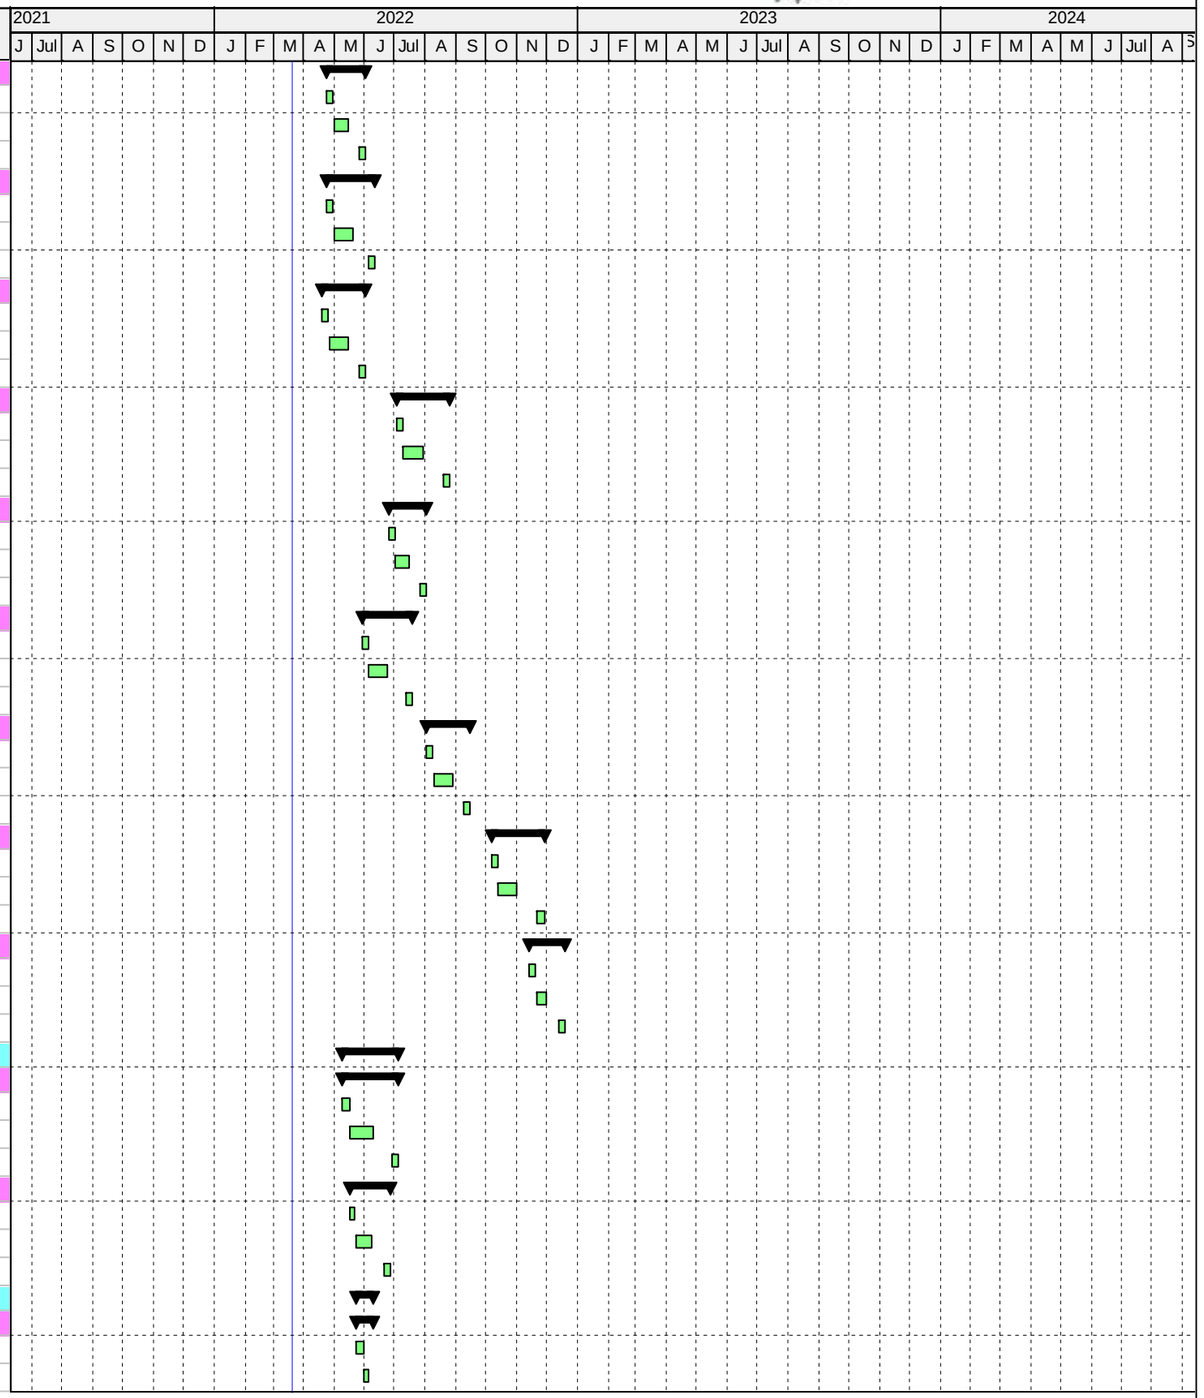


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P07-E	VDR For Geomembrane - BK14	5	0%	$20.57	05-Jun-22	10-Jun-22
Geotextile		17	0%	$27.43	24-May-22	10-Jun-22
P07-E	PMR For Geotextile - BK14	7	0%	$2.74	24-May-22	31-May-22
P07-E	TBE For Geotextile - BK14	5	0%	$4.11	31-May-22	05-Jun-22
P07-E	VDR For Geotextile - BK14	5	0%	$20.57	05-Jun-22	10-Jun-22
HVAC		41	0%	$41.35	05-Feb-23	17-Mar-23
Main HVAC Equipment		41	0%	$41.35	05-Feb-23	17-Mar-23
P07-E	PMR For Main HVAC Equipment - BK14	7	0%	$4.14	05-Feb-23	11-Feb-23
P07-E	TBE For Main HVAC Equipment - BK14	15	0%	$6.20	12-Feb-23	26-Feb-23
P07-E	VDR For Main HVAC Equipment - BK14	7	0%	$31.01	11-Mar-23	17-Mar-23
Commissioning Engineering		345	0%	$267.64	18-Jun-22	28-May-23
P07-EP	Operability Review	5	0%	$53.53	04-May-23	08-May-23
P07-EP	Pre-Commissioning, Commissioning & Startup Procedure - BI	44	0%	$160.58	18-Jun-22	31-Jul-22
P07-EP	Operating Manual - BK14	25	0%	$53.53	04-May-23	28-May-23
Field Engineering		344	0%	$2,007.30	24-Jun-22	02-Jun-23
P07-EP	Technical/Site Queries	44	0%	$1,003.65	24-Jun-22	06-Aug-22
Dossier		5	0%	$1,003.65	29-May-23	02-Jun-23
P07-EI	As-Built Document Booklets - BK14	5	0%	$1,003.65	29-May-23	02-Jun-23
Engineering Final Documentation		5	0%	$1,338.20	03-Jun-23	07-Jun-23
P07-EP	Final Engineering Dossier - BK14	5	0%	$1,338.20	03-Jun-23	07-Jun-23
PROCUREMENT		353	0%	$327,506.00	16-May-22	03-May-23
Mechanical		94	0%	$16,015.04	10-Jun-22	11-Sep-22
Fuel Oil Storage Drum		60	0%	$9,609.03	10-Jun-22	08-Aug-22
P07-EI	Tendering & Selection	7	0%	$384.36	10-Jun-22	16-Jun-22
P07-EI	Contract Effectiveness / PO	5	0%	$576.54	17-Jun-22	21-Jun-22
P07-EI	Manufacturing / Fabrication / Supply	30	0%	$4,804.51	22-Jun-22	21-Jul-22
P07-EI	Final Inspection	7	0%	$960.90	22-Jul-22	28-Jul-22
P07-EI	Delivery On Site	5	0%	$1,921.81	29-Jul-22	02-Aug-22
P07-EI	Submitting Vendor Data Book	3	0%	$480.45	03-Aug-22	05-Aug-22
P07-EI	Delivering Spare Parts	3	0%	$480.45	06-Aug-22	08-Aug-22
Potable Water Tank		66	0%	$6,406.02	08-Jul-22	11-Sep-22
P07-EI	Tendering & Selection	7	0%	$256.24	08-Jul-22	14-Jul-22
P07-EI	Contract Effectiveness / PO	5	0%	$384.36	15-Jul-22	19-Jul-22
P07-EI	Manufacturing / Fabrication / Supply	30	0%	$3,203.01	20-Jul-22	18-Aug-22
P07-EI	Final Inspection	7	0%	$640.60	19-Aug-22	25-Aug-22
P07-EI	Delivery On Site	7	0%	$1,281.20	26-Aug-22	01-Sep-22
P07-EI	Submitting Vendor Data Book	5	0%	$320.30	02-Sep-22	06-Sep-22
P07-EI	Delivering Spare Parts	5	0%	$320.30	07-Sep-22	11-Sep-22
Piping		77	0%	$29,999.55	08-Jun-22	23-Aug-22
Pipes - BK14		69	0%	$23,999.64	16-Jun-22	23-Aug-22
P07-EI	Tendering & Selection	7	0%	$959.99	16-Jun-22	22-Jun-22
P07-EI	Contract Effectiveness / PO	5	0%	$1,439.98	23-Jun-22	27-Jun-22
P07-EI	Manufacturing / Fabrication / Supply	40	0%	$11,999.82	28-Jun-22	06-Aug-22
P07-EI	Final Inspection	7	0%	$2,399.96	07-Aug-22	13-Aug-22
P07-EI	Delivery On Site	5	0%	$5,999.91	14-Aug-22	18-Aug-22
P07-EI	Submitting Vendor Data Book	5	0%	$1,199.98	19-Aug-22	23-Aug-22
Pipe Support - BK14		61	0%	$5,999.91	08-Jun-22	07-Aug-22
P07-EI	Tendering & Selection	7	0%	$240.00	08-Jun-22	14-Jun-22
P07-EI	Contract Effectiveness / PO	5	0%	$359.99	15-Jun-22	19-Jun-22

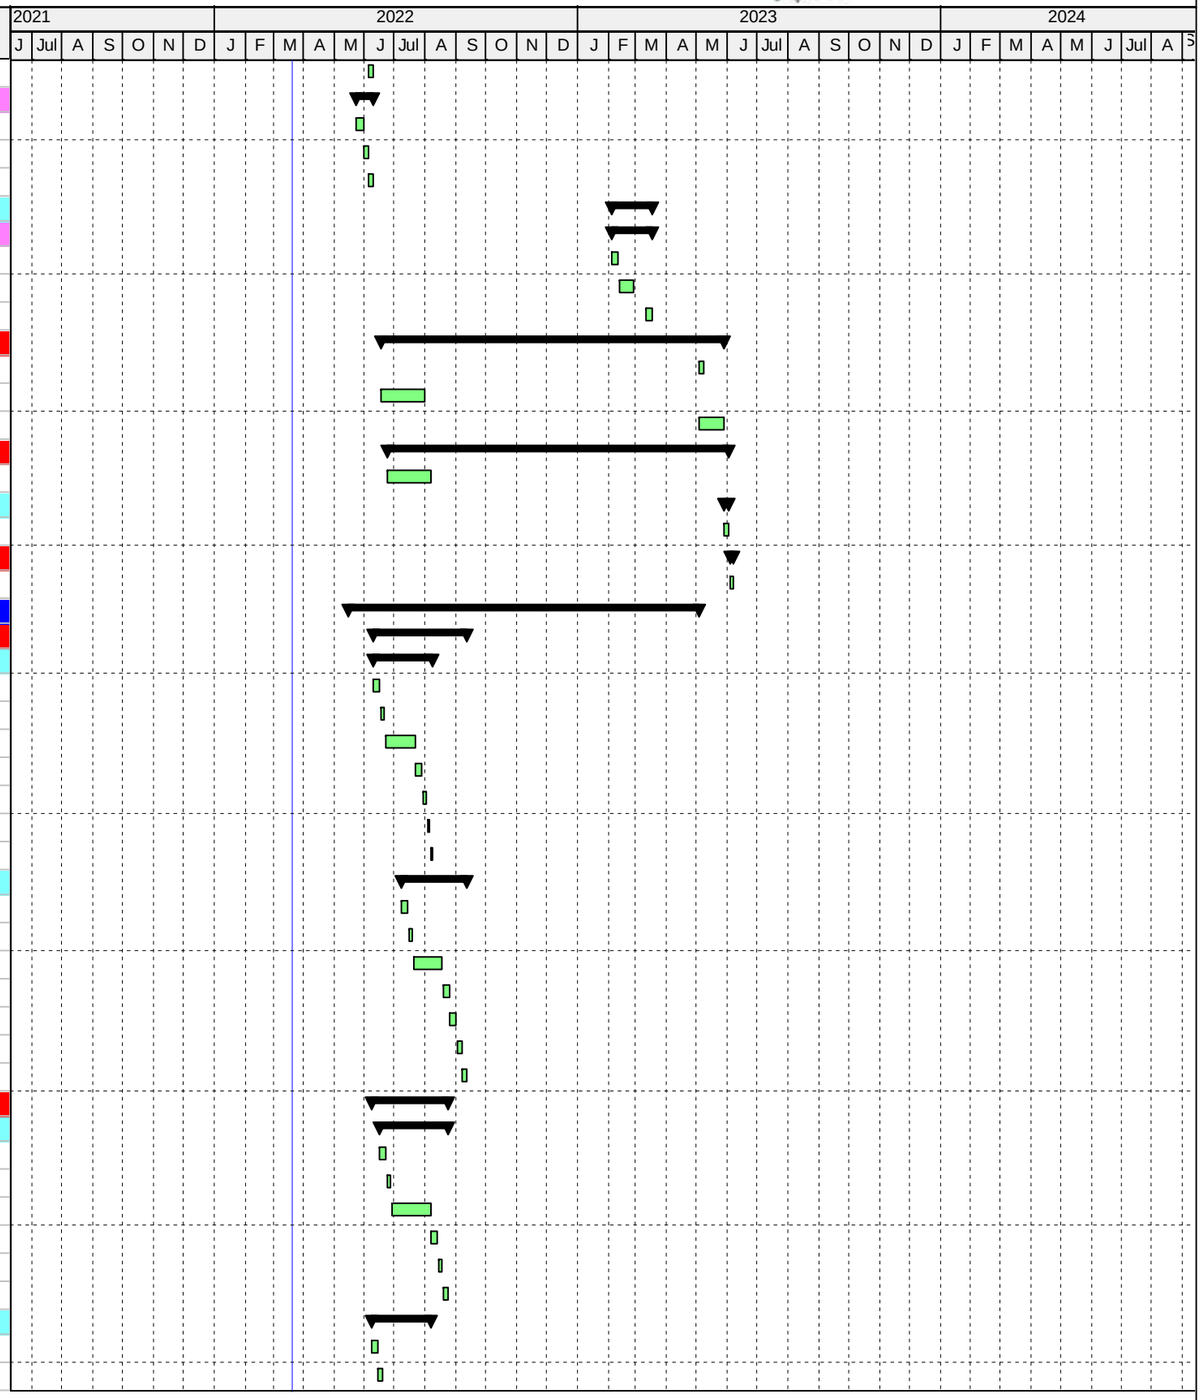


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P07-EF	Manufacturing / Fabrication / Supply	30	0%	$2,999.95	20-Jun-22	19-Jul-22
P07-EF	Final Inspection	7	0%	$599.99	20-Jul-22	26-Jul-22
P07-EF	Delivery On Site	7	0%	$1,499.98	27-Jul-22	02-Aug-22
P07-EF	Submitting Vendor Data Book	5	0%	$300.00	03-Aug-22	07-Aug-22
HVAC		66	0%	$5,993.36	27-Feb-23	03-May-23
Main HVAC Equipment - BK14		66	0%	$5,993.36	27-Feb-23	03-May-23
P07-EF	Tendering & Selection	7	0%	$239.73	27-Feb-23	05-Mar-23
P07-EF	Contract Effectiveness / PO	5	0%	$359.60	06-Mar-23	10-Mar-23
P07-EF	Manufacturing / Fabrication / Supply	35	0%	$2,996.68	11-Mar-23	14-Apr-23
P07-EF	Final Inspection	7	0%	$599.34	15-Apr-23	21-Apr-23
P07-EF	Delivery On Site	7	0%	$1,498.34	22-Apr-23	28-Apr-23
P07-EF	Submitting Vendor Data Book	5	0%	$299.67	29-Apr-23	03-May-23
Electrical		265	0%	$275,498.05	16-May-22	04-Feb-23
Electrical Bulk Items - BK14		66	0%	$2,231.53	01-Dec-22	04-Feb-23
P07-EF	Tendering & Selection	7	0%	$89.26	01-Dec-22	07-Dec-22
P07-EF	Contract Effectiveness / PO	5	0%	$133.89	08-Dec-22	12-Dec-22
P07-EF	Manufacturing / Fabrication / Supply	35	0%	$1,115.77	13-Dec-22	16-Jan-23
P07-EF	Final Inspection	7	0%	$223.15	17-Jan-23	23-Jan-23
P07-EF	Delivery On Site	7	0%	$557.88	24-Jan-23	30-Jan-23
P07-EF	Submitting Vendor Data Book	5	0%	$111.58	31-Jan-23	04-Feb-23
Lighting and Small Power Equipment - BK14		71	0%	$12,700.46	30-Jun-22	08-Sep-22
P07-EF	Tendering & Selection	7	0%	$508.02	30-Jun-22	06-Jul-22
P07-EF	Contract Effectiveness / PO	5	0%	$762.03	07-Jul-22	11-Jul-22
P07-EF	Manufacturing / Fabrication / Supply	35	0%	$6,350.23	12-Jul-22	15-Aug-22
P07-EF	Final Inspection	7	0%	$1,270.05	16-Aug-22	22-Aug-22
P07-EF	Delivery On Site	7	0%	$2,540.09	23-Aug-22	29-Aug-22
P07-EF	Submitting Vendor Data Book	5	0%	$635.02	30-Aug-22	03-Sep-22
P07-EF	Delivering Spare Parts	5	0%	$635.02	04-Sep-22	08-Sep-22
DC Charger - BK14		74	0%	$17,273.73	21-May-22	02-Aug-22
P07-EF	Tendering & Selection	10	0%	$690.95	21-May-22	30-May-22
P07-EF	Contract Effectiveness / PO	5	0%	$1,036.42	31-May-22	04-Jun-22
P07-EF	Manufacturing / Fabrication / Supply	35	0%	$8,636.86	05-Jun-22	09-Jul-22
P07-EF	Final Inspection	7	0%	$1,727.37	10-Jul-22	16-Jul-22
P07-EF	Delivery On Site	7	0%	$3,454.75	17-Jul-22	23-Jul-22
P07-EF	Submitting Vendor Data Book	5	0%	$863.69	24-Jul-22	28-Jul-22
P07-EF	Delivering Spare Parts	5	0%	$863.69	29-Jul-22	02-Aug-22
Tray/Ladder and Accessories - BK14		64	0%	$2,231.53	29-Aug-22	31-Oct-22
P07-EF	Tendering & Selection	5	0%	$89.26	29-Aug-22	02-Sep-22
P07-EF	Contract Effectiveness / PO	5	0%	$133.89	03-Sep-22	07-Sep-22
P07-EF	Manufacturing / Fabrication / Supply	35	0%	$1,115.77	08-Sep-22	12-Oct-22
P07-EF	Final Inspection	7	0%	$223.15	13-Oct-22	19-Oct-22
P07-EF	Delivery On Site	7	0%	$557.88	20-Oct-22	26-Oct-22
P07-EF	Submitting Vendor Data Book	5	0%	$111.58	27-Oct-22	31-Oct-22
Lighting & Distribution Main Panels - BK14		69	0%	$6,226.26	09-Aug-22	16-Oct-22
P07-EF	Tendering & Selection	5	0%	$249.05	09-Aug-22	13-Aug-22
P07-EF	Contract Effectiveness / PO	5	0%	$373.58	14-Aug-22	18-Aug-22
P07-EF	Manufacturing / Fabrication / Supply	35	0%	$3,113.13	19-Aug-22	22-Sep-22
P07-EF	Final Inspection	7	0%	$622.63	23-Sep-22	29-Sep-22
P07-EF	Delivery On Site	7	0%	$1,245.25	30-Sep-22	06-Oct-22

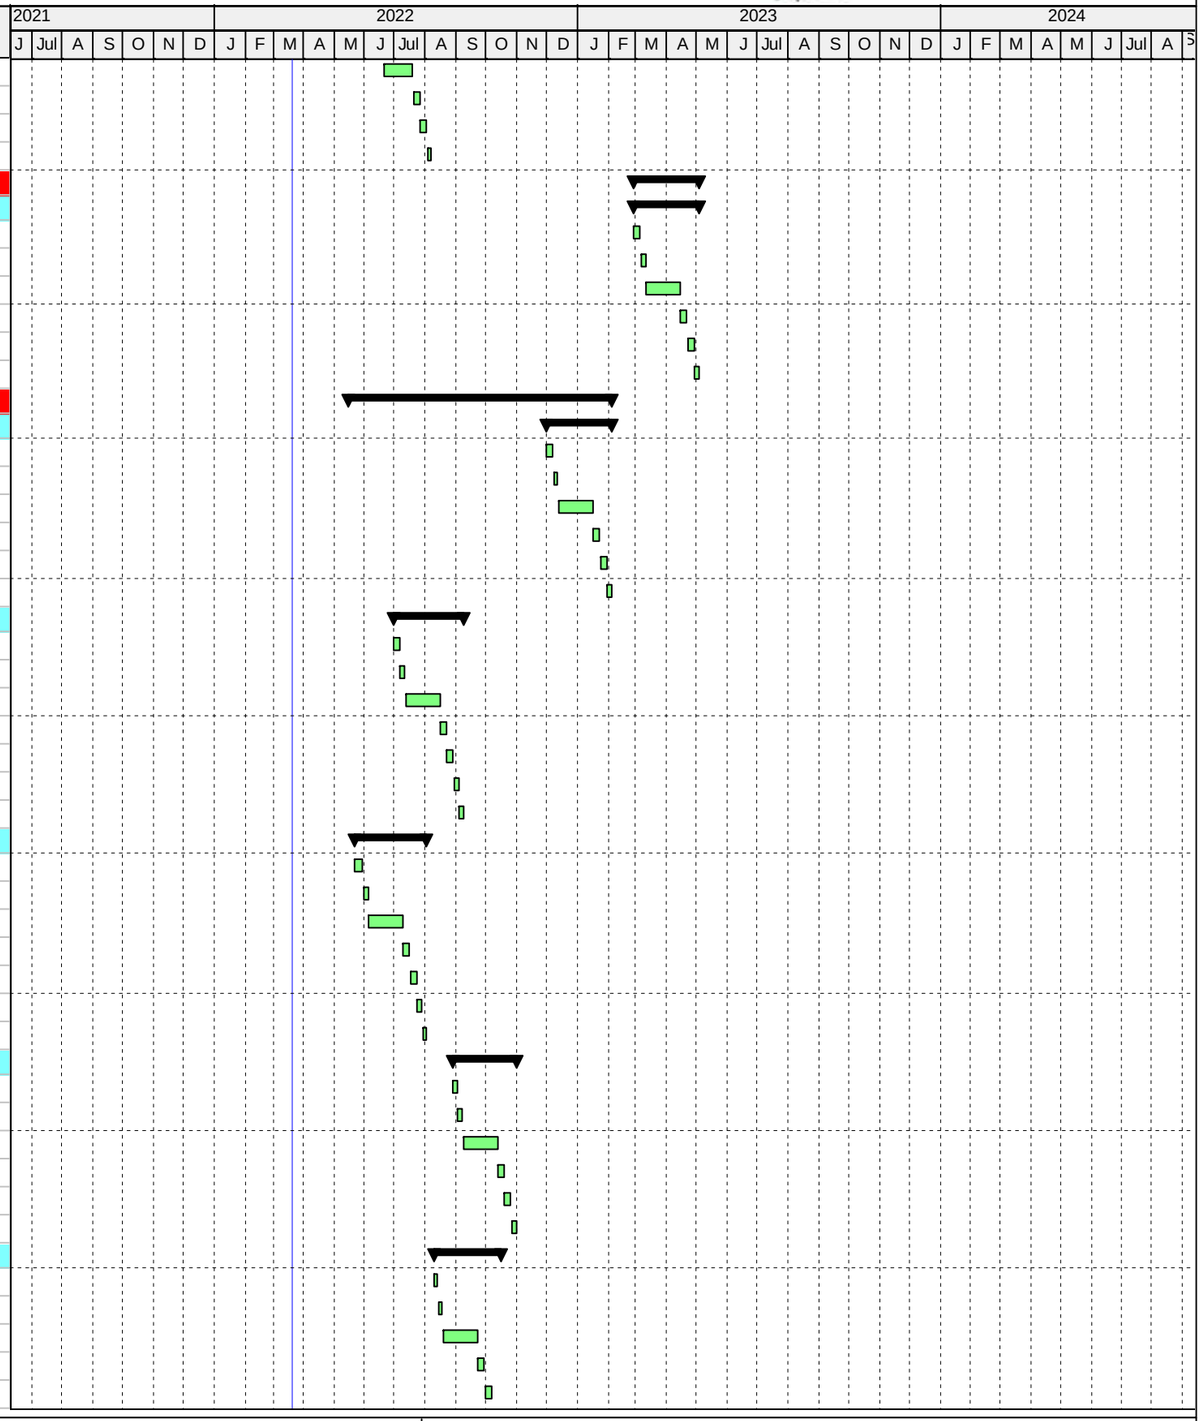


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P07-EI	Submitting Vendor Data Book	5	0%	$311.31	07-Oct-22	11-Oct-22
P07-EI	Delivering Spare Parts	5	0%	$311.31	12-Oct-22	16-Oct-22
Capacitor Bank - BK14		69	0%	$5,206.91	16-May-22	23-Jul-22
P07-EI	Tendering & Selection	5	0%	$208.28	16-May-22	20-May-22
P07-EI	Contract Effectiveness / PO	5	0%	$312.41	21-May-22	25-May-22
P07-EI	Manufacturing / Fabrication / Supply	35	0%	$2,603.46	26-May-22	29-Jun-22
P07-EI	Final Inspection	7	0%	$520.69	30-Jun-22	06-Jul-22
P07-EI	Delivery On Site	7	0%	$1,041.38	07-Jul-22	13-Jul-22
P07-EI	Submitting Vendor Data Book	5	0%	$260.35	14-Jul-22	18-Jul-22
P07-EI	Delivering Spare Parts	5	0%	$260.35	19-Jul-22	23-Jul-22
Emergency Diesel Generator - BK14		69	0%	$26,833.51	16-May-22	23-Jul-22
P07-EI	Tendering & Selection	5	0%	$1,073.34	16-May-22	20-May-22
P07-EI	Contract Effectiveness / PO	5	0%	$1,610.01	21-May-22	25-May-22
P07-EI	Manufacturing / Fabrication / Supply	35	0%	$13,416.75	26-May-22	29-Jun-22
P07-EI	Final Inspection	7	0%	$2,683.35	30-Jun-22	06-Jul-22
P07-EI	Delivery On Site	7	0%	$5,366.70	07-Jul-22	13-Jul-22
P07-EI	Submitting Vendor Data Book	5	0%	$1,341.68	14-Jul-22	18-Jul-22
P07-EI	Delivering Spare Parts	5	0%	$1,341.68	19-Jul-22	23-Jul-22
UPS System - BK14		69	0%	$16,612.53	19-Aug-22	26-Oct-22
P07-EI	Tendering & Selection	5	0%	$664.50	19-Aug-22	23-Aug-22
P07-EI	Contract Effectiveness / PO	5	0%	$996.75	24-Aug-22	28-Aug-22
P07-EI	Manufacturing / Fabrication / Supply	35	0%	$8,306.27	29-Aug-22	02-Oct-22
P07-EI	Final Inspection	7	0%	$1,661.25	03-Oct-22	09-Oct-22
P07-EI	Delivery On Site	7	0%	$3,322.51	10-Oct-22	16-Oct-22
P07-EI	Submitting Vendor Data Book	5	0%	$830.63	17-Oct-22	21-Oct-22
P07-EI	Delivering Spare Parts	5	0%	$830.63	22-Oct-22	26-Oct-22
Transformers - BK14		69	0%	$30,359.88	26-May-22	02-Aug-22
P07-EI	Tendering & Selection	5	0%	$1,214.40	26-May-22	30-May-22
P07-EI	Contract Effectiveness / PO	5	0%	$1,821.59	31-May-22	04-Jun-22
P07-EI	Manufacturing / Fabrication / Supply	35	0%	$15,179.94	05-Jun-22	09-Jul-22
P07-EI	Final Inspection	7	0%	$3,035.99	10-Jul-22	16-Jul-22
P07-EI	Delivery On Site	7	0%	$6,071.98	17-Jul-22	23-Jul-22
P07-EI	Submitting Vendor Data Book	5	0%	$1,517.99	24-Jul-22	28-Jul-22
P07-EI	Delivering Spare Parts	5	0%	$1,517.99	29-Jul-22	02-Aug-22
Earthing & Lightning System - BK14		59	0%	$10,110.78	17-Jul-22	13-Sep-22
P07-EI	Tendering & Selection	5	0%	$404.43	17-Jul-22	21-Jul-22
P07-EI	Contract Effectiveness / PO	5	0%	$606.65	22-Jul-22	26-Jul-22
P07-EI	Manufacturing / Fabrication / Supply	25	0%	$5,055.39	27-Jul-22	20-Aug-22
P07-EI	Final Inspection	7	0%	$1,011.08	21-Aug-22	27-Aug-22
P07-EI	Delivery On Site	7	0%	$2,022.16	28-Aug-22	03-Sep-22
P07-EI	Submitting Vendor Data Book	5	0%	$505.54	04-Sep-22	08-Sep-22
P07-EI	Delivering Spare Parts	5	0%	$505.54	09-Sep-22	13-Sep-22
LV Switchgear & MCC - BK14		64	0%	$26,199.86	26-May-22	28-Jul-22
P07-EI	Tendering & Selection	5	0%	$1,047.99	26-May-22	30-May-22
P07-EI	Contract Effectiveness / PO	5	0%	$1,571.99	31-May-22	04-Jun-22
P07-EI	Manufacturing / Fabrication / Supply	30	0%	$13,099.93	05-Jun-22	04-Jul-22
P07-EI	Final Inspection	7	0%	$2,619.99	05-Jul-22	11-Jul-22
P07-EI	Delivery On Site	7	0%	$5,239.97	12-Jul-22	18-Jul-22
P07-EI	Submitting Vendor Data Book	5	0%	$1,309.99	19-Jul-22	23-Jul-22

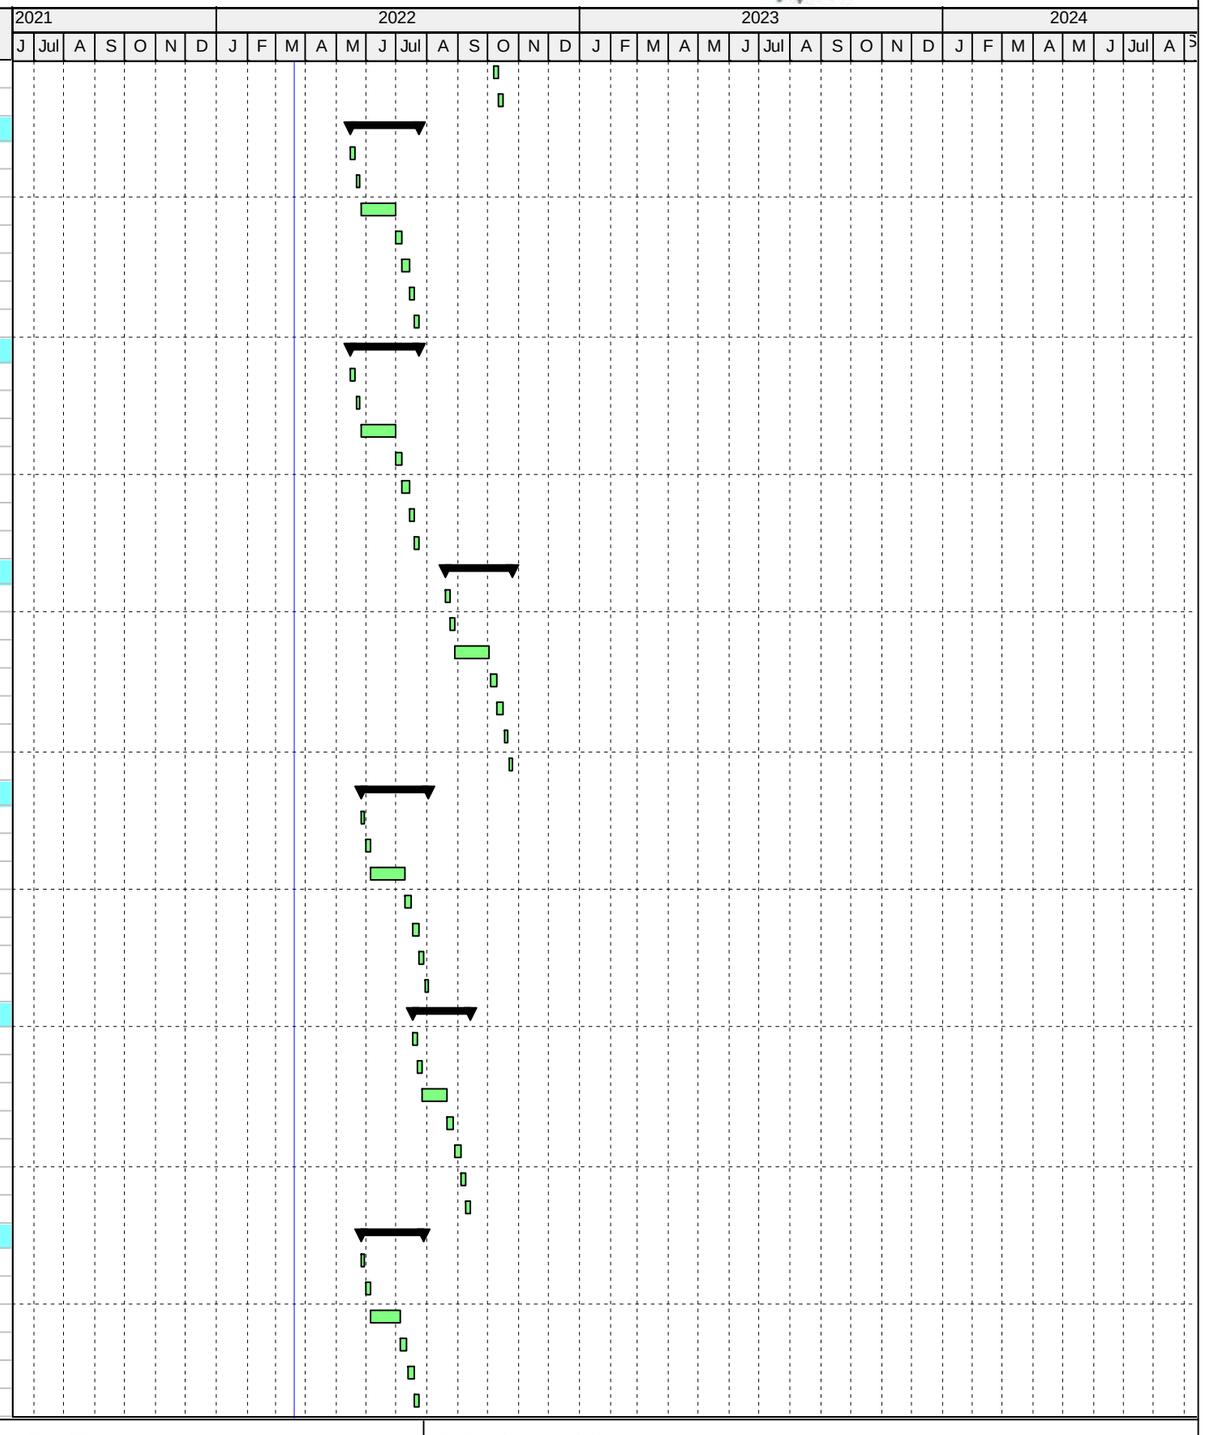


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P07-EI	Delivering Spare Parts	5	0%	$1,309.99	24-Jul-22	28-Jul-22
Transmission Over head Line - BK14		57	0%	$104,193.36	11-Aug-22	06-Oct-22
P07-EI	Tendering & Selection	5	0%	$4,167.73	11-Aug-22	15-Aug-22
P07-EI	Contract Effectiveness / PO	5	0%	$6,251.60	16-Aug-22	20-Aug-22
P07-EI	Manufacturing / Fabrication / Supply	30	0%	$52,096.68	21-Aug-22	19-Sep-22
P07-EI	Final Inspection	7	0%	$10,419.34	20-Sep-22	26-Sep-22
P07-EI	Delivery On Site	5	0%	$26,048.34	27-Sep-22	01-Oct-22
P07-EI	Submitting Vendor Data Book	5	0%	$5,209.67	02-Oct-22	06-Oct-22
Power & Control Cables - BK14		54	0%	$15,317.69	12-Nov-22	04-Jan-23
P07-EI	Tendering & Selection	5	0%	$612.71	12-Nov-22	16-Nov-22
P07-EI	Contract Effectiveness / PO	5	0%	$919.06	17-Nov-22	21-Nov-22
P07-EI	Manufacturing / Fabrication / Supply	25	0%	$7,658.85	22-Nov-22	16-Dec-22
P07-EI	Final Inspection	7	0%	$1,531.77	17-Dec-22	23-Dec-22
P07-EI	Delivery On Site	7	0%	$3,829.42	24-Dec-22	30-Dec-22
P07-EI	Submitting Vendor Data Book	5	0%	$765.88	31-Dec-22	04-Jan-23
Construction		436	0%	$162,772.00	24-Jun-22	02-Sep-23
Wellpad and Access Road		60	0%	$48,831.60	24-Jun-22	22-Aug-22
Access Road		39	0%	$19,532.64	24-Jun-22	01-Aug-22
Access Road		39	0%	$17,579.38	24-Jun-22	01-Aug-22
P07-E	Access Road Preparation	5	0%	$10,547.63	24-Jun-22	28-Jun-22
P07-E	Filling and Compaction	10	0%	$878.97	08-Jul-22	17-Jul-22
P07-E	Sub-Base Layer	15	0%	$1,757.94	18-Jul-22	01-Aug-22
Retaining wall		17	0%	$3,515.88	29-Jun-22	15-Jul-22
P07-	Excavation	5	0%	$351.59	29-Jun-22	03-Jul-22
P07-	lean concrete	2	0%	$527.38	04-Jul-22	05-Jul-22
P07-	form working	5	0%	$1,230.56	06-Jul-22	10-Jul-22
P07-	concrete pouring	5	0%	$1,406.35	11-Jul-22	15-Jul-22
Construction of Culvert and Bridge		34	0%	$878.97	29-Jun-22	01-Aug-22
bridge		34	0%	$351.59	29-Jun-22	01-Aug-22
P07	Excavation	5	0%	$35.16	29-Jun-22	03-Jul-22
P07	lean concrete	2	0%	$28.13	04-Jul-22	05-Jul-22
P07	wall	5	0%	$63.29	06-Jul-22	10-Jul-22
P07	reinforcement	5	0%	$70.32	11-Jul-22	15-Jul-22
P07	form working	5	0%	$35.16	16-Jul-22	20-Jul-22
P07	concrete pouring	5	0%	$105.48	21-Jul-22	25-Jul-22
P07	protect stone	2	0%	$7.03	26-Jul-22	27-Jul-22
P07	Backfill	5	0%	$7.03	28-Jul-22	01-Aug-22
culverts		9	0%	$527.38	29-Jun-22	07-Jul-22
P07	pipeway culvert	5	0%	$210.95	29-Jun-22	03-Jul-22
P07	pipeway	2	0%	$158.21	04-Jul-22	05-Jul-22
P07	pipeline culvert	2	0%	$158.21	06-Jul-22	07-Jul-22
Burn Pit Access Road		25	0%	$1,953.26	29-Jun-22	23-Jul-22
P07-E	ROW Preparation	10	0%	$1,074.30	29-Jun-22	08-Jul-22
P07-E	Filling and Compaction	10	0%	$390.65	09-Jul-22	18-Jul-22
P07-E	Sub-Base Layer	5	0%	$488.32	19-Jul-22	23-Jul-22
Wellpad		60	0%	$29,298.96	24-Jun-22	22-Aug-22
Site Preparation		10	0%	$4,394.84	29-Jun-22	08-Jul-22
P07-E	Site Preparation #14	10	0%	$4,394.84	29-Jun-22	08-Jul-22
Civil Work		10	0%	$7,617.73	09-Jul-22	18-Jul-22

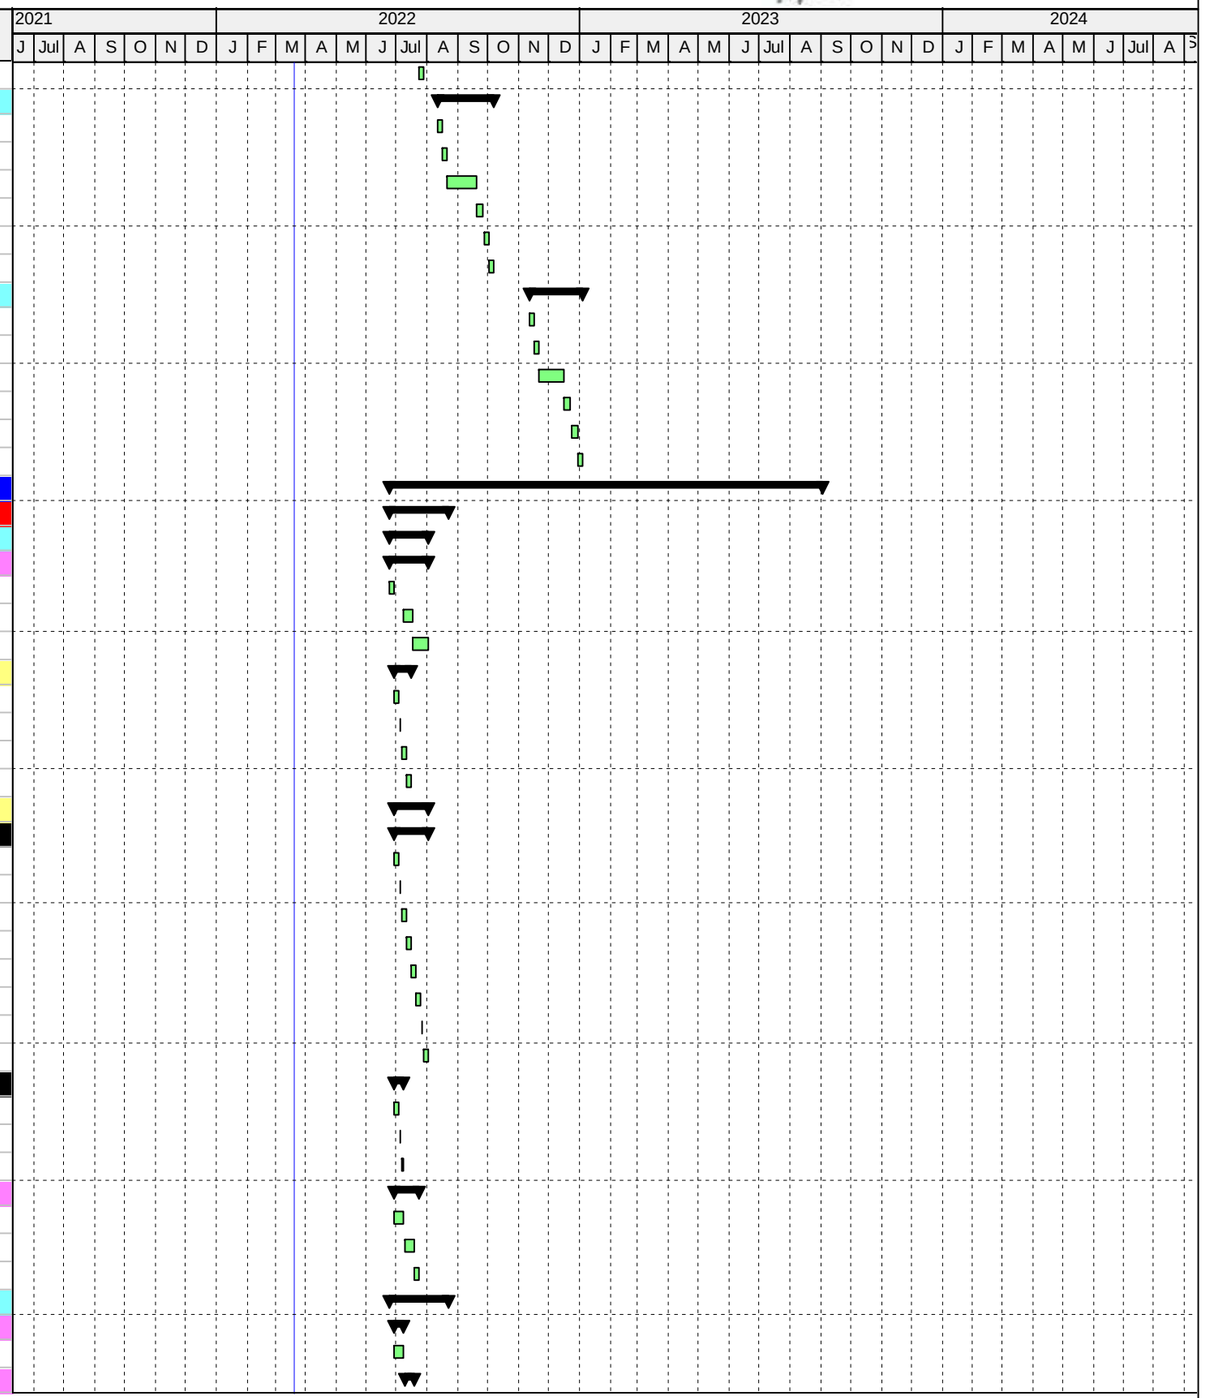


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P07-E	Excavation and Soil Removal (Cellar)	3	0%	$4,951.52	09-Jul-22	11-Jul-22
P07-E	Installation of Conductor Pipe	5	0%	$380.89	12-Jul-22	16-Jul-22
P07-E	Form Work (Above Cellar)	5	0%	$380.89	12-Jul-22	16-Jul-22
P07-E	Armed Concrete	2	0%	$1,904.43	17-Jul-22	18-Jul-22
Burn Pit		35	0%	$1,171.96	19-Jul-22	22-Aug-22
P07-E	Soil Removal, Triming ,Filling and Compaction of Burn Pit Are	10	0%	$937.57	19-Jul-22	28-Jul-22
P07-E	Construction & Installation of Support	15	0%	$58.60	29-Jul-22	12-Aug-22
P07-E	Welding, Installation and Testing	10	0%	$175.79	13-Aug-22	22-Aug-22
Surface Preparation		5	0%	$878.97	09-Jul-22	13-Jul-22
P07-E	Gravel Paving	5	0%	$878.97	09-Jul-22	13-Jul-22
Mud Channel		5	0%	$878.97	09-Jul-22	13-Jul-22
P07-E	Excavation & Repair	5	0%	$878.97	09-Jul-22	13-Jul-22
Mud Pit		12	0%	$4,394.84	11-Jul-22	23-Jul-22
P07-E	Soil Removal, Filling and Compaction of Mud Pit Area	7	0%	$1,538.20	12-Jul-22	18-Jul-22
P07-E	Construction of Mud Pit's Walls	5	0%	$878.97	11-Jul-22	16-Jul-22
P07-E	Supply & Installation sealling Layer	7	0%	$1,977.68	16-Jul-22	23-Jul-22
SepticTank		16	0%	$2,050.93	12-Jul-22	27-Jul-22
P07-E	Excavation & Soil Transfer	4	0%	$615.28	12-Jul-22	15-Jul-22
P07-E	Levelling	2	0%	$10.25	16-Jul-22	17-Jul-22
P07-E	Tank Supply	7	0%	$1,169.03	12-Jul-22	18-Jul-22
P07-E	Tank Execution	3	0%	$194.84	19-Jul-22	21-Jul-22
P07-E	Backfilling & Compaction	6	0%	$61.53	22-Jul-22	27-Jul-22
Gasoil Pad		12	0%	$1,464.95	09-Jul-22	20-Jul-22
P07-E	Excavation	3	0%	$292.99	09-Jul-22	11-Jul-22
P07-E	lean concrete	2	0%	$439.48	11-Jul-22	13-Jul-22
P07-E	Form work	5	0%	$146.49	13-Jul-22	18-Jul-22
P07-E	Armed Concrete	2	0%	$585.98	18-Jul-22	20-Jul-22
Demolition & Disassemble		7	0%	$4,394.84	09-Jul-22	15-Jul-22
P07-E	Demolition of concrete support	3	0%	$1,318.45	09-Jul-22	11-Jul-22
P07-E	Fence Disassmble	4	0%	$3,076.39	12-Jul-22	15-Jul-22
Water Supply		15	0%	$2,050.93	24-Jun-22	08-Jul-22
P07-E	Water Supply	15	0%	$2,050.93	24-Jun-22	08-Jul-22
Wellhead Facility and Flowline		247	0%	$111,498.82	04-Oct-22	07-Jun-23
Civil, Structure & Architecture		212	0%	$39,024.59	04-Oct-22	03-May-23
Civil Works		28	0%	$10,926.88	04-Oct-22	31-Oct-22
P07-E	Steel Works(Wellhead Facilities)	5	0%	$4,917.10	04-Oct-22	08-Oct-22
P07-E	Out Door Post Works For New Gantry (Fundation, Fencing ..	5	0%	$2,731.72	27-Oct-22	31-Oct-22
P07-E	Out Door Post Works For Wellhead Post (Fundation, Fencing	5	0%	$2,731.72	17-Oct-22	21-Oct-22
P07-E	Well Pad Fencing	5	0%	$546.34	22-Oct-22	26-Oct-22
Buildings		194	0%	$21,853.77	22-Oct-22	03-May-23
Construction of Guard House		191	0%	$6,119.06	22-Oct-22	30-Apr-23
Foundation		55	0%	$1,896.91	22-Oct-22	15-Dec-22
P07	Excavation & Soil Transfer (Removing of Vegetal Soil)	2	0%	$379.38	22-Oct-22	23-Oct-22
P07	Levelling	30	0%	$37.94	24-Oct-22	22-Nov-22
P07	Lean Concrete	2	0%	$189.69	23-Nov-22	24-Nov-22
P07	Reinforced Work	3	0%	$379.38	25-Nov-22	27-Nov-22
P07	Formwork	7	0%	$151.75	28-Nov-22	04-Dec-22
P07	Main Concrete Pouring	5	0%	$739.79	05-Dec-22	09-Dec-22
P07	Backfilling & Compaction	6	0%	$18.97	10-Dec-22	15-Dec-22
Structure		17	0%	$2,447.62	16-Dec-22	01-Jan-23

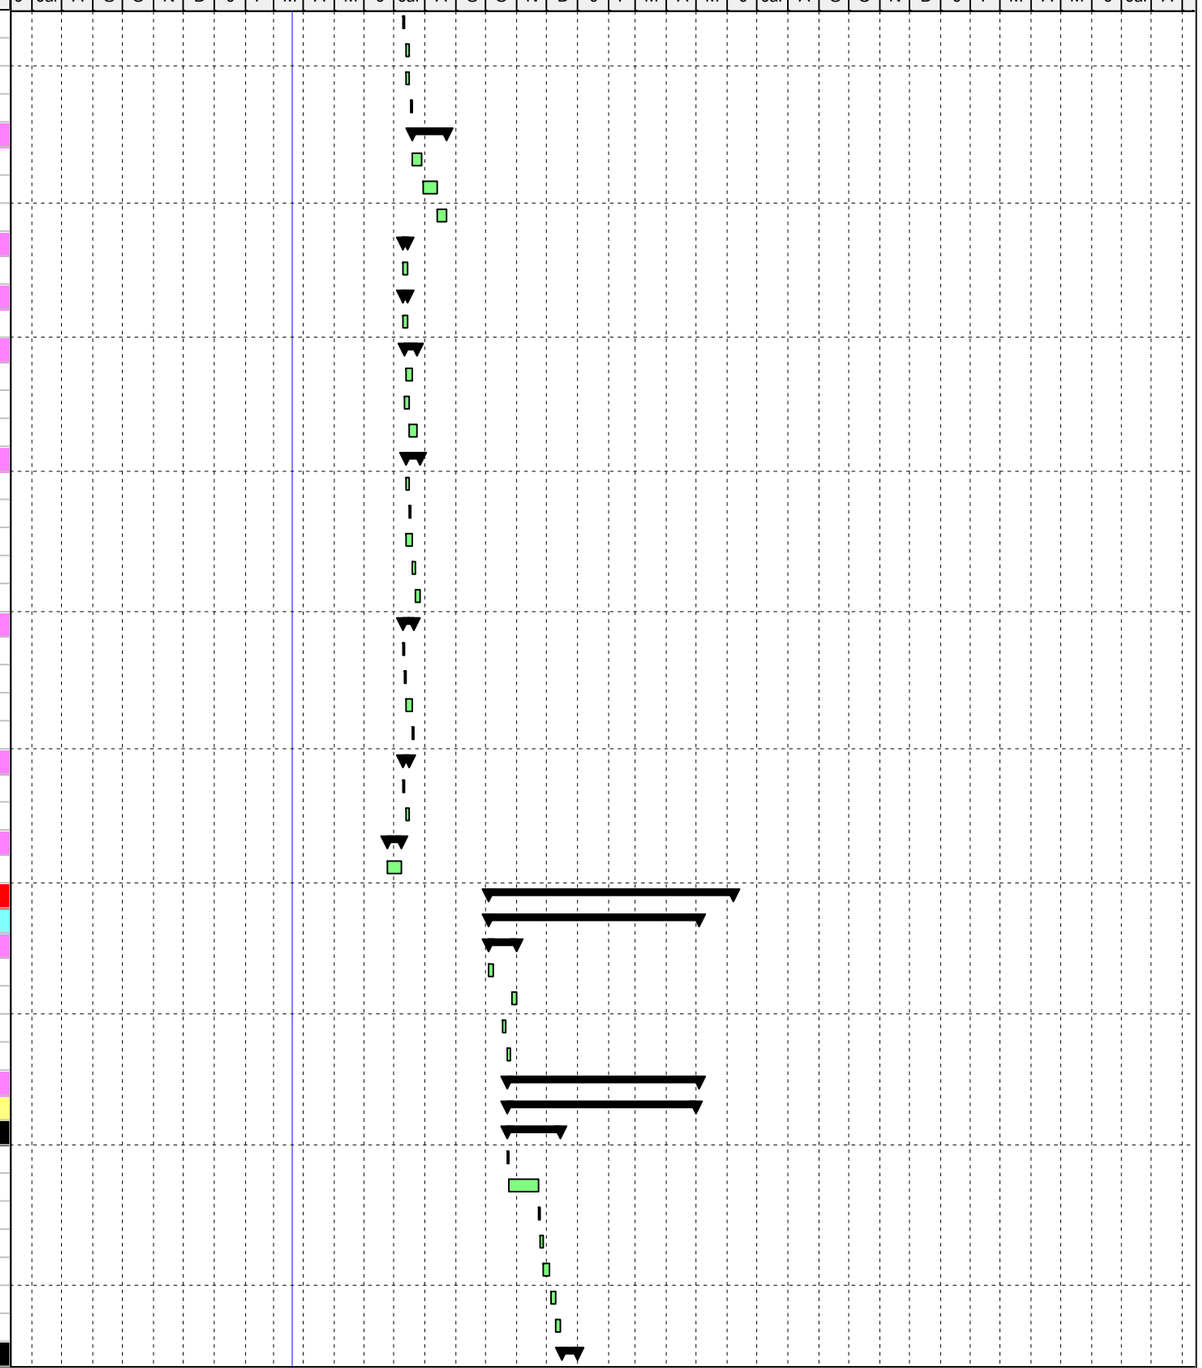


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P07	Steel Material Supply	5	0%	$1,223.81	16-Dec-22	20-Dec-22
P07	Shop Fabrication of Steel Structure	5	0%	$489.52	21-Dec-22	25-Dec-22
P07	Structural Installation	5	0%	$489.52	26-Dec-22	30-Dec-22
P07	Structural Painting	2	0%	$244.76	31-Dec-22	01-Jan-23
Architectural		115	0%	$1,774.53	06-Jan-23	30-Apr-23
P07	Wall Execution	2	0%	$867.21	06-Jan-23	07-Jan-23
P07	Roof Covering	2	0%	$211.17	08-Jan-23	09-Jan-23
P07	Roof Execution (Block Joist, Concrete Pouring)	2	0%	$269.37	10-Jan-23	11-Jan-23
P07	Building Walkway (around Building)	3	0%	$91.21	12-Jan-23	14-Jan-23
P07	Joinery (Cornice, Faï?½ade, Plaster)	2	0%	$335.56	29-Apr-23	30-Apr-23
Construction of Switchgear		194	0%	$15,734.71	22-Oct-22	03-May-23
Foundation		30	0%	$4,877.76	22-Oct-22	20-Nov-22
P07	Excavation & Soil Transfer (Removing of Vegetal Soil)	2	0%	$975.55	22-Oct-22	23-Oct-22
P07	Levelling	5	0%	$97.56	24-Oct-22	28-Oct-22
P07	Lean Concrete	2	0%	$487.78	29-Oct-22	30-Oct-22
P07	Reinforced Work	7	0%	$975.55	31-Oct-22	06-Nov-22
P07	Formwork	3	0%	$390.22	07-Nov-22	09-Nov-22
P07	Main Concrete Pouring	5	0%	$1,902.33	10-Nov-22	14-Nov-22
P07	Backfilling & Compaction	6	0%	$48.78	15-Nov-22	20-Nov-22
Structure		15	0%	$6,293.89	19-Nov-22	03-Dec-22
P07	Steel Material Supply	4	0%	$3,146.94	19-Nov-22	22-Nov-22
P07	Shop Fabrication of Steel Structure	4	0%	$1,258.78	23-Nov-22	26-Nov-22
P07	Structural Installation	4	0%	$1,258.78	27-Nov-22	30-Nov-22
P07	Structural Painting	3	0%	$629.39	01-Dec-22	03-Dec-22
Architectural		151	0%	$4,563.07	04-Dec-22	03-May-23
P07	Wall Execution	5	0%	$2,229.97	04-Dec-22	08-Dec-22
P07	Roof Covering	3	0%	$543.00	09-Dec-22	11-Dec-22
P07	Roof Execution (Block Joist, Concrete Pouring)	2	0%	$692.67	12-Dec-22	13-Dec-22
P07	Building Walkway (around Building)	5	0%	$234.54	14-Dec-22	18-Dec-22
P07	Joinery (Cornice, Faï?½ade, Plaster)	5	0%	$862.88	29-Apr-23	03-May-23
Shelters		9	0%	$6,243.93	22-Oct-22	30-Oct-22
Fire Fighting Shelter		9	0%	$5,120.03	22-Oct-22	30-Oct-22
P07-	Fabrication	5	0%	$3,584.02	22-Oct-22	26-Oct-22
P07-	Installation	4	0%	$1,536.01	27-Oct-22	30-Oct-22
Diesel Generator Shelter		9	0%	$1,123.91	22-Oct-22	30-Oct-22
P07-	Fabrication	5	0%	$786.74	22-Oct-22	26-Oct-22
P07-	Installation	4	0%	$337.17	27-Oct-22	30-Oct-22
Mechanical		7	0%	$11,149.88	27-Oct-22	02-Nov-22
P07-EI	Fuel Oil Storage Drum	7	0%	$5,574.94	27-Oct-22	02-Nov-22
P07-EI	Potable Water Tank	7	0%	$5,574.94	27-Oct-22	02-Nov-22
Piping		17	0%	$11,149.88	19-Oct-22	04-Nov-22
P07-EI	Sweep Bend Installation	5	0%	$557.49	19-Oct-22	23-Oct-22
P07-EI	Piping Work (Fit up, Welding, NDT…)	7	0%	$4,459.95	24-Oct-22	30-Oct-22
P07-EI	Valves, Fitting and Spools Installation and Hydrotest	5	0%	$6,132.44	31-Oct-22	04-Nov-22
Instrument Works		5	0%	$0.00	04-May-23	08-May-23
P07-EI	Devices Installation and Piping Connecton	5	0%	$0.00	04-May-23	08-May-23
Electrical		198	0%	$47,944.49	23-Oct-22	08-May-23
P07-EI	Over Head line	10	0%	$34,040.59	31-Dec-22	09-Jan-23
P07-EI	Wellhead Electrical Equipment	5	0%	$3,835.56	04-May-23	08-May-23

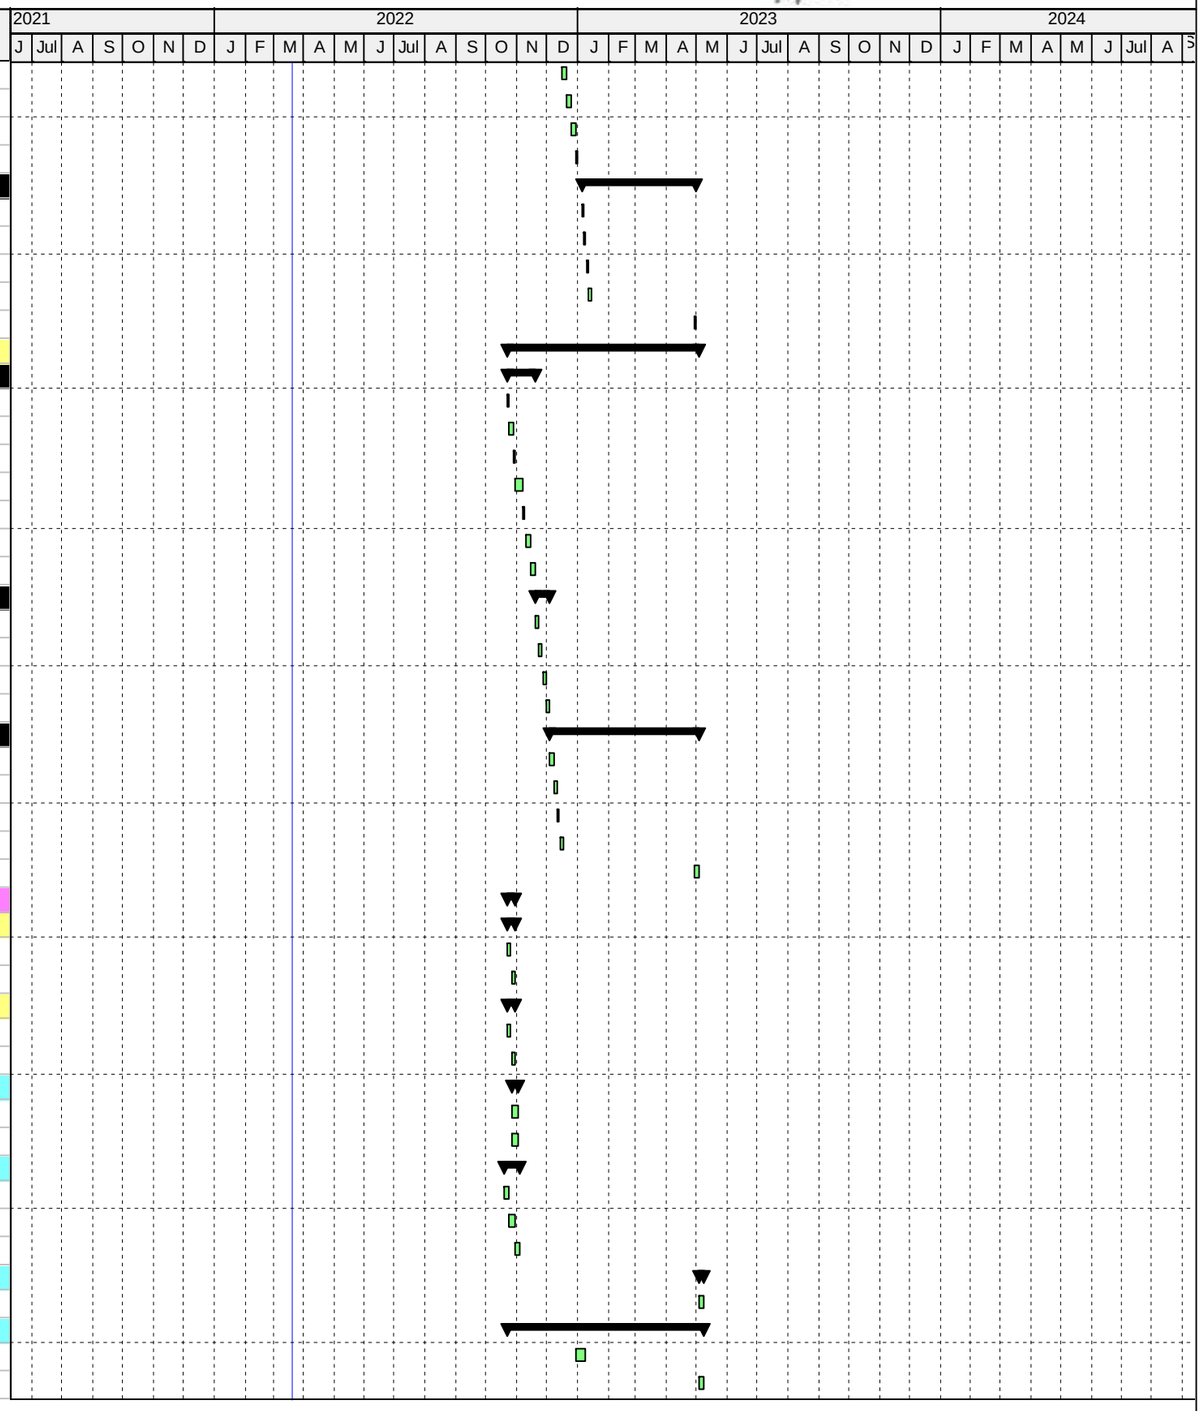


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P07-EF	Dismantling of existing Gantry	7	0%	$2,397.22	31-Jan-23	06-Feb-23
P07-EF	Outdoor Post (new Gantry)	7	0%	$3,835.56	14-Nov-22	20-Nov-22
P07-EF	Outdoor Post (Wellhead Post)	7	0%	$3,835.56	23-Oct-22	29-Oct-22
Pre-commissioning		10	0%	$2,229.98	29-May-23	07-Jun-23
P07-EF	Pre-commissioning	5	0%	$2,006.98	29-May-23	02-Jun-23
P07-EF	Ready for Comm.Certificate(RFCC)	5	0%	$223.00	03-Jun-23	07-Jun-23
Job Site HSE Supervision (Surface)		125	0%	$325.54	24-Jun-22	26-Oct-22
P07-EP	Job Site HSE Supervision (Surface)	125	0%	$325.54	24-Jun-22	26-Oct-22
Commissioning, Startup & Handover		87	0%	$2,116.04	08-Jun-23	02-Sep-23
Commissioning		32	0%	$634.81	08-Jun-23	09-Jul-23
P07-EF	Materials & Utilities Ready for Commissioning	3	0%	$31.74	08-Jun-23	10-Jun-23
P07-EF	Receiving Facilities Ready for Commissioning	2	0%	$31.74	11-Jun-23	12-Jun-23
P07-EF	Permits Obtained for Commissioning	10	0%	$31.74	13-Jun-23	22-Jun-23
P07-EF	Integrated Commissioning	2	0%	$507.85	23-Jun-23	24-Jun-23
P07-EF	Ready for Startup Certificate (RFSU)	15	0%	$31.74	25-Jun-23	09-Jul-23
Startup & Performance Test		18	0%	$846.41	10-Jul-23	27-Jul-23
P07-EF	Startup & Performance Test Run	3	0%	$677.13	10-Jul-23	12-Jul-23
P07-EF	Start of Production (SOP)	15	0%	$169.28	13-Jul-23	27-Jul-23
Handover		37	0%	$634.81	28-Jul-23	02-Sep-23
P07-EF	Compiling & Submitting Final Documentation	20	0%	$190.44	28-Jul-23	16-Aug-23
P07-EF	Training of Operator's Personnel	2	0%	$253.92	17-Aug-23	18-Aug-23
P07-EF	Provisional Acceptance Certificate (PAC)	15	0%	$190.44	19-Aug-23	02-Sep-23
Package 08-Workover # 12		513	0.67%	$408,986.00	24-Jul-21 A	14-Aug-23
ENGINEERING		439	20.43%	$13,382.00	24-Jul-21 A	23-May-23
Basic Design Endorsement		30	100%	$669.10	31-Jul-21 A	20-Mar-22
P08-EP	Endorsement Report For Basic Design & Scope of Work	30	100%	$669.10	31-Jul-21 A	20-Mar-22
Value Engineering		44	60%	$401.46	01-Feb-22	20-Mar-22
P08-EP	Value Engineering Study Report	44	60%	$401.46	01-Feb-22	20-Mar-22
Detail Design		439	24.77%	$7,360.10	24-Jul-21 A	14-Jan-23
Process		88	65%	$350.34	15-Nov-21	10-Jun-22
Drawing/Diagram		44	80%	$245.24	15-Nov-21	02-May-22
P08-E	P&ID for Diesel Oil Drum- BK12	44	80%	$122.62	15-Nov-21	02-May-22
P08-E	P&ID for Potable Water Tank - BK12	44	80%	$122.62	15-Nov-21	02-May-22
List		44	60%	$52.55	27-Feb-22	02-May-22
P08-E	Line List - BK12	44	60%	$52.55	27-Feb-22	02-May-22
Data Sheet		39	0%	$52.55	03-May-22	10-Jun-22
P08-E	Process Data Sheets For Instrument Devices - BK12	39	0%	$17.87	03-May-22	10-Jun-22
P08-E	Process Data Sheets For Fuel Oil Storage Drum of Well Pads	25	0%	$17.34	04-May-22	28-May-22
P08-E	Process Data Sheets For Potable Water Tank of Well Pads	25	0%	$17.34	09-May-22	02-Jun-22
Mechanical		99	77.78%	$490.92	28-Jul-21 A	26-Jun-22
Basis/Criteria		54	60%	$54.54	28-Jul-21 A	12-May-22
P08-E	Mechanical Design Criteria	54	60%	$54.54	28-Jul-21 A	12-May-22
Specification		79	60%	$81.84	28-Jul-21 A	26-Jun-22
P08-E	Specification For Pressure Vessels	54	60%	$40.92	28-Jul-21 A	12-May-22
P08-E	Specification For Atmospheric Above Ground Welded Steel T	79	60%	$40.92	28-Jul-21 A	26-Jun-22
Data Sheets		35	60%	$136.38	16-Jan-22	08-May-22
P08-E	Data Sheets For Fuel Oil Storage Drum of Well Pads	25	60%	$68.19	16-Jan-22	03-May-22
P08-E	Data Sheets For Potable Water Tank of Well Pads	25	60%	$68.19	09-Feb-22	08-May-22
Drawing/Diagram		34	100%	$218.16	28-Jul-21 A	09-Apr-22
P08-E	Standard Detail Drawing For Pressure Vessels and Heat Excl	14	100%	$109.08	28-Jul-21 A	09-Apr-22

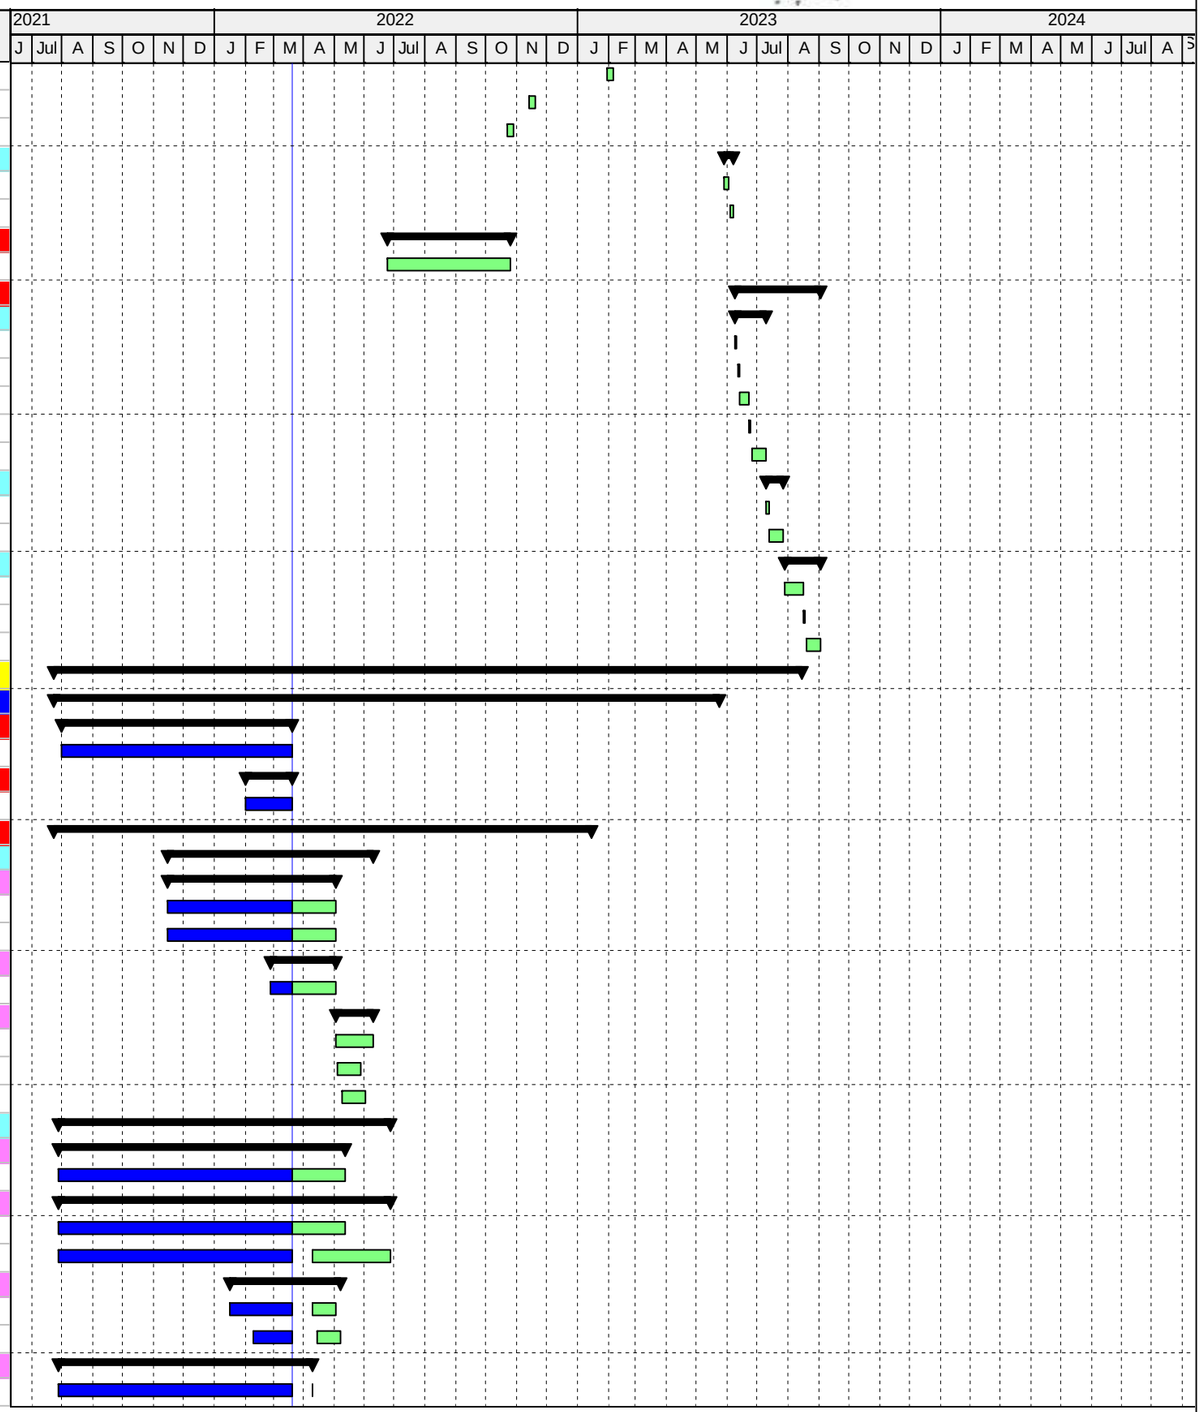


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P08-E	Standard Detail Drawing For Storage Tanks	14	100%	$109.08	28-Jul-21 A	09-Apr-22
HVAC/Plumbing		402	5.17%	$420.26	24-Jul-21 A	14-Jan-23
Basis/Criteria		64	100%	$6.09	24-Jul-21 A	14-May-22
P08-E	HVAC & Plumbing Design Criteria	64	100%	$6.09	24-Jul-21 A	14-May-22
Specification		64	100%	$9.75	24-Jul-21 A	27-Mar-22
P08-E	Specification For HVAC Equipment	64	100%	$6.09	24-Jul-21 A	27-Mar-22
P08-E	Specification For Duct Work & Pipe Work	64	100%	$3.66	24-Jul-21 A	27-Mar-22
Calculation		173	0%	$97.46	13-May-22	01-Nov-22
P08-E	HVAC Calculation Note For Switchgear Building - BK12	44	0%	$48.73	13-May-22	25-Jun-22
P08-E	HVAC Calculation Note For Security Building - BK12	44	0%	$48.73	19-Sep-22	01-Nov-22
Drawing/Diagram		247	2.82%	$209.54	24-Jul-21 A	31-Dec-22
P08-E	Standard Drawing For HVAC & Plumbing	14	100%	$4.67	24-Jul-21 A	30-Mar-22
P08-E	Symbol & Legend For HVAC & Plumbing	35	60%	$2.03	22-Aug-21	03-May-22
P08-E	HVAC System Layout For Switchgear Building - BK12	30	0%	$50.71	26-Jun-22	25-Jul-22
P08-E	HVAC System Layout For Security Building - BK12	30	0%	$50.71	02-Nov-22	01-Dec-22
P08-E	Plumbing & Sewage Piping Layout For Switchgear Building - I	30	0%	$50.71	26-Jul-22	24-Aug-22
P08-E	Plumbing & Sewage Piping Layout For Security Building - Bk	30	0%	$50.71	02-Dec-22	31-Dec-22
Data Sheets		44	0%	$48.71	02-Dec-22	14-Jan-23
P08-E	Data Sheets For Main HVAC Equipment - BK12	44	0%	$48.71	02-Dec-22	14-Jan-23
MTO		7	0%	$48.71	01-Jan-23	07-Jan-23
P08-E	MTO For Building HVAC & Plumbing Systems - BK12	7	0%	$48.71	01-Jan-23	07-Jan-23
Piping		49	59.5%	$350.34	24-Jul-21 A	09-May-22
Basis/Criteria		39	100%	$7.01	24-Jul-21 A	20-Mar-22
P08-E	Piping Design Criteria	39	100%	$7.01	24-Jul-21 A	20-Mar-22
Specification		49	72.38%	$133.13	24-Jul-21 A	04-May-22
P08-E	Specification For Color Coding and Marking	39	60%	$9.71	09-Aug-21	01-May-22
P08-E	Specification For Transportation, Handling, Storage of pipes	39	80%	$10.58	12-Dec-21	01-May-22
P08-E	Specification For the Design of Piping in Mechanical Packages	40	60%	$9.71	09-Aug-21	28-Apr-22
P08-E	Specification For Metallic Pipes	39	80%	$9.71	24-Jul-21 A	01-May-22
P08-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$9.71	24-Jul-21 A	24-Mar-22
P08-E	Specification For Painting	39	100%	$11.65	24-Jul-21 A	27-Mar-22
P08-E	Specification For Lining (Internal Protection of Equipment by F	39	60%	$9.71	09-Aug-21	04-May-22
P08-E	Specification For Material Requirements in Sour service	39	60%	$9.71	09-Aug-21	04-May-22
P08-E	Specification For Manual Valves	39	60%	$9.71	09-Aug-21	04-May-22
P08-E	Specification For Plant Piping Systems Pressure Testing	39	60%	$9.71	09-Aug-21	04-May-22
P08-E	Specification For Welding of Plant Piping System	39	60%	$10.58	09-Aug-21	04-May-22
P08-E	Specification For Flexibility Analysis	39	60%	$12.97	09-Aug-21	04-May-22
P08-E	Specification For Piping Cleaning and Flushing	39	100%	$9.71	24-Aug-21	30-Mar-22
Drawing/Diagram		14	100%	$105.10	19-Feb-22	20-Mar-22
P08-E	Standard Pipe Support Drawings	14	100%	$105.10	19-Feb-22	20-Mar-22
MTO		7	0%	$105.10	03-May-22	09-May-22
P08-E	MTO For Pipes - BK12	7	0%	$105.10	03-May-22	09-May-22
Electrical		223	27.05%	$1,780.41	24-Jul-21 A	25-Nov-22
Basis/Criteria		54	100%	$10.15	03-Aug-21	20-Mar-22
P08-E	Electrical System Design Criteria	54	100%	$10.15	03-Aug-21	20-Mar-22
Specification		55	100%	$119.82	24-Jul-21 A	30-Mar-22
P08-E	Specification For LV Switchgear & Motor Control Centers	49	100%	$6.21	24-Jul-21 A	24-Mar-22
P08-E	Specification For MV Switchgear	49	100%	$7.12	24-Jul-21 A	24-Mar-22
P08-E	Specification For UPS System	49	100%	$7.12	04-Aug-21	24-Mar-22
P08-E	Specification For Transformers	49	100%	$7.12	24-Jul-21 A	24-Mar-22

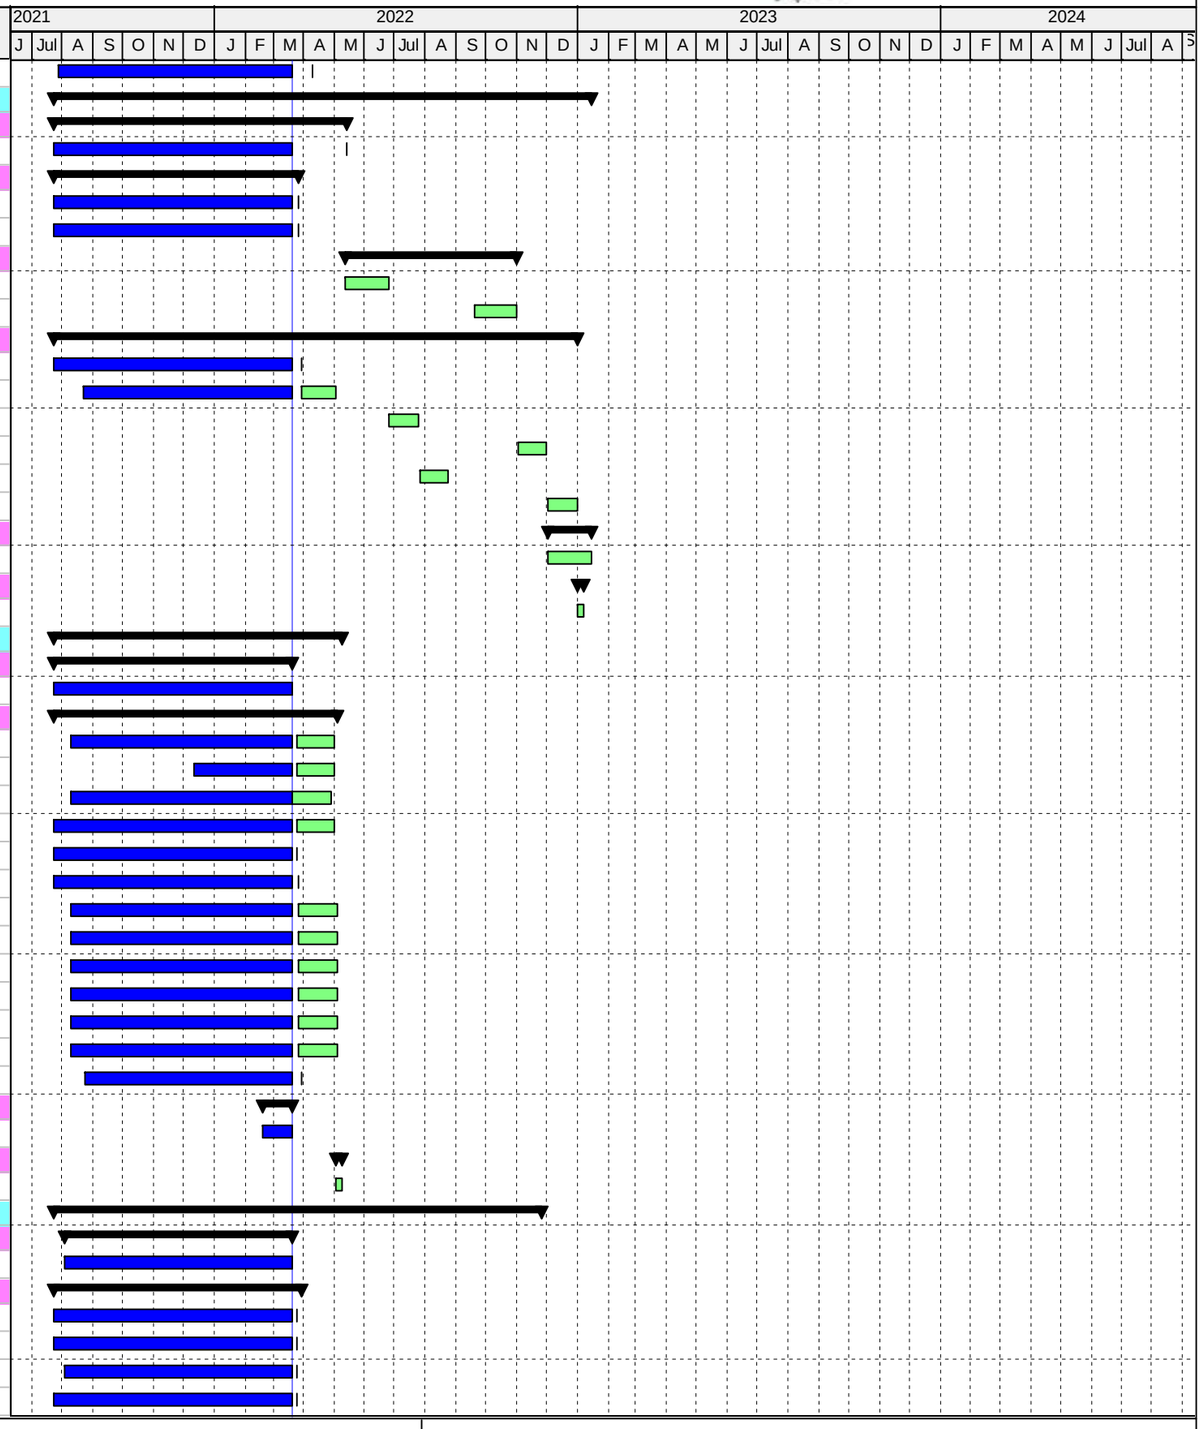


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P08-E	Specification For DC Charger	49	100%	$7.12	04-Aug-21	24-Mar-22
P08-E	Specification For Earthing & Lightning System	49	100%	$4.53	28-Jul-21 A	24-Mar-22
P08-E	Specification For Lighting & Small Power System	49	100%	$6.22	28-Jul-21 A	27-Mar-22
P08-E	Specification For Bulk Materials	49	100%	$6.22	24-Jul-21 A	27-Mar-22
P08-E	Specification For Diesel Generator	49	100%	$7.12	28-Jul-21 A	27-Mar-22
P08-E	Specification For LV Induction Motors	49	100%	$6.52	24-Jul-21 A	27-Mar-22
P08-E	Specification For Electrical Requirements of Packaged Units	49	100%	$7.12	28-Jul-21 A	27-Mar-22
P08-E	Specification For Capacitor Bank	49	100%	$7.12	24-Jul-21 A	27-Mar-22
P08-E	Specification For Distribution & Lighting Panels	49	100%	$7.12	28-Jul-21 A	30-Mar-22
P08-E	Specification For Power & Control Cables	49	100%	$6.22	24-Jul-21 A	30-Mar-22
P08-E	Specification For Cathodic Protection System	49	100%	$6.22	31-Jul-21 A	30-Mar-22
P08-E	Specification For MV Induction Motors	49	100%	$6.52	24-Jul-21 A	30-Mar-22
P08-E	Specification For NGR	49	100%	$7.12	24-Jul-21 A	30-Mar-22
P08-E	Specification For Overhead Transmission Lines	49	100%	$7.12	28-Jul-21 A	30-Mar-22
Calculation		223	40.68%	$196.38	11-Oct-21 A	16-Jul-22
P08-E	Calculation Note For Lighting System of Well Pads Switchgea	64	0%	$14.49	27-Apr-22	29-Jun-22
P08-E	Calculation Note For Lighting System of Well Pads Security B	64	0%	$14.49	27-Apr-22	29-Jun-22
P08-E	Calculation Note For Lighting System of Well Pads Area	74	0%	$19.34	27-Apr-22	09-Jul-22
P08-E	Calculation Note For Cable Sizing of Well Pads	74	80%	$19.34	02-Nov-21	11-Jun-22
P08-E	Calculation Note For UPS System of Well Pads	74	0%	$19.34	04-May-22	16-Jul-22
P08-E	Calculation Note For Earthing & Lightning System of Well Pac	74	0%	$19.34	19-Apr-22	01-Jul-22
P08-E	Calculation Note For Diesel Generator Sizing of Well Pads	64	60%	$14.49	26-Jan-22	27-May-22
P08-E	Calculation Note For DC Charger of Well Pads	74	80%	$19.34	26-Jan-22	06-Jun-22
P08-E	Calculation Note For LV Capacitor Bank of Well Pads	44	60%	$23.55	29-Jan-22	17-May-22
P08-E	Calculation Note For 11 KV Over Head Line Sag and Tension	44	80%	$16.32	13-Oct-21	17-May-22
P08-E	Calculation Note For 33 KV Over Head Line Sag and Tension	44	80%	$16.32	11-Oct-21 A	17-May-22
Data Sheets		208	67.99%	$166.47	12-Sep-21	10-Aug-22
P08-E	Data Sheets For UPS of Well Pads	59	0%	$14.28	13-Jun-22	10-Aug-22
P08-E	Data Sheets For DC Charger of Well Pads	59	80%	$14.28	29-Jan-22	22-May-22
P08-E	Data Sheets For Diesel Generator of Well Pads	59	60%	$14.28	20-Sep-21	22-May-22
P08-E	Data Sheets For LV Capacitor Bank of Well Pads	59	80%	$14.28	12-Sep-21	17-May-22
P08-E	Data Sheets For LV Switchgear of Well Pads	54	60%	$14.28	19-Feb-22	12-May-22
P08-E	Data Sheets For Power & Control Cables of Well Pads	59	80%	$14.28	13-Sep-21	27-May-22
P08-E	Data Sheets For Power Transformers of Well Pads	59	80%	$14.28	15-Sep-21	17-May-22
P08-E	Data Sheets For Distribution & Lighting Panels of Well Pads	59	60%	$14.28	12-Sep-21	31-Jul-22
P08-E	Data Sheets For 11 KV Over Head Line Equipment	44	80%	$26.10	10-Nov-21	16-Jul-22
P08-E	Data Sheets For 33 KV Over Head Line Equipment	44	80%	$26.10	10-Nov-21	16-Jul-22
Drawing/Diagram		221	29.58%	$472.34	09-Aug-21	25-Nov-22
P08-E	Electrical Legend and Symbols	49	100%	$4.06	09-Aug-21	30-Mar-22
P08-E	Typical Installation Details & Notes For Earthing and Lightning	14	100%	$12.14	25-Aug-21	30-Mar-22
P08-E	Typical Installation Details & Notes For Lighting System	14	100%	$10.77	25-Aug-21	30-Mar-22
P08-E	Typical Installation Details & Notes For Power System	14	100%	$3.59	25-Aug-21	30-Mar-22
P08-E	Installation Details & Notes For Cathodic Protection Systems	74	100%	$3.64	25-Aug-21	30-Mar-22
P08-E	Typical Installation Details For Over Head Line Equipment	14	100%	$8.08	22-Aug-21	19-Apr-22
P08-E	Installation Detail & Notes for Connection OHL to Gantries for	54	60%	$32.88	06-Mar-22	12-May-22
P08-E	Electrical Typical Schematic Diagrams For LV Panels of Well F	14	100%	$20.22	30-Aug-21	20-Mar-22
P08-E	Control Logic Diagram For LV Incomers of Well Pads	74	80%	$16.20	30-Aug-21	01-Jun-22
P08-E	Earthing Layout For Electrical Tower (Gantry) of Well Pads	64	0%	$12.14	16-Jul-22	17-Sep-22

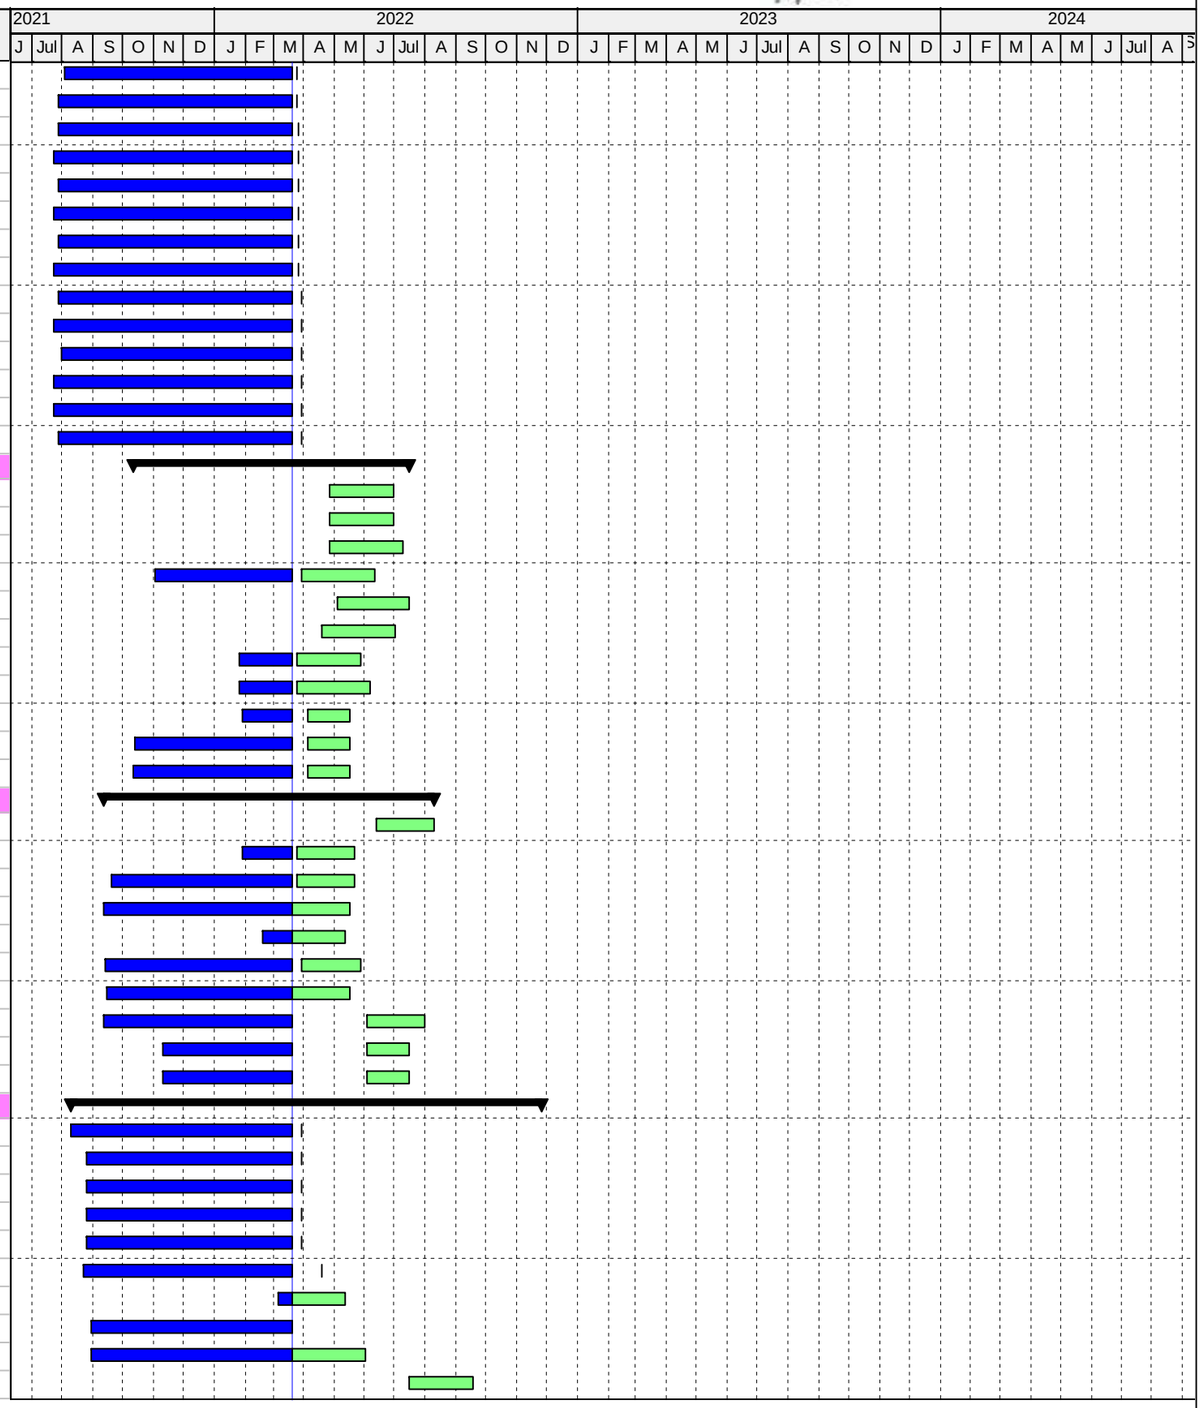


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P08-E	Cable Route Layout For Electrical Tower (Gantry) of Well Pac	74	0%	$16.20	16-Jul-22	27-Sep-22
P08-E	Overall Single Line Diagram of Well Pads	79	60%	$20.22	02-Mar-22	21-Jun-22
P08-E	Single Line Diagram For LV Switchgear of Well Pads	74	60%	$16.20	08-Feb-22	16-Jun-22
P08-E	Single Line Diagram For LV Power Distribution Panel of Well	74	0%	$16.20	04-May-22	16-Jul-22
P08-E	Single Line Diagram For DC Charger of Well Pads	74	80%	$16.20	06-Feb-22	16-Jun-22
P08-E	Single Line Diagram For Capacitor Banks of Well Pads	74	60%	$16.20	02-Feb-22	16-Jun-22
P08-E	Interconnection Wiring Diagram of Well Pads	64	0%	$24.28	04-May-22	06-Jul-22
P08-E	Area Lighting & Small Power Layout of Well Pads of Well Pad	74	0%	$16.20	16-Jul-22	27-Sep-22
P08-E	Lighting & Small Power Layout For Switchgear Building of We	64	0%	$12.14	13-May-22	15-Jul-22
P08-E	Lighting & Small Power Layout For Security Building of Well P	64	0%	$12.14	23-Sep-22	25-Nov-22
P08-E	Area Electrical Cable Route & Section Layout of Well Pads	79	0%	$20.22	16-Jul-22	02-Oct-22
P08-E	Electrical Cable Route & Section Layout For Switchgear Buildi	74	0%	$39.63	16-Jul-22	27-Sep-22
P08-E	Electrical Equipment Arrangement Layout For Switchgear Buil	79	0%	$24.94	13-May-22	30-Jul-22
P08-E	Earthing & Lightning Layout for well pads	64	0%	$16.34	29-May-22	31-Jul-22
P08-E	11KV Over Head Line Study Report	44	0%	$40.76	01-Aug-22	13-Sep-22
P08-E	33KV Over Head Line Study Report	44	0%	$40.76	08-Jul-22	20-Aug-22
List		113	37.67%	$49.85	25-Jan-22	22-Oct-22
P08-E	Electrical Load List of Well Pads	45	80%	$23.48	25-Jan-22	03-May-22
P08-E	Electrical Power & Control Cable List of Well Pads	74	0%	$13.19	10-Aug-22	22-Oct-22
P08-E	Cable Drum Schedule and Cutting List of Well Pads	74	0%	$13.19	10-Aug-22	22-Oct-22
Report		133	0%	$332.76	04-May-22	13-Sep-22
P08-E	Electrical Network (Load Flow, Motor Starting & Short Circuit)	54	0%	$95.24	04-May-22	26-Jun-22
P08-E	Relay Coordination & Setting Study Report of Well Pads	54	0%	$95.24	27-Jun-22	19-Aug-22
P08-E	11KV Over Head Line Study Report	44	0%	$71.14	01-Aug-22	13-Sep-22
P08-E	33KV Over Head Line Study Report	44	0%	$71.14	08-Jul-22	20-Aug-22
MTO		149	0%	$432.64	18-Jun-22	13-Nov-22
P08-E	MTO For Transmission Over Head Line - BK12	7	0%	$99.94	28-Jun-22	04-Jul-22
P08-E	MTO For Lighting & Small Powers - BK12	7	0%	$66.54	07-Nov-22	13-Nov-22
P08-E	MTO For Power & Control Cables - BK12	7	0%	$66.54	29-Sep-22	05-Oct-22
P08-E	MTO For Tray/Ladder and Accessories - BK12	7	0%	$66.54	26-Jul-22	01-Aug-22
P08-E	MTO For Electrical Bulk Items - BK12	7	0%	$66.54	07-Nov-22	13-Nov-22
P08-E	MTO For Earthing & Lightning Systems - BK12	7	0%	$66.54	18-Jun-22	24-Jun-22
Architecture		273	16.97%	$771.34	08-Feb-22	25-Sep-22
Basis/Criteria		74	60%	$155.89	08-Feb-22	01-Jun-22
P08-E	Architectural Design Criteria	74	60%	$155.89	08-Feb-22	01-Jun-22
Specification		44	0%	$194.76	20-Mar-22	02-May-22
P08-E	Buildings General Specification	44	0%	$194.76	20-Mar-22	02-May-22
Drawing/Diagram		238	20%	$186.97	24-Apr-22	18-Sep-22
P08-E	Architectural Drawing For Diesel Generator Shelter of Well P	40	0%	$62.34	24-Apr-22	02-Jun-22
P08-E	Architectural Drawing For Switchgear Building of Well Pads -	40	60%	$62.32	18-May-22	12-May-22
P08-E	Architectural Drawing For Security Building of Well Pads - BK	40	0%	$62.32	10-Aug-22	18-Sep-22
MTO		7	0%	$233.72	19-Sep-22	25-Sep-22
P08-E	MTO For Architectural Works - BK12	7	0%	$233.72	19-Sep-22	25-Sep-22
Civil		128	15.14%	$739.69	01-Aug-21	25-Jul-22
Basis/Criteria		90	20%	$2.59	13-Feb-22	22-May-22
P08-E	Civil Design Criteria	64	60%	$0.86	13-Feb-22	22-May-22
P08-E	Design Criteria for Sewerage & Drainage	44	0%	$0.86	24-Mar-22	06-May-22
P08-E	Design Criteria for Road and Paving	44	0%	$0.86	27-Mar-22	09-May-22
Specification		94	72%	$13.24	09-Aug-21	06-Jun-22

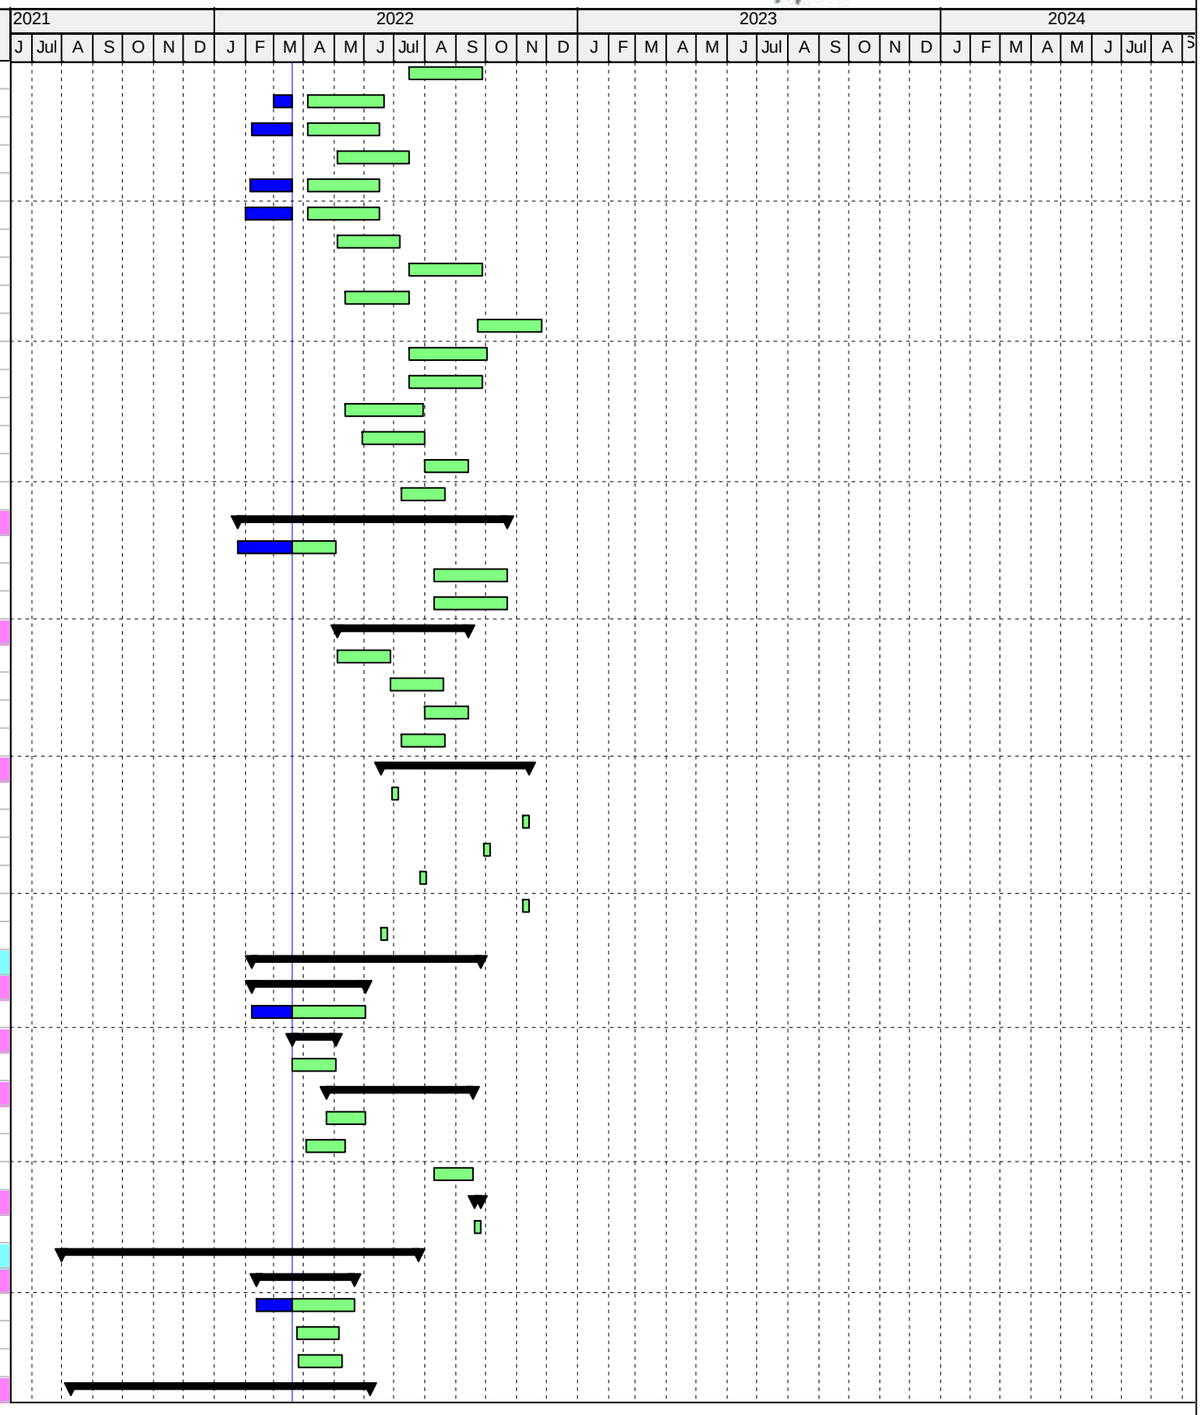


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P08-E	Specification For Civil Works	79	0%	$1.32	20-Mar-22	06-Jun-22
P08-E	Specification For Road & Paving	64	80%	$2.65	09-Aug-21	22-May-22
P08-E	Specification For Fence & Gate	64	100%	$2.65	18-Sep-21	20-Mar-22
P08-E	Specification For Earth Work	64	80%	$2.65	09-Aug-21	22-May-22
P08-E	Specification For Sewerage & Drainage	64	100%	$2.65	09-Aug-21	20-Mar-22
P08-E	Specification For Geological & Geotechnical Survey	44	0%	$1.32	20-Mar-22	02-May-22
Drawing/Diagram		84	18.08%	$563.94	01-Aug-21	11-Jun-22
P08-E	Standard Drawing For Civil Works	45	0%	$6.15	20-Mar-22	03-May-22
P08-E	Standard Drawing For Slope Protection Details	45	100%	$6.15	22-Aug-21	20-Mar-22
P08-E	Standard Drawing For Roads	45	80%	$6.15	22-Aug-21	03-May-22
P08-E	Standard Drawing For Electrical Cable Trench	45	100%	$6.15	22-Aug-21	20-Mar-22
P08-E	Standard Drawing For Manholes	45	80%	$6.15	22-Aug-21	03-May-22
P08-E	Standard Drawing For Catch Basins	45	80%	$6.15	22-Aug-21	03-May-22
P08-E	Standard Drawing For Sewerage & Drainage Details	45	60%	$6.15	02-Feb-22	03-May-22
P08-E	Standard Drawing For Civil Underground Crossings	38	60%	$10.43	07-Feb-22	26-Apr-22
P08-E	Standard Drawing For Fence & Gate Details	45	100%	$6.15	18-Sep-21	20-Mar-22
P08-E	Standard Drawing For Concrete Continues Weight	38	100%	$10.21	01-Aug-21	20-Mar-22
P08-E	Standard Drawing For Major Floodway Crossing	38	0%	$10.21	20-Mar-22	26-Apr-22
P08-E	Standard Drawing For Culvert & Details	38	100%	$10.21	25-Sep-21	20-Mar-22
P08-E	Standard Drawing For Valve Box	38	100%	$10.21	12-Jan-22	20-Mar-22
P08-E	Standard Drawing For Fire Hydrant Pit	38	60%	$10.21	13-Mar-22	26-Apr-22
P08-E	Standard Drawing For Cable Pull Pit	45	0%	$0.00	20-Mar-22	03-May-22
P08-E	Standard Drawing For Pavings	38	60%	$10.21	08-Jan-22	26-Apr-22
P08-E	Standard Drawing For Earth Pit	38	60%	$10.21	13-Feb-22	26-Apr-22
P08-E	Standard Detail For Pipe Bedding	50	100%	$6.15	22-Aug-21	20-Mar-22
P08-E	Standard Details of Miscellaneous Items	50	60%	$6.15	06-Mar-22	08-May-22
P08-E	BINAK Oil Field Project Overall Well Location/Facilities Layou	45	0%	$4.62	20-Mar-22	03-May-22
P08-E	Civil and Structural drawings - BK12	40	0%	$130.66	03-May-22	11-Jun-22
P08-E	General Civil Layout - BK12	40	0%	$130.66	03-May-22	11-Jun-22
P08-E	Rough Grading Plans -BK12	40	0%	$154.63	03-May-22	11-Jun-22
Report		44	0%	$96.46	20-Mar-22	02-May-22
P08-E	Site Visit Report (Civil Work) - BK12	44	0%	$96.46	20-Mar-22	02-May-22
MTO		44	0%	$63.47	12-Jun-22	25-Jul-22
P08-E	MTO For Civil Works - BK12	44	0%	$63.47	12-Jun-22	25-Jul-22
Structure		250	15.19%	$981.10	08-Aug-21	24-Nov-22
Basis/Criteria		64	0%	$10.69	20-Mar-22	22-May-22
P08-E	Structural Design Criteria	64	0%	$3.57	20-Mar-22	22-May-22
P08-E	Design Criteria For Steel Structure	44	0%	$3.56	20-Mar-22	02-May-22
P08-E	Design Criteria For Load & Forces	44	0%	$3.56	20-Mar-22	02-May-22
Specification		98	98.97%	$81.73	14-Aug-21	26-May-22
P08-E	Specification For Concrete Work	64	80%	$1.19	14-Aug-21	26-May-22
P08-E	Specification For Storage Tank Foundation	38	100%	$30.97	23-Nov-21	24-Mar-22
P08-E	Specification for Fabrication of Steel Structures	64	100%	$0.61	24-Jan-22	24-Mar-22
P08-E	Specification For Grouting	64	100%	$23.98	14-Aug-21	24-Mar-22
P08-E	Specification for Erection of Steel Structures	64	100%	$0.80	24-Jan-22	24-Mar-22
P08-E	Specification for Fireproofing	64	100%	$23.57	18-Sep-21	24-Mar-22
P08-E	Specification For Steel Structural Works	37	0%	$0.60	20-Mar-22	25-Apr-22
Drawing/Diagram		233	10.78%	$632.71	08-Aug-21	17-Nov-22
P08-E	Standard Drawing For Fire Proofing	40	100%	$4.05	08-Aug-21	03-Apr-22

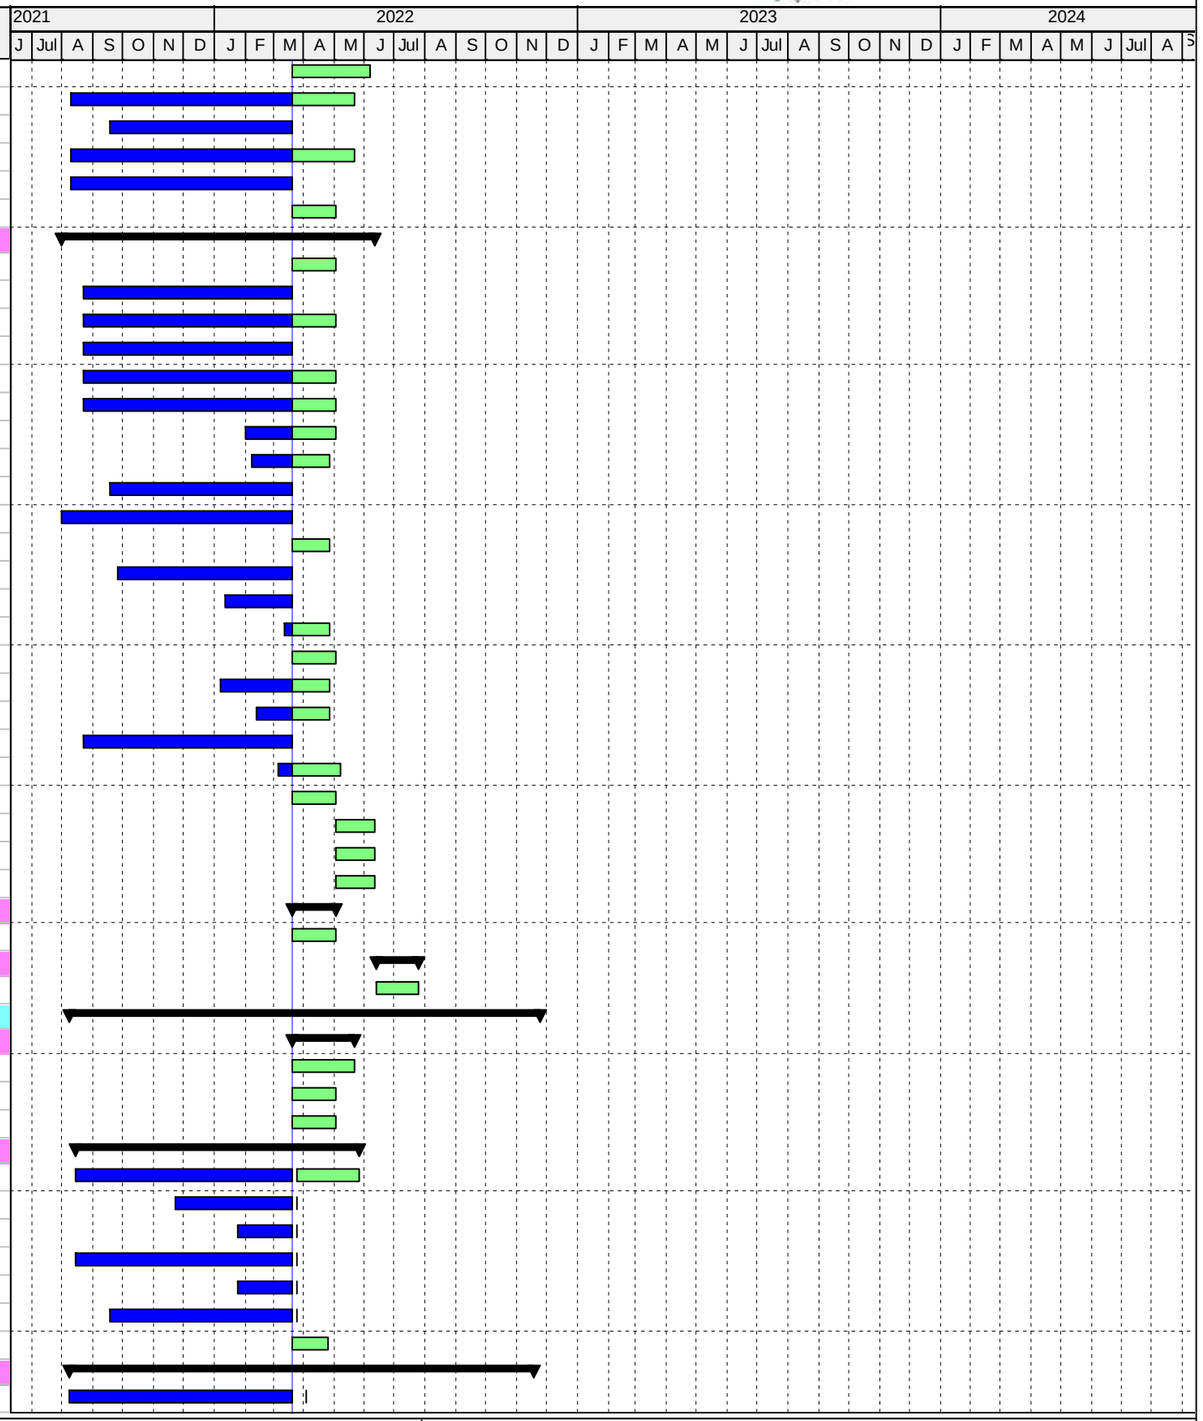


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P08-E	Standard Drawing For Anchor Bolts	40	100%	$4.05	15-Dec-21	03-Apr-22
P08-E	Standard Drawing For Steel Stairs	40	100%	$4.05	18-Dec-21	03-Apr-22
P08-E	Standard Drawing For Operating Platform	38	100%	$4.81	27-Dec-21	30-Mar-22
P08-E	Standard Drawing For Handrail	38	100%	$6.83	18-Dec-21	30-Mar-22
P08-E	Standard Drawing For Insert Plates in Concrete	38	100%	$6.83	08-Aug-21	30-Mar-22
P08-E	Standard Details For Ladder & Safety Cage	40	100%	$4.05	15-Dec-21	03-Apr-22
P08-E	Standard Drawing For Lighting pole foundation Plan & Details	38	60%	$6.83	29-Jan-22	06-May-22
P08-E	General Notes - Steel Structures	38	100%	$4.81	25-Jan-22	30-Mar-22
P08-E	General Notes - Reinforced Concrete Structures	38	100%	$6.83	20-Dec-21	30-Mar-22
P08-E	Standard Drawing For Structural Built-up Sections	30	80%	$6.83	04-Dec-21	28-Apr-22
P08-E	Standard Drawing For Steel Flooring, Grating and Chequere	30	100%	$6.83	05-Jan-22	30-Mar-22
P08-E	Concrete Reinforcement Shape Code	30	0%	$6.83	30-Mar-22	28-Apr-22
P08-E	Standard Drawing For Septic Tank	30	80%	$6.83	22-Jan-22	28-Apr-22
P08-E	Fuel Oil Storage Drum Detail Drawing For Well Pads - BK-12	30	0%	$69.03	10-Jul-22	08-Aug-22
P08-E	Foundation Drawing For Security Building For Well Pads - Bk	30	0%	$69.03	19-Sep-22	18-Oct-22
P08-E	Structural Drawing For Security Building For Well Pads - BK-	30	0%	$69.03	19-Oct-22	17-Nov-22
P08-E	Foundation Drawing For Switchgear Building For Well Pads -	30	0%	$69.03	13-May-22	11-Jun-22
P08-E	Structural Drawing For Switchgear Building For Well Pads - E	30	0%	$69.03	12-Jun-22	11-Jul-22
P08-E	Foundation Drawing For Potable Water Tank For Well Pads -	30	0%	$69.03	28-Aug-22	26-Sep-22
P08-E	Foundation Drawing For Diesel Generator Shelter For Well F	30	0%	$69.03	03-Jun-22	02-Jul-22
P08-E	Structural Drawing For Diesel Generator Shelter For Well Pa	30	0%	$69.03	03-Jul-22	01-Aug-22
MTO		7	0%	$255.97	18-Nov-22	24-Nov-22
P08-E	MTO For Structural Works - BK12	7	0%	$255.97	18-Nov-22	24-Nov-22
General		123	7.46%	$1,475.70	11-Aug-21	20-Jul-22
Geotechnic		104	8%	$1,180.56	11-Aug-21	02-May-22
Procedure/Plan		44	100%	$94.44	11-Aug-21	19-Apr-22
P08-	Geotechnical Investigation Plan for Well Pads	44	100%	$94.44	11-Aug-21	19-Apr-22
Report		44	0%	$1,086.12	20-Mar-22	02-May-22
P08-	Geotechnical Investigation Report - BK12	44	0%	$1,086.12	20-Mar-22	02-May-22
Survey		39	0%	$147.57	12-Jun-22	20-Jul-22
Drawing/Diagram		39	0%	$147.57	12-Jun-22	20-Jul-22
P08-	Over Head Line Plan and Profile - BK12	39	0%	$147.57	12-Jun-22	20-Jul-22
QC/QA		116	10.58%	$147.57	20-Sep-21	13-Jul-22
QC Management		116	38.9%	$12.00	08-Dec-21	13-Jul-22
P08-	Project Audit Procedure	44	0%	$0.60	20-Mar-22	02-May-22
P08-	Specification For Final Data Book (FDB) Requirements	44	0%	$0.60	20-Mar-22	02-May-22
P08-	Non Conformance Control Procedure	36	0%	$0.60	03-May-22	07-Jun-22
P08-	Corrective Action Procedure	36	0%	$0.60	08-Jun-22	13-Jul-22
P08-	Material Reciving, Storage, Handling Procedure	39	60%	$0.60	20-Feb-22	27-Apr-22
P08-	Packing, Marking, Transportation Procedure	39	0%	$0.60	20-Mar-22	27-Apr-22
P08-	Criticality Assessment Procedure	39	0%	$2.40	20-Mar-22	27-Apr-22
P08-	Project Quality Plan	44	80%	$5.40	08-Dec-21	02-May-22
P08-	Technical Query Procedure	44	0%	$0.60	30-Mar-22	12-May-22
QC General Document		55	8.57%	$17.52	28-Nov-21	16-May-22
P08-	Quality Control Plan (QCP)	39	60%	$2.50	28-Nov-21	27-Apr-22
P08-	Specification for Welding Procedure	44	0%	$2.50	03-Apr-22	16-May-22
P08-	Heat Treatment Procedure (Pre Heating , PWHT)	44	0%	$2.50	03-Apr-22	16-May-22
P08-	Welder Performance Qualification Test (WQT) Procedure	44	0%	$2.50	03-Apr-22	16-May-22
P08-	NDT Procedure	44	0%	$2.50	03-Apr-22	16-May-22

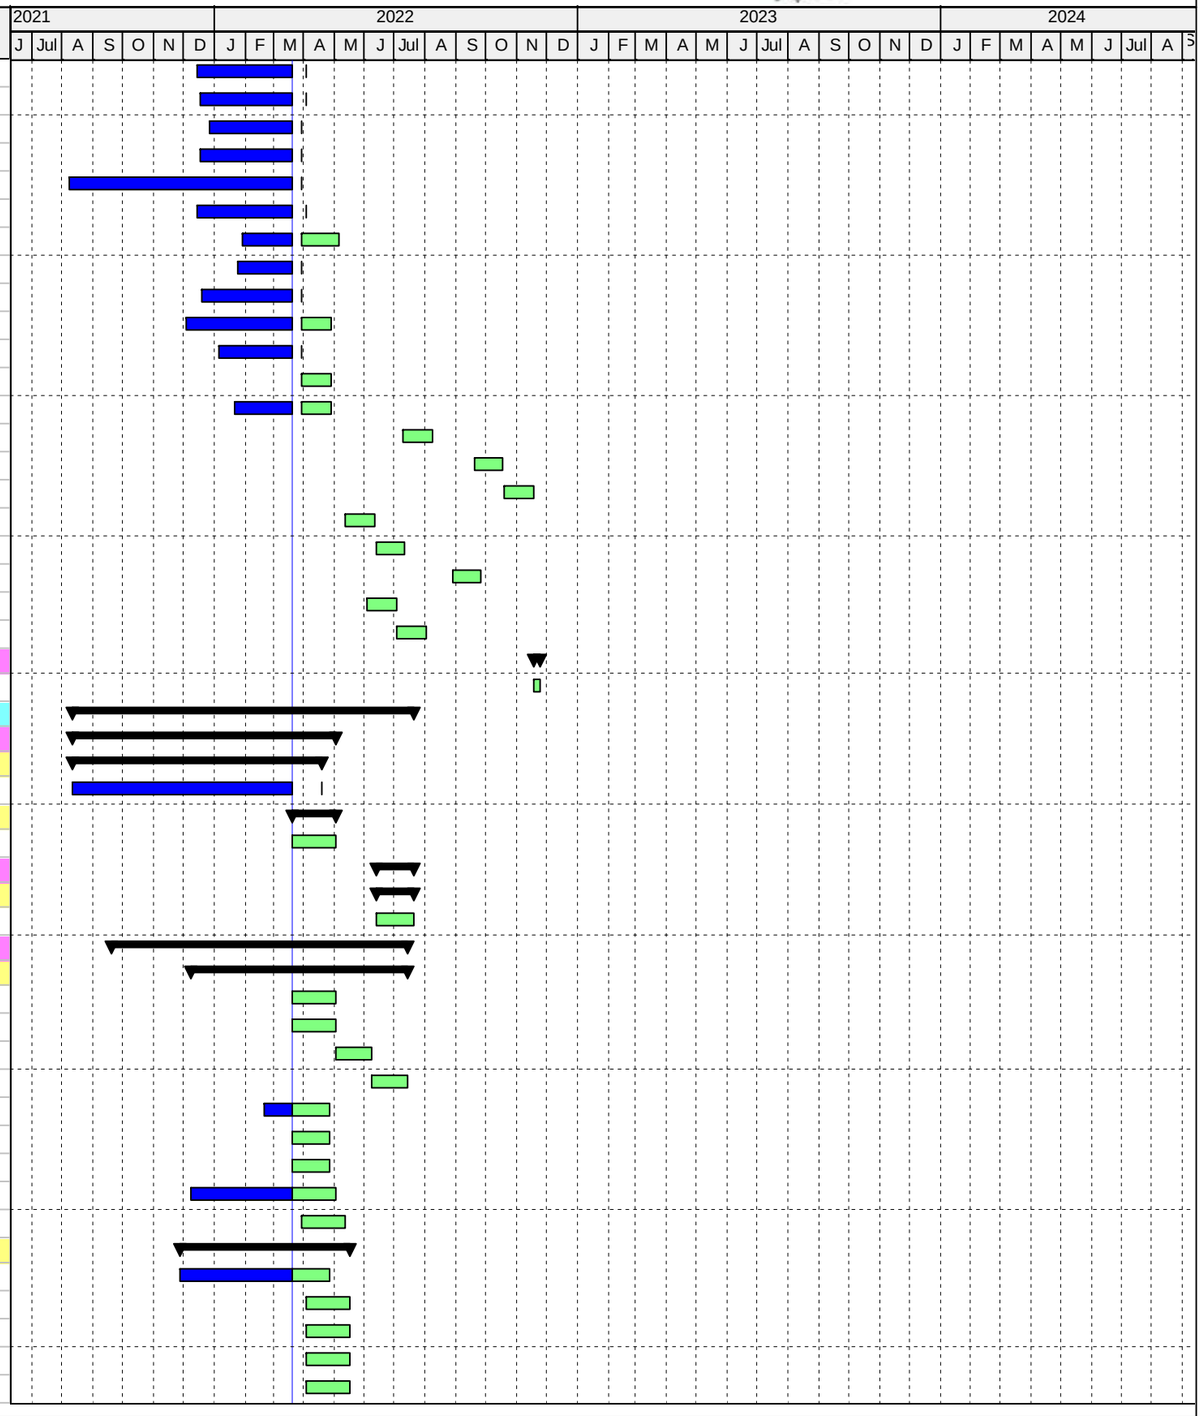


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P08-	Surface Preparation and Coating/Painting Procedure	44	0%	$2.50	03-Apr-22	16-May-22
P08-	Control of Inspection Measuring and Test Equipment Procedu	44	0%	$2.49	03-Apr-22	16-May-22
QC Discipline Document		95	7.99%	$118.06	20-Sep-21	29-Jun-22
Piping		95	0%	$29.51	27-Mar-22	29-Jun-22
P08	ITP For Piping Works	44	0%	$2.95	27-Mar-22	09-May-22
P08	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$3.32	03-Apr-22	16-May-22
P08	PIPING WPS (Welding Procedure Specification)	44	0%	$3.32	03-Apr-22	16-May-22
P08	PIPING PQR (Procedure Qualification Record)	44	0%	$3.32	03-Apr-22	16-May-22
P08	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$3.32	03-Apr-22	16-May-22
P08	PIPING WPS (Preliminary Welding Procedure Specification) f	44	0%	$3.32	03-Apr-22	16-May-22
P08	PIPING PQR (Procedure Qualification Record) for Repair We	44	0%	$3.32	03-Apr-22	16-May-22
P08	Field Joint Coating Procedure For Pipeline	44	0%	$3.32	03-Apr-22	16-May-22
P08	Pressure Test Procedure	44	0%	$3.32	17-May-22	29-Jun-22
Telecomm.		44	0%	$5.90	27-Mar-22	09-May-22
P08	ITP For Telecommunication Installation	44	0%	$5.90	27-Mar-22	09-May-22
Safety		44	0%	$5.90	27-Mar-22	09-May-22
P08	ITP For Safety Installation	44	0%	$5.90	27-Mar-22	09-May-22
Architectural		44	0%	$5.90	27-Mar-22	09-May-22
P08	ITP For Architectural Works	44	0%	$5.90	27-Mar-22	09-May-22
Mechanical		44	0%	$5.90	27-Mar-22	09-May-22
P08	ITP For Mechanical Installation	44	0%	$5.90	27-Mar-22	09-May-22
Structure		51	0%	$23.61	27-Mar-22	16-May-22
P08	ITP For Steel Structural Works	44	0%	$2.36	27-Mar-22	09-May-22
P08	Steel Structure WPS (Welding Procedure Specification)	44	0%	$3.54	03-Apr-22	16-May-22
P08	Steel Structure PQR (Procedure Qualification Record)	44	0%	$3.54	03-Apr-22	16-May-22
P08	Steel Structure WPS (Welding Procedure Specification) For F	44	0%	$3.54	03-Apr-22	16-May-22
P08	Steel Structure PQR (Procedure Qualification Record) For Re	44	0%	$3.54	03-Apr-22	16-May-22
P08	Weld Map For Steel Structures	44	0%	$3.54	03-Apr-22	16-May-22
P08	NDT Plan For steel Structures	44	0%	$3.54	03-Apr-22	16-May-22
Instrumentation		44	0%	$5.90	27-Mar-22	09-May-22
P08	ITP For I&C Installation	44	0%	$5.90	27-Mar-22	09-May-22
Pipeline		74	15%	$23.61	16-Jan-22	16-May-22
P08	ITP For Pipeline	44	60%	$2.36	16-Jan-22	09-May-22
P08	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	60%	$3.54	23-Feb-22	16-May-22
P08	PIPELINE WPS (Welding Procedure Specification)	44	0%	$3.54	03-Apr-22	16-May-22
P08	PIPELINE PQR (Procedure Qualification Record)	44	0%	$3.54	03-Apr-22	16-May-22
P08	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	0%	$3.54	03-Apr-22	16-May-22
P08	PIPELINE WPS (Preliminary Welding Procedure Specificatior	44	0%	$3.54	03-Apr-22	16-May-22
P08	PIPELINE PQR (Procedure Qualification Record) for Repair \	44	0%	$3.54	03-Apr-22	16-May-22
Civil		44	100%	$5.90	20-Sep-21	27-Mar-22
P08	ITP For Civil Works	44	100%	$5.90	20-Sep-21	27-Mar-22
Electrical		44	0%	$5.90	27-Mar-22	09-May-22
P08	ITP For Electrical Installation	44	0%	$5.90	27-Mar-22	09-May-22
Procurement Engineering		308	0%	$1,338.20	19-Apr-22	20-Feb-23
Mechanical		49	0%	$133.82	29-May-22	16-Jul-22
Drum		42	0%	$80.29	29-May-22	09-Jul-22
P08-E	PMR For Drum - BK12	5	0%	$8.03	29-May-22	02-Jun-22
P08-E	TBE For Main Drum - BK12	5	0%	$12.04	03-Jun-22	07-Jun-22
P08-E	VDR For Drum - BK12	7	0%	$60.22	03-Jul-22	09-Jul-22
Potable Tanks		44	0%	$53.53	03-Jun-22	16-Jul-22

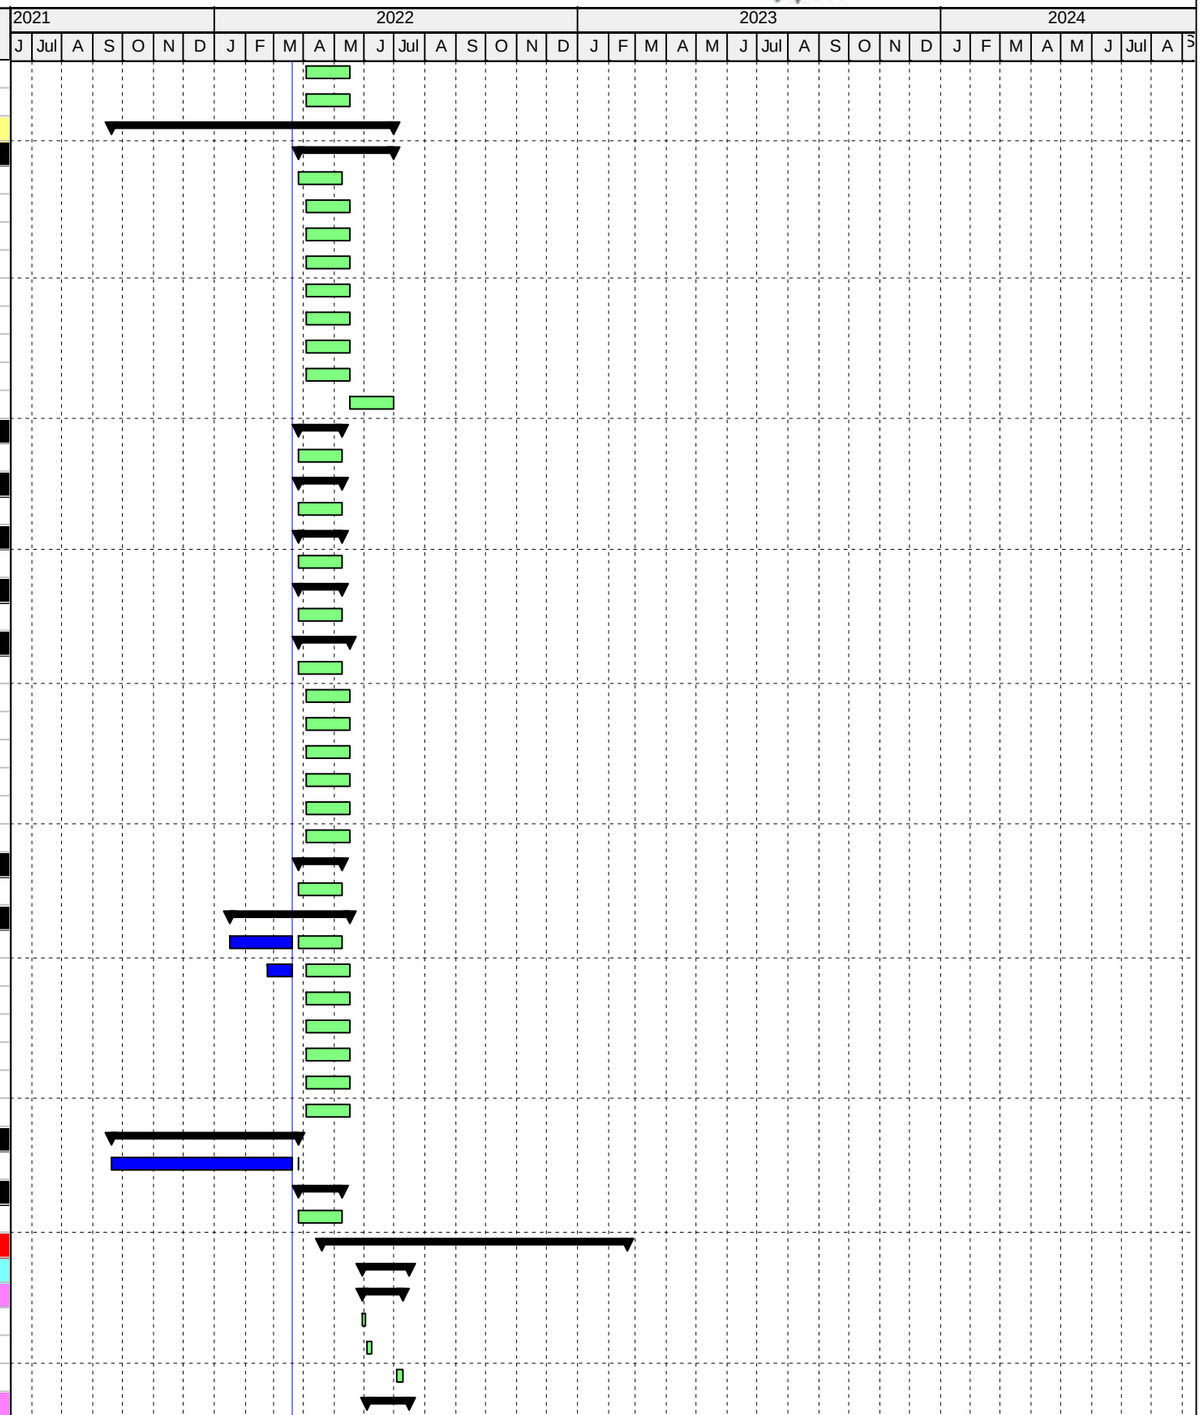


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P08-E	PMR For Potable Tanks - BK12	20	0%	$5.35	03-Jun-22	22-Jun-22
P08-E	TBE For Potable Tanks - BK12	5	0%	$8.03	23-Jun-22	27-Jun-22
P08-E	VDR For Potable Tanks - BK12	7	0%	$40.15	10-Jul-22	16-Jul-22
Electrical		246	0%	$1,012.62	19-Apr-22	20-Dec-22
Electrical Bulk Items		37	0%	$76.35	14-Nov-22	20-Dec-22
P08-E	PMR For Electrical Bulk Items - BK12	20	0%	$7.64	14-Nov-22	03-Dec-22
P08-E	TBE For Electrical Bulk Items - BK12	30	0%	$11.45	21-Nov-22	20-Dec-22
P08-E	VDR For Electrical Bulk Items - BK12	7	0%	$57.26	01-Dec-22	07-Dec-22
Lighting & Distribution Main Panels		37	0%	$76.45	01-Aug-22	06-Sep-22
P08-E	PMR For Lighting & Distribution Main Panels - BK12	20	0%	$7.65	01-Aug-22	20-Aug-22
P08-E	TBE For Lighting & Distribution Main Panels - BK12	30	0%	$11.47	08-Aug-22	06-Sep-22
P08-E	VDR For Lighting & Distribution Main Panels - BK12	7	0%	$57.34	23-Aug-22	29-Aug-22
Earthing & Lightning System		37	0%	$76.45	25-Jun-22	31-Jul-22
P08-E	PMR For Earthing & Lightning System - BK12	20	0%	$7.65	25-Jun-22	14-Jul-22
P08-E	TBE For Earthing & Lightning System - BK12	30	0%	$11.47	02-Jul-22	31-Jul-22
P08-E	VDR For Earthing & Lightning System - BK12	7	0%	$57.34	12-Jul-22	18-Jul-22
Lighting and Small Power Equipment		37	0%	$76.45	14-Nov-22	20-Dec-22
P08-E	PMR For Lighting and Small Power Equipment - BK12	20	0%	$7.65	14-Nov-22	03-Dec-22
P08-E	TBE For Lighting and Small Power Equipment - BK12	30	0%	$11.47	21-Nov-22	20-Dec-22
P08-E	VDR For Lighting and Small Power Equipment - BK12	7	0%	$57.34	06-Dec-22	12-Dec-22
Tray/Ladder and Accessories		37	0%	$76.35	02-Aug-22	07-Sep-22
P08-E	PMR For Tray/Ladder and Accessories - BK12	20	0%	$7.64	02-Aug-22	21-Aug-22
P08-E	TBE For Tray/Ladder and Accessories - BK12	30	0%	$11.45	09-Aug-22	07-Sep-22
P08-E	VDR For Tray/Ladder and Accessories - BK12	7	0%	$57.26	24-Aug-22	30-Aug-22
Power & Control Cables		37	0%	$76.35	06-Oct-22	11-Nov-22
P08-E	PMR For Power & Control Cables - BK12	20	0%	$7.64	06-Oct-22	25-Oct-22
P08-E	TBE For Power & Control Cables - BK12	30	0%	$11.45	13-Oct-22	11-Nov-22
P08-E	VDR For Power & Control Cables - BK12	7	0%	$57.26	28-Oct-22	03-Nov-22
Transmission Over head Line		37	0%	$95.49	05-Jul-22	10-Aug-22
P08-E	PMR For Transmission Over head Line - BK12	20	0%	$9.55	05-Jul-22	24-Jul-22
P08-E	TBE For Transmission Over head Line - BK12	30	0%	$14.32	12-Jul-22	10-Aug-22
P08-E	VDR For Transmission Over head Line - BK12	7	0%	$71.62	22-Jul-22	28-Jul-22
Emergency Diesel Generator		37	0%	$76.45	24-Apr-22	30-May-22
P08-E	PMR For Emergency Diesel Generator - BK12	20	0%	$7.65	24-Apr-22	13-May-22
P08-E	TBE For Emergency Diesel Generator - BK12	30	0%	$11.47	01-May-22	30-May-22
P08-E	VDR For Emergency Diesel Generator - BK12	7	0%	$57.34	11-May-22	17-May-22
Transformers		37	0%	$76.45	19-Apr-22	25-May-22
P08-E	PMR For Transformers - BK12	20	0%	$7.65	19-Apr-22	08-May-22
P08-E	TBE For Transformers - BK12	30	0%	$11.47	26-Apr-22	25-May-22
P08-E	VDR For Transformers - BK12	7	0%	$57.34	11-May-22	17-May-22
LV Switchgear & MCC		37	0%	$76.45	19-Apr-22	25-May-22
P08-E	PMR For LV Switchgear & MCC - BK12	20	0%	$7.65	19-Apr-22	08-May-22
P08-E	TBE For LV Switchgear & MCC - BK12	30	0%	$11.47	26-Apr-22	25-May-22
P08-E	VDR For LV Switchgear & MCC - BK12	7	0%	$57.34	11-May-22	17-May-22
UPS System		37	0%	$76.45	13-Jul-22	18-Aug-22
P08-E	PMR For UPS System - BK12	20	0%	$7.65	13-Jul-22	01-Aug-22
P08-E	TBE For UPS System - BK12	30	0%	$11.47	20-Jul-22	18-Aug-22
P08-E	VDR For UPS System - BK12	7	0%	$57.34	01-Aug-22	07-Aug-22
DC Charger		37	0%	$76.45	24-Apr-22	30-May-22

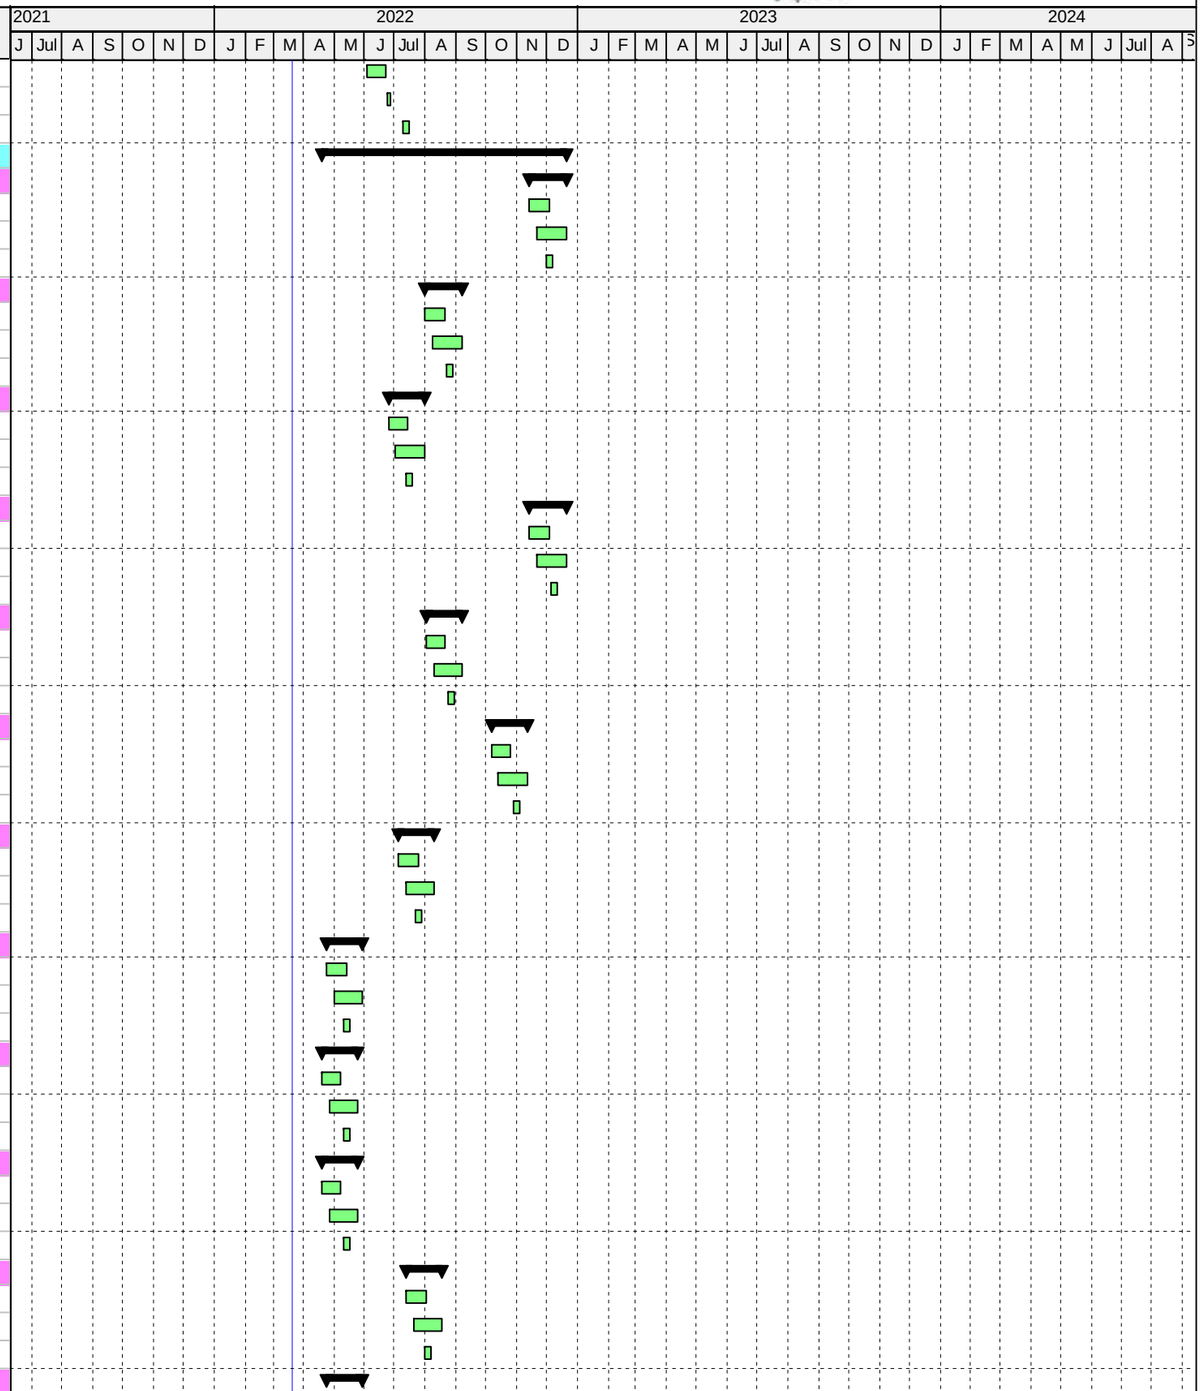

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P08-E	PMR For DC Charger - BK12	20	0%	$7.65	24-Apr-22	13-May-22
P08-E	TBE For DC Charger - BK12	30	0%	$11.47	01-May-22	30-May-22
P08-E	VDR For DC Charger - BK12	7	0%	$57.34	11-May-22	17-May-22
Capacitor Bank		37	0%	$76.45	19-Apr-22	25-May-22
P08-E	PMR For Capacitor Bank - BK12	20	0%	$7.65	19-Apr-22	08-May-22
P08-E	TBE For Capacitor Bank - BK12	30	0%	$11.47	26-Apr-22	25-May-22
P08-E	VDR For Capacitor Bank - BK12	7	0%	$57.34	11-May-22	17-May-22
Structure		43	0%	$85.91	25-Nov-22	06-Jan-23
Steel Structure Items		19	0%	$28.64	25-Nov-22	13-Dec-22
P08-E	PMR For Steel Structure Items - BK12	10	0%	$2.86	25-Nov-22	04-Dec-22
P08-E	TBE For Steel Structure Items - BK12	7	0%	$4.30	02-Dec-22	08-Dec-22
P08-E	VDR For Steel Structure Items - BK12	5	0%	$21.48	09-Dec-22	13-Dec-22
Anchor Bolts		43	0%	$28.63	25-Nov-22	06-Jan-23
P08-E	PMR For Anchor Bolts - BK12	10	0%	$2.86	25-Nov-22	04-Dec-22
P08-E	TBE For Anchor Bolts - BK12	30	0%	$4.30	02-Dec-22	31-Dec-22
P08-E	VDR For Anchor Bolts - BK12	6	0%	$21.48	01-Jan-23	06-Jan-23
Blast Proof Doors		43	0%	$28.63	25-Nov-22	06-Jan-23
P08-E	PMR For Blast Proof Doors - BK12	10	0%	$2.86	25-Nov-22	04-Dec-22
P08-E	TBE For Blast Proof Doors - BK12	30	0%	$4.30	02-Dec-22	31-Dec-22
P08-E	VDR For Blast Proof Doors - BK12	6	0%	$21.48	01-Jan-23	06-Jan-23
HVAC		44	0%	$48.58	08-Jan-23	20-Feb-23
Main HVAC Equipment		44	0%	$48.58	08-Jan-23	20-Feb-23
P08-E	PMR For Main HVAC Equipment - BK12	7	0%	$4.86	08-Jan-23	14-Jan-23
P08-E	TBE For Main HVAC Equipment - BK12	20	0%	$7.29	15-Jan-23	03-Feb-23
P08-E	VDR For Main HVAC Equipment - BK12	7	0%	$36.43	14-Feb-23	20-Feb-23
Piping		58	0%	$57.27	10-May-22	06-Jul-22
Pipe		51	0%	$28.64	10-May-22	29-Jun-22
P08-E	PMR For Pipes - BK12	7	0%	$2.86	10-May-22	16-May-22
P08-E	TBE For Pipes - BK12	25	0%	$4.30	17-May-22	10-Jun-22
P08-E	VDR For Pipes - BK12	7	0%	$21.48	23-Jun-22	29-Jun-22
Pipe Support		51	0%	$28.64	17-May-22	06-Jul-22
P08-E	PMR For Pipe Support - BK12	7	0%	$2.86	17-May-22	23-May-22
P08-E	TBE For Pipe Support - BK12	25	0%	$4.30	24-May-22	17-Jun-22
P08-E	VDR For Pipe Support - BK12	7	0%	$21.48	30-Jun-22	06-Jul-22
Commissioning Engineering		420	0%	$267.64	20-Mar-22	13-May-23
P08-EP	Operability Review	5	0%	$53.53	20-Mar-22	24-Mar-22
P08-EP	Pre-Commissioning, Commissioning & Startup Procedure - BI	44	0%	$160.58	20-Mar-22	02-May-22
P08-EP	Operating Manual - BK12	30	0%	$53.53	14-Apr-23	13-May-23
Field Engineering		346	0%	$3,345.50	12-Jun-22	23-May-23
P08-EP	Technical/Site Queries	44	0%	$1,003.65	12-Jun-22	25-Jul-22
P08-EP	As-Built Document Booklets - BK12	10	0%	$1,003.65	14-May-23	23-May-23
Dossier		44	0%	$1,338.20	15-Jan-23	27-Feb-23
P08-EF	Final Engineering Dossier - BK12	44	0%	$1,338.20	15-Jan-23	27-Feb-23
PROCUREMENT		353	0%	$258,521.00	26-Apr-22	13-Apr-23
Mechanical		89	0%	$16,002.45	08-Jun-22	04-Sep-22
Drum		89	0%	$9,601.47	08-Jun-22	04-Sep-22
P08-EF	Tendering & Selection	5	0%	$384.06	08-Jun-22	12-Jun-22
P08-EF	Contract Effectiveness / PO	5	0%	$576.09	28-Jun-22	02-Jul-22
P08-EF	Manufacturing / Fabrication / Supply	40	0%	$4,800.73	03-Jul-22	11-Aug-22
P08-EF	Final Inspection	7	0%	$960.15	12-Aug-22	18-Aug-22




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P08-EI	Delivery On Site	7	0%	$1,920.29	19-Aug-22	25-Aug-22
P08-EI	Submitting Vendor Data Book	5	0%	$480.07	26-Aug-22	30-Aug-22
P08-EI	Delivering Spare Parts	5	0%	$480.07	31-Aug-22	04-Sep-22
Potable Tanks		66	0%	$6,400.98	28-Jun-22	01-Sep-22
P08-EI	Tendering & Selection	7	0%	$256.04	28-Jun-22	04-Jul-22
P08-EI	Contract Effectiveness / PO	5	0%	$384.06	05-Jul-22	09-Jul-22
P08-EI	Manufacturing / Fabrication / Supply	30	0%	$3,200.49	10-Jul-22	08-Aug-22
P08-EI	Final Inspection	7	0%	$640.10	09-Aug-22	15-Aug-22
P08-EI	Delivery On Site	7	0%	$1,280.20	16-Aug-22	22-Aug-22
P08-EI	Submitting Vendor Data Book	5	0%	$320.05	23-Aug-22	27-Aug-22
P08-EI	Delivering Spare Parts	5	0%	$320.05	28-Aug-22	01-Sep-22
Piping		73	0%	$30,014.29	11-Jun-22	22-Aug-22
Pipes - BK12		71	0%	$24,011.43	11-Jun-22	20-Aug-22
P08-EI	Tendering & Selection	7	0%	$960.46	11-Jun-22	17-Jun-22
P08-EI	Contract Effectiveness / PO	5	0%	$1,440.69	18-Jun-22	22-Jun-22
P08-EI	Manufacturing / Fabrication / Supply	40	0%	$12,005.72	23-Jun-22	01-Aug-22
P08-EI	Final Inspection	7	0%	$2,401.14	02-Aug-22	08-Aug-22
P08-EI	Delivery On Site	7	0%	$6,002.86	09-Aug-22	15-Aug-22
P08-EI	Submitting Vendor Data Book	5	0%	$1,200.57	16-Aug-22	20-Aug-22
Pipe Support - BK12		66	0%	$6,002.86	18-Jun-22	22-Aug-22
P08-EI	Tendering & Selection	7	0%	$240.11	18-Jun-22	24-Jun-22
P08-EI	Contract Effectiveness / PO	5	0%	$360.17	25-Jun-22	29-Jun-22
P08-EI	Manufacturing / Fabrication / Supply	35	0%	$3,001.43	30-Jun-22	03-Aug-22
P08-EI	Final Inspection	7	0%	$600.29	04-Aug-22	10-Aug-22
P08-EI	Delivery On Site	7	0%	$1,500.71	11-Aug-22	17-Aug-22
P08-EI	Submitting Vendor Data Book	5	0%	$300.14	18-Aug-22	22-Aug-22
HVAC		69	0%	$5,997.69	04-Feb-23	13-Apr-23
Main HVAC Equipment - BK12		69	0%	$5,997.69	04-Feb-23	13-Apr-23
P08-EI	Tendering & Selection	5	0%	$239.91	04-Feb-23	08-Feb-23
P08-EI	Contract Effectiveness / PO	5	0%	$359.86	09-Feb-23	13-Feb-23
P08-EI	Manufacturing / Fabrication / Supply	40	0%	$2,998.84	14-Feb-23	25-Mar-23
P08-EI	Final Inspection	7	0%	$599.77	26-Mar-23	01-Apr-23
P08-EI	Delivery On Site	7	0%	$1,499.42	02-Apr-23	08-Apr-23
P08-EI	Submitting Vendor Data Book	5	0%	$299.88	09-Apr-23	13-Apr-23
Electrical		289	0%	$206,506.58	26-Apr-22	08-Feb-23
Tray/Ladder and Accessories - BK12		94	0%	$2,168.32	09-Aug-22	10-Nov-22
P08-EI	Tendering & Selection	10	0%	$86.73	09-Aug-22	18-Aug-22
P08-EI	Contract Effectiveness / PO	5	0%	$130.10	19-Aug-22	23-Aug-22
P08-EI	Manufacturing / Fabrication / Supply	60	0%	$1,084.16	24-Aug-22	22-Oct-22
P08-EI	Final Inspection	7	0%	$216.83	23-Oct-22	29-Oct-22
P08-EI	Delivery On Site	7	0%	$542.08	30-Oct-22	05-Nov-22
P08-EI	Submitting Vendor Data Book	5	0%	$108.42	06-Nov-22	10-Nov-22
Emergency Diesel Generator - BK12		84	0%	$26,143.73	01-May-22	23-Jul-22
P08-EI	Tendering & Selection	5	0%	$1,045.75	01-May-22	05-May-22
P08-EI	Contract Effectiveness / PO	5	0%	$1,568.62	06-May-22	10-May-22
P08-EI	Manufacturing / Fabrication / Supply	50	0%	$13,071.87	11-May-22	29-Jun-22
P08-EI	Final Inspection	7	0%	$2,614.37	30-Jun-22	06-Jul-22
P08-EI	Delivery On Site	7	0%	$5,228.75	07-Jul-22	13-Jul-22
P08-EI	Submitting Vendor Data Book	5	0%	$1,307.19	14-Jul-22	18-Jul-22

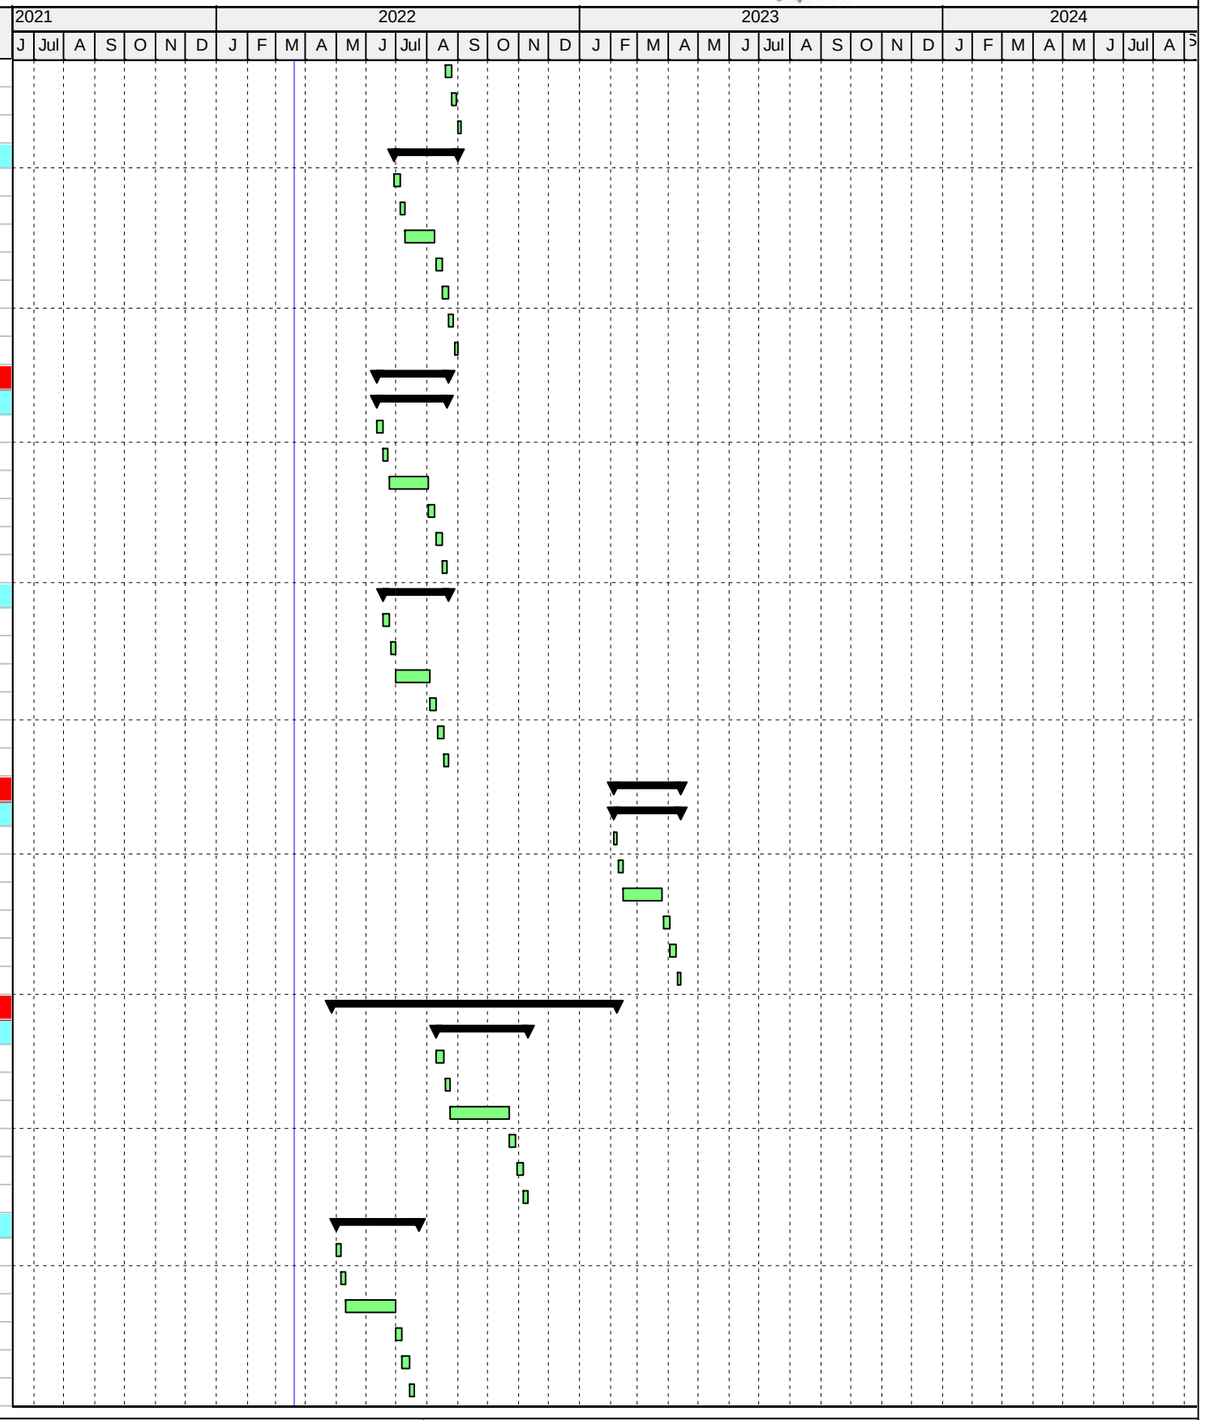


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P08-EI	Delivering Spare Parts	5	0%	$1,307.19	19-Jul-22	23-Jul-22
DC Charger - BK12		84	0%	$16,830.29	01-May-22	23-Jul-22
P08-EI	Tendering & Selection	5	0%	$673.21	01-May-22	05-May-22
P08-EI	Contract Effectiveness / PO	5	0%	$1,009.82	06-May-22	10-May-22
P08-EI	Manufacturing / Fabrication / Supply	50	0%	$8,415.14	11-May-22	29-Jun-22
P08-EI	Final Inspection	7	0%	$1,683.03	30-Jun-22	06-Jul-22
P08-EI	Delivery On Site	7	0%	$3,366.06	07-Jul-22	13-Jul-22
P08-EI	Submitting Vendor Data Book	5	0%	$841.51	14-Jul-22	18-Jul-22
P08-EI	Delivering Spare Parts	5	0%	$841.51	19-Jul-22	23-Jul-22
Electrical Bulk Items - BK12		69	0%	$2,168.32	21-Nov-22	28-Jan-23
P08-EI	Tendering & Selection	5	0%	$86.73	21-Nov-22	25-Nov-22
P08-EI	Contract Effectiveness / PO	5	0%	$130.10	26-Nov-22	30-Nov-22
P08-EI	Manufacturing / Fabrication / Supply	40	0%	$1,084.16	01-Dec-22	09-Jan-23
P08-EI	Final Inspection	7	0%	$216.83	10-Jan-23	16-Jan-23
P08-EI	Delivery On Site	7	0%	$542.08	17-Jan-23	23-Jan-23
P08-EI	Submitting Vendor Data Book	5	0%	$108.42	24-Jan-23	28-Jan-23
Transmission Over head Line - BK12		89	0%	$39,546.01	12-Jul-22	08-Oct-22
P08-EI	Tendering & Selection	5	0%	$1,581.84	12-Jul-22	16-Jul-22
P08-EI	Contract Effectiveness / PO	5	0%	$2,372.76	17-Jul-22	21-Jul-22
P08-EI	Manufacturing / Fabrication / Supply	60	0%	$19,773.00	22-Jul-22	19-Sep-22
P08-EI	Final Inspection	7	0%	$3,954.60	20-Sep-22	26-Sep-22
P08-EI	Delivery On Site	7	0%	$9,886.50	27-Sep-22	03-Oct-22
P08-EI	Submitting Vendor Data Book	5	0%	$1,977.30	04-Oct-22	08-Oct-22
Transformers - BK12		120	0%	$29,592.39	26-Apr-22	23-Aug-22
P08-EI	Tendering & Selection	10	0%	$1,183.70	26-Apr-22	05-May-22
P08-EI	Contract Effectiveness / PO	5	0%	$1,775.54	06-May-22	10-May-22
P08-EI	Manufacturing / Fabrication / Supply	65	0%	$14,796.20	11-May-22	14-Jul-22
P08-EI	Final Inspection	7	0%	$2,959.24	15-Jul-22	21-Jul-22
P08-EI	Delivery On Site	7	0%	$5,918.48	22-Jul-22	28-Jul-22
P08-EI	Submitting Vendor Data Book	21	0%	$1,479.62	29-Jul-22	18-Aug-22
P08-EI	Delivering Spare Parts	5	0%	$1,479.62	19-Aug-22	23-Aug-22
LV Switchgear & MCC - BK12		114	0%	$25,524.21	26-Apr-22	17-Aug-22
P08-EI	Tendering & Selection	10	0%	$1,020.97	26-Apr-22	05-May-22
P08-EI	Contract Effectiveness / PO	5	0%	$1,531.45	06-May-22	10-May-22
P08-EI	Manufacturing / Fabrication / Supply	60	0%	$12,762.11	11-May-22	09-Jul-22
P08-EI	Final Inspection	7	0%	$2,552.42	10-Jul-22	16-Jul-22
P08-EI	Delivery On Site	7	0%	$5,104.84	17-Jul-22	23-Jul-22
P08-EI	Submitting Vendor Data Book	20	0%	$1,276.21	24-Jul-22	12-Aug-22
P08-EI	Delivering Spare Parts	5	0%	$1,276.21	13-Aug-22	17-Aug-22
Capacitor Bank - BK12		115	0%	$5,100.71	26-Apr-22	18-Aug-22
P08-EI	Tendering & Selection	10	0%	$204.03	26-Apr-22	05-May-22
P08-EI	Contract Effectiveness / PO	5	0%	$306.04	06-May-22	10-May-22
P08-EI	Manufacturing / Fabrication / Supply	60	0%	$2,550.36	11-May-22	09-Jul-22
P08-EI	Final Inspection	7	0%	$510.07	10-Jul-22	16-Jul-22
P08-EI	Delivery On Site	7	0%	$1,020.14	17-Jul-22	23-Jul-22
P08-EI	Submitting Vendor Data Book	20	0%	$255.04	24-Jul-22	12-Aug-22
P08-EI	Delivering Spare Parts	6	0%	$255.04	13-Aug-22	18-Aug-22
Lighting & Distribution Main Panels - BK12		99	0%	$6,112.59	08-Aug-22	14-Nov-22
P08-EI	Tendering & Selection	10	0%	$244.50	08-Aug-22	17-Aug-22

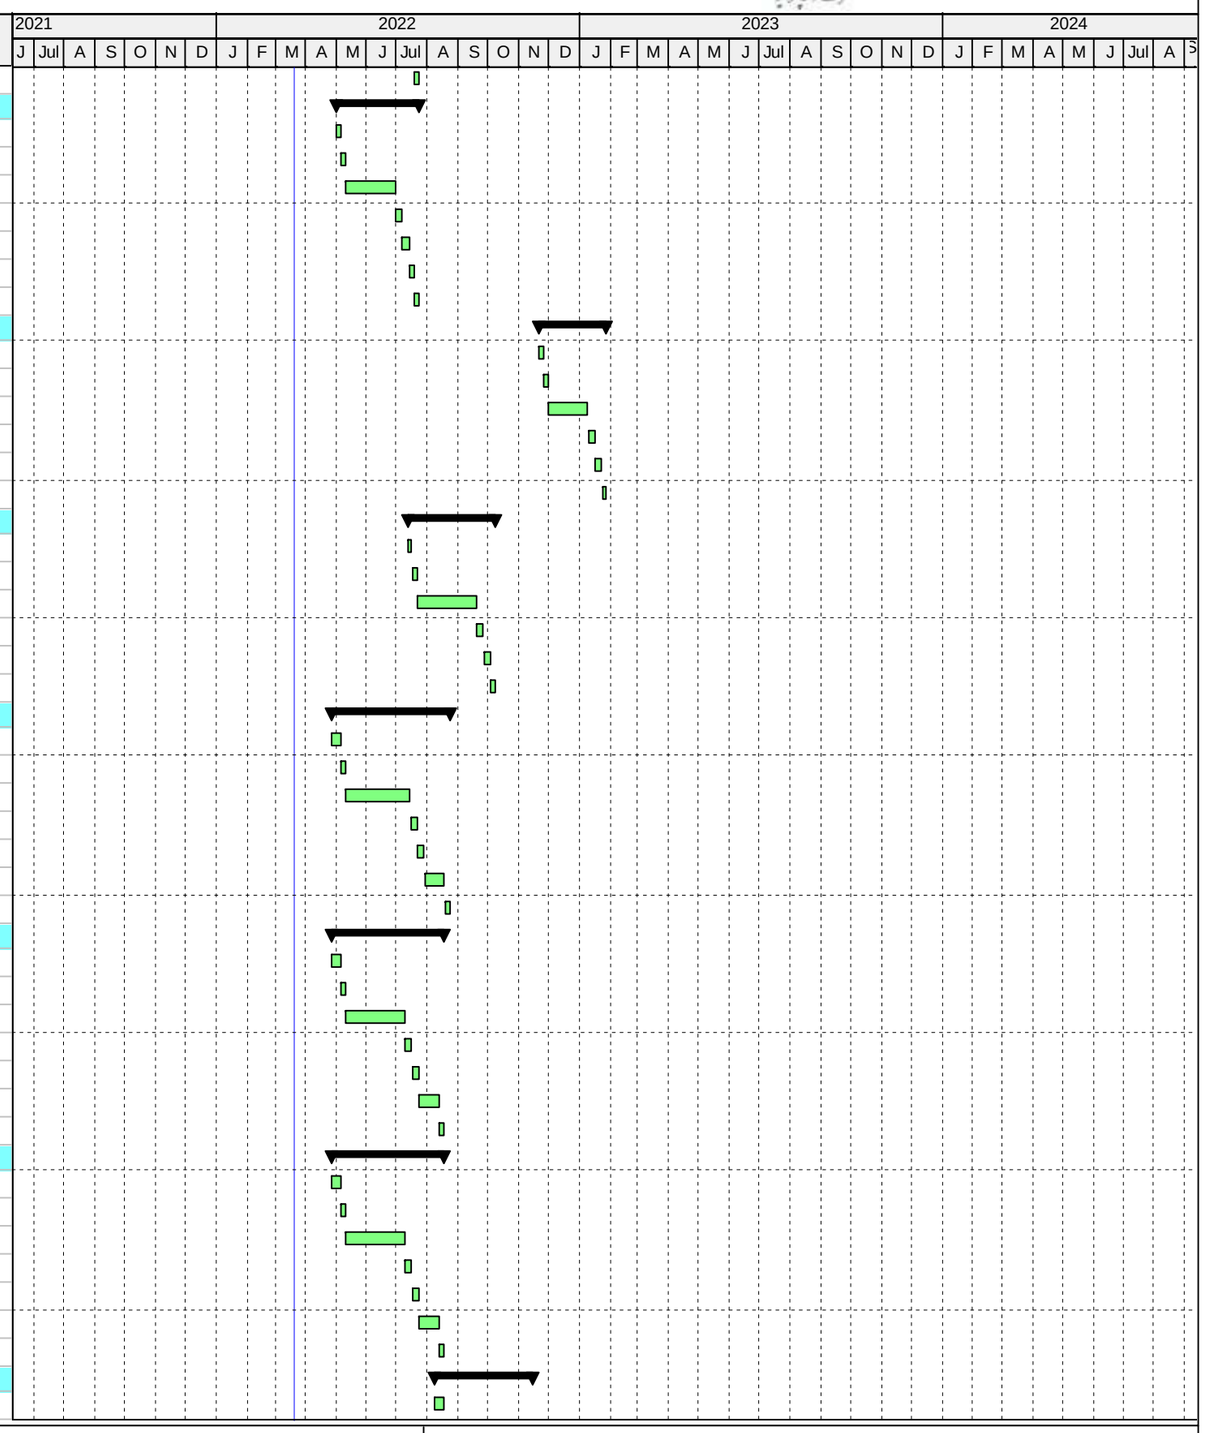


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P08-EF	Contract Effectiveness / PO	5	0%	$366.76	18-Aug-22	22-Aug-22
P08-EF	Manufacturing / Fabrication / Supply	60	0%	$3,056.30	23-Aug-22	21-Oct-22
P08-EF	Final Inspection	7	0%	$611.26	22-Oct-22	28-Oct-22
P08-EF	Delivery On Site	7	0%	$1,222.52	29-Oct-22	04-Nov-22
P08-EF	Submitting Vendor Data Book	5	0%	$305.63	05-Nov-22	09-Nov-22
P08-EF	Delivering Spare Parts	5	0%	$305.63	10-Nov-22	14-Nov-22
Lighting and Small Power Equipment - BK12		80	0%	$12,369.74	21-Nov-22	08-Feb-23
P08-EF	Tendering & Selection	10	0%	$494.79	21-Nov-22	30-Nov-22
P08-EF	Contract Effectiveness / PO	5	0%	$742.18	01-Dec-22	05-Dec-22
P08-EF	Manufacturing / Fabrication / Supply	41	0%	$6,184.87	06-Dec-22	15-Jan-23
P08-EF	Final Inspection	7	0%	$1,236.97	16-Jan-23	22-Jan-23
P08-EF	Delivery On Site	7	0%	$2,473.95	23-Jan-23	29-Jan-23
P08-EF	Submitting Vendor Data Book	5	0%	$618.49	30-Jan-23	03-Feb-23
P08-EF	Delivering Spare Parts	5	0%	$618.49	04-Feb-23	08-Feb-23
Power & Control Cables - BK12		74	0%	$14,930.43	13-Oct-22	25-Dec-22
P08-EF	Tendering & Selection	10	0%	$597.22	13-Oct-22	22-Oct-22
P08-EF	Contract Effectiveness / PO	5	0%	$895.83	23-Oct-22	27-Oct-22
P08-EF	Manufacturing / Fabrication / Supply	40	0%	$7,465.21	28-Oct-22	06-Dec-22
P08-EF	Final Inspection	7	0%	$1,493.04	07-Dec-22	13-Dec-22
P08-EF	Delivery On Site	7	0%	$3,732.61	14-Dec-22	20-Dec-22
P08-EF	Submitting Vendor Data Book	5	0%	$746.52	21-Dec-22	25-Dec-22
UPS System - BK12		106	0%	$16,190.12	20-Jul-22	02-Nov-22
P08-EF	Tendering & Selection	7	0%	$647.60	20-Jul-22	26-Jul-22
P08-EF	Contract Effectiveness / PO	5	0%	$971.41	27-Jul-22	31-Jul-22
P08-EF	Manufacturing / Fabrication / Supply	70	0%	$8,095.06	01-Aug-22	09-Oct-22
P08-EF	Final Inspection	7	0%	$1,619.01	10-Oct-22	16-Oct-22
P08-EF	Delivery On Site	7	0%	$3,238.02	17-Oct-22	23-Oct-22
P08-EF	Submitting Vendor Data Book	5	0%	$809.51	24-Oct-22	28-Oct-22
P08-EF	Delivering Spare Parts	5	0%	$809.51	29-Oct-22	02-Nov-22
Earthing & Lightning System - BK12		74	0%	$9,829.71	02-Jul-22	13-Sep-22
P08-EF	Tendering & Selection	5	0%	$393.19	02-Jul-22	06-Jul-22
P08-EF	Contract Effectiveness / PO	5	0%	$589.78	07-Jul-22	11-Jul-22
P08-EF	Manufacturing / Fabrication / Supply	40	0%	$4,914.86	12-Jul-22	20-Aug-22
P08-EF	Final Inspection	7	0%	$982.97	21-Aug-22	27-Aug-22
P08-EF	Delivery On Site	7	0%	$1,965.94	28-Aug-22	03-Sep-22
P08-EF	Submitting Vendor Data Book	5	0%	$491.49	04-Sep-22	08-Sep-22
P08-EF	Delivering Spare Parts	5	0%	$491.49	09-Sep-22	13-Sep-22
Construction		429	0%	$137,083.00	12-Jun-22	14-Aug-23
Wellpad and Access Road		112	0%	$41,124.90	12-Jun-22	01-Oct-22
Access Road		53	0%	$14,393.72	12-Jun-22	03-Aug-22
Wellpad Access Road		53	0%	$12,954.34	12-Jun-22	03-Aug-22
P08-E	Access Road Preparation	10	0%	$7,772.61	12-Jun-22	21-Jun-22
P08-E	Filling and Compaction	5	0%	$647.72	25-Jul-22	29-Jul-22
P08-E	Sub-Base Layer	5	0%	$1,295.43	30-Jul-22	03-Aug-22
Retaining wall		22	0%	$2,590.87	22-Jun-22	13-Jul-22
P08-	Excavation	10	0%	$259.09	22-Jun-22	01-Jul-22
P08-	lean concrete	5	0%	$388.63	02-Jul-22	06-Jul-22
P08-	form working	2	0%	$906.80	07-Jul-22	08-Jul-22
P08-	concrete pouring	5	0%	$1,036.35	09-Jul-22	13-Jul-22

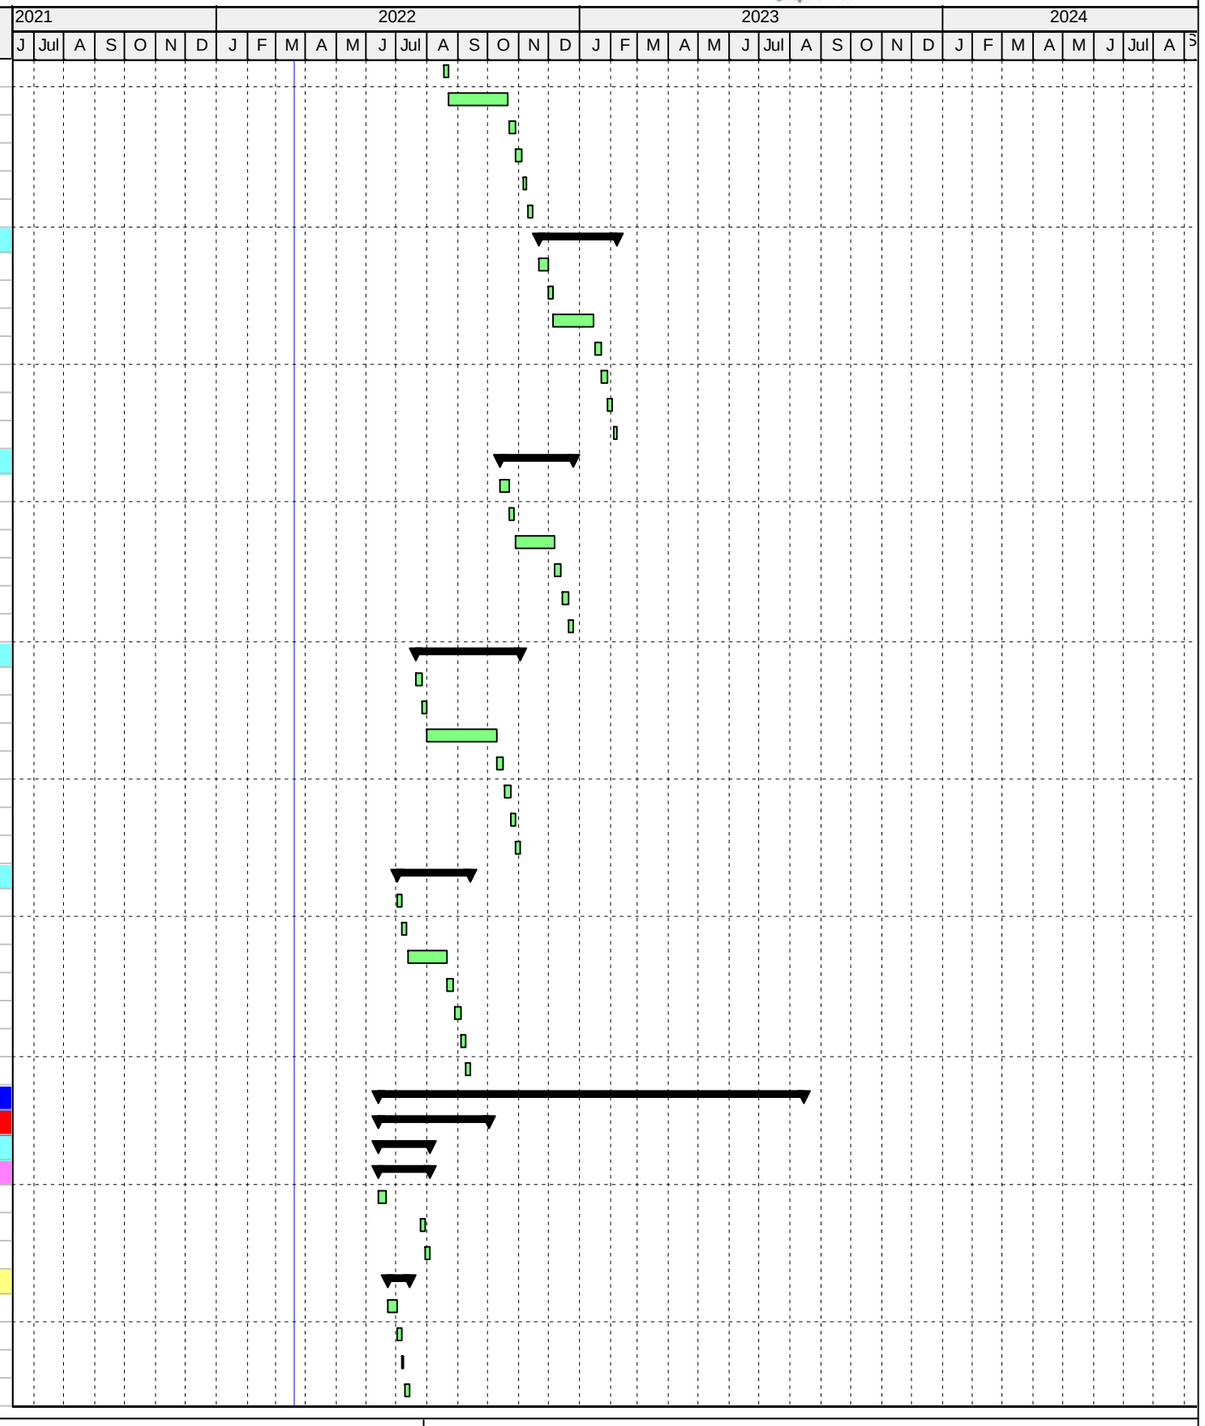

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Construction of Culvert and Bridge		33	0%	$647.72	22-Jun-22	24-Jul-22
bridge		33	0%	$259.09	22-Jun-22	24-Jul-22
P08	Excavation	10	0%	$25.91	22-Jun-22	01-Jul-22
P08	lean concrete	2	0%	$20.73	02-Jul-22	03-Jul-22
P08	wall	3	0%	$46.64	04-Jul-22	06-Jul-22
P08	reinforcement	3	0%	$51.82	06-Jul-22	08-Jul-22
P08	form working	2	0%	$25.91	09-Jul-22	10-Jul-22
P08	concrete pouring	5	0%	$77.73	11-Jul-22	15-Jul-22
P08	protect stone	3	0%	$5.18	16-Jul-22	18-Jul-22
P08	Backfill	6	0%	$5.18	19-Jul-22	24-Jul-22
culverts		19	0%	$388.63	22-Jun-22	10-Jul-22
P08	pipeway culvert	8	0%	$155.45	22-Jun-22	29-Jun-22
P08	pipeway	4	0%	$116.59	30-Jun-22	03-Jul-22
P08	pipeline culvert	7	0%	$116.59	03-Jul-22	10-Jul-22
Burn Pit Access Road		17	0%	$1,439.37	29-Jun-22	16-Jul-22
P08-E	ROW Preparation	10	0%	$791.65	29-Jun-22	09-Jul-22
P08-E	Filling and Compaction	5	0%	$287.87	09-Jul-22	14-Jul-22
P08-E	Sub-Base Layer	2	0%	$359.84	14-Jul-22	16-Jul-22
Wellpad		112	0%	$26,731.19	12-Jun-22	01-Oct-22
Water Supply		25	0%	$1,871.18	12-Jun-22	06-Jul-22
P08-E	Water Supply	25	0%	$1,871.18	12-Jun-22	06-Jul-22
Demolition & Disassemble		9	0%	$4,009.68	12-Jul-22	20-Jul-22
P08-E	Demolition of concrete Well Pad	5	0%	$1,202.90	12-Jul-22	16-Jul-22
P08-E	Fence Disassmble	4	0%	$2,806.77	17-Jul-22	20-Jul-22
Site Preparation		20	0%	$4,009.68	22-Jun-22	11-Jul-22
P08-E	Site Preparation #12	20	0%	$4,009.68	22-Jun-22	11-Jul-22
Surface Preparation		4	0%	$1,069.25	14-Aug-22	18-Aug-22
P08-E	Gravel Paving	4	0%	$1,069.25	14-Aug-22	18-Aug-22
Civil Work		34	0%	$6,682.80	12-Jul-22	14-Aug-22
P08-E	Excavation and Soil Removal (Cellar)	15	0%	$4,343.82	12-Jul-22	26-Jul-22
P08-E	Installation of Conductor Pipe	15	0%	$400.97	12-Jul-22	26-Jul-22
P08-E	Form Work (Above Cellar)	9	0%	$267.31	27-Jul-22	04-Aug-22
P08-E	Armed Concrete	10	0%	$1,670.70	04-Aug-22	14-Aug-22
Mud Channel		15	0%	$801.94	12-Jul-22	26-Jul-22
P08-E	Excavation & Repair	15	0%	$801.94	12-Jul-22	26-Jul-22
Mud Pit		30	0%	$4,009.68	27-Jul-22	25-Aug-22
P08-E	Soil Removal, Filling and Compaction of Mud Pit Area	15	0%	$1,403.39	27-Jul-22	10-Aug-22
P08-E	Construction of Mud Pit's Walls	19	0%	$801.94	01-Aug-22	19-Aug-22
P08-E	Supply & Installation sealling Layer	6	0%	$1,804.35	19-Aug-22	25-Aug-22
SepticTank		60	0%	$1,871.18	27-Jul-22	24-Sep-22
P08-E	Excavation & Soil Transfer	20	0%	$561.35	27-Jul-22	15-Aug-22
P08-E	Levelling	15	0%	$9.36	16-Aug-22	30-Aug-22
P08-E	Tank Supply	20	0%	$1,066.57	27-Jul-22	15-Aug-22
P08-E	Tank Execution	15	0%	$177.76	31-Aug-22	14-Sep-22
P08-E	Backfilling & Compaction	10	0%	$56.14	15-Sep-22	24-Sep-22
Burn Pit		80	0%	$1,069.25	14-Jul-22	01-Oct-22
P08-E	Soil Removal, Triming ,Filling and Compaction of Burn Pit Are	30	0%	$855.40	14-Jul-22	13-Aug-22
P08-E	Construction & Installation of Support	35	0%	$53.46	14-Jul-22	18-Aug-22
P08-E	Welding, Installation and Testing	7	0%	$160.39	25-Sep-22	01-Oct-22
Gasoil Pad		15	0%	$1,336.56	28-Jul-22	12-Aug-22



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P08-E	Excavation	5	0%	$267.31	28-Jul-22	02-Aug-22
P08-E	lean concrete	2	0%	$400.97	02-Aug-22	04-Aug-22
P08-E	Form work	3	0%	$133.66	04-Aug-22	07-Aug-22
P08-E	Armed Concrete	5	0%	$534.62	07-Aug-22	12-Aug-22
Wellhead Facility and Flowline		171	0%	$93,901.86	01-Dec-22	20-May-23
Civil, Structure & Architecture		131	0%	$32,865.65	01-Dec-22	10-Apr-23
Civil Works		54	0%	$6,901.79	01-Dec-22	23-Jan-23
P08-E	Steel Works(Wellhead Facilities)	10	0%	$3,105.80	07-Jan-23	16-Jan-23
P08-E	Out Door Post Works For New Gantry (Fundation, Fencing .	7	0%	$1,725.45	17-Jan-23	23-Jan-23
P08-E	Out Door Post Works For Wellhead Post (Fundation, Fencinç	12	0%	$1,725.45	01-Dec-22	12-Dec-22
P08-E	Well Pad Fencing	12	0%	$345.09	01-Dec-22	12-Dec-22
Buildings		131	0%	$20,048.05	01-Dec-22	10-Apr-23
Construction of Guard House		52	0%	$5,613.45	01-Dec-22	21-Jan-23
Foundation		29	0%	$1,740.17	01-Dec-22	29-Dec-22
P08	Excavation & Soil Transfer (Removing of Vegetal Soil)	2	0%	$348.03	01-Dec-22	02-Dec-22
P08	Levelling	5	0%	$34.80	03-Dec-22	07-Dec-22
P08	Lean Concrete	2	0%	$174.02	08-Dec-22	09-Dec-22
P08	Reinforced Work	5	0%	$348.03	10-Dec-22	14-Dec-22
P08	Formwork	4	0%	$139.21	15-Dec-22	18-Dec-22
P08	Main Concrete Pouring	5	0%	$678.67	18-Dec-22	23-Dec-22
P08	Backfilling & Compaction	6	0%	$17.40	23-Dec-22	29-Dec-22
Structure		20	0%	$2,245.38	09-Dec-22	28-Dec-22
P08	Steel Material Supply	5	0%	$1,122.69	09-Dec-22	13-Dec-22
P08	Shop Fabrication of Steel Structure	7	0%	$449.08	14-Dec-22	20-Dec-22
P08	Structural Installation	5	0%	$449.08	21-Dec-22	25-Dec-22
P08	Structural Painting	3	0%	$224.54	26-Dec-22	28-Dec-22
Architectural		21	0%	$1,627.90	01-Jan-23	21-Jan-23
P08	Wall Execution	5	0%	$795.56	01-Jan-23	05-Jan-23
P08	Roof Covering	4	0%	$193.72	06-Jan-23	09-Jan-23
P08	Roof Execution (Block Joist, Concrete Pouring)	4	0%	$247.12	10-Jan-23	13-Jan-23
P08	Building Walkway (around Building)	5	0%	$83.67	14-Jan-23	18-Jan-23
P08	Joinery (Cornice, Faï?½ade, Plaster)	3	0%	$307.84	19-Jan-23	21-Jan-23
Construction of Switchgear		131	0%	$14,434.59	01-Dec-22	10-Apr-23
Foundation		26	0%	$4,474.72	01-Dec-22	26-Dec-22
P08	Excavation & Soil Transfer (Removing of Vegetal Soil)	2	0%	$894.94	01-Dec-22	02-Dec-22
P08	Levelling	6	0%	$89.49	03-Dec-22	09-Dec-22
P08	Lean Concrete	2	0%	$447.47	09-Dec-22	11-Dec-22
P08	Reinforced Work	5	0%	$894.94	11-Dec-22	16-Dec-22
P08	Formwork	4	0%	$357.98	16-Dec-22	19-Dec-22
P08	Main Concrete Pouring	5	0%	$1,745.14	20-Dec-22	24-Dec-22
P08	Backfilling & Compaction	2	0%	$44.75	25-Dec-22	26-Dec-22
Structure		17	0%	$5,773.84	09-Dec-22	25-Dec-22
P08	Steel Material Supply	5	0%	$2,886.92	09-Dec-22	13-Dec-22
P08	Shop Fabrication of Steel Structure	5	0%	$1,154.77	14-Dec-22	18-Dec-22
P08	Structural Installation	5	0%	$1,154.77	19-Dec-22	23-Dec-22
P08	Structural Painting	2	0%	$577.38	24-Dec-22	25-Dec-22
Architectural		106	0%	$4,186.03	26-Dec-22	10-Apr-23
P08	Wall Execution	4	0%	$2,045.71	26-Dec-22	29-Dec-22
P08	Roof Covering	3	0%	$498.14	30-Dec-22	01-Jan-23




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P08	Roof Execution (Block Joist, Concrete Pouring)	3	0%	$635.44	02-Jan-23	04-Jan-23
P08	Building Walkway (around Building)	3	0%	$215.16	05-Jan-23	07-Jan-23
P08	Joinery (Cornice, Faï?½ade, Plaster)	2	0%	$791.58	09-Apr-23	10-Apr-23
Shelters		17	0%	$5,915.82	17-Jan-23	02-Feb-23
Diesel Generator Shelter		17	0%	$4,850.97	17-Jan-23	02-Feb-23
P08-	Fabrication	10	0%	$3,395.68	17-Jan-23	26-Jan-23
P08-	Installation	7	0%	$1,455.29	27-Jan-23	02-Feb-23
Fire Fighting Shelter		17	0%	$1,064.85	17-Jan-23	02-Feb-23
P08-	Fabrication	10	0%	$745.39	17-Jan-23	26-Jan-23
P08-	Installation	7	0%	$319.45	27-Jan-23	02-Feb-23
Piping		25	0%	$9,390.19	01-Dec-22	25-Dec-22
P08-EF	Sweep Bend Installation	7	0%	$469.51	01-Dec-22	07-Dec-22
P08-EF	Piping Work (Fit up, Welding, NDT…)	15	0%	$3,756.07	01-Dec-22	15-Dec-22
P08-EF	Valves, Fitting and Spools Installation and Hydrotest	10	0%	$5,164.60	16-Dec-22	25-Dec-22
Instrument Works		7	0%	$0.00	11-Apr-23	17-Apr-23
P08-EF	Devices Installation and Piping Connecton	7	0%	$0.00	11-Apr-23	17-Apr-23
Mechanical		7	0%	$9,390.19	27-Jan-23	02-Feb-23
P08-EF	Fuel Oil Storage Drum	7	0%	$4,695.09	27-Jan-23	02-Feb-23
P08-EF	Potable Water Tank	7	0%	$4,695.09	27-Jan-23	02-Feb-23
Electrical		138	0%	$40,377.80	01-Dec-22	17-Apr-23
P08-EF	Over Head line	15	0%	$21,400.23	01-Dec-22	15-Dec-22
P08-EF	Wellhead Electrical Equipment	7	0%	$12,113.34	11-Apr-23	17-Apr-23
P08-EF	Outdoor Post (Wellhead Post)	10	0%	$6,864.23	13-Dec-22	22-Dec-22
Pre-commissioning		7	0%	$1,878.04	14-May-23	20-May-23
P08-EF	Pre-commissioning	7	0%	$1,690.23	14-May-23	20-May-23
P08-EF	Ready for Comm.Certificate(RFCC)	5	0%	$187.80	14-May-23	19-May-23
Job Site HSE Supervision (Surface)		200	0%	$274.17	12-Jun-22	28-Dec-22
P08-EP	Job Site HSE Supervision (Surface)	200	0%	$274.17	12-Jun-22	28-Dec-22
Commissioning, Startup & Handover		87	0%	$1,782.08	19-May-23	14-Aug-23
Commissioning		32	0%	$534.62	19-May-23	20-Jun-23
P08-EF	Materials & Utilities Ready for Commissioning	3	0%	$26.73	19-May-23	22-May-23
P08-EF	Receiving Facilities Ready for Commissioning	2	0%	$26.73	22-May-23	24-May-23
P08-EF	Permits Obtained for Commissioning	10	0%	$26.73	24-May-23	03-Jun-23
P08-EF	Integrated Commissioning	2	0%	$427.70	03-Jun-23	05-Jun-23
P08-EF	Ready for Startup Certificate (RFSU)	15	0%	$26.73	05-Jun-23	20-Jun-23
Startup & Performance Test		18	0%	$712.83	20-Jun-23	08-Jul-23
P08-EF	Startup & Performance Test Run	3	0%	$570.27	20-Jun-23	23-Jun-23
P08-EF	Start of Production (SOP)	15	0%	$142.57	23-Jun-23	08-Jul-23
Handover		37	0%	$534.62	08-Jul-23	14-Aug-23
P08-EF	Compiling & Submitting Final Documentation	20	0%	$160.39	08-Jul-23	28-Jul-23
P08-EF	Training of Operator's Personnel	2	0%	$213.85	28-Jul-23	30-Jul-23
P08-EF	Provisional Acceptance Certificate (PAC)	15	0%	$160.39	30-Jul-23	14-Aug-23
Package 09-Workover # 15		499	0.44%	$613,274.00	24-Jul-21 A	31-Jul-23
ENGINEERING		439	20.11%	$13,382.00	24-Jul-21 A	12-May-23
Basic Design Endorsement		30	100%	$669.10	31-Jul-21 A	20-Mar-22
P09-EP	Endorsement Report For Basic Design & Scope of Work	30	100%	$669.10	31-Jul-21 A	20-Mar-22
Value Engineering		44	60%	$401.46	01-Feb-22	20-Mar-22
P09-EP	Value Engineering Study Report	44	60%	$401.46	01-Feb-22	20-Mar-22
Detail Design		439	24.21%	$7,360.10	24-Jul-21 A	25-Nov-22
Process		109	65%	$350.34	15-Nov-21	05-Aug-22

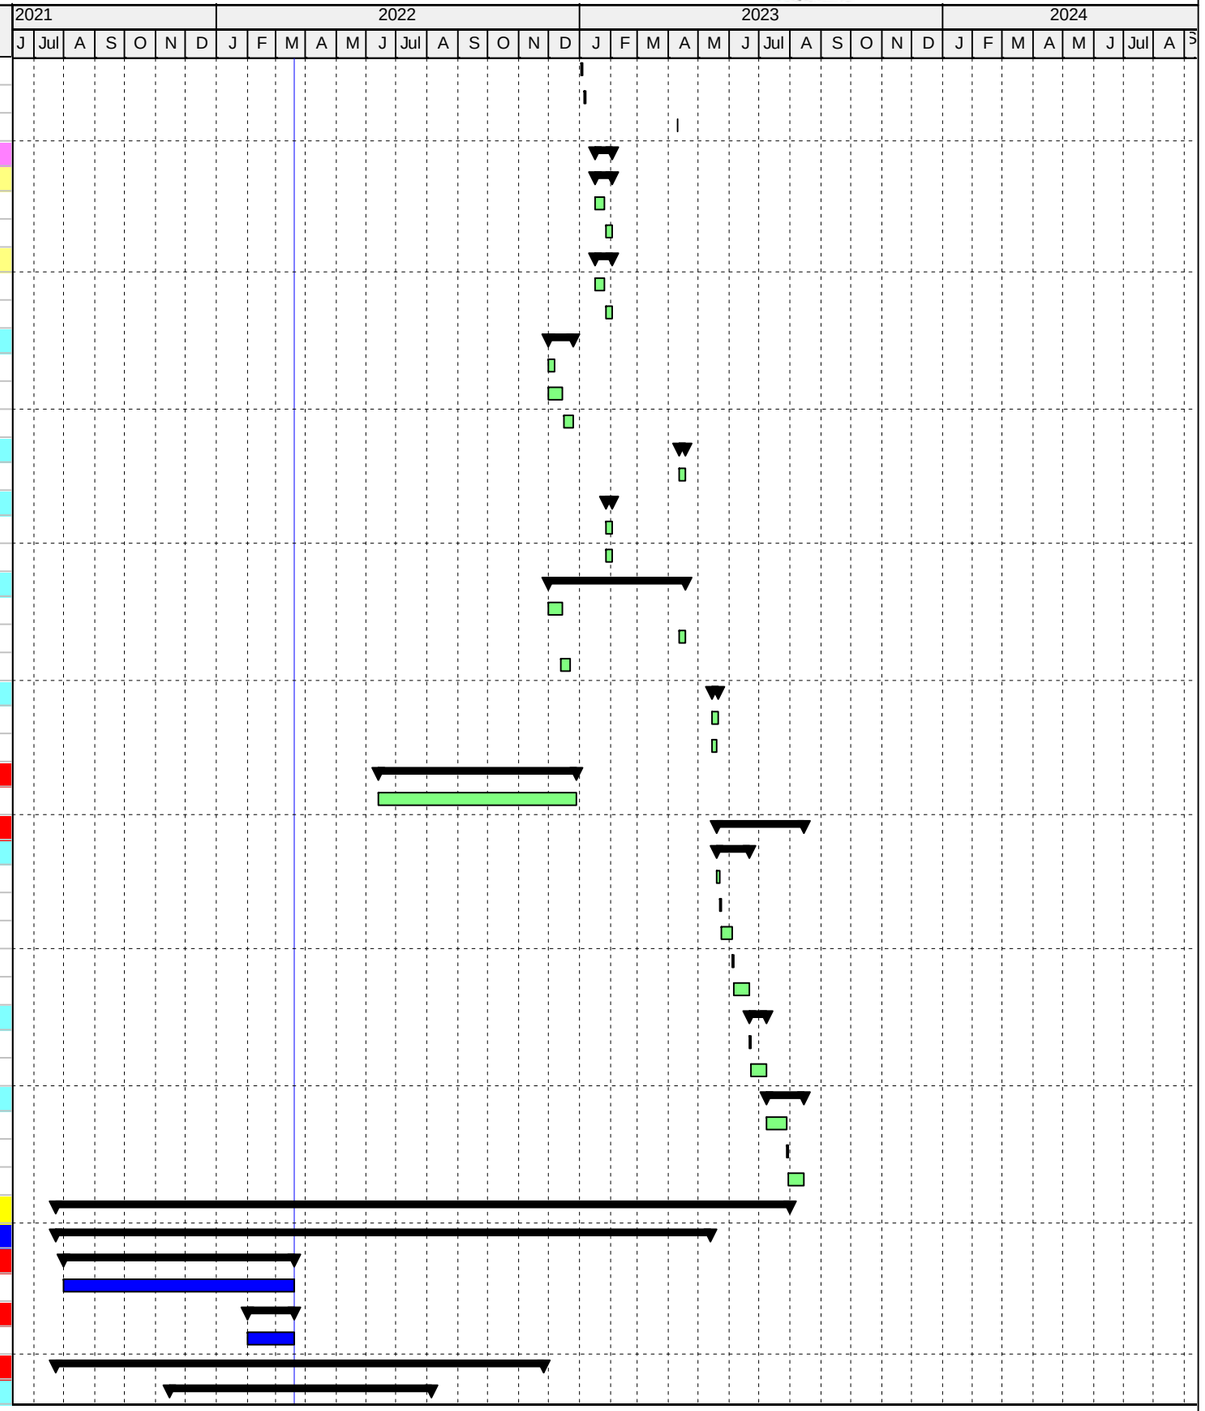


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Drawing/Diagram		44	80%	$245.24	15-Nov-21	02-May-22
P09-E	P&ID for Diesel Oil Drum- BK15	44	80%	$122.62	15-Nov-21	02-May-22
P09-E	P&ID for Potable Water Tank - BK15	44	80%	$122.62	15-Nov-21	02-May-22
List		44	60%	$52.55	27-Feb-22	02-May-22
P09-E	Line List - BK15	44	60%	$52.55	27-Feb-22	02-May-22
Data Sheet		95	0%	$52.55	03-May-22	05-Aug-22
P09-E	Process Data Sheets For Instrument Devices - BK15	36	0%	$17.87	03-May-22	07-Jun-22
P09-E	Process Data Sheets For Fuel Oil Storage Drum of Well Pads	55	0%	$17.34	12-Jun-22	05-Aug-22
P09-E	Process Data Sheets For Potable Water Tank of Well Pads	45	0%	$17.34	17-Jun-22	31-Jul-22
Mechanical		114	77.78%	$490.92	28-Jul-21 A	26-Jun-22
Basis/Criteria		54	60%	$54.54	28-Jul-21 A	12-May-22
P09-E	Mechanical Design Criteria	54	60%	$54.54	28-Jul-21 A	12-May-22
Specification		79	60%	$81.84	28-Jul-21 A	26-Jun-22
P09-E	Specification For Pressure Vessels	54	60%	$40.92	28-Jul-21 A	01-Jun-22
P09-E	Specification For Atmospheric Above Ground Welded Steel Ta	79	60%	$40.92	28-Jul-21 A	26-Jun-22
Data Sheets		74	60%	$136.38	16-Jan-22	16-Jun-22
P09-E	Data Sheets For Fuel Oil Storage Drum of Well Pads	64	60%	$68.19	16-Jan-22	11-Jun-22
P09-E	Data Sheets For Potable Water Tank of Well Pads	64	60%	$68.19	09-Feb-22	16-Jun-22
Drawing/Diagram		34	100%	$218.16	28-Jul-21 A	09-Apr-22
P09-E	Standard Detail Drawing For Pressure Vessels and Heat Exch	14	100%	$109.08	28-Jul-21 A	09-Apr-22
P09-E	Standard Detail Drawing For Storage Tanks	14	100%	$109.08	28-Jul-21 A	09-Apr-22
HVAC/Plumbing		402	5.17%	$420.26	24-Jul-21 A	19-Nov-22
Basis/Criteria		64	100%	$6.09	24-Jul-21 A	14-May-22
P09-E	HVAC & Plumbing Design Criteria	64	100%	$6.09	24-Jul-21 A	14-May-22
Specification		64	100%	$9.75	24-Jul-21 A	27-Mar-22
P09-E	Specification For HVAC Equipment	64	100%	$6.09	24-Jul-21 A	27-Mar-22
P09-E	Specification For Duct Work & Pipe Work	64	100%	$3.66	24-Jul-21 A	27-Mar-22
Calculation		96	0%	$97.46	13-May-22	16-Aug-22
P09-E	HVAC Calculation Note For Switchgear Building - BK15	44	0%	$48.73	04-Jul-22	16-Aug-22
P09-E	HVAC Calculation Note For Security Building - BK15	44	0%	$48.73	13-May-22	25-Jun-22
Data Sheets		44	0%	$48.71	30-Sep-22	12-Nov-22
P09-E	Data Sheets For Main HVAC Equipment - BK15	44	0%	$48.71	30-Sep-22	12-Nov-22
Drawing/Diagram		198	2.82%	$209.54	24-Jul-21 A	12-Nov-22
P09-E	Standard Drawing For HVAC & Plumbing	14	100%	$4.67	24-Jul-21 A	30-Mar-22
P09-E	Symbol & Legend For HVAC & Plumbing	48	60%	$2.03	22-Aug-21	16-May-22
P09-E	HVAC System Layout For Switchgear Building - BK15	44	0%	$50.71	17-Aug-22	29-Sep-22
P09-E	HVAC System Layout For Security Building - BK15	44	0%	$50.71	26-Jun-22	08-Aug-22
P09-E	Plumbing & Sewage Piping Layout For Switchgear Building - I	44	0%	$50.71	30-Sep-22	12-Nov-22
P09-E	Plumbing & Sewage Piping Layout For Security Building - BK	44	0%	$50.71	09-Aug-22	21-Sep-22
MTO		7	0%	$48.71	13-Nov-22	19-Nov-22
P09-E	MTO For Building HVAC & Plumbing Systems - BK15	7	0%	$48.71	13-Nov-22	19-Nov-22
Piping		67	59.5%	$350.34	24-Jul-21 A	24-Jun-22
Basis/Criteria		39	100%	$7.01	24-Jul-21 A	20-Mar-22
P09-E	Piping Design Criteria	39	100%	$7.01	24-Jul-21 A	20-Mar-22
Specification		45	72.38%	$133.13	24-Jul-21 A	04-May-22
P09-E	Specification For Color Coding and Marking	39	60%	$9.71	09-Aug-21	01-May-22
P09-E	Specification For Transportation, Handling, Storage of pipes	39	80%	$10.58	12-Dec-21	01-May-22
P09-E	Specification For the Design of Piping in Mechanical Packages	39	60%	$9.71	09-Aug-21	01-May-22
P09-E	Specification For Metallic Pipes	39	80%	$9.71	24-Jul-21 A	01-May-22
P09-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$9.71	24-Jul-21 A	24-Mar-22

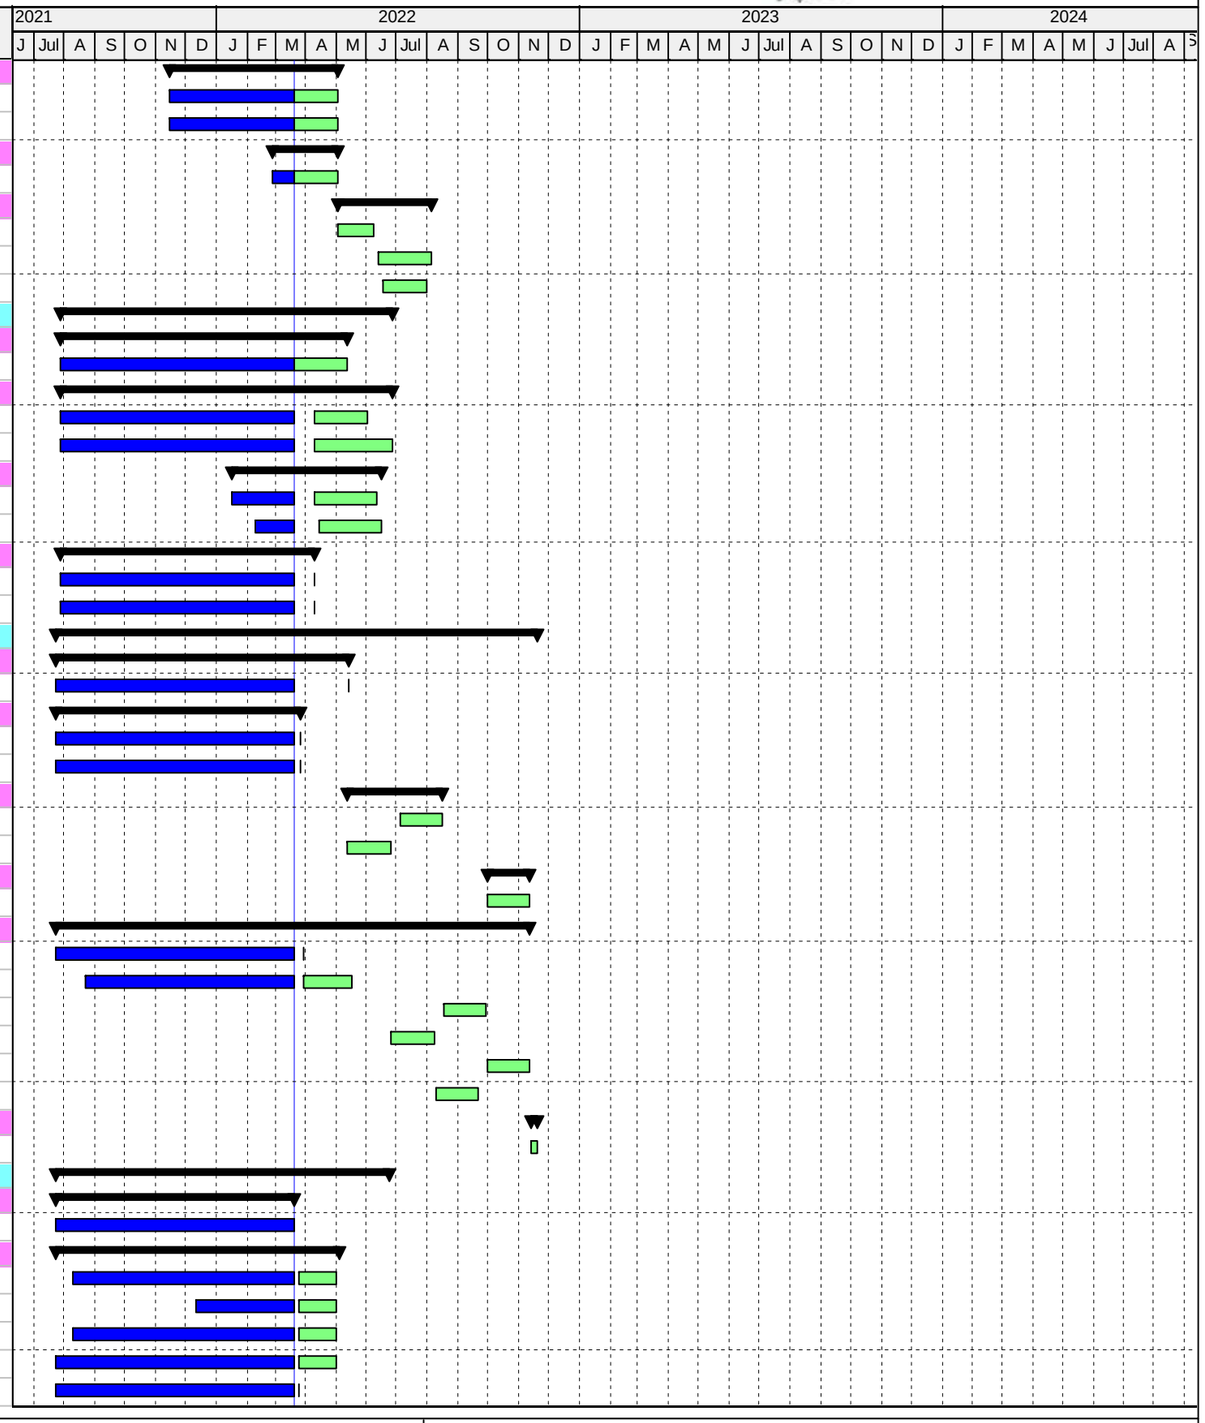


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P09-E	Specification For Painting	39	100%	$11.65	24-Jul-21 A	27-Mar-22
P09-E	Specification For Lining (Internal Protection of Equipment by F	39	60%	$9.71	09-Aug-21	04-May-22
P09-E	Specification For Material Requirements in Sour service	39	60%	$9.71	09-Aug-21	04-May-22
P09-E	Specification For Manual Valves	39	60%	$9.71	09-Aug-21	04-May-22
P09-E	Specification For Plant Piping Systems Pressure Testing	39	60%	$9.71	09-Aug-21	04-May-22
P09-E	Specification For Welding of Plant Piping System	39	60%	$10.58	09-Aug-21	04-May-22
P09-E	Specification For Flexibility Analysis	39	60%	$12.97	09-Aug-21	04-May-22
P09-E	Specification For Piping Cleaning and Flushing	39	100%	$9.71	24-Aug-21	30-Mar-22
Drawing/Diagram		14	100%	$105.10	19-Feb-22	20-Mar-22
P09-E	Standard Pipe Support Drawings	14	100%	$105.10	19-Feb-22	20-Mar-22
MTO		7	0%	$105.10	18-Jun-22	24-Jun-22
P09-E	MTO For Pipes - BK15	7	0%	$105.10	18-Jun-22	24-Jun-22
Electrical		247	24.7%	$1,780.41	24-Jul-21 A	25-Nov-22
Basis/Criteria		54	100%	$10.15	03-Aug-21	20-Mar-22
P09-E	Electrical System Design Criteria	54	100%	$10.15	03-Aug-21	20-Mar-22
Specification		55	100%	$119.82	24-Jul-21 A	30-Mar-22
P09-E	Specification For LV Switchgear & Motor Control Centers	49	100%	$6.21	24-Jul-21 A	24-Mar-22
P09-E	Specification For MV Switchgear	49	100%	$7.12	24-Jul-21 A	24-Mar-22
P09-E	Specification For UPS System	49	100%	$7.12	04-Aug-21	24-Mar-22
P09-E	Specification For Transformers	49	100%	$7.12	24-Jul-21 A	24-Mar-22
P09-E	Specification For DC Charger	49	100%	$7.12	04-Aug-21	24-Mar-22
P09-E	Specification For Earthing & Lightning System	49	100%	$4.53	28-Jul-21 A	24-Mar-22
P09-E	Specification For Lighting & Small Power System	49	100%	$6.22	28-Jul-21 A	27-Mar-22
P09-E	Specification For Bulk Materials	49	100%	$6.22	24-Jul-21 A	27-Mar-22
P09-E	Specification For Diesel Generator	49	100%	$7.12	28-Jul-21 A	27-Mar-22
P09-E	Specification For LV Induction Motors	49	100%	$6.52	24-Jul-21 A	27-Mar-22
P09-E	Specification For Electrical Requirements of Packaged Units	49	100%	$7.12	28-Jul-21 A	27-Mar-22
P09-E	Specification For Capacitor Bank	49	100%	$7.12	24-Jul-21 A	27-Mar-22
P09-E	Specification For Distribution & Lighting Panels	49	100%	$7.12	28-Jul-21 A	30-Mar-22
P09-E	Specification For Power & Control Cables	49	100%	$6.22	24-Jul-21 A	30-Mar-22
P09-E	Specification For Cathodic Protection System	49	100%	$6.22	31-Jul-21 A	30-Mar-22
P09-E	Specification For MV Induction Motors	49	100%	$6.52	24-Jul-21 A	30-Mar-22
P09-E	Specification For NGR	49	100%	$7.12	24-Jul-21 A	30-Mar-22
P09-E	Specification For Overhead Transmission Lines	49	100%	$7.12	28-Jul-21 A	30-Mar-22
Calculation		139	40.68%	$196.38	11-Oct-21 A	25-Jun-22
P09-E	Calculation Note For Lighting System of Well Pads Switchgea	55	0%	$14.49	27-Apr-22	20-Jun-22
P09-E	Calculation Note For Lighting System of Well Pads Security B	55	0%	$14.49	27-Apr-22	20-Jun-22
P09-E	Calculation Note For Lighting System of Well Pads Area	60	0%	$19.34	27-Apr-22	25-Jun-22
P09-E	Calculation Note For Cable Sizing of Well Pads	60	80%	$19.34	02-Nov-21	28-May-22
P09-E	Calculation Note For UPS System of Well Pads	60	0%	$19.34	24-Mar-22	22-May-22
P09-E	Calculation Note For Earthing & Lightning System of Well Pac	60	0%	$19.34	24-Mar-22	22-May-22
P09-E	Calculation Note For Diesel Generator Sizing of Well Pads	55	60%	$14.49	26-Jan-22	20-May-22
P09-E	Calculation Note For DC Charger of Well Pads	60	80%	$19.34	26-Jan-22	22-May-22
P09-E	Calculation Note For LV Capacitor Bank of Well Pads	40	60%	$23.55	29-Jan-22	05-May-22
P09-E	Calculation Note For 11 KV Over Head Line Sag and Tension	40	80%	$16.32	13-Oct-21	08-May-22
P09-E	Calculation Note For 33 KV Over Head Line Sag and Tension	40	80%	$16.32	11-Oct-21 A	08-May-22
Data Sheets		198	42.89%	$166.47	12-Sep-21	31-Jul-22
P09-E	Data Sheets For UPS of Well Pads	59	0%	$14.28	23-May-22	20-Jul-22
P09-E	Data Sheets For DC Charger of Well Pads	59	80%	$14.28	29-Jan-22	22-May-22

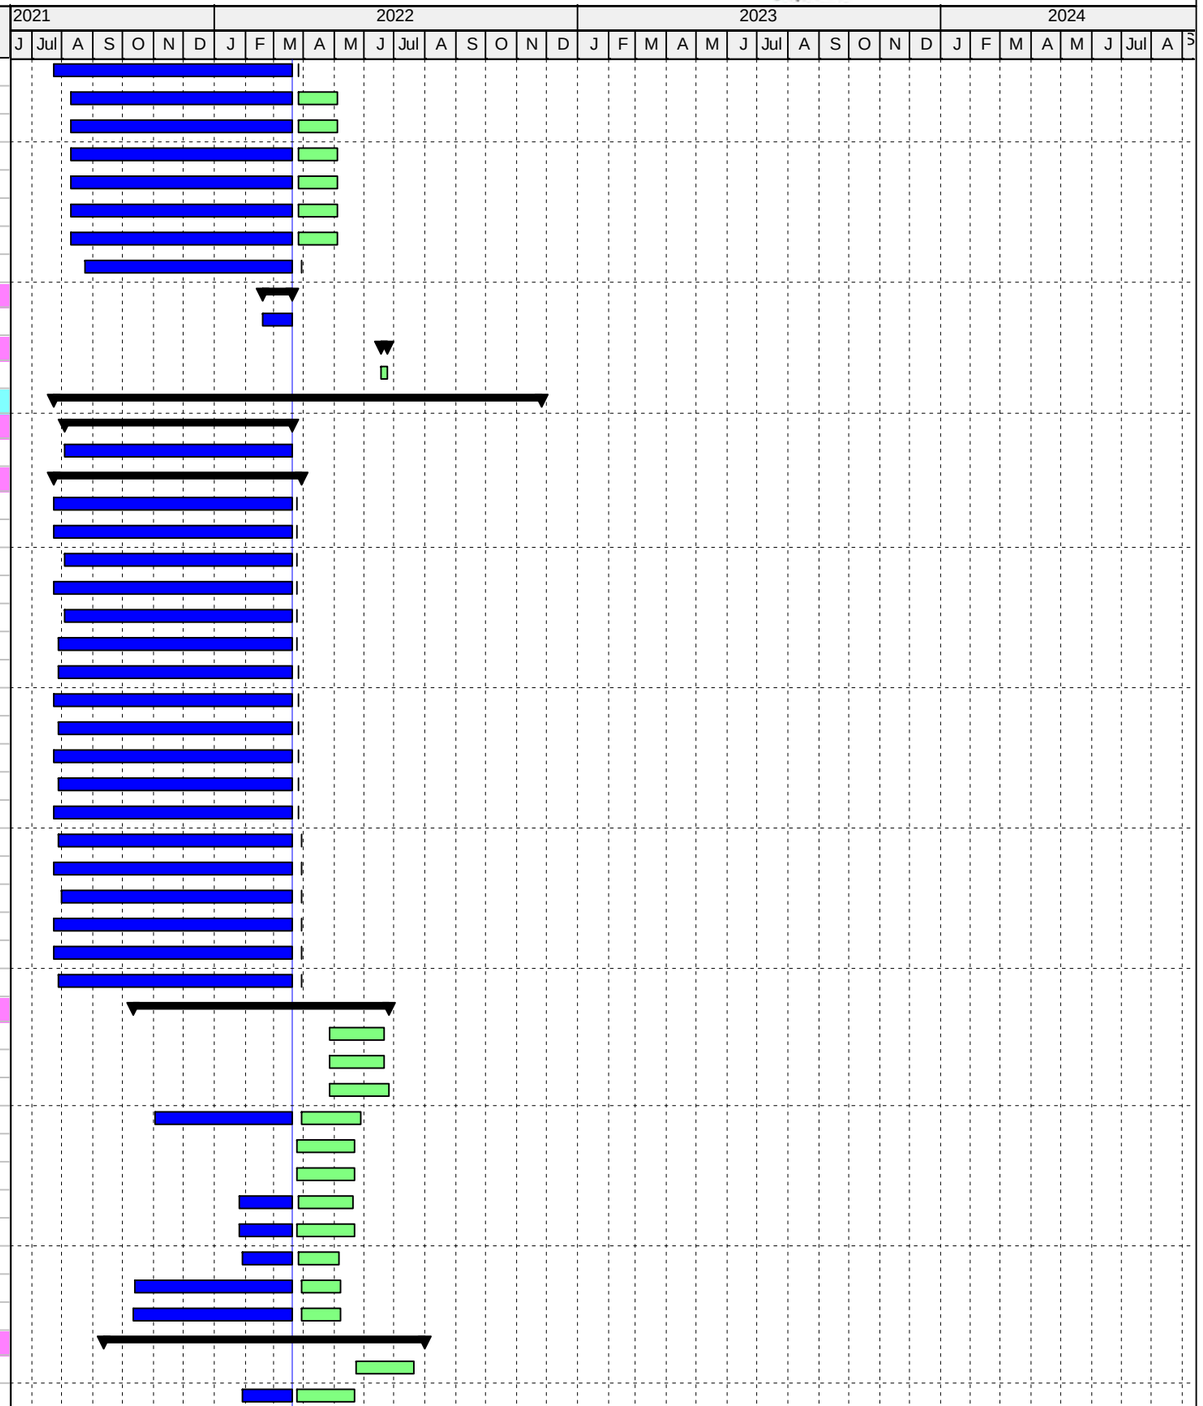


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P09-E	Data Sheets For Diesel Generator of Well Pads	59	60%	$14.28	20-Sep-21	20-May-22
P09-E	Data Sheets For LV Capacitor Bank of Well Pads	59	80%	$14.28	12-Sep-21	17-May-22
P09-E	Data Sheets For LV Switchgear of Well Pads	54	60%	$14.28	19-Feb-22	12-May-22
P09-E	Data Sheets For Power & Control Cables of Well Pads	59	80%	$14.28	13-Sep-21	27-May-22
P09-E	Data Sheets For Power Transformers of Well Pads	59	80%	$14.28	15-Sep-21	17-May-22
P09-E	Data Sheets For Distribution & Lighting Panels of Well Pads	59	60%	$14.28	12-Sep-21	31-Jul-22
P09-E	11KV Over Head Line Study Report	44	0%	$26.10	03-Jun-22	16-Jul-22
P09-E	33KV Over Head Line Study Report	44	0%	$26.10	03-Jun-22	16-Jul-22
Drawing/Diagram		221	29.58%	$472.34	09-Aug-21	25-Nov-22
P09-E	Electrical Legend and Symbols	49	100%	$4.06	09-Aug-21	30-Mar-22
P09-E	Typical Installation Details & Notes For Earthing and Lightning	14	100%	$12.14	25-Aug-21	30-Mar-22
P09-E	Typical Installation Details & Notes For Lighting System	14	100%	$10.77	25-Aug-21	30-Mar-22
P09-E	Typical Installation Details & Notes For Power System	14	100%	$3.59	25-Aug-21	30-Mar-22
P09-E	Installation Details & Notes For Cathodic Protection Systems	74	100%	$3.64	25-Aug-21	30-Mar-22
P09-E	Typical Installation Details For Over Head Line Equipment	14	100%	$8.08	22-Aug-21	19-Apr-22
P09-E	Installation Detail & Notes for Connection OHL to Gantries for	54	60%	$32.88	06-Mar-22	12-May-22
P09-E	Electrical Typical Schematic Diagrams For LV Panels of Well F	14	100%	$20.22	30-Aug-21	20-Mar-22
P09-E	Control Logic Diagram For LV Incomers of Well Pads	74	80%	$16.20	30-Aug-21	01-Jun-22
P09-E	Earthing Layout For Electrical Tower (Gantry) of Well Pads	64	0%	$12.14	16-Jul-22	17-Sep-22
P09-E	Cable Route Layout For Electrical Tower (Gantry) of Well Pac	74	0%	$16.20	16-Jul-22	27-Sep-22
P09-E	Overall Single Line Diagram of Well Pads	79	60%	$20.22	02-Mar-22	21-Jun-22
P09-E	Single Line Diagram For LV Switchgear of Well Pads	74	60%	$16.20	08-Feb-22	16-Jun-22
P09-E	Single Line Diagram For LV Power Distribution Panel of Well	74	0%	$16.20	04-May-22	16-Jul-22
P09-E	Single Line Diagram For DC Charger of Well Pads	74	80%	$16.20	06-Feb-22	16-Jun-22
P09-E	Single Line Diagram For Capacitor Banks of Well Pads	74	60%	$16.20	02-Feb-22	16-Jun-22
P09-E	Interconnection Wiring Diagram of Well Pads	64	0%	$24.28	04-May-22	06-Jul-22
P09-E	Area Lighting & Small Power Layout of Well Pads of Well Pad	74	0%	$16.20	16-Jul-22	27-Sep-22
P09-E	Lighting & Small Power Layout For Switchgear Building of We	64	0%	$12.14	13-May-22	15-Jul-22
P09-E	Lighting & Small Power Layout For Security Building of Well P	64	0%	$12.14	23-Sep-22	25-Nov-22
P09-E	Area Electrical Cable Route & Section Layout of Well Pads	79	0%	$20.22	16-Jul-22	02-Oct-22
P09-E	Electrical Cable Route & Section Layout For Switchgear Build	74	0%	$39.63	16-Jul-22	27-Sep-22
P09-E	Electrical Equipment Arrangement Layout For Switchgear Bui	79	0%	$24.94	13-May-22	30-Jul-22
P09-E	Earthing & Lightning Layout for well pads	64	0%	$16.34	29-May-22	31-Jul-22
P09-E	11KV Over Head Line Study Report	44	0%	$40.76	01-Aug-22	13-Sep-22
P09-E	33KV Over Head Line Study Report	44	0%	$40.76	08-Jul-22	20-Aug-22
List		113	37.67%	$49.85	25-Jan-22	22-Oct-22
P09-E	Electrical Load List of Well Pads	45	80%	$23.48	25-Jan-22	03-May-22
P09-E	Electrical Power & Control Cable List of Well Pads	74	0%	$13.19	10-Aug-22	22-Oct-22
P09-E	Cable Drum Schedule and Cutting List of Well Pads	74	0%	$13.19	10-Aug-22	22-Oct-22
Report		133	0%	$332.76	04-May-22	13-Sep-22
P09-E	Electrical Network (Load Flow, Motor Starting & Short Circuit)	54	0%	$95.24	04-May-22	26-Jun-22
P09-E	Relay Coordination & Setting Study Report of Well Pads	54	0%	$95.24	27-Jun-22	19-Aug-22
P09-E	11KV Over Head Line Study Report	44	0%	$71.14	01-Aug-22	13-Sep-22
P09-E	33KV Over Head Line Study Report	44	0%	$71.14	08-Jul-22	20-Aug-22
MTO		146	0%	$432.64	06-Jun-22	29-Oct-22
P09-E	MTO For Transmission Over Head Line - BK15	7	0%	$99.94	01-Aug-22	07-Aug-22
P09-E	MTO For Lighting & Small Powers - BK15	7	0%	$66.54	06-Jun-22	12-Jun-22
P09-E	MTO For Power & Control Cables - BK15	7	0%	$66.54	23-Oct-22	29-Oct-22

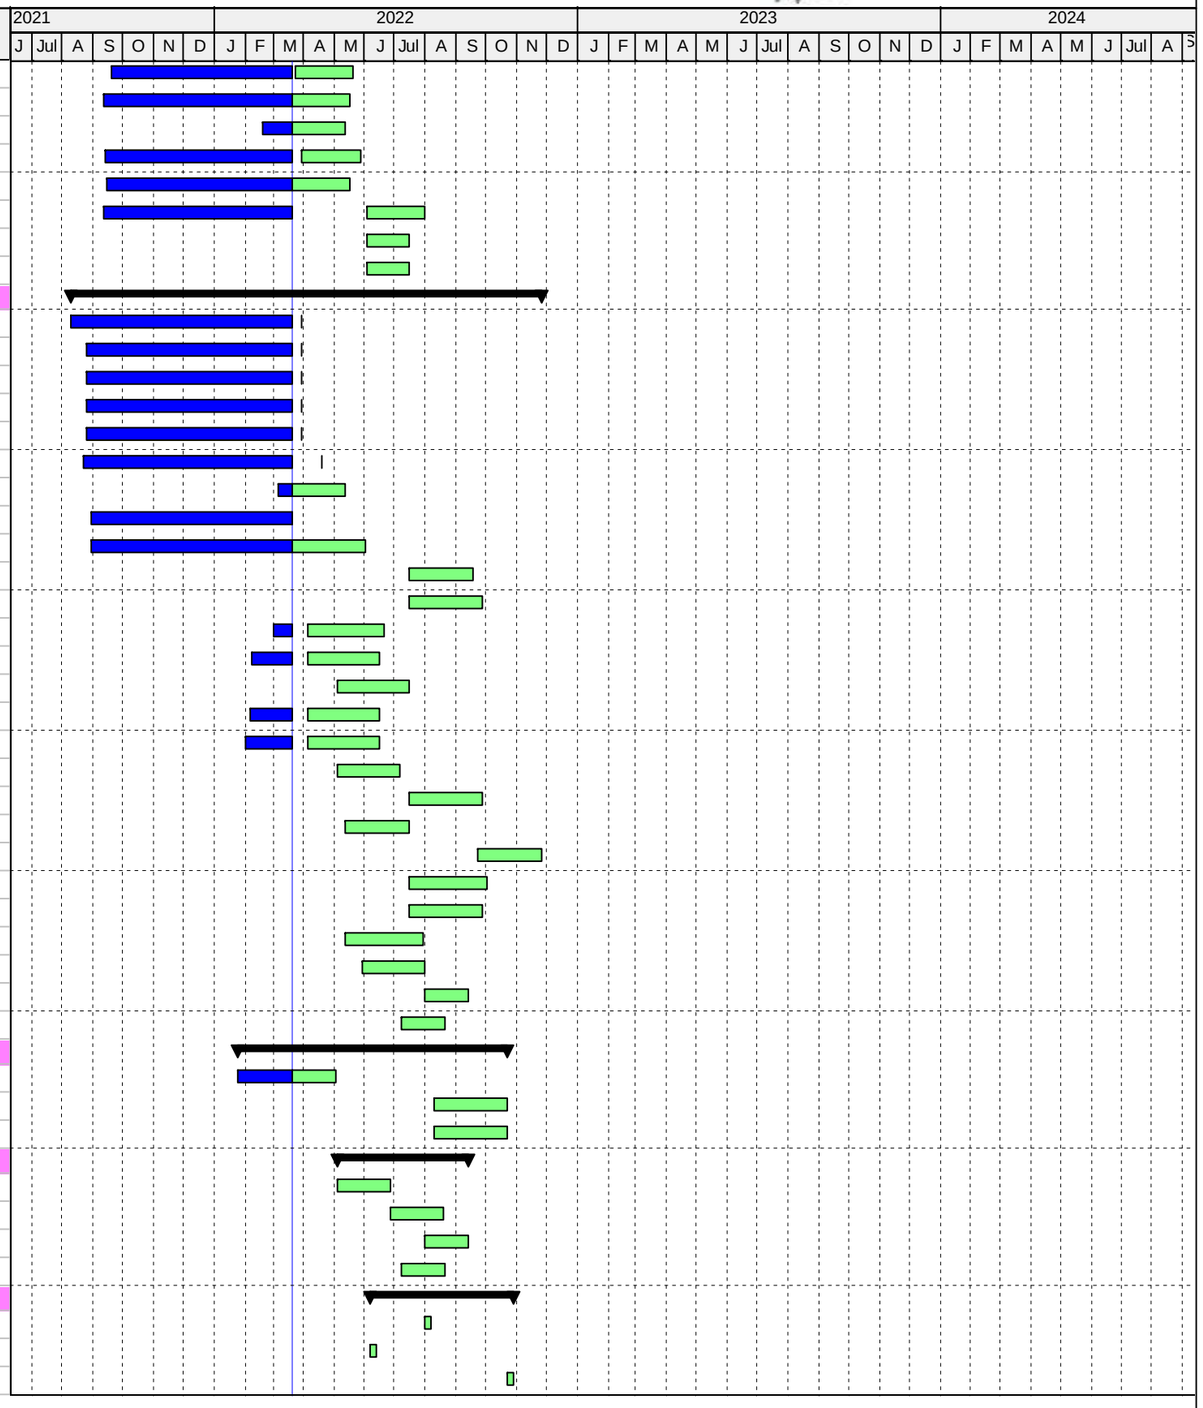


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P09-E	MTO For Tray/Ladder and Accessories - BK15	7	0%	$66.54	10-Aug-22	16-Aug-22
P09-E	MTO For Electrical Bulk Items - BK15	7	0%	$66.54	18-Oct-22	24-Oct-22
P09-E	MTO For Earthing & Lightning Systems - BK15	7	0%	$66.54	15-Aug-22	21-Aug-22
Architecture		277	16.97%	$771.34	08-Feb-22	10-Jul-22
Basis/Criteria		74	60%	$155.89	08-Feb-22	01-Jun-22
P09-E	Architectural Design Criteria	74	60%	$155.89	08-Feb-22	01-Jun-22
Specification		44	0%	$194.76	20-Mar-22	02-May-22
P09-E	Buildings General Specification	44	0%	$194.76	20-Mar-22	02-May-22
Drawing/Diagram		267	20%	$186.97	30-Mar-22	03-Jul-22
P09-E	Architectural Drawing For Diesel Generator Shelter of Well P	44	0%	$62.34	21-May-22	03-Jul-22
P09-E	Architectural Drawing For Switchgear Building of Well Pads -	44	60%	$62.32	18-May-22	12-May-22
P09-E	Architectural Drawing For Security Building of Well Pads - BK	44	0%	$62.32	30-Mar-22	12-May-22
MTO		7	0%	$233.72	04-Jul-22	10-Jul-22
P09-E	MTO For Architectural Works - BK15	7	0%	$233.72	04-Jul-22	10-Jul-22
Civil		95	15.14%	$739.69	01-Aug-21	22-Jun-22
Basis/Criteria		90	20%	$2.59	13-Feb-22	22-May-22
P09-E	Civil Design Criteria	64	60%	$0.86	13-Feb-22	22-May-22
P09-E	Design Criteria for Sewerage & Drainage	44	0%	$0.86	24-Mar-22	06-May-22
P09-E	Design Criteria for Road and Paving	44	0%	$0.86	27-Mar-22	09-May-22
Specification		94	72%	$13.24	09-Aug-21	06-Jun-22
P09-E	Specification For Civil Works	79	0%	$1.32	20-Mar-22	06-Jun-22
P09-E	Specification For Road & Paving	64	80%	$2.65	09-Aug-21	22-May-22
P09-E	Specification For Fence & Gate	64	100%	$2.65	18-Sep-21	20-Mar-22
P09-E	Specification For Earth Work	64	80%	$2.65	09-Aug-21	22-May-22
P09-E	Specification For Sewerage & Drainage	64	100%	$2.65	09-Aug-21	20-Mar-22
P09-E	Specification For Geological & Geotechnical Survey	44	0%	$1.32	20-Mar-22	02-May-22
Drawing/Diagram		89	18.08%	$563.94	01-Aug-21	15-Jun-22
P09-E	Standard Drawing For Civil Works	45	0%	$6.15	30-Mar-22	13-May-22
P09-E	Standard Drawing For Slope Protection Details	45	100%	$6.15	22-Aug-21	30-Mar-22
P09-E	Standard Drawing For Roads	45	80%	$6.15	22-Aug-21	13-May-22
P09-E	Standard Drawing For Electrical Cable Trench	45	100%	$6.15	22-Aug-21	30-Mar-22
P09-E	Standard Drawing For Manholes	45	80%	$6.15	22-Aug-21	13-May-22
P09-E	Standard Drawing For Catch Basins	45	80%	$6.15	22-Aug-21	17-May-22
P09-E	Standard Drawing For Sewerage & Drainage Details	45	60%	$6.15	02-Feb-22	17-May-22
P09-E	Standard Drawing For Civil Underground Crossings	38	60%	$10.43	07-Feb-22	10-May-22
P09-E	Standard Drawing For Fence & Gate Details	45	100%	$6.15	18-Sep-21	03-Apr-22
P09-E	Standard Drawing For Concrete Continues Weight	38	100%	$10.21	01-Aug-21	20-Mar-22
P09-E	Standard Drawing For Major Floodway Crossing	38	0%	$10.21	03-Apr-22	10-May-22
P09-E	Standard Drawing For Culvert & Details	38	100%	$10.21	25-Sep-21	03-Apr-22
P09-E	Standard Drawing For Valve Box	38	100%	$10.21	12-Jan-22	03-Apr-22
P09-E	Standard Drawing For Fire Hydrant Pit	38	60%	$10.21	13-Mar-22	10-May-22
P09-E	Standard Drawing For Cable Pull Pit	45	0%	$0.00	03-Apr-22	17-May-22
P09-E	Standard Drawing For Pavings	38	60%	$10.21	08-Jan-22	10-May-22
P09-E	Standard Drawing For Earth Pit	38	60%	$10.21	13-Feb-22	10-May-22
P09-E	Standard Detail For Pipe Bedding	45	100%	$6.15	22-Aug-21	03-Apr-22
P09-E	Standard Details of Miscellaneous Items	45	60%	$6.15	06-Mar-22	17-May-22
P09-E	BINAK Oil Field Project Overall Well Location/Facilities Layou	45	0%	$4.62	20-Mar-22	03-May-22
P09-E	Civil and Structural drawings - BK15	44	0%	$130.66	03-May-22	15-Jun-22
P09-E	General Civil Layout - BK15	44	0%	$130.66	03-May-22	15-Jun-22

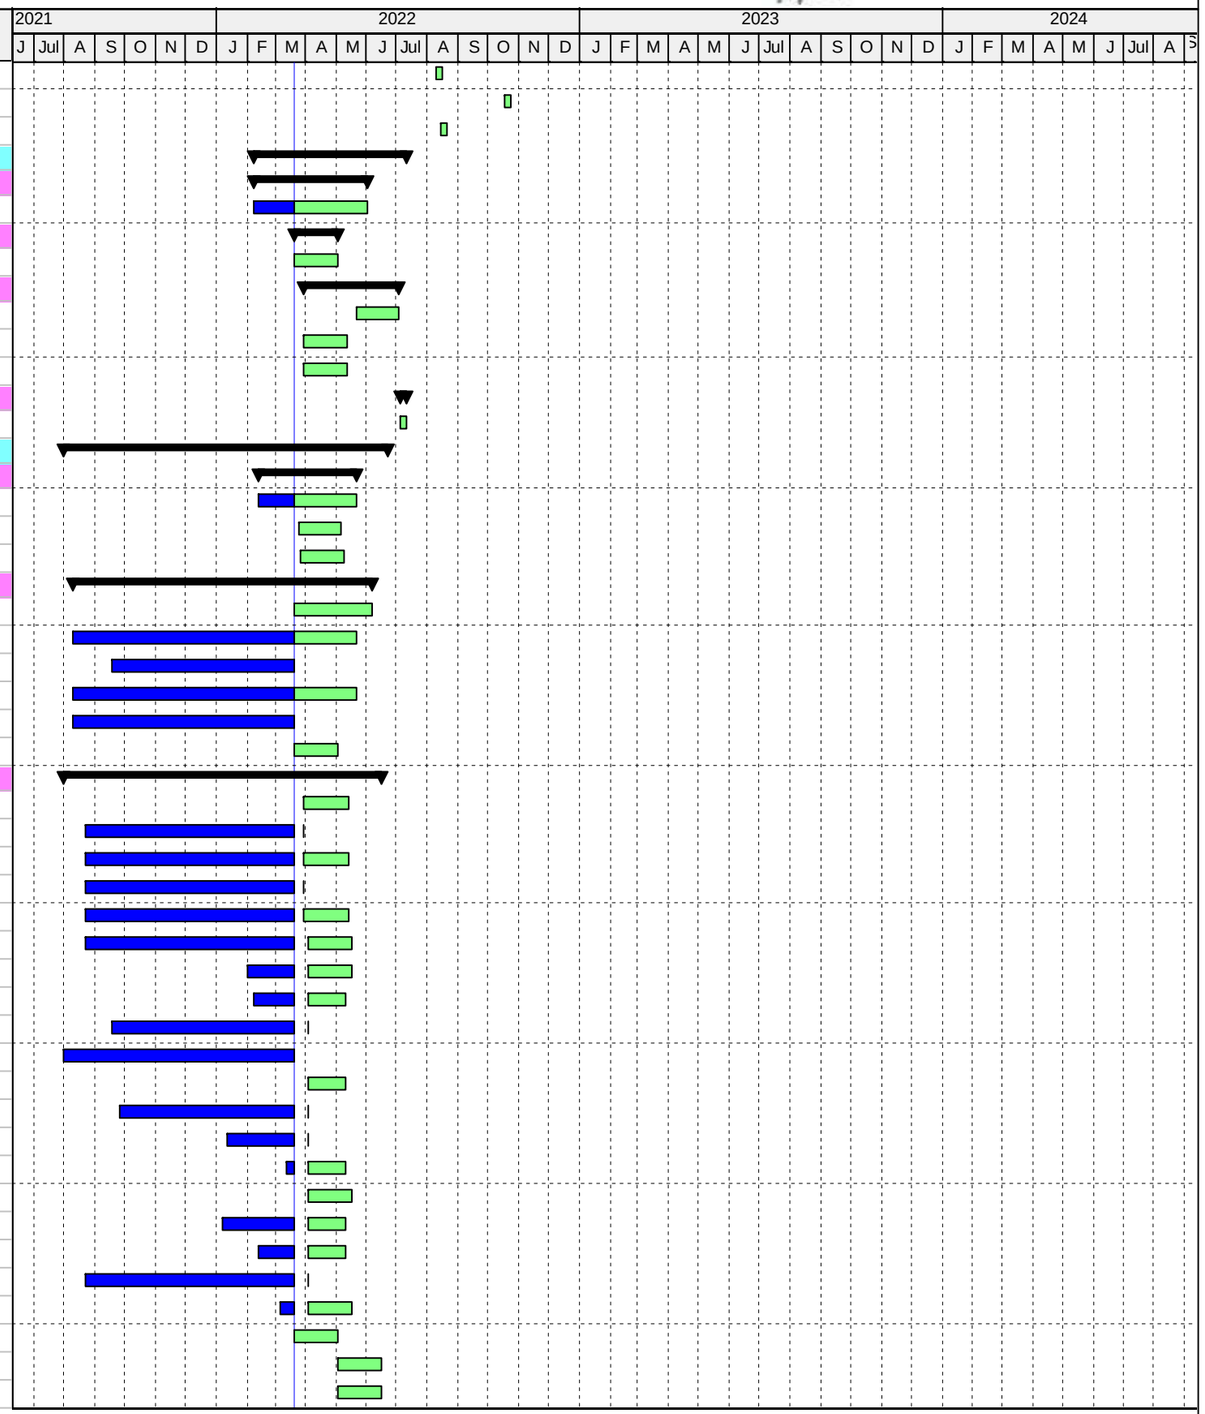


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P09-E	Rough Grading Plans -BK15	44	0%	$154.63	03-May-22	15-Jun-22
Report		44	0%	$96.46	20-Mar-22	02-May-22
P09-E	Site Visit Report (Civil Work) - BK15	44	0%	$96.46	20-Mar-22	02-May-22
MTO		7	0%	$63.47	16-Jun-22	22-Jun-22
P09-E	MTO For Civil Works - BK15	7	0%	$63.47	16-Jun-22	22-Jun-22
Structure		201	15.19%	$981.10	08-Aug-21	06-Oct-22
Basis/Criteria		64	0%	$10.69	20-Mar-22	22-May-22
P09-E	Structural Design Criteria	64	0%	$3.57	20-Mar-22	22-May-22
P09-E	Design Criteria For Steel Structure	44	0%	$3.56	20-Mar-22	02-May-22
P09-E	Design Criteria For Load & Forces	44	0%	$3.56	20-Mar-22	02-May-22
Specification		98	98.97%	$81.73	14-Aug-21	26-May-22
P09-E	Specification For Concrete Work	64	80%	$1.19	14-Aug-21	26-May-22
P09-E	Specification For Storage Tank Foundation	38	100%	$30.97	23-Nov-21	24-Mar-22
P09-E	Specification for Fabrication of Steel Structures	64	100%	$0.61	24-Jan-22	24-Mar-22
P09-E	Specification For Grouting	64	100%	$23.98	14-Aug-21	24-Mar-22
P09-E	Specification for Erection of Steel Structures	64	100%	$0.80	24-Jan-22	24-Mar-22
P09-E	Specification for Fireproofing	64	100%	$23.57	18-Sep-21	24-Mar-22
P09-E	Specification For Steel Structural Works	37	0%	$0.60	20-Mar-22	25-Apr-22
Drawing/Diagram		185	10.78%	$632.71	08-Aug-21	30-Sep-22
P09-E	Standard Drawing For Fire Proofing	64	100%	$4.05	08-Aug-21	03-Apr-22
P09-E	Standard Drawing For Anchor Bolts	64	100%	$4.05	15-Dec-21	03-Apr-22
P09-E	Standard Drawing For Steel Stairs	64	100%	$4.05	18-Dec-21	03-Apr-22
P09-E	Standard Drawing For Operating Platform	38	100%	$4.81	27-Dec-21	30-Mar-22
P09-E	Standard Drawing For Handrail	38	100%	$6.83	18-Dec-21	30-Mar-22
P09-E	Standard Drawing For Insert Plates in Concrete	38	100%	$6.83	08-Aug-21	30-Mar-22
P09-E	Standard Details For Ladder & Safety Cage	64	100%	$4.05	15-Dec-21	03-Apr-22
P09-E	Standard Drawing For Lighting pole foundation Plan & Details	38	60%	$6.83	29-Jan-22	06-May-22
P09-E	General Notes - Steel Structures	38	100%	$4.81	25-Jan-22	30-Mar-22
P09-E	General Notes - Reinforced Concrete Structures	38	100%	$6.83	20-Dec-21	30-Mar-22
P09-E	Standard Drawing For Structural Built-up Sections	44	80%	$6.83	04-Dec-21	12-May-22
P09-E	Standard Drawing For Steel Flooring, Grating and Chequere	44	100%	$6.83	05-Jan-22	30-Mar-22
P09-E	Concrete Reinforcement Shape Code	44	0%	$6.83	30-Mar-22	12-May-22
P09-E	Standard Drawing For Septic Tank	44	80%	$6.83	22-Jan-22	12-May-22
P09-E	Fuel Oil Storage Drum Detail Drawing For Well Pads - BK-15	44	0%	$69.03	18-Aug-22	30-Sep-22
P09-E	Foundation Drawing For Security Building For Well Pads - Bk	44	0%	$69.03	13-May-22	25-Jun-22
P09-E	Structural Drawing For Security Building For Well Pads - BK-:	44	0%	$69.03	26-Jun-22	08-Aug-22
P09-E	Foundation Drawing For Switchgear Building For Well Pads -	44	0%	$69.03	13-May-22	25-Jun-22
P09-E	Structural Drawing For Switchgear Building For Well Pads - E	44	0%	$69.03	26-Jun-22	08-Aug-22
P09-E	Foundation Drawing For Potable Water Tank For Well Pads -	44	0%	$69.03	13-Aug-22	25-Sep-22
P09-E	Foundation Drawing For Diesel Generator Shelter For Well F	44	0%	$69.03	04-Jul-22	16-Aug-22
P09-E	Structural Drawing For Diesel Generator Shelter For Well Pa	44	0%	$69.03	17-Aug-22	29-Sep-22
MTO		7	0%	$255.97	30-Sep-22	06-Oct-22
P09-E	MTO For Structural Works - BK15	7	0%	$255.97	30-Sep-22	06-Oct-22
General		116	7.46%	$1,475.70	11-Aug-21	13-Jul-22
Geotechnic		60	8%	$1,180.56	11-Aug-21	15-Jun-22
Procedure/Plan		44	100%	$94.44	11-Aug-21	19-Apr-22
P09-	Geotechnical Investigation Plan for Well Pads	44	100%	$94.44	11-Aug-21	19-Apr-22
Report		44	0%	$1,086.12	03-May-22	15-Jun-22
P09-	Geotechnical Investigation Report - BK15	44	0%	$1,086.12	03-May-22	15-Jun-22

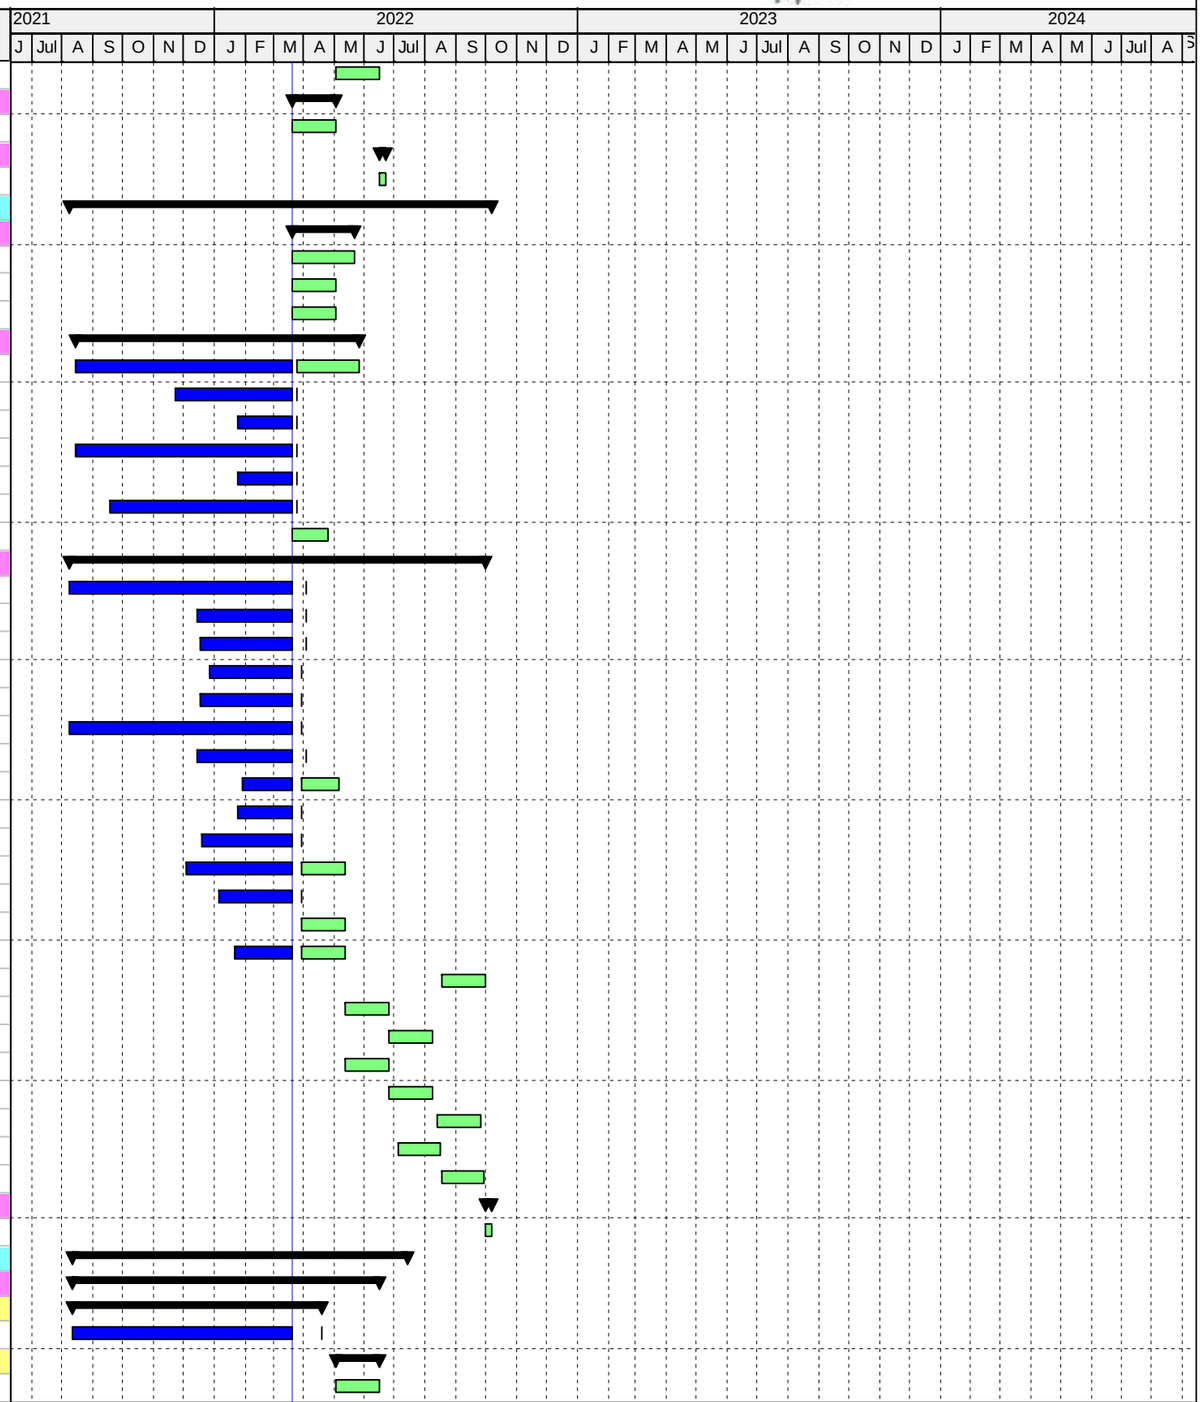


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Survey		5	0%	$147.57	16-Jun-22	20-Jun-22
Drawing/Diagram		5	0%	$147.57	16-Jun-22	20-Jun-22
P09-	Over Head Line Plan and Profile - BK15	5	0%	$147.57	16-Jun-22	20-Jun-22
QC/QA		116	10.58%	$147.57	20-Sep-21	13-Jul-22
QC Management		116	38.9%	$12.00	08-Dec-21	13-Jul-22
P09-	Project Audit Procedure	44	0%	$0.60	20-Mar-22	02-May-22
P09-	Specification For Final Data Book (FDB) Requirements	44	0%	$0.60	20-Mar-22	02-May-22
P09-	Non Conformance Control Procedure	36	0%	$0.60	03-May-22	07-Jun-22
P09-	Corrective Action Procedure	36	0%	$0.60	08-Jun-22	13-Jul-22
P09-	Material Reciving, Storage, Handling Procedure	39	60%	$0.60	20-Feb-22	27-Apr-22
P09-	Packing, Marking, Transportation Procedure	39	0%	$0.60	20-Mar-22	27-Apr-22
P09-	Criticality Assessment Procedure	39	0%	$2.40	20-Mar-22	27-Apr-22
P09-	Project Quality Plan	44	80%	$5.40	08-Dec-21	02-May-22
P09-	Technical Query Procedure	44	0%	$0.60	30-Mar-22	12-May-22
QC General Document		55	8.57%	$17.52	28-Nov-21	16-May-22
P09-	Quality Control Plan (QCP)	39	60%	$2.50	28-Nov-21	27-Apr-22
P09-	Specification for Welding Procedure	44	0%	$2.50	03-Apr-22	16-May-22
P09-	Heat Treatment Procedure (Pre Heating , PWHT)	44	0%	$2.50	03-Apr-22	16-May-22
P09-	Welder Performance Qualification Test (WQT) Procedure	44	0%	$2.50	03-Apr-22	16-May-22
P09-	NDT Procedure	44	0%	$2.50	03-Apr-22	16-May-22
P09-	Surface Preparation and Coating/Painting Procedure	44	0%	$2.50	03-Apr-22	16-May-22
P09-	Control of Inspection Measuring and Test Equipment Procedu	44	0%	$2.49	03-Apr-22	16-May-22
QC Discipline Document		95	7.99%	$118.06	20-Sep-21	29-Jun-22
Piping		95	0%	$29.51	27-Mar-22	29-Jun-22
P09	ITP For Piping Works	44	0%	$2.95	27-Mar-22	09-May-22
P09	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$3.32	03-Apr-22	16-May-22
P09	PIPING WPS (Welding Procedure Specification)	44	0%	$3.32	03-Apr-22	16-May-22
P09	PIPING PQR (Procedure Qualification Record)	44	0%	$3.32	03-Apr-22	16-May-22
P09	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$3.32	03-Apr-22	16-May-22
P09	PIPING WPS (Preliminary Welding Procedure Specification) f	44	0%	$3.32	03-Apr-22	16-May-22
P09	PIPING PQR (Procedure Qualification Record) for Repair We	44	0%	$3.32	03-Apr-22	16-May-22
P09	Field Joint Coating Procedure For Pipeline	44	0%	$3.32	03-Apr-22	16-May-22
P09	Pressure Test Procedure	44	0%	$3.32	17-May-22	29-Jun-22
Telecomm.		44	0%	$5.90	27-Mar-22	09-May-22
P09	ITP For Telecommunication Installation	44	0%	$5.90	27-Mar-22	09-May-22
Safety		44	0%	$5.90	27-Mar-22	09-May-22
P09	ITP For Safety Installation	44	0%	$5.90	27-Mar-22	09-May-22
Architectural		44	0%	$5.90	27-Mar-22	09-May-22
P09	ITP For Architectural Works	44	0%	$5.90	27-Mar-22	09-May-22
Mechanical		44	0%	$5.90	27-Mar-22	09-May-22
P09	ITP For Mechanical Installation	44	0%	$5.90	27-Mar-22	09-May-22
Structure		51	0%	$23.61	27-Mar-22	16-May-22
P09	ITP For Steel Structural Works	44	0%	$2.36	27-Mar-22	09-May-22
P09	Steel Structure WPS (Welding Procedure Specification)	44	0%	$3.54	03-Apr-22	16-May-22
P09	Steel Structure PQR (Procedure Qualification Record)	44	0%	$3.54	03-Apr-22	16-May-22
P09	Steel Structure WPS (Welding Procedure Specification) For F	44	0%	$3.54	03-Apr-22	16-May-22
P09	Steel Structure PQR (Procedure Qualification Record) For R	44	0%	$3.54	03-Apr-22	16-May-22
P09	Weld Map For Steel Structures	44	0%	$3.54	03-Apr-22	16-May-22
P09	NDT Plan For steel Structures	44	0%	$3.54	03-Apr-22	16-May-22

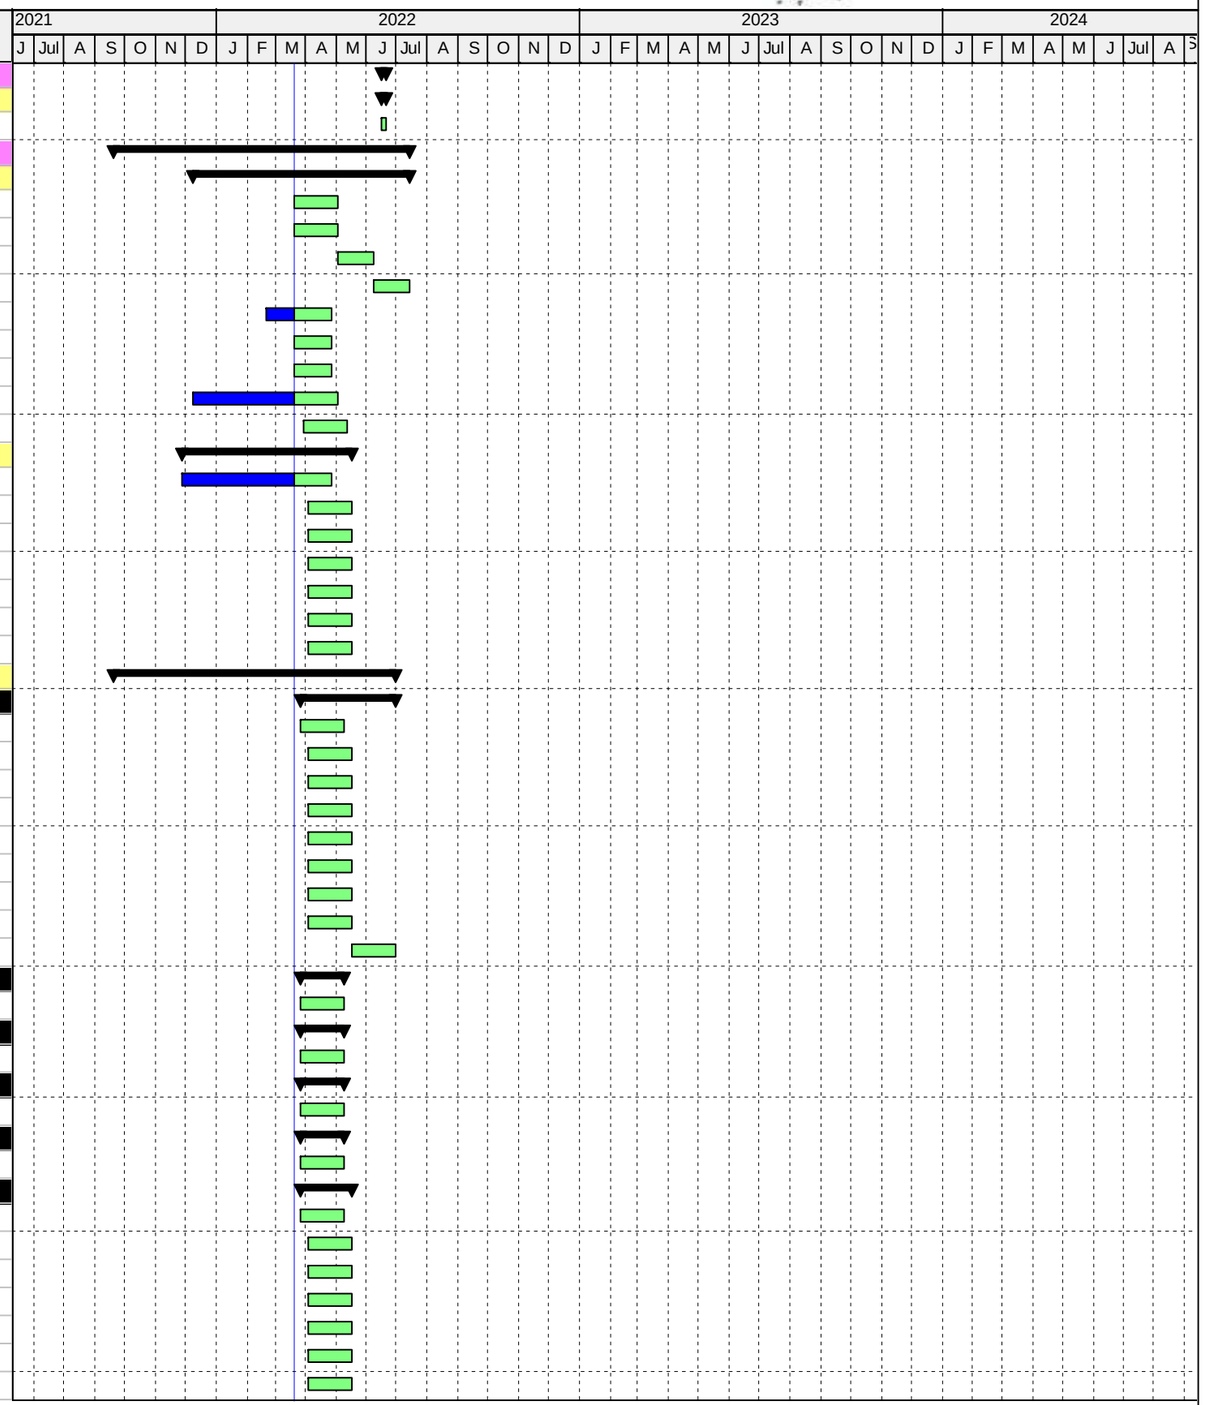


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Instrumentation		44	0%	$5.90	27-Mar-22	09-May-22
P09	ITP For I&C Installation	44	0%	$5.90	27-Mar-22	09-May-22
Pipeline		74	15%	$23.61	16-Jan-22	16-May-22
P09	ITP For Pipeline	44	60%	$2.36	16-Jan-22	09-May-22
P09	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	60%	$3.54	23-Feb-22	16-May-22
P09	PIPELINE WPS (Welding Procedure Specification)	44	0%	$3.54	03-Apr-22	16-May-22
P09	PIPELINE PQR (Procedure Qualification Record)	44	0%	$3.54	03-Apr-22	16-May-22
P09	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	0%	$3.54	03-Apr-22	16-May-22
P09	PIPELINE WPS (Preliminary Welding Procedure Specificatior	44	0%	$3.54	03-Apr-22	16-May-22
P09	PIPELINE PQR (Procedure Qualification Record) for Repair \	44	0%	$3.54	03-Apr-22	16-May-22
Civil		44	100%	$5.90	20-Sep-21	27-Mar-22
P09	ITP For Civil Works	44	100%	$5.90	20-Sep-21	27-Mar-22
Electrical		44	0%	$5.90	27-Mar-22	09-May-22
P09	ITP For Electrical Installation	44	0%	$5.90	27-Mar-22	09-May-22
Procurement Engineering		241	0%	$1,338.20	04-May-22	30-Dec-22
Mechanical		106	0%	$133.82	04-May-22	17-Aug-22
Drum		106	0%	$80.29	04-May-22	17-Aug-22
P09-E	PMR For Drum - BK15	21	0%	$8.03	04-May-22	24-May-22
P09-E	TBE For Main Drum - BK15	5	0%	$12.04	25-May-22	29-May-22
P09-E	VDR For Drum - BK15	7	0%	$60.22	11-Aug-22	17-Aug-22
Potable Tanks		96	0%	$53.53	09-May-22	12-Aug-22
P09-E	PMR For Potable Tanks - BK15	21	0%	$5.35	09-May-22	29-May-22
P09-E	TBE For Potable Tanks - BK15	5	0%	$8.03	30-May-22	03-Jun-22
P09-E	VDR For Potable Tanks - BK15	7	0%	$40.15	06-Aug-22	12-Aug-22
Electrical		226	0%	$1,012.62	06-May-22	17-Dec-22
Transformers		46	0%	$76.45	18-May-22	02-Jul-22
P09-E	PMR For Transformers - BK15	10	0%	$7.65	18-May-22	27-May-22
P09-E	TBE For Transformers - BK15	20	0%	$11.47	25-May-22	13-Jun-22
P09-E	VDR For Transformers - BK15	7	0%	$57.34	26-Jun-22	02-Jul-22
LV Switchgear & MCC		49	0%	$76.45	06-May-22	23-Jun-22
P09-E	PMR For LV Switchgear & MCC - BK15	10	0%	$7.65	06-May-22	15-May-22
P09-E	TBE For LV Switchgear & MCC - BK15	20	0%	$11.47	13-May-22	01-Jun-22
P09-E	VDR For LV Switchgear & MCC - BK15	7	0%	$57.34	17-Jun-22	23-Jun-22
Emergency Diesel Generator		49	0%	$76.45	21-May-22	08-Jul-22
P09-E	PMR For Emergency Diesel Generator - BK15	10	0%	$7.65	21-May-22	30-May-22
P09-E	TBE For Emergency Diesel Generator - BK15	20	0%	$11.47	28-May-22	16-Jun-22
P09-E	VDR For Emergency Diesel Generator - BK15	7	0%	$57.34	02-Jul-22	08-Jul-22
UPS System		49	0%	$76.45	23-May-22	10-Jul-22
P09-E	PMR For UPS System - BK15	10	0%	$7.65	23-May-22	01-Jun-22
P09-E	TBE For UPS System - BK15	20	0%	$11.47	30-May-22	18-Jun-22
P09-E	VDR For UPS System - BK15	7	0%	$57.34	04-Jul-22	10-Jul-22
DC Charger		46	0%	$76.45	23-May-22	07-Jul-22
P09-E	PMR For DC Charger - BK15	10	0%	$7.65	23-May-22	01-Jun-22
P09-E	TBE For DC Charger - BK15	20	0%	$11.47	30-May-22	18-Jun-22
P09-E	VDR For DC Charger - BK15	7	0%	$57.34	01-Jul-22	07-Jul-22
Capacitor Bank		49	0%	$76.45	06-May-22	23-Jun-22
P09-E	PMR For Capacitor Bank - BK15	10	0%	$7.65	06-May-22	15-May-22
P09-E	TBE For Capacitor Bank - BK15	20	0%	$11.47	13-May-22	01-Jun-22
P09-E	VDR For Capacitor Bank - BK15	7	0%	$57.34	17-Jun-22	23-Jun-22
Lighting & Distribution Main Panels		49	0%	$76.45	01-Aug-22	18-Sep-22

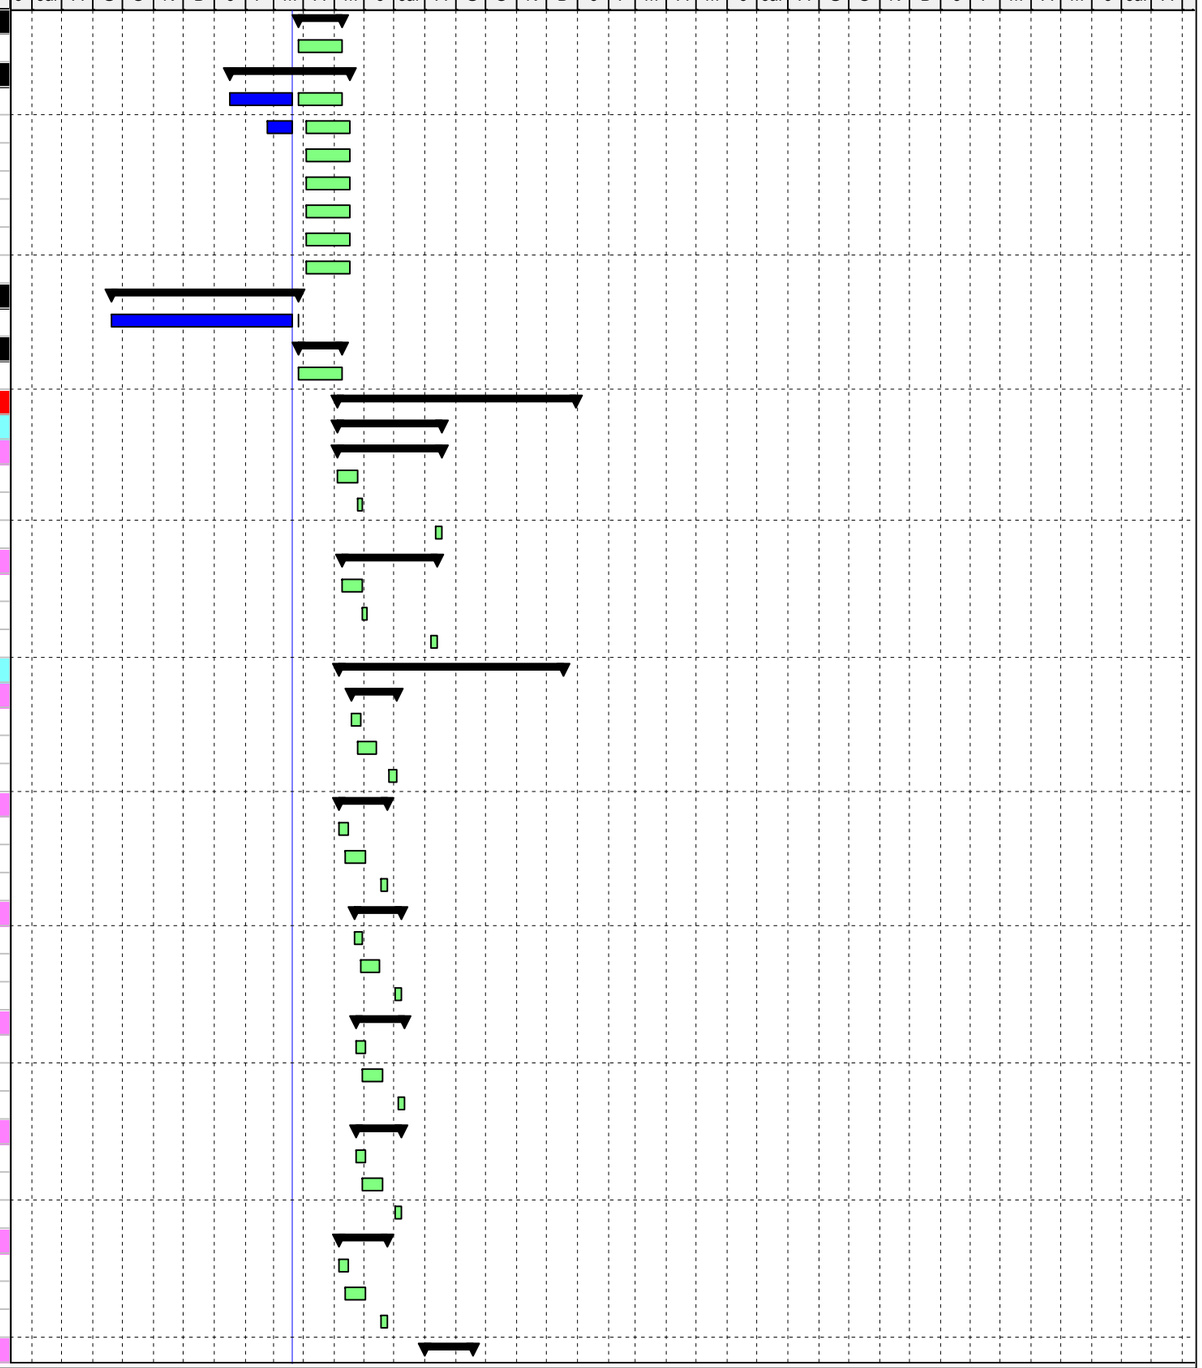


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P09-E	PMR For Lighting & Distribution Main Panels - BK15	10	0%	$7.65	01-Aug-22	10-Aug-22
P09-E	TBE For Lighting & Distribution Main Panels - BK15	20	0%	$11.47	08-Aug-22	27-Aug-22
P09-E	VDR For Lighting & Distribution Main Panels - BK15	7	0%	$57.34	12-Sep-22	18-Sep-22
Earthing & Lightning System		47	0%	$76.45	22-Aug-22	07-Oct-22
P09-E	PMR For Earthing & Lightning System - BK15	10	0%	$7.65	22-Aug-22	31-Aug-22
P09-E	TBE For Earthing & Lightning System - BK15	20	0%	$11.47	29-Aug-22	17-Sep-22
P09-E	VDR For Earthing & Lightning System - BK15	7	0%	$57.34	01-Oct-22	07-Oct-22
Lighting and Small Power Equipment		49	0%	$76.45	13-Jun-22	31-Jul-22
P09-E	PMR For Lighting and Small Power Equipment - BK15	10	0%	$7.65	13-Jun-22	22-Jun-22
P09-E	TBE For Lighting and Small Power Equipment - BK15	20	0%	$11.47	20-Jun-22	09-Jul-22
P09-E	VDR For Lighting and Small Power Equipment - BK15	7	0%	$57.34	25-Jul-22	31-Jul-22
Tray/Ladder and Accessories		49	0%	$76.35	17-Aug-22	04-Oct-22
P09-E	PMR For Tray/Ladder and Accessories - BK15	10	0%	$7.64	17-Aug-22	26-Aug-22
P09-E	TBE For Tray/Ladder and Accessories - BK15	20	0%	$11.45	24-Aug-22	12-Sep-22
P09-E	VDR For Tray/Ladder and Accessories - BK15	7	0%	$57.26	28-Sep-22	04-Oct-22
Power & Control Cables		49	0%	$76.35	30-Oct-22	17-Dec-22
P09-E	PMR For Power & Control Cables - BK15	10	0%	$7.64	30-Oct-22	08-Nov-22
P09-E	TBE For Power & Control Cables - BK15	20	0%	$11.45	06-Nov-22	25-Nov-22
P09-E	VDR For Power & Control Cables - BK15	7	0%	$57.26	11-Dec-22	17-Dec-22
Electrical Bulk Items		49	0%	$76.35	25-Oct-22	12-Dec-22
P09-E	PMR For Electrical Bulk Items - BK15	10	0%	$7.64	25-Oct-22	03-Nov-22
P09-E	TBE For Electrical Bulk Items - BK15	20	0%	$11.45	01-Nov-22	20-Nov-22
P09-E	VDR For Electrical Bulk Items - BK15	7	0%	$57.26	06-Dec-22	12-Dec-22
Transmission Over head Line		49	0%	$95.49	08-Aug-22	25-Sep-22
P09-E	PMR For Transmission Over head Line - BK15	10	0%	$9.55	08-Aug-22	17-Aug-22
P09-E	TBE For Transmission Over head Line - BK15	20	0%	$14.32	15-Aug-22	03-Sep-22
P09-E	VDR For Transmission Over head Line - BK15	7	0%	$71.62	19-Sep-22	25-Sep-22
HVAC		41	0%	$48.58	20-Nov-22	30-Dec-22
Main HVAC Equipment		41	0%	$48.58	20-Nov-22	30-Dec-22
P09-E	PMR For Main HVAC Equipment - BK15	5	0%	$4.86	20-Nov-22	24-Nov-22
P09-E	TBE For Main HVAC Equipment - BK15	15	0%	$7.29	27-Nov-22	11-Dec-22
P09-E	VDR For Main HVAC Equipment - BK15	7	0%	$36.43	24-Dec-22	30-Dec-22
Structure		42	0%	$85.91	07-Oct-22	17-Nov-22
Steel Structure Items		19	0%	$28.64	07-Oct-22	25-Oct-22
P09-E	PMR For Steel Structure Items - BK15	10	0%	$2.86	07-Oct-22	16-Oct-22
P09-E	TBE For Steel Structure Items - BK15	7	0%	$4.30	14-Oct-22	20-Oct-22
P09-E	VDR For Steel Structure Items - BK15	5	0%	$21.48	21-Oct-22	25-Oct-22
Anchor Bolts		42	0%	$28.63	07-Oct-22	17-Nov-22
P09-E	PMR For Anchor Bolts - BK15	10	0%	$2.86	07-Oct-22	16-Oct-22
P09-E	TBE For Anchor Bolts - BK15	30	0%	$4.30	14-Oct-22	12-Nov-22
P09-E	VDR For Anchor Bolts - BK15	5	0%	$21.48	13-Nov-22	17-Nov-22
Blast Proof Doors		42	0%	$28.63	07-Oct-22	17-Nov-22
P09-E	PMR For Blast Proof Doors - BK15	10	0%	$2.86	07-Oct-22	16-Oct-22
P09-E	TBE For Blast Proof Doors - BK15	30	0%	$4.30	14-Oct-22	12-Nov-22
P09-E	VDR For Blast Proof Doors - BK15	5	0%	$21.48	13-Nov-22	17-Nov-22
Piping		41	0%	$57.27	25-Jun-22	04-Aug-22
Pipe		41	0%	$28.64	25-Jun-22	04-Aug-22
P09-E	PMR For Pipes - BK15	5	0%	$2.86	25-Jun-22	29-Jun-22
P09-E	TBE For Pipes - BK15	15	0%	$4.30	02-Jul-22	16-Jul-22

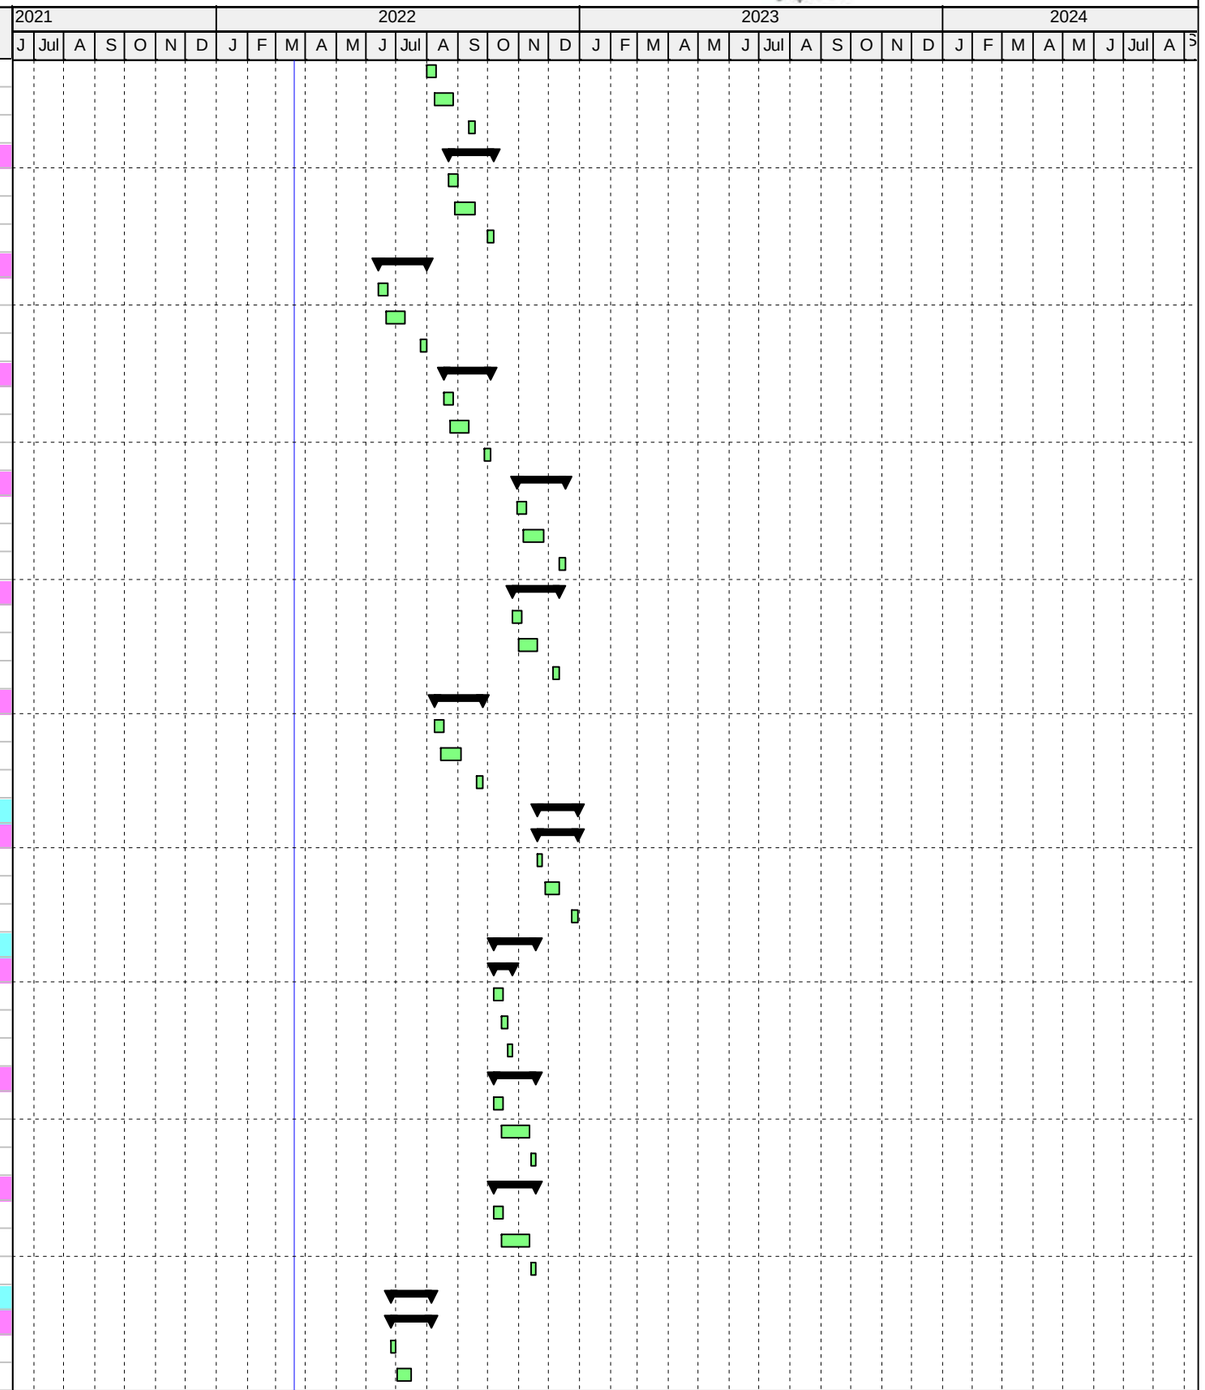


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P09-E	VDR For Pipes - BK15	7	0%	$21.48	29-Jul-22	04-Aug-22
Pipe Support		31	0%	$28.64	30-Jun-22	30-Jul-22
P09-E	PMR For Pipe Support - BK15	5	0%	$2.86	30-Jun-22	04-Jul-22
P09-E	TBE For Pipe Support - BK15	5	0%	$4.30	07-Jul-22	11-Jul-22
P09-E	VDR For Pipe Support - BK15	7	0%	$21.48	24-Jul-22	30-Jul-22
Commissioning Engineering		203	0%	$267.64	16-Sep-22	06-Apr-23
P09-EP	Operability Review	5	0%	$53.53	16-Sep-22	20-Sep-22
P09-EP	Pre-Commissioning, Commissioning & Startup Procedure - BI	44	0%	$160.58	16-Sep-22	29-Oct-22
P09-EP	Operating Manual - BK15	30	0%	$53.53	08-Mar-23	06-Apr-23
Field Engineering		204	0%	$2,007.30	14-Oct-22	05-May-23
P09-EP	Technical/Site Queries	30	0%	$1,003.65	14-Oct-22	12-Nov-22
P09-EP	As-Built Document Booklets - BK15	10	0%	$1,003.65	26-Apr-23	05-May-23
Engineering Final Documentation		7	0%	$1,338.20	06-May-23	12-May-23
P09-EP	Final Engineering Dossier - BK15	7	0%	$1,338.20	06-May-23	12-May-23
PROCUREMENT		282	0%	$400,673.00	30-May-22	07-Mar-23
Mechanical		142	0%	$15,986.85	30-May-22	18-Oct-22
Drum		142	0%	$9,592.11	30-May-22	18-Oct-22
P09-EI	Tendering & Selection	30	0%	$383.68	30-May-22	28-Jun-22
P09-EI	Contract Effectiveness / PO	5	0%	$575.53	06-Aug-22	10-Aug-22
P09-EI	Manufacturing / Fabrication / Supply	40	0%	$4,796.06	11-Aug-22	19-Sep-22
P09-EI	Final Inspection	12	0%	$959.21	20-Sep-22	01-Oct-22
P09-EI	Delivery On Site	7	0%	$1,918.42	02-Oct-22	08-Oct-22
P09-EI	Submitting Vendor Data Book	5	0%	$479.61	09-Oct-22	13-Oct-22
P09-EI	Delivering Spare Parts	5	0%	$479.61	14-Oct-22	18-Oct-22
Potable Tanks		132	0%	$6,394.74	04-Jun-22	13-Oct-22
P09-EI	Tendering & Selection	30	0%	$255.79	04-Jun-22	03-Jul-22
P09-EI	Contract Effectiveness / PO	5	0%	$383.68	01-Aug-22	05-Aug-22
P09-EI	Manufacturing / Fabrication / Supply	40	0%	$3,197.37	06-Aug-22	14-Sep-22
P09-EI	Final Inspection	12	0%	$639.47	15-Sep-22	26-Sep-22
P09-EI	Delivery On Site	7	0%	$1,278.95	27-Sep-22	03-Oct-22
P09-EI	Submitting Vendor Data Book	5	0%	$319.74	04-Oct-22	08-Oct-22
P09-EI	Delivering Spare Parts	5	0%	$319.74	09-Oct-22	13-Oct-22
Electrical		271	0%	$346,662.28	02-Jun-22	27-Feb-23
Electrical Bulk Items - BK15		79	0%	$2,911.96	21-Nov-22	07-Feb-23
P09-EI	Tendering & Selection	10	0%	$116.48	21-Nov-22	30-Nov-22
P09-EI	Contract Effectiveness / PO	5	0%	$174.72	01-Dec-22	05-Dec-22
P09-EI	Manufacturing / Fabrication / Supply	45	0%	$1,455.98	06-Dec-22	19-Jan-23
P09-EI	Final Inspection	7	0%	$291.20	20-Jan-23	26-Jan-23
P09-EI	Delivery On Site	7	0%	$727.99	27-Jan-23	02-Feb-23
P09-EI	Submitting Vendor Data Book	5	0%	$145.60	03-Feb-23	07-Feb-23
Power & Control Cables - BK15		94	0%	$20,002.41	26-Nov-22	27-Feb-23
P09-EI	Tendering & Selection	10	0%	$800.10	26-Nov-22	05-Dec-22
P09-EI	Contract Effectiveness / PO	5	0%	$1,200.14	06-Dec-22	10-Dec-22
P09-EI	Manufacturing / Fabrication / Supply	60	0%	$10,001.21	11-Dec-22	08-Feb-23
P09-EI	Final Inspection	7	0%	$2,000.24	09-Feb-23	15-Feb-23
P09-EI	Delivery On Site	7	0%	$5,000.60	16-Feb-23	22-Feb-23
P09-EI	Submitting Vendor Data Book	5	0%	$1,000.12	23-Feb-23	27-Feb-23
Lighting & Distribution Main Panels - BK15		99	0%	$8,181.23	28-Aug-22	04-Dec-22
P09-EI	Tendering & Selection	10	0%	$327.25	28-Aug-22	06-Sep-22

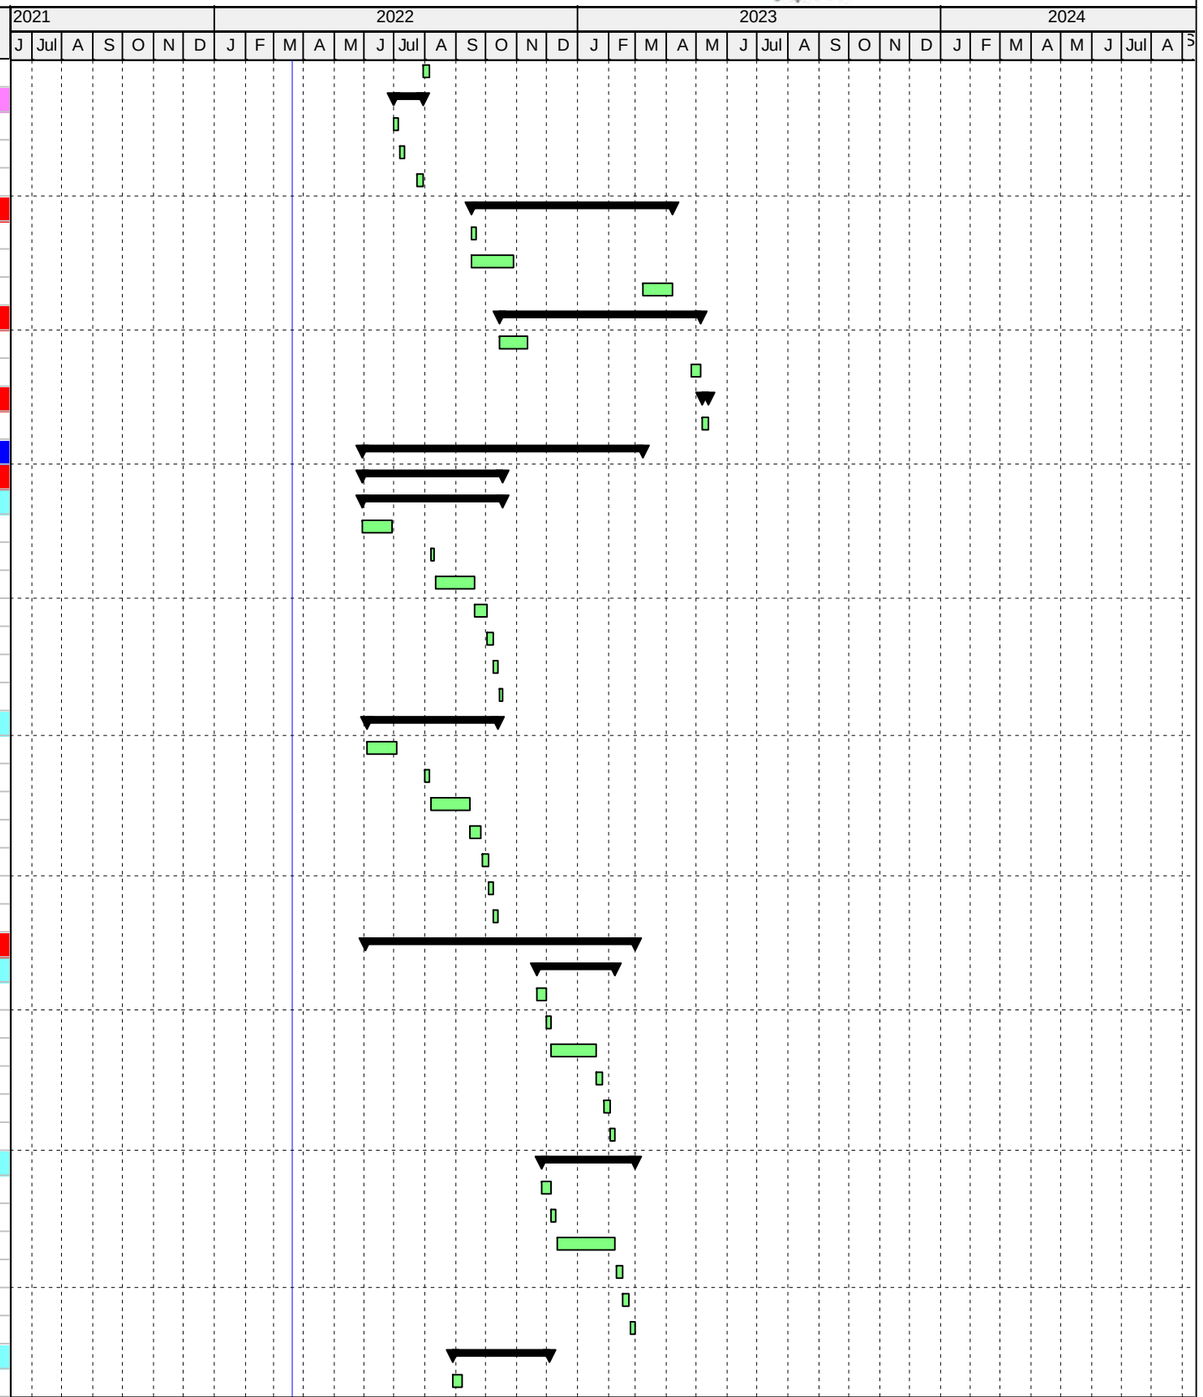


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P09-EF	Contract Effectiveness / PO	5	0%	$490.87	07-Sep-22	11-Sep-22
P09-EF	Manufacturing / Fabrication / Supply	60	0%	$4,090.61	12-Sep-22	10-Nov-22
P09-EF	Final Inspection	7	0%	$818.12	11-Nov-22	17-Nov-22
P09-EF	Delivery On Site	7	0%	$1,636.25	18-Nov-22	24-Nov-22
P09-EF	Submitting Vendor Data Book	5	0%	$409.06	25-Nov-22	29-Nov-22
P09-EF	Delivering Spare Parts	5	0%	$409.06	30-Nov-22	04-Dec-22
Transmission Over head Line - BK15		104	0%	$123,099.78	04-Sep-22	16-Dec-22
P09-EF	Tendering & Selection	10	0%	$4,923.99	04-Sep-22	13-Sep-22
P09-EF	Contract Effectiveness / PO	5	0%	$7,385.99	14-Sep-22	18-Sep-22
P09-EF	Manufacturing / Fabrication / Supply	70	0%	$61,549.89	19-Sep-22	27-Nov-22
P09-EF	Final Inspection	7	0%	$12,309.98	28-Nov-22	04-Dec-22
P09-EF	Delivery On Site	7	0%	$30,774.94	05-Dec-22	11-Dec-22
P09-EF	Submitting Vendor Data Book	5	0%	$6,154.99	12-Dec-22	16-Dec-22
Tray/Ladder and Accessories - BK15		94	0%	$2,911.96	13-Sep-22	15-Dec-22
P09-EF	Tendering & Selection	10	0%	$116.48	13-Sep-22	22-Sep-22
P09-EF	Contract Effectiveness / PO	5	0%	$174.72	23-Sep-22	27-Sep-22
P09-EF	Manufacturing / Fabrication / Supply	60	0%	$1,455.98	28-Sep-22	26-Nov-22
P09-EF	Final Inspection	7	0%	$291.20	27-Nov-22	03-Dec-22
P09-EF	Delivery On Site	7	0%	$727.99	04-Dec-22	10-Dec-22
P09-EF	Submitting Vendor Data Book	5	0%	$145.60	11-Dec-22	15-Dec-22
Earthing & Lightning System - BK15		97	0%	$13,173.17	18-Sep-22	23-Dec-22
P09-EF	Tendering & Selection	7	0%	$526.93	18-Sep-22	24-Sep-22
P09-EF	Contract Effectiveness / PO	6	0%	$790.39	25-Sep-22	30-Sep-22
P09-EF	Manufacturing / Fabrication / Supply	60	0%	$6,586.58	01-Oct-22	29-Nov-22
P09-EF	Final Inspection	7	0%	$1,317.32	30-Nov-22	06-Dec-22
P09-EF	Delivery On Site	7	0%	$2,634.63	07-Dec-22	13-Dec-22
P09-EF	Submitting Vendor Data Book	5	0%	$658.66	14-Dec-22	18-Dec-22
P09-EF	Delivering Spare Parts	5	0%	$658.66	19-Dec-22	23-Dec-22
Lighting and Small Power Equipment - BK15		84	0%	$16,570.46	10-Jul-22	01-Oct-22
P09-EF	Tendering & Selection	10	0%	$662.82	10-Jul-22	19-Jul-22
P09-EF	Contract Effectiveness / PO	5	0%	$994.23	20-Jul-22	24-Jul-22
P09-EF	Manufacturing / Fabrication / Supply	45	0%	$8,285.23	25-Jul-22	07-Sep-22
P09-EF	Final Inspection	7	0%	$1,657.05	08-Sep-22	14-Sep-22
P09-EF	Delivery On Site	7	0%	$3,314.09	15-Sep-22	21-Sep-22
P09-EF	Submitting Vendor Data Book	5	0%	$828.52	22-Sep-22	26-Sep-22
P09-EF	Delivering Spare Parts	5	0%	$828.52	27-Sep-22	01-Oct-22
DC Charger - BK15		103	0%	$22,533.05	19-Jun-22	29-Sep-22
P09-EF	Tendering & Selection	7	0%	$901.32	19-Jun-22	25-Jun-22
P09-EF	Contract Effectiveness / PO	5	0%	$1,351.98	26-Jun-22	30-Jun-22
P09-EF	Manufacturing / Fabrication / Supply	65	0%	$11,266.52	01-Jul-22	03-Sep-22
P09-EF	Final Inspection	7	0%	$2,253.30	04-Sep-22	10-Sep-22
P09-EF	Delivery On Site	7	0%	$4,506.61	11-Sep-22	17-Sep-22
P09-EF	Submitting Vendor Data Book	7	0%	$1,126.65	18-Sep-22	24-Sep-22
P09-EF	Delivering Spare Parts	5	0%	$1,126.65	25-Sep-22	29-Sep-22
Capacitor Bank - BK15		114	0%	$6,829.25	02-Jun-22	23-Sep-22
P09-EF	Tendering & Selection	10	0%	$273.17	02-Jun-22	11-Jun-22
P09-EF	Contract Effectiveness / PO	5	0%	$409.75	12-Jun-22	16-Jun-22
P09-EF	Manufacturing / Fabrication / Supply	75	0%	$3,414.62	17-Jun-22	30-Aug-22
P09-EF	Final Inspection	7	0%	$682.92	31-Aug-22	06-Sep-22

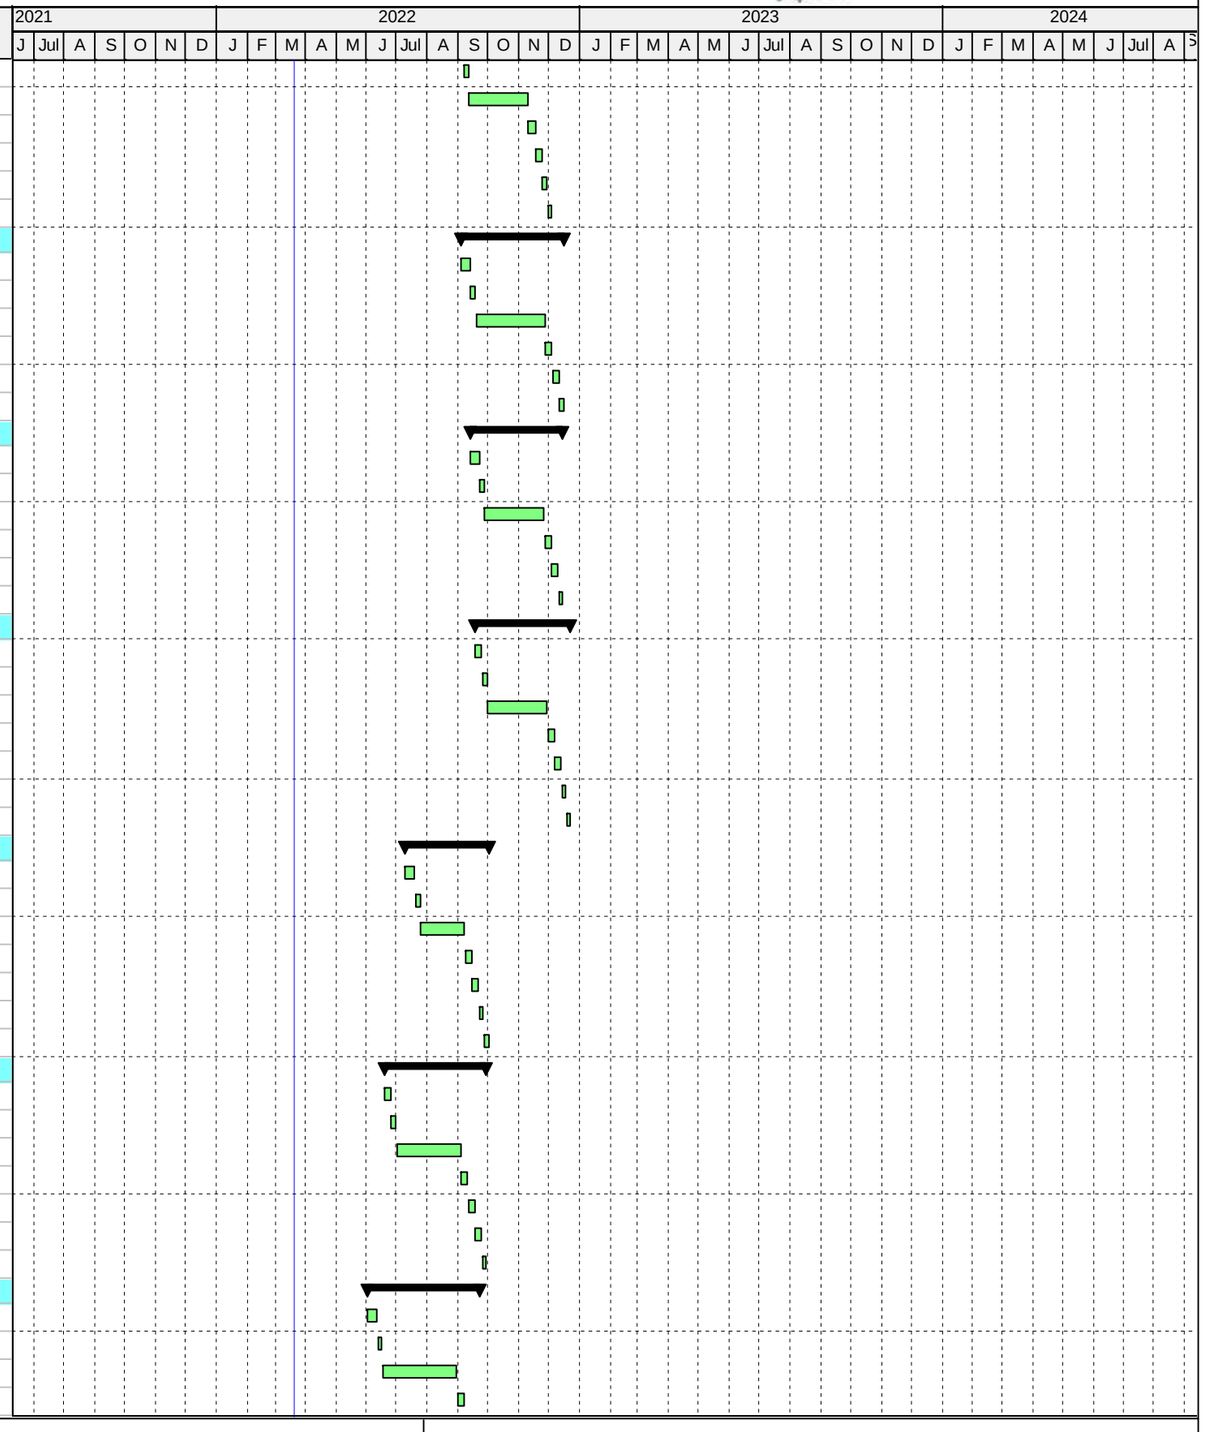


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P09-EI	Delivery On Site	7	0%	$1,365.85	07-Sep-22	13-Sep-22
P09-EI	Submitting Vendor Data Book	5	0%	$341.46	14-Sep-22	18-Sep-22
P09-EI	Delivering Spare Parts	5	0%	$341.46	19-Sep-22	23-Sep-22
Transformers - BK15		111	0%	$39,623.50	14-Jun-22	02-Oct-22
P09-EI	Tendering & Selection	7	0%	$1,584.94	14-Jun-22	20-Jun-22
P09-EI	Contract Effectiveness / PO	5	0%	$2,377.41	21-Jun-22	25-Jun-22
P09-EI	Manufacturing / Fabrication / Supply	75	0%	$19,811.75	26-Jun-22	08-Sep-22
P09-EI	Final Inspection	7	0%	$3,962.35	09-Sep-22	15-Sep-22
P09-EI	Delivery On Site	7	0%	$7,924.70	16-Sep-22	22-Sep-22
P09-EI	Submitting Vendor Data Book	5	0%	$1,981.17	23-Sep-22	27-Sep-22
P09-EI	Delivering Spare Parts	5	0%	$1,981.17	28-Sep-22	02-Oct-22
Emergency Diesel Generator - BK15		104	0%	$34,978.22	17-Jun-22	28-Sep-22
P09-EI	Tendering & Selection	10	0%	$1,399.13	17-Jun-22	26-Jun-22
P09-EI	Contract Effectiveness / PO	5	0%	$2,098.69	27-Jun-22	01-Jul-22
P09-EI	Manufacturing / Fabrication / Supply	65	0%	$17,489.11	02-Jul-22	04-Sep-22
P09-EI	Final Inspection	7	0%	$3,497.82	05-Sep-22	11-Sep-22
P09-EI	Delivery On Site	7	0%	$6,995.64	12-Sep-22	18-Sep-22
P09-EI	Submitting Vendor Data Book	5	0%	$1,748.91	19-Sep-22	23-Sep-22
P09-EI	Delivering Spare Parts	5	0%	$1,748.91	24-Sep-22	28-Sep-22
UPS System - BK15		109	0%	$21,666.39	19-Jun-22	05-Oct-22
P09-EI	Tendering & Selection	10	0%	$866.66	19-Jun-22	28-Jun-22
P09-EI	Contract Effectiveness / PO	5	0%	$1,299.98	29-Jun-22	03-Jul-22
P09-EI	Manufacturing / Fabrication / Supply	70	0%	$10,833.20	04-Jul-22	11-Sep-22
P09-EI	Final Inspection	7	0%	$2,166.64	12-Sep-22	18-Sep-22
P09-EI	Delivery On Site	7	0%	$4,333.28	19-Sep-22	25-Sep-22
P09-EI	Submitting Vendor Data Book	5	0%	$1,083.32	26-Sep-22	30-Sep-22
P09-EI	Delivering Spare Parts	5	0%	$1,083.32	01-Oct-22	05-Oct-22
LV Switchgear & MCC - BK15		114	0%	$34,180.90	02-Jun-22	23-Sep-22
P09-EI	Tendering & Selection	10	0%	$1,367.24	02-Jun-22	11-Jun-22
P09-EI	Contract Effectiveness / PO	5	0%	$2,050.85	12-Jun-22	16-Jun-22
P09-EI	Manufacturing / Fabrication / Supply	75	0%	$17,090.45	17-Jun-22	30-Aug-22
P09-EI	Final Inspection	7	0%	$3,418.09	31-Aug-22	06-Sep-22
P09-EI	Delivery On Site	7	0%	$6,836.18	07-Sep-22	13-Sep-22
P09-EI	Submitting Vendor Data Book	5	0%	$1,709.05	14-Sep-22	18-Sep-22
P09-EI	Delivering Spare Parts	5	0%	$1,709.05	19-Sep-22	23-Sep-22
HVAC		86	0%	$6,010.10	12-Dec-22	07-Mar-23
Main HVAC Equipment - BK15		86	0%	$6,010.10	12-Dec-22	07-Mar-23
P09-EI	Tendering & Selection	7	0%	$240.40	12-Dec-22	18-Dec-22
P09-EI	Contract Effectiveness / PO	5	0%	$360.61	19-Dec-22	23-Dec-22
P09-EI	Manufacturing / Fabrication / Supply	55	0%	$3,005.05	24-Dec-22	16-Feb-23
P09-EI	Final Inspection	7	0%	$601.01	17-Feb-23	23-Feb-23
P09-EI	Delivery On Site	7	0%	$1,502.52	24-Feb-23	02-Mar-23
P09-EI	Submitting Vendor Data Book	5	0%	$300.50	03-Mar-23	07-Mar-23
Piping		86	0%	$32,013.77	12-Jul-22	05-Oct-22
Pipes - BK15		81	0%	$25,611.02	17-Jul-22	05-Oct-22
P09-EI	Tendering & Selection	7	0%	$1,024.44	17-Jul-22	23-Jul-22
P09-EI	Contract Effectiveness / PO	5	0%	$1,536.66	24-Jul-22	28-Jul-22
P09-EI	Manufacturing / Fabrication / Supply	50	0%	$12,805.51	29-Jul-22	16-Sep-22
P09-EI	Final Inspection	7	0%	$2,561.10	17-Sep-22	23-Sep-22

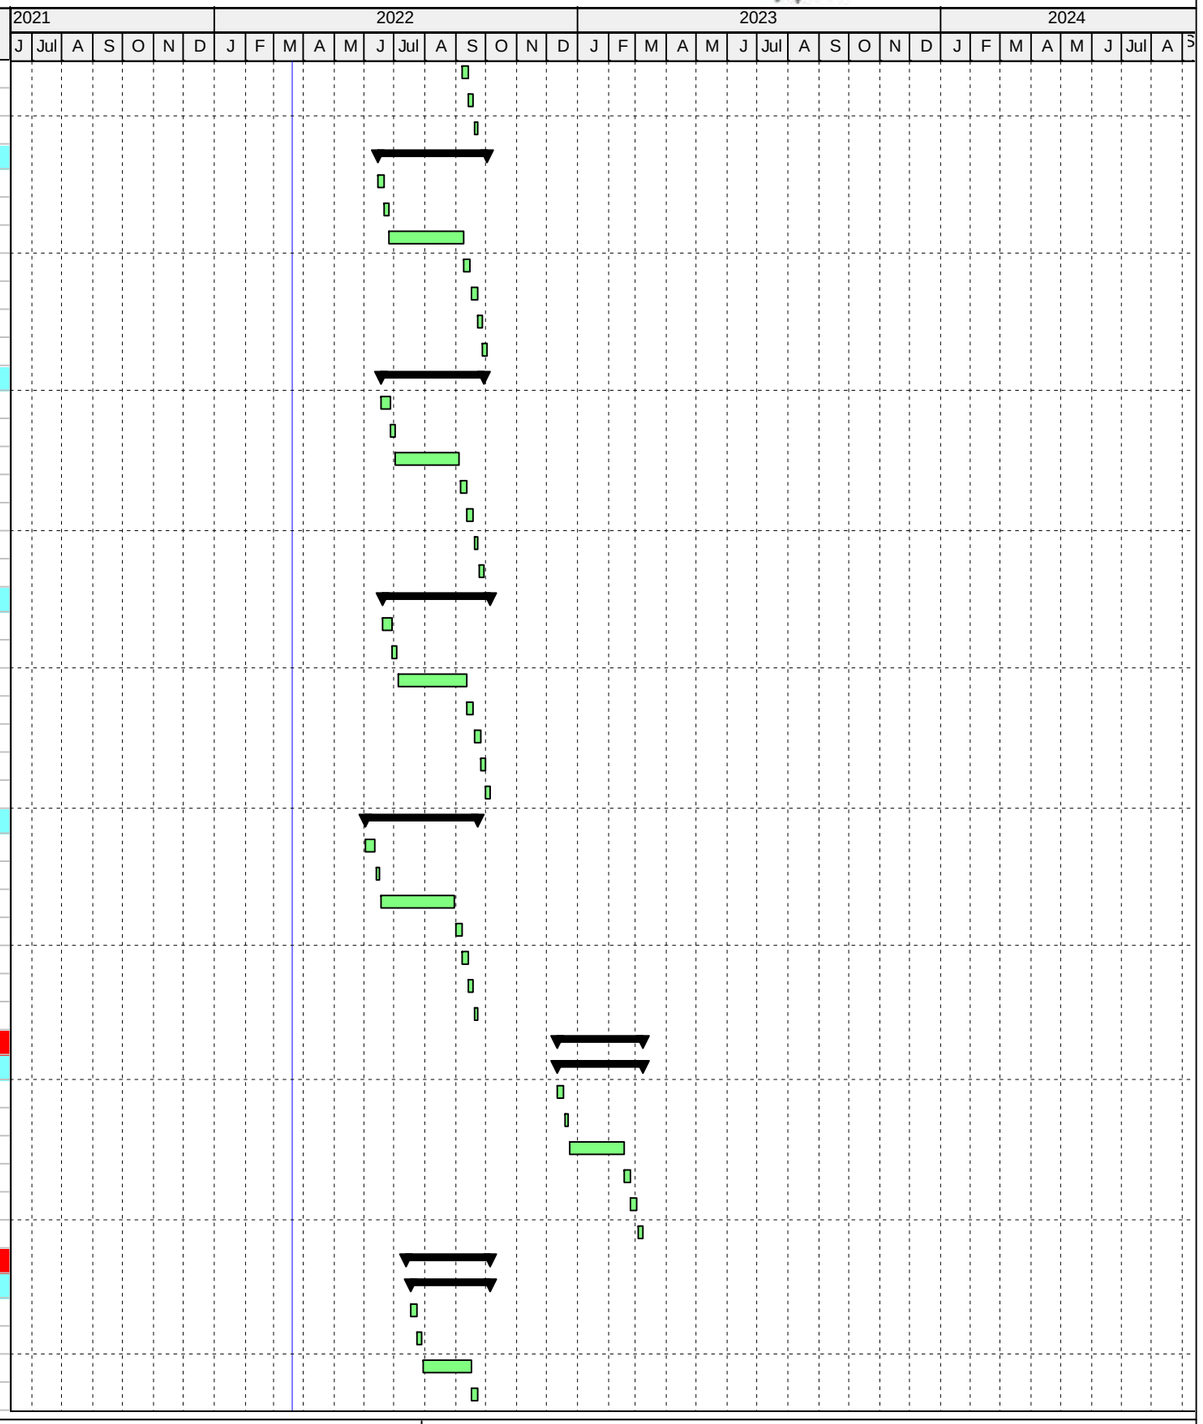


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P09-EF	Delivery On Site	7	0%	$6,402.75	24-Sep-22	30-Sep-22
P09-EF	Submitting Vendor Data Book	5	0%	$1,280.55	01-Oct-22	05-Oct-22
Pipe Support - BK15		81	0%	$6,402.75	12-Jul-22	30-Sep-22
P09-EF	Tendering & Selection	7	0%	$256.11	12-Jul-22	18-Jul-22
P09-EF	Contract Effectiveness / PO	5	0%	$384.17	19-Jul-22	23-Jul-22
P09-EF	Manufacturing / Fabrication / Supply	50	0%	$3,201.38	24-Jul-22	11-Sep-22
P09-EF	Final Inspection	7	0%	$640.28	12-Sep-22	18-Sep-22
P09-EF	Delivery On Site	7	0%	$1,600.69	19-Sep-22	25-Sep-22
P09-EF	Submitting Vendor Data Book	5	0%	$320.14	26-Sep-22	30-Sep-22
Construction		291	0%	$199,219.00	14-Oct-22	31-Jul-23
Wellpad and Access Road		45	0%	$50,800.85	14-Oct-22	27-Nov-22
Access Road		45	0%	$20,320.34	14-Oct-22	27-Nov-22
Wellpad Access Road		45	0%	$18,288.30	14-Oct-22	27-Nov-22
P09-E	Access Road Preparation	5	0%	$10,972.98	14-Oct-22	18-Oct-22
P09-E	Filling and Compaction	5	0%	$914.42	17-Nov-22	22-Nov-22
P09-E	Sub-Base Layer	5	0%	$1,828.83	22-Nov-22	27-Nov-22
Retaining wall		16	0%	$3,657.66	19-Oct-22	03-Nov-22
P09-	Excavation	5	0%	$365.77	19-Oct-22	23-Oct-22
P09-	lean concrete	2	0%	$548.65	24-Oct-22	25-Oct-22
P09-	form working	7	0%	$1,280.18	26-Oct-22	01-Nov-22
P09-	concrete pouring	2	0%	$1,463.06	02-Nov-22	03-Nov-22
Construction of Culvert and Bridge		30	0%	$914.42	19-Oct-22	17-Nov-22
bridge		30	0%	$365.77	19-Oct-22	17-Nov-22
P09	Excavation	5	0%	$36.58	19-Oct-22	23-Oct-22
P09	lean concrete	2	0%	$29.26	24-Oct-22	25-Oct-22
P09	wall	5	0%	$65.84	26-Oct-22	30-Oct-22
P09	reinforcement	3	0%	$73.15	31-Oct-22	02-Nov-22
P09	form working	5	0%	$36.58	02-Nov-22	07-Nov-22
P09	concrete pouring	5	0%	$109.73	07-Nov-22	12-Nov-22
P09	protect stone	3	0%	$7.32	12-Nov-22	15-Nov-22
P09	Backfill	2	0%	$7.32	15-Nov-22	17-Nov-22
culverts		13	0%	$548.65	19-Oct-22	31-Oct-22
P09	pipeway culvert	5	0%	$219.46	19-Oct-22	23-Oct-22
P09	pipeway	4	0%	$164.59	24-Oct-22	27-Oct-22
P09	pipeline culvert	4	0%	$164.59	27-Oct-22	31-Oct-22
Burn Pit Access Road		13	0%	$2,032.03	29-Oct-22	10-Nov-22
P09-E	ROW Preparation	5	0%	$1,117.62	29-Oct-22	02-Nov-22
P09-E	Filling and Compaction	5	0%	$406.41	03-Nov-22	07-Nov-22
P09-E	Sub-Base Layer	3	0%	$508.01	08-Nov-22	10-Nov-22
Wellpad		39	0%	$30,480.51	14-Oct-22	21-Nov-22
Water Supply		10	0%	$2,133.64	14-Oct-22	23-Oct-22
P09-E	Water Supply	10	0%	$2,133.64	14-Oct-22	23-Oct-22
Surface Preparation		5	0%	$4,572.08	17-Nov-22	21-Nov-22
P09-E	Gravel Paving	5	0%	$4,572.08	17-Nov-22	21-Nov-22
Demolition & Disassemble		17	0%	$4,572.08	29-Oct-22	14-Nov-22
P09-E	Demolition of concrete support	12	0%	$1,371.62	29-Oct-22	09-Nov-22
P09-E	Fence Disassmble	5	0%	$3,200.45	10-Nov-22	14-Nov-22
SepticTank		12	0%	$1,219.22	05-Nov-22	16-Nov-22
P09-E	Excavation & Soil Transfer	5	0%	$365.77	05-Nov-22	09-Nov-22
P09-E	Levelling	2	0%	$6.10	10-Nov-22	11-Nov-22

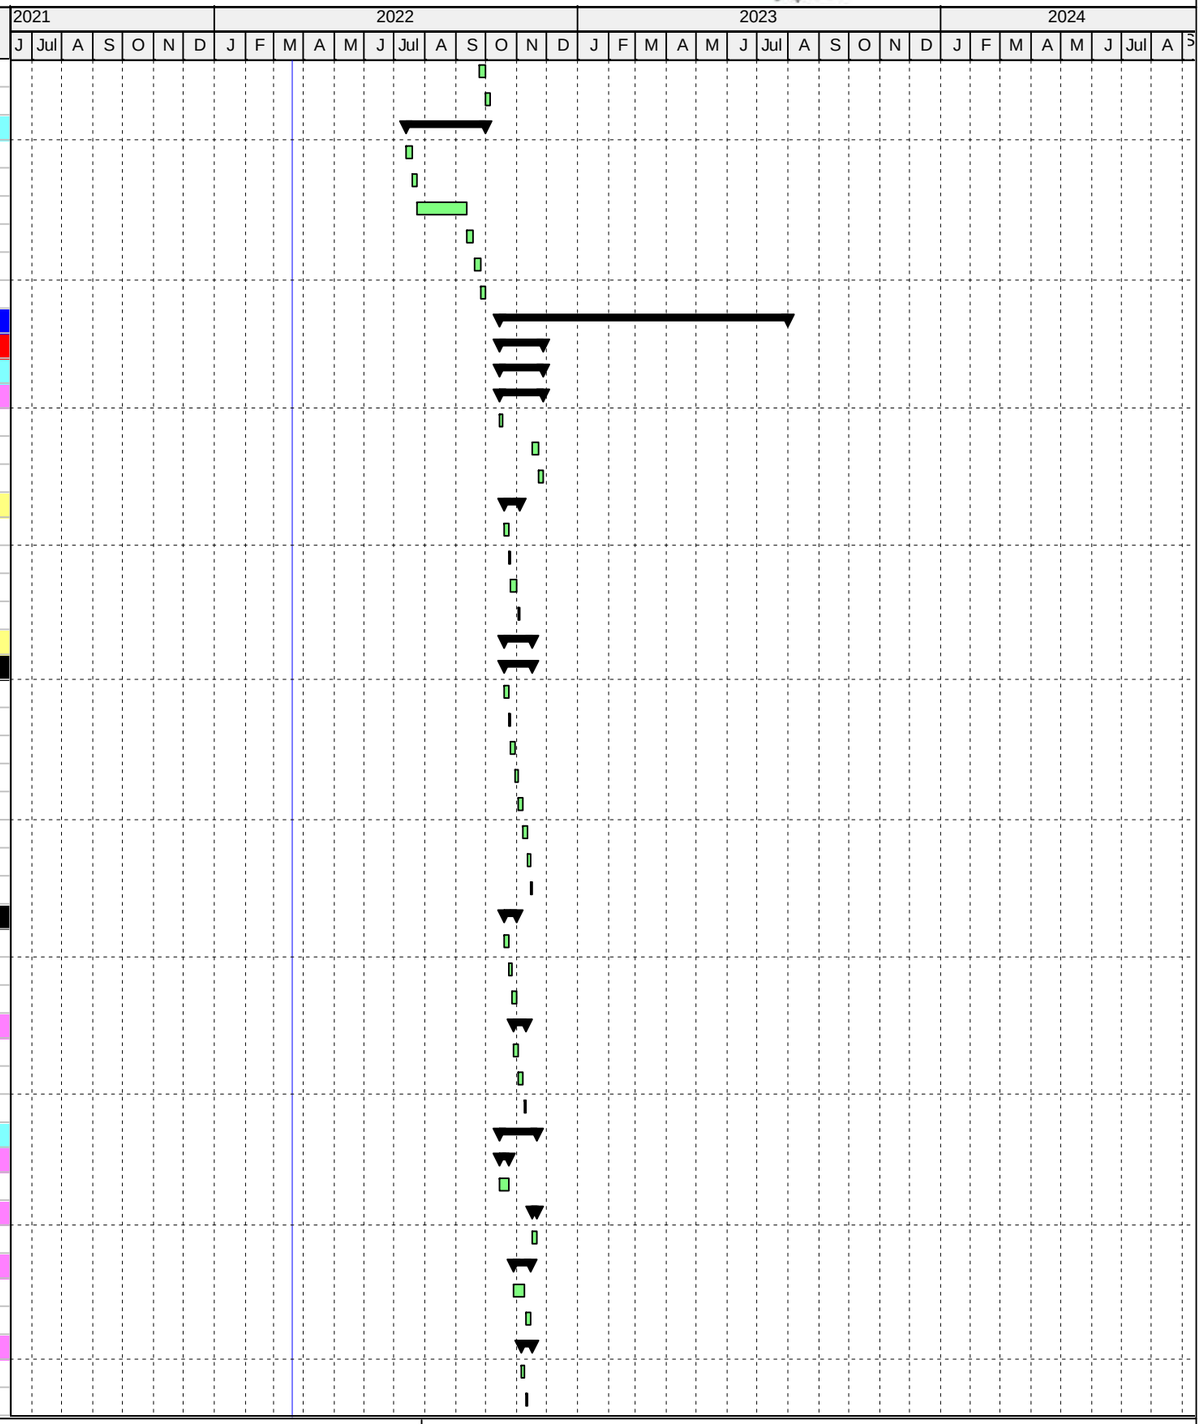


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P09-E	Tank Supply	7	0%	$694.96	05-Nov-22	11-Nov-22
P09-E	Tank Execution	3	0%	$115.83	12-Nov-22	14-Nov-22
P09-E	Backfilling & Compaction	2	0%	$36.58	14-Nov-22	16-Nov-22
Site Preparation		10	0%	$4,572.08	19-Oct-22	28-Oct-22
P09-E	Site Preparation #15	10	0%	$4,572.08	19-Oct-22	28-Oct-22
Civil Work		19	0%	$7,620.13	29-Oct-22	16-Nov-22
P09-E	Excavation and Soil Removal (Cellar)	7	0%	$4,953.08	29-Oct-22	04-Nov-22
P09-E	Installation of Conductor Pipe	5	0%	$457.21	10-Nov-22	14-Nov-22
P09-E	Form Work (Above Cellar)	5	0%	$304.81	05-Nov-22	09-Nov-22
P09-E	Armed Concrete	2	0%	$1,905.03	15-Nov-22	16-Nov-22
Mud Channel		10	0%	$914.42	29-Oct-22	07-Nov-22
P09-E	Excavation & Repair	10	0%	$914.42	29-Oct-22	07-Nov-22
Mud Pit		13	0%	$2,438.44	02-Nov-22	14-Nov-22
P09-E	Soil Removal, Filling and Compaction of Mud Pit Area	5	0%	$853.45	05-Nov-22	09-Nov-22
P09-E	Construction of Mud Pit's Walls	10	0%	$487.69	02-Nov-22	12-Nov-22
P09-E	Supply & Installation sealling Layer	3	0%	$1,097.30	12-Nov-22	14-Nov-22
Burn Pit		13	0%	$914.42	08-Nov-22	20-Nov-22
P09-E	Soil Removal, Triming ,Filling and Compaction of Burn Pit Are	5	0%	$731.53	08-Nov-22	12-Nov-22
P09-E	Construction & Installation of Support	5	0%	$45.72	13-Nov-22	17-Nov-22
P09-E	Welding, Installation and Testing	5	0%	$137.16	15-Nov-22	20-Nov-22
Gasoil Pad		11	0%	$1,524.03	29-Oct-22	08-Nov-22
P09-E	Excavation	2	0%	$304.81	29-Oct-22	30-Oct-22
P09-E	lean concrete	2	0%	$457.21	31-Oct-22	01-Nov-22
P09-E	Form work	4	0%	$152.40	02-Nov-22	05-Nov-22
P09-E	Armed Concrete	3	0%	$609.61	05-Nov-22	08-Nov-22
Wellhead Facility and Flowline		120	0%	$145,429.87	06-Jan-23	05-May-23
Civil, Structure & Architecture		105	0%	$50,900.45	06-Jan-23	20-Apr-23
Civil Works		8	0%	$10,689.10	21-Jan-23	28-Jan-23
P09-E	Steel Works(Wellhead Facilities)	5	0%	$4,810.09	21-Jan-23	25-Jan-23
P09-E	Out Door Post Works For New Gantry (Fundation, Fencing .	3	0%	$2,672.27	26-Jan-23	28-Jan-23
P09-E	Out Door Post Works For Wellhead Post (Fundation, Fencing	5	0%	$2,672.27	21-Jan-23	25-Jan-23
P09-E	Well Pad Fencing	3	0%	$534.45	26-Jan-23	28-Jan-23
Buildings		90	0%	$31,049.28	21-Jan-23	20-Apr-23
Construction of Guard House		80	0%	$8,693.80	21-Jan-23	10-Apr-23
Foundation		50	0%	$2,695.08	21-Jan-23	11-Mar-23
P09	Excavation & Soil Transfer (Removing of Vegetal Soil)	2	0%	$539.02	21-Jan-23	22-Jan-23
P09	Levelling	30	0%	$53.90	23-Jan-23	21-Feb-23
P09	Lean Concrete	2	0%	$269.51	22-Feb-23	23-Feb-23
P09	Reinforced Work	3	0%	$539.02	24-Feb-23	26-Feb-23
P09	Formwork	2	0%	$215.61	27-Feb-23	28-Feb-23
P09	Main Concrete Pouring	5	0%	$1,051.08	01-Mar-23	05-Mar-23
P09	Backfilling & Compaction	6	0%	$26.95	06-Mar-23	11-Mar-23
Structure		17	0%	$3,477.52	12-Mar-23	28-Mar-23
P09	Steel Material Supply	5	0%	$1,738.76	12-Mar-23	16-Mar-23
P09	Shop Fabrication of Steel Structure	5	0%	$695.50	17-Mar-23	21-Mar-23
P09	Structural Installation	5	0%	$695.50	22-Mar-23	26-Mar-23
P09	Structural Painting	2	0%	$347.75	27-Mar-23	28-Mar-23
Architectural		13	0%	$2,521.20	29-Mar-23	10-Apr-23
P09	Wall Execution	2	0%	$1,232.06	29-Mar-23	30-Mar-23

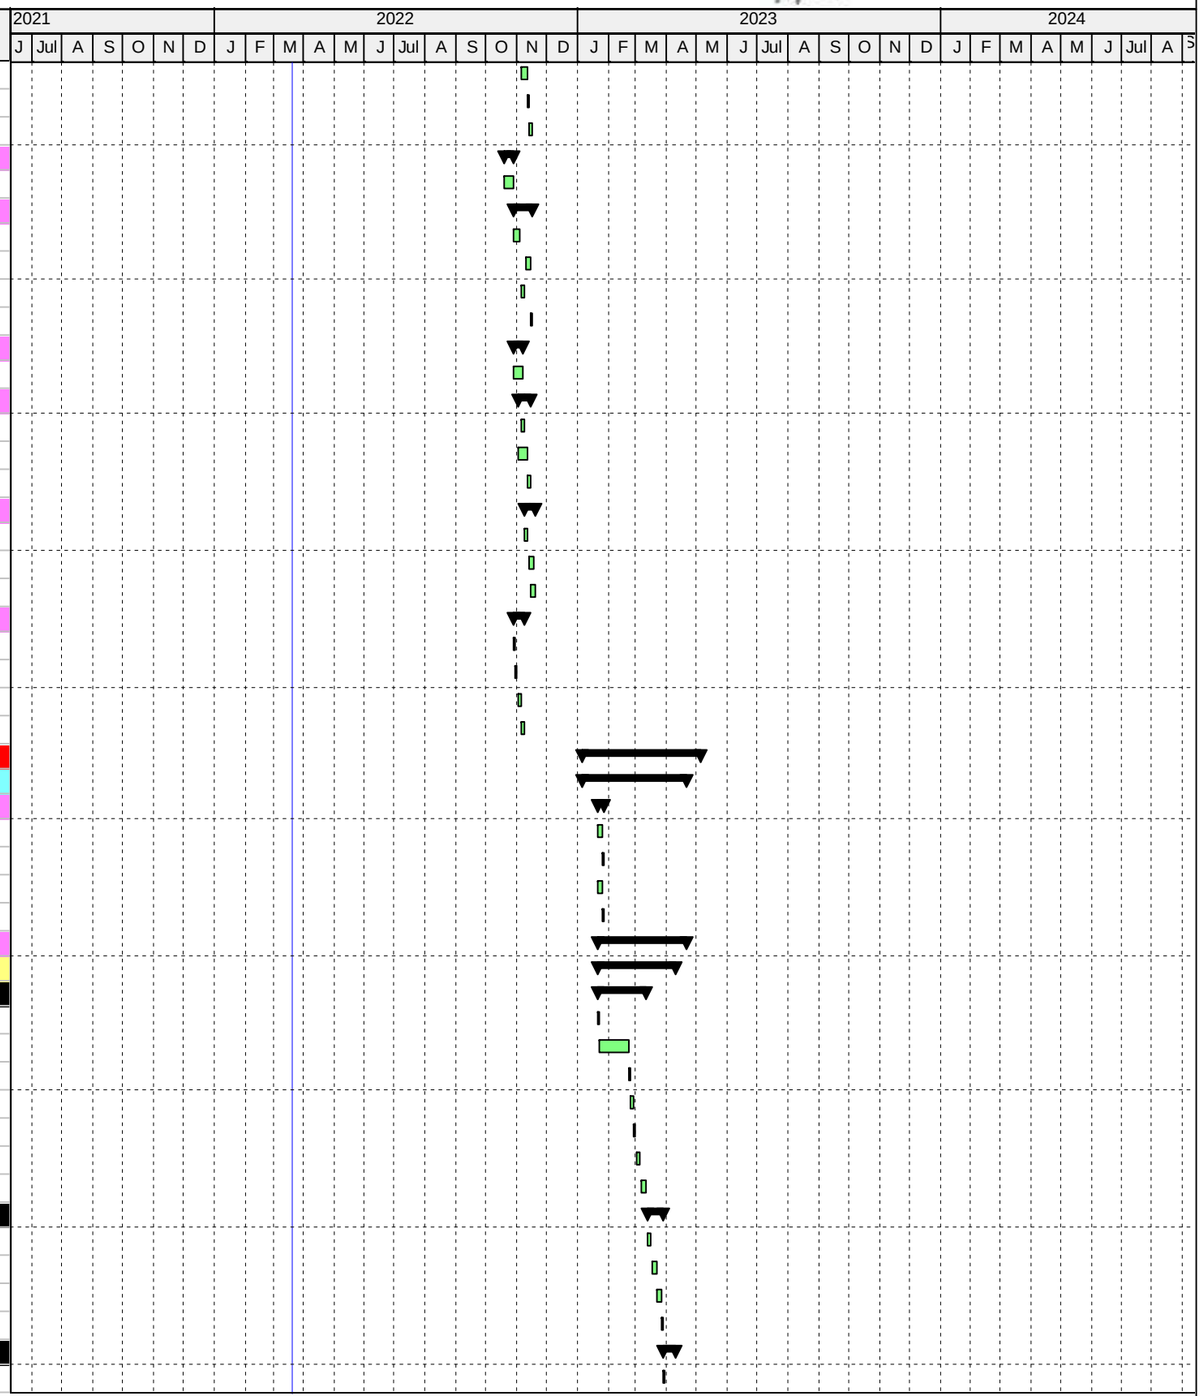


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P09	Roof Covering	3	0%	$300.15	31-Mar-23	02-Apr-23
P09	Roof Execution (Block Joist, Concrete Pouring)	3	0%	$382.75	03-Apr-23	05-Apr-23
P09	Building Walkway (around Building)	3	0%	$129.48	06-Apr-23	08-Apr-23
P09	Joinery (Cornice, Faï?½ade, Plaster)	2	0%	$476.76	09-Apr-23	10-Apr-23
Construction of Switchgear		90	0%	$22,355.48	21-Jan-23	20-Apr-23
Foundation		50	0%	$6,930.20	21-Jan-23	11-Mar-23
P09	Excavation & Soil Transfer (Removing of Vegetal Soil)	2	0%	$1,386.04	21-Jan-23	22-Jan-23
P09	Levelling	30	0%	$138.60	23-Jan-23	21-Feb-23
P09	Lean Concrete	2	0%	$693.02	22-Feb-23	23-Feb-23
P09	Reinforced Work	2	0%	$1,386.04	24-Feb-23	25-Feb-23
P09	Formwork	3	0%	$554.42	26-Feb-23	28-Feb-23
P09	Main Concrete Pouring	5	0%	$2,702.78	01-Mar-23	05-Mar-23
P09	Backfilling & Compaction	6	0%	$69.30	06-Mar-23	11-Mar-23
Structure		17	0%	$8,942.19	12-Mar-23	28-Mar-23
P09	Steel Material Supply	5	0%	$4,471.10	12-Mar-23	16-Mar-23
P09	Shop Fabrication of Steel Structure	5	0%	$1,788.44	17-Mar-23	21-Mar-23
P09	Structural Installation	5	0%	$1,788.44	22-Mar-23	26-Mar-23
P09	Structural Painting	2	0%	$894.22	27-Mar-23	28-Mar-23
Architectural		23	0%	$6,483.09	29-Mar-23	20-Apr-23
P09	Wall Execution	5	0%	$3,168.16	29-Mar-23	02-Apr-23
P09	Roof Covering	5	0%	$771.81	03-Apr-23	07-Apr-23
P09	Roof Execution (Block Joist, Concrete Pouring)	5	0%	$984.22	08-Apr-23	12-Apr-23
P09	Building Walkway (around Building)	3	0%	$332.96	13-Apr-23	15-Apr-23
P09	Joinery (Cornice, Faï?½ade, Plaster)	5	0%	$1,225.94	16-Apr-23	20-Apr-23
Shelters		25	0%	$9,162.08	06-Jan-23	30-Jan-23
Fire Fighting Shelter		25	0%	$7,512.91	06-Jan-23	30-Jan-23
P09-	Fabrication	10	0%	$5,259.03	21-Jan-23	30-Jan-23
P09-	Installation	25	0%	$2,253.87	06-Jan-23	30-Jan-23
Diesel Generator Shelter		25	0%	$1,649.17	06-Jan-23	30-Jan-23
P09-	Fabrication	10	0%	$1,154.42	21-Jan-23	30-Jan-23
P09-	Installation	25	0%	$494.75	06-Jan-23	30-Jan-23
Piping		35	0%	$14,542.99	21-Jan-23	24-Feb-23
P09-EF	Sweep Bend Installation	10	0%	$727.15	21-Jan-23	30-Jan-23
P09-EF	Piping Works (Fit up, Welding, NDT…)	20	0%	$5,817.19	31-Jan-23	19-Feb-23
P09-EF	Valves, Fitting and Spools Installation and Hydrotest	10	0%	$7,998.64	15-Feb-23	24-Feb-23
Electrical		95	0%	$62,534.84	21-Jan-23	25-Apr-23
P09-EF	Over Head line	20	0%	$33,143.47	21-Jan-23	09-Feb-23
P09-EF	Wellhead Electrical Equipment	5	0%	$18,760.45	21-Apr-23	25-Apr-23
P09-EF	Outdoor Post (Wellhead Post)	10	0%	$10,630.92	29-Jan-23	07-Feb-23
Mechanical		7	0%	$14,542.99	31-Jan-23	06-Feb-23
P09-EF	Fuel Oil Storage Drum	7	0%	$7,271.49	31-Jan-23	06-Feb-23
P09-EF	Potable Water Tank	7	0%	$7,271.49	31-Jan-23	06-Feb-23
Pre-commissioning		10	0%	$2,908.60	26-Apr-23	05-May-23
P09-EF	Pre-commissioning	5	0%	$2,617.74	26-Apr-23	30-Apr-23
P09-EF	Ready for Comm.Certificate(RFCC)	5	0%	$290.86	01-May-23	05-May-23
Job Site HSE Supervision (Surface)		140	0%	$398.44	14-Oct-22	02-Mar-23
P09-EP	Job Site HSE Supervision (Surface)	140	0%	$398.44	14-Oct-22	02-Mar-23
Commissioning, Startup & Handover		87	0%	$2,589.85	06-May-23	31-Jul-23
Handover		37	0%	$776.95	25-Jun-23	31-Jul-23

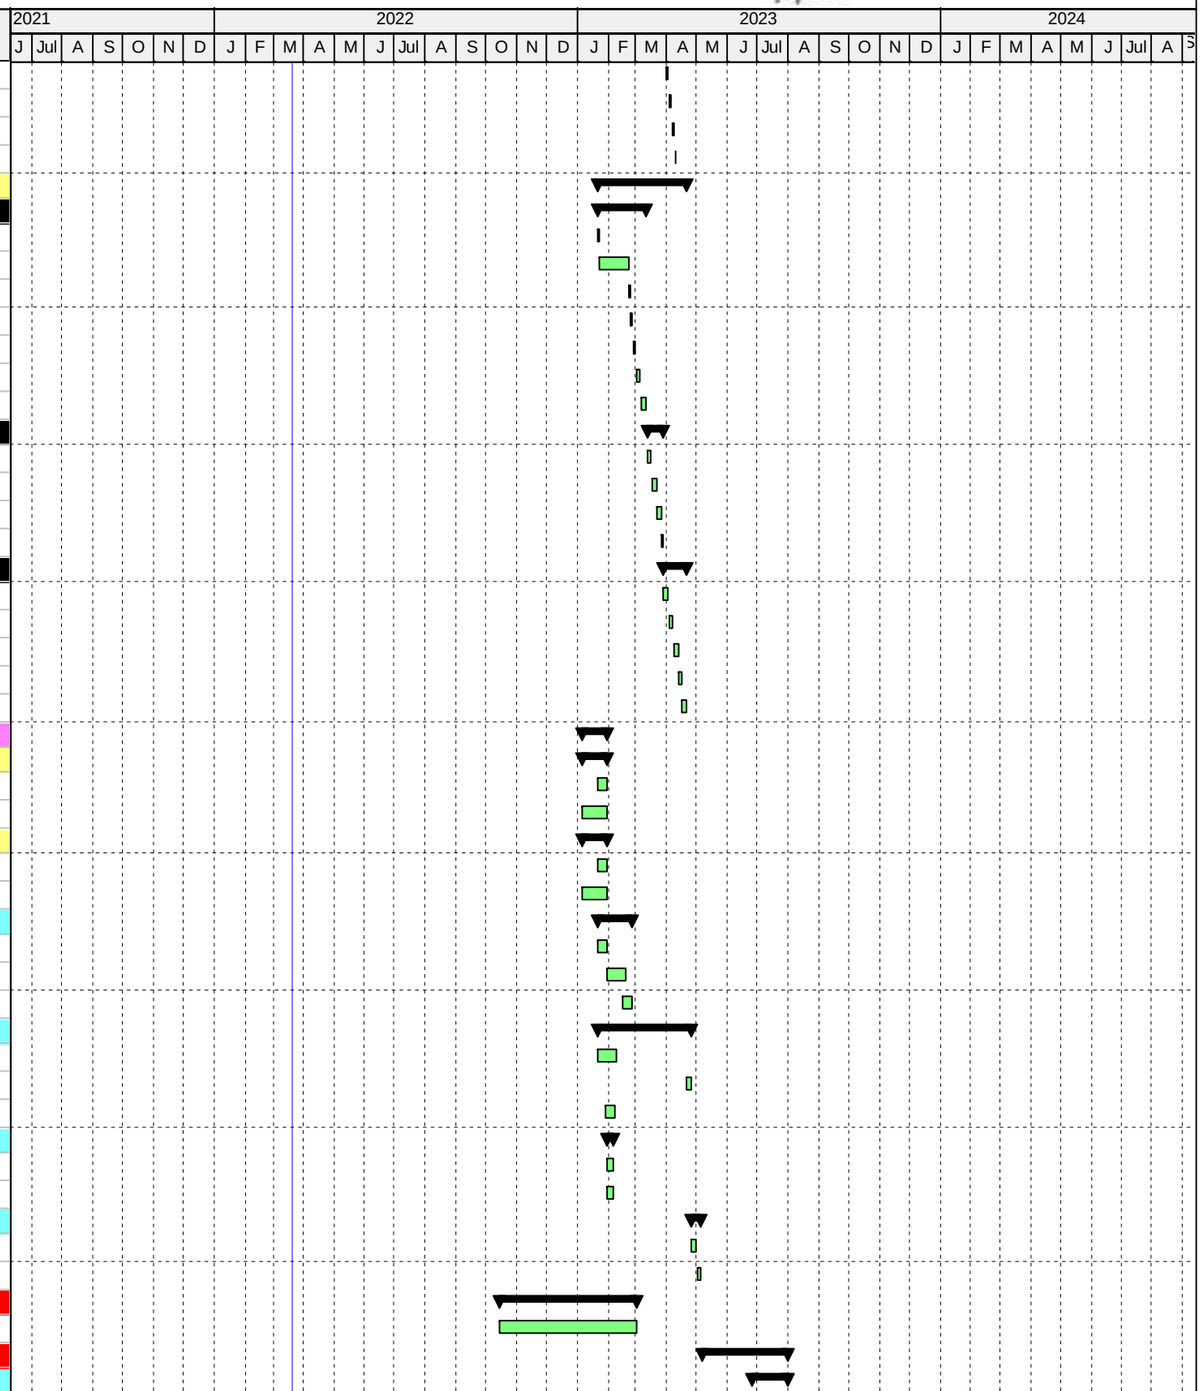


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P09-EF	Compiling & Submitting Final Documentation	20	0%	$233.09	25-Jun-23	14-Jul-23
P09-EF	Training of Operator's Personnel	2	0%	$310.78	15-Jul-23	16-Jul-23
P09-EF	Provisional Acceptance Certificate (PAC)	15	0%	$233.09	17-Jul-23	31-Jul-23
Startup & Performance Test		18	0%	$1,035.94	07-Jun-23	24-Jun-23
P09-EF	Startup & Performance Test Run	3	0%	$828.75	07-Jun-23	09-Jun-23
P09-EF	Start of Production (SOP)	15	0%	$207.19	10-Jun-23	24-Jun-23
Commissioning		32	0%	$776.95	06-May-23	06-Jun-23
P09-EF	Materials & Utilities Ready for Commissioning	3	0%	$38.85	06-May-23	08-May-23
P09-EF	Receiving Facilities Ready for Commissioning	2	0%	$38.85	09-May-23	10-May-23
P09-EF	Permits Obtained for Commissioning	10	0%	$38.85	11-May-23	20-May-23
P09-EF	Integrated Commissioning	2	0%	$621.56	21-May-23	22-May-23
P09-EF	Ready for Startup Certificate (RFSU)	15	0%	$38.85	23-May-23	06-Jun-23
Package 10-Workover # 05		552	0.63%	$434,537.00	24-Jul-21 A	22-Sep-23
ENGINEERING		485	20.43%	$13,382.00	24-Jul-21 A	17-Jul-23
Basic Design Endorsement		30	100%	$669.10	31-Jul-21 A	20-Mar-22
P10-EP	Endorsement Report For Basic Design & Scope of Work	30	100%	$669.10	31-Jul-21 A	20-Mar-22
Value Engineering		44	60%	$401.46	01-Feb-22	20-Mar-22
P10-EP	Value Engineering Study Report	44	60%	$401.46	01-Feb-22	20-Mar-22
Detail Design		439	24.77%	$7,360.10	24-Jul-21 A	26-Dec-22
Process		109	65%	$350.34	15-Nov-21	05-Aug-22
Drawing/Diagram		39	80%	$245.24	15-Nov-21	27-Apr-22
P10-E	P&ID for Diesel Oil Drum- BK05	39	80%	$122.62	15-Nov-21	27-Apr-22
P10-E	P&ID for Potable Water Tank - BK05	39	80%	$122.62	15-Nov-21	27-Apr-22
List		39	60%	$52.55	27-Feb-22	27-Apr-22
P10-E	Line List - BK05	39	60%	$52.55	27-Feb-22	27-Apr-22
Data Sheet		100	0%	$52.55	28-Apr-22	05-Aug-22
P10-E	Process Data Sheets For Instrument Devices - BK05	39	0%	$17.87	28-Apr-22	05-Jun-22
P10-E	Process Data Sheets For Fuel Oil Storage Drum of Well Pads	55	0%	$17.34	12-Jun-22	05-Aug-22
P10-E	Process Data Sheets For Potable Water Tank of Well Pads	45	0%	$17.34	17-Jun-22	31-Jul-22
Mechanical		114	77.78%	$490.92	28-Jul-21 A	26-Jun-22
Basis/Criteria		54	60%	$54.54	28-Jul-21 A	12-May-22
P10-E	Mechanical Design Criteria	54	60%	$54.54	28-Jul-21 A	12-May-22
Specification		79	60%	$81.84	28-Jul-21 A	26-Jun-22
P10-E	Specification For Pressure Vessels	54	60%	$40.92	28-Jul-21 A	01-Jun-22
P10-E	Specification For Atmospheric Above Ground Welded Steel Ta	79	60%	$40.92	28-Jul-21 A	26-Jun-22
Data Sheets		74	60%	$136.38	16-Jan-22	16-Jun-22
P10-E	Data Sheets For Fuel Oil Storage Drum of Well Pads	64	60%	$68.19	16-Jan-22	11-Jun-22
P10-E	Data Sheets For Potable Water Tank of Well Pads	64	60%	$68.19	09-Feb-22	16-Jun-22
Drawing/Diagram		34	100%	$218.16	28-Jul-21 A	09-Apr-22
P10-E	Standard Detail Drawing For Pressure Vessels and Heat Exch	14	100%	$109.08	28-Jul-21 A	09-Apr-22
P10-E	Standard Detail Drawing For Storage Tanks	14	100%	$109.08	28-Jul-21 A	09-Apr-22
HVAC/Plumbing		402	5.17%	$420.26	24-Jul-21 A	26-Dec-22
Basis/Criteria		64	100%	$6.09	24-Jul-21 A	14-May-22
P10-E	HVAC & Plumbing Design Criteria	64	100%	$6.09	24-Jul-21 A	14-May-22
Specification		64	100%	$9.75	24-Jul-21 A	27-Mar-22
P10-E	Specification For HVAC Equipment	64	100%	$6.09	24-Jul-21 A	27-Mar-22
P10-E	Specification For Duct Work & Pipe Work	64	100%	$3.66	24-Jul-21 A	27-Mar-22
Calculation		177	0%	$97.46	13-May-22	05-Nov-22
P10-E	HVAC Calculation Note For Switchgear Building - BK05	44	0%	$48.73	13-May-22	25-Jun-22
P10-E	HVAC Calculation Note For Security Building - BK05	44	0%	$48.73	23-Sep-22	05-Nov-22

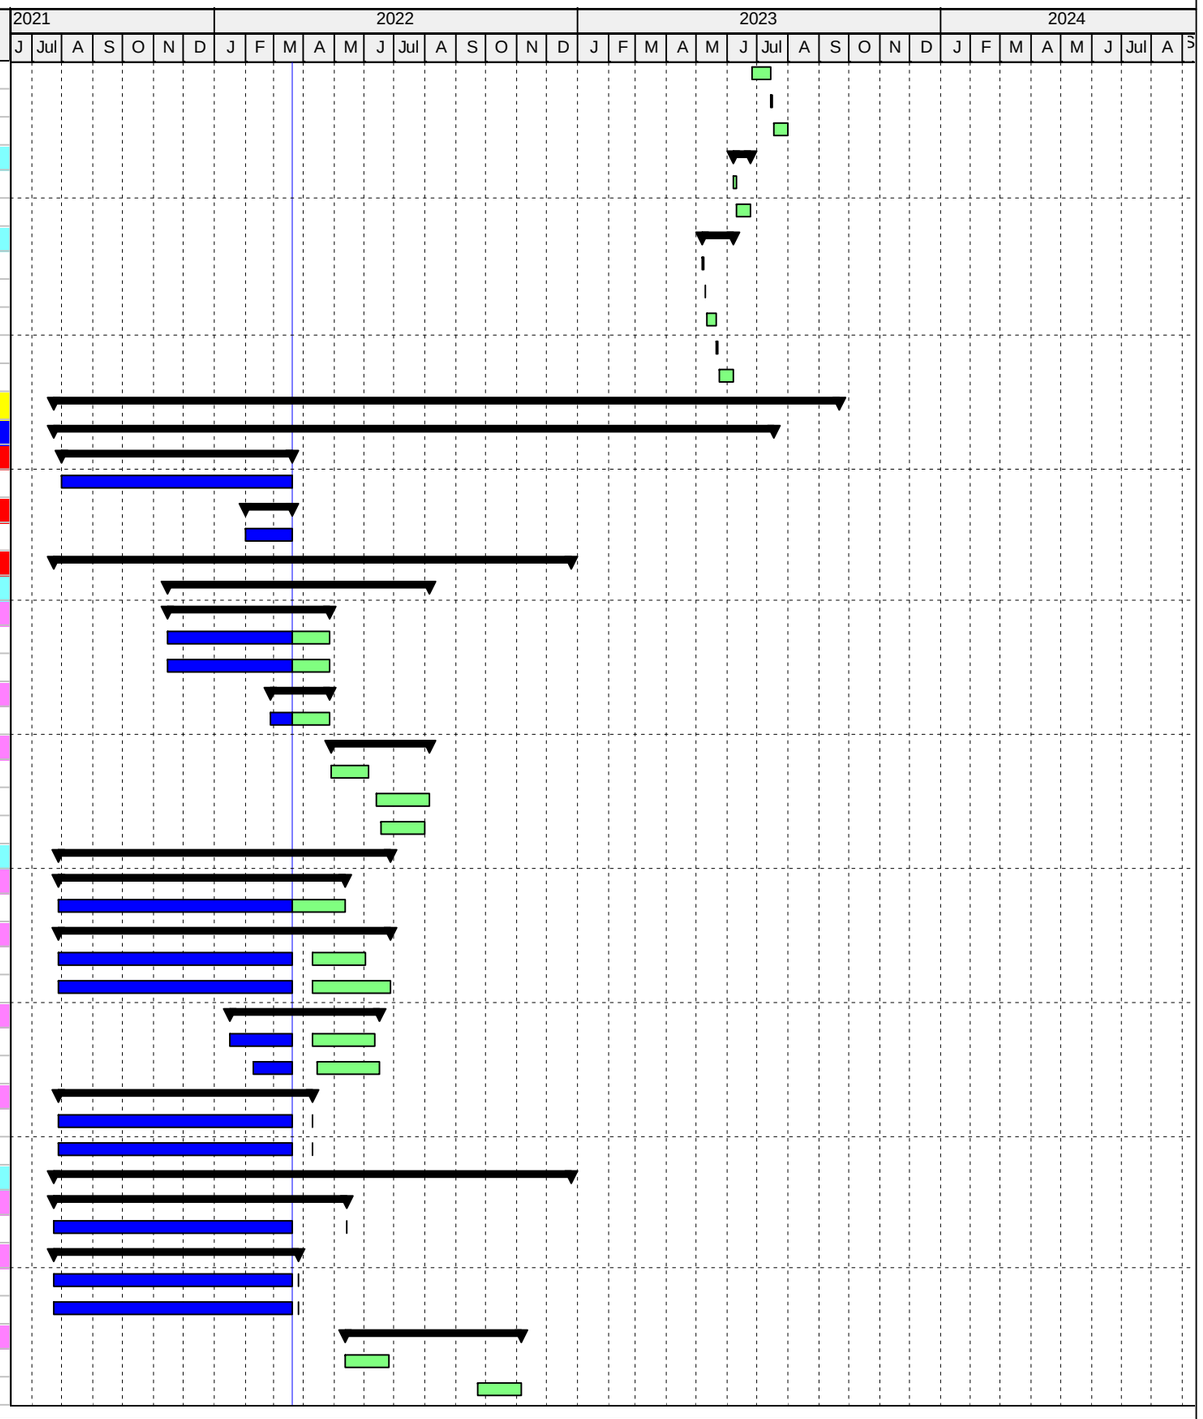


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Data Sheets		44	0%	$48.71	06-Nov-22	19-Dec-22
P10-E	Data Sheets For Main HVAC Equipment - BK05	44	0%	$48.71	06-Nov-22	19-Dec-22
Drawing/Diagram		235	2.82%	$209.54	24-Jul-21 A	19-Dec-22
P10-E	Standard Drawing For HVAC & Plumbing	14	100%	$4.67	24-Jul-21 A	30-Mar-22
P10-E	Symbol & Legend For HVAC & Plumbing	48	60%	$2.03	22-Aug-21	16-May-22
P10-E	HVAC System Layout For Switchgear Building - BK05	44	0%	$50.71	13-May-22	25-Jun-22
P10-E	HVAC System Layout For Security Building - BK05	44	0%	$50.71	23-Sep-22	05-Nov-22
P10-E	Plumbing & Sewage Piping Layout For Switchgear Building - I	44	0%	$50.71	26-Jun-22	08-Aug-22
P10-E	Plumbing & Sewage Piping Layout For Security Building - BK	44	0%	$50.71	06-Nov-22	19-Dec-22
MTO		7	0%	$48.71	20-Dec-22	26-Dec-22
P10-E	MTO For Building HVAC & Plumbing Systems - BK05	7	0%	$48.71	20-Dec-22	26-Dec-22
Piping		117	59.5%	$350.34	24-Jul-21 A	13-Aug-22
Basis/Criteria		39	100%	$7.01	24-Jul-21 A	20-Mar-22
P10-E	Piping Design Criteria	39	100%	$7.01	24-Jul-21 A	20-Mar-22
Specification		49	72.38%	$133.13	24-Jul-21 A	04-May-22
P10-E	Specification For Color Coding and Marking	39	60%	$9.71	09-Aug-21	01-May-22
P10-E	Specification For Transportation, Handling, Storage of pipes	39	80%	$10.58	12-Dec-21	01-May-22
P10-E	Specification For the Design of Piping in Mechanical Packages	45	60%	$9.71	09-Aug-21	03-May-22
P10-E	Specification For Metallic Pipes	39	80%	$9.71	24-Jul-21 A	01-May-22
P10-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$9.71	24-Jul-21 A	24-Mar-22
P10-E	Specification For Painting	39	100%	$11.65	24-Jul-21 A	27-Mar-22
P10-E	Specification For Lining (Internal Protection of Equipment by F	39	60%	$9.71	09-Aug-21	04-May-22
P10-E	Specification For Material Requirements in Sour service	39	60%	$9.71	09-Aug-21	04-May-22
P10-E	Specification For Manual Valves	39	60%	$9.71	09-Aug-21	04-May-22
P10-E	Specification For Plant Piping Systems Pressure Testing	39	60%	$9.71	09-Aug-21	04-May-22
P10-E	Specification For Welding of Plant Piping System	39	60%	$10.58	09-Aug-21	04-May-22
P10-E	Specification For Flexibility Analysis	39	60%	$12.97	09-Aug-21	04-May-22
P10-E	Specification For Piping Cleaning and Flushing	39	100%	$9.71	24-Aug-21	30-Mar-22
Drawing/Diagram		14	100%	$105.10	19-Feb-22	20-Mar-22
P10-E	Standard Pipe Support Drawings	14	100%	$105.10	19-Feb-22	20-Mar-22
MTO		7	0%	$105.10	07-Aug-22	13-Aug-22
P10-E	MTO For Pipes - BK05	7	0%	$105.10	07-Aug-22	13-Aug-22
Electrical		223	27.05%	$1,780.41	24-Jul-21 A	25-Nov-22
Basis/Criteria		54	100%	$10.15	03-Aug-21	20-Mar-22
P10-E	Electrical System Design Criteria	54	100%	$10.15	03-Aug-21	20-Mar-22
Specification		55	100%	$119.82	24-Jul-21 A	30-Mar-22
P10-E	Specification For LV Switchgear & Motor Control Centers	49	100%	$6.21	24-Jul-21 A	24-Mar-22
P10-E	Specification For MV Switchgear	49	100%	$7.12	24-Jul-21 A	24-Mar-22
P10-E	Specification For UPS System	49	100%	$7.12	04-Aug-21	24-Mar-22
P10-E	Specification For Transformers	49	100%	$7.12	24-Jul-21 A	24-Mar-22
P10-E	Specification For DC Charger	49	100%	$7.12	04-Aug-21	24-Mar-22
P10-E	Specification For Earthing & Lightning System	49	100%	$4.53	28-Jul-21 A	24-Mar-22
P10-E	Specification For Lighting & Small Power System	49	100%	$6.22	28-Jul-21 A	27-Mar-22
P10-E	Specification For Bulk Materials	49	100%	$6.22	24-Jul-21 A	27-Mar-22
P10-E	Specification For Diesel Generator	49	100%	$7.12	28-Jul-21 A	27-Mar-22
P10-E	Specification For LV Induction Motors	49	100%	$6.52	24-Jul-21 A	27-Mar-22
P10-E	Specification For Electrical Requirements of Packaged Units	49	100%	$7.12	28-Jul-21 A	27-Mar-22
P10-E	Specification For Capacitor Bank	49	100%	$7.12	24-Jul-21 A	27-Mar-22
P10-E	Specification For Distribution & Lighting Panels	49	100%	$7.12	28-Jul-21 A	30-Mar-22

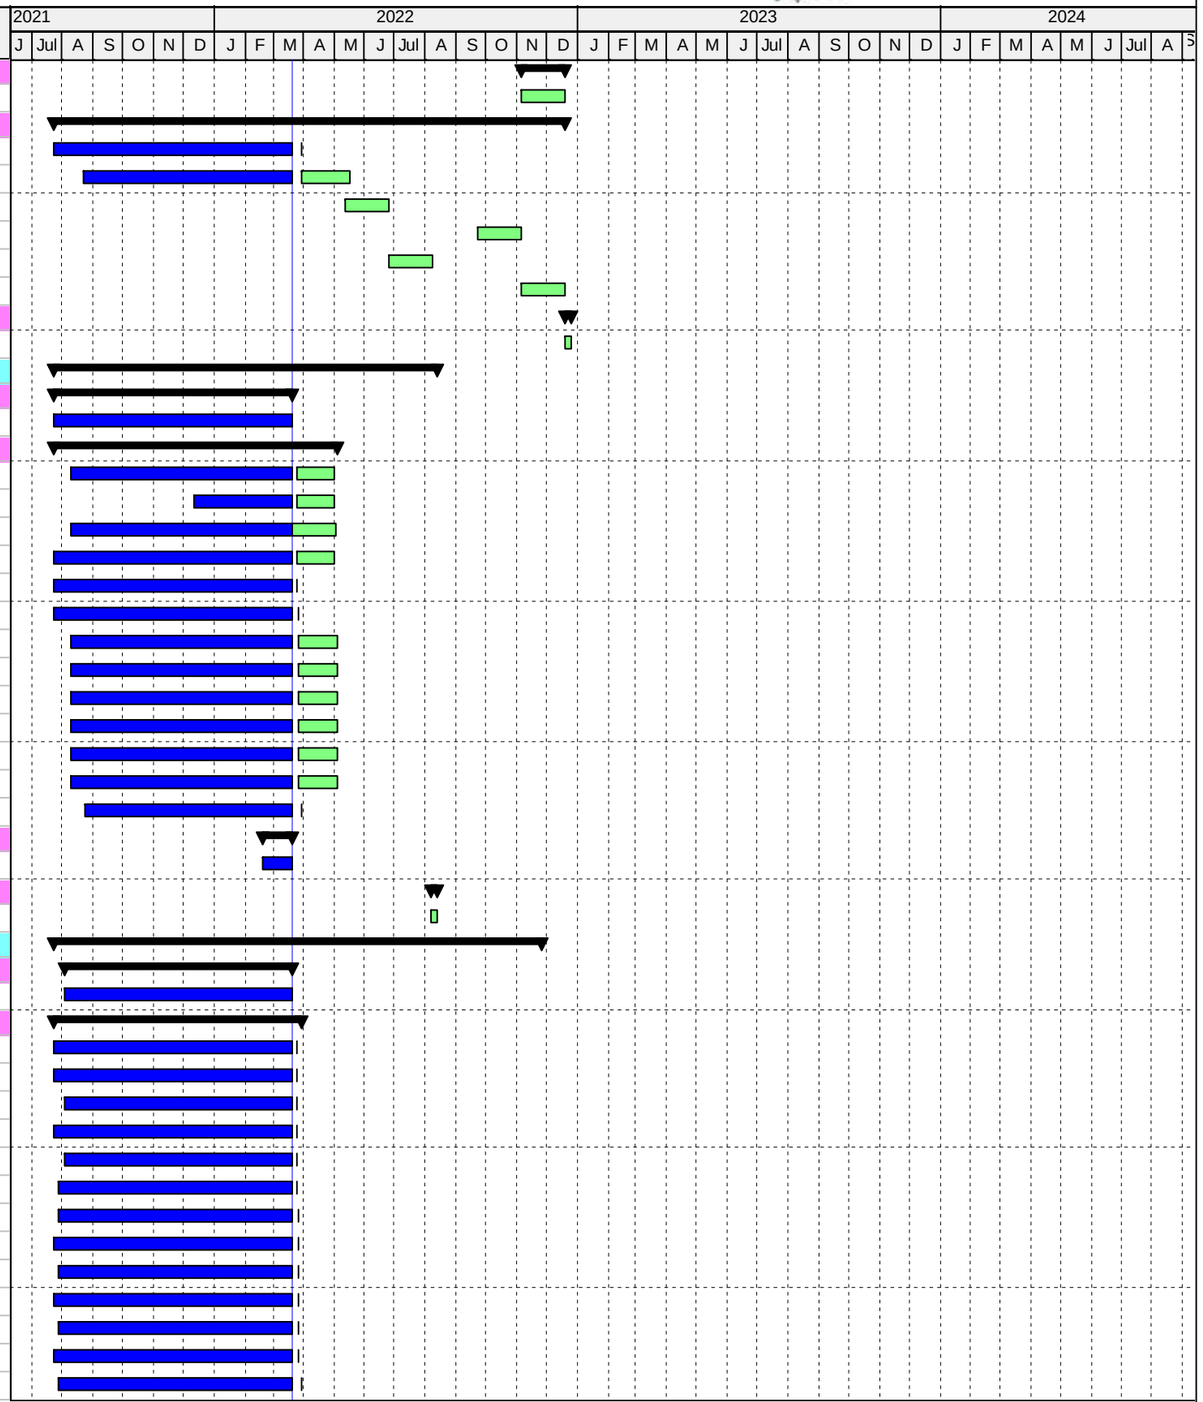


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P10-E	Specification For Power & Control Cables	49	100%	$6.22	24-Jul-21 A	30-Mar-22
P10-E	Specification For Cathodic Protection System	49	100%	$6.22	31-Jul-21 A	30-Mar-22
P10-E	Specification For MV Induction Motors	49	100%	$6.52	24-Jul-21 A	30-Mar-22
P10-E	Specification For NGR	49	100%	$7.12	24-Jul-21 A	30-Mar-22
P10-E	Specification For Overhead Transmission Lines	49	100%	$7.12	28-Jul-21 A	30-Mar-22
Calculation		223	40.68%	$196.38	11-Oct-21 A	16-Jul-22
P10-E	Calculation Note For Lighting System of Well Pads Switchgea	64	0%	$14.49	27-Apr-22	29-Jun-22
P10-E	Calculation Note For Lighting System of Well Pads Security B	64	0%	$14.49	27-Apr-22	29-Jun-22
P10-E	Calculation Note For Lighting System of Well Pads Area	74	0%	$19.34	27-Apr-22	09-Jul-22
P10-E	Calculation Note For Cable Sizing of Well Pads	74	80%	$19.34	02-Nov-21	11-Jun-22
P10-E	Calculation Note For UPS System of Well Pads	74	0%	$19.34	04-May-22	16-Jul-22
P10-E	Calculation Note For Earthing & Lightning System of Well Pac	74	0%	$19.34	19-Apr-22	01-Jul-22
P10-E	Calculation Note For Diesel Generator Sizing of Well Pads	64	60%	$14.49	26-Jan-22	27-May-22
P10-E	Calculation Note For DC Charger of Well Pads	74	80%	$19.34	26-Jan-22	06-Jun-22
P10-E	Calculation Note For LV Capacitor Bank of Well Pads	44	60%	$23.55	29-Jan-22	17-May-22
P10-E	Calculation Note For 11 KV Over Head Line Sag and Tension	44	80%	$16.32	13-Oct-21	17-May-22
P10-E	Calculation Note For 33 KV Over Head Line Sag and Tension	44	80%	$16.32	11-Oct-21 A	17-May-22
Data Sheets		208	67.99%	$166.47	12-Sep-21	10-Aug-22
P10-E	Data Sheets For UPS of Well Pads	59	0%	$14.28	13-Jun-22	10-Aug-22
P10-E	Data Sheets For DC Charger of Well Pads	59	80%	$14.28	29-Jan-22	22-May-22
P10-E	Data Sheets For Diesel Generator of Well Pads	59	60%	$14.28	20-Sep-21	22-May-22
P10-E	Data Sheets For LV Capacitor Bank of Well Pads	59	80%	$14.28	12-Sep-21	17-May-22
P10-E	Data Sheets For LV Switchgear of Well Pads	54	60%	$14.28	19-Feb-22	12-May-22
P10-E	Data Sheets For Power & Control Cables of Well Pads	59	80%	$14.28	13-Sep-21	27-May-22
P10-E	Data Sheets For Power Transformers of Well Pads	59	80%	$14.28	15-Sep-21	17-May-22
P10-E	Data Sheets For Distribution & Lighting Panels of Well Pads	59	60%	$14.28	12-Sep-21	31-Jul-22
P10-E	Data Sheets For 11 KV Over Head Line Equipment	44	80%	$26.10	10-Nov-21	16-Jul-22
P10-E	Data Sheets For 33 KV Over Head Line Equipment	44	80%	$26.10	10-Nov-21	16-Jul-22
Drawing/Diagram		221	29.58%	$472.34	09-Aug-21	25-Nov-22
P10-E	Electrical Legend and Symbols	49	100%	$4.06	09-Aug-21	30-Mar-22
P10-E	Typical Installation Details & Notes For Earthing and Lightning	14	100%	$12.14	25-Aug-21	30-Mar-22
P10-E	Typical Installation Details & Notes For Lighting System	14	100%	$10.77	25-Aug-21	30-Mar-22
P10-E	Typical Installation Details & Notes For Power System	14	100%	$3.59	25-Aug-21	30-Mar-22
P10-E	Installation Details & Notes For Cathodic Protection Systems	74	100%	$3.64	25-Aug-21	30-Mar-22
P10-E	Typical Installation Details For Over Head Line Equipment	14	100%	$8.08	22-Aug-21	19-Apr-22
P10-E	Installation Detail & Notes for Connection OHL to Gantries for	54	60%	$32.88	06-Mar-22	12-May-22
P10-E	Electrical Typical Schematic Diagrams For LV Panels of Well F	14	100%	$20.22	30-Aug-21	20-Mar-22
P10-E	Control Logic Diagram For LV Incomers of Well Pads	74	80%	$16.20	30-Aug-21	01-Jun-22
P10-E	Earthing Layout For Electrical Tower (Gantry) of Well Pads	64	0%	$12.14	16-Jul-22	17-Sep-22
P10-E	Cable Route Layout For Electrical Tower (Gantry) of Well Pac	74	0%	$16.20	16-Jul-22	27-Sep-22
P10-E	Overall Single Line Diagram of Well Pads	79	60%	$20.22	02-Mar-22	21-Jun-22
P10-E	Single Line Diagram For LV Switchgear of Well Pads	74	60%	$16.20	08-Feb-22	16-Jun-22
P10-E	Single Line Diagram For LV Power Distribution Panel of Well	74	0%	$16.20	04-May-22	16-Jul-22
P10-E	Single Line Diagram For DC Charger of Well Pads	74	80%	$16.20	06-Feb-22	16-Jun-22
P10-E	Single Line Diagram For Capacitor Banks of Well Pads	74	60%	$16.20	02-Feb-22	16-Jun-22
P10-E	Interconnection Wiring Diagram of Well Pads	64	0%	$24.28	04-May-22	06-Jul-22
P10-E	Area Lighting & Small Power Layout of Well Pads of Well Pad	74	0%	$16.20	16-Jul-22	27-Sep-22
P10-E	Lighting & Small Power Layout For Switchgear Building of We	64	0%	$12.14	13-May-22	15-Jul-22

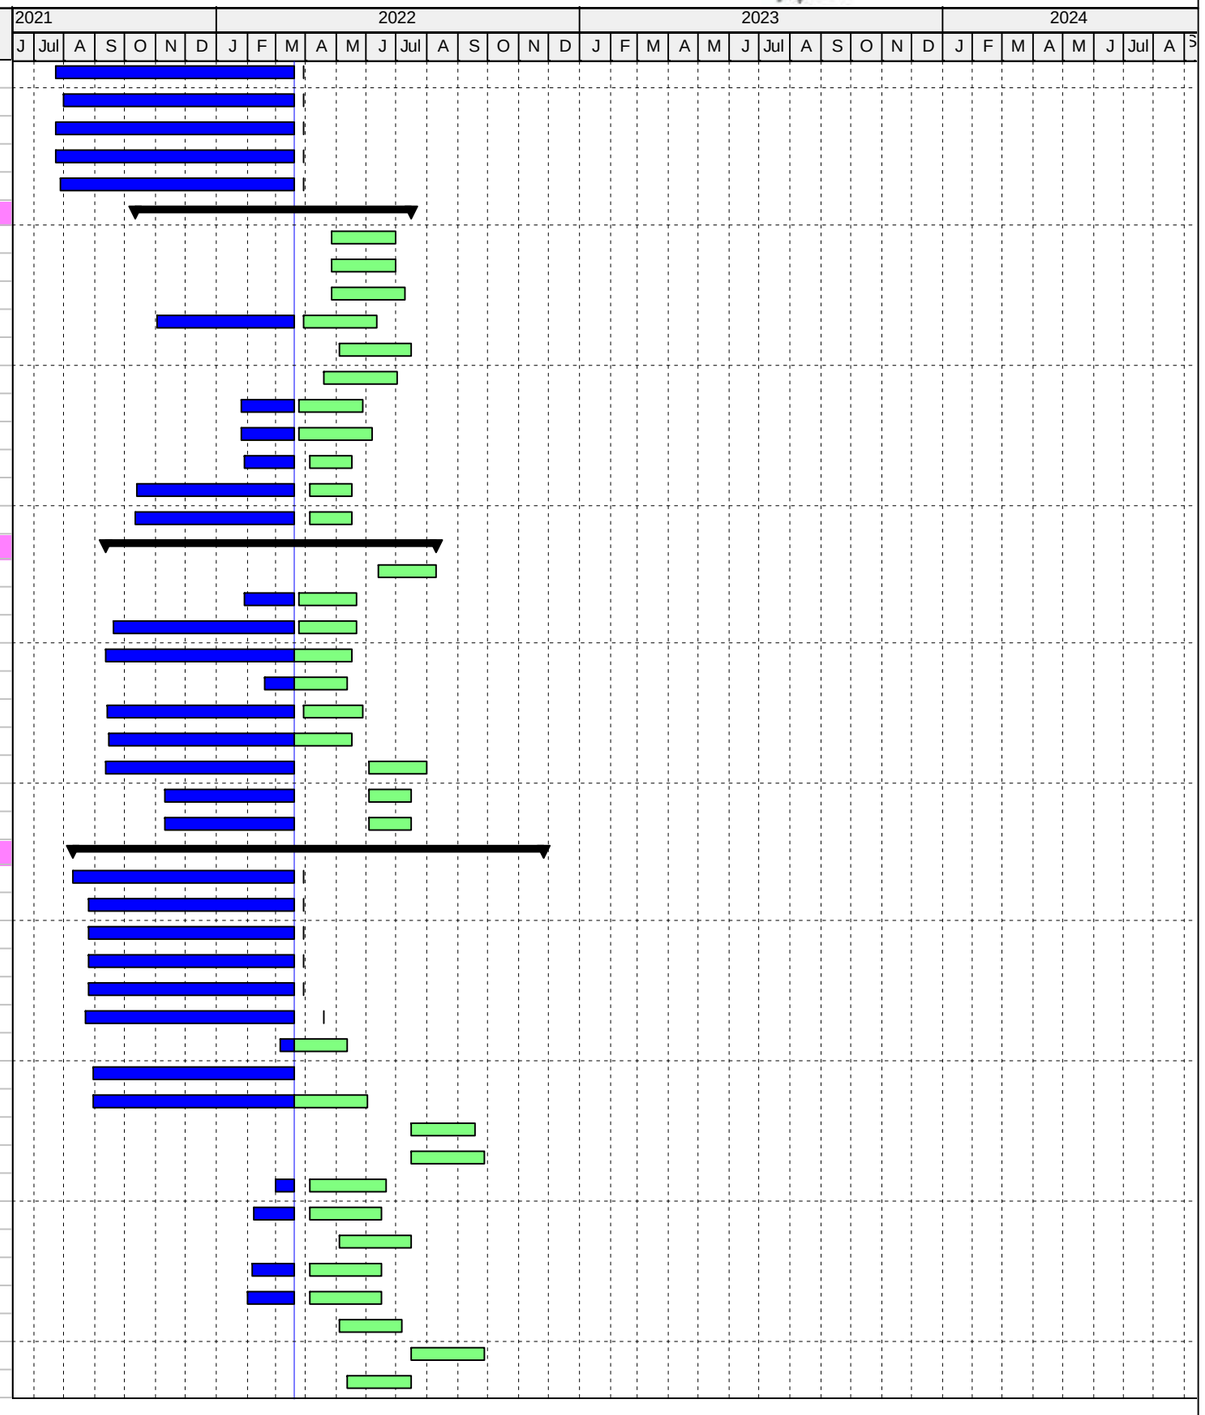


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P10-E	Lighting & Small Power Layout For Security Building of Well P	64	0%	$12.14	23-Sep-22	25-Nov-22
P10-E	Area Electrical Cable Route & Section Layout of Well Pads	79	0%	$20.22	16-Jul-22	02-Oct-22
P10-E	Electrical Cable Route & Section Layout For Switchgear Buildi	74	0%	$39.63	16-Jul-22	27-Sep-22
P10-E	Electrical Equipment Arrangement Layout For Switchgear Buil	79	0%	$24.94	13-May-22	30-Jul-22
P10-E	Earthing & Lightning Layout for well pads	64	0%	$16.34	29-May-22	31-Jul-22
P10-E	11KV Over Head Line Study Report	44	0%	$40.76	01-Aug-22	13-Sep-22
P10-E	33KV Over Head Line Study Report	44	0%	$40.76	08-Jul-22	20-Aug-22
List		113	37.67%	$49.85	25-Jan-22	22-Oct-22
P10-E	Electrical Load List of Well Pads	45	80%	$23.48	25-Jan-22	03-May-22
P10-E	Electrical Power & Control Cable List of Well Pads	74	0%	$13.19	10-Aug-22	22-Oct-22
P10-E	Cable Drum Schedule and Cutting List of Well Pads	74	0%	$13.19	10-Aug-22	22-Oct-22
Report		133	0%	$332.76	04-May-22	13-Sep-22
P10-E	Electrical Network (Load Flow, Motor Starting & Short Circuit)	54	0%	$95.24	04-May-22	26-Jun-22
P10-E	Relay Coordination & Setting Study Report of Well Pads	54	0%	$95.24	27-Jun-22	19-Aug-22
P10-E	11KV Over Head Line Study Report	44	0%	$71.14	01-Aug-22	13-Sep-22
P10-E	33KV Over Head Line Study Report	44	0%	$71.14	08-Jul-22	20-Aug-22
MTO		146	0%	$432.64	06-Jun-22	29-Oct-22
P10-E	MTO For Transmission Over Head Line - BK05	7	0%	$99.94	16-Jun-22	22-Jun-22
P10-E	MTO For Lighting & Small Powers - BK05	7	0%	$66.54	06-Jun-22	12-Jun-22
P10-E	MTO For Power & Control Cables - BK05	7	0%	$66.54	23-Oct-22	29-Oct-22
P10-E	MTO For Tray/Ladder and Accessories - BK05	7	0%	$66.54	10-Aug-22	16-Aug-22
P10-E	MTO For Electrical Bulk Items - BK05	7	0%	$66.54	18-Oct-22	24-Oct-22
P10-E	MTO For Earthing & Lightning Systems - BK05	7	0%	$66.54	15-Aug-22	21-Aug-22
Architecture		277	16.97%	$771.34	08-Feb-22	22-Sep-22
Basis/Criteria		74	60%	$155.89	08-Feb-22	01-Jun-22
P10-E	Architectural Design Criteria	74	60%	$155.89	08-Feb-22	01-Jun-22
Specification		44	0%	$194.76	20-Mar-22	02-May-22
P10-E	Buildings General Specification	44	0%	$194.76	20-Mar-22	02-May-22
Drawing/Diagram		213	20%	$186.97	18-May-22	22-Sep-22
P10-E	Architectural Drawing For Diesel Generator Shelter of Well P.	44	0%	$62.34	23-May-22	05-Jul-22
P10-E	Architectural Drawing For Switchgear Building of Well Pads -	44	60%	$62.32	18-May-22	12-May-22
P10-E	Architectural Drawing For Security Building of Well Pads - BK	44	0%	$62.32	10-Aug-22	22-Sep-22
MTO		7	0%	$233.72	04-Jul-22	10-Jul-22
P10-E	MTO For Architectural Works - BK05	7	0%	$233.72	04-Jul-22	10-Jul-22
Civil		139	15.14%	$739.69	01-Aug-21	05-Aug-22
Basis/Criteria		97	20%	$2.59	13-Feb-22	22-May-22
P10-E	Civil Design Criteria	64	60%	$0.86	13-Feb-22	22-May-22
P10-E	Design Criteria for Sewerage & Drainage	44	0%	$0.86	24-Mar-22	06-May-22
P10-E	Design Criteria for Road and Paving	44	0%	$0.86	27-Mar-22	09-May-22
Specification		94	72%	$13.24	09-Aug-21	06-Jun-22
P10-E	Specification For Civil Works	79	0%	$1.32	20-Mar-22	06-Jun-22
P10-E	Specification For Road & Paving	64	80%	$2.65	09-Aug-21	22-May-22
P10-E	Specification For Fence & Gate	64	100%	$2.65	18-Sep-21	20-Mar-22
P10-E	Specification For Earth Work	64	80%	$2.65	09-Aug-21	22-May-22
P10-E	Specification For Sewerage & Drainage	64	100%	$2.65	09-Aug-21	20-Mar-22
P10-E	Specification For Geological & Geotechnical Survey	44	0%	$1.32	20-Mar-22	02-May-22
Drawing/Diagram		132	18.08%	$563.94	01-Aug-21	29-Jul-22
P10-E	Standard Drawing For Civil Works	64	0%	$6.15	30-Mar-22	01-Jun-22
P10-E	Standard Drawing For Slope Protection Details	64	100%	$6.15	22-Aug-21	30-Mar-22

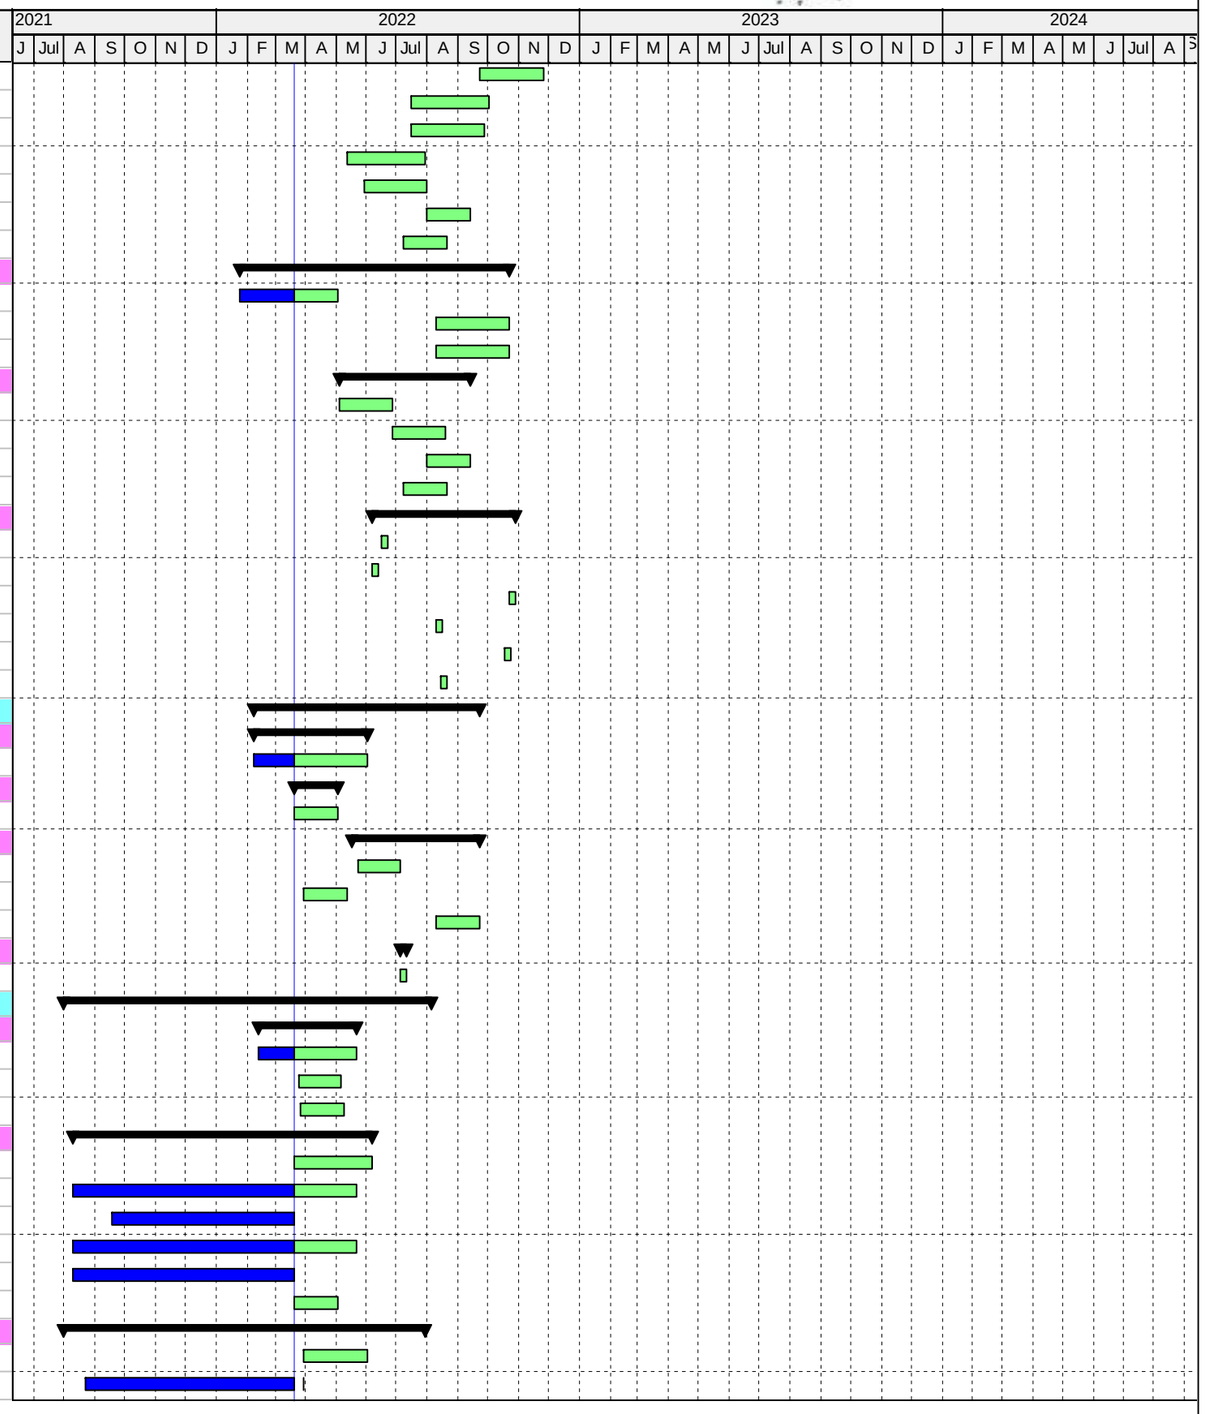


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P10-E	Standard Drawing For Roads	64	80%	$6.15	22-Aug-21	01-Jun-22
P10-E	Standard Drawing For Electrical Cable Trench	64	100%	$6.15	22-Aug-21	30-Mar-22
P10-E	Standard Drawing For Manholes	64	80%	$6.15	22-Aug-21	01-Jun-22
P10-E	Standard Drawing For Catch Basins	64	80%	$6.15	22-Aug-21	05-Jun-22
P10-E	Standard Drawing For Sewerage & Drainage Details	64	60%	$6.15	02-Feb-22	05-Jun-22
P10-E	Standard Drawing For Civil Underground Crossings	38	60%	$10.43	07-Feb-22	10-May-22
P10-E	Standard Drawing For Fence & Gate Details	64	100%	$6.15	18-Sep-21	03-Apr-22
P10-E	Standard Drawing For Concrete Continues Weight	38	100%	$10.21	01-Aug-21	20-Mar-22
P10-E	Standard Drawing For Major Floodway Crossing	38	0%	$10.21	03-Apr-22	10-May-22
P10-E	Standard Drawing For Culvert & Details	38	100%	$10.21	25-Sep-21	03-Apr-22
P10-E	Standard Drawing For Valve Box	38	100%	$10.21	12-Jan-22	03-Apr-22
P10-E	Standard Drawing For Fire Hydrant Pit	38	60%	$10.21	13-Mar-22	10-May-22
P10-E	Standard Drawing For Cable Pull Pit	64	0%	$0.00	03-Apr-22	05-Jun-22
P10-E	Standard Drawing For Pavings	38	60%	$10.21	08-Jan-22	10-May-22
P10-E	Standard Drawing For Earth Pit	38	60%	$10.21	13-Feb-22	10-May-22
P10-E	Standard Detail For Pipe Bedding	64	100%	$6.15	22-Aug-21	03-Apr-22
P10-E	Standard Details of Miscellaneous Items	64	60%	$6.15	06-Mar-22	05-Jun-22
P10-E	BINAK Oil Field Project Overall Well Location/Facilities Layou	54	0%	$4.62	20-Mar-22	12-May-22
P10-E	Civil and Structural drawings - BK05	44	0%	$130.66	20-Mar-22	02-May-22
P10-E	General Civil Layout - BK05	44	0%	$130.66	16-Jun-22	29-Jul-22
P10-E	Rough Grading Plans -BK05	44	0%	$154.63	16-Jun-22	29-Jul-22
Report		44	0%	$96.46	03-May-22	15-Jun-22
P10-E	Site Visit Report (Civil Work) - BK05	44	0%	$96.46	03-May-22	15-Jun-22
MTO		7	0%	$63.47	30-Jul-22	05-Aug-22
P10-E	MTO For Civil Works - BK05	7	0%	$63.47	30-Jul-22	05-Aug-22
Structure		282	15.19%	$981.10	08-Aug-21	26-Dec-22
Basis/Criteria		64	0%	$10.69	20-Mar-22	22-May-22
P10-E	Structural Design Criteria	64	0%	$3.57	20-Mar-22	22-May-22
P10-E	Design Criteria For Steel Structure	44	0%	$3.56	20-Mar-22	02-May-22
P10-E	Design Criteria For Load & Forces	44	0%	$3.56	20-Mar-22	02-May-22
Specification		98	98.97%	$81.73	14-Aug-21	26-May-22
P10-E	Specification For Concrete Work	64	80%	$1.19	14-Aug-21	26-May-22
P10-E	Specification For Storage Tank Foundation	38	100%	$30.97	23-Nov-21	24-Mar-22
P10-E	Specification for Fabrication of Steel Structures	64	100%	$0.61	24-Jan-22	24-Mar-22
P10-E	Specification For Grouting	64	100%	$23.98	14-Aug-21	24-Mar-22
P10-E	Specification for Erection of Steel Structures	64	100%	$0.80	24-Jan-22	24-Mar-22
P10-E	Specification for Fireproofing	64	100%	$23.57	18-Sep-21	24-Mar-22
P10-E	Specification For Steel Structural Works	37	0%	$0.60	20-Mar-22	25-Apr-22
Drawing/Diagram		265	10.78%	$632.71	08-Aug-21	19-Dec-22
P10-E	Standard Drawing For Fire Proofing	64	100%	$4.05	08-Aug-21	03-Apr-22
P10-E	Standard Drawing For Anchor Bolts	64	100%	$4.05	15-Dec-21	03-Apr-22
P10-E	Standard Drawing For Steel Stairs	64	100%	$4.05	18-Dec-21	03-Apr-22
P10-E	Standard Drawing For Operating Platform	38	100%	$4.81	27-Dec-21	30-Mar-22
P10-E	Standard Drawing For Handrail	38	100%	$6.83	18-Dec-21	30-Mar-22
P10-E	Standard Drawing For Insert Plates in Concrete	38	100%	$6.83	08-Aug-21	30-Mar-22
P10-E	Standard Details For Ladder & Safety Cage	64	100%	$4.05	15-Dec-21	03-Apr-22
P10-E	Standard Drawing For Lighting pole foundation Plan & Details	38	60%	$6.83	29-Jan-22	06-May-22
P10-E	General Notes - Steel Structures	38	100%	$4.81	25-Jan-22	30-Mar-22
P10-E	General Notes - Reinforced Concrete Structures	38	100%	$6.83	20-Dec-21	30-Mar-22

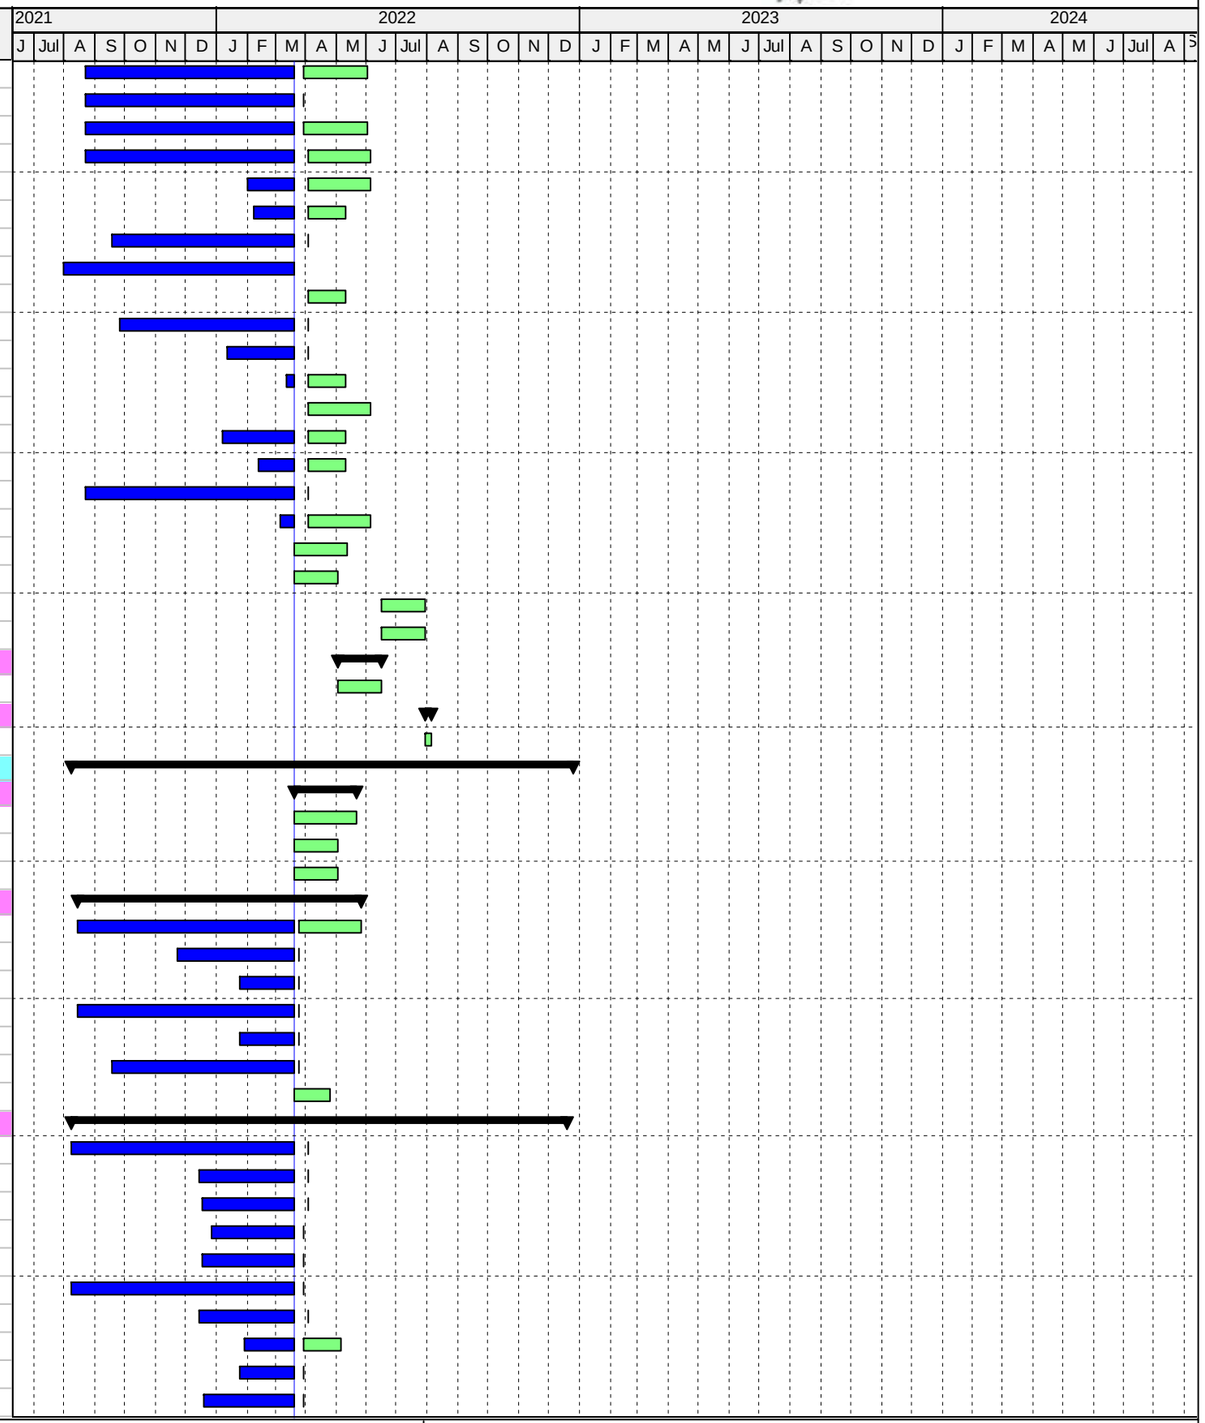


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P10-E	Standard Drawing For Structural Built-up Sections	44	80%	$6.83	04-Dec-21	12-May-22
P10-E	Standard Drawing For Steel Flooring, Grating and Chequere	44	100%	$6.83	05-Jan-22	30-Mar-22
P10-E	Concrete Reinforcement Shape Code	44	0%	$6.83	30-Mar-22	12-May-22
P10-E	Standard Drawing For Septic Tank	44	80%	$6.83	22-Jan-22	12-May-22
P10-E	Fuel Oil Storage Drum Detail Drawing For Well Pads - BK-05	44	0%	$69.03	04-May-22	16-Jun-22
P10-E	Foundation Drawing For Security Building For Well Pads - BK	44	0%	$69.03	23-Sep-22	05-Nov-22
P10-E	Structural Drawing For Security Building For Well Pads - BK-(	44	0%	$69.03	06-Nov-22	19-Dec-22
P10-E	Foundation Drawing For Switchgear Building For Well Pads -	44	0%	$69.03	13-May-22	25-Jun-22
P10-E	Structural Drawing For Switchgear Building For Well Pads - E	44	0%	$69.03	26-Jun-22	08-Aug-22
P10-E	Foundation Drawing For Potable Water Tank For Well Pads -	44	0%	$69.03	09-May-22	21-Jun-22
P10-E	Foundation Drawing For Diesel Generator Shelter For Well F	44	0%	$69.03	06-Jul-22	18-Aug-22
P10-E	Structural Drawing For Diesel Generator Shelter For Well Pa	44	0%	$69.03	19-Aug-22	01-Oct-22
MTO		7	0%	$255.97	20-Dec-22	26-Dec-22
P10-E	MTO For Structural Works - BK05	7	0%	$255.97	20-Dec-22	26-Dec-22
General		137	7.46%	$1,475.70	11-Aug-21	03-Aug-22
Geotechnic		104	8%	$1,180.56	11-Aug-21	02-May-22
Procedure/Plan		44	100%	$94.44	11-Aug-21	19-Apr-22
P10-	Geotechnical Investigation Plan for Well Pads	44	100%	$94.44	11-Aug-21	19-Apr-22
Report		44	0%	$1,086.12	20-Mar-22	02-May-22
P10-	Geotechnical Investigation Report - BK05	44	0%	$1,086.12	20-Mar-22	02-May-22
Survey		5	0%	$147.57	30-Jul-22	03-Aug-22
Drawing/Diagram		5	0%	$147.57	30-Jul-22	03-Aug-22
P10-	Over Head Line Plan and Profile - BK05	5	0%	$147.57	30-Jul-22	03-Aug-22
QC/QA		116	10.58%	$147.57	20-Sep-21	13-Jul-22
QC Management		116	38.9%	$12.00	08-Dec-21	13-Jul-22
P10-	Project Audit Procedure	44	0%	$0.60	20-Mar-22	02-May-22
P10-	Specification For Final Data Book (FDB) Requirements	44	0%	$0.60	20-Mar-22	02-May-22
P10-	Non Conformance Control Procedure	36	0%	$0.60	03-May-22	07-Jun-22
P10-	Corrective Action Procedure	36	0%	$0.60	08-Jun-22	13-Jul-22
P10-	Material Reciving, Storage, Handling Procedure	39	60%	$0.60	20-Feb-22	27-Apr-22
P10-	Packing, Marking, Transportation Procedure	39	0%	$0.60	20-Mar-22	27-Apr-22
P10-	Criticality Assessment Procedure	39	0%	$2.40	20-Mar-22	27-Apr-22
P10-	Project Quality Plan	44	80%	$5.40	08-Dec-21	02-May-22
P10-	Technical Query Procedure	44	0%	$0.60	30-Mar-22	12-May-22
QC General Document		55	8.57%	$17.52	28-Nov-21	16-May-22
P10-	Quality Control Plan (QCP)	39	60%	$2.50	28-Nov-21	27-Apr-22
P10-	Specification for Welding Procedure	44	0%	$2.50	03-Apr-22	16-May-22
P10-	Heat Treatment Procedure (Pre Heating , PWHT)	44	0%	$2.50	03-Apr-22	16-May-22
P10-	Welder Performance Qualification Test (WQT) Procedure	44	0%	$2.50	03-Apr-22	16-May-22
P10-	NDT Procedure	44	0%	$2.50	03-Apr-22	16-May-22
P10-	Surface Preparation and Coating/Painting Procedure	44	0%	$2.50	03-Apr-22	16-May-22
P10-	Control of Inspection Measuring and Test Equipment Procedu	44	0%	$2.49	03-Apr-22	16-May-22
QC Discipline Document		95	7.99%	$118.06	20-Sep-21	29-Jun-22
Piping		95	0%	$29.51	27-Mar-22	29-Jun-22
P10	ITP For Piping Works	44	0%	$2.95	27-Mar-22	09-May-22
P10	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$3.32	03-Apr-22	16-May-22
P10	PIPING WPS (Welding Procedure Specification)	44	0%	$3.32	03-Apr-22	16-May-22
P10	PIPING PQR (Procedure Qualification Record)	44	0%	$3.32	03-Apr-22	16-May-22
P10	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$3.32	03-Apr-22	16-May-22

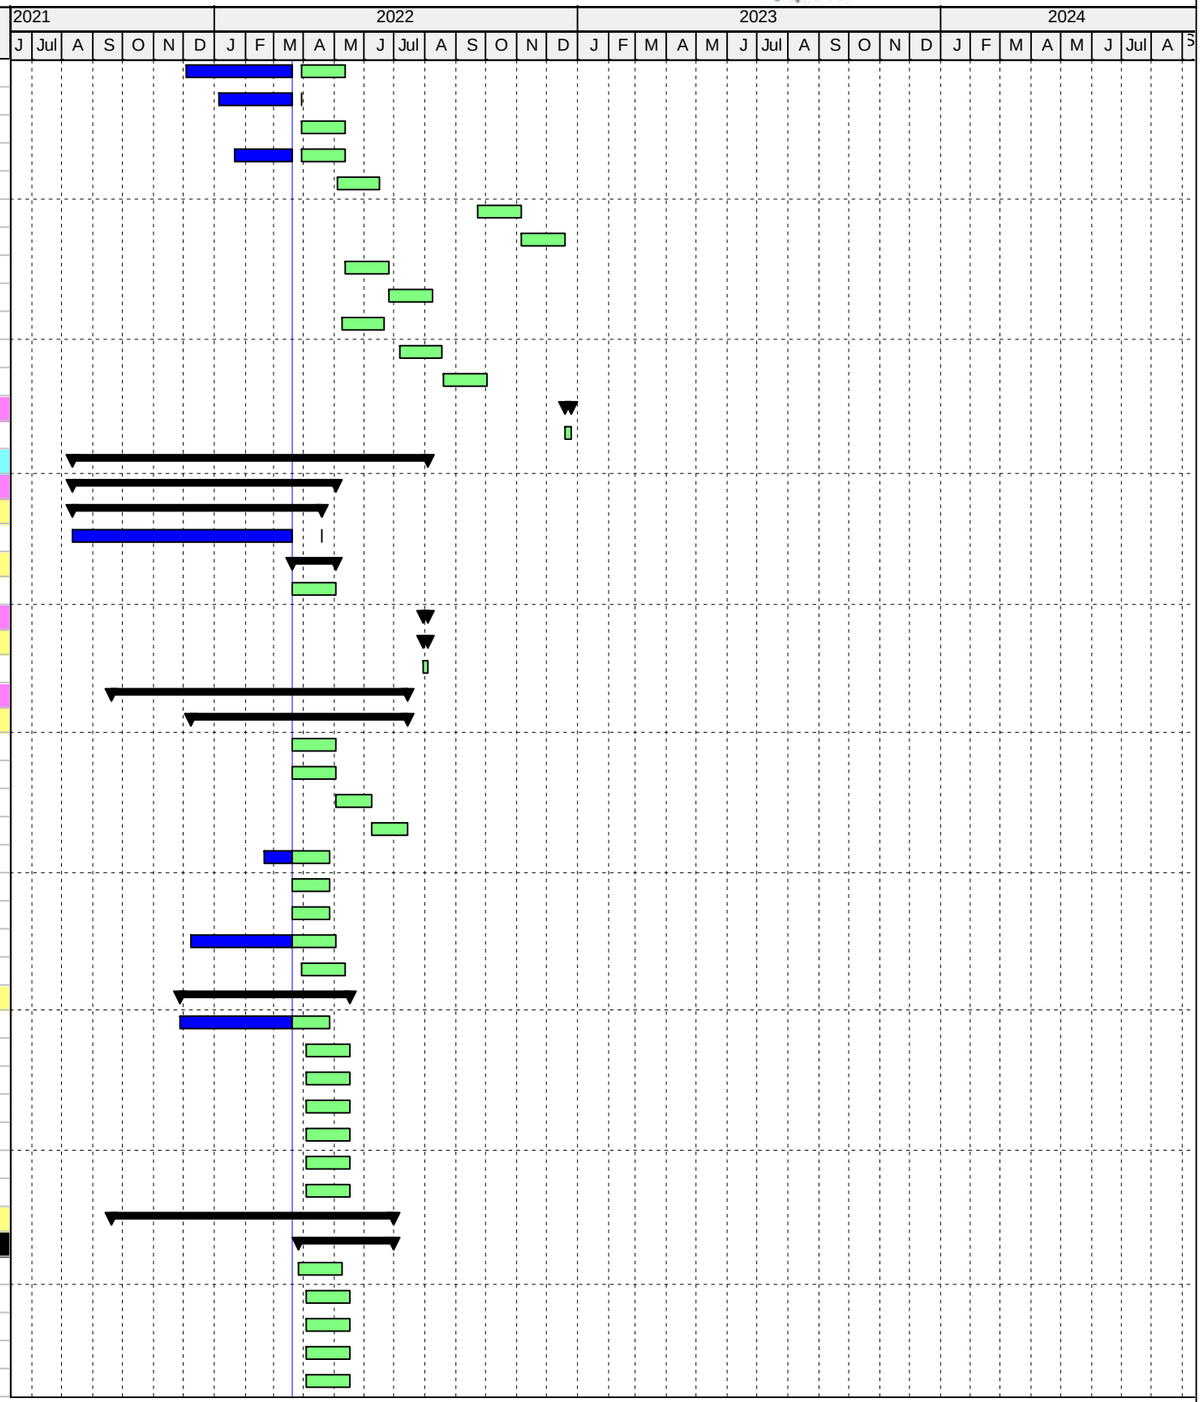

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P10	PIPING WPS (Preliminary Welding Procedure Specification) f	44	0%	$3.32	03-Apr-22	16-May-22
P10	PIPING PQR (Procedure Qualification Record) for Repair We	44	0%	$3.32	03-Apr-22	16-May-22
P10	Field Joint Coating Procedure For Pipeline	44	0%	$3.32	03-Apr-22	16-May-22
P10	Pressure Test Procedure	44	0%	$3.32	17-May-22	29-Jun-22
Telecomm.		44	0%	$5.90	27-Mar-22	09-May-22
P10	ITP For Telecommunication Installation	44	0%	$5.90	27-Mar-22	09-May-22
Safety		44	0%	$5.90	27-Mar-22	09-May-22
P10	ITP For Safety Installation	44	0%	$5.90	27-Mar-22	09-May-22
Architectural		44	0%	$5.90	27-Mar-22	09-May-22
P10	ITP For Architectural Works	44	0%	$5.90	27-Mar-22	09-May-22
Mechanical		44	0%	$5.90	27-Mar-22	09-May-22
P10	ITP For Mechanical Installation	44	0%	$5.90	27-Mar-22	09-May-22
Structure		51	0%	$23.61	27-Mar-22	16-May-22
P10	ITP For Steel Structural Works	44	0%	$2.36	27-Mar-22	09-May-22
P10	Steel Structure WPS (Welding Procedure Specification)	44	0%	$3.54	03-Apr-22	16-May-22
P10	Steel Structure PQR (Procedure Qualification Record)	44	0%	$3.54	03-Apr-22	16-May-22
P10	Steel Structure WPS (Welding Procedure Specification) For F	44	0%	$3.54	03-Apr-22	16-May-22
P10	Steel Structure PQR (Procedure Qualification Record) For Re	44	0%	$3.54	03-Apr-22	16-May-22
P10	Weld Map For Steel Structures	44	0%	$3.54	03-Apr-22	16-May-22
P10	NDT Plan For steel Structures	44	0%	$3.54	03-Apr-22	16-May-22
Instrumentation		44	0%	$5.90	27-Mar-22	09-May-22
P10	ITP For I&C Installation	44	0%	$5.90	27-Mar-22	09-May-22
Pipeline		88	15%	$23.61	16-Jan-22	29-Jun-22
P10	ITP For Pipeline	44	60%	$2.36	16-Jan-22	09-May-22
P10	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	60%	$3.54	23-Feb-22	16-May-22
P10	PIPELINE WPS (Welding Procedure Specification)	44	0%	$3.54	03-Apr-22	16-May-22
P10	PIPELINE PQR (Procedure Qualification Record)	44	0%	$3.54	03-Apr-22	16-May-22
P10	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	0%	$3.54	03-Apr-22	16-May-22
P10	PIPELINE WPS (Preliminary Welding Procedure Specificatior	44	0%	$3.54	17-May-22	29-Jun-22
P10	PIPELINE PQR (Procedure Qualification Record) for Repair \	44	0%	$3.54	03-Apr-22	16-May-22
Civil		44	100%	$5.90	20-Sep-21	27-Mar-22
P10	ITP For Civil Works	44	100%	$5.90	20-Sep-21	27-Mar-22
Electrical		44	0%	$5.90	27-Mar-22	09-May-22
P10	ITP For Electrical Installation	44	0%	$5.90	27-Mar-22	09-May-22
Procurement Engineering		287	0%	$1,338.20	13-May-22	23-Feb-23
Mechanical		57	0%	$133.82	01-Aug-22	26-Sep-22
Drum		52	0%	$80.29	06-Aug-22	26-Sep-22
P10-E	PMR For Drum - BK05	25	0%	$8.03	06-Aug-22	30-Aug-22
P10-E	TBE For Main Drum - BK05	5	0%	$12.04	31-Aug-22	04-Sep-22
P10-E	VDR For Drum - BK05	7	0%	$60.22	20-Sep-22	26-Sep-22
Potable Tanks		52	0%	$53.53	01-Aug-22	21-Sep-22
P10-E	PMR For Potable Tanks - BK05	25	0%	$5.35	01-Aug-22	25-Aug-22
P10-E	TBE For Potable Tanks - BK05	5	0%	$8.03	26-Aug-22	30-Aug-22
P10-E	VDR For Potable Tanks - BK05	7	0%	$40.15	15-Sep-22	21-Sep-22
HVAC		59	0%	$48.58	27-Dec-22	23-Feb-23
Main HVAC Equipment		59	0%	$48.58	27-Dec-22	23-Feb-23
P10-E	PMR For Main HVAC Equipment - BK05	25	0%	$4.86	27-Dec-22	20-Jan-23
P10-E	TBE For Main HVAC Equipment - BK05	30	0%	$7.29	03-Jan-23	01-Feb-23
P10-E	VDR For Main HVAC Equipment - BK05	7	0%	$36.43	17-Feb-23	23-Feb-23
Electrical		234	0%	$1,012.62	13-May-22	01-Jan-23




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Earthing & Lightning System		64	0%	$76.45	22-Aug-22	24-Oct-22
P10-E	PMR For Earthing & Lightning System - BK05	25	0%	$7.65	22-Aug-22	15-Sep-22
P10-E	TBE For Earthing & Lightning System - BK05	30	0%	$11.47	29-Aug-22	27-Sep-22
P10-E	VDR For Earthing & Lightning System - BK05	7	0%	$57.34	18-Oct-22	24-Oct-22
Electrical Bulk Items		69	0%	$76.35	25-Oct-22	01-Jan-23
P10-E	PMR For Electrical Bulk Items - BK05	25	0%	$7.64	25-Oct-22	18-Nov-22
P10-E	TBE For Electrical Bulk Items - BK05	30	0%	$11.45	01-Nov-22	30-Nov-22
P10-E	VDR For Electrical Bulk Items - BK05	7	0%	$57.26	26-Dec-22	01-Jan-23
Transmission Over head Line		99	0%	$95.49	23-Jun-22	29-Sep-22
P10-E	PMR For Transmission Over head Line - BK05	25	0%	$9.55	23-Jun-22	17-Jul-22
P10-E	TBE For Transmission Over head Line - BK05	60	0%	$14.32	30-Jun-22	28-Aug-22
P10-E	VDR For Transmission Over head Line - BK05	7	0%	$71.62	23-Sep-22	29-Sep-22
Capacitor Bank		69	0%	$76.45	18-May-22	25-Jul-22
P10-E	PMR For Capacitor Bank - BK05	25	0%	$7.65	18-May-22	11-Jun-22
P10-E	TBE For Capacitor Bank - BK05	30	0%	$11.47	25-May-22	23-Jun-22
P10-E	VDR For Capacitor Bank - BK05	7	0%	$57.34	19-Jul-22	25-Jul-22
Lighting and Small Power Equipment		79	0%	$76.45	13-Jun-22	30-Aug-22
P10-E	PMR For Lighting and Small Power Equipment - BK05	25	0%	$7.65	13-Jun-22	07-Jul-22
P10-E	TBE For Lighting and Small Power Equipment - BK05	30	0%	$11.47	20-Jun-22	19-Jul-22
P10-E	VDR For Lighting and Small Power Equipment - BK05	7	0%	$57.34	24-Aug-22	30-Aug-22
Transformers		64	0%	$76.45	18-May-22	20-Jul-22
P10-E	PMR For Transformers - BK05	25	0%	$7.65	18-May-22	11-Jun-22
P10-E	TBE For Transformers - BK05	30	0%	$11.47	25-May-22	23-Jun-22
P10-E	VDR For Transformers - BK05	7	0%	$57.34	14-Jul-22	20-Jul-22
UPS System		69	0%	$76.45	11-Aug-22	18-Oct-22
P10-E	PMR For UPS System - BK05	25	0%	$7.65	11-Aug-22	04-Sep-22
P10-E	TBE For UPS System - BK05	30	0%	$11.47	18-Aug-22	16-Sep-22
P10-E	VDR For UPS System - BK05	7	0%	$57.34	12-Oct-22	18-Oct-22
Emergency Diesel Generator		59	0%	$76.45	23-May-22	20-Jul-22
P10-E	PMR For Emergency Diesel Generator - BK05	25	0%	$7.65	23-May-22	16-Jun-22
P10-E	TBE For Emergency Diesel Generator - BK05	30	0%	$11.47	30-May-22	28-Jun-22
P10-E	VDR For Emergency Diesel Generator - BK05	7	0%	$57.34	14-Jul-22	20-Jul-22
DC Charger		64	0%	$76.45	23-May-22	25-Jul-22
P10-E	PMR For DC Charger - BK05	25	0%	$7.65	23-May-22	16-Jun-22
P10-E	TBE For DC Charger - BK05	30	0%	$11.47	30-May-22	28-Jun-22
P10-E	VDR For DC Charger - BK05	7	0%	$57.34	19-Jul-22	25-Jul-22
Tray/Ladder and Accessories		69	0%	$76.35	17-Aug-22	24-Oct-22
P10-E	PMR For Tray/Ladder and Accessories - BK05	25	0%	$7.64	17-Aug-22	10-Sep-22
P10-E	TBE For Tray/Ladder and Accessories - BK05	30	0%	$11.45	24-Aug-22	22-Sep-22
P10-E	VDR For Tray/Ladder and Accessories - BK05	7	0%	$57.26	18-Oct-22	24-Oct-22
Power & Control Cables		64	0%	$76.35	30-Oct-22	01-Jan-23
P10-E	PMR For Power & Control Cables - BK05	25	0%	$7.64	30-Oct-22	23-Nov-22
P10-E	TBE For Power & Control Cables - BK05	30	0%	$11.45	06-Nov-22	05-Dec-22
P10-E	VDR For Power & Control Cables - BK05	7	0%	$57.26	26-Dec-22	01-Jan-23
Lighting & Distribution Main Panels		80	0%	$76.45	01-Aug-22	19-Oct-22
P10-E	PMR For Lighting & Distribution Main Panels - BK05	25	0%	$7.65	01-Aug-22	25-Aug-22
P10-E	TBE For Lighting & Distribution Main Panels - BK05	30	0%	$11.47	08-Aug-22	06-Sep-22
P10-E	VDR For Lighting & Distribution Main Panels - BK05	8	0%	$57.34	12-Oct-22	19-Oct-22
LV Switchgear & MCC		69	0%	$76.45	13-May-22	20-Jul-22

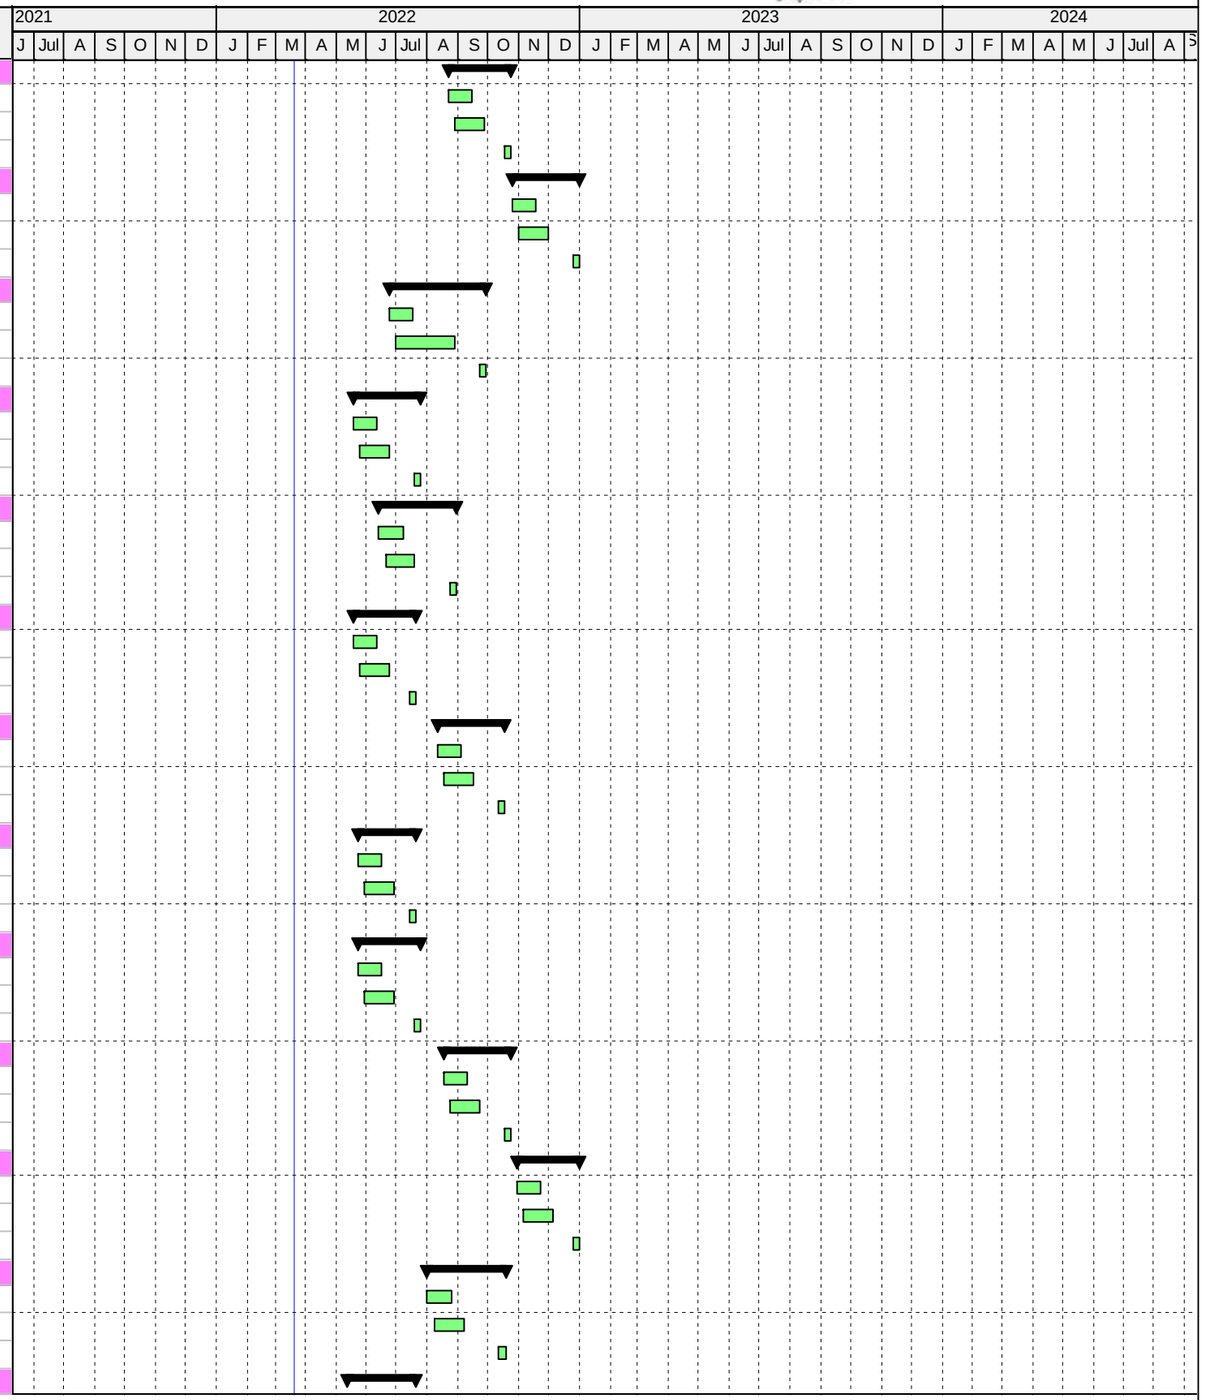


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P10-E	PMR For LV Switchgear & MCC - BK05	25	0%	$7.65	13-May-22	06-Jun-22
P10-E	TBE For LV Switchgear & MCC - BK05	30	0%	$11.47	20-May-22	18-Jun-22
P10-E	VDR For LV Switchgear & MCC - BK05	7	0%	$57.34	14-Jul-22	20-Jul-22
Structure		57	0%	$85.91	27-Dec-22	21-Feb-23
Steel Structure Items		19	0%	$28.64	27-Dec-22	14-Jan-23
P10-E	PMR For Steel Structure Items - BK05	10	0%	$2.86	27-Dec-22	05-Jan-23
P10-E	TBE For Steel Structure Items - BK05	7	0%	$4.30	03-Jan-23	09-Jan-23
P10-E	VDR For Steel Structure Items - BK05	5	0%	$21.48	10-Jan-23	14-Jan-23
Anchor Bolts		42	0%	$28.63	27-Dec-22	06-Feb-23
P10-E	PMR For Anchor Bolts - BK05	10	0%	$2.86	27-Dec-22	05-Jan-23
P10-E	TBE For Anchor Bolts - BK05	30	0%	$4.30	03-Jan-23	01-Feb-23
P10-E	VDR For Anchor Bolts - BK05	5	0%	$21.48	02-Feb-23	06-Feb-23
Blast Proof Doors		57	0%	$28.63	27-Dec-22	21-Feb-23
P10-E	PMR For Blast Proof Doors - BK05	10	0%	$2.86	27-Dec-22	05-Jan-23
P10-E	TBE For Blast Proof Doors - BK05	30	0%	$4.30	03-Jan-23	01-Feb-23
P10-E	VDR For Blast Proof Doors - BK05	20	0%	$21.48	02-Feb-23	21-Feb-23
Piping		62	0%	$57.27	14-Aug-22	14-Oct-22
Pipe		62	0%	$28.64	14-Aug-22	14-Oct-22
P10-E	PMR For Pipes - BK05	10	0%	$2.86	14-Aug-22	23-Aug-22
P10-E	TBE For Pipes - BK05	30	0%	$4.30	24-Aug-22	22-Sep-22
P10-E	VDR For Pipes - BK05	7	0%	$21.48	08-Oct-22	14-Oct-22
Pipe Support		52	0%	$28.64	24-Aug-22	14-Oct-22
P10-E	PMR For Pipe Support - BK05	10	0%	$2.86	24-Aug-22	02-Sep-22
P10-E	TBE For Pipe Support - BK05	5	0%	$4.30	03-Sep-22	07-Sep-22
P10-E	VDR For Pipe Support - BK05	7	0%	$21.48	08-Oct-22	14-Oct-22
Commissioning Engineering		335	0%	$267.64	18-Jul-22	17-Jun-23
P10-EP	Operability Review	5	0%	$53.53	19-May-23	23-May-23
P10-EP	Pre-Commissioning, Commissioning & Startup Procedure - BI	44	0%	$160.58	18-Jul-22	30-Aug-22
P10-EP	Operating Manual - BK05	30	0%	$53.53	19-May-23	17-Jun-23
Field Engineering		218	0%	$2,007.30	27-Nov-22	02-Jul-23
P10-EP	Technical/Site Queries	30	0%	$1,003.65	27-Nov-22	26-Dec-22
P10-EP	As-Built Document Booklets - BK05	15	0%	$1,003.65	18-Jun-23	02-Jul-23
Engineering Final Documentation		15	0%	$1,338.20	03-Jul-23	17-Jul-23
P10-EP	Final Engineering Dossier - BK05	15	0%	$1,338.20	03-Jul-23	17-Jul-23
PROCUREMENT		334	0%	$286,195.00	19-Jun-22	18-May-23
Mechanical		89	0%	$15,998.30	31-Aug-22	27-Nov-22
Drum		84	0%	$9,598.98	05-Sep-22	27-Nov-22
P10-EF	Tendering & Selection	10	0%	$383.96	05-Sep-22	14-Sep-22
P10-EF	Contract Effectiveness / PO	5	0%	$575.94	15-Sep-22	19-Sep-22
P10-EF	Manufacturing / Fabrication / Supply	45	0%	$4,799.49	20-Sep-22	03-Nov-22
P10-EF	Final Inspection	7	0%	$959.90	04-Nov-22	10-Nov-22
P10-EF	Delivery On Site	7	0%	$1,919.80	11-Nov-22	17-Nov-22
P10-EF	Submitting Vendor Data Book	5	0%	$479.95	18-Nov-22	22-Nov-22
P10-EF	Delivering Spare Parts	5	0%	$479.95	23-Nov-22	27-Nov-22
Potable Tanks		79	0%	$6,399.32	31-Aug-22	17-Nov-22
P10-EF	Tendering & Selection	10	0%	$255.97	31-Aug-22	09-Sep-22
P10-EF	Contract Effectiveness / PO	5	0%	$383.96	10-Sep-22	14-Sep-22
P10-EF	Manufacturing / Fabrication / Supply	40	0%	$3,199.66	15-Sep-22	24-Oct-22
P10-EF	Final Inspection	7	0%	$639.93	25-Oct-22	31-Oct-22

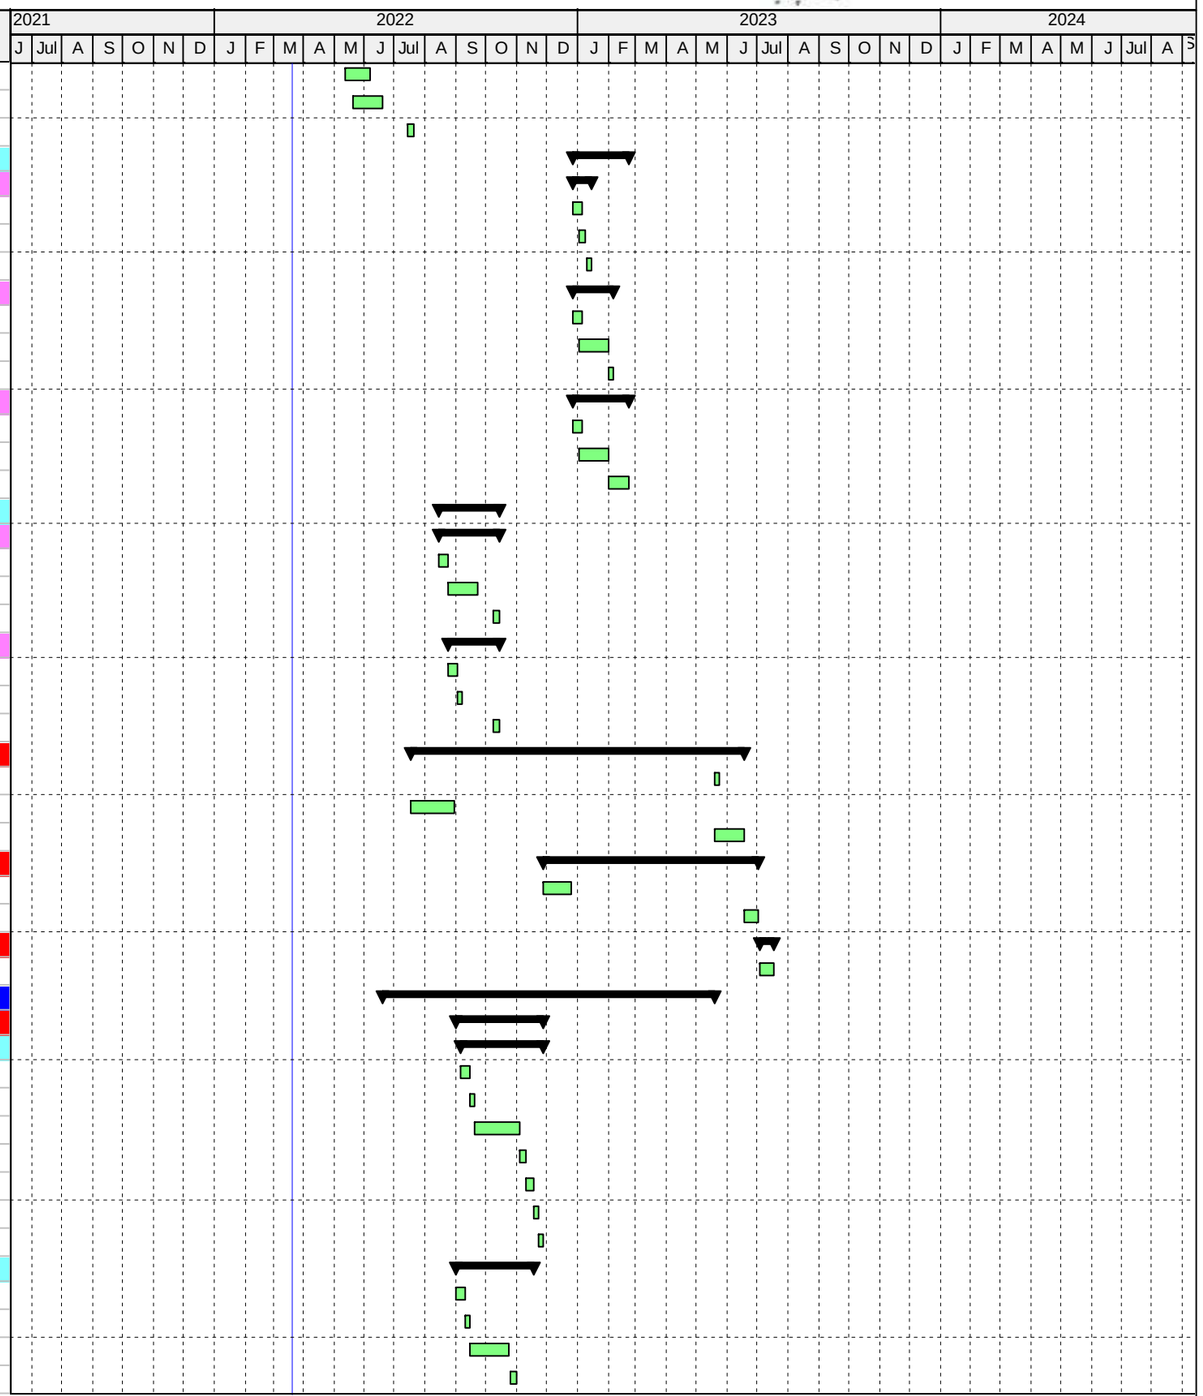


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P10-EF	Delivery On Site	7	0%	$1,279.86	01-Nov-22	07-Nov-22
P10-EF	Submitting Vendor Data Book	5	0%	$319.97	08-Nov-22	12-Nov-22
P10-EF	Delivering Spare Parts	5	0%	$319.97	13-Nov-22	17-Nov-22
HVAC		79	0%	$6,010.10	02-Feb-23	21-Apr-23
Main HVAC Equipment - BK05		79	0%	$6,010.10	02-Feb-23	21-Apr-23
P10-EF	Tendering & Selection	10	0%	$240.40	02-Feb-23	11-Feb-23
P10-EF	Contract Effectiveness / PO	5	0%	$360.61	12-Feb-23	16-Feb-23
P10-EF	Manufacturing / Fabrication / Supply	45	0%	$3,005.05	17-Feb-23	02-Apr-23
P10-EF	Final Inspection	7	0%	$601.01	03-Apr-23	09-Apr-23
P10-EF	Delivery On Site	7	0%	$1,502.52	10-Apr-23	16-Apr-23
P10-EF	Submitting Vendor Data Book	5	0%	$300.50	17-Apr-23	21-Apr-23
Piping		99	0%	$29,993.24	08-Sep-22	15-Dec-22
Pipes - BK05		84	0%	$23,994.59	23-Sep-22	15-Dec-22
P10-EF	Tendering & Selection	10	0%	$959.78	23-Sep-22	02-Oct-22
P10-EF	Contract Effectiveness / PO	5	0%	$1,439.68	03-Oct-22	07-Oct-22
P10-EF	Manufacturing / Fabrication / Supply	50	0%	$11,997.29	08-Oct-22	26-Nov-22
P10-EF	Final Inspection	7	0%	$2,399.46	27-Nov-22	03-Dec-22
P10-EF	Delivery On Site	7	0%	$5,998.65	04-Dec-22	10-Dec-22
P10-EF	Submitting Vendor Data Book	5	0%	$1,199.73	11-Dec-22	15-Dec-22
Pipe Support - BK05		84	0%	$5,998.65	08-Sep-22	30-Nov-22
P10-EF	Tendering & Selection	10	0%	$239.95	08-Sep-22	17-Sep-22
P10-EF	Contract Effectiveness / PO	5	0%	$359.92	18-Sep-22	22-Sep-22
P10-EF	Manufacturing / Fabrication / Supply	50	0%	$2,999.32	23-Sep-22	11-Nov-22
P10-EF	Final Inspection	7	0%	$599.86	12-Nov-22	18-Nov-22
P10-EF	Delivery On Site	7	0%	$1,499.66	19-Nov-22	25-Nov-22
P10-EF	Submitting Vendor Data Book	5	0%	$299.93	26-Nov-22	30-Nov-22
Electrical		334	0%	$234,193.37	19-Jun-22	18-May-23
LV Switchgear & MCC - BK05		174	0%	$20,749.53	19-Jun-22	09-Dec-22
P10-EF	Tendering & Selection	20	0%	$829.98	19-Jun-22	08-Jul-22
P10-EF	Contract Effectiveness / PO	5	0%	$1,244.97	09-Jul-22	13-Jul-22
P10-EF	Manufacturing / Fabrication / Supply	120	0%	$10,374.77	14-Jul-22	10-Nov-22
P10-EF	Final Inspection	12	0%	$2,074.95	11-Nov-22	22-Nov-22
P10-EF	Delivery On Site	7	0%	$4,149.91	23-Nov-22	29-Nov-22
P10-EF	Submitting Vendor Data Book	5	0%	$1,037.48	30-Nov-22	04-Dec-22
P10-EF	Delivering Spare Parts	5	0%	$1,037.48	05-Dec-22	09-Dec-22
Capacitor Bank - BK05		169	0%	$4,613.61	24-Jun-22	09-Dec-22
P10-EF	Tendering & Selection	20	0%	$184.54	24-Jun-22	13-Jul-22
P10-EF	Contract Effectiveness / PO	5	0%	$276.82	14-Jul-22	18-Jul-22
P10-EF	Manufacturing / Fabrication / Supply	120	0%	$2,306.80	19-Jul-22	15-Nov-22
P10-EF	Final Inspection	7	0%	$461.36	16-Nov-22	22-Nov-22
P10-EF	Delivery On Site	7	0%	$922.72	23-Nov-22	29-Nov-22
P10-EF	Submitting Vendor Data Book	5	0%	$230.68	30-Nov-22	04-Dec-22
P10-EF	Delivering Spare Parts	5	0%	$230.68	05-Dec-22	09-Dec-22
Lighting and Small Power Equipment - BK05		164	0%	$11,194.44	20-Jul-22	30-Dec-22
P10-EF	Tendering & Selection	30	0%	$447.78	20-Jul-22	18-Aug-22
P10-EF	Contract Effectiveness / PO	5	0%	$671.67	19-Aug-22	23-Aug-22
P10-EF	Manufacturing / Fabrication / Supply	85	0%	$5,597.22	24-Aug-22	16-Nov-22
P10-EF	Final Inspection	12	0%	$1,119.44	17-Nov-22	28-Nov-22
P10-EF	Delivery On Site	7	0%	$2,238.89	29-Nov-22	05-Dec-22

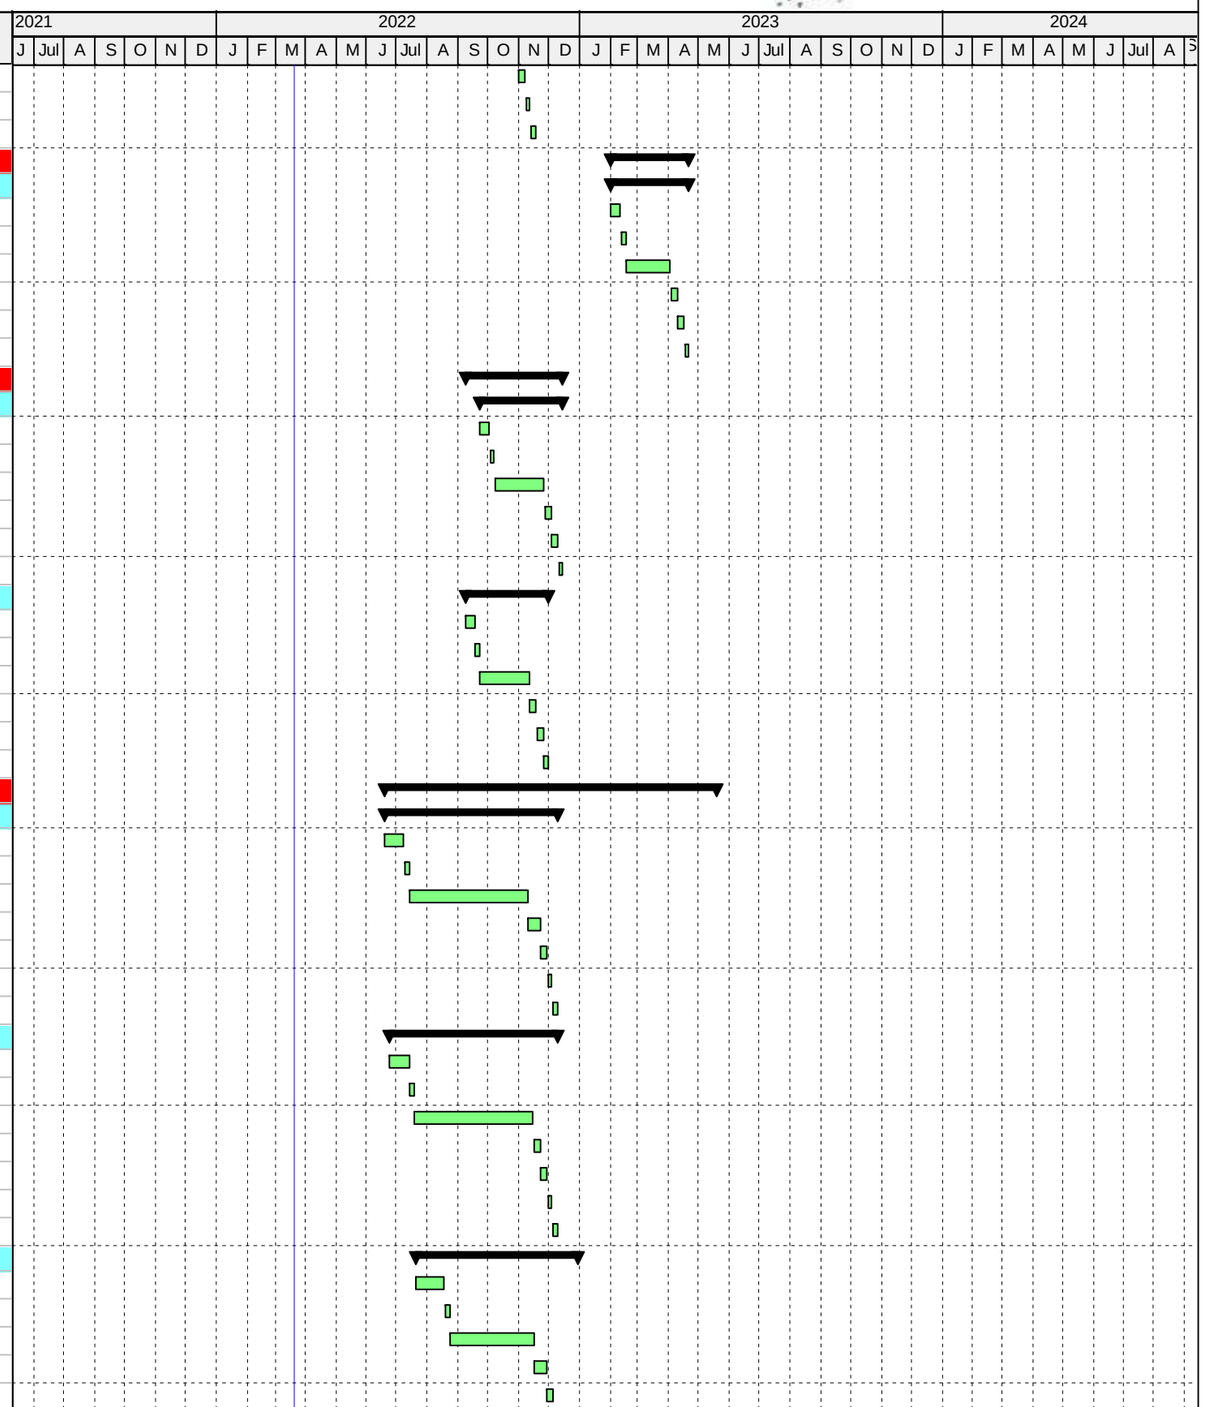


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P10-EF	Submitting Vendor Data Book	20	0%	$559.72	06-Dec-22	25-Dec-22
P10-EF	Delivering Spare Parts	5	0%	$559.72	26-Dec-22	30-Dec-22
Transmission Over head Line - BK05		149	0%	$92,693.74	29-Aug-22	24-Jan-23
P10-EF	Tendering & Selection	20	0%	$3,707.75	29-Aug-22	17-Sep-22
P10-EF	Contract Effectiveness / PO	5	0%	$5,561.62	18-Sep-22	22-Sep-22
P10-EF	Manufacturing / Fabrication / Supply	100	0%	$46,346.87	23-Sep-22	31-Dec-22
P10-EF	Final Inspection	12	0%	$9,269.37	01-Jan-23	12-Jan-23
P10-EF	Delivery On Site	7	0%	$23,173.43	13-Jan-23	19-Jan-23
P10-EF	Submitting Vendor Data Book	5	0%	$4,634.69	20-Jan-23	24-Jan-23
Transformers - BK05		164	0%	$24,426.37	24-Jun-22	04-Dec-22
P10-EF	Tendering & Selection	15	0%	$977.05	24-Jun-22	08-Jul-22
P10-EF	Contract Effectiveness / PO	5	0%	$1,465.58	09-Jul-22	13-Jul-22
P10-EF	Manufacturing / Fabrication / Supply	120	0%	$12,213.18	14-Jul-22	10-Nov-22
P10-EF	Final Inspection	7	0%	$2,442.64	11-Nov-22	17-Nov-22
P10-EF	Delivery On Site	7	0%	$4,885.27	18-Nov-22	24-Nov-22
P10-EF	Submitting Vendor Data Book	5	0%	$1,221.32	25-Nov-22	29-Nov-22
P10-EF	Delivering Spare Parts	5	0%	$1,221.32	30-Nov-22	04-Dec-22
Emergency Diesel Generator - BK05		129	0%	$21,311.60	29-Jun-22	04-Nov-22
P10-EF	Tendering & Selection	10	0%	$852.46	29-Jun-22	08-Jul-22
P10-EF	Contract Effectiveness / PO	5	0%	$1,278.70	09-Jul-22	13-Jul-22
P10-EF	Manufacturing / Fabrication / Supply	90	0%	$10,655.80	14-Jul-22	11-Oct-22
P10-EF	Final Inspection	7	0%	$2,131.16	12-Oct-22	18-Oct-22
P10-EF	Delivery On Site	7	0%	$4,262.32	19-Oct-22	25-Oct-22
P10-EF	Submitting Vendor Data Book	5	0%	$1,065.58	26-Oct-22	30-Oct-22
P10-EF	Delivering Spare Parts	5	0%	$1,065.58	31-Oct-22	04-Nov-22
UPS System - BK05		169	0%	$12,412.25	17-Sep-22	04-Mar-23
P10-EF	Tendering & Selection	20	0%	$496.49	17-Sep-22	06-Oct-22
P10-EF	Contract Effectiveness / PO	5	0%	$744.73	07-Oct-22	11-Oct-22
P10-EF	Manufacturing / Fabrication / Supply	120	0%	$6,206.12	12-Oct-22	08-Feb-23
P10-EF	Final Inspection	7	0%	$1,241.22	09-Feb-23	15-Feb-23
P10-EF	Delivery On Site	7	0%	$2,482.45	16-Feb-23	22-Feb-23
P10-EF	Submitting Vendor Data Book	5	0%	$620.61	23-Feb-23	27-Feb-23
P10-EF	Delivering Spare Parts	5	0%	$620.61	28-Feb-23	04-Mar-23
DC Charger - BK05		154	0%	$14,918.12	29-Jun-22	29-Nov-22
P10-EF	Tendering & Selection	15	0%	$596.72	29-Jun-22	13-Jul-22
P10-EF	Contract Effectiveness / PO	5	0%	$895.09	14-Jul-22	18-Jul-22
P10-EF	Manufacturing / Fabrication / Supply	110	0%	$7,459.06	19-Jul-22	05-Nov-22
P10-EF	Final Inspection	7	0%	$1,491.81	06-Nov-22	12-Nov-22
P10-EF	Delivery On Site	7	0%	$2,983.62	13-Nov-22	19-Nov-22
P10-EF	Submitting Vendor Data Book	5	0%	$745.91	20-Nov-22	24-Nov-22
P10-EF	Delivering Spare Parts	5	0%	$745.91	25-Nov-22	29-Nov-22
Lighting & Distribution Main Panels - BK05		184	0%	$5,526.96	07-Sep-22	09-Mar-23
P10-EF	Tendering & Selection	30	0%	$221.08	07-Sep-22	06-Oct-22
P10-EF	Contract Effectiveness / PO	5	0%	$331.62	07-Oct-22	11-Oct-22
P10-EF	Manufacturing / Fabrication / Supply	120	0%	$2,763.48	12-Oct-22	08-Feb-23
P10-EF	Final Inspection	12	0%	$552.70	09-Feb-23	20-Feb-23
P10-EF	Delivery On Site	7	0%	$1,105.39	21-Feb-23	27-Feb-23
P10-EF	Submitting Vendor Data Book	5	0%	$276.35	28-Feb-23	04-Mar-23
P10-EF	Delivering Spare Parts	5	0%	$276.35	05-Mar-23	09-Mar-23

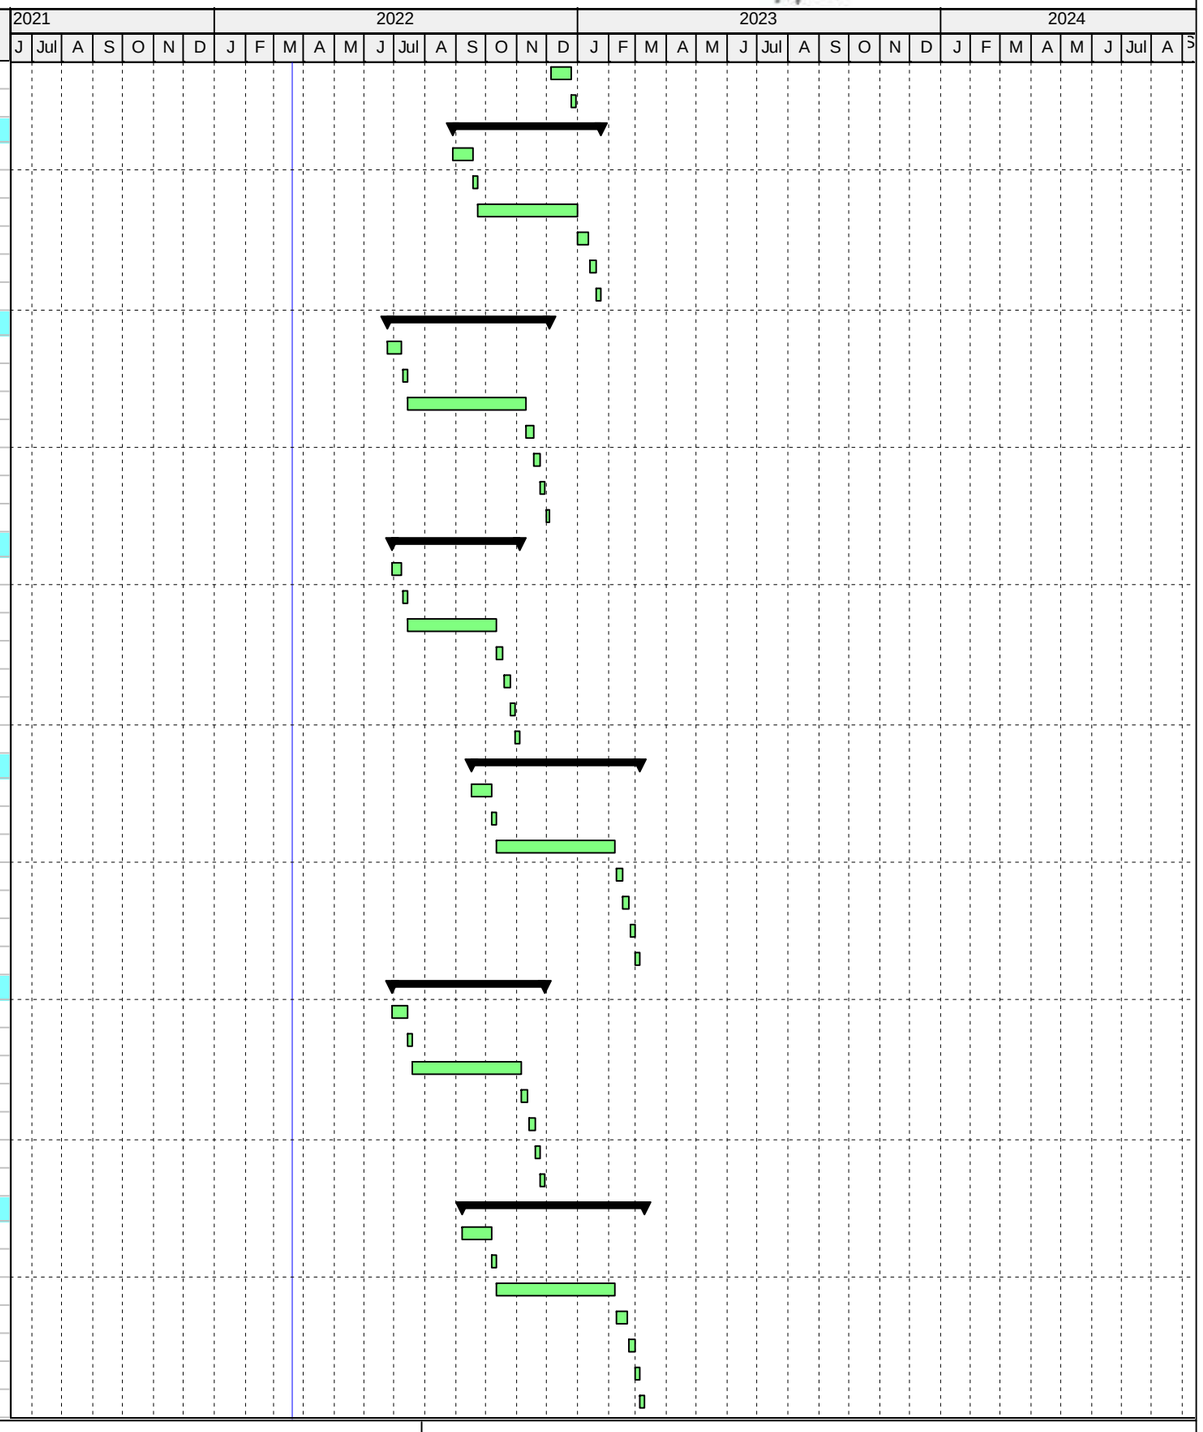

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Earthing & Lightning System - BK05		164	0%	$8,899.35	28-Sep-22	10-Mar-23
P10-EI	Tendering & Selection	15	0%	$355.97	28-Sep-22	12-Oct-22
P10-EI	Contract Effectiveness / PO	5	0%	$533.96	13-Oct-22	17-Oct-22
P10-EI	Manufacturing / Fabrication / Supply	120	0%	$4,449.67	18-Oct-22	14-Feb-23
P10-EI	Final Inspection	7	0%	$889.93	15-Feb-23	21-Feb-23
P10-EI	Delivery On Site	7	0%	$1,779.87	22-Feb-23	28-Feb-23
P10-EI	Submitting Vendor Data Book	5	0%	$444.97	01-Mar-23	05-Mar-23
P10-EI	Delivering Spare Parts	5	0%	$444.97	06-Mar-23	10-Mar-23
Tray/Ladder and Accessories - BK05		149	0%	$1,967.22	23-Sep-22	18-Feb-23
P10-EI	Tendering & Selection	20	0%	$78.69	23-Sep-22	12-Oct-22
P10-EI	Contract Effectiveness / PO	5	0%	$118.03	13-Oct-22	17-Oct-22
P10-EI	Manufacturing / Fabrication / Supply	100	0%	$983.61	18-Oct-22	25-Jan-23
P10-EI	Final Inspection	12	0%	$196.72	26-Jan-23	06-Feb-23
P10-EI	Delivery On Site	7	0%	$491.81	07-Feb-23	13-Feb-23
P10-EI	Submitting Vendor Data Book	5	0%	$98.36	14-Feb-23	18-Feb-23
Power & Control Cables - BK05		164	0%	$13,512.96	06-Dec-22	18-May-23
P10-EI	Tendering & Selection	15	0%	$540.52	06-Dec-22	20-Dec-22
P10-EI	Contract Effectiveness / PO	5	0%	$810.78	21-Dec-22	25-Dec-22
P10-EI	Manufacturing / Fabrication / Supply	120	0%	$6,756.48	26-Dec-22	24-Apr-23
P10-EI	Final Inspection	12	0%	$1,351.30	25-Apr-23	06-May-23
P10-EI	Delivery On Site	7	0%	$3,378.24	07-May-23	13-May-23
P10-EI	Submitting Vendor Data Book	5	0%	$675.65	14-May-23	18-May-23
Electrical Bulk Items - BK05		129	0%	$1,967.22	01-Dec-22	08-Apr-23
P10-EI	Tendering & Selection	20	0%	$78.69	01-Dec-22	20-Dec-22
P10-EI	Contract Effectiveness / PO	5	0%	$118.03	21-Dec-22	25-Dec-22
P10-EI	Manufacturing / Fabrication / Supply	90	0%	$983.61	26-Dec-22	25-Mar-23
P10-EI	Final Inspection	7	0%	$196.72	26-Mar-23	01-Apr-23
P10-EI	Delivery On Site	7	0%	$491.81	02-Apr-23	08-Apr-23
P10-EI	Submitting Vendor Data Book	5	0%	$98.36	02-Jan-23	06-Jan-23
Construction		300	0%	$134,960.00	27-Nov-22	22-Sep-23
Wellpad and Access Road		56	0%	$39,138.40	27-Nov-22	21-Jan-23
Access Road		56	0%	$27,396.88	27-Nov-22	21-Jan-23
Wellpad Access Road		56	0%	$27,396.88	27-Nov-22	21-Jan-23
P10-E	Access Road Preparation	5	0%	$14,794.32	27-Nov-22	01-Dec-22
P10-E	Filling and Compaction	10	0%	$1,232.86	03-Jan-23	13-Jan-23
P10-E	Sub-Base Layer	9	0%	$2,465.72	13-Jan-23	21-Jan-23
Retaining wall		12	0%	$4,931.44	02-Dec-22	13-Dec-22
P10-	Excavation	2	0%	$493.14	02-Dec-22	03-Dec-22
P10-	lean concrete	2	0%	$739.72	04-Dec-22	05-Dec-22
P10-	form working	3	0%	$1,726.00	06-Dec-22	08-Dec-22
P10-	concrete pouring	5	0%	$1,972.58	09-Dec-22	13-Dec-22
Construction of Culvert and Bridge		32	0%	$1,232.86	02-Dec-22	03-Jan-23
bridge		32	0%	$493.14	02-Dec-22	03-Jan-23
P10	Excavation	2	0%	$49.31	02-Dec-22	03-Dec-22
P10	lean concrete	2	0%	$39.45	04-Dec-22	05-Dec-22
P10	wall	9	0%	$88.77	06-Dec-22	14-Dec-22
P10	reinforcement	3	0%	$98.63	14-Dec-22	17-Dec-22
P10	form working	3	0%	$49.31	17-Dec-22	20-Dec-22
P10	concrete pouring	5	0%	$147.94	20-Dec-22	25-Dec-22




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P10	protect stone	3	0%	$9.86	25-Dec-22	28-Dec-22
P10	Backfill	6	0%	$9.86	28-Dec-22	03-Jan-23
culverts		16	0%	$739.72	02-Dec-22	18-Dec-22
P10	pipeway culvert	9	0%	$295.89	02-Dec-22	10-Dec-22
P10	pipeway	4	0%	$221.91	10-Dec-22	14-Dec-22
P10	pipeline culvert	4	0%	$221.91	14-Dec-22	18-Dec-22
Burn Pit Access Road		18	0%	$2,739.69	04-Dec-22	22-Dec-22
P10-	ROW Preparation	5	0%	$1,506.83	04-Dec-22	09-Dec-22
P10-	Filling and Compaction	7	0%	$547.94	09-Dec-22	16-Dec-22
P10-	Sub-Base Layer	6	0%	$684.92	16-Dec-22	22-Dec-22
Wellpad		50	0%	$11,741.52	27-Nov-22	15-Jan-23
Water Supply		25	0%	$821.91	27-Nov-22	21-Dec-22
P10-E	Water Supply	25	0%	$821.91	27-Nov-22	21-Dec-22
Gasoil Pad		16	0%	$587.08	17-Dec-22	01-Jan-23
P10-E	Excavation	5	0%	$117.42	17-Dec-22	21-Dec-22
P10-E	lean concrete	2	0%	$176.12	22-Dec-22	23-Dec-22
P10-E	Form work	4	0%	$58.71	24-Dec-22	27-Dec-22
P10-E	Armed Concrete	5	0%	$234.83	27-Dec-22	01-Jan-23
Site Preparation		15	0%	$1,174.15	02-Dec-22	16-Dec-22
P10-E	Site Preparation #05	15	0%	$1,174.15	02-Dec-22	16-Dec-22
Demolition & Disassemble (Fence & Paving)		10	0%	$2,348.30	17-Dec-22	26-Dec-22
P10-E	Demolition of concrete Cellar	5	0%	$704.49	17-Dec-22	21-Dec-22
P10-E	Fence Disassmble	5	0%	$1,643.81	22-Dec-22	26-Dec-22
Civil Work		24	0%	$2,935.38	17-Dec-22	09-Jan-23
P10-E	Excavation and Soil Removal (Cellar)	10	0%	$1,908.00	17-Dec-22	26-Dec-22
P10-E	Installation of Conductor Pipe	15	0%	$146.77	17-Dec-22	31-Dec-22
P10-E	Form Work (Above Cellar)	9	0%	$146.77	27-Dec-22	04-Jan-23
P10-E	Armed Concrete	5	0%	$733.85	04-Jan-23	09-Jan-23
Mud Channel		15	0%	$352.25	17-Dec-22	31-Dec-22
P10-E	Excavation & Repair	15	0%	$352.25	17-Dec-22	31-Dec-22
Mud Pit		14	0%	$1,761.23	24-Dec-22	07-Jan-23
P10-E	Soil Removal, Filling and Compaction of Mud Pit Area	5	0%	$616.43	27-Dec-22	31-Dec-22
P10-E	Construction of Mud Pit's Walls	7	0%	$352.25	24-Dec-22	31-Dec-22
P10-E	Supply & Installation sealling Layer	7	0%	$792.55	31-Dec-22	07-Jan-23
Burn Pit		18	0%	$469.66	17-Dec-22	03-Jan-23
P10-E	Soil Removal, Triming ,Filling and Compaction of Burn Pit Are	5	0%	$375.73	17-Dec-22	21-Dec-22
P10-E	Construction & Installation of Support	7	0%	$23.48	22-Dec-22	28-Dec-22
P10-E	Welding, Installation and Testing	7	0%	$70.45	27-Dec-22	03-Jan-23
SepticTank		20	0%	$939.32	27-Dec-22	15-Jan-23
P10-E	Excavation & Soil Transfer	5	0%	$281.80	27-Dec-22	31-Dec-22
P10-E	Levelling	3	0%	$4.70	01-Jan-23	03-Jan-23
P10-E	Tank Supply	8	0%	$535.41	04-Jan-23	11-Jan-23
P10-E	Tank Execution	2	0%	$89.24	12-Jan-23	13-Jan-23
P10-E	Backfilling & Compaction	2	0%	$28.18	14-Jan-23	15-Jan-23
Surface Preparation		7	0%	$352.25	17-Dec-22	23-Dec-22
P10-E	Gravel Paving	7	0%	$352.25	17-Dec-22	23-Dec-22
Wellhead Facility and Flowline		97	0%	$93,797.20	23-Mar-23	27-Jun-23
Civil, Structure & Architecture		83	0%	$32,829.02	23-Mar-23	13-Jun-23
Civil Works		23	0%	$6,894.09	23-Mar-23	14-Apr-23
P10-E	Steel Works(Wellhead Facilities)	5	0%	$3,102.34	23-Mar-23	27-Mar-23

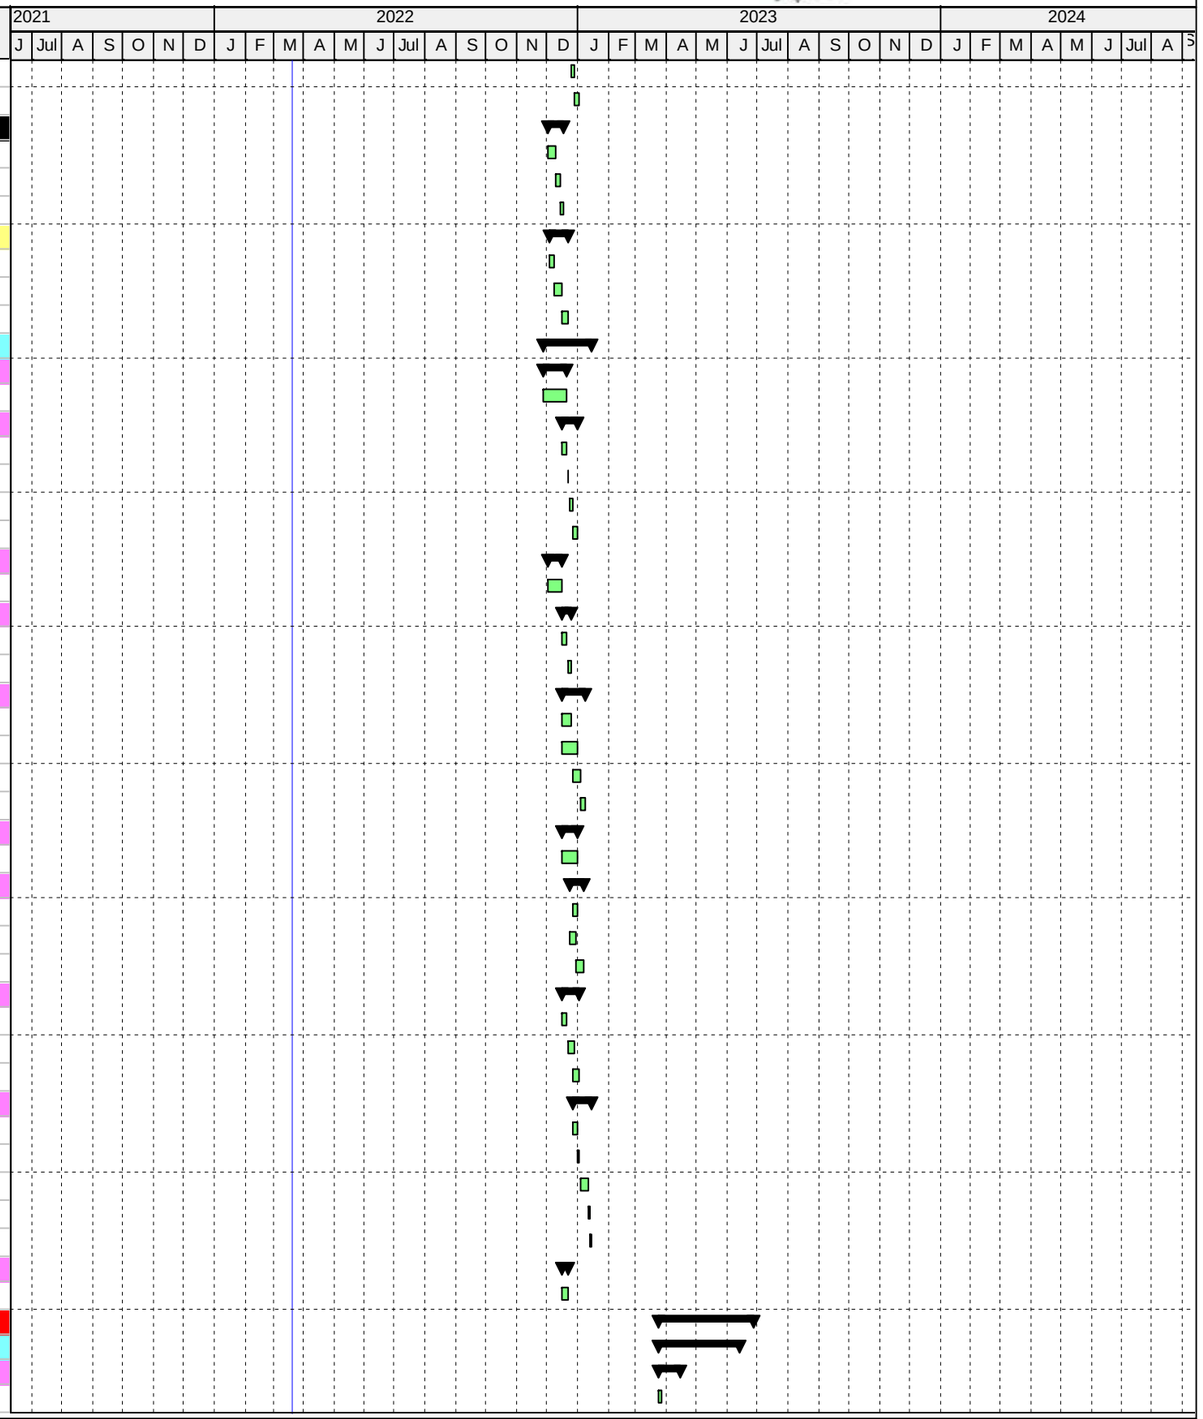


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P10-E	Out Door Post Works For New Gantry (Fundation, Fencing .	5	0%	$1,723.52	28-Mar-23	01-Apr-23
P10-E	Out Door Post Works For Wellhead Post (Fundation, Fencing	5	0%	$1,723.52	09-Apr-23	14-Apr-23
P10-E	Well Pad Fencing	5	0%	$344.70	28-Mar-23	01-Apr-23
Buildings		83	0%	$20,025.70	23-Mar-23	13-Jun-23
Construction of Guard House		83	0%	$5,607.20	23-Mar-23	13-Jun-23
Foundation		54	0%	$1,738.23	23-Mar-23	15-May-23
P10	Excavation & Soil Transfer (Removing of Vegetal Soil)	2	0%	$347.65	23-Mar-23	24-Mar-23
P10	Levelling	30	0%	$34.76	25-Mar-23	23-Apr-23
P10	Lean Concrete	2	0%	$173.82	24-Apr-23	25-Apr-23
P10	Reinforced Work	5	0%	$347.65	26-Apr-23	30-Apr-23
P10	Formwork	4	0%	$139.06	01-May-23	04-May-23
P10	Main Concrete Pouring	5	0%	$677.91	04-May-23	09-May-23
P10	Backfilling & Compaction	6	0%	$17.38	09-May-23	15-May-23
Structure		16	0%	$2,242.88	15-May-23	31-May-23
P10	Steel Material Supply	6	0%	$1,121.44	15-May-23	21-May-23
P10	Shop Fabrication of Steel Structure	4	0%	$448.58	21-May-23	25-May-23
P10	Structural Installation	4	0%	$448.58	25-May-23	29-May-23
P10	Structural Painting	2	0%	$224.29	29-May-23	31-May-23
Architectural		13	0%	$1,626.09	31-May-23	13-Jun-23
P10	Wall Execution	3	0%	$794.64	31-May-23	03-Jun-23
P10	Roof Covering	4	0%	$193.59	03-Jun-23	07-Jun-23
P10	Roof Execution (Block Joist, Concrete Pouring)	4	0%	$246.86	07-Jun-23	11-Jun-23
P10	Building Walkway (around Building)	2	0%	$83.51	11-Jun-23	13-Jun-23
P10	Joinery (Cornice, Faï?½ade, Plaster)	2	0%	$307.49	11-Jun-23	13-Jun-23
Construction of Switchgear		66	0%	$14,418.51	23-Mar-23	27-May-23
Foundation		29	0%	$4,469.74	23-Mar-23	20-Apr-23
P10	Excavation & Soil Transfer (Removing of Vegetal Soil)	2	0%	$893.95	23-Mar-23	24-Mar-23
P10	Levelling	5	0%	$89.39	25-Mar-23	29-Mar-23
P10	Lean Concrete	2	0%	$446.97	30-Mar-23	31-Mar-23
P10	Reinforced Work	5	0%	$893.95	01-Apr-23	05-Apr-23
P10	Formwork	4	0%	$357.58	06-Apr-23	09-Apr-23
P10	Main Concrete Pouring	5	0%	$1,743.20	09-Apr-23	14-Apr-23
P10	Backfilling & Compaction	6	0%	$44.70	14-Apr-23	20-Apr-23
Structure		17	0%	$5,767.40	20-Apr-23	07-May-23
P10	Steel Material Supply	5	0%	$2,883.70	20-Apr-23	25-Apr-23
P10	Shop Fabrication of Steel Structure	5	0%	$1,153.48	25-Apr-23	30-Apr-23
P10	Structural Installation	5	0%	$1,153.48	30-Apr-23	05-May-23
P10	Structural Painting	2	0%	$576.74	05-May-23	07-May-23
Architectural		20	0%	$4,181.37	07-May-23	27-May-23
P10	Wall Execution	7	0%	$2,043.35	07-May-23	14-May-23
P10	Roof Covering	5	0%	$497.79	14-May-23	19-May-23
P10	Roof Execution (Block Joist, Concrete Pouring)	5	0%	$634.79	19-May-23	24-May-23
P10	Building Walkway (around Building)	3	0%	$214.75	24-May-23	27-May-23
P10	Joinery (Cornice, Faï?½ade, Plaster)	2	0%	$790.69	24-May-23	26-May-23
Shelters		30	0%	$5,909.22	23-Mar-23	21-Apr-23
Fire Fighting Shelter		20	0%	$4,845.56	02-Apr-23	21-Apr-23
P10-	Fabrication	10	0%	$3,391.89	02-Apr-23	11-Apr-23
P10-	Installation	10	0%	$1,453.67	12-Apr-23	21-Apr-23
Diesel Generator Shelter		20	0%	$1,063.66	23-Mar-23	11-Apr-23

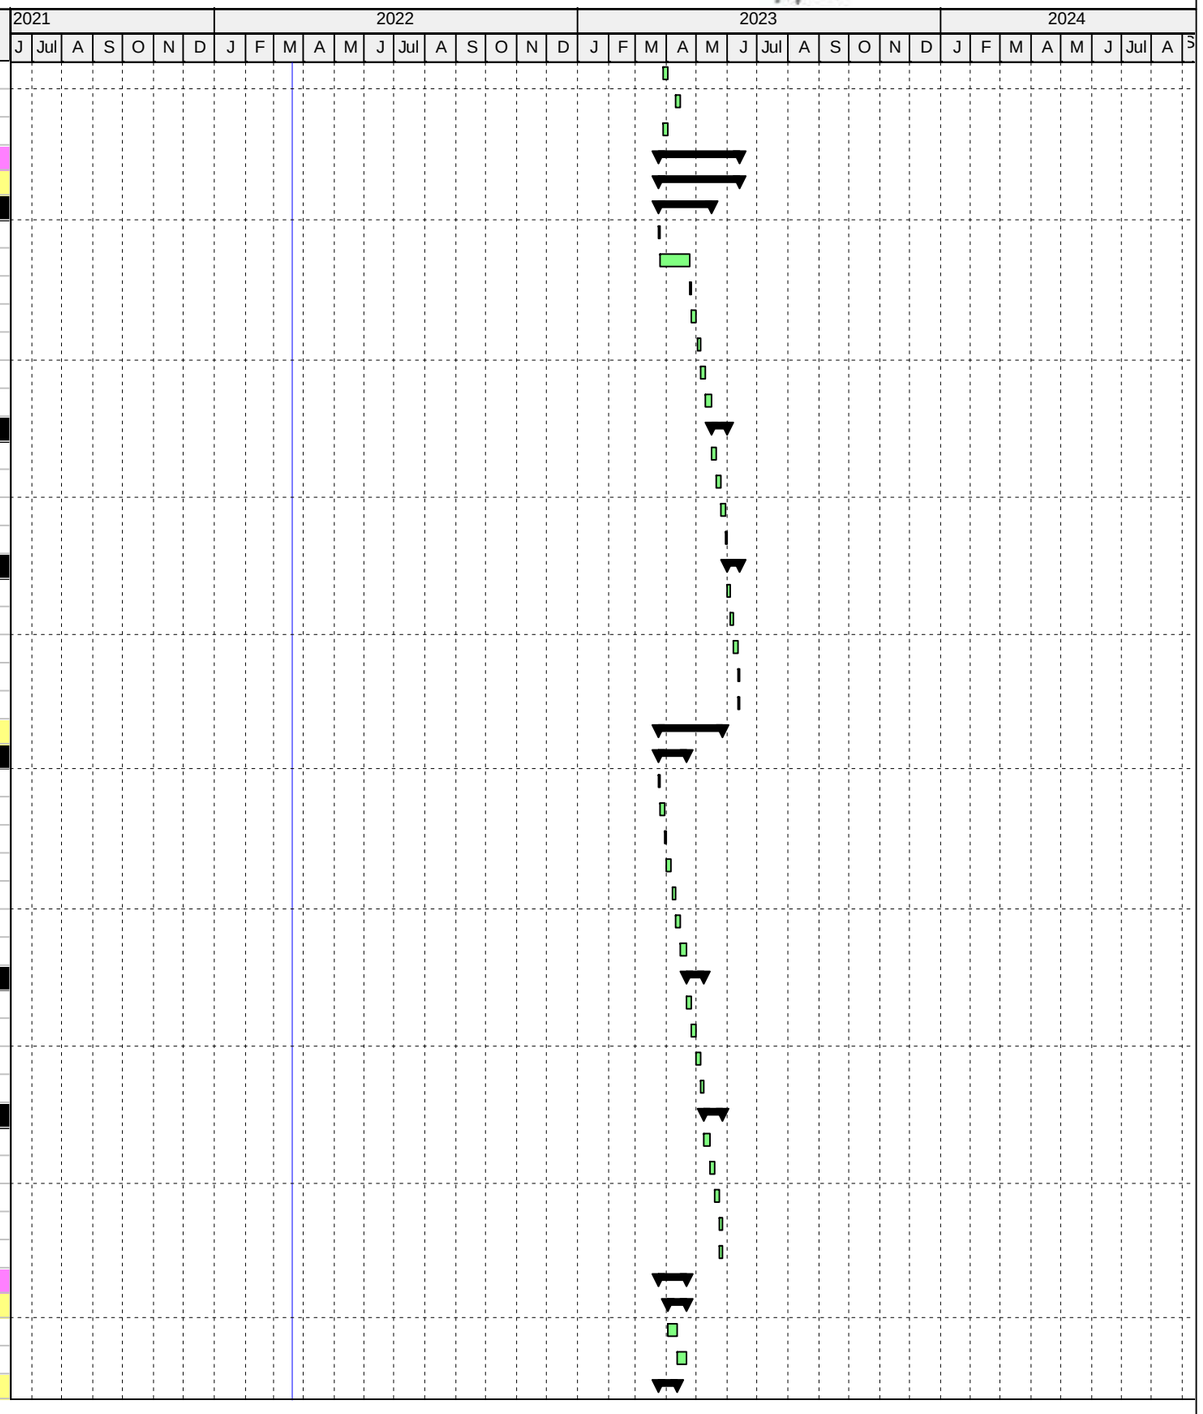

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P10-	Fabrication	10	0%	$744.56	23-Mar-23	01-Apr-23
P10-	Installation	10	0%	$319.10	02-Apr-23	11-Apr-23
Piping		25	0%	$9,379.72	23-Mar-23	16-Apr-23
P10-EI	Sweep Bend Installation	10	0%	$468.99	23-Mar-23	01-Apr-23
P10-EI	Piping Work (Fit up, Welding, NDT…)	15	0%	$3,751.89	02-Apr-23	16-Apr-23
P10-EI	Valves, Fitting and Spools Installation and Hydrotest	10	0%	$5,158.85	07-Apr-23	16-Apr-23
Mechanical		17	0%	$9,379.72	02-Apr-23	18-Apr-23
P10-EI	Fuel Oil Storage Drum	7	0%	$4,689.86	02-Apr-23	08-Apr-23
P10-EI	Potable Water Tank	7	0%	$4,689.86	12-Apr-23	18-Apr-23
Instrument Works		5	0%	$0.00	26-May-23	31-May-23
P10-EI	Devices Installation and Piping Connecton	5	0%	$0.00	26-May-23	31-May-23
Electrical		75	0%	$40,332.80	23-Mar-23	05-Jun-23
P10-EI	Over Head line	20	0%	$21,376.38	23-Mar-23	11-Apr-23
P10-EI	Wellhead Electrical Equipment	10	0%	$12,099.84	26-May-23	05-Jun-23
P10-EI	Outdoor Post (Wellhead Post)	10	0%	$6,856.58	14-Apr-23	24-Apr-23
Pre-commissioning		10	0%	$1,875.94	18-Jun-23	27-Jun-23
P10-EI	Pre-commissioning	5	0%	$1,688.35	18-Jun-23	22-Jun-23
P10-EI	Ready for Comm.Certificate(RFCC)	5	0%	$187.59	23-Jun-23	27-Jun-23
Job Site HSE Supervision (Surface)		160	0%	$269.92	27-Nov-22	05-May-23
P10-EP(	Job Site HSE Supervision (Surface)	160	0%	$269.92	27-Nov-22	05-May-23
Commissioning, Startup & Handover		87	0%	$1,754.48	28-Jun-23	22-Sep-23
Handover		38	0%	$526.34	16-Aug-23	22-Sep-23
P10-EI	Compiling & Submitting Final Documentation	20	0%	$157.90	16-Aug-23	04-Sep-23
P10-EI	Training of Operator's Personnel	3	0%	$210.54	05-Sep-23	07-Sep-23
P10-EI	Provisional Acceptance Certificate (PAC)	15	0%	$157.90	07-Sep-23	22-Sep-23
Commissioning		32	0%	$526.34	28-Jun-23	29-Jul-23
P10-EI	Materials & Utilities Ready for Commissioning	2	0%	$26.32	28-Jun-23	29-Jun-23
P10-EI	Receiving Facilities Ready for Commissioning	3	0%	$26.32	30-Jun-23	02-Jul-23
P10-EI	Permits Obtained for Commissioning	10	0%	$26.32	02-Jul-23	12-Jul-23
P10-EI	Integrated Commissioning	3	0%	$421.08	12-Jul-23	14-Jul-23
P10-EI	Ready for Startup Certificate (RFSU)	15	0%	$26.32	15-Jul-23	29-Jul-23
Startup & Performance Test		17	0%	$701.79	30-Jul-23	15-Aug-23
P10-EI	Startup & Performance Test Run	2	0%	$561.43	30-Jul-23	31-Jul-23
P10-EI	Start of Production (SOP)	15	0%	$140.36	01-Aug-23	15-Aug-23
SURFACE DEVELOPMENT		826	0.57%	$27,467,919.99	24-Jul-21 A	22-Jun-24
Package 11- EPC Pipeline 8" & 4"		670	0.49%	$5,513,440.01	24-Jul-21 A	18-Jan-24
ENGINEERING		644	18.32%	$146,041.00	24-Jul-21 A	23-Dec-23
Basic Design Endorsement		30	100%	$7,302.05	31-Jul-21 A	20-Mar-22
P11-EP(	Endorsement Report For Basic Design & Scope of Work	30	100%	$7,302.05	31-Jul-21 A	20-Mar-22
Value Engineering		145	36%	$4,381.23	01-Feb-22	30-Jul-22
P11-EP(	Value Engineering Study Report	44	60%	$2,628.74	01-Feb-22	20-Mar-22
P11-EP(	HAZID Report For Pipeline	44	0%	$657.18	17-Jun-22	30-Jul-22
P11-EP(	HAZOP Report For Pipeline	44	0%	$1,095.31	17-Jun-22	30-Jul-22
Detail Design		455	22%	$80,322.55	24-Jul-21 A	01-Apr-23
Process		391	52.19%	$6,128.61	27-Jul-21 A	18-Sep-22
Basis/Criteria		93	86.96%	$139.12	27-Jul-21 A	12-May-22
P11-E	Process Design Criteria	39	100%	$48.39	27-Jul-21 A	20-Mar-22
P11-E	Process Basis Of Design	54	80%	$90.73	27-Jul-21 A	12-May-22
Philosophy		214	36.8%	$301.53	21-Nov-21	22-May-22
P11-E	Drainage Philosophy	44	60%	$48.24	31-Jan-22	22-May-22




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-E	Control Philosophy	44	0%	$72.37	09-Apr-22	22-May-22
P11-E	Flare,Blow Down And Relief Philosophy	44	60%	$72.37	06-Feb-22	22-May-22
P11-E	Isolation Philosophy	44	80%	$48.24	21-Nov-21	22-May-22
P11-E	ESD Philosophy	44	0%	$60.31	09-Apr-22	22-May-22
Description		44	60%	$579.15	19-Feb-22	23-May-22
P11-E	Process Description	44	60%	$579.15	19-Feb-22	23-May-22
Calculation		44	60%	$289.88	19-Feb-22	02-May-22
P11-E	Calculation Note For PSV Sizing	44	60%	$289.88	19-Feb-22	02-May-22
Drawing/Diagram		278	55.59%	$2,136.43	17-Nov-21	30-Jul-22
P11-E	Symbol & Legend For PFD and P&ID	44	80%	$36.11	24-Jan-22	02-May-22
P11-E	Process Flow Diagram For pipelines	44	80%	$579.40	17-Nov-21	16-Jun-22
P11-E	P&ID - Gas Pipeline (to Siahmakan G.I. Station)	44	80%	$434.55	17-Nov-21	16-Jun-22
P11-E	P&ID - Condensate Pipeline (to Binak PU)	44	80%	$434.55	17-Nov-21	16-Jun-22
P11-E	ESD Block Diagram	44	0%	$362.13	17-Jun-22	30-Jul-22
P11-E	Cause & Effect Diagram	44	0%	$289.70	17-Jun-22	30-Jul-22
Data Sheet		39	0%	$799.17	11-Aug-22	18-Sep-22
P11-E	Process Data Sheets For Instrument Devices	39	0%	$799.17	11-Aug-22	18-Sep-22
Report		44	80%	$1,086.60	17-Nov-21	16-Jun-22
P11-E	Pipelines Hydraulic Calculation Report	44	80%	$1,086.60	17-Nov-21	16-Jun-22
List		322	48.75%	$796.72	16-Feb-22	30-Jul-22
P11-E	Equipment List	44	60%	$149.38	19-Feb-22	16-Jun-22
P11-E	Line List	44	60%	$248.97	16-Feb-22	16-Jun-22
P11-E	Relief Load Summary	44	0%	$149.38	17-Jun-22	30-Jul-22
P11-E	Tie in list	44	60%	$248.97	19-Feb-22	16-Jun-22
Mechanical		249	85.82%	$1,172.71	24-Jul-21 A	26-Jun-22
Basis/Criteria		249	82.23%	$74.82	24-Jul-21 A	14-May-22
P11-E	HVAC & Plumbing Design Criteria	64	100%	$41.57	24-Jul-21 A	14-May-22
P11-E	Mechanical Design Criteria	54	60%	$33.25	28-Jul-21 A	12-May-22
Specification		79	96.25%	$532.29	24-Jul-21 A	26-Jun-22
Fixed Equipment		79	96.25%	$532.29	24-Jul-21 A	26-Jun-22
P11-I	Specification For HVAC Equipment	64	100%	$41.57	24-Jul-21 A	27-Mar-22
P11-I	Specification For Duct Work & Pipe Work	64	100%	$24.96	24-Jul-21 A	27-Mar-22
P11-I	Specification For Pressure Vessels	54	60%	$24.96	28-Jul-21 A	01-Jun-22
P11-I	Specification For Atmospheric Above Ground Welded Steel Ta	79	60%	$24.91	28-Jul-21 A	26-Jun-22
P11-I	Specification For Pig Traps	74	100%	$415.88	04-Sep-21	20-Mar-22
Data Sheets		64	60%	$332.70	13-Dec-21	22-May-22
Fixed Equipment		64	60%	$332.70	13-Dec-21	22-May-22
P11-I	Data Sheets For Pig Traps	64	60%	$332.70	13-Dec-21	22-May-22
Drawing/Diagram		14	100%	$232.90	28-Jul-21 A	09-Apr-22
P11-E	Standard Detail Drawing For Pressure Vessels and Heat Exch	14	100%	$116.45	28-Jul-21 A	09-Apr-22
P11-E	Standard Detail Drawing For Storage Tanks	14	100%	$116.45	28-Jul-21 A	09-Apr-22
Piping		411	8.09%	$16,666.93	24-Jul-21 A	01-Apr-23
Basis/Criteria		39	100%	$11.67	24-Jul-21 A	20-Mar-22
P11-E	Piping Design Criteria	39	100%	$11.67	24-Jul-21 A	20-Mar-22
Specification		265	79.87%	$161.67	24-Jul-21 A	17-Jun-22
P11-E	Specification For Color Coding and Marking	39	60%	$0.42	09-Aug-21	01-May-22
P11-E	Specification For Transportation, Handling, Storage of pipes	39	80%	$0.45	12-Dec-21	01-May-22
P11-E	Specification For the Design of Piping in Mechanical Packages	39	60%	$0.61	09-Aug-21	01-May-22
P11-E	Specification For Metallic Pipes	39	80%	$0.42	24-Jul-21 A	01-May-22
P11-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$0.42	24-Jul-21 A	24-Mar-22

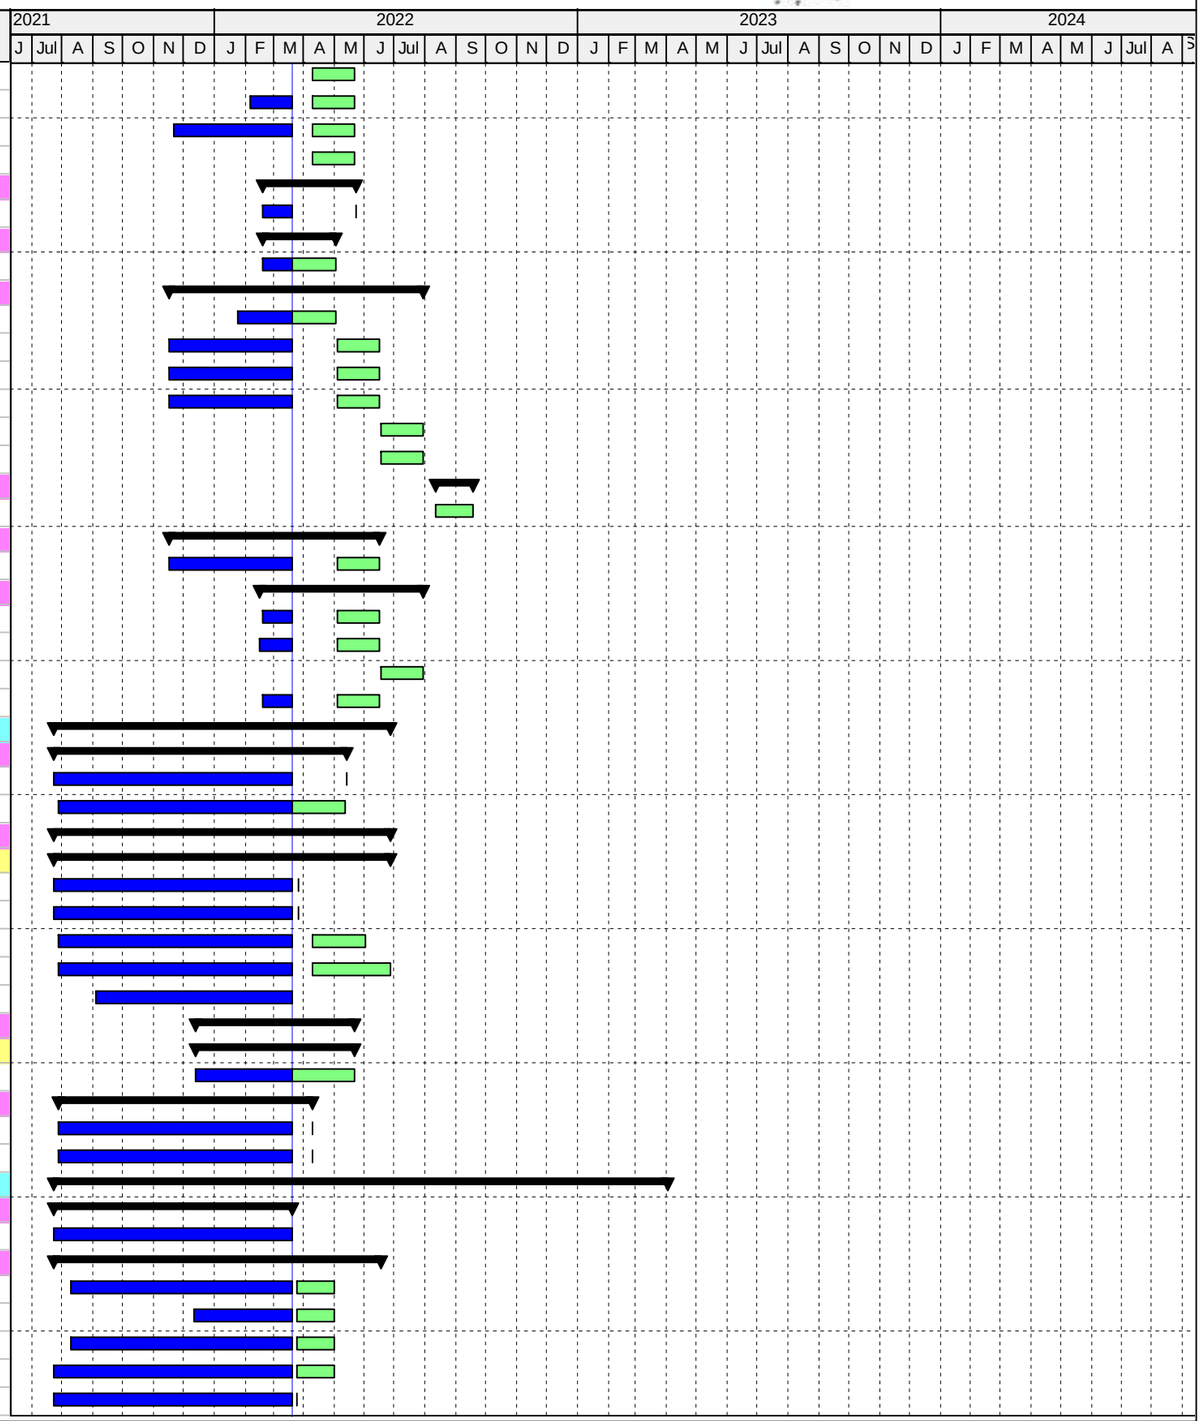


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-E	Specification For Painting	39	100%	$0.42	24-Jul-21 A	27-Mar-22
P11-E	Specification For Lining (Internal Protection of Equipment by F	39	60%	$0.50	09-Aug-21	04-May-22
P11-E	Specification For Material Requirements in Sour service	39	60%	$0.42	09-Aug-21	04-May-22
P11-E	Specification For Manual Valves	39	60%	$0.42	09-Aug-21	04-May-22
P11-E	Specification For Plant Piping Systems Pressure Testing	39	60%	$0.42	09-Aug-21	04-May-22
P11-E	Specification For Welding of Plant Piping System	39	60%	$0.42	09-Aug-21	04-May-22
P11-E	Specification For Flexibility Analysis	39	60%	$0.45	09-Aug-21	04-May-22
P11-E	Specification For Coating Of Underground Piping	39	100%	$0.71	24-Jul-21 A	30-Mar-22
P11-E	Specification For Pipe Support	39	60%	$0.55	09-Aug-21	27-Apr-22
P11-E	Specification For Piping Construction, Fabrication & Erection	39	60%	$0.71	09-Aug-21	27-Apr-22
P11-E	Specification For Piping Design & Plant Layout	39	60%	$1.24	09-Aug-21	27-Apr-22
P11-E	Specification For HDPE Pipes	39	100%	$1.86	24-Aug-21	20-Mar-22
P11-E	Specification For Insulation	39	100%	$1.24	24-Aug-21	30-Mar-22
P11-E	Piping Material Specification	44	80%	$149.54	12-Dec-21	17-Jun-22
P11-E	Specification For Piping Cleaning and Flushing	39	100%	$0.42	24-Aug-21	30-Mar-22
Procedure/Plan-1		39	100%	$5.00	24-Jul-21 A	03-Apr-22
P11-E	3D-Model (PDMS) Review Procedure	39	100%	$5.00	24-Jul-21 A	03-Apr-22
Drawing/Diagram		289	0%	$1,948.36	17-Jun-22	01-Apr-23
P11-E	Unit Plot Plan For Pig Receiver Area (in Siahmakan G.I. Stati	39	0%	$556.65	17-Jun-22	25-Jul-22
P11-E	A/G Piping Plan	44	0%	$556.65	09-Jan-23	21-Feb-23
P11-E	A/G Piping Isometric	39	0%	$278.42	22-Feb-23	01-Apr-23
P11-E	Unit Plot Plan For Binak Production Unit	54	0%	$556.65	16-Nov-22	08-Jan-23
Report		322	10.1%	$11,913.52	12-Dec-21	21-Feb-23
P11-E	Corrosion Study & Material Selection Report	44	80%	$835.14	12-Dec-21	16-Jun-22
P11-E	Wall Thickness Calculation Report	39	80%	$668.35	12-Dec-21	17-Jun-22
P11-E	Stress Analysis Calculations Report	44	0%	$668.35	09-Jan-23	21-Feb-23
P11-E	PDMS Model Review Report (30%)	54	0%	$2,783.00	26-Jul-22	17-Sep-22
P11-E	PDMS Model Review Report (60%)	59	0%	$4,175.69	18-Sep-22	15-Nov-22
P11-E	PDMS Model Review Report (90%)	54	0%	$2,783.00	16-Nov-22	08-Jan-23
List		250	0%	$556.68	17-Jun-22	21-Feb-23
P11-E	Pipe Support List	44	0%	$278.34	09-Jan-23	21-Feb-23
P11-E	Piping Tie-In List	39	0%	$278.34	17-Jun-22	25-Jul-22
Procedure/Plan		44	0%	$1,235.02	03-May-22	15-Jun-22
P11-E	Piping Hydrostatic Test Diagram - PPL	44	0%	$1,235.02	03-May-22	15-Jun-22
MTO		61	0%	$835.01	16-Nov-22	15-Jan-23
P11-E	MTO For Pipes	7	0%	$83.50	09-Jan-23	15-Jan-23
P11-E	MTO For Fittings	7	0%	$83.50	09-Jan-23	15-Jan-23
P11-E	MTO For Flanges	7	0%	$83.50	09-Jan-23	15-Jan-23
P11-E	MTO For Manual Valves	7	0%	$83.50	09-Jan-23	15-Jan-23
P11-E	MTO For Gaskets	7	0%	$83.50	09-Jan-23	15-Jan-23
P11-E	MTO For Bolt & Nuts	7	0%	$83.50	09-Jan-23	15-Jan-23
P11-E	MTO For Insulation Joints	5	0%	$83.50	16-Nov-22	20-Nov-22
P11-E	MTO For Insulation	7	0%	$83.50	09-Jan-23	15-Jan-23
P11-E	MTO For Painting	7	0%	$83.50	09-Jan-23	15-Jan-23
P11-E	MTO For Coating of Underground Piping	7	0%	$83.50	09-Jan-23	15-Jan-23
Pipeline		431	44.02%	$12,281.32	24-Jul-21 A	03-Mar-23
Basis/Criteria		39	100%	$210.01	28-Aug-21	20-Mar-22
P11-E	Pipeline Design Criteria	39	100%	$210.01	28-Aug-21	20-Mar-22
Specification		241	85.34%	$2,216.78	24-Jul-21 A	16-Jun-22

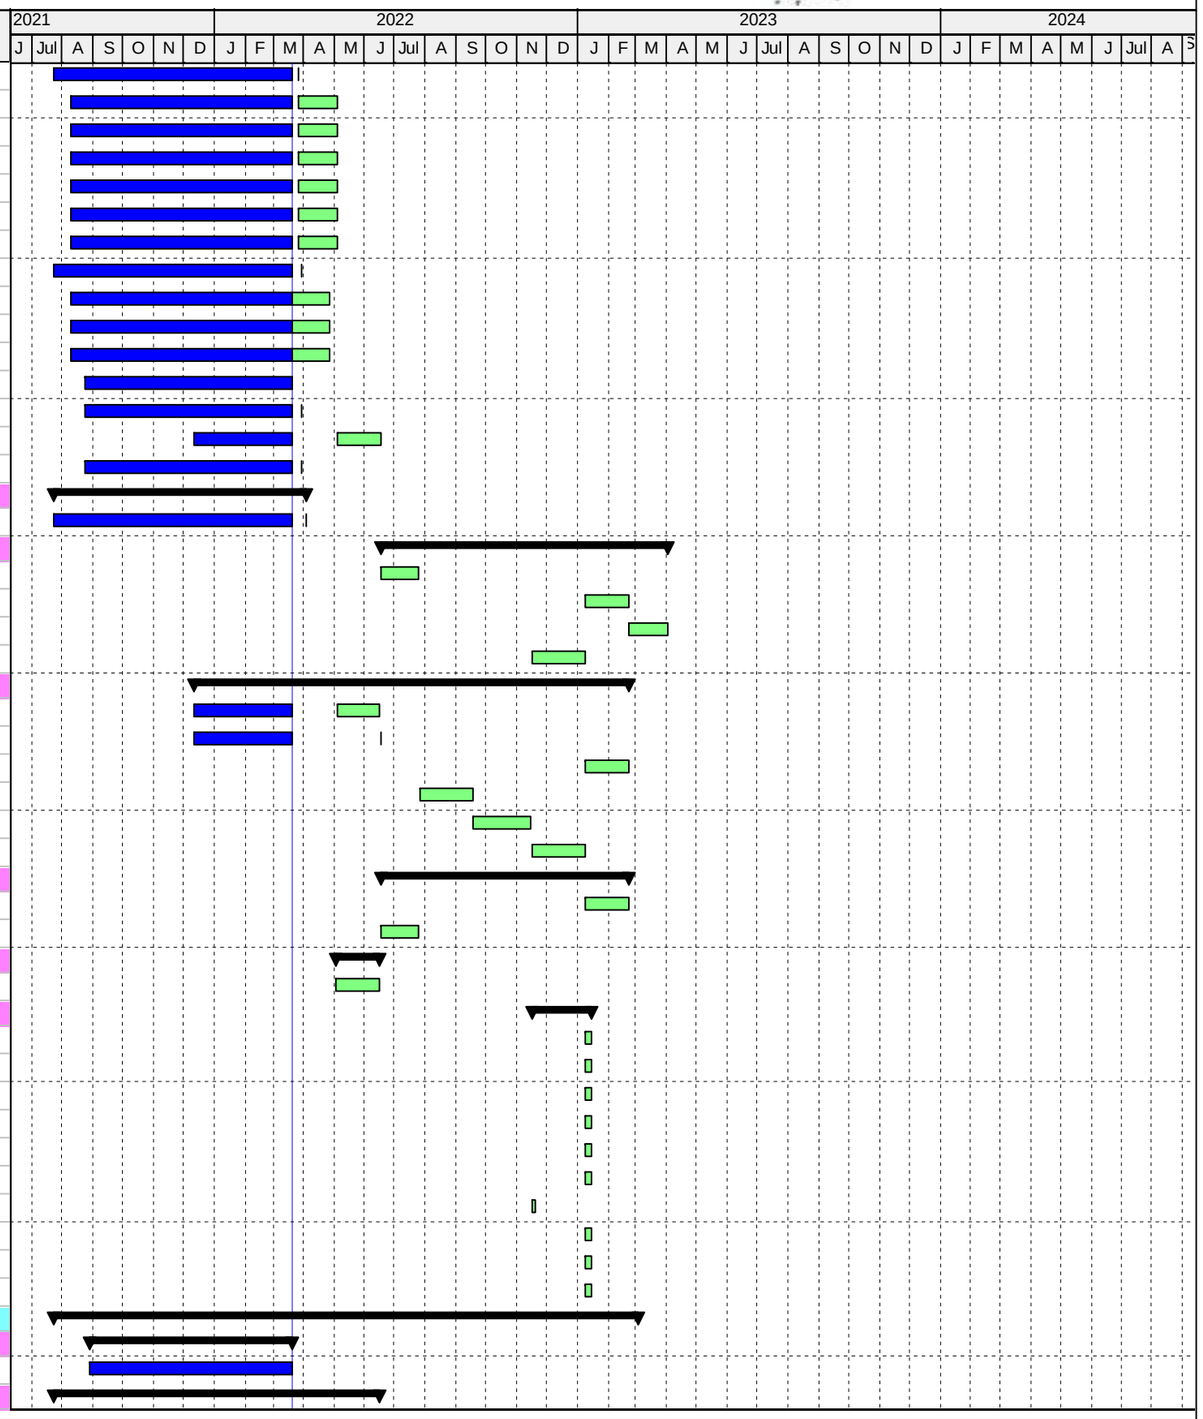


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-E	Specification For Line Pipes	39	100%	$148.08	24-Jul-21 A	24-Mar-22
P11-E	Specification For Pipeline Cold Bending	39	80%	$148.08	28-Aug-21	01-May-22
P11-E	Specification For Barred Tee	39	80%	$148.08	28-Aug-21	01-May-22
P11-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$148.08	24-Jul-21 A	24-Mar-22
P11-E	Specification For Pipeline Valves	39	80%	$148.08	28-Aug-21	01-May-22
P11-E	Specification For Pipeline Coating	39	100%	$147.64	24-Jul-21 A	24-Mar-22
P11-E	Specification For Pipeline Flushing, Cleaning And Hydrostatic	39	100%	$147.64	24-Jul-21 A	27-Mar-22
P11-E	Specification For Welding of Transportation Pipeline	39	80%	$147.64	12-Dec-21	04-May-22
P11-E	Specification For Pipeline Stress Analysis	39	80%	$147.64	24-Jul-21 A	04-May-22
P11-E	Specification For Pipeline Insulation Joint	39	100%	$147.64	24-Jul-21 A	27-Mar-22
P11-E	Specification For Pipeline Construction	39	80%	$147.64	25-Jan-22	04-May-22
P11-E	Specification For Anchor Flanges	39	80%	$147.64	28-Aug-21	07-May-22
P11-E	Specification For Pigs	39	80%	$147.64	28-Aug-21	07-May-22
P11-E	Pipeline Material Specification	44	80%	$147.64	12-Dec-21	16-Jun-22
P11-E	Specification For Pipeline Cleaning and Flushing	35	60%	$147.64	24-Jul-21 A	23-Apr-22
Calculation		44	80%	$2,096.42	12-Dec-21	17-Jun-22
P11-E	Calculation Note For Pipeline Wall Thickness	44	80%	$2,096.42	12-Dec-21	17-Jun-22
Data Sheets		39	0%	$1,692.37	01-Nov-22	09-Dec-22
P11-E	Data Sheets For Anchor Flanges	39	0%	$423.09	01-Nov-22	09-Dec-22
P11-E	Data Sheets For Barred Tee	39	0%	$423.09	01-Nov-22	09-Dec-22
P11-E	Data Sheets For Insulation Joints	39	0%	$423.09	01-Nov-22	09-Dec-22
P11-E	Data Sheets For Rock Shield	39	0%	$423.09	01-Nov-22	09-Dec-22
Drawing/Diagram		225	8%	$2,000.63	18-Sep-21	28-May-22
P11-E	Standard Support Drawings	35	0%	$900.28	24-Apr-22	28-May-22
P11-E	Pipeline Standard Drawings	35	0%	$900.28	20-Mar-22	23-Apr-22
P11-E	Pipeline Standard Drawing For Line Marker Post and Cathodi	35	80%	$200.06	18-Sep-21	23-Apr-22
Procedure/Plan		44	0%	$245.63	03-May-22	15-Jun-22
P11-E	Pipeline Hydrostatic Test Diagram - PPL	44	0%	$245.63	03-May-22	15-Jun-22
Report		116	40%	$2,920.50	12-Dec-21	03-Mar-23
P11-E	Stress Analysis Calculations Report For Pipelines	54	0%	$1,460.25	09-Jan-23	03-Mar-23
P11-E	Corrosion Study & Material Selection Report	44	80%	$1,460.25	12-Dec-21	04-May-22
MTO		131	33.34%	$898.99	22-Aug-21	22-Nov-22
P11-E	MTO For Line Pipe	7	100%	$299.72	22-Aug-21	26-Jul-22
P11-E	MTO For Pipeline Field Joints Coating	7	0%	$299.63	16-Nov-22	22-Nov-22
P11-E	MTO For Pipeline Flange, Fittings, Gasket and Bolt	7	0%	$299.63	16-Nov-22	22-Nov-22
Control & Instrumentation		445	12.96%	$12,458.03	24-Jul-21 A	04-Jan-23
Basis/Criteria		229	30%	$488.35	03-Jan-22	30-Apr-22
P11-E	Instrument & Control System Design Criteria	39	60%	$244.18	03-Jan-22	30-Apr-22
P11-E	Fire & Gas Detection Design Criteria	37	0%	$244.18	20-Mar-22	25-Apr-22
Specification		39	79.26%	$453.47	24-Jul-21 A	04-May-22
P11-E	Specification For Instrumentation	39	100%	$16.78	26-Jul-21 A	23-Mar-22
P11-E	Specification For Control System	39	80%	$44.80	28-Jul-21 A	30-Apr-22
P11-E	Specification For ESD System	39	80%	$44.80	28-Jul-21 A	30-Apr-22
P11-E	Specification For Instrument and Control of Package Unit Sys	39	60%	$33.47	04-Aug-21	30-Apr-22
P11-E	Specification For Control Valves	39	80%	$44.80	24-Jul-21 A	30-Apr-22
P11-E	Specification For On-off /Shut Down Valves(ESDV/MOV)	39	80%	$44.80	24-Jul-21 A	30-Apr-22
P11-E	Specification For Pressure Safety Valves(PSV)	39	100%	$44.80	24-Jul-21 A	27-Mar-22
P11-E	Specification For Fire & Gas Sensor and Devices	39	80%	$44.80	26-Jul-21 A	04-May-22
P11-E	Specification For Instrument/F&G Cables	39	60%	$44.80	04-Aug-21	04-May-22

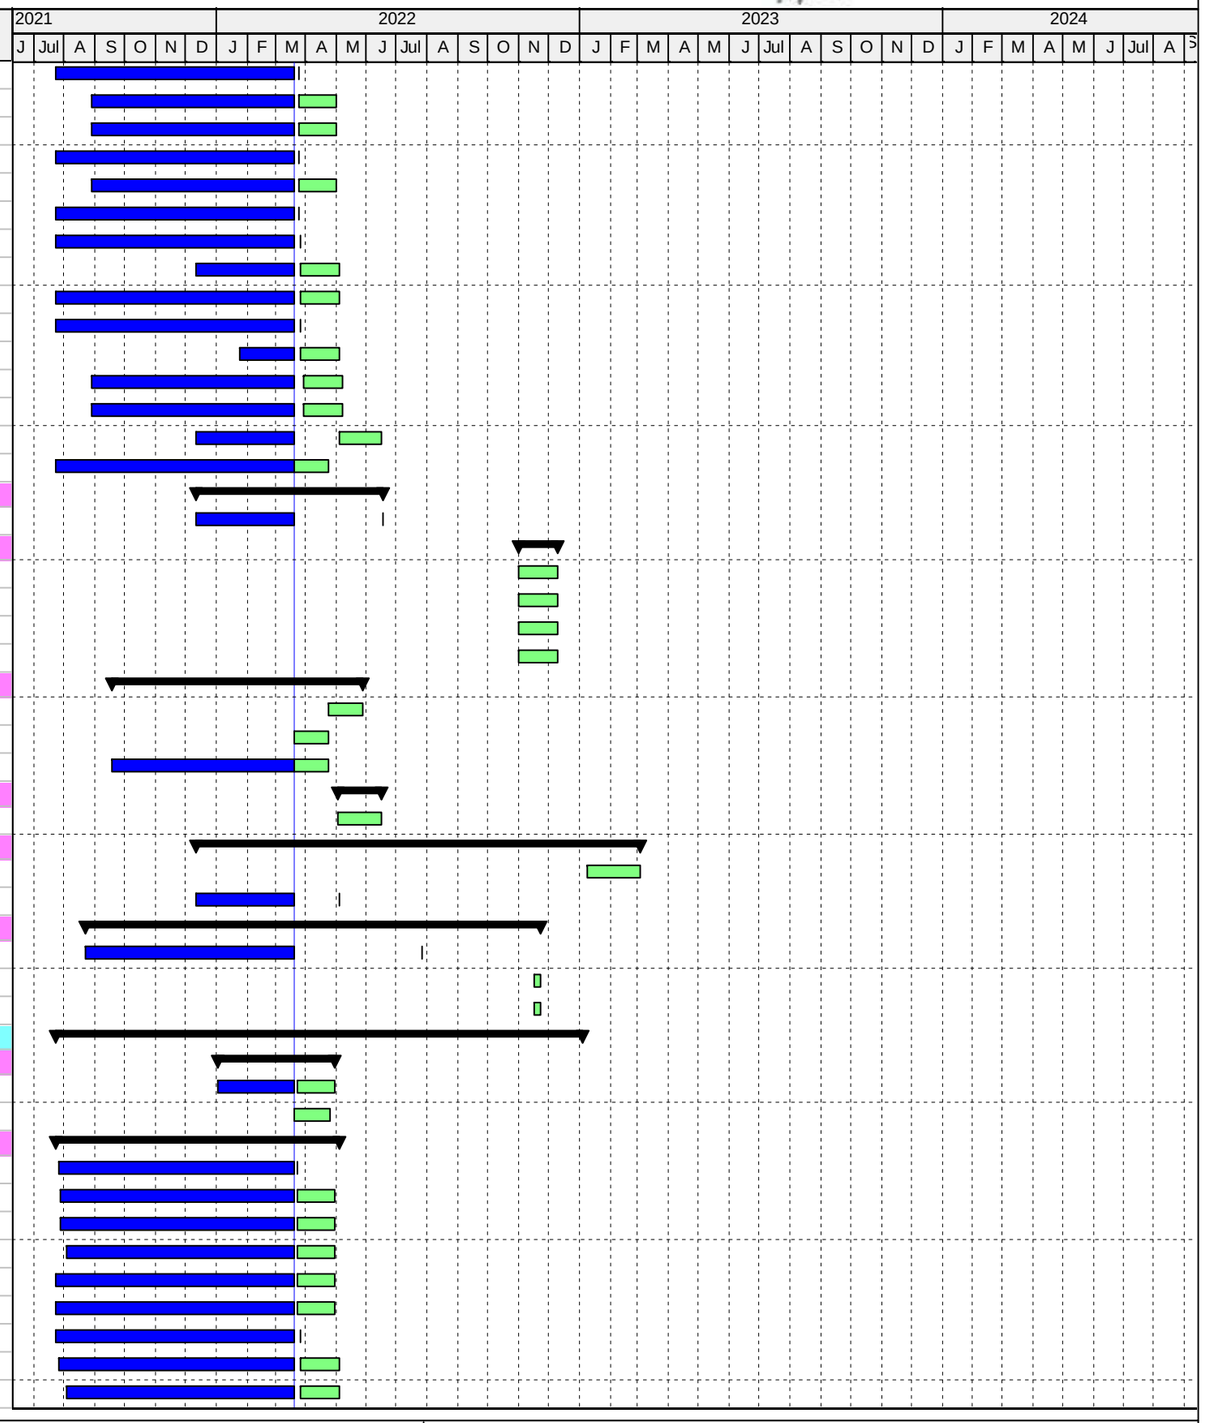


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-E	Specification For Control Panels and System Cabinets	39	60%	$44.80	24-Jul-21 A	04-May-22
P11-E	Specification For Fire & Gas System	39	100%	$44.80	28-Jul-21 A	20-Mar-22
Data Sheets		445	27.3%	$2,651.07	02-Feb-22	25-Jul-22
P11-E	Data Sheets For Pressure & Diff. Pressure Gauge	38	60%	$241.25	02-Feb-22	29-Apr-22
P11-E	Data Sheets For Temperature Gauge	38	60%	$241.25	05-Feb-22	29-Apr-22
P11-E	Data Sheets For Pressure/Diff. Pressure Transmitter	38	60%	$241.25	13-Feb-22	29-Apr-22
P11-E	Data Sheets For Pressure & Safety Relief Valves	39	0%	$334.83	17-Jun-22	25-Jul-22
P11-E	Data Sheets For ON/OFF & Shutdown Valves	39	0%	$334.83	17-Jun-22	25-Jul-22
P11-E	Data Sheets For Corrosion Coupon/ Probe	39	60%	$241.25	02-Feb-22	16-Jun-22
P11-E	Data Sheets For Pig Signaler	38	60%	$241.25	02-Feb-22	16-Jun-22
P11-E	Data Sheets For F&G Detectors & Equipment	39	0%	$334.56	27-Mar-22	04-May-22
P11-E	Data Sheets For LBV	36	0%	$440.61	20-Mar-22	24-Apr-22
Drawing/Diagram		291	5.04%	$5,513.92	01-Sep-21	04-Jan-23
P11-E	Typical Instrument Installation Drawing	35	0%	$315.95	20-Mar-22	23-Apr-22
P11-E	Block Diagram Configuration For Control/ESD/F&G System	38	80%	$189.68	01-Sep-21	30-Apr-22
P11-E	Instrument Earthing Typical Diagram	35	100%	$126.27	29-Dec-21	20-Mar-22
P11-E	Instrument Hook-up Diagram	40	0%	$315.95	17-Jun-22	26-Jul-22
P11-E	ESD Level Hierarchy	40	0%	$126.27	27-Jul-22	04-Sep-22
P11-E	ESD System Loop Diagram	42	0%	$315.95	19-Oct-22	29-Nov-22
P11-E	Control System Loop Diagram	42	0%	$315.95	19-Oct-22	29-Nov-22
P11-E	Instrument Air Piping and Air Header Diagram	42	0%	$126.27	16-Nov-22	27-Dec-22
P11-E	Instrument & F&G Junction Box Termination Diagram	42	0%	$379.36	27-Jul-22	06-Sep-22
P11-E	Control System Logic Diagram	42	0%	$252.54	27-Jul-22	06-Sep-22
P11-E	ESD Logic Diagram	42	0%	$252.54	27-Jul-22	06-Sep-22
P11-E	Control Room Cable Route Layout	42	0%	$252.54	24-Nov-22	04-Jan-23
P11-E	Instrument Location Layout	42	0%	$252.54	16-Nov-22	27-Dec-22
P11-E	Instrument Cable Trench/Route Layout Drawing	42	0%	$315.95	07-Sep-22	18-Oct-22
P11-E	Control Room Arrangement Layout	39	0%	$252.54	16-Oct-22	23-Nov-22
P11-E	F&G System Loop Diagram	39	0%	$957.77	26-Apr-22	03-Jun-22
P11-E	F&G Cause and Effect Diagram	39	0%	$513.35	26-Apr-22	03-Jun-22
P11-E	F&G Location Layout For Process Area	39	0%	$252.54	26-Apr-22	03-Jun-22
List		330	6.64%	$1,605.84	02-Feb-22	01-Jan-23
P11-E	Instrument Index	39	60%	$177.61	02-Feb-22	16-Jun-22
P11-E	I/O List For Control System	40	0%	$236.86	17-Jun-22	26-Jul-22
P11-E	I/O List For ESD /F&G System	40	0%	$177.61	17-Jun-22	26-Jul-22
P11-E	Panels & Junction Box List	39	0%	$118.35	07-Sep-22	15-Oct-22
P11-E	Set Point & Alarm List	40	0%	$177.61	17-Jun-22	26-Jul-22
P11-E	I&C Power Consumption Summary	39	0%	$118.35	24-Nov-22	01-Jan-23
P11-E	Instrument and F&G Cable List	42	0%	$177.61	07-Sep-22	18-Oct-22
P11-E	F&G Detector List	36	0%	$421.85	04-Jun-22	09-Jul-22
MTO		213	0%	$1,745.37	24-Apr-22	22-Nov-22
P11-E	MTO for Bulk Item and Installation Accessories	7	0%	$349.07	24-Apr-22	30-Apr-22
P11-E	MTO For Instrument/F&G Cable	7	0%	$349.07	19-Oct-22	25-Oct-22
P11-E	MTO For Instrument/F&G Junction box and Gland	7	0%	$349.07	16-Oct-22	22-Oct-22
P11-E	MTO For Instrument Tube and Fitting	7	0%	$349.07	27-Jul-22	02-Aug-22
P11-E	MTO For Instrument Cable Tray/Ladder	7	0%	$349.07	16-Nov-22	22-Nov-22
Safety & Fire Fighting		360	40.72%	$3,534.19	24-Jul-21 A	21-Feb-23
Basis/Criteria		44	60%	$256.94	16-Nov-21	02-May-22
P11-E	Active Fire Protection and Safety Concept	44	60%	$256.94	16-Nov-21	02-May-22

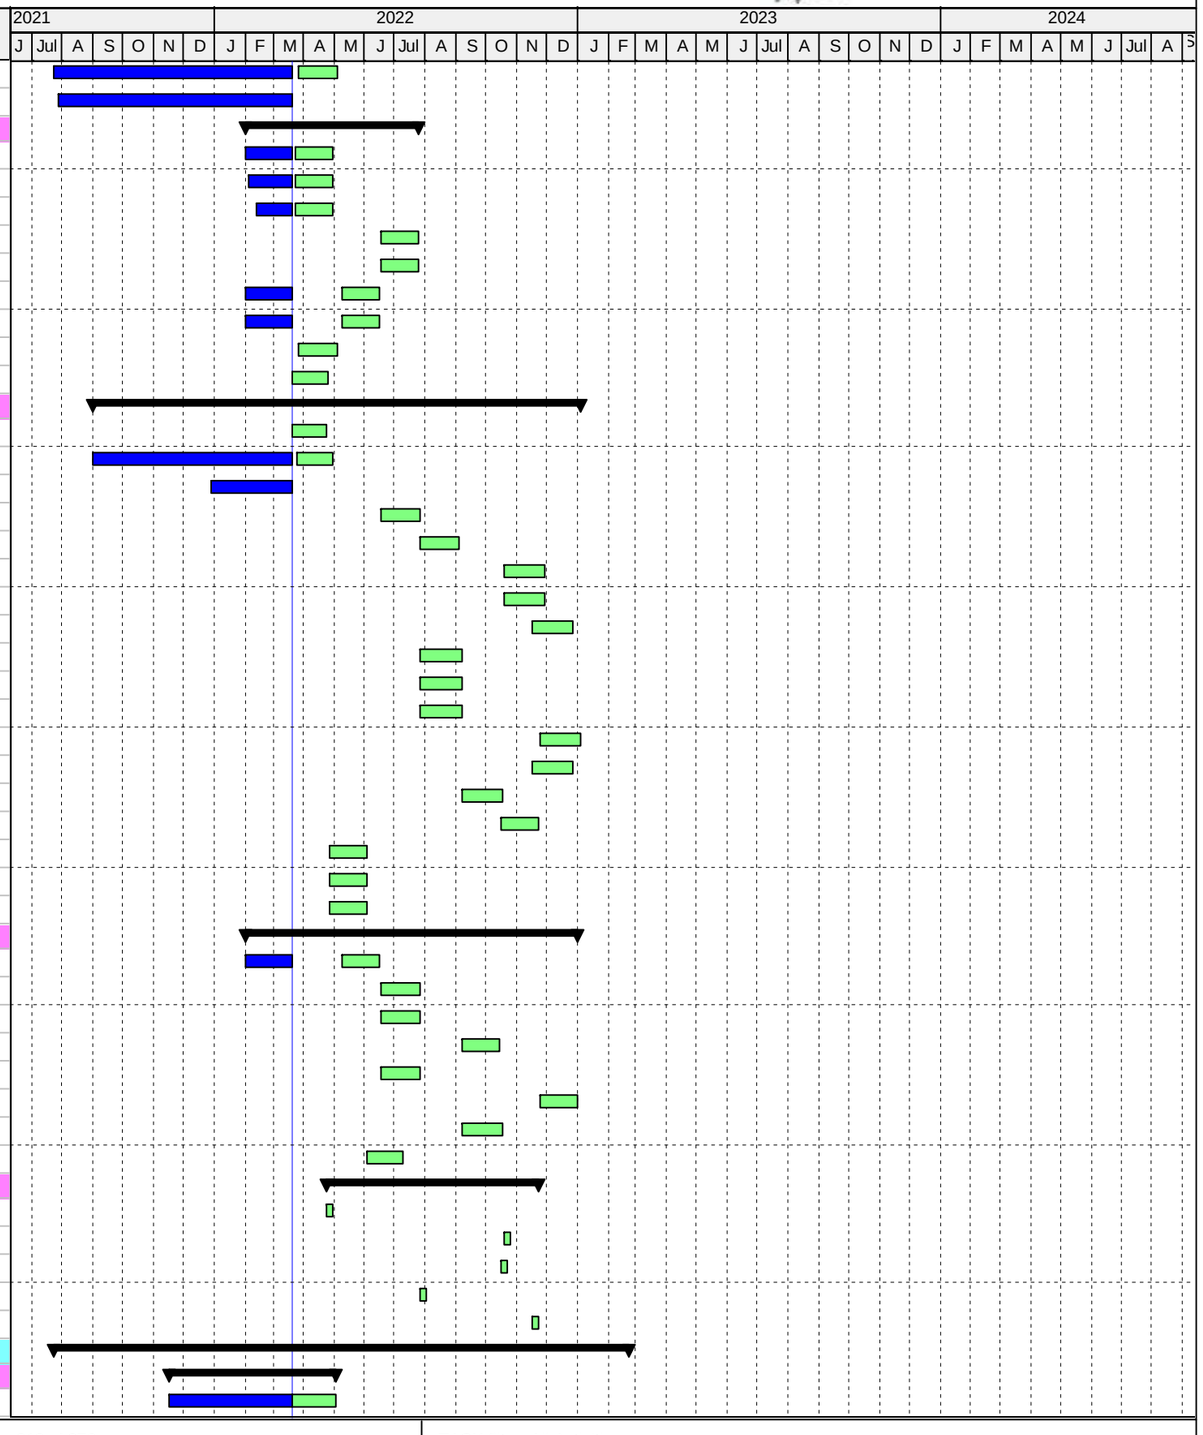


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Specification		44	90%	$770.81	24-Jul-21 A	06-May-22
P11-E	Specification For Fire Fighting Equipment	44	100%	$128.42	29-Aug-21	24-Mar-22
P11-E	Specification For Hazardous Area Classification	44	100%	$128.42	24-Jul-21 A	24-Mar-22
P11-E	Specification For Fire Water System	44	80%	$128.49	24-Jul-21 A	06-May-22
P11-E	Specification For Environmental Job	44	60%	$128.49	11-Aug-21	06-May-22
P11-E	Specification For Safety Equipment	44	100%	$128.49	29-Aug-21	27-Mar-22
P11-E	Specification For Safety Signs	44	100%	$128.49	24-Jul-21 A	27-Mar-22
Data Sheets		209	0%	$417.74	27-Mar-22	21-Oct-22
P11-E	Data Sheets For Safety Equipment	44	0%	$139.28	08-Sep-22	21-Oct-22
P11-E	Data Sheets For fire fighting Equipment	44	0%	$139.23	08-Sep-22	21-Oct-22
P11-E	Data Sheets For safety sign	44	0%	$139.23	27-Mar-22	09-May-22
Drawing/Diagram		106	47.05%	$1,092.42	29-Aug-21	07-Sep-22
P11-E	Typical Installation Detail for Safety & Fire Fighting Equipment	14	100%	$256.94	29-Dec-21	27-Mar-22
P11-E	Symbol & Legend For Safety & Firefighting Systems	44	100%	$257.05	29-Aug-21	27-Mar-22
P11-E	Hazardous Area Classification Layout	44	0%	$192.81	26-Jul-22	07-Sep-22
P11-E	Safety & Fire Fighting Equipment Location Layout	44	0%	$192.81	26-Jul-22	07-Sep-22
P11-E	Escape Route & Safety Sign Layout	44	0%	$192.81	26-Jul-22	07-Sep-22
Report		44	0%	$771.16	09-Jan-23	21-Feb-23
P11-E	QRA Report	44	0%	$771.16	09-Jan-23	21-Feb-23
List		44	60%	$128.64	16-Nov-21	16-Jun-22
P11-E	Hazard Source List	44	60%	$128.64	16-Nov-21	16-Jun-22
MTO		128	0%	$96.48	10-May-22	14-Sep-22
P11-E	MTO For Safety & Fire Fighting Equipment	7	0%	$48.24	08-Sep-22	14-Sep-22
P11-E	MTO For Safety Sign	5	0%	$48.24	10-May-22	14-May-22
Electrical		260	6.41%	$5,887.64	24-Jul-21 A	05-Nov-22
Basis/Criteria		54	100%	$25.32	03-Aug-21	20-Mar-22
P11-E	Electrical System Design Criteria	54	100%	$25.32	03-Aug-21	20-Mar-22
Specification		49	100%	$299.68	24-Jul-21 A	30-Mar-22
P11-E	Specification For LV Switchgear & Motor Control Centers	49	100%	$59.94	24-Jul-21 A	24-Mar-22
P11-E	Specification For Lighting & Small Power System	49	100%	$59.94	28-Jul-21 A	27-Mar-22
P11-E	Specification For Bulk Materials	49	100%	$59.94	24-Jul-21 A	27-Mar-22
P11-E	Specification For Power & Control Cables	49	100%	$59.94	24-Jul-21 A	30-Mar-22
P11-E	Specification For Cathodic Protection System	49	100%	$59.94	31-Jul-21 A	30-Mar-22
Calculation		44	0%	$416.26	03-May-22	15-Jun-22
P11-E	Calculation Note For Cathodic Protection System for Siahmak	44	0%	$416.26	03-May-22	15-Jun-22
Data Sheets		59	0%	$416.26	13-Jun-22	10-Aug-22
P11-E	Data Sheets For Expansion of LV Switchgear in Siahmakan G	59	0%	$208.13	13-Jun-22	10-Aug-22
P11-E	Data Sheets For Cathodic Protection System for Siahmakan (	44	0%	$208.13	16-Jun-22	29-Jul-22
Drawing/Diagram		260	2.36%	$2,231.42	09-Aug-21	05-Nov-22
P11-E	Electrical Legend and Symbols	49	100%	$10.49	09-Aug-21	30-Mar-22
P11-E	Typical Installation Details & Notes For Earthing and Lightning	14	100%	$14.06	25-Aug-21	30-Mar-22
P11-E	Typical Installation Details & Notes For Lighting System	14	100%	$14.06	25-Aug-21	30-Mar-22
P11-E	Installation Details & Notes For Cathodic Protection Systems	74	100%	$14.06	25-Aug-21	30-Mar-22
P11-E	Single Line Diagram For Expansion Of Upstream LV Switchge	62	0%	$461.01	19-Aug-22	19-Oct-22
P11-E	Interconnection Wiring Diagram in Siahmakan Gas Injection	79	0%	$419.06	19-Aug-22	05-Nov-22
P11-E	Interconnection Wiring Diagrams For Cathodic Protection Sys	44	0%	$418.84	30-Jul-22	11-Sep-22
P11-E	Area Earthing Layout in Siahmakan Gas Injection	59	0%	$209.53	24-Mar-22	21-May-22
P11-E	Area Electrical Cable Route & Section Layout in Siahmakan G	59	0%	$209.53	16-Jun-22	13-Aug-22
P11-E	Layout For Cathodic Protection System for Siahmakan Gas Ir	44	0%	$460.79	16-Jun-22	29-Jul-22

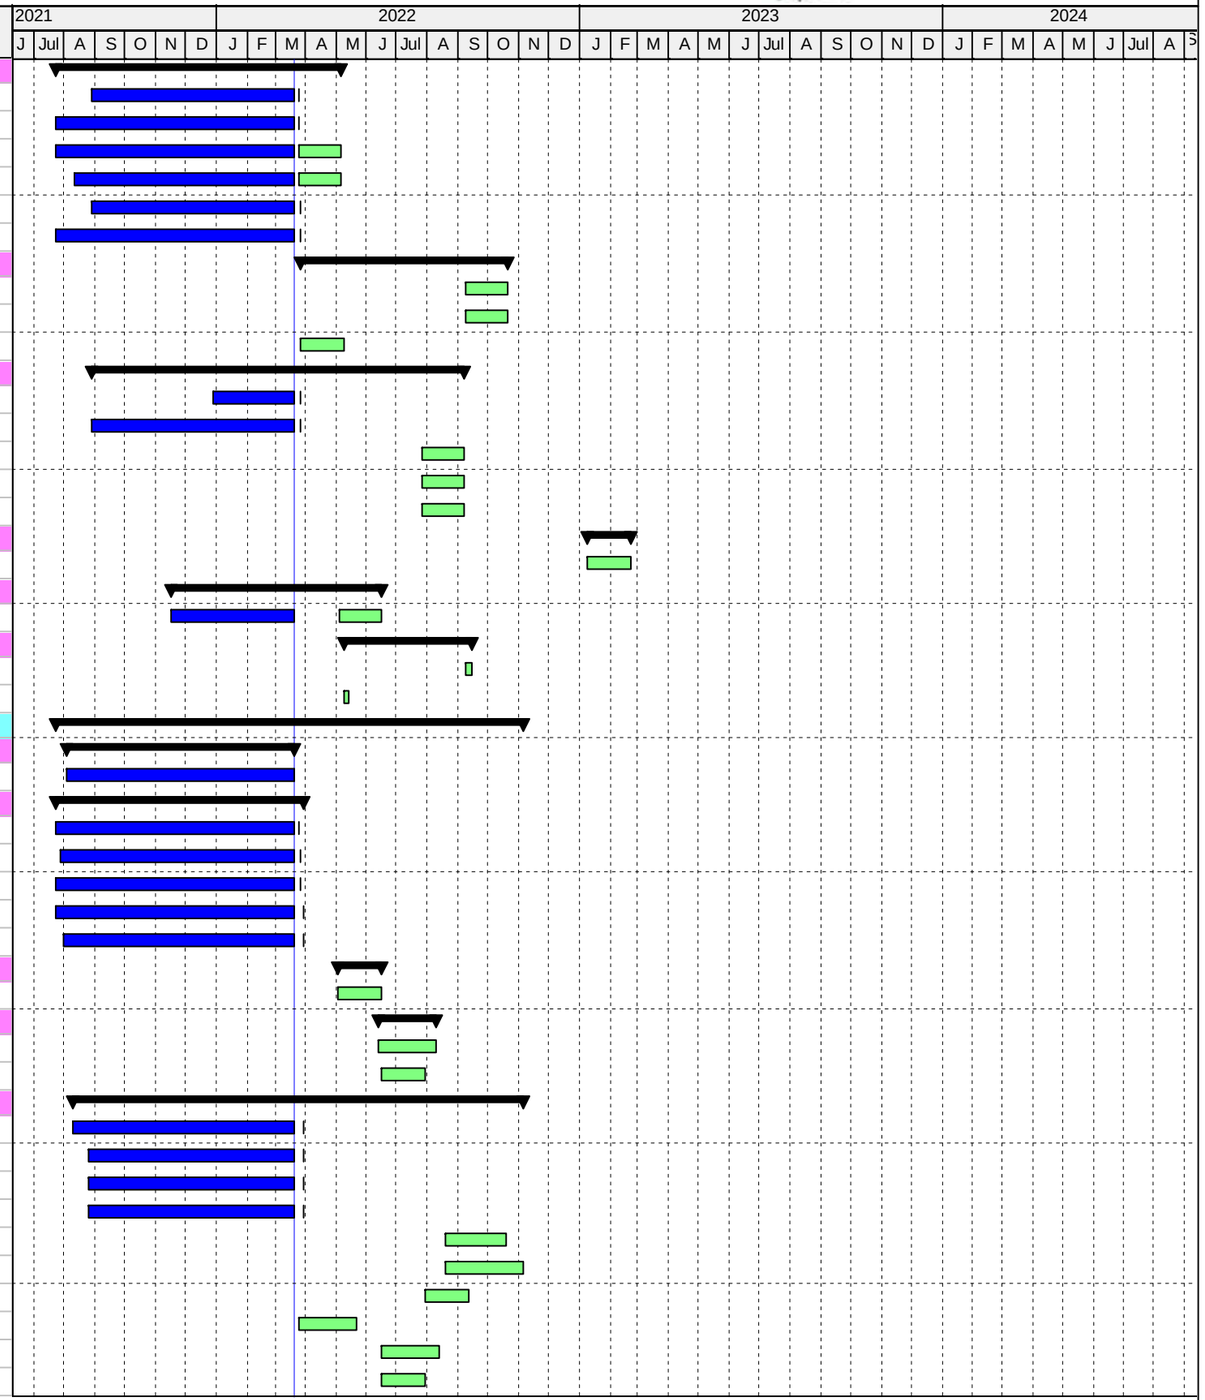


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
List		64	0%	$833.10	16-Jun-22	18-Aug-22
P11-E	Electrical Load List in Siahmakan Gas Injection	64	0%	$249.93	16-Jun-22	18-Aug-22
P11-E	Electrical Power & Control Cable List in Siahmakan Gas Inject	64	0%	$249.93	16-Jun-22	18-Aug-22
P11-E	Cable Schedule For Cathodic Protection System for Siahmaka	44	0%	$333.24	16-Jun-22	29-Jul-22
MTO		96	0%	$1,665.61	22-May-22	25-Aug-22
P11-E	MTO For Earthing & Lightning Systems in Siahmakan Gas Inj	7	0%	$333.12	22-May-22	28-May-22
P11-E	MTO For Power & Control Cables in Siahmakan Gas Injectio	7	0%	$333.12	19-Aug-22	25-Aug-22
P11-E	MTO For Cathodic Protection System for Siahmakan Gas Inje	7	0%	$333.12	19-Aug-22	25-Aug-22
P11-E	MTO For Electrical Bulk Items in Siahmakan Gas Injection	7	0%	$333.12	19-Aug-22	25-Aug-22
P11-E	MTO For Lighting & Small Powers in Siahmakan Gas Injectio	7	0%	$333.12	22-May-22	28-May-22
Civil		254	13.48%	$2,433.77	01-Aug-21	10-Nov-22
Basis/Criteria		250	20%	$73.01	13-Feb-22	22-May-22
P11-E	Civil Design Criteria	64	60%	$24.34	13-Feb-22	22-May-22
P11-E	Design Criteria for Sewerage & Drainage	44	0%	$24.34	24-Mar-22	06-May-22
P11-E	Design Criteria for Road and Paving	44	0%	$24.34	27-Mar-22	09-May-22
Specification		254	60%	$97.35	09-Aug-21	06-Jun-22
P11-E	Specification For Civil Works	79	0%	$16.22	20-Mar-22	06-Jun-22
P11-E	Specification For Road & Paving	64	80%	$16.22	09-Aug-21	22-May-22
P11-E	Specification For Fence & Gate	64	100%	$16.23	18-Sep-21	20-Mar-22
P11-E	Specification For Earth Work	64	80%	$16.23	09-Aug-21	22-May-22
P11-E	Specification For Sewerage & Drainage	64	100%	$16.23	09-Aug-21	20-Mar-22
P11-E	Specification For Geological & Geotechnical Survey	44	0%	$16.23	20-Mar-22	02-May-22
Drawing/Diagram		244	12.47%	$2,044.37	01-Aug-21	10-Nov-22
P11-E	Standard Drawing For Civil Works	64	0%	$15.54	30-Mar-22	01-Jun-22
P11-E	Standard Drawing For Slope Protection Details	64	100%	$15.54	22-Aug-21	30-Mar-22
P11-E	Standard Drawing For Roads	64	80%	$15.54	22-Aug-21	01-Jun-22
P11-E	Standard Drawing For Electrical Cable Trench	64	100%	$15.54	22-Aug-21	30-Mar-22
P11-E	Standard Drawing For Manholes	64	80%	$15.54	22-Aug-21	01-Jun-22
P11-E	Standard Drawing For Catch Basins	64	80%	$15.54	22-Aug-21	05-Jun-22
P11-E	Standard Drawing For Sewerage & Drainage Details	64	60%	$15.54	02-Feb-22	05-Jun-22
P11-E	Standard Drawing For Civil Underground Crossings	38	60%	$25.35	07-Feb-22	10-May-22
P11-E	Standard Drawing For Fence & Gate Details	64	100%	$15.54	18-Sep-21	03-Apr-22
P11-E	Standard Drawing For Concrete Continues Weight	38	100%	$25.35	01-Aug-21	20-Mar-22
P11-E	Standard Drawing For Major Floodway Crossing	38	0%	$25.35	03-Apr-22	10-May-22
P11-E	Standard Drawing For Culvert & Details	38	100%	$25.35	25-Sep-21	03-Apr-22
P11-E	Standard Drawing For Valve Box	38	100%	$25.35	12-Jan-22	03-Apr-22
P11-E	Standard Drawing For Fire Hydrant Pit	38	60%	$25.35	13-Mar-22	10-May-22
P11-E	Standard Drawing For Cable Pull Pit	64	0%	$15.54	03-Apr-22	05-Jun-22
P11-E	Standard Drawing For Pavings	38	60%	$25.35	08-Jan-22	10-May-22
P11-E	Standard Drawing For Earth Pit	38	60%	$25.35	13-Feb-22	10-May-22
P11-E	Standard Detail For Pipe Bedding	64	100%	$15.54	22-Aug-21	03-Apr-22
P11-E	Standard Details of Miscellaneous Items	64	60%	$15.54	06-Mar-22	05-Jun-22
P11-E	Civil Layout For Pig Receiver Area (In Siahmakan G.I. Statior	64	0%	$918.13	26-Jul-22	27-Sep-22
P11-E	Civil Layout For LBV Stations	44	0%	$752.53	28-Sep-22	10-Nov-22
Report		44	0%	$219.04	16-Sep-22	29-Oct-22
P11-E	Site Visit Report (Civil Work) - 8" & 4" Pipelines	44	0%	$219.04	16-Sep-22	29-Oct-22
Structure		254	75.51%	$891.58	08-Aug-21	28-Nov-22
Basis/Criteria		64	0%	$34.24	20-Mar-22	22-May-22
P11-E	Structural Design Criteria	64	0%	$11.41	20-Mar-22	22-May-22

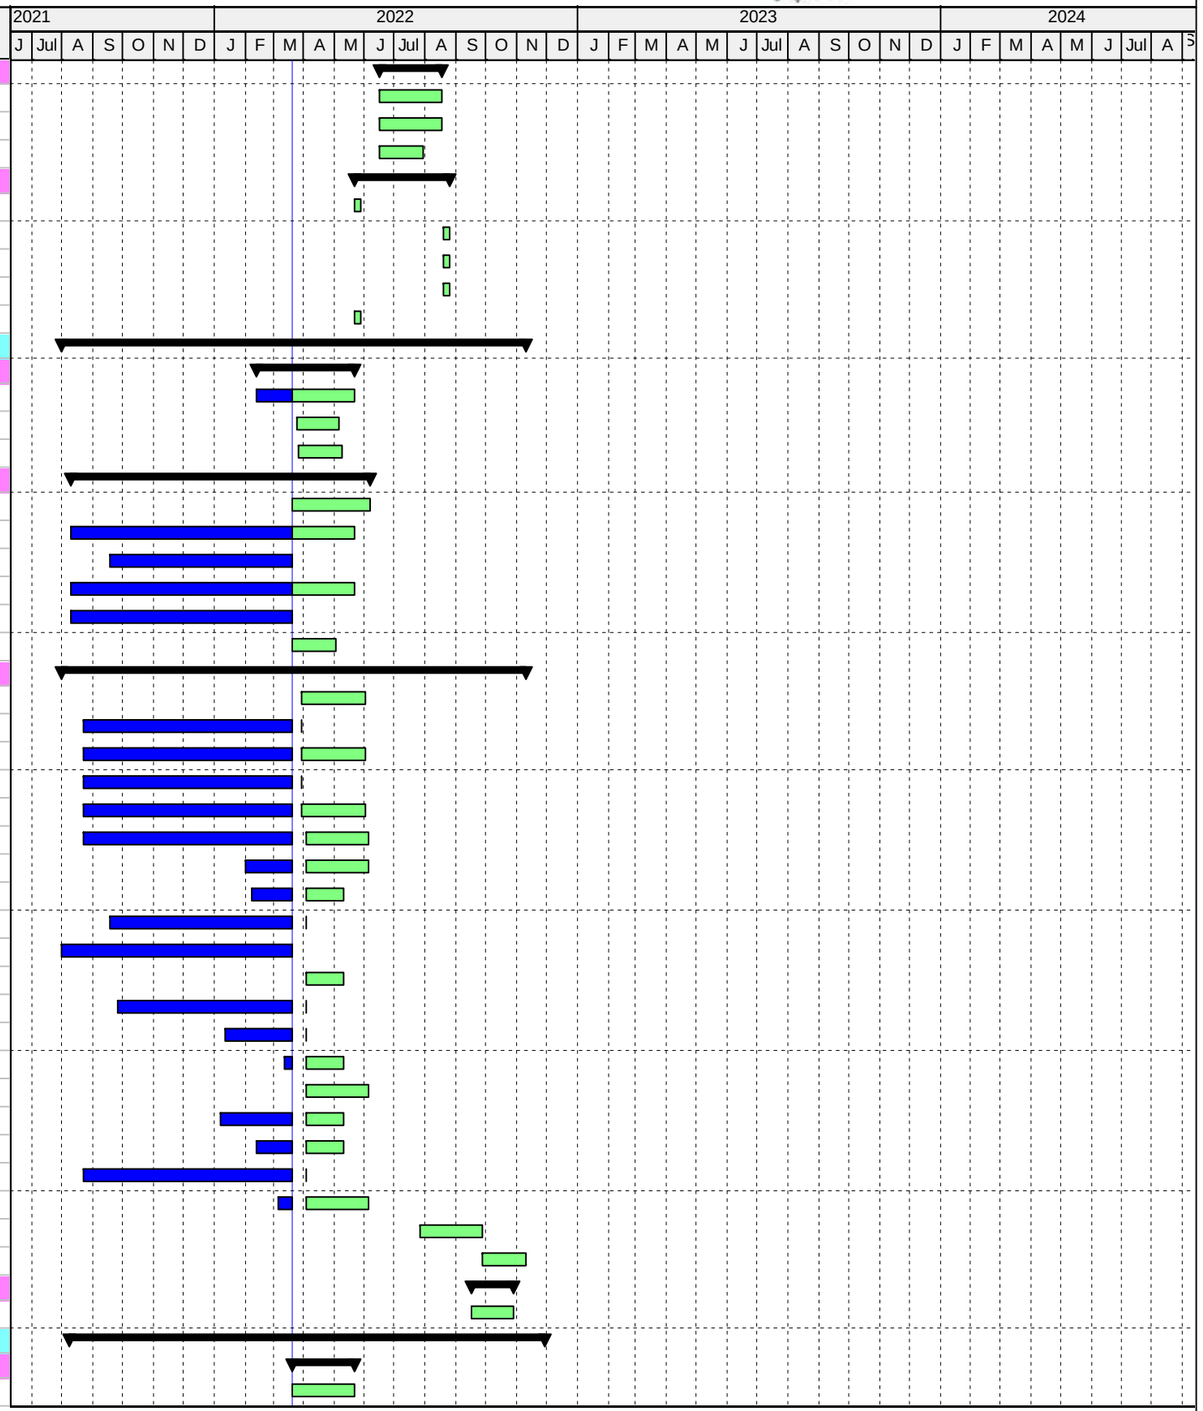


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-E	Design Criteria For Steel Structure	44	0%	$11.41	20-Mar-22	02-May-22
P11-E	Design Criteria For Load & Forces	44	0%	$11.41	20-Mar-22	02-May-22
Specification		254	83.04%	$262.93	14-Aug-21	26-May-22
P11-E	Specification For Concrete Work	64	80%	$38.52	14-Aug-21	26-May-22
P11-E	Specification for Fabrication of Steel Structures	64	100%	$49.75	24-Jan-22	24-Mar-22
P11-E	Specification For Grouting	64	100%	$38.52	14-Aug-21	24-Mar-22
P11-E	Specification for Erection of Steel Structures	64	100%	$50.06	24-Jan-22	24-Mar-22
P11-E	Specification for Fireproofing	64	100%	$49.19	18-Sep-21	24-Mar-22
P11-E	Specification For Steel Structural Works	37	0%	$36.89	20-Mar-22	25-Apr-22
Drawing/Diagram		244	76.52%	$594.42	08-Aug-21	28-Nov-22
P11-E	Standard Drawing For Fire Proofing	64	100%	$25.74	08-Aug-21	03-Apr-22
P11-E	Standard Drawing For Anchor Bolts	64	100%	$25.74	15-Dec-21	03-Apr-22
P11-E	Standard Drawing For Steel Stairs	64	100%	$25.74	18-Dec-21	03-Apr-22
P11-E	Standard Drawing For Operating Platform	38	100%	$42.92	27-Dec-21	30-Mar-22
P11-E	Standard Drawing For Handrail	38	100%	$42.92	18-Dec-21	30-Mar-22
P11-E	Standard Drawing For Insert Plates in Concrete	38	100%	$42.92	08-Aug-21	30-Mar-22
P11-E	Standard Details For Ladder & Safety Cage	64	100%	$25.74	15-Dec-21	03-Apr-22
P11-E	Standard Drawing For Lighting pole foundation Plan & Details	38	60%	$42.92	29-Jan-22	06-May-22
P11-E	General Notes - Steel Structures	38	100%	$42.92	25-Jan-22	30-Mar-22
P11-E	General Notes - Reinforced Concrete Structures	38	100%	$42.92	20-Dec-21	30-Mar-22
P11-E	Standard Drawing For Structural Built-up Sections	44	80%	$42.92	04-Dec-21	12-May-22
P11-E	Standard Drawing For Steel Flooring, Grating and Chequere	44	100%	$42.92	05-Jan-22	30-Mar-22
P11-E	Concrete Reinforcement Shape Code	44	0%	$42.86	30-Mar-22	12-May-22
P11-E	Standard Drawing For Septic Tank	44	80%	$42.86	22-Jan-22	12-May-22
P11-E	Foundation Drawing For Pig Receiver (PL-3101 In Siahmaka	44	0%	$31.21	16-Oct-22	28-Nov-22
P11-E	Structural Drawing For LBV Pits	44	0%	$31.21	04-Aug-22	16-Sep-22
Survey (Topography) & Geotechnic		234	12.06%	$18,867.77	11-Aug-21	07-Sep-22
Risk Assessment		44	100%	$943.39	05-Sep-21	20-Mar-22
Procedure/Plan		44	100%	$943.39	05-Sep-21	20-Mar-22
P11-I	HAZOP Study Procedure	44	100%	$471.69	25-Oct-21	20-Mar-22
P11-I	HAZID Study Procedure	44	100%	$471.69	05-Sep-21	20-Mar-22
Geotechnic		229	8%	$14,150.83	11-Aug-21	02-May-22
Procedure/Plan		39	100%	$1,132.07	11-Aug-21	20-Mar-22
P11-I	Geotechnical Investigation Plan for Pipelines	39	100%	$1,132.07	11-Aug-21	20-Mar-22
Report		44	0%	$13,018.76	20-Mar-22	02-May-22
P11-I	Geotechnical Investigation Report for Pipelines	44	0%	$13,018.76	20-Mar-22	02-May-22
Survey		128	0%	$1,886.78	03-May-22	07-Sep-22
Drawing/Diagram		128	0%	$1,886.78	03-May-22	07-Sep-22
P11-I	Plan & Profile Drawings For Gas Pipeline (to Siahmakan)	39	0%	$754.71	03-May-22	10-Jun-22
P11-I	Transversal Profiles For Gas Pipeline (to Siahmakan)	44	0%	$566.03	17-Jun-22	30-Jul-22
P11-I	Plan & Profile Drawings For Condensate Pipeline (to Binak Pl	39	0%	$377.36	17-Jun-22	25-Jul-22
P11-I	Transversal Profiles For Condensate Pipeline (to Binak PU)	44	0%	$188.68	26-Jul-22	07-Sep-22
QC/QA		234	10.59%	$1,886.78	20-Sep-21	13-Jul-22
QC Management		234	39%	$153.39	08-Dec-21	13-Jul-22
P11-I	Project Audit Procedure	44	0%	$7.67	20-Mar-22	02-May-22
P11-I	Specification For Final Data Book (FDB) Requirements	44	0%	$7.67	20-Mar-22	02-May-22
P11-I	Non Conformance Control Procedure	36	0%	$7.67	03-May-22	07-Jun-22
P11-I	Corrective Action Procedure	36	0%	$7.67	08-Jun-22	13-Jul-22
P11-I	Material Reciving, Storage, Handling Procedure	39	60%	$7.67	20-Feb-22	27-Apr-22

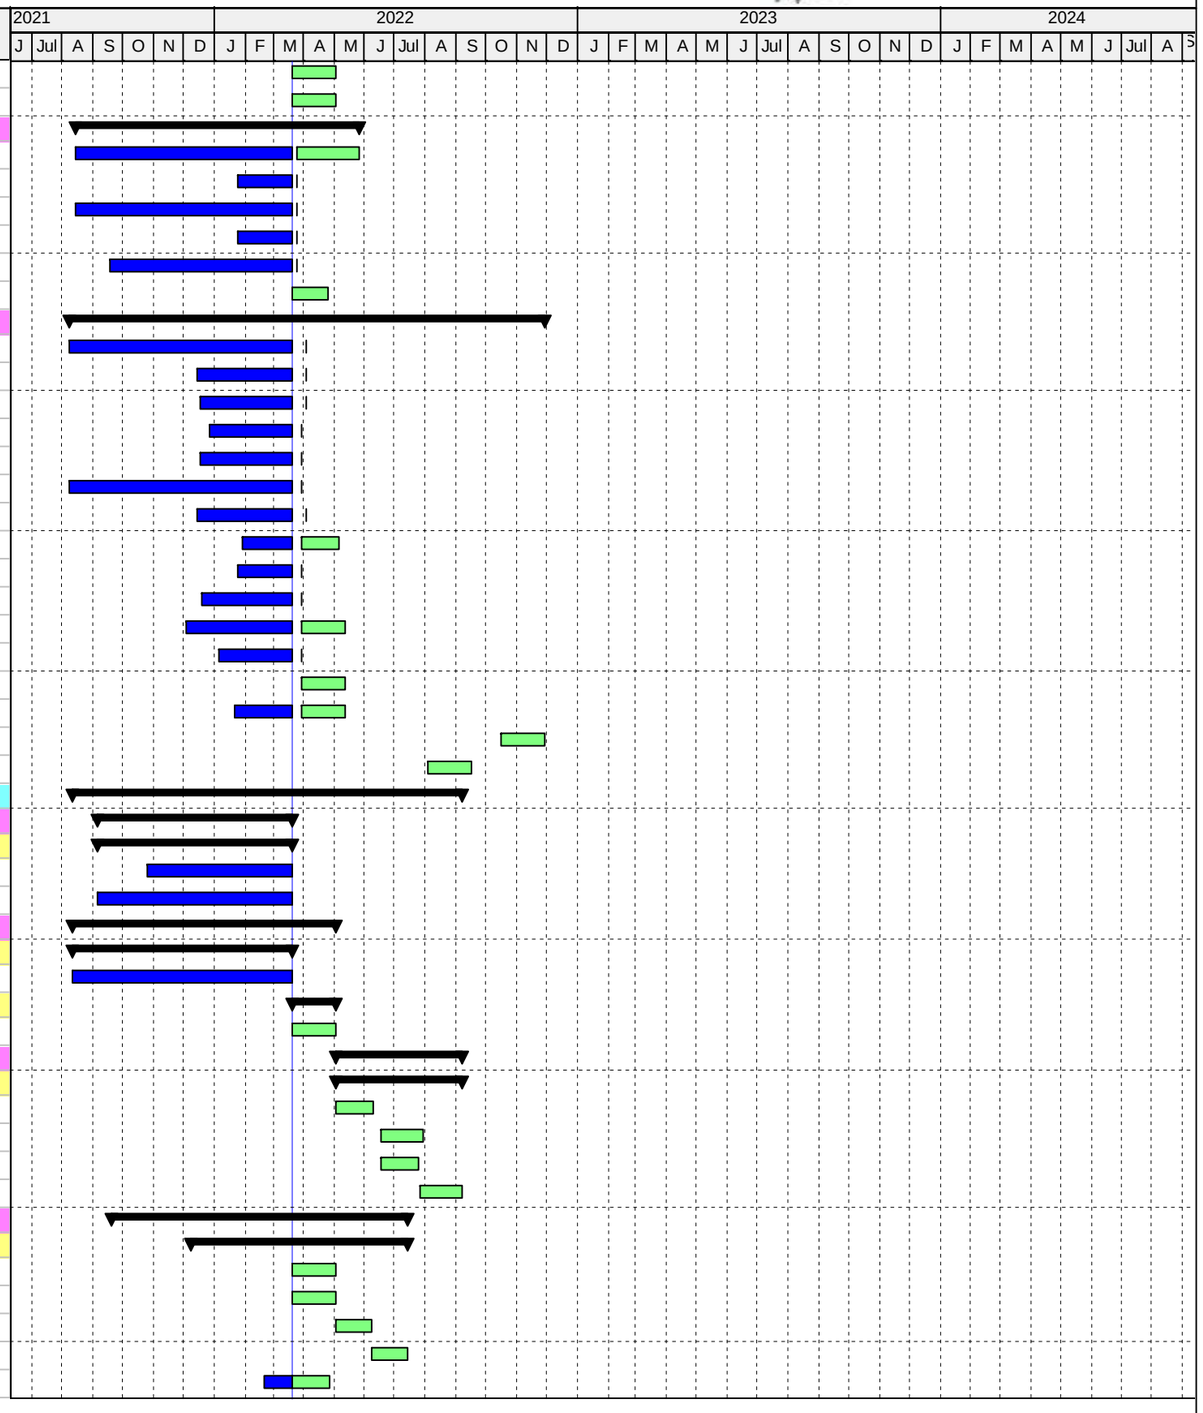


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-I	Packing, Marking, Transportation Procedure	39	0%	$7.67	20-Mar-22	27-Apr-22
P11-I	Criticality Assessment Procedure	39	0%	$30.68	20-Mar-22	27-Apr-22
P11-I	Project Quality Plan	44	80%	$69.03	08-Dec-21	02-May-22
P11-I	Technical Query Procedure	44	0%	$7.67	30-Mar-22	12-May-22
QC General Document		215	8.58%	$223.96	28-Nov-21	16-May-22
P11-I	Quality Control Plan (QCP)	39	60%	$32.03	28-Nov-21	27-Apr-22
P11-I	Specification for Welding Procedure	44	0%	$32.03	03-Apr-22	16-May-22
P11-I	Heat Treatment Procedure (Pre Heating , PWHT)	44	0%	$32.03	03-Apr-22	16-May-22
P11-I	Welder Performance Qualification Test (WQT) Procedure	44	0%	$32.03	03-Apr-22	16-May-22
P11-I	NDT Procedure	44	0%	$32.03	03-Apr-22	16-May-22
P11-I	Surface Preparation and Coating/Painting Procedure	44	0%	$32.03	03-Apr-22	16-May-22
P11-I	Control of Inspection Measuring and Test Equipment Procedu	44	0%	$31.80	03-Apr-22	16-May-22
QC Discipline Document		227	8%	$1,509.42	20-Sep-21	29-Jun-22
Piping		95	0%	$377.36	27-Mar-22	29-Jun-22
P11	ITP For Piping Works	44	0%	$37.74	27-Mar-22	09-May-22
P11	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$42.45	03-Apr-22	16-May-22
P11	PIPING WPS (Welding Procedure Specification)	44	0%	$42.45	03-Apr-22	16-May-22
P11	PIPING PQR (Procedure Qualification Record)	44	0%	$42.45	03-Apr-22	16-May-22
P11	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$42.45	03-Apr-22	16-May-22
P11	PIPING WPS (Preliminary Welding Procedure Specification) f	44	0%	$42.45	03-Apr-22	16-May-22
P11	PIPING PQR (Procedure Qualification Record) for Repair We	44	0%	$42.45	03-Apr-22	16-May-22
P11	Field Joint Coating Procedure For Pipeline	44	0%	$42.45	03-Apr-22	16-May-22
P11	Pressure Test Procedure	44	0%	$42.45	17-May-22	29-Jun-22
Telecomm.		44	0%	$75.47	27-Mar-22	09-May-22
P11	ITP For Telecommunication Installation	44	0%	$75.47	27-Mar-22	09-May-22
Safety		44	0%	$75.47	27-Mar-22	09-May-22
P11	ITP For Safety Installation	44	0%	$75.47	27-Mar-22	09-May-22
Architectural		44	0%	$75.47	27-Mar-22	09-May-22
P11	ITP For Architectural Works	44	0%	$75.47	27-Mar-22	09-May-22
Mechanical		44	0%	$75.47	27-Mar-22	09-May-22
P11	ITP For Mechanical Installation	44	0%	$75.47	27-Mar-22	09-May-22
Structure		51	0%	$301.88	27-Mar-22	16-May-22
P11	ITP For Steel Structural Works	44	0%	$30.19	27-Mar-22	09-May-22
P11	Steel Structure WPS (Welding Procedure Specification)	44	0%	$45.28	03-Apr-22	16-May-22
P11	Steel Structure PQR (Procedure Qualification Record)	44	0%	$45.28	03-Apr-22	16-May-22
P11	Steel Structure WPS (Welding Procedure Specification) For F	44	0%	$45.28	03-Apr-22	16-May-22
P11	Steel Structure PQR (Procedure Qualification Record) For Re	44	0%	$45.28	03-Apr-22	16-May-22
P11	Weld Map For Steel Structures	44	0%	$45.28	03-Apr-22	16-May-22
P11	NDT Plan For steel Structures	44	0%	$45.28	03-Apr-22	16-May-22
Instrumentation		44	0%	$75.47	27-Mar-22	09-May-22
P11	ITP For I&C Installation	44	0%	$75.47	27-Mar-22	09-May-22
Pipeline		220	15%	$301.88	16-Jan-22	16-May-22
P11	ITP For Pipeline	44	60%	$30.19	16-Jan-22	09-May-22
P11	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	60%	$45.28	23-Feb-22	16-May-22
P11	PIPELINE WPS (Welding Procedure Specification)	44	0%	$45.28	03-Apr-22	16-May-22
P11	PIPELINE PQR (Procedure Qualification Record)	44	0%	$45.28	03-Apr-22	16-May-22
P11	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	0%	$45.28	03-Apr-22	16-May-22
P11	PIPELINE WPS (Preliminary Welding Procedure Specificatior	44	0%	$45.28	03-Apr-22	16-May-22
P11	PIPELINE PQR (Procedure Qualification Record) for Repair \	44	0%	$45.28	03-Apr-22	16-May-22

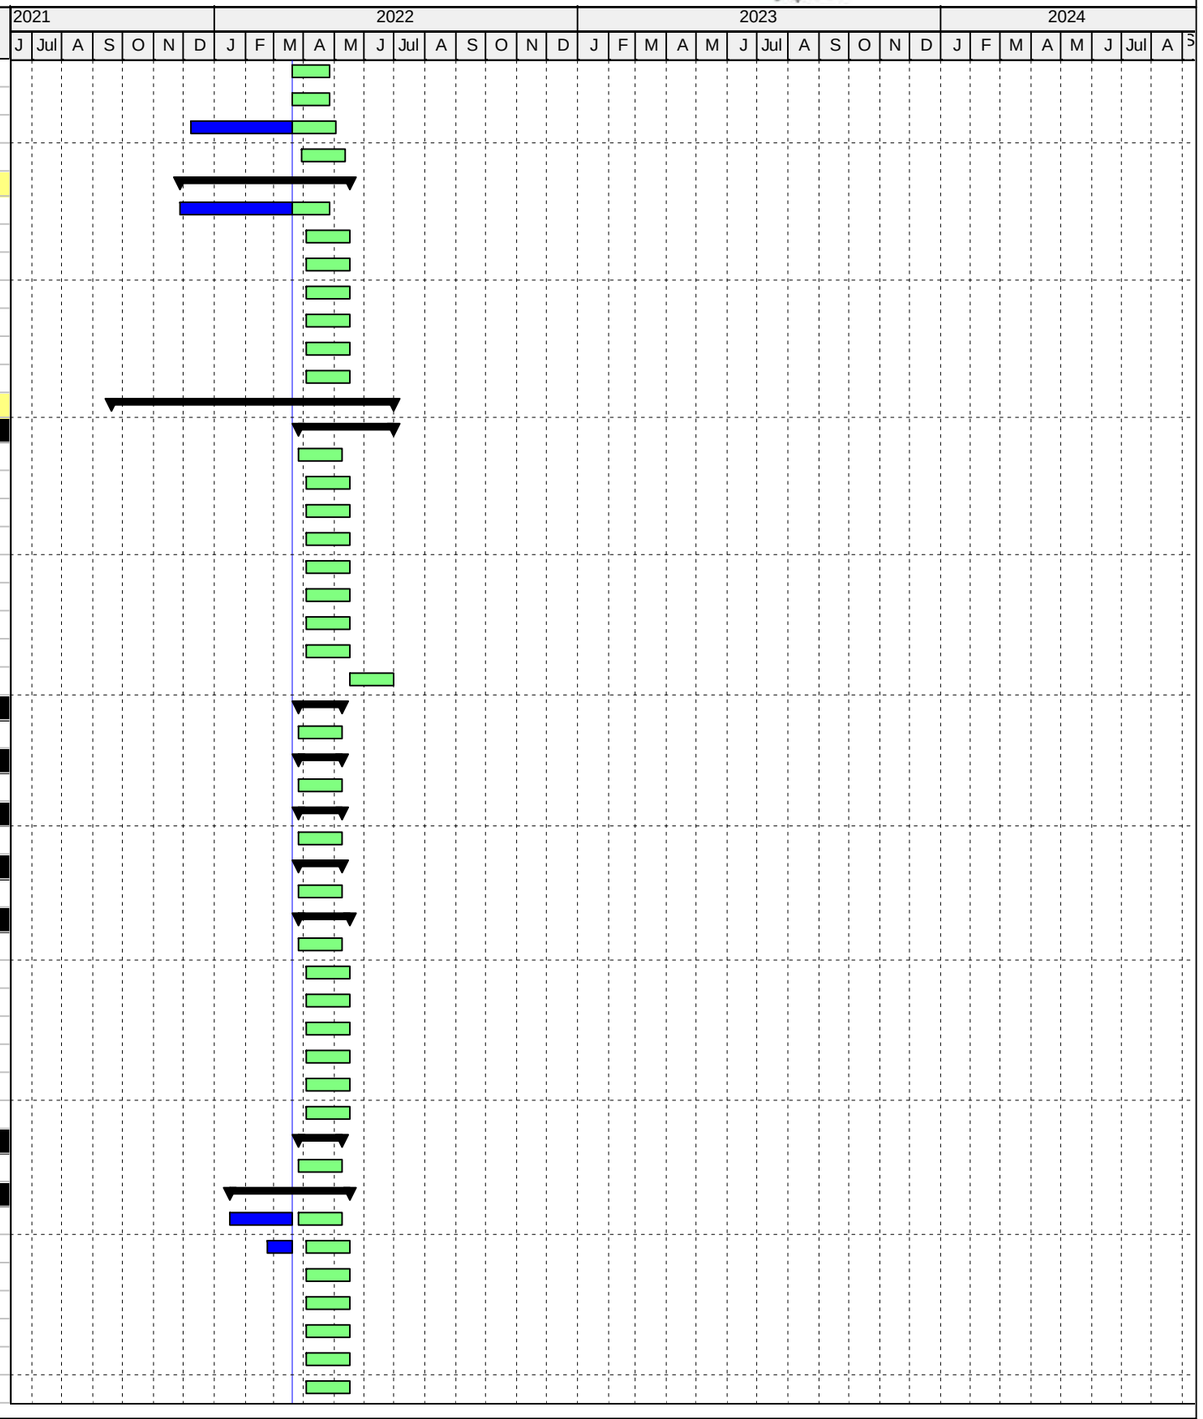

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Civil		44	100%	$75.47	20-Sep-21	27-Mar-22
P11	ITP For Civil Works	44	100%	$75.47	20-Sep-21	27-Mar-22
Electrical		44	0%	$75.47	27-Mar-22	09-May-22
P11	ITP For Electrical Installation	44	0%	$75.47	27-Mar-22	09-May-22
Procurement Engineering		412	1.45%	$14,604.10	06-Dec-21	10-Jun-23
Mechanical		222	10%	$1,533.43	16-Feb-22	15-Oct-22
Pig Traps		222	10%	$1,533.43	16-Feb-22	15-Oct-22
P11-E	PMR For Pig Traps	12	100%	$153.34	16-Feb-22	23-May-22
P11-E	TBE For Pig Traps	45	0%	$230.01	23-May-22	06-Jul-22
P11-E	VDR For Pig Traps	7	0%	$1,150.07	09-Oct-22	15-Oct-22
Piping		202	0%	$1,022.29	21-Nov-22	10-Jun-23
Pipes		99	0%	$143.12	16-Jan-23	24-Apr-23
P11-E	PMR For Pipes	10	0%	$14.31	16-Jan-23	25-Jan-23
P11-E	TBE For Pipes	45	0%	$21.47	23-Jan-23	08-Mar-23
P11-E	VDR For Pipes	7	0%	$107.34	18-Apr-23	24-Apr-23
Fittings		99	0%	$40.89	16-Jan-23	24-Apr-23
P11-E	PMR For Fittings	10	0%	$4.09	16-Jan-23	25-Jan-23
P11-E	TBE For Fitting	45	0%	$6.13	23-Jan-23	08-Mar-23
P11-E	VDR For Fitting	7	0%	$30.67	18-Apr-23	24-Apr-23
Flanges		99	0%	$40.89	16-Jan-23	24-Apr-23
P11-E	PMR For Flanges	10	0%	$4.09	16-Jan-23	25-Jan-23
P11-E	TBE For Flanges	45	0%	$6.13	23-Jan-23	08-Mar-23
P11-E	VDR For Flanges	7	0%	$30.67	18-Apr-23	24-Apr-23
Manual Valves		99	0%	$245.35	16-Jan-23	24-Apr-23
P11-E	PMR For Manual Valves	10	0%	$24.53	16-Jan-23	25-Jan-23
P11-E	TBE For Manual Valves	45	0%	$36.80	23-Jan-23	08-Mar-23
P11-E	VDR For Manual Valves	7	0%	$184.01	18-Apr-23	24-Apr-23
Gaskets		99	0%	$102.23	16-Jan-23	24-Apr-23
P11-E	PMR For Gaskets	10	0%	$10.22	16-Jan-23	25-Jan-23
P11-E	TBE For Gaskets	45	0%	$15.33	23-Jan-23	08-Mar-23
P11-E	VDR For Gaskets	7	0%	$76.67	18-Apr-23	24-Apr-23
Bolt & Nuts		67	0%	$122.67	16-Jan-23	23-Mar-23
P11-E	PMR For Bolt/Nuts	10	0%	$12.27	16-Jan-23	25-Jan-23
P11-E	PMR For Bolt/Nuts	10	0%	$18.40	26-Jan-23	04-Feb-23
P11-E	VDR For Bolt/Nuts	7	0%	$92.01	17-Mar-23	23-Mar-23
Insulation		99	0%	$81.78	16-Jan-23	24-Apr-23
P11-E	PMR For Insulation	10	0%	$8.18	16-Jan-23	25-Jan-23
P11-E	TBE For Insulation	45	0%	$12.27	23-Jan-23	08-Mar-23
P11-E	VDR For Insulation	7	0%	$61.34	18-Apr-23	24-Apr-23
Insulation Joints		94	0%	$81.78	21-Nov-22	22-Feb-23
P11-E	PMR For Insulation Joints	10	0%	$8.18	21-Nov-22	30-Nov-22
P11-E	TBE For Insulation Joints	45	0%	$12.27	28-Nov-22	11-Jan-23
P11-E	VDR For Insulation Joints	7	0%	$61.34	16-Feb-23	22-Feb-23
Painting		146	0%	$61.34	16-Jan-23	10-Jun-23
P11-E	PMR For Painting	10	0%	$6.13	16-Jan-23	25-Jan-23
P11-E	TBE For Painting	45	0%	$9.20	23-Jan-23	08-Mar-23
P11-E	VDR For Painting	7	0%	$46.00	04-Jun-23	10-Jun-23
Coating of Underground Piping		57	0%	$102.23	22-Feb-23	19-Apr-23
P11-E	PMR For Coating of Underground Piping	10	0%	$10.22	22-Feb-23	03-Mar-23
P11-E	TBE For Coating of Underground Piping	45	0%	$15.33	01-Mar-23	14-Apr-23




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-E	VDR For Coating of Underground Piping	5	0%	$76.67	15-Apr-23	19-Apr-23
Pipeline		352	2%	$2,909.14	06-Dec-21	28-Mar-23
Line Pipe		313	10%	$581.83	06-Dec-21	04-Nov-22
P11-E	PMR For Line Pipe	10	100%	$58.18	06-Dec-21	26-Jul-22
P11-E	TBE For Line Pipe	45	0%	$87.27	26-Jul-22	08-Sep-22
P11-E	VDR For Line Pipe	7	0%	$436.37	29-Oct-22	04-Nov-22
Insulation Joints		109	0%	$581.83	10-Dec-22	28-Mar-23
P11-E	PMR For Line Insulation Joints	10	0%	$58.18	10-Dec-22	19-Dec-22
P11-E	TBE For Line Insulation Joints	45	0%	$87.27	17-Dec-22	30-Jan-23
P11-E	VDR For Line Insulation Joints	7	0%	$436.37	22-Mar-23	28-Mar-23
Anchor Flanges		97	0%	$581.83	30-Nov-22	06-Mar-23
P11-E	PMR For Anchor Flanges	10	0%	$58.18	30-Nov-22	09-Dec-22
P11-E	TBE For Anchor Flanges	45	0%	$87.27	10-Dec-22	23-Jan-23
P11-E	VDR For Anchor Flanges	7	0%	$436.37	28-Feb-23	06-Mar-23
Pipeline Flange, Fittings, Gasket and Bolt		109	0%	$581.83	23-Nov-22	11-Mar-23
P11-E	PMR For Pipeline Flange, Fittings, Gasket and Bolt	10	0%	$58.18	23-Nov-22	02-Dec-22
P11-E	TBE For Pipeline Flange, Fittings, Gasket and Bolt	45	0%	$87.27	30-Nov-22	13-Jan-23
P11-E	VDR For Pipeline Flange, Fittings, Gasket and Bolt	7	0%	$436.37	05-Mar-23	11-Mar-23
Pipeline Rock Shield		59	0%	$581.83	17-Jun-22	14-Aug-22
P11-E	PMR For Pipeline Rock Shield	10	0%	$58.18	17-Jun-22	26-Jun-22
P11-E	TBE For Pipeline Rock Shield	45	0%	$87.27	24-Jun-22	07-Aug-22
P11-E	VDR For Pipeline Rock Shield	7	0%	$436.37	08-Aug-22	14-Aug-22
Control & Instrumentation		321	0%	$6,872.69	25-Apr-22	11-Mar-23
Control System/Console/Furniture		69	0%	$529.20	27-Jul-22	03-Oct-22
P11-E	PMR For Control System/Console/Furniture	10	0%	$52.92	27-Jul-22	05-Aug-22
P11-E	TBE For Control System/Console/Furniture	45	0%	$79.38	03-Aug-22	16-Sep-22
P11-E	VDR For Control System/Console/Furniture	7	0%	$396.90	27-Sep-22	03-Oct-22
ESD System		69	0%	$525.07	27-Jul-22	03-Oct-22
P11-E	PMR For ESD System	10	0%	$52.51	27-Jul-22	05-Aug-22
P11-E	TBE For ESD System	45	0%	$78.76	03-Aug-22	16-Sep-22
P11-E	VDR For ESD System	7	0%	$393.81	27-Sep-22	03-Oct-22
Instrument Junction box and Gland		139	0%	$406.86	23-Oct-22	10-Mar-23
P11-E	PMR For Instrument and F&G Junction box and Gland	10	0%	$40.69	23-Oct-22	01-Nov-22
P11-E	TBE For Instrument and F&G Junction box and Gland	45	0%	$61.03	30-Oct-22	13-Dec-22
P11-E	VDR For Instrument and F&G Junction box and Gland	7	0%	$305.15	04-Mar-23	10-Mar-23
Instrument Tube and Fitting		107	0%	$406.86	03-Aug-22	17-Nov-22
P11-E	PMR For Instrument Tube and Fitting	10	0%	$40.69	03-Aug-22	12-Aug-22
P11-E	TBE For Instrument Tube and Fitting	45	0%	$61.03	10-Aug-22	23-Sep-22
P11-E	VDR For Instrument Tube and Fitting	5	0%	$305.15	13-Nov-22	17-Nov-22
Instrument Cable		107	0%	$406.86	26-Oct-22	09-Feb-23
P11-E	PMR For Instrument and F&G Cable	10	0%	$40.69	26-Oct-22	04-Nov-22
P11-E	TBE For Instrument and F&G Cable	45	0%	$61.03	02-Nov-22	16-Dec-22
P11-E	VDR For Instrument and F&G Cable	5	0%	$305.15	05-Feb-23	09-Feb-23
Corrosion Probe/Coupon		109	0%	$406.86	17-Jun-22	03-Oct-22
P11-E	PMR For Corrosion Probe/Coupon	10	0%	$40.69	17-Jun-22	26-Jun-22
P11-E	TBE For Corrosion Probe/Coupon	45	0%	$61.03	24-Jun-22	07-Aug-22
P11-E	VDR For Corrosion Probe/Coupon	7	0%	$305.15	27-Sep-22	03-Oct-22
ON/OFF & Shutdown Valves		119	0%	$406.86	26-Jul-22	21-Nov-22
P11-E	PMR For ON/OFF & Shutdown Valves	10	0%	$40.69	26-Jul-22	04-Aug-22

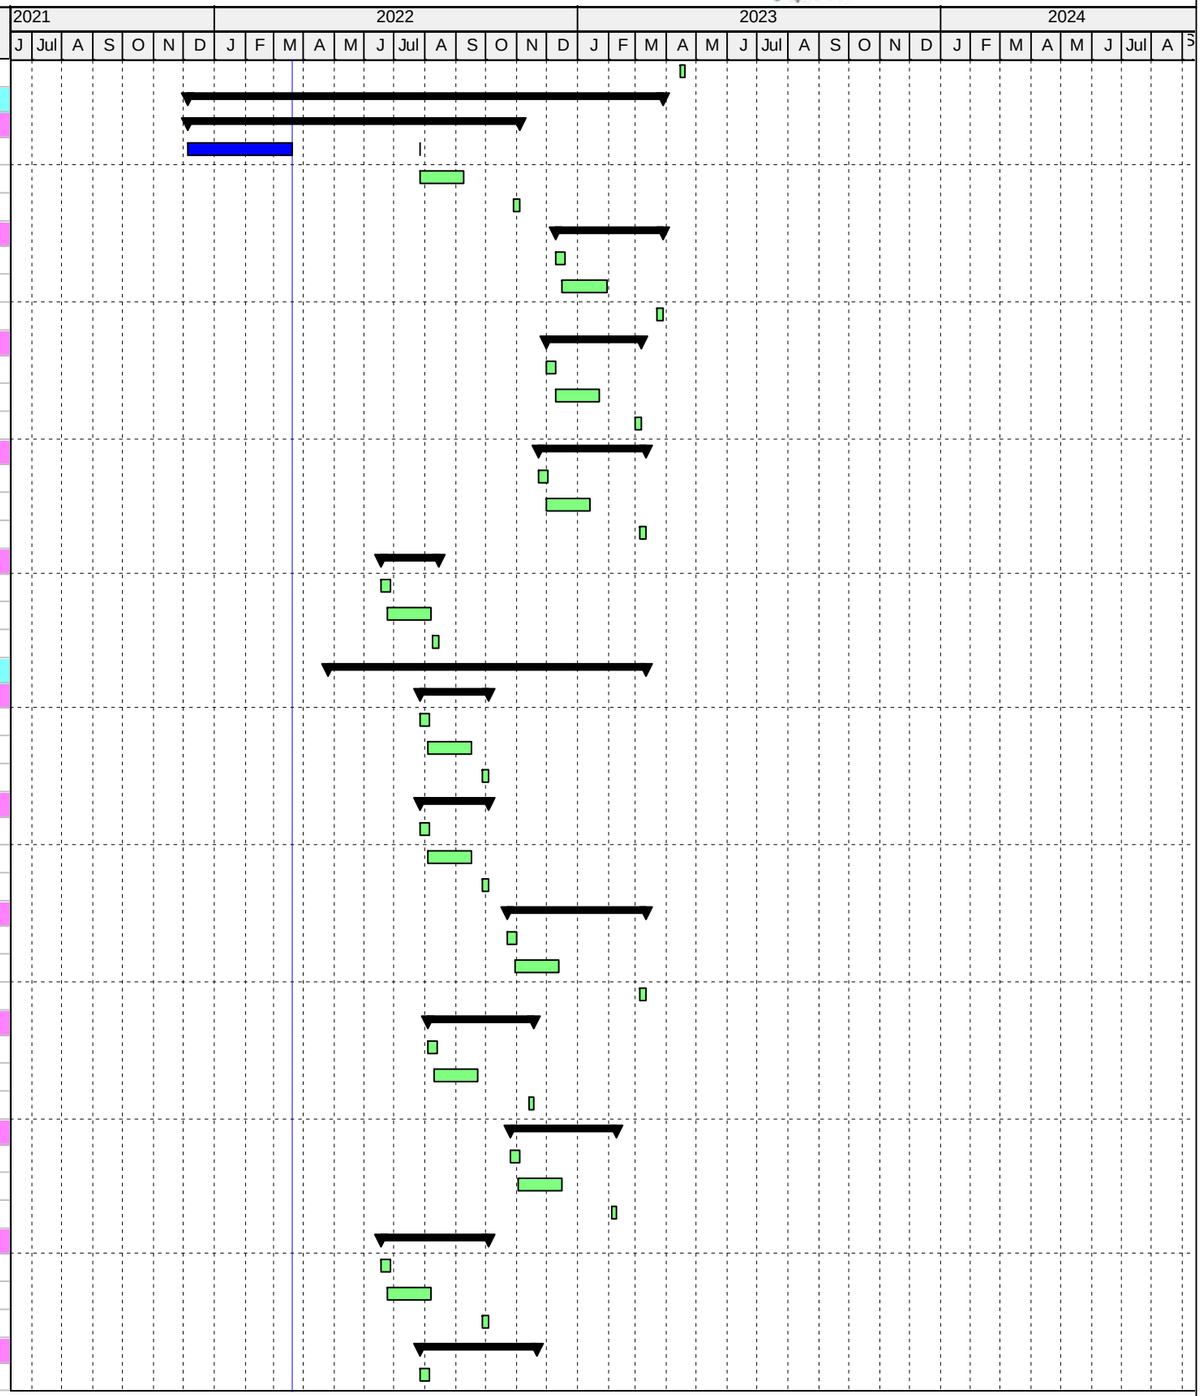


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-E	TBE For ON/OFF & Shutdown Valves	45	0%	$61.03	02-Aug-22	15-Sep-22
P11-E	VDR For ON/OFF & Shutdown Valves	7	0%	$305.15	15-Nov-22	21-Nov-22
Pressure Safety Valves (PSV)		119	0%	$406.86	26-Jul-22	21-Nov-22
P11-E	PMR For Pressure Safety Valves (PSV)	10	0%	$40.69	26-Jul-22	04-Aug-22
P11-E	TBE For Pressure Safety Valves (PSV)	45	0%	$61.03	02-Aug-22	15-Sep-22
P11-E	VDR For Pressure Safety Valves (PSV)	7	0%	$305.15	15-Nov-22	21-Nov-22
Differential Pressure/Pressure Gauge		109	0%	$406.86	30-Apr-22	16-Aug-22
P11-E	PMR For Differential Pressure/Pressure Gauge	10	0%	$40.69	30-Apr-22	09-May-22
P11-E	TBE For Differential Pressure/Pressure Gauge	45	0%	$61.03	07-May-22	20-Jun-22
P11-E	VDR For Differential Pressure/Pressure Gauge	7	0%	$305.15	10-Aug-22	16-Aug-22
Pressure/Diff. Pressure Transmitter		109	0%	$406.86	30-Apr-22	16-Aug-22
P11-E	PMR For Pressure/Diff. Pressure Transmitter	10	0%	$40.69	30-Apr-22	09-May-22
P11-E	TBE For Pressure/Diff. Pressure Transmitter	45	0%	$61.03	07-May-22	20-Jun-22
P11-E	VDR For Pressure/Diff. Pressure Transmitter	7	0%	$305.15	10-Aug-22	16-Aug-22
Temperature Gauge		112	0%	$406.86	09-Aug-22	28-Nov-22
P11-E	PMR For Temperature Gauge	10	0%	$40.69	09-Aug-22	18-Aug-22
P11-E	TBE For Temperature Gauge	45	0%	$61.03	19-Aug-22	02-Oct-22
P11-E	VDR For Temperature Gauge	7	0%	$305.15	22-Nov-22	28-Nov-22
Pig Signaler		109	0%	$406.86	23-May-22	08-Sep-22
P11-E	PMR For Pig Signaler	10	0%	$40.69	23-May-22	01-Jun-22
P11-E	TBE For Pig Signaler	45	0%	$61.03	30-May-22	13-Jul-22
P11-E	VDR For Pig Signaler	7	0%	$305.15	02-Sep-22	08-Sep-22
Instrument Installation Accessories		109	0%	$406.86	01-May-22	17-Aug-22
P11-E	PMR For Instrument Installation Accessories	10	0%	$40.69	01-May-22	10-May-22
P11-E	TBE For Instrument Installation Accessories	45	0%	$61.03	08-May-22	21-Jun-22
P11-E	VDR For Instrument Installation Accessories	7	0%	$305.15	11-Aug-22	17-Aug-22
Instrument Cable Tray		109	0%	$406.86	23-Nov-22	11-Mar-23
P11-E	PMR For Instrument Cable Tray	10	0%	$40.69	23-Nov-22	02-Dec-22
P11-E	TBE For Instrument Cable Tray	45	0%	$61.03	30-Nov-22	13-Jan-23
P11-E	VDR For Instrument Cable Tray	7	0%	$305.15	05-Mar-23	11-Mar-23
F&G Devices		87	0%	$406.86	10-Jul-22	04-Oct-22
P11-E	PMR For F&G Devices	20	0%	$40.69	10-Jul-22	29-Jul-22
P11-E	TBE For F&G Devices	7	0%	$61.03	17-Jul-22	23-Jul-22
P11-E	VDR For F&G Devices	7	0%	$305.15	28-Sep-22	04-Oct-22
LBV		101	0%	$529.20	25-Apr-22	03-Aug-22
P11-E	PMR For LBV	3	0%	$52.92	25-Apr-22	27-Apr-22
P11-E	TBE For LBV	7	0%	$79.38	02-May-22	08-May-22
P11-E	VDR For LBV	7	0%	$396.90	28-Jul-22	03-Aug-22
Electrical		154	0%	$1,873.71	11-Aug-22	11-Jan-23
Expansion Of LV Switchgear		139	0%	$416.34	11-Aug-22	27-Dec-22
P11-E	PMR For Expansion Of LV Switchgear in Siahmakan Gas Inje	10	0%	$41.63	11-Aug-22	20-Aug-22
P11-E	TBE For Expansion Of LV Switchgear in Siahmakan Gas Injec	45	0%	$62.45	18-Aug-22	01-Oct-22
P11-E	VDR For Expansion Of LV Switchgear in Siahmakan Gas Inje	7	0%	$312.25	21-Dec-22	27-Dec-22
Power & Control Cables		109	0%	$416.34	26-Aug-22	12-Dec-22
P11-E	PMR For Power & Control Cables in Siahmakan Gas Injectior	10	0%	$41.63	26-Aug-22	04-Sep-22
P11-E	TBE For Power & Control Cables in Siahmakan Gas Injection	45	0%	$62.45	02-Sep-22	16-Oct-22
P11-E	VDR For Power & Control Cables in Siahmakan Gas Injection	7	0%	$312.25	06-Dec-22	12-Dec-22
Cathodic Protection System		139	0%	$624.69	26-Aug-22	11-Jan-23
P11-E	PMR For Cathodic Protection System	10	0%	$62.47	26-Aug-22	04-Sep-22

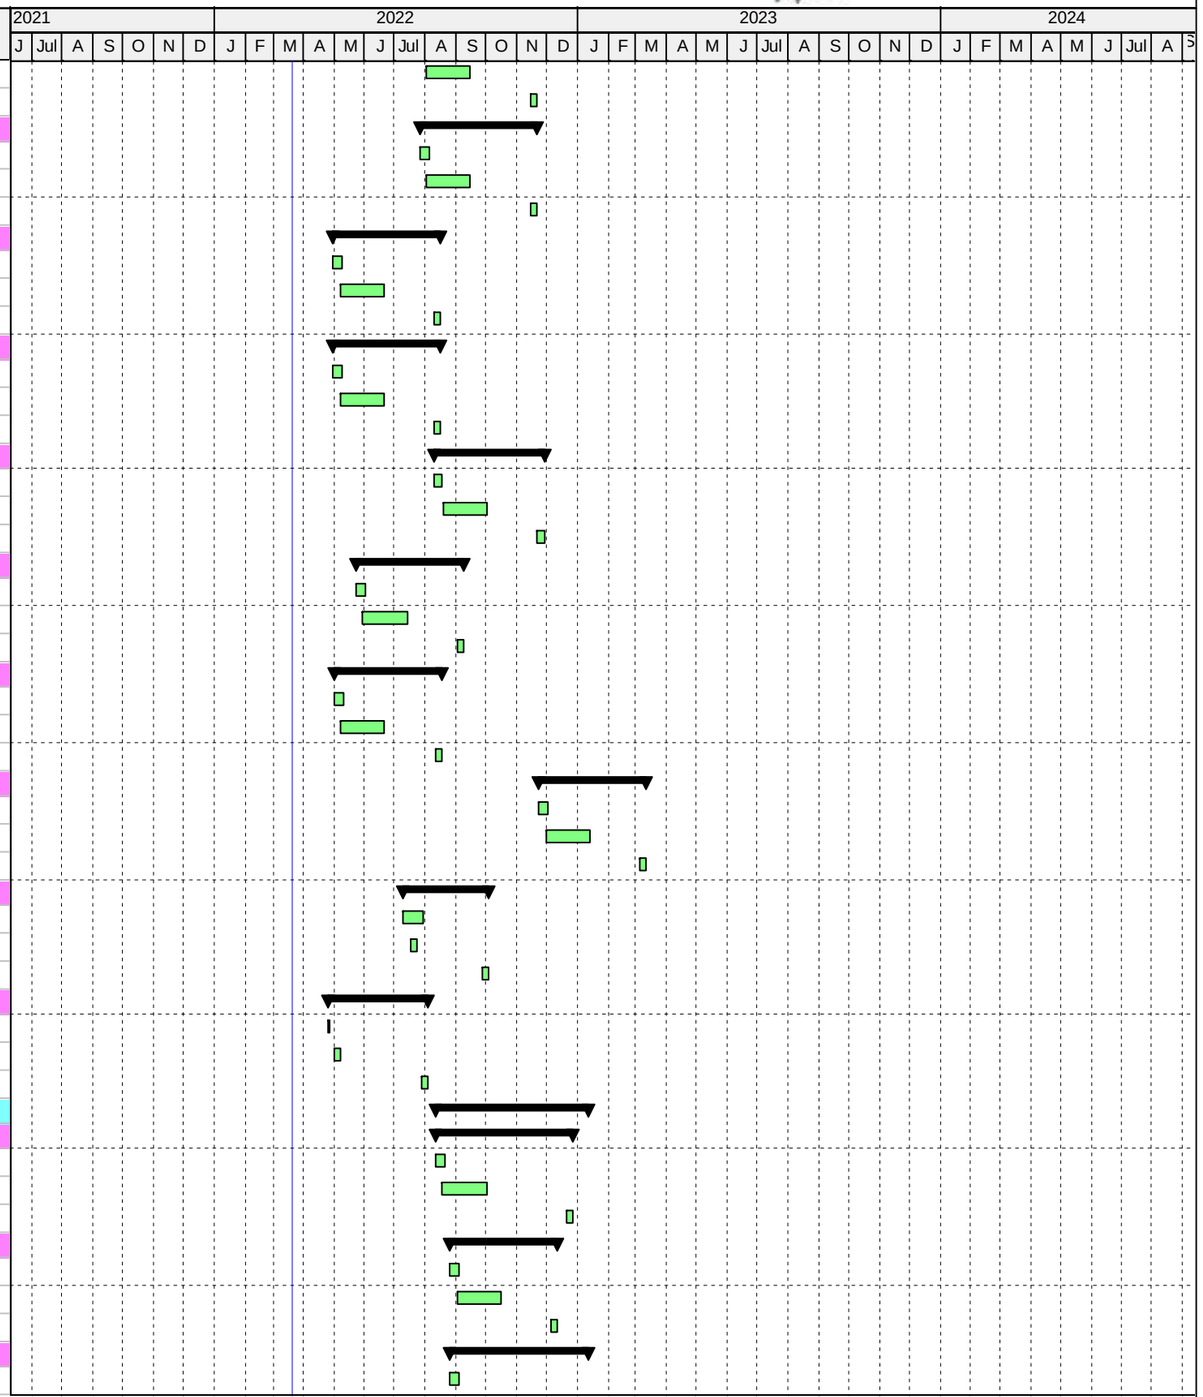

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-E	TBE For Cathodic Protection System	45	0%	$93.70	02-Sep-22	16-Oct-22
P11-E	VDR For Cathodic Protection System	7	0%	$468.52	05-Jan-23	11-Jan-23
Electrical Bulk Items & Earthing & Lighting		109	0%	$416.34	26-Aug-22	12-Dec-22
P11-E	PMR For Bulk Items, Earthing & Lighting in Siahmakan Gas Ir	10	0%	$41.63	26-Aug-22	04-Sep-22
P11-E	TBE For Bulk Items, Earthing & Lighting in Siahmakan Gas In	45	0%	$62.45	02-Sep-22	16-Oct-22
P11-E	VDR For Bulk Items, Earthing & Lighting in Siahmakan Gas Ir	7	0%	$312.25	06-Dec-22	12-Dec-22
Safety & Fire Fighting		269	0%	$392.85	15-May-22	07-Feb-23
Safety Signs		109	0%	$105.40	15-May-22	31-Aug-22
P11-E	PMR For Safety Signs	10	0%	$10.54	15-May-22	24-May-22
P11-E	TBE For Safety Signs	45	0%	$15.81	22-May-22	05-Jul-22
P11-E	VDR For Safety Signs	7	0%	$79.05	25-Aug-22	31-Aug-22
Fire Fighting Equipment		109	0%	$143.70	15-Sep-22	01-Jan-23
P11-E	PMR For Fire Fighting Equipment	10	0%	$14.37	15-Sep-22	24-Sep-22
P11-E	TBE For Fire Fighting Equipment	45	0%	$21.56	22-Sep-22	05-Nov-22
P11-E	VDR For Fire Fighting Equipment	7	0%	$107.78	26-Dec-22	01-Jan-23
Safety Equipment		109	0%	$143.74	22-Oct-22	07-Feb-23
P11-E	PMR For Safety Equipment	10	0%	$14.37	22-Oct-22	31-Oct-22
P11-E	TBE For Safety Equipment	45	0%	$21.56	29-Oct-22	12-Dec-22
P11-E	VDR For Safety Equipment	7	0%	$107.81	01-Feb-23	07-Feb-23
Commissioning Engineering		569	0%	$2,920.82	20-Mar-22	09-Oct-23
P11-EP(	Operability Review	5	0%	$584.16	03-May-22	07-May-22
P11-EP(	Pre-Commissioning, Commissioning & Startup Procedure	44	0%	$1,752.49	20-Mar-22	02-May-22
P11-EP(	Operating Manual	30	0%	$584.16	10-Sep-23	09-Oct-23
Field Engineering		419	0%	$21,906.15	17-Sep-22	09-Nov-23
P11-EP(	Technical/Site Queries	44	0%	$10,953.08	17-Sep-22	30-Oct-22
P11-EP(	As-Built Document Booklets	10	0%	$10,953.08	31-Oct-23	09-Nov-23
Engineering Final Documentation		44	0%	$14,604.10	10-Nov-23	23-Dec-23
P11-EP(	Final Engineering Dossier	44	0%	$14,604.10	10-Nov-23	23-Dec-23
PROCUREMENT		489	0%	$3,919,957.01	09-May-22	09-Sep-23
Main Procurement		464	0%	$3,135,965.60	09-May-22	15-Aug-23
Mechanical		244	0%	$169,969.34	07-Jul-22	07-Mar-23
Pig Launcher/ Reciever (PL/PR-1001)		244	0%	$169,969.34	07-Jul-22	07-Mar-23
P11-E	Tendering & Selection	45	0%	$6,798.77	07-Jul-22	20-Aug-22
P11-E	Contract Effectiveness / PO	30	0%	$10,198.16	09-Sep-22	08-Oct-22
P11-E	Manufacturing / Fabrication / Supply	150	0%	$152,972.40	09-Oct-22	07-Mar-23
Piping		216	0%	$95,646.95	12-Jan-23	15-Aug-23
Pipes		160	0%	$50,367.68	09-Mar-23	15-Aug-23
P11-E	Tendering & Selection	20	0%	$2,014.71	09-Mar-23	28-Mar-23
P11-E	Contract Effectiveness / PO	20	0%	$3,022.06	29-Mar-23	17-Apr-23
P11-E	Manufacturing / Fabrication / Supply	120	0%	$45,330.92	18-Apr-23	15-Aug-23
Fittings		150	0%	$6,838.76	09-Mar-23	05-Aug-23
P11-E	Tendering & Selection	30	0%	$273.55	09-Mar-23	07-Apr-23
P11-E	Contract Effectiveness / PO	20	0%	$410.33	08-Apr-23	27-Apr-23
P11-E	Manufacturing / Fabrication / Supply	100	0%	$6,154.88	28-Apr-23	05-Aug-23
Flanges		150	0%	$3,950.22	09-Mar-23	05-Aug-23
P11-E	Tendering & Selection	30	0%	$158.01	09-Mar-23	07-Apr-23
P11-E	Contract Effectiveness / PO	20	0%	$237.01	08-Apr-23	27-Apr-23
P11-E	Manufacturing / Fabrication / Supply	100	0%	$3,555.20	28-Apr-23	05-Aug-23
Manual Valves		150	0%	$32,261.72	09-Mar-23	05-Aug-23
P11-E	Tendering & Selection	30	0%	$1,290.47	09-Mar-23	07-Apr-23




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-E	Contract Effectiveness / PO	20	0%	$1,935.70	08-Apr-23	27-Apr-23
P11-E	Manufacturing / Fabrication / Supply	100	0%	$29,035.54	28-Apr-23	05-Aug-23
Gaskets		130	0%	$573.88	09-Mar-23	16-Jul-23
P11-E	Tendering & Selection	20	0%	$22.96	09-Mar-23	28-Mar-23
P11-E	Contract Effectiveness / PO	20	0%	$34.43	29-Mar-23	17-Apr-23
P11-E	Manufacturing / Fabrication / Supply	90	0%	$516.49	18-Apr-23	16-Jul-23
Bolt & Nuts		130	0%	$411.28	05-Feb-23	14-Jun-23
P11-E	Tendering & Selection	20	0%	$16.45	05-Feb-23	24-Feb-23
P11-E	Contract Effectiveness / PO	20	0%	$24.68	25-Feb-23	16-Mar-23
P11-E	Manufacturing / Fabrication / Supply	90	0%	$370.15	17-Mar-23	14-Jun-23
Insulating Joint		155	0%	$162.60	12-Jan-23	15-Jun-23
P11-E	Tendering & Selection	20	0%	$6.50	12-Jan-23	31-Jan-23
P11-E	Contract Effectiveness / PO	15	0%	$9.76	01-Feb-23	15-Feb-23
P11-E	Manufacturing / Fabrication / Supply	120	0%	$146.34	16-Feb-23	15-Jun-23
Insulation		130	0%	$334.76	09-Mar-23	16-Jul-23
P11-E	Tendering & Selection	20	0%	$13.39	09-Mar-23	28-Mar-23
P11-E	Contract Effectiveness / PO	20	0%	$20.09	29-Mar-23	17-Apr-23
P11-E	Manufacturing / Fabrication / Supply	90	0%	$301.29	18-Apr-23	16-Jul-23
Painting		120	0%	$411.28	09-Mar-23	06-Jul-23
P11-E	Tendering & Selection	30	0%	$16.45	09-Mar-23	07-Apr-23
P11-E	Contract Effectiveness / PO	20	0%	$24.68	08-Apr-23	27-Apr-23
P11-E	Manufacturing / Fabrication / Supply	70	0%	$370.15	28-Apr-23	06-Jul-23
Coating of Underground Piping		120	0%	$334.76	15-Apr-23	12-Aug-23
P11-E	Tendering & Selection	30	0%	$13.39	15-Apr-23	14-May-23
P11-E	Contract Effectiveness / PO	20	0%	$20.09	15-May-23	03-Jun-23
P11-E	Manufacturing / Fabrication / Supply	70	0%	$301.29	04-Jun-23	12-Aug-23
Pipeline		284	0%	$2,656,790.06	09-Sep-22	19-Jun-23
Line Pipe		200	0%	$2,497,382.66	09-Sep-22	27-Mar-23
8"-U/G Gas Pipeline		200	0%	$2,397,487.35	09-Sep-22	27-Mar-23
P11-I	Tendering & Selection	30	0%	$95,899.49	09-Sep-22	08-Oct-22
P11-I	Contract Effectiveness / PO	20	0%	$143,849.24	09-Oct-22	28-Oct-22
P11-I	Manufacturing / Fabrication / Supply	150	0%	$2,157,738.61	29-Oct-22	27-Mar-23
4"-A/G Condensate Pipeline		160	0%	$99,895.31	09-Sep-22	15-Feb-23
P11-I	Tendering & Selection	20	0%	$3,995.81	09-Sep-22	28-Sep-22
P11-I	Contract Effectiveness / PO	20	0%	$5,993.72	29-Sep-22	18-Oct-22
P11-I	Manufacturing / Fabrication / Supply	120	0%	$89,905.78	19-Oct-22	15-Feb-23
Insulation Joints		140	0%	$53,135.80	31-Jan-23	19-Jun-23
P11-E	Tendering & Selection	30	0%	$2,125.43	31-Jan-23	01-Mar-23
P11-E	Contract Effectiveness / PO	20	0%	$3,188.15	02-Mar-23	21-Mar-23
P11-E	Manufacturing / Fabrication / Supply	90	0%	$47,822.22	22-Mar-23	19-Jun-23
Anchor Flanges		125	0%	$53,135.80	24-Jan-23	28-May-23
P11-E	Tendering & Selection	20	0%	$2,125.43	24-Jan-23	12-Feb-23
P11-E	Contract Effectiveness / PO	15	0%	$3,188.15	13-Feb-23	27-Feb-23
P11-E	Manufacturing / Fabrication / Supply	90	0%	$47,822.22	28-Feb-23	28-May-23
Pipeline Material Flange, Fittings, Gasket and Bolt		140	0%	$53,135.80	14-Jan-23	02-Jun-23
P11-E	Tendering & Selection	30	0%	$2,125.43	14-Jan-23	12-Feb-23
P11-E	Contract Effectiveness / PO	20	0%	$3,188.15	13-Feb-23	04-Mar-23
P11-E	Manufacturing / Fabrication / Supply	90	0%	$47,822.22	05-Mar-23	02-Jun-23
Electrical		275	0%	$115,717.13	02-Oct-22	03-Jul-23
Expansion Of LV Switchgear		200	0%	$6,943.03	02-Oct-22	19-Apr-23

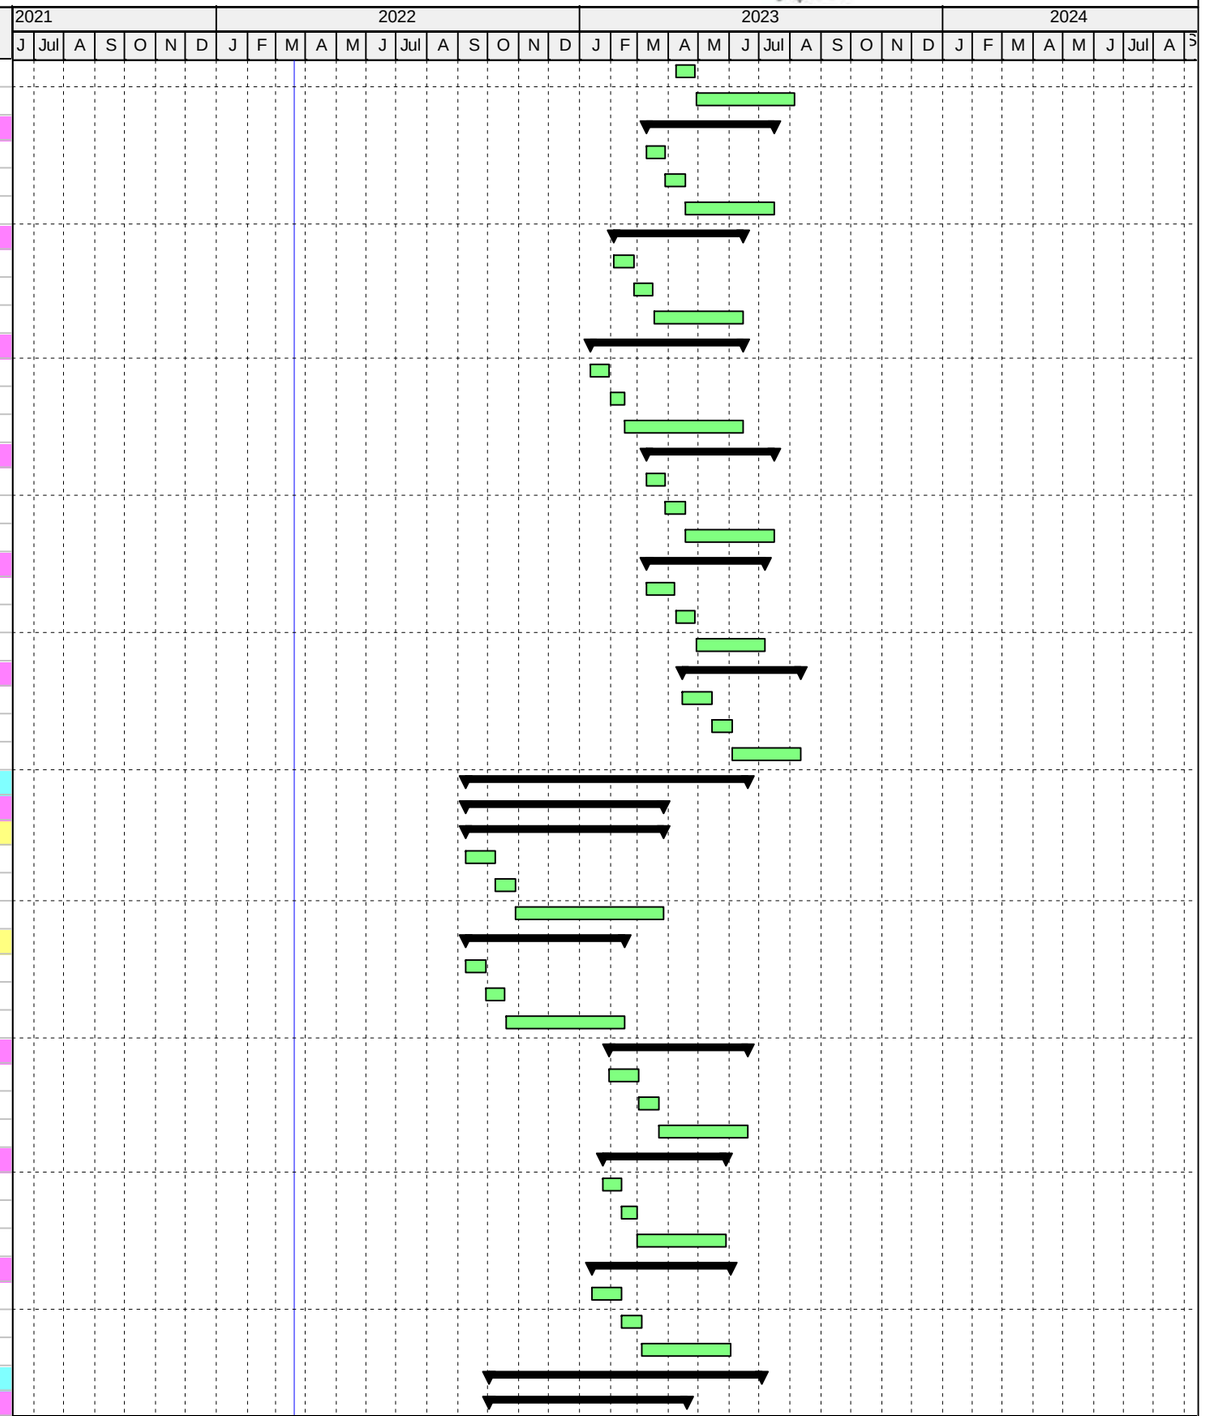

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-E	Tendering & Selection	50	0%	$277.72	02-Oct-22	20-Nov-22
P11-E	Contract Effectiveness / PO	30	0%	$416.58	21-Nov-22	20-Dec-22
P11-E	Manufacturing / Fabrication / Supply	120	0%	$6,248.73	21-Dec-22	19-Apr-23
Cable		215	0%	$20,829.08	17-Oct-22	19-May-23
P11-E	Tendering & Selection	30	0%	$833.16	17-Oct-22	15-Nov-22
P11-E	Contract Effectiveness / PO	20	0%	$1,249.75	16-Nov-22	05-Dec-22
P11-E	Manufacturing / Fabrication / Supply	165	0%	$18,746.18	06-Dec-22	19-May-23
Cathodic Protection System		260	0%	$83,316.33	17-Oct-22	03-Jul-23
P11-E	Tendering & Selection	60	0%	$3,332.65	17-Oct-22	15-Dec-22
P11-E	Contract Effectiveness / PO	20	0%	$4,998.98	16-Dec-22	04-Jan-23
P11-E	Manufacturing / Fabrication / Supply	180	0%	$74,984.70	05-Jan-23	03-Jul-23
Electrical Bulk Items & Earthing		140	0%	$4,628.69	17-Oct-22	05-Mar-23
P11-E	Tendering & Selection	30	0%	$185.15	17-Oct-22	15-Nov-22
P11-E	Contract Effectiveness / PO	20	0%	$277.72	16-Nov-22	05-Dec-22
P11-E	Manufacturing / Fabrication / Supply	90	0%	$4,165.82	06-Dec-22	05-Mar-23
Control & Instrumentation		422	0%	$94,392.56	09-May-22	04-Jul-23
Control System/Console/Furniture		230	0%	$10,571.97	17-Sep-22	04-May-23
P11-E	Tendering & Selection	60	0%	$422.88	17-Sep-22	15-Nov-22
P11-E	Contract Effectiveness / PO	30	0%	$634.32	16-Nov-22	15-Dec-22
P11-E	Manufacturing / Fabrication / Supply	140	0%	$9,514.77	16-Dec-22	04-May-23
ESD System		220	0%	$7,390.94	17-Sep-22	24-Apr-23
P11-E	Tendering & Selection	60	0%	$295.64	17-Sep-22	15-Nov-22
P11-E	Contract Effectiveness / PO	20	0%	$443.46	16-Nov-22	05-Dec-22
P11-E	Manufacturing / Fabrication / Supply	140	0%	$6,651.84	06-Dec-22	24-Apr-23
Corrosion Coupon/Probe		170	0%	$3,171.59	08-Aug-22	24-Jan-23
P11-E	Tendering & Selection	30	0%	$126.86	08-Aug-22	06-Sep-22
P11-E	Contract Effectiveness / PO	20	0%	$190.30	07-Sep-22	26-Sep-22
P11-E	Manufacturing / Fabrication / Supply	120	0%	$2,854.43	27-Sep-22	24-Jan-23
Pneumatic On/Off & Shutdown Valves		180	0%	$16,613.09	16-Sep-22	14-Mar-23
P11-E	Tendering & Selection	30	0%	$664.52	16-Sep-22	15-Oct-22
P11-E	Contract Effectiveness / PO	30	0%	$996.79	16-Oct-22	14-Nov-22
P11-E	Manufacturing / Fabrication / Supply	120	0%	$14,951.78	15-Nov-22	14-Mar-23
Pressure Safety Valves (PSV)		210	0%	$5,370.94	16-Sep-22	13-Apr-23
P11-E	Tendering & Selection	30	0%	$214.84	16-Sep-22	15-Oct-22
P11-E	Contract Effectiveness / PO	30	0%	$322.26	16-Oct-22	14-Nov-22
P11-E	Manufacturing / Fabrication / Supply	150	0%	$4,833.84	15-Nov-22	13-Apr-23
Differential Pressure/Pressure Gauge		230	0%	$575.79	21-Jun-22	05-Feb-23
P11-E	Tendering & Selection	30	0%	$23.03	21-Jun-22	20-Jul-22
P11-E	Contract Effectiveness / PO	20	0%	$34.55	21-Jul-22	09-Aug-22
P11-E	Manufacturing / Fabrication / Supply	180	0%	$518.22	10-Aug-22	05-Feb-23
Pressure/Diff. Pressure Transmitter		200	0%	$887.29	21-Jun-22	06-Jan-23
P11-E	Tendering & Selection	30	0%	$35.49	21-Jun-22	20-Jul-22
P11-E	Contract Effectiveness / PO	20	0%	$53.24	21-Jul-22	09-Aug-22
P11-E	Manufacturing / Fabrication / Supply	150	0%	$798.56	10-Aug-22	06-Jan-23
Temperature Gauge		170	0%	$528.60	03-Oct-22	21-Mar-23
P11-E	Tendering & Selection	30	0%	$21.14	03-Oct-22	01-Nov-22
P11-E	Contract Effectiveness / PO	20	0%	$31.72	02-Nov-22	21-Nov-22
P11-E	Manufacturing / Fabrication / Supply	120	0%	$475.74	22-Nov-22	21-Mar-23
Pig Signaler		170	0%	$2,218.23	14-Jul-22	30-Dec-22



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-E	Tendering & Selection	30	0%	$88.73	14-Jul-22	12-Aug-22
P11-E	Contract Effectiveness / PO	20	0%	$133.09	13-Aug-22	01-Sep-22
P11-E	Manufacturing / Fabrication / Supply	120	0%	$1,996.40	02-Sep-22	30-Dec-22
Instrument Installation Accessories		110	0%	$7,372.06	22-Jun-22	09-Oct-22
P11-E	Tendering & Selection	30	0%	$294.88	22-Jun-22	21-Jul-22
P11-E	Contract Effectiveness / PO	20	0%	$442.32	22-Jul-22	10-Aug-22
P11-E	Manufacturing / Fabrication / Supply	60	0%	$6,634.85	11-Aug-22	09-Oct-22
Instrument Cable Tray/Ladder		170	0%	$6,909.54	14-Jan-23	02-Jul-23
P11-E	Tendering & Selection	30	0%	$276.38	14-Jan-23	12-Feb-23
P11-E	Contract Effectiveness / PO	20	0%	$414.57	13-Feb-23	04-Mar-23
P11-E	Manufacturing / Fabrication / Supply	120	0%	$6,218.58	05-Mar-23	02-Jul-23
Instrument/F&G Junction box and Gland		200	0%	$6,248.79	14-Dec-22	01-Jul-23
P11-E	Tendering & Selection	60	0%	$249.95	14-Dec-22	11-Feb-23
P11-E	Contract Effectiveness / PO	20	0%	$374.93	12-Feb-23	03-Mar-23
P11-E	Manufacturing / Fabrication / Supply	120	0%	$5,623.91	04-Mar-23	01-Jul-23
Instrument Tube and Fitting		125	0%	$4,530.84	24-Sep-22	26-Jan-23
P11-E	Tendering & Selection	30	0%	$181.23	24-Sep-22	23-Oct-22
P11-E	Contract Effectiveness / PO	20	0%	$271.85	24-Oct-22	12-Nov-22
P11-E	Manufacturing / Fabrication / Supply	75	0%	$4,077.76	13-Nov-22	26-Jan-23
F&G Devices		240	0%	$7,381.50	30-Jul-22	26-Mar-23
P11-E	Tendering & Selection	30	0%	$295.26	30-Jul-22	28-Aug-22
P11-E	Contract Effectiveness / PO	30	0%	$442.89	29-Aug-22	27-Sep-22
P11-E	Manufacturing / Fabrication / Supply	180	0%	$6,643.35	28-Sep-22	26-Mar-23
LBV		260	0%	$11,978.42	09-May-22	23-Jan-23
P11-E	Tendering & Selection	60	0%	$479.14	09-May-22	07-Jul-22
P11-E	Contract Effectiveness / PO	20	0%	$718.70	08-Jul-22	27-Jul-22
P11-E	Manufacturing / Fabrication / Supply	180	0%	$10,780.57	28-Jul-22	23-Jan-23
Instrument Cable		200	0%	$2,642.99	17-Dec-22	04-Jul-23
P11-E	Tendering & Selection	30	0%	$105.72	17-Dec-22	15-Jan-23
P11-E	Contract Effectiveness / PO	20	0%	$158.58	16-Jan-23	04-Feb-23
P11-E	Manufacturing / Fabrication / Supply	150	0%	$2,378.69	05-Feb-23	04-Jul-23
Safety		230	0%	$3,449.56	06-Jul-22	20-Feb-23
Safety Equipment		70	0%	$1,379.82	13-Dec-22	20-Feb-23
P11-E	Tendering & Selection	30	0%	$55.19	13-Dec-22	11-Jan-23
P11-E	Contract Effectiveness / PO	20	0%	$82.79	12-Jan-23	31-Jan-23
P11-E	Manufacturing / Fabrication / Supply	20	0%	$1,241.84	01-Feb-23	20-Feb-23
Fire Fighting Equipment		70	0%	$1,379.82	06-Nov-22	14-Jan-23
P11-E	Tendering & Selection	30	0%	$55.19	06-Nov-22	05-Dec-22
P11-E	Contract Effectiveness / PO	20	0%	$82.79	06-Dec-22	25-Dec-22
P11-E	Manufacturing / Fabrication / Supply	20	0%	$1,241.84	26-Dec-22	14-Jan-23
Safety Signs		70	0%	$689.91	06-Jul-22	13-Sep-22
P11-E	Tendering & Selection	30	0%	$27.60	06-Jul-22	04-Aug-22
P11-E	Contract Effectiveness / PO	20	0%	$41.39	05-Aug-22	24-Aug-22
P11-E	Manufacturing / Fabrication / Supply	20	0%	$620.92	25-Aug-22	13-Sep-22
Customs Clearance & Delivery To Site		346	0%	$391,995.70	14-Sep-22	25-Aug-23
Mechanical		10	0%	$21,246.17	08-Mar-23	17-Mar-23
P11-EF	Pig Traps	10	0%	$21,246.17	08-Mar-23	17-Mar-23
Piping (Pipes ,Manual Valves, Gaskets,Strainers, Bolt & Nuts, Fitti		72	0%	$11,955.87	15-Jun-23	25-Aug-23
P11-EF	Pipes	10	0%	$6,295.96	16-Aug-23	25-Aug-23




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-EF	Fittings	10	0%	$854.84	06-Aug-23	15-Aug-23
P11-EF	Flanges	10	0%	$493.78	06-Aug-23	15-Aug-23
P11-EF	Manual Valves	10	0%	$4,032.71	06-Aug-23	15-Aug-23
P11-EF	Gaskets	10	0%	$71.74	17-Jul-23	26-Jul-23
P11-EF	Bolt & Nuts	10	0%	$51.41	15-Jun-23	24-Jun-23
P11-EF	Insulation kits	10	0%	$20.32	16-Jun-23	25-Jun-23
P11-EF	Insulation	5	0%	$41.85	17-Jul-23	21-Jul-23
P11-EF	Painting	5	0%	$51.41	13-Aug-23	17-Aug-23
P11-EF	Coating of Underground Piping	5	0%	$41.85	18-Aug-23	22-Aug-23
Pipeline		89	0%	$332,098.76	28-Mar-23	24-Jun-23
P11-EF	Insulation Joints	5	0%	$6,641.98	20-Jun-23	24-Jun-23
P11-EF	Anchor Flanges	5	0%	$6,641.98	29-May-23	02-Jun-23
P11-EF	Pipeline Material Flange, Fittings, Gasket and Bolt	5	0%	$6,641.98	03-Jun-23	07-Jun-23
Line Pipe		10	0%	$312,172.83	28-Mar-23	06-Apr-23
P11-E	8"-U/G Gas Pipeline	10	0%	$299,685.92	28-Mar-23	06-Apr-23
P11-E	4"-A/G Condensate Pipeline	10	0%	$12,486.91	28-Mar-23	06-Apr-23
Control & Instrumentation		278	0%	$11,799.07	10-Oct-22	14-Jul-23
P11-EF	Control System/Console/Furniture	5	0%	$1,321.50	05-May-23	09-May-23
P11-EF	ESD System	5	0%	$923.87	25-Apr-23	29-Apr-23
P11-EF	Corrosion Probe/Coupon	10	0%	$396.45	25-Jan-23	03-Feb-23
P11-EF	ON/OFF & Shutdown Valves	10	0%	$2,076.64	15-Mar-23	24-Mar-23
P11-EF	Pressure Safety Valves (PSV)	10	0%	$671.37	14-Apr-23	23-Apr-23
P11-EF	Differential Pressure/Pressure Gauge	5	0%	$71.97	06-Feb-23	10-Feb-23
P11-EF	Pressure/Diff. Pressure Transmitter	10	0%	$110.91	07-Jan-23	16-Jan-23
P11-EF	Temperature Gauge	10	0%	$66.07	22-Mar-23	31-Mar-23
P11-EF	Pig Signaler	10	0%	$277.28	31-Dec-22	09-Jan-23
P11-EF	Instrument Installation Accessories	5	0%	$921.51	10-Oct-22	14-Oct-22
P11-EF	Instrument Cable Tray	10	0%	$863.69	03-Jul-23	12-Jul-23
P11-EF	Instrument Junction box and Gland	10	0%	$781.10	02-Jul-23	11-Jul-23
P11-EF	Instrument Tube and Fitting	10	0%	$566.36	27-Jan-23	05-Feb-23
P11-EF	F&G Devices	5	0%	$922.69	27-Mar-23	31-Mar-23
P11-EF	LBV	10	0%	$1,497.30	24-Jan-23	02-Feb-23
P11-EF	Instrument Cable	10	0%	$330.37	05-Jul-23	14-Jul-23
Safety		165	0%	$431.20	14-Sep-22	25-Feb-23
P11-EF	Safety Equipment	5	0%	$172.48	21-Feb-23	25-Feb-23
P11-EF	Fire Fighting Equipment	5	0%	$172.48	15-Jan-23	19-Jan-23
P11-EF	Safety Signs	5	0%	$86.24	14-Sep-22	18-Sep-22
Electrical		125	0%	$14,464.64	06-Mar-23	08-Jul-23
P11-EF	Expansion Of LV Switchgear	5	0%	$867.88	20-Apr-23	24-Apr-23
P11-EF	Power & Control Cables	5	0%	$2,603.64	20-May-23	24-May-23
P11-EF	Cathodic Protection System	5	0%	$10,414.54	04-Jul-23	08-Jul-23
P11-EF	Electrical Bulk Items & Earthing	5	0%	$578.59	06-Mar-23	10-Mar-23
Inspection		351	0%	$78,399.14	19-Sep-22	04-Sep-23
Mechanical		10	0%	$4,249.23	18-Mar-23	27-Mar-23
P11-EF	Pig Traps	10	0%	$4,249.23	18-Mar-23	27-Mar-23
Piping (Pipes ,Manual Valves, Gaskets,Strainers, Bolt & Nuts, Fitti		72	0%	$2,391.17	25-Jun-23	04-Sep-23
P11-EF	Pipes	10	0%	$1,259.19	26-Aug-23	04-Sep-23
P11-EF	Fittings	10	0%	$170.97	16-Aug-23	25-Aug-23
P11-EF	Flanges	5	0%	$98.76	16-Aug-23	20-Aug-23

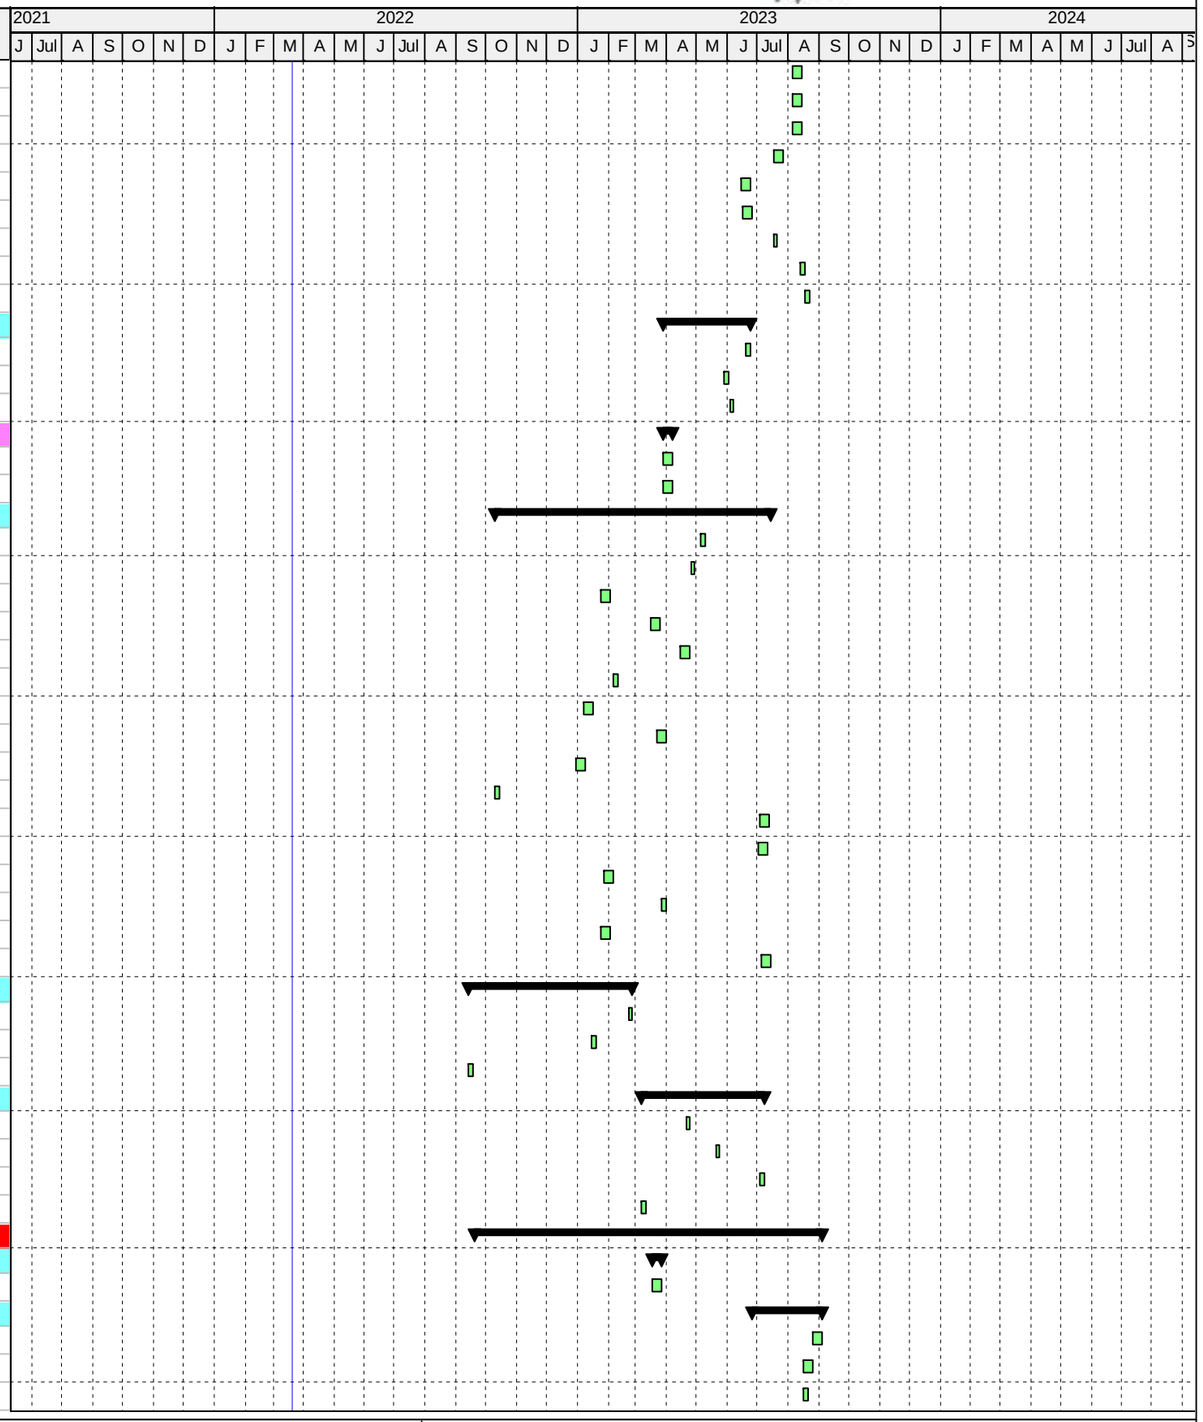


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-EF	Manual Valves	10	0%	$806.54	16-Aug-23	25-Aug-23
P11-EF	Gaskets	10	0%	$14.35	27-Jul-23	05-Aug-23
P11-EF	Bolt & Nuts	10	0%	$10.28	25-Jun-23	04-Jul-23
P11-EF	Insulation kits	10	0%	$4.06	26-Jun-23	05-Jul-23
P11-EF	Insulation	5	0%	$8.37	22-Jul-23	26-Jul-23
P11-EF	Painting	5	0%	$10.28	18-Aug-23	22-Aug-23
P11-EF	Coating of Underground Piping	5	0%	$8.37	13-Aug-23	17-Aug-23
Pipeline		84	0%	$66,419.75	07-Apr-23	29-Jun-23
P11-EF	Insulation Joints	5	0%	$1,328.40	25-Jun-23	29-Jun-23
P11-EF	Anchor Flanges	5	0%	$1,328.40	03-Jun-23	07-Jun-23
P11-EF	Pipeline Material Flange, Fittings, Gasket and Bolt	5	0%	$1,328.40	08-Jun-23	12-Jun-23
Line Pipe		10	0%	$62,434.57	07-Apr-23	16-Apr-23
P11-E	8"-U/G Gas Pipeline	10	0%	$59,937.18	07-Apr-23	16-Apr-23
P11-E	4"-A/G Condensate Pipeline	10	0%	$2,497.38	07-Apr-23	16-Apr-23
Control & Instrumentation		283	0%	$2,359.81	15-Oct-22	24-Jul-23
P11-EF	Control System/Console/Furniture	5	0%	$264.30	05-May-23	09-May-23
P11-EF	ESD System	5	0%	$184.77	25-Apr-23	29-Apr-23
P11-EF	Corrosion Probe/Coupon	10	0%	$79.29	10-May-23	19-May-23
P11-EF	ON/OFF & Shutdown Valves	10	0%	$415.33	25-Mar-23	03-Apr-23
P11-EF	Pressure Safety Valves (PSV)	10	0%	$134.27	24-Apr-23	03-May-23
P11-EF	Differential Pressure/Pressure Gauge	5	0%	$14.39	11-Feb-23	15-Feb-23
P11-EF	Pressure/Diff. Pressure Transmitter	10	0%	$22.18	17-Jan-23	26-Jan-23
P11-EF	Temperature Gauge	10	0%	$13.21	01-Apr-23	10-Apr-23
P11-EF	Pig Signaler	10	0%	$55.46	10-Jan-23	19-Jan-23
P11-EF	Instrument Installation Accessories	5	0%	$184.30	15-Oct-22	19-Oct-22
P11-EF	Instrument Cable Tray	10	0%	$172.74	13-Jul-23	22-Jul-23
P11-EF	Instrument Junction box and Gland	10	0%	$156.22	12-Jul-23	21-Jul-23
P11-EF	Instrument Tube and Fitting	10	0%	$113.27	06-Feb-23	15-Feb-23
P11-EF	F&G Devices	5	0%	$184.54	01-Apr-23	05-Apr-23
P11-EF	LBV	10	0%	$299.46	03-Feb-23	12-Feb-23
P11-EF	Instrument Cable	10	0%	$66.07	15-Jul-23	24-Jul-23
Safety		165	0%	$86.24	19-Sep-22	02-Mar-23
P11-EF	Safety Equipment	5	0%	$34.50	26-Feb-23	02-Mar-23
P11-EF	Fire Fighting Equipment	5	0%	$34.50	20-Jan-23	24-Jan-23
P11-EF	Safety Signs	5	0%	$17.25	19-Sep-22	23-Sep-22
Electrical		125	0%	$2,892.93	11-Mar-23	13-Jul-23
P11-EF	Expansion Of LV Switchgear	5	0%	$173.58	25-Apr-23	29-Apr-23
P11-EF	Power & Control Cables	5	0%	$520.73	25-May-23	29-May-23
P11-EF	Cathodic Protection System	5	0%	$2,082.91	09-Jul-23	13-Jul-23
P11-EF	Electrical Bulk Items & Earthing	5	0%	$115.72	11-Mar-23	15-Mar-23
Submmiting Vendor Data Book		351	0%	$117,598.71	24-Sep-22	09-Sep-23
Mechanical		5	0%	$6,373.85	28-Mar-23	01-Apr-23
P11-EF	Pig Traps	5	0%	$6,373.85	28-Mar-23	01-Apr-23
Piping (Pipes ,Manual Valves, Gaskets,Strainers, Bolt & Nuts, Fitt		67	0%	$3,586.76	05-Jul-23	09-Sep-23
P11-EF	Pipes	5	0%	$1,888.79	05-Sep-23	09-Sep-23
P11-EF	Fittings	5	0%	$256.45	26-Aug-23	30-Aug-23
P11-EF	Flanges	5	0%	$148.13	21-Aug-23	25-Aug-23
P11-EF	Manual Valves	5	0%	$1,209.81	26-Aug-23	30-Aug-23
P11-EF	Gaskets	5	0%	$21.52	06-Aug-23	10-Aug-23

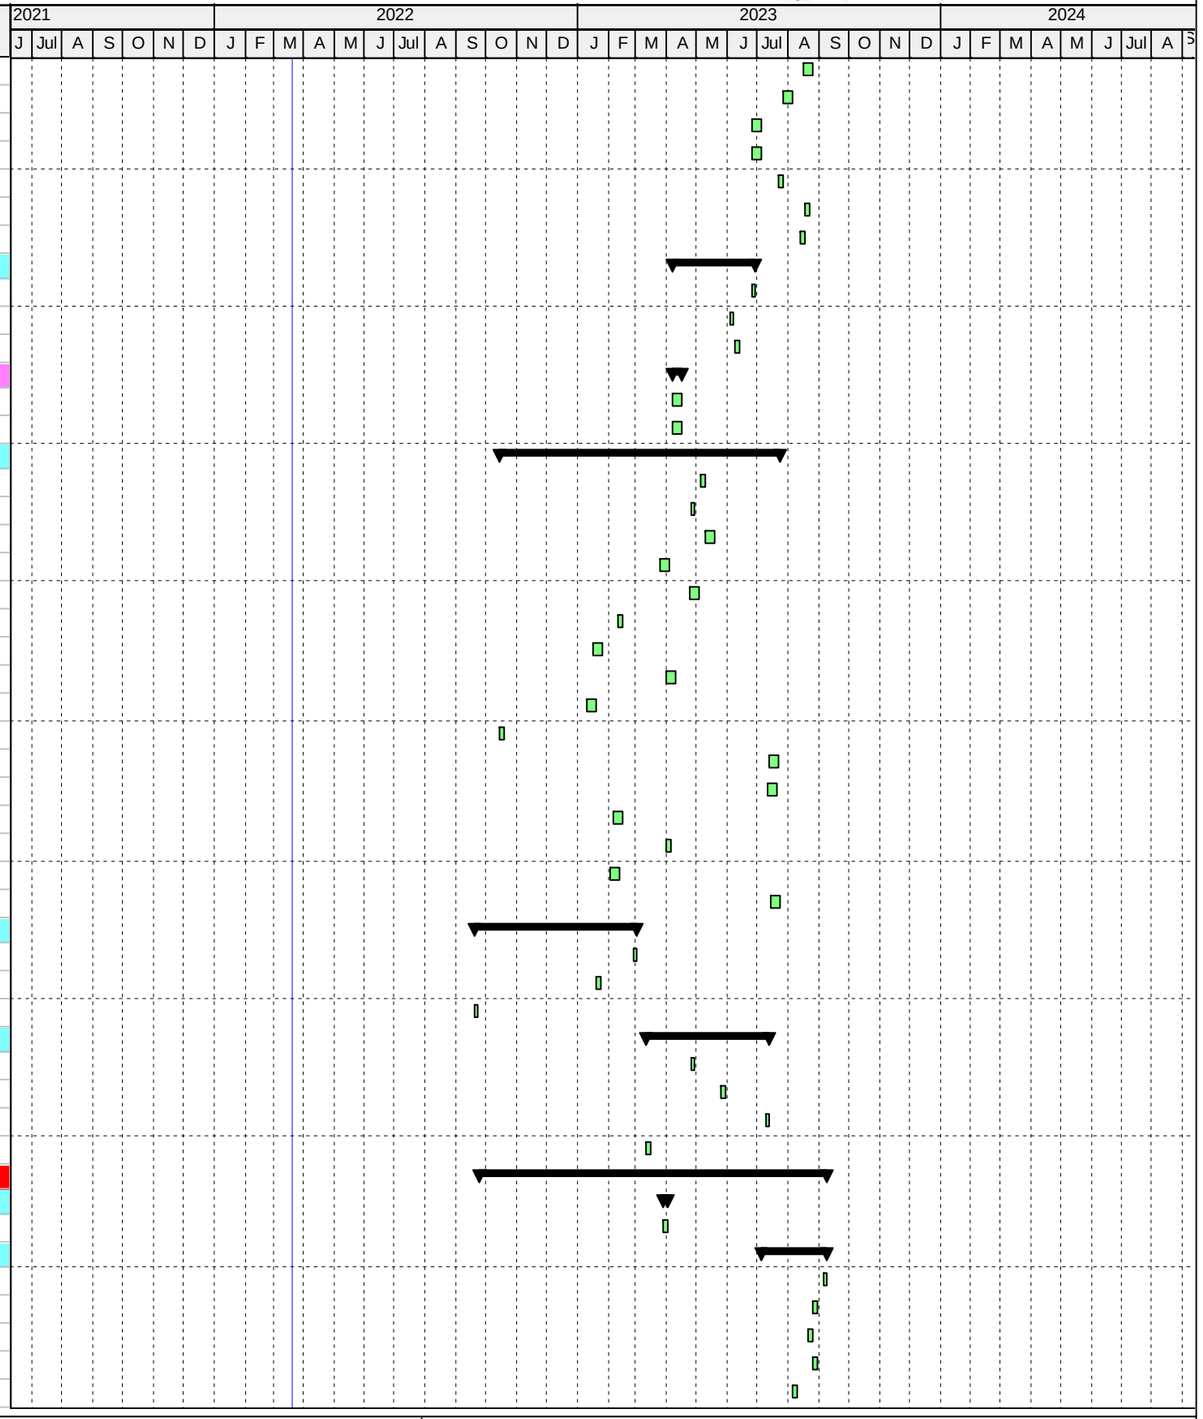


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-EF	Bolt & Nuts	5	0%	$15.42	05-Jul-23	09-Jul-23
P11-EF	Insulation kits	5	0%	$6.10	26-Aug-23	30-Aug-23
P11-EF	Insulation	5	0%	$12.55	27-Jul-23	31-Jul-23
P11-EF	Painting	5	0%	$15.42	23-Aug-23	27-Aug-23
P11-EF	Coating of Underground Piping	5	0%	$12.55	23-Aug-23	27-Aug-23
Pipeline		79	0%	$99,629.63	17-Apr-23	04-Jul-23
P11-EF	8"-U/G Gas Pipeline	5	0%	$89,905.78	17-Apr-23	21-Apr-23
P11-EF	4"-A/G Condensate Pipeline	5	0%	$3,746.07	17-Apr-23	21-Apr-23
P11-EF	Insulation Joints	5	0%	$1,992.59	30-Jun-23	04-Jul-23
P11-EF	Anchor Flanges	5	0%	$1,992.59	08-Jun-23	12-Jun-23
P11-EF	Pipeline Material Flange, Fittings, Gasket and Bolt	5	0%	$1,992.59	13-Jun-23	17-Jun-23
Control & Instrumentation		283	0%	$3,539.72	20-Oct-22	29-Jul-23
P11-EF	Control System/Console/Furniture	5	0%	$396.45	10-May-23	14-May-23
P11-EF	ESD System	5	0%	$277.16	30-Apr-23	04-May-23
P11-EF	Corrosion Probe/Coupon	5	0%	$118.93	20-May-23	24-May-23
P11-EF	ON/OFF & Shutdown Valves	5	0%	$622.99	04-Apr-23	08-Apr-23
P11-EF	Pressure Safety Valves (PSV)	5	0%	$201.41	04-May-23	08-May-23
P11-EF	Differential Pressure/Pressure Gauge	5	0%	$21.59	16-Feb-23	20-Feb-23
P11-EF	Pressure/Diff. Pressure Transmitter	5	0%	$33.27	27-Jan-23	31-Jan-23
P11-EF	Temperature Gauge	5	0%	$19.82	11-Apr-23	15-Apr-23
P11-EF	Pig Signaler	5	0%	$83.18	20-Jan-23	24-Jan-23
P11-EF	Instrument Installation Accessories	5	0%	$276.45	20-Oct-22	24-Oct-22
P11-EF	Instrument Cable Tray	5	0%	$259.11	23-Jul-23	27-Jul-23
P11-EF	Instrument Junction box and Gland	5	0%	$234.33	22-Jul-23	26-Jul-23
P11-EF	Instrument Tube and Fitting	5	0%	$169.91	16-Feb-23	20-Feb-23
P11-EF	F&G Devices	5	0%	$276.81	06-Apr-23	10-Apr-23
P11-EF	LBV	5	0%	$449.19	13-Feb-23	17-Feb-23
P11-EF	Instrument Cable	5	0%	$99.11	25-Jul-23	29-Jul-23
Safety		165	0%	$129.36	24-Sep-22	07-Mar-23
P11-EF	Safety Equipment	5	0%	$51.74	03-Mar-23	07-Mar-23
P11-EF	Fire Fighting Equipment	5	0%	$51.74	25-Jan-23	29-Jan-23
P11-EF	Safety Signs	5	0%	$25.87	24-Sep-22	28-Sep-22
Electrical		125	0%	$4,339.39	16-Mar-23	18-Jul-23
P11-EF	Expansion Of LV Switchgear	5	0%	$260.36	30-Apr-23	04-May-23
P11-EF	Power & Control Cables	5	0%	$781.09	30-May-23	03-Jun-23
P11-EF	Cathodic Protection System	5	0%	$3,124.36	14-Jul-23	18-Jul-23
P11-EF	Electrical Bulk Items & Earthing	5	0%	$173.58	16-Mar-23	20-Mar-23
Delivering Spare Part		221	0%	$195,997.85	17-Jan-23	25-Aug-23
Mechanical		10	0%	$70,030.03	18-Mar-23	27-Mar-23
P11-EF	Pig Traps	10	0%	$70,030.03	18-Mar-23	27-Mar-23
Piping (Pipes ,Manual Valves, Gaskets,Strainers, Bolt & Nuts, Fitti		10	0%	$39,415.17	16-Aug-23	25-Aug-23
P11-EF	Manual Valves	10	0%	$39,415.17	16-Aug-23	25-Aug-23
Control & Instrumentation		123	0%	$38,885.97	17-Jan-23	19-May-23
P11-EF	Control System/Console/Furniture	10	0%	$6,376.62	10-May-23	19-May-23
P11-EF	ESD System	10	0%	$4,457.94	30-Apr-23	09-May-23
P11-EF	Corrosion Probe/Coupon	10	0%	$1,912.98	04-Feb-23	13-Feb-23
P11-EF	ON/OFF & Shutdown Valves	10	0%	$14,575.12	25-Mar-23	03-Apr-23
P11-EF	Pressure Safety Valves (PSV)	10	0%	$3,239.55	24-Apr-23	03-May-23
P11-EF	Differential Pressure/Pressure Gauge	10	0%	$347.30	11-Feb-23	20-Feb-23

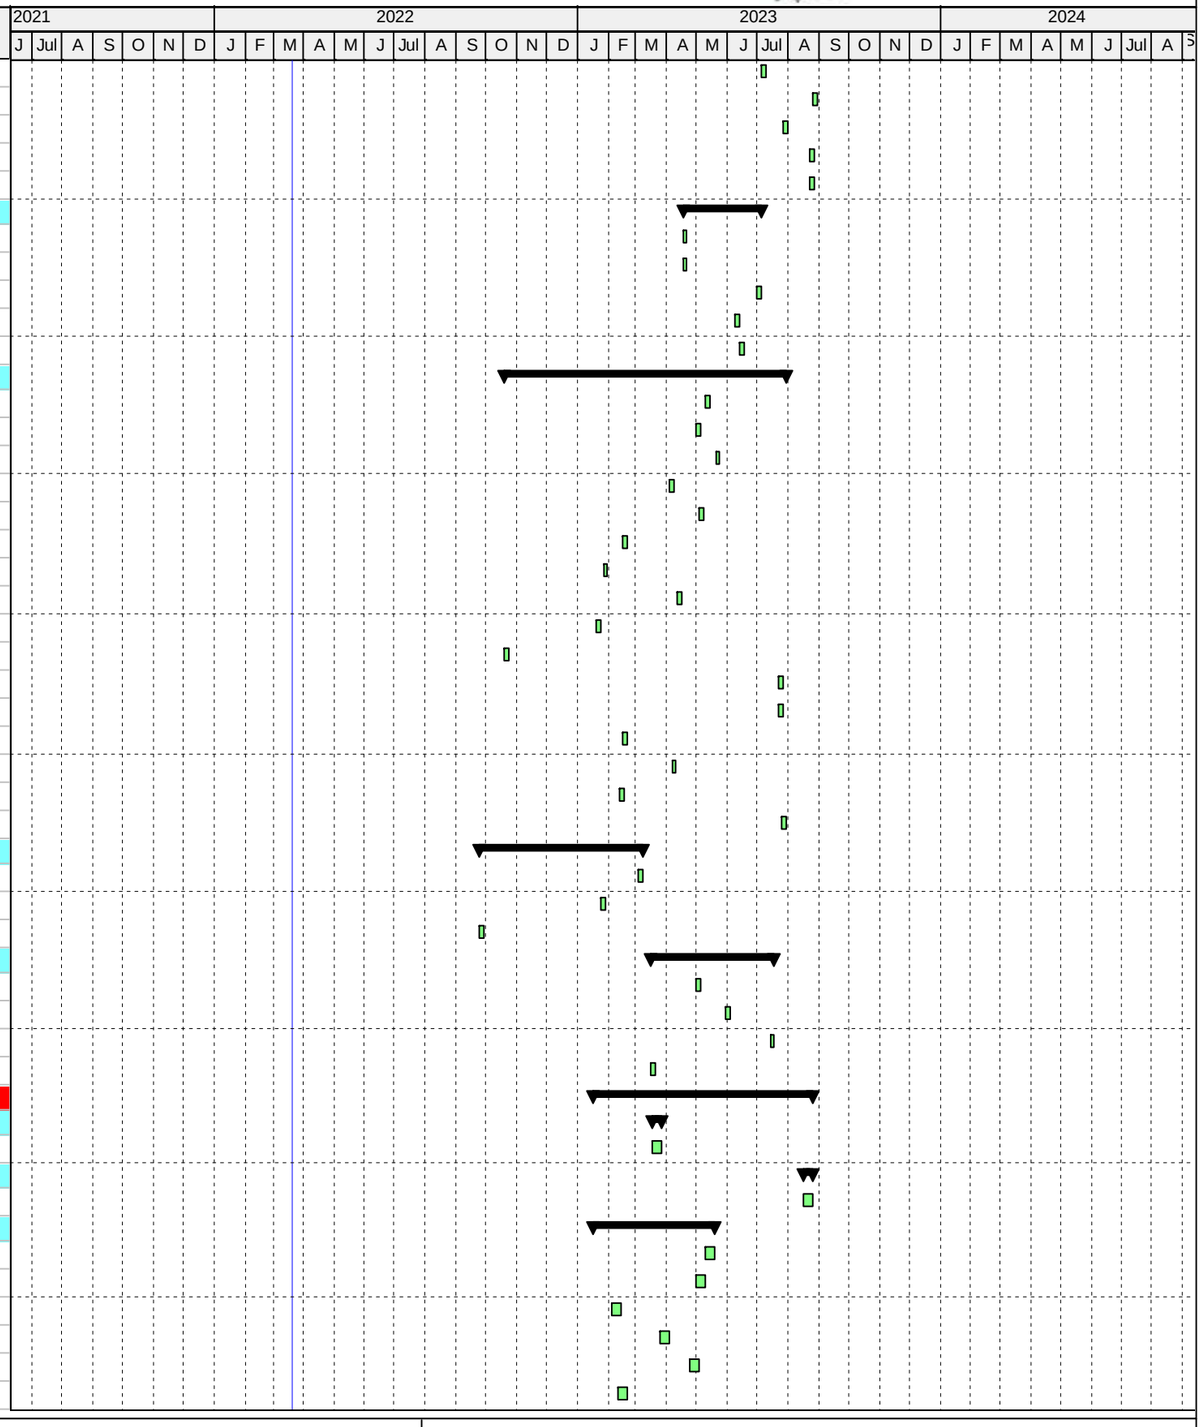


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-EF	Pressure/Diff. Pressure Transmitter	10	0%	$535.18	17-Jan-23	26-Jan-23
P11-EF	Temperature Gauge	10	0%	$318.83	01-Apr-23	10-Apr-23
P11-EF	F&G Devices	10	0%	$4,452.24	01-Apr-23	10-Apr-23
P11-EF	LBV	10	0%	$2,670.21	03-Feb-23	12-Feb-23
Electrical		80	0%	$47,666.68	25-Apr-23	13-Jul-23
P11-EF	Expansion Of LV Switchgear	5	0%	$3,813.33	25-Apr-23	29-Apr-23
P11-EF	Cathodic Protection System	5	0%	$43,853.34	09-Jul-23	13-Jul-23
CONSTRUCTION		443	0%	$1,394,941.00	08-Sep-22	24-Nov-23
4"-5.2 Km A/G Condensate Pipeline (From Binak Compressor Stat		442	0%	$69,747.05	08-Sep-22	23-Nov-23
ROW		60	0%	$11,159.53	08-Sep-22	06-Nov-22
P11-EF	Excavation & Soil Transfer	45	0%	$10,043.58	08-Sep-22	22-Oct-22
P11-EF	Levelling & Compaction	35	0%	$1,115.95	03-Oct-22	06-Nov-22
PipelineSupportFoundation		57	0%	$3,487.35	09-Sep-22	04-Nov-22
P11-EF	Excavation & Soil Transfer	20	0%	$871.84	17-Sep-22	06-Oct-22
P11-EF	Levelling	20	0%	$27.90	27-Sep-22	16-Oct-22
P11-EF	Lean Concrete	2	0%	$198.78	07-Oct-22	08-Oct-22
P11-EF	Reinforced Work	45	0%	$1,743.68	09-Sep-22	23-Oct-22
P11-EF	Nylon Execution	15	0%	$6.97	14-Oct-22	28-Oct-22
P11-EF	Main Concrete Pouring	2	0%	$627.72	29-Oct-22	30-Oct-22
P11-EF	Backfilling & Compaction	15	0%	$10.46	21-Oct-22	04-Nov-22
PipelineSupportErection		45	0%	$6,974.71	22-Feb-23	07-Apr-23
P11-EF	Support Fabrication	35	0%	$4,533.56	22-Feb-23	28-Mar-23
P11-EF	Support Erection	30	0%	$2,441.15	09-Mar-23	07-Apr-23
Pipeline		95	0%	$45,335.58	07-Apr-23	10-Jul-23
P11-EF	Material Handeling	45	0%	$6,800.34	07-Apr-23	21-May-23
P11-EF	Fit-Up & Welding	60	0%	$27,201.35	22-Apr-23	20-Jun-23
P11-EF	NDT	40	0%	$6,800.34	22-May-23	30-Jun-23
P11-EF	Hydrotest	20	0%	$4,533.56	21-Jun-23	10-Jul-23
Instrument Works		45	0%	$1,394.94	15-Jul-23	28-Aug-23
P11-EF	Devices Installation and Piping Connecton	45	0%	$1,394.94	15-Jul-23	28-Aug-23
Pre-commissioning		45	0%	$1,394.94	10-Oct-23	23-Nov-23
P11-EF	Pre-commissioning	25	0%	$1,255.45	10-Oct-23	03-Nov-23
P11-EF	Ready for Comm.Certificate(RFCC)	20	0%	$139.49	04-Nov-23	23-Nov-23
8"-44 Km U/G Gas Pipeline (From Binak Compressor Station to Sa		434	0%	$1,311,244.54	17-Sep-22	24-Nov-23
Pig Luncher / Reciver		30	0%	$26,224.89	18-Mar-23	16-Apr-23
P11-EF	Pig Luncher / Reciver Civil Works	30	0%	$26,224.89	18-Mar-23	16-Apr-23
Civil Works		30	0%	$39,337.34	17-Sep-22	16-Oct-22
P11-EF	Civil Works	30	0%	$39,337.34	17-Sep-22	16-Oct-22
ROW		160	0%	$157,349.35	17-Oct-22	25-Mar-23
P11-EF	Excavation & Soil Transfer	80	0%	$141,614.41	17-Oct-22	04-Jan-23
P11-EF	Levelling & Compaction	100	0%	$15,734.93	16-Dec-22	25-Mar-23
Pipe Line Trench		269	0%	$340,923.58	04-Feb-23	30-Oct-23
P11-EF	Pipe Line trench excavation	50	0%	$221,600.33	04-Feb-23	25-Mar-23
P11-EF	Pipe Line trench back filling	50	0%	$119,323.25	11-Sep-23	30-Oct-23
Pipeline		167	0%	$629,397.38	07-Apr-23	20-Sep-23
P11-EF	Pipe Line strining	50	0%	$66,086.72	07-Apr-23	26-May-23
P11-EF	Pipe Line laying	60	0%	$66,086.72	08-Jun-23	06-Aug-23
P11-EF	Pipe welding	60	0%	$251,758.95	18-Jun-23	16-Aug-23
P11-EF	NDT	50	0%	$31,469.87	03-Jul-23	21-Aug-23
P11-EF	Pipe Line Tie in connection	35	0%	$31,469.87	17-Aug-23	20-Sep-23

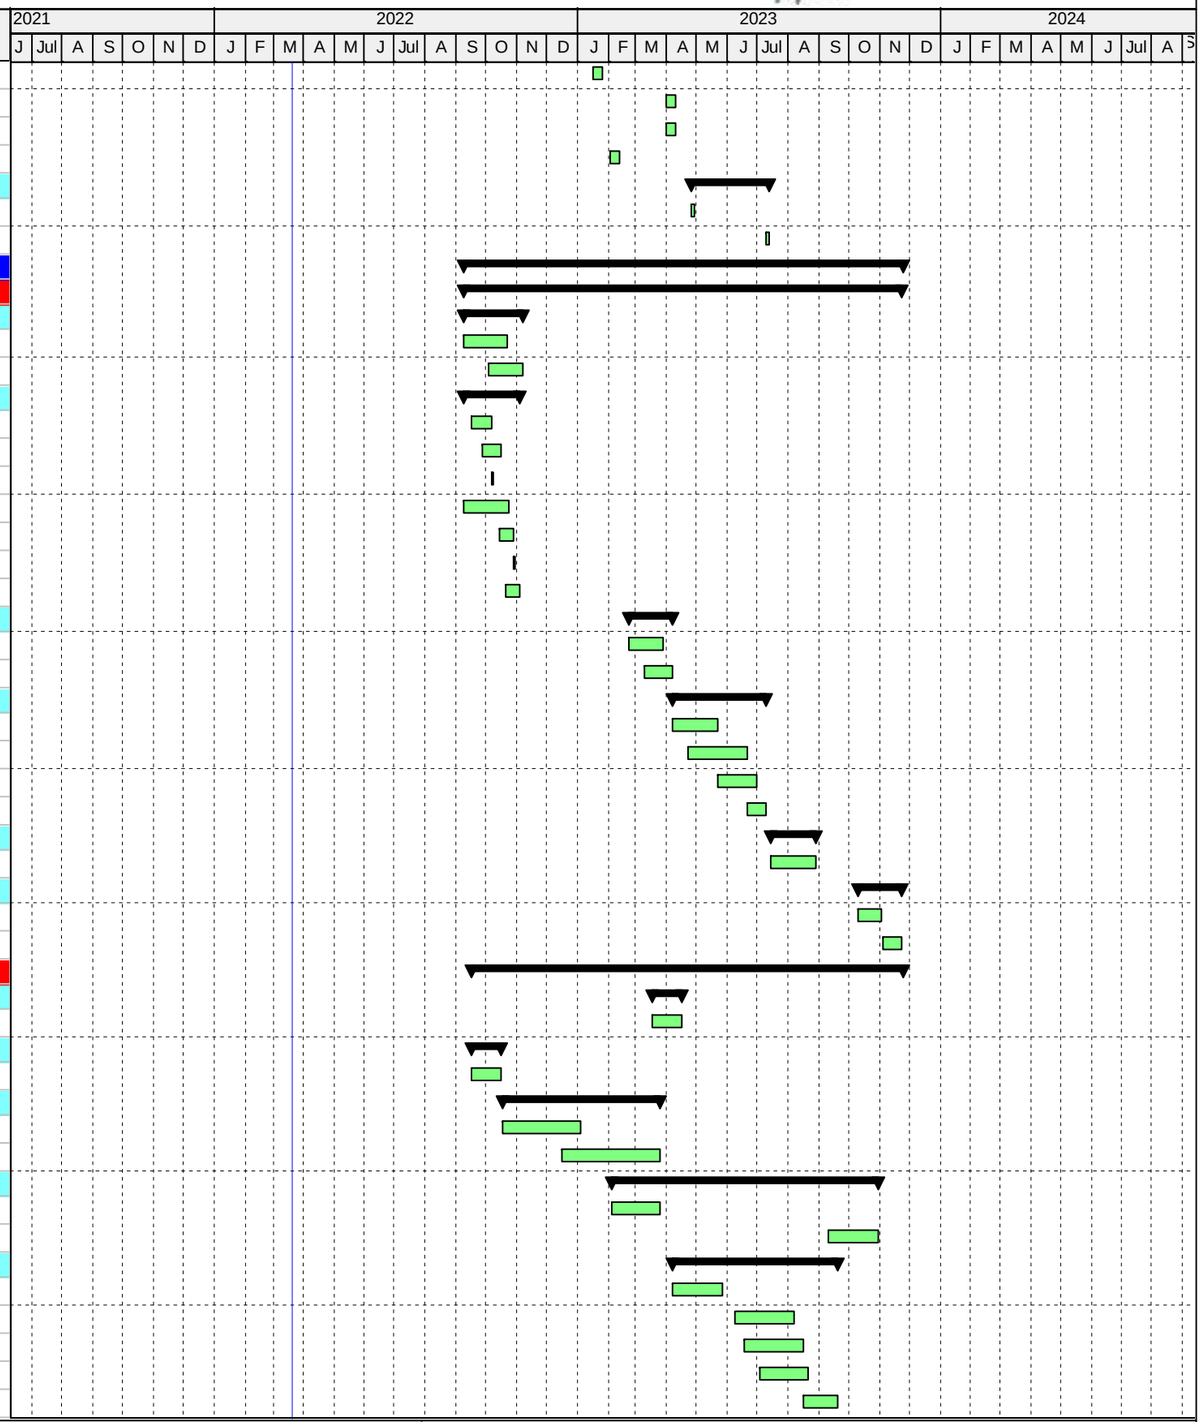


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P11-EF	Pipe Line test	20	0%	$62,939.74	22-Aug-23	10-Sep-23
P11-EF	Pipe Line joint coating	60	0%	$56,645.76	23-Jul-23	20-Sep-23
P11-EF	Crossing	35	0%	$62,939.74	03-Jul-23	06-Aug-23
Piping & Painting ,....		30	0%	$39,337.34	18-Aug-23	16-Sep-23
P11-EF	Piping & Painting ,....	30	0%	$39,337.34	18-Aug-23	16-Sep-23
Instrument Instalation		30	0%	$13,112.45	15-Jul-23	13-Aug-23
P11-EF	Instrument Instalation	30	0%	$13,112.45	15-Jul-23	13-Aug-23
Catodic Protection Instalation		30	0%	$39,337.34	22-Aug-23	20-Sep-23
P11-EF	Catodic Protection Instalation	30	0%	$39,337.34	22-Aug-23	20-Sep-23
Pre-commissioning		25	0%	$26,224.89	31-Oct-23	24-Nov-23
P11-EF	Pre-commissioning	15	0%	$23,602.40	31-Oct-23	14-Nov-23
P11-EF	Ready for Comm.Certificate(RFCC)	10	0%	$2,622.49	15-Nov-23	24-Nov-23
Job Site HSE Supervision (Surface)		320	0%	$13,949.41	17-Oct-22	01-Sep-23
P11-EP(	Job Site HSE Supervision (Surface)	320	0%	$13,949.41	17-Oct-22	01-Sep-23
Commissioning, Startup & Handover		55	0%	$52,501.00	25-Nov-23	18-Jan-24
Commissioning		30	0%	$15,750.30	25-Nov-23	24-Dec-23
P11-EP(	Materials & Utilities Ready for Commissioning	20	0%	$787.52	25-Nov-23	14-Dec-23
P11-EP(	Receiving Facilities Ready for Commissioning	20	0%	$787.52	30-Nov-23	19-Dec-23
P11-EP(	Permits Obtained for Commissioning	10	0%	$787.52	10-Dec-23	19-Dec-23
P11-EP(	Integrated Commissioning	10	0%	$12,600.24	10-Dec-23	19-Dec-23
P11-EP(	Ready for Startup Certificate (RFSU)	15	0%	$787.52	10-Dec-23	24-Dec-23
Startup & Performance Test		30	0%	$21,000.40	05-Dec-23	03-Jan-24
P11-EP(	Startup & Performance Test Run	25	0%	$16,800.32	05-Dec-23	29-Dec-23
P11-EP(	Start of Production (SOP)	15	0%	$4,200.08	20-Dec-23	03-Jan-24
Handover		35	0%	$15,750.30	15-Dec-23	18-Jan-24
P11-EP(	Compiling & Submitting Final Documentation	25	0%	$4,725.09	15-Dec-23	08-Jan-24
P11-EP(	Training of Operator's Personnel	15	0%	$6,300.12	30-Dec-23	13-Jan-24
P11-EP(	Provisional Acceptance Certificate (PAC)	15	0%	$4,725.09	04-Jan-24	18-Jan-24
Package 12- EPC # Compressor Station		826	0.59%	$21,954,479.98	24-Jul-21 A	22-Jun-24
ENGINEERING		793	18.49%	$703,959.00	24-Jul-21 A	20-May-24
Basic Design Endorsement		30	100%	$35,197.95	31-Jul-21 A	20-Mar-22
P12-EP(	Endorsement Report For Basic Design & Scope of Work	30	100%	$35,197.95	31-Jul-21 A	20-Mar-22
Value Engineering		112	30%	$21,118.77	01-Feb-22	08-Aug-22
P12-EP(	Value Engineering Study Report	44	60%	$10,559.39	01-Feb-22	20-Mar-22
P12-EP(	HAZID Report For Compressor Station	44	0%	$2,111.88	13-May-22	25-Jun-22
P12-EP(	HAZOP Report For Compressor Station	44	0%	$5,279.69	13-May-22	25-Jun-22
P12-EP(	SIL Report For Compressor Station	44	0%	$3,167.82	26-Jun-22	08-Aug-22
Detail Design		596	21.99%	$387,177.45	24-Jul-21 A	05-Jun-23
Process		413	61.16%	$36,781.86	27-Jul-21 A	10-Jul-22
Basis/Criteria		45	86.95%	$106.67	27-Jul-21 A	03-May-22
P12-E	Process Design Criteria	35	100%	$37.10	27-Jul-21 A	20-Mar-22
P12-E	Process Basis Of Design	45	80%	$69.57	27-Jul-21 A	03-May-22
Philosophy		44	63.2%	$231.73	21-Nov-21	02-May-22
P12-E	Drainage Philosophy	44	80%	$37.08	21-Nov-21	02-May-22
P12-E	Control Philosophy	44	60%	$55.61	20-Feb-22	02-May-22
P12-E	Flare,Blow Down And Relief Philosophy	44	60%	$55.61	21-Nov-21	02-May-22
P12-E	Isolation Philosophy	44	60%	$37.08	21-Nov-21	02-May-22
P12-E	ESD Philosophy	44	60%	$46.35	20-Feb-22	02-May-22
Procedure		54	0%	$1,430.81	03-May-22	25-Jun-22
P12-E	Chemical Regeneration Procedure	44	0%	$715.41	13-May-22	25-Jun-22

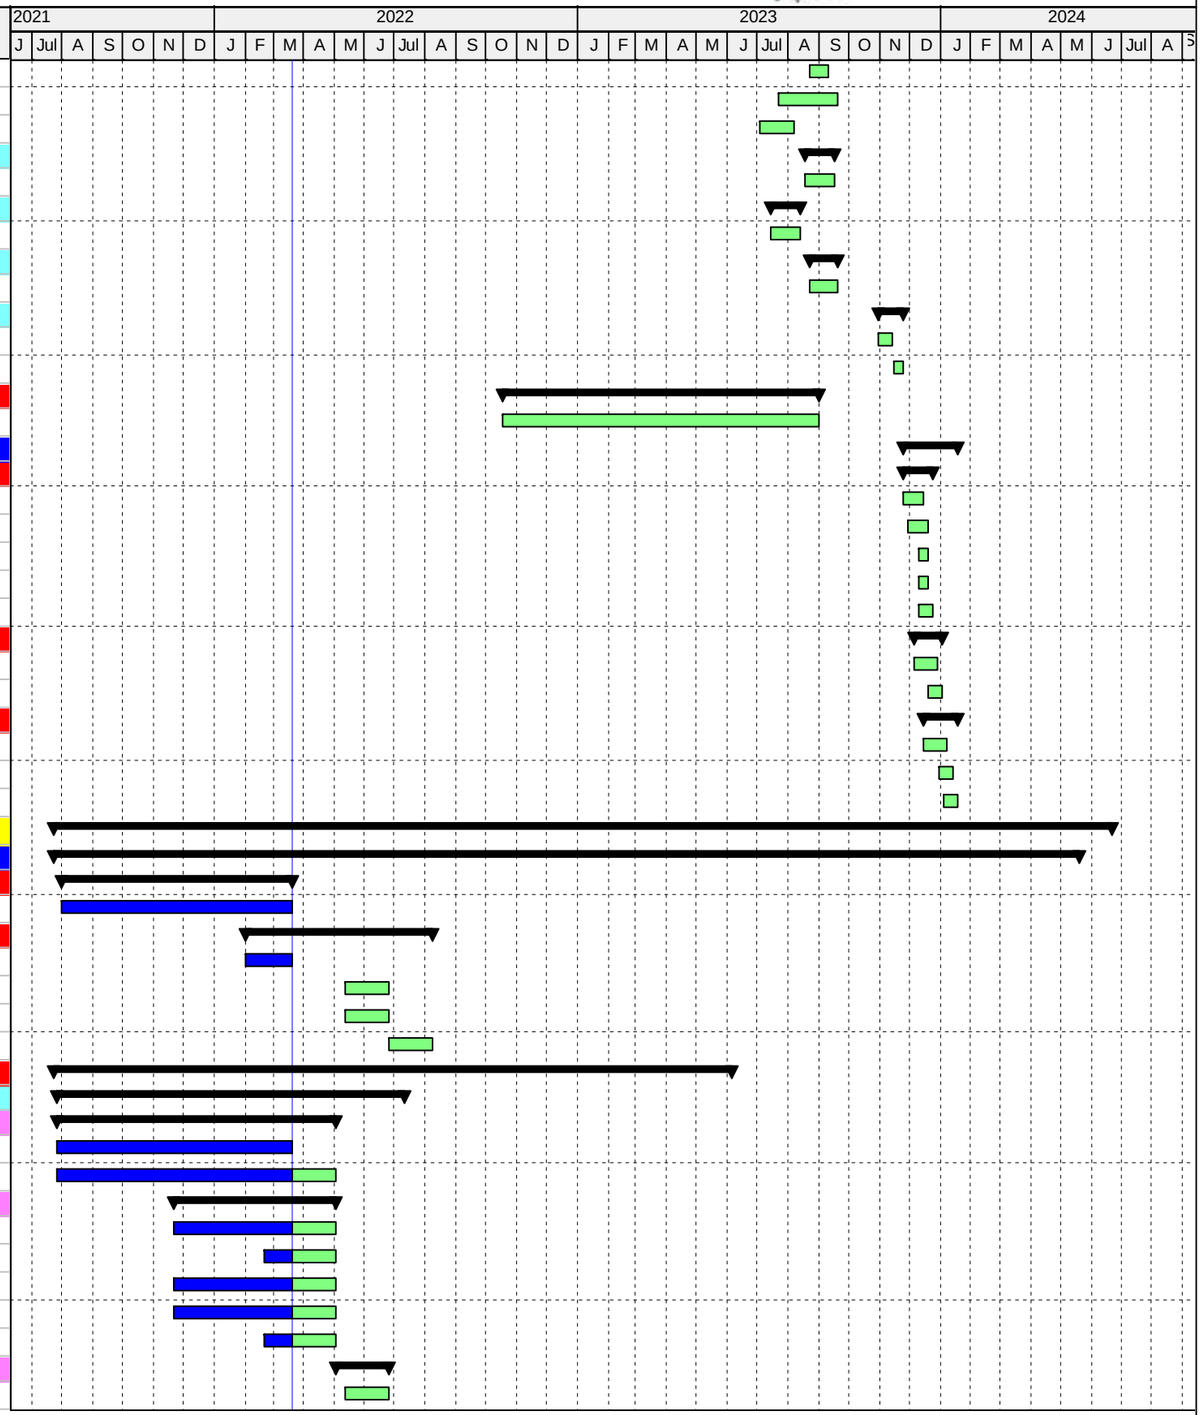


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Startup And Shutdown Procedure	44	0%	$715.41	03-May-22	15-Jun-22
Description		44	60%	$834.95	20-Feb-22	02-May-22
P12-E	Process & Utility Description	44	60%	$834.95	20-Feb-22	02-May-22
Duty Specification		358	70%	$1,673.57	08-Dec-21	22-May-22
P12-E	Duty Specification For Gas Dehydration Package	64	80%	$418.39	08-Dec-21	22-May-22
P12-E	Duty Specification for Instrument/Plant Air & Nitrogen Package	64	80%	$418.39	28-Dec-21	22-May-22
P12-E	Duty Specification for LP Flare Package	64	60%	$418.39	09-Mar-22	22-May-22
P12-E	Duty Specification for Chemical Injection Package	64	60%	$418.39	09-Mar-22	22-May-22
Calculation		305	68.83%	$5,682.80	26-Sep-21	25-Jun-22
P12-E	Calculation Note For Pumps	44	80%	$835.37	13-Dec-21	12-May-22
P12-E	Calculation Note For Drum Sizing	44	80%	$835.94	26-Sep-21	12-May-22
P12-E	Calculation Note For Flow Element Sizing	44	0%	$445.53	13-May-22	25-Jun-22
P12-E	Calculation Note For PSV Sizing	44	80%	$222.77	26-Sep-21	13-May-22
P12-E	Calculation Note For Line Sizing	44	80%	$1,114.40	26-Sep-21	13-May-22
P12-E	Calculation Note For Control Valve Sizing	44	80%	$835.94	26-Sep-21	13-May-22
P12-E	Calculation Note For Depressurizing (Min. Design Temperatu	44	60%	$1,392.85	13-Dec-21	13-May-22
Data Sheets		269	58.11%	$14,922.40	07-Nov-21	10-Jul-22
Fixed Equipment		98	68.89%	$6,073.42	07-Nov-21	13-May-22
P12-	Process Data Sheets For Inlet Gas K.O. Drum	44	80%	$337.68	10-Nov-21	12-May-22
P12-	Process Data Sheets For 1st Stage G.C. Suction Drums	44	80%	$337.68	10-Nov-21	12-May-22
P12-	Process Data Sheets For 1st Stage Gas Air Coolers	44	80%	$337.68	07-Nov-21	12-May-22
P12-	Process Data Sheets For 2nd Stage G.C. Suction Drums	44	80%	$337.68	10-Nov-21	12-May-22
P12-	Process Data Sheets For 2nd Stage Gas Air Coolers	44	80%	$337.68	07-Nov-21	12-May-22
P12-	Process Data Sheets For Discharge Gas K.O. Drum	44	80%	$337.68	10-Nov-21	12-May-22
P12-	Process Data Sheets For Diesel Oil Drum	44	80%	$337.07	10-Nov-21	13-May-22
P12-	Process Data Sheets For Instrument Air Receiver	44	80%	$337.07	10-Nov-21	13-May-22
P12-	Process Data Sheets For Nitrogen Receiver	44	60%	$337.07	10-Nov-21	13-May-22
P12-	Process Data Sheets For Close Drain Drum	44	60%	$337.68	10-Nov-21	13-May-22
P12-	Process Data Sheets For Elevated Potable Water Tank	44	60%	$337.68	10-Nov-21	13-May-22
P12-	Process Data Sheets For Flare K.O. Drum	44	60%	$337.68	10-Nov-21	13-May-22
P12-	Process Data Sheets For Fuel Gas K.O. Drum	44	60%	$337.68	10-Nov-21	13-May-22
P12-	Process Data Sheets For Slug Catcher	44	60%	$337.07	10-Nov-21	12-May-22
P12-	Process Data Sheets For Degassing Vessel	44	60%	$337.07	10-Nov-21	12-May-22
P12-	Process Data Sheets For Lean Glycol Storage Tank	44	60%	$337.07	27-Nov-21	12-May-22
P12-	Process Data Sheets For Slug Storage Tank	44	60%	$337.07	27-Nov-21	12-May-22
P12-	Process Data Sheets For Glycol Sump Drum	44	60%	$337.07	28-Dec-21	12-May-22
Rotary Equipment		160	60%	$6,158.47	28-Nov-21	16-Jun-22
P12-	Process Data Sheets For Slug Pumps	44	60%	$615.85	27-Mar-22	16-Jun-22
P12-	Process Data Sheets For Glycol Transfer Pumps	44	60%	$615.85	28-Mar-22	12-May-22
P12-	Process Data Sheets For Glycol Manual Pump	44	60%	$615.85	28-Mar-22	12-May-22
P12-	Process Data Sheets For Closed Drain Pumps	44	60%	$615.85	28-Mar-22	12-May-22
P12-	Process Data Sheets For Sump Pumps	44	60%	$615.85	28-Mar-22	12-May-22
P12-	Process Data Sheets For Flare KO Drum Pumps	44	60%	$615.85	28-Mar-22	12-May-22
P12-	Process Data Sheets For Potable Water Pump	44	60%	$615.85	28-Mar-22	12-May-22
P12-	Process Data Sheets For Glycol Sump Pumps	44	60%	$615.85	28-Nov-21	12-May-22
P12-	Process Data Sheets For Glycol Drain Pump	44	60%	$615.85	28-Mar-22	12-May-22
P12-	Process Data Sheets of Diesel Pump	44	60%	$615.85	28-Mar-22	12-May-22
Packaged Equipment		109	40%	$1,980.20	07-Nov-21	10-Jul-22
P12-	Process Data Sheets For Gas Compressors Packages	44	80%	$990.10	07-Nov-21	13-May-22

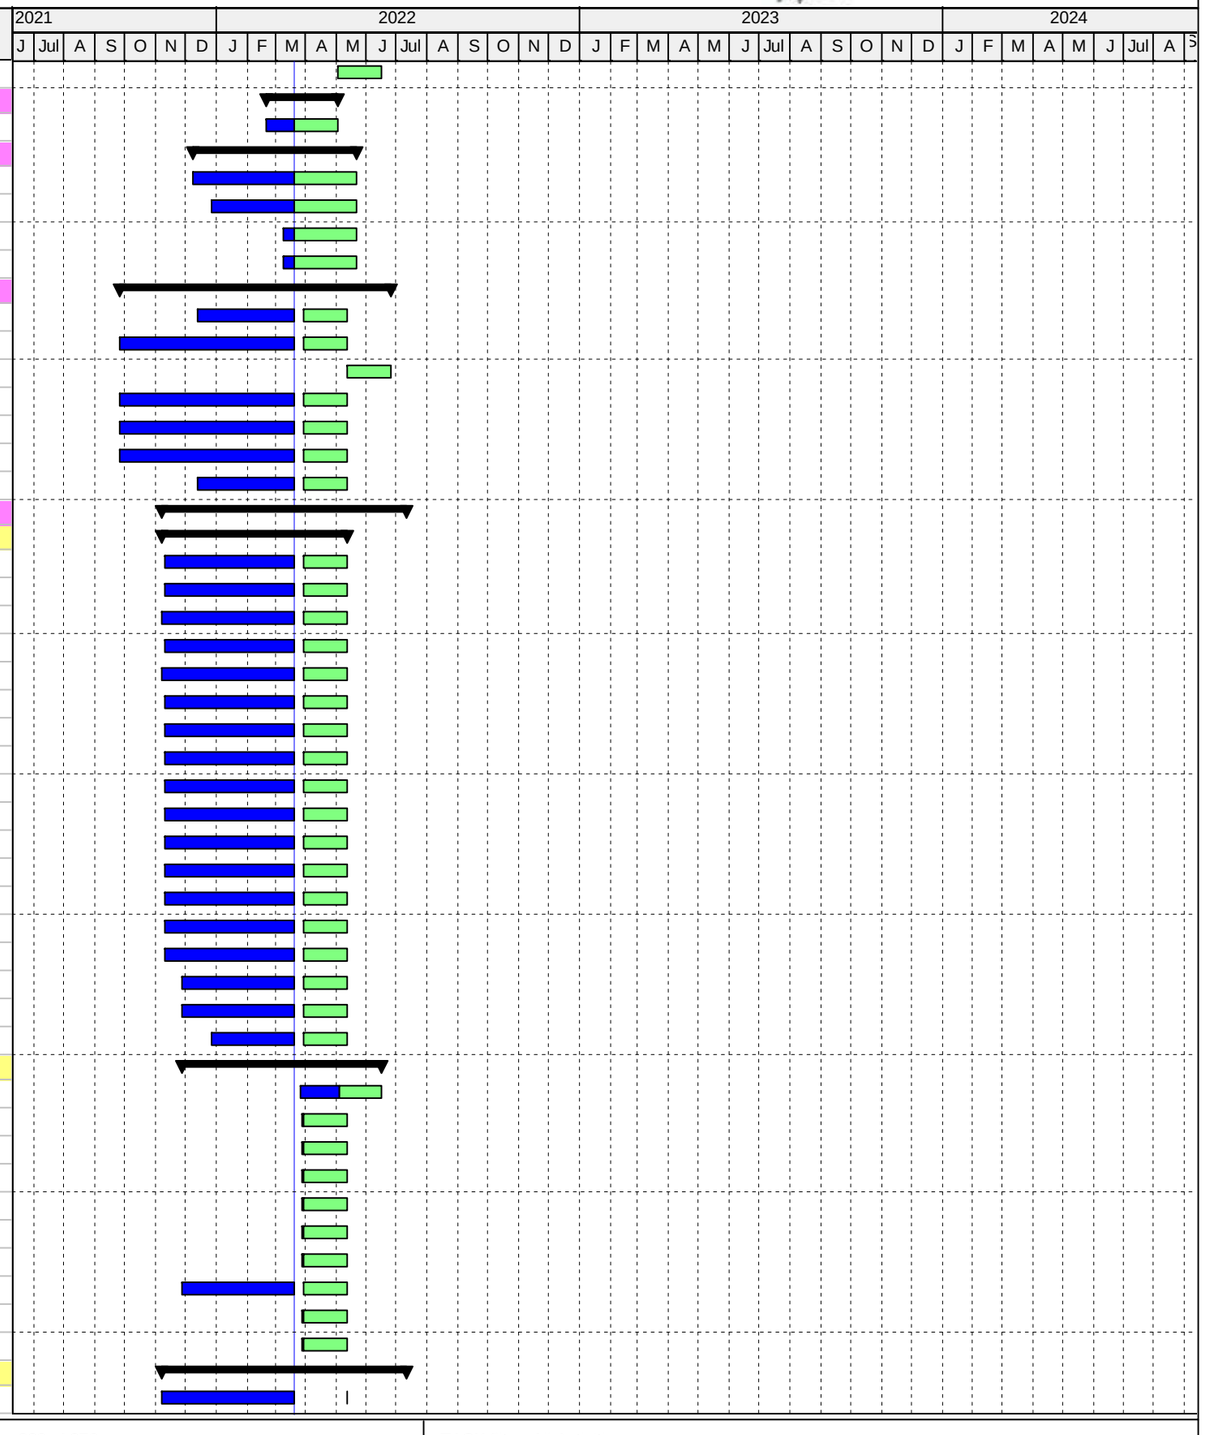


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-	Process Data Sheets For Chemical Injection Packages	59	0%	$990.10	13-May-22	10-Jul-22
Instruments		37	0%	$710.31	13-May-22	18-Jun-22
P12-	Process Data Sheets For Instrument Devices	37	0%	$710.31	13-May-22	18-Jun-22
Drawing/Diagram		241	73.02%	$7,830.86	14-Aug-21	25-Jun-22
P12-E	Process Flow Diagram (PFD)	54	80%	$790.92	14-Aug-21	12-May-22
P12-E	Utility Flow Diagrams (UFD)	54	80%	$1,057.95	18-Oct-21	12-May-22
P12-E	Symbol & Legend For PFD and P&ID	44	80%	$212.22	04-Oct-21	12-May-22
P12-E	P&ID - Gas Compression Inlet Gas Pipeline (Binak)	44	80%	$212.22	26-Sep-21	12-May-22
P12-E	P&ID - Gas Compression Inlet Gas Pipeline (Golkhari)	44	80%	$212.22	26-Sep-21	12-May-22
P12-E	P&ID - Slug Catcher System	44	80%	$212.22	26-Sep-21	12-May-22
P12-E	P&ID - Gas Compression Inlet Knock Out Drum	44	80%	$212.22	26-Sep-21	12-May-22
P12-E	P&ID - 1st Stage Gas Compression Suction Drums	54	80%	$212.22	26-Sep-21	12-May-22
P12-E	P&ID - 1st Stage Gas Compression Compressors	54	80%	$211.43	26-Sep-21	13-May-22
P12-E	P&ID - 1st Stage Gas Compression Air Coolers	44	80%	$211.43	26-Sep-21	13-May-22
P12-E	P&ID - 2nd Stage Gas Compression Suction Drums	44	80%	$211.43	26-Sep-21	13-May-22
P12-E	P&ID - 2nd Stage Gas Compression Compressors	44	80%	$211.43	26-Sep-21	13-May-22
P12-E	P&ID - 2nd Stage Gas Compression Air Coolers	44	80%	$211.43	26-Sep-21	13-May-22
P12-E	P&ID - 2nd Stage Gas Compression Discharge Drum	44	80%	$211.43	26-Sep-21	13-May-22
P12-E	P&ID - Gas Compression Dehydration Package	44	80%	$211.43	26-Sep-21	13-May-22
P12-E	P&ID - Lean Glycol Storage Tank	44	80%	$211.43	26-Sep-21	13-May-22
P12-E	P&ID - Instrument & Plant Air System	44	80%	$212.22	03-Jan-22	12-May-22
P12-E	P&ID - Nitrogen Generation System	44	80%	$212.22	03-Jan-22	12-May-22
P12-E	P&ID - Close Drain System	44	80%	$212.22	18-Oct-21	12-May-22
P12-E	P&ID - Corrosion Inhibitor Package	44	80%	$212.22	18-Oct-21	12-May-22
P12-E	P&ID - Methanol Injection Package	44	80%	$212.22	18-Oct-21	12-May-22
P12-E	P&ID - LP Flare System	44	80%	$212.22	18-Oct-21	12-May-22
P12-E	P&ID - Oily Water Sewer	44	80%	$212.22	18-Oct-21	12-May-22
P12-E	P&ID - Fuel Gas System	44	80%	$212.22	18-Oct-21	12-May-22
P12-E	P&ID - Diesel Oil System	44	80%	$212.22	18-Oct-21	12-May-22
P12-E	P&ID - Potable Water System	44	80%	$212.22	18-Oct-21	12-May-22
P12-E	ESD Block Diagram	44	0%	$258.42	30-Mar-22	12-May-22
P12-E	Cause & Effect Diagram	44	0%	$212.22	13-May-22	25-Jun-22
P12-E	P&ID - Glycol Sump Drum	44	80%	$212.22	26-Sep-21	12-May-22
P12-E	Chemical Injection Points Diagram	44	0%	$212.22	13-May-22	25-Jun-22
List		285	49.3%	$2,398.18	28-Dec-21	25-Jun-22
P12-E	Process Main Equipment List	44	60%	$334.79	20-Feb-22	13-May-22
P12-E	Process Load List	44	80%	$223.03	19-Jan-22	13-May-22
P12-E	Tie in list	44	60%	$278.91	20-Feb-22	13-May-22
P12-E	Line List	44	0%	$278.91	13-May-22	25-Jun-22
P12-E	Chemical Consumption List	44	60%	$334.55	09-Mar-22	13-May-22
P12-E	Utility Consumption List	44	80%	$334.55	28-Dec-21	13-May-22
P12-E	Emission and Effluent Summary	44	0%	$334.55	13-May-22	25-Jun-22
P12-E	Relief Load Summery	44	60%	$278.91	26-Jan-22	13-May-22
Report		299	66%	$1,669.90	17-Oct-21	13-May-22
P12-E	Flare Network Study Report	44	60%	$667.96	05-Jan-22	13-May-22
P12-E	Flare Radiation & Dispersion Study Report	44	60%	$500.97	05-Jan-22	13-May-22
P12-E	Process Simulation Report	44	80%	$500.97	17-Oct-21	02-May-22
Mechanical		506	68.23%	$19,358.87	28-Jul-21 A	05-Jul-22
Basis/Criteria		54	60%	$34.85	28-Jul-21 A	12-May-22

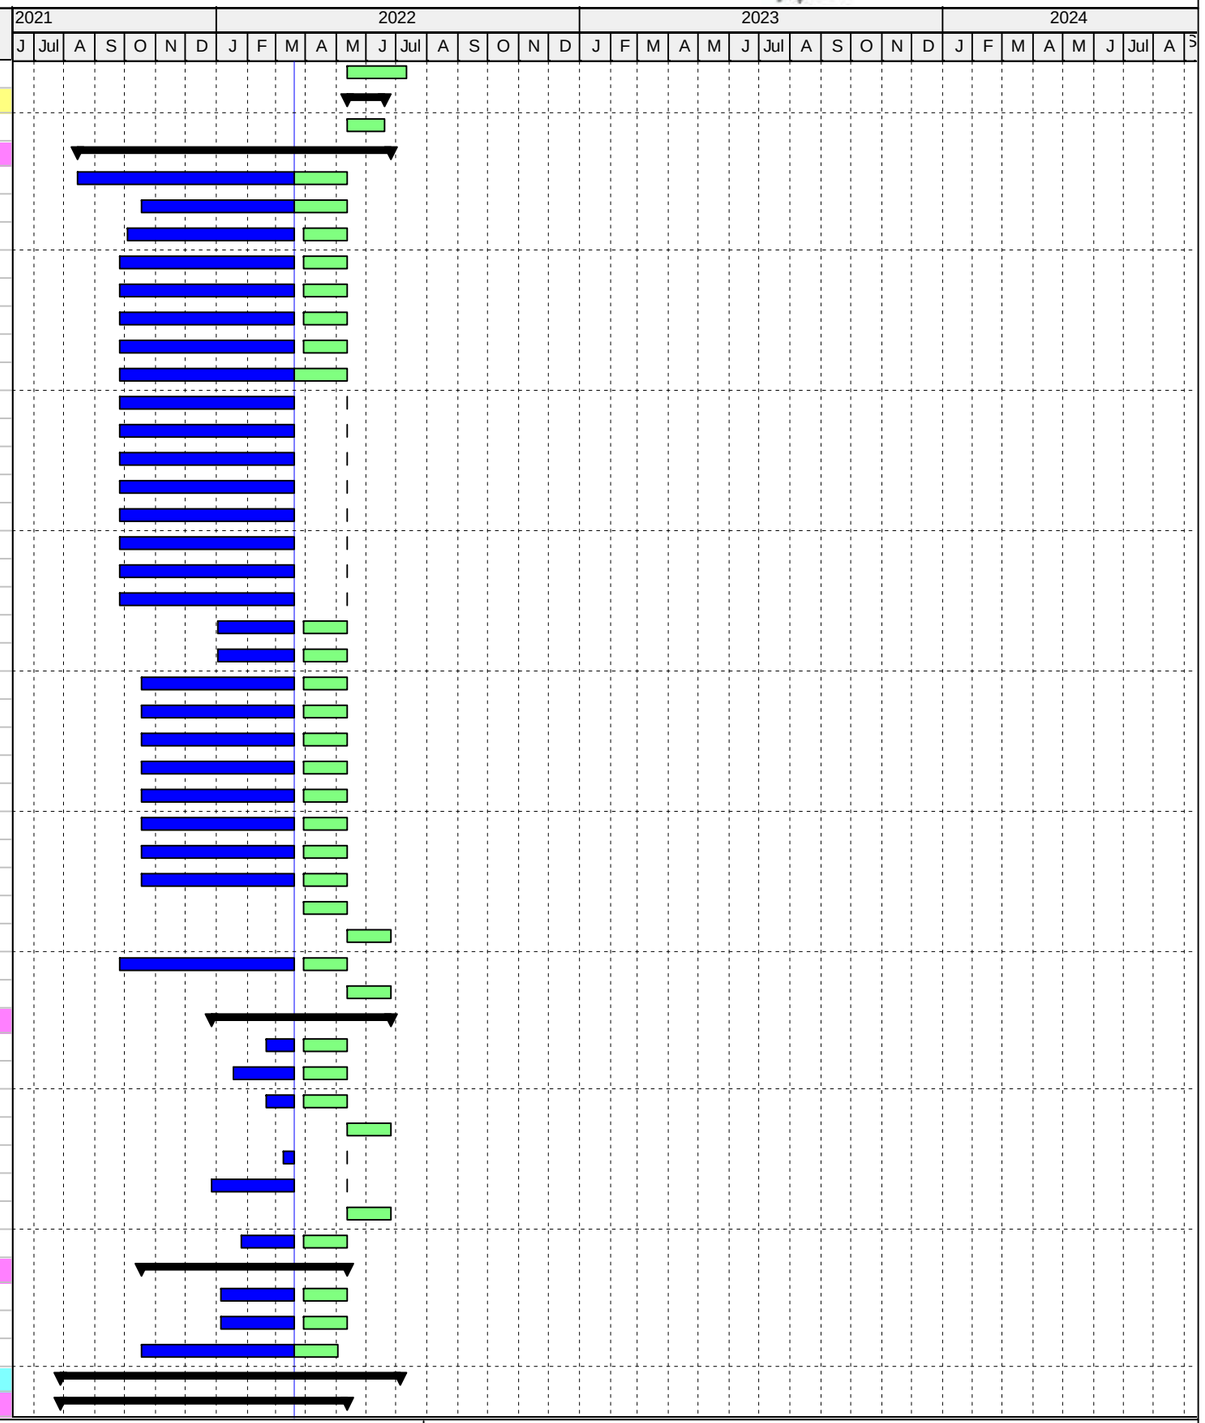


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Mechanical Design Criteria	54	60%	$34.85	28-Jul-21 A	12-May-22
Specification		104	81.88%	$5,042.99	28-Jul-21 A	26-Jun-22
Packaged Equipment		59	80%	$1,750.92	14-Aug-21	20-Mar-22
P12-	Specification For Air Compressor Package	44	100%	$350.18	14-Aug-21	20-Mar-22
P12-	Specification For Air Dryer Package	44	60%	$350.18	14-Aug-21	20-Mar-22
P12-	Specification For Chemical Injection Package	44	60%	$350.18	22-Aug-21	20-Mar-22
P12-	Specification For Nitrogen Package	44	80%	$350.18	06-Oct-21	20-Mar-22
P12-	Specification For Flare Package	59	100%	$350.18	24-Aug-21	20-Mar-22
Fixed Equipment		84	78.87%	$927.91	28-Jul-21 A	26-Jun-22
P12-	Specification For Pressure Vessels	54	60%	$26.26	28-Jul-21 A	01-Jun-22
P12-	Specification For Atmospheric Above Ground Welded Steel Ta	79	60%	$26.26	28-Jul-21 A	26-Jun-22
P12-	Specification For Air Cooled Heat Exchangers	64	60%	$437.69	14-Aug-21	22-May-22
P12-	Specification For Large Welded Low Pressure Storage Tanks	62	100%	$437.69	24-Aug-21	29-Apr-22
Rotary Equipment		59	84.45%	$2,364.15	14-Aug-21	17-May-22
P12-	Specification For Reciprocating Compressor (API 618)	44	100%	$525.55	14-Aug-21	20-Mar-22
P12-	Specification For Centrifugal Pumps For Process Services (AI	44	80%	$525.31	22-Aug-21	02-May-22
P12-	Specification For Centrifugal Pumps For General Services	44	80%	$262.66	14-Aug-21	02-May-22
P12-	Specification For Fire Water Pumps	44	80%	$262.66	22-Aug-21	02-May-22
P12-	Specification For Overhead Travelling Cranes	59	60%	$262.66	14-Aug-21	17-May-22
P12-	Specification for Control Volume Pump (API 675)	44	80%	$262.66	24-Aug-21	02-May-22
P12-	Specification For Diesel Engines	44	100%	$262.66	24-Aug-21	20-Mar-22
Data Sheets		506	63.07%	$14,139.72	12-Sep-21	05-Jul-22
Fixed Equipment		144	65.36%	$6,041.90	27-Nov-21	11-Jun-22
P12-	Mechanical Data Sheets For Inlet Gas K.O. Drum	64	80%	$350.43	07-Dec-21	11-Jun-22
P12-	Mechanical Data Sheets For 1st Stage G.C. Suction Drums	64	80%	$350.43	13-Dec-21	11-Jun-22
P12-	Mechanical Data Sheets For 1st Stage Gas Air Coolers	64	60%	$393.93	29-Dec-21	22-May-22
P12-	Mechanical Data Sheets For 2nd Stage G.C. Suction Drums	64	80%	$350.43	13-Dec-21	11-Jun-22
P12-	Mechanical Data Sheets For 2nd Stage Gas Air Coolers	64	60%	$393.93	29-Dec-21	22-May-22
P12-	Mechanical Data Sheets For Discharge Gas K.O. Drum	64	80%	$349.83	27-Dec-21	11-Jun-22
P12-	Mechanical Data Sheets For Diesel Oil Drum	64	60%	$349.83	13-Dec-21	11-Jun-22
P12-	Mechanical Data Sheets For Instrument Air Receiver	64	60%	$349.83	07-Dec-21	11-Jun-22
P12-	Mechanical Data Sheets For Nitrogen Receiver	64	80%	$349.83	27-Nov-21	11-Jun-22
P12-	Mechanical Data Sheets For Close Drain Drum	64	60%	$350.43	13-Dec-21	11-Jun-22
P12-	Mechanical Data Sheets For Elevated Potable Water Tank	64	80%	$263.43	27-Nov-21	29-Apr-22
P12-	Mechanical Data Sheets For Flare K.O. Drum	64	60%	$350.43	03-Jan-22	11-Jun-22
P12-	Mechanical Data Sheets For Fuel Gas K.O. Drum	64	60%	$350.43	13-Dec-21	11-Jun-22
P12-	Mechanical Data Sheets For Slug Catcher	64	60%	$350.43	28-Dec-21	11-Jun-22
P12-	Mechanical Data Sheets For Degassing Vessel	84	60%	$350.43	06-Mar-22	11-Jun-22
P12-	Mechanical Data Sheets For Lean Glycol Storage Tank	64	80%	$196.97	28-Nov-21	11-Jun-22
P12-	Mechanical Data Sheets For Fire Water Storage Tank	64	0%	$196.97	09-Apr-22	11-Jun-22
P12-	Mechanical Data Sheets For Slug Storage Tank	64	60%	$196.97	14-Dec-21	22-May-22
P12-	Mechanical Data Sheets For Glycol Sump Drum	64	60%	$196.97	05-Jan-22	22-May-22
Rotary Equipment		456	72.5%	$6,128.15	27-Nov-21	05-Jul-22
P12-	Mechanical Data Sheets For Slug Pumps	54	80%	$383.01	07-Dec-21	16-Jun-22
P12-	Mechanical Data Sheets For Glycol Transfer Pumps	44	80%	$383.01	27-Nov-21	25-Jun-22
P12-	Mechanical Data Sheets For Glycol Manual Pump	54	80%	$383.01	27-Nov-21	05-Jul-22
P12-	Mechanical Data Sheets For Closed Drain Pumps	54	80%	$383.01	27-Nov-21	22-May-22
P12-	Mechanical Data Sheets For Sump Pumps	54	80%	$383.01	07-Dec-21	22-May-22
P12-	Mechanical Data Sheets For Flare KO Drum Pumps	54	80%	$383.01	27-Nov-21	22-May-22

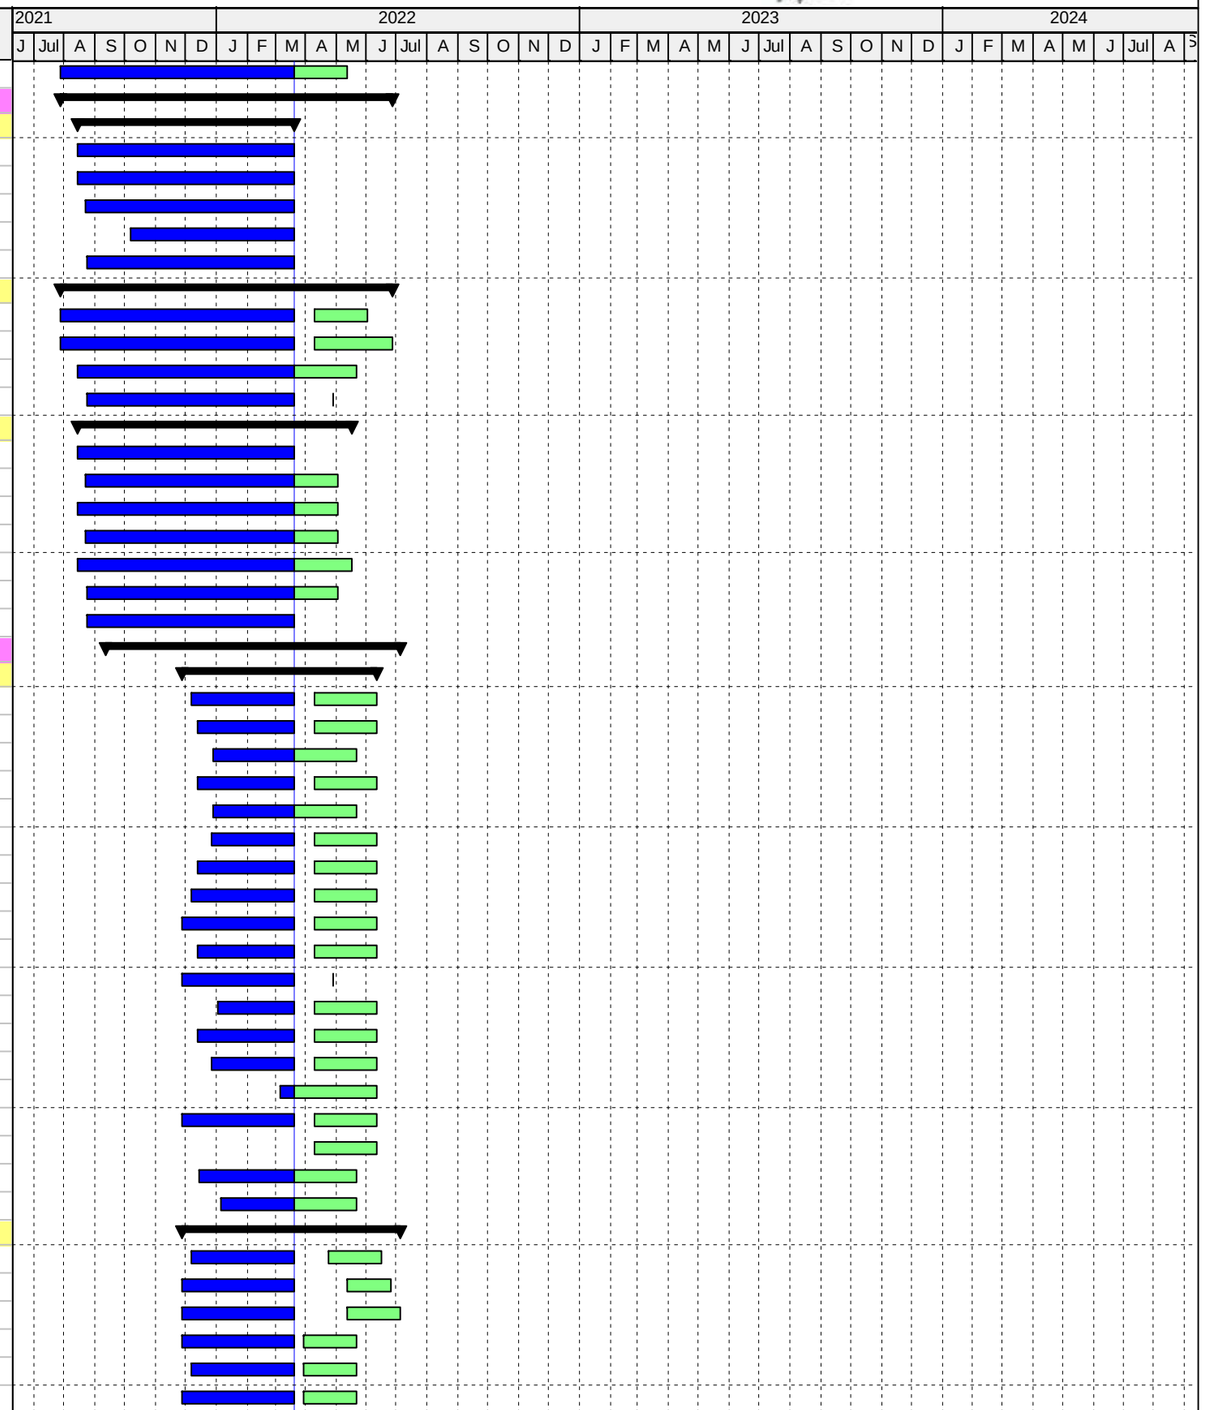


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-	Mechanical Data Sheets For Potable Water Pump	54	80%	$383.01	07-Dec-21	22-May-22
P12-	Mechanical Data Sheets For Diesel Pump	54	80%	$383.01	27-Nov-21	22-May-22
P12-	Mechanical Data Sheets For Overhead Traveling Cranes	54	60%	$766.02	13-Feb-22	20-Mar-22
P12-	Mechanical Data Sheets For Fire Water Jockey Pumps	54	60%	$383.01	21-Feb-22	13-May-22
P12-	Mechanical Data Sheets For Fire Water Main Pumps - Elect.	54	60%	$383.01	21-Feb-22	13-May-22
P12-	Mechanical Data Sheets For Fire Water Main Pumps - Diesel	54	60%	$766.02	16-Feb-22	13-May-22
P12-	Mechanical Data Sheets For Glycol Sump Pumps	54	80%	$383.01	08-Dec-21	12-May-22
P12-	Mechanical Data Sheets For Glycol Drain Pump	54	80%	$383.01	08-Dec-21	12-May-22
Packaged Equipment		276	26.67%	$1,969.66	12-Sep-21	22-May-22
P12-	Mechanical Data Sheets For Gas Compressors Packages	49	80%	$656.69	12-Sep-21	13-May-22
P12-	Mechanical Data Sheets For Chemical Injection Packages	56	0%	$656.49	20-Mar-22	15-May-22
P12-	Mechanical Data Sheets For Overhead Traveling Cranes	64	0%	$656.49	20-Mar-22	22-May-22
Drawing/Diagram		34	100%	$141.32	28-Jul-21 A	09-Apr-22
P12-E	Standard Detail Drawing For Pressure Vessels and Heat Excl	14	100%	$70.66	28-Jul-21 A	09-Apr-22
P12-E	Standard Detail Drawing For Storage Tanks	14	100%	$70.66	28-Jul-21 A	09-Apr-22
HVAC/Plumbing		402	3.06%	$7,743.55	24-Jul-21 A	29-May-23
Basis/Criteria		64	100%	$53.43	24-Jul-21 A	14-May-22
P12-E	HVAC & Plumbing Design Criteria	64	100%	$53.43	24-Jul-21 A	14-May-22
Specification		64	100%	$85.18	24-Jul-21 A	27-Mar-22
P12-E	Specification For HVAC Equipment	64	100%	$53.24	24-Jul-21 A	27-Mar-22
P12-E	Specification For Duct Work & Pipe Work	64	100%	$31.94	24-Jul-21 A	27-Mar-22
Calculation		63	0%	$1,281.56	13-May-22	14-Jul-22
P12-E	HVAC Calculation Note For Control Building	62	0%	$640.78	14-May-22	14-Jul-22
P12-E	HVAC Calculation Note For Extension of Existing Elect. Buildir	62	0%	$640.78	13-May-22	13-Jul-22
Data Sheets		127	0%	$854.11	23-Jan-23	29-May-23
P12-E	Data Sheets For Main HVAC Equipment of Control Building	64	0%	$427.06	23-Jan-23	27-Mar-23
P12-E	Data Sheets For Main HVAC Equipment of Extension of Existi	64	0%	$427.06	27-Mar-23	29-May-23
Drawing/Diagram		332	2.13%	$4,614.38	24-Jul-21 A	26-Mar-23
P12-E	Standard Drawing For HVAC & Plumbing	14	100%	$53.53	24-Jul-21 A	30-Mar-22
P12-E	Symbol & Legend For HVAC & Plumbing	48	60%	$74.75	22-Aug-21	16-May-22
P12-E	Plumbing & Sewage Piping Layout For Control Building	64	0%	$320.70	14-May-22	16-Jul-22
P12-E	HVAC Flow Diagram For Control Building	64	0%	$427.29	15-Jul-22	16-Sep-22
P12-E	HVAC Room Layout & Section For Control Building	64	0%	$320.24	20-Nov-22	22-Jan-23
P12-E	HVAC System Duct Plan For Control Building	64	0%	$427.29	17-Sep-22	19-Nov-22
P12-E	HVAC System Roof Layout For Control Building	64	0%	$320.24	20-Nov-22	22-Jan-23
P12-E	HVAC I&C Diagram For Control Building	64	0%	$427.29	17-Sep-22	19-Nov-22
P12-E	Plumbing & Sewage Piping Layout For Extension of Existing E	64	0%	$320.24	13-May-22	15-Jul-22
P12-E	HVAC Flow Diagram For Extension of Existing Elect. Building	64	0%	$427.29	14-Jul-22	15-Sep-22
P12-E	HVAC System Layout & Section For Extension of Existing Elec	64	0%	$320.70	19-Nov-22	21-Jan-23
P12-E	HVAC System Duct Plan For Extension of Existing Elect. Build	64	0%	$427.29	16-Sep-22	18-Nov-22
P12-E	HVAC System Roof Layout For Extension of Existing Elect. Bu	64	0%	$320.24	22-Jan-23	26-Mar-23
P12-E	HVAC I&C Diagram For Extension of Existing Elect. Building	64	0%	$427.29	16-Sep-22	18-Nov-22
MTO		70	0%	$854.89	23-Jan-23	02-Apr-23
P12-E	MTO For HVAC & Plumbing For Control Building	7	0%	$427.44	23-Jan-23	29-Jan-23
P12-E	MTO For HVAC & Plumbing For Extension of Existing Elect. E	7	0%	$427.44	27-Mar-23	02-Apr-23
Piping		443	14.56%	$73,563.72	24-Jul-21 A	05-Jun-23
Basis/Criteria		39	100%	$14.71	24-Jul-21 A	20-Mar-22
P12-E	Piping Design Criteria	39	100%	$14.71	24-Jul-21 A	20-Mar-22
Specification		359	79.86%	$5,134.75	24-Jul-21 A	13-May-22

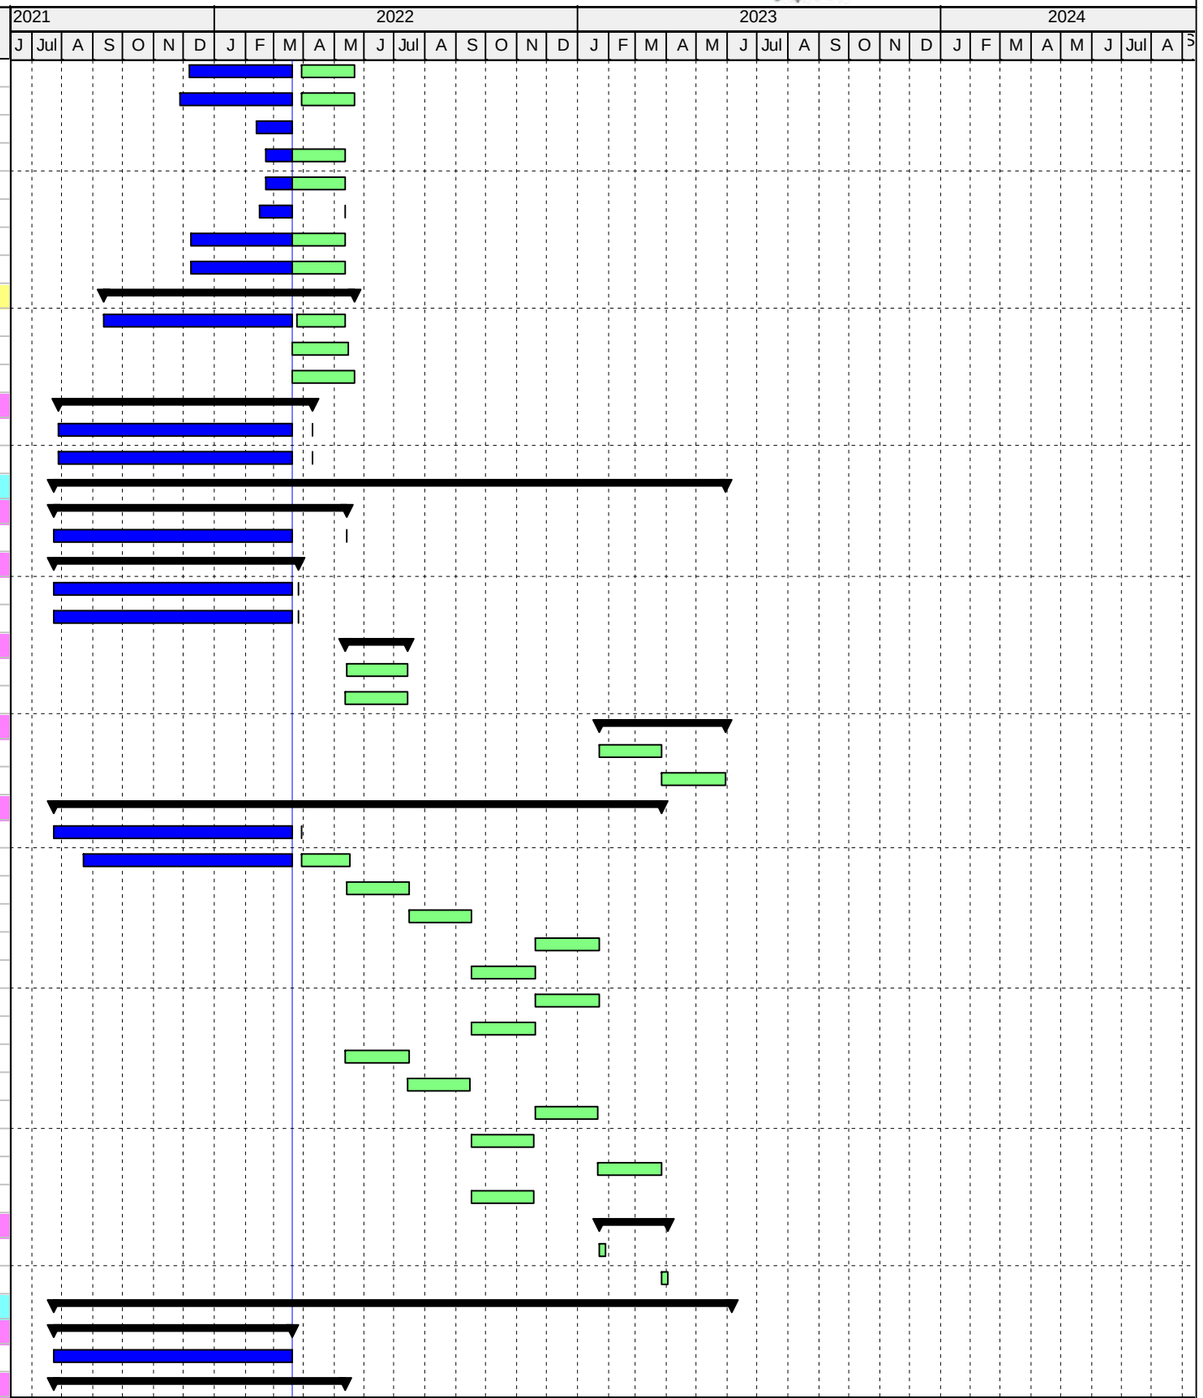


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Specification For Color Coding and Marking	39	60%	$13.35	09-Aug-21	01-May-22
P12-E	Specification For Transportation, Handling, Storage of pipes	39	80%	$14.38	12-Dec-21	01-May-22
P12-E	Specification For the Design of Piping in Mechanical Packages	39	60%	$19.51	09-Aug-21	01-May-22
P12-E	Specification For Metallic Pipes	39	80%	$13.35	24-Jul-21 A	01-May-22
P12-E	Specification For Fittings, Flanges, Gaskets and Bolts	39	100%	$13.35	24-Jul-21 A	24-Mar-22
P12-E	Specification For Painting	39	100%	$13.35	24-Jul-21 A	27-Mar-22
P12-E	Specification For Lining (Internal Protection of Equipment by F	39	60%	$15.92	09-Aug-21	04-May-22
P12-E	Specification For Material Requirements in Sour service	39	60%	$13.35	09-Aug-21	04-May-22
P12-E	Specification For Manual Valves	39	60%	$13.35	09-Aug-21	04-May-22
P12-E	Specification For Plant Piping Systems Pressure Testing	39	60%	$13.35	09-Aug-21	04-May-22
P12-E	Specification For Welding of Plant Piping System	39	60%	$13.35	09-Aug-21	04-May-22
P12-E	Specification For Flexibility Analysis	39	60%	$14.38	09-Aug-21	04-May-22
P12-E	Specification For Coating Of Underground Piping	39	100%	$22.59	24-Jul-21 A	30-Mar-22
P12-E	Specification For Pipe Support	39	60%	$17.46	09-Aug-21	07-May-22
P12-E	Specification For Piping Construction, Fabrication & Erection	39	60%	$22.59	09-Aug-21	07-May-22
P12-E	Specification For Piping Design & Plant Layout	39	60%	$39.54	09-Aug-21	07-May-22
P12-E	Specification For HDPE Pipes	39	100%	$59.05	24-Aug-21	20-Mar-22
P12-E	Specification For Insulation	39	100%	$39.54	24-Aug-21	30-Mar-22
P12-E	Piping Material Specification	54	80%	$4,749.64	06-Dec-21	13-May-22
P12-E	Specification For Piping Cleaning and Flushing	39	100%	$13.35	24-Aug-21	30-Mar-22
Procedure/Plan		39	100%	$14.71	24-Jul-21 A	03-Apr-22
P12-E	3D-Model (PDMS) Review Procedure	39	100%	$14.71	24-Jul-21 A	03-Apr-22
Data Sheets		130	0%	$4,509.46	26-Nov-22	04-Apr-23
P12-E	Data Sheets For Strainers	39	0%	$232.24	26-Nov-22	03-Jan-23
P12-E	Data Sheets For Manual valves	39	0%	$2,341.76	26-Nov-22	03-Jan-23
P12-E	Data Sheets and MTO For Piping Special Items	39	0%	$464.47	26-Nov-22	03-Jan-23
P12-E	Data Sheets For Special Pipe Supports	39	0%	$774.27	26-Nov-22	03-Jan-23
P12-E	Data Sheets For Piping Insulation Joints	39	0%	$232.24	26-Nov-22	03-Jan-23
P12-E	Data Sheets For Expansion Joints	36	0%	$464.47	28-Feb-23	04-Apr-23
Drawing/Diagram		443	20.28%	$17,699.43	12-Sep-21	05-Jun-23
P12-E	Unit Plot Plan Drawing	49	80%	$4,486.81	12-Sep-21	13-May-22
P12-E	Standard Pipe Support Drawings	55	0%	$746.92	20-Mar-22	13-May-22
P12-E	Piping Assembly Drawing	54	0%	$1,495.60	14-Aug-22	06-Oct-22
P12-E	Piping Key Plan	44	0%	$746.92	26-Nov-22	08-Jan-23
P12-E	A/G Piping Plan	54	0%	$1,495.60	28-Feb-23	22-Apr-23
P12-E	U/G Piping Plan	49	0%	$745.15	26-Nov-22	13-Jan-23
P12-E	A/G Piping Isometric	44	0%	$746.92	23-Apr-23	05-Jun-23
P12-E	U/G Piping Isometric	44	0%	$746.92	14-Jan-23	26-Feb-23
P12-E	Overall Plot Plan Drawing	44	0%	$2,991.20	13-May-22	25-Jun-22
P12-E	Special Pipe Support Drawings	44	0%	$1,315.07	15-Jan-23	27-Feb-23
P12-E	Piping Hydrostatic Test Diagram - GCS	44	0%	$987.63	20-Mar-22	02-May-22
P12-E	Material flow Diagram	39	0%	$1,194.71	13-May-22	20-Jun-22
List		291	0%	$3,222.09	13-May-22	27-Feb-23
P12-E	Critical Line List	39	0%	$1,611.05	26-Jun-22	03-Aug-22
P12-E	Pipe Support List	44	0%	$805.52	15-Jan-23	27-Feb-23
P12-E	Piping Tie-In Schedule List	39	0%	$805.52	13-May-22	20-Jun-22
Report		247	7.38%	$40,555.68	06-Dec-21	27-Feb-23
P12-E	Piping Corrosion Study & Material Selection Report	44	60%	$2,417.12	06-Dec-21	13-May-22

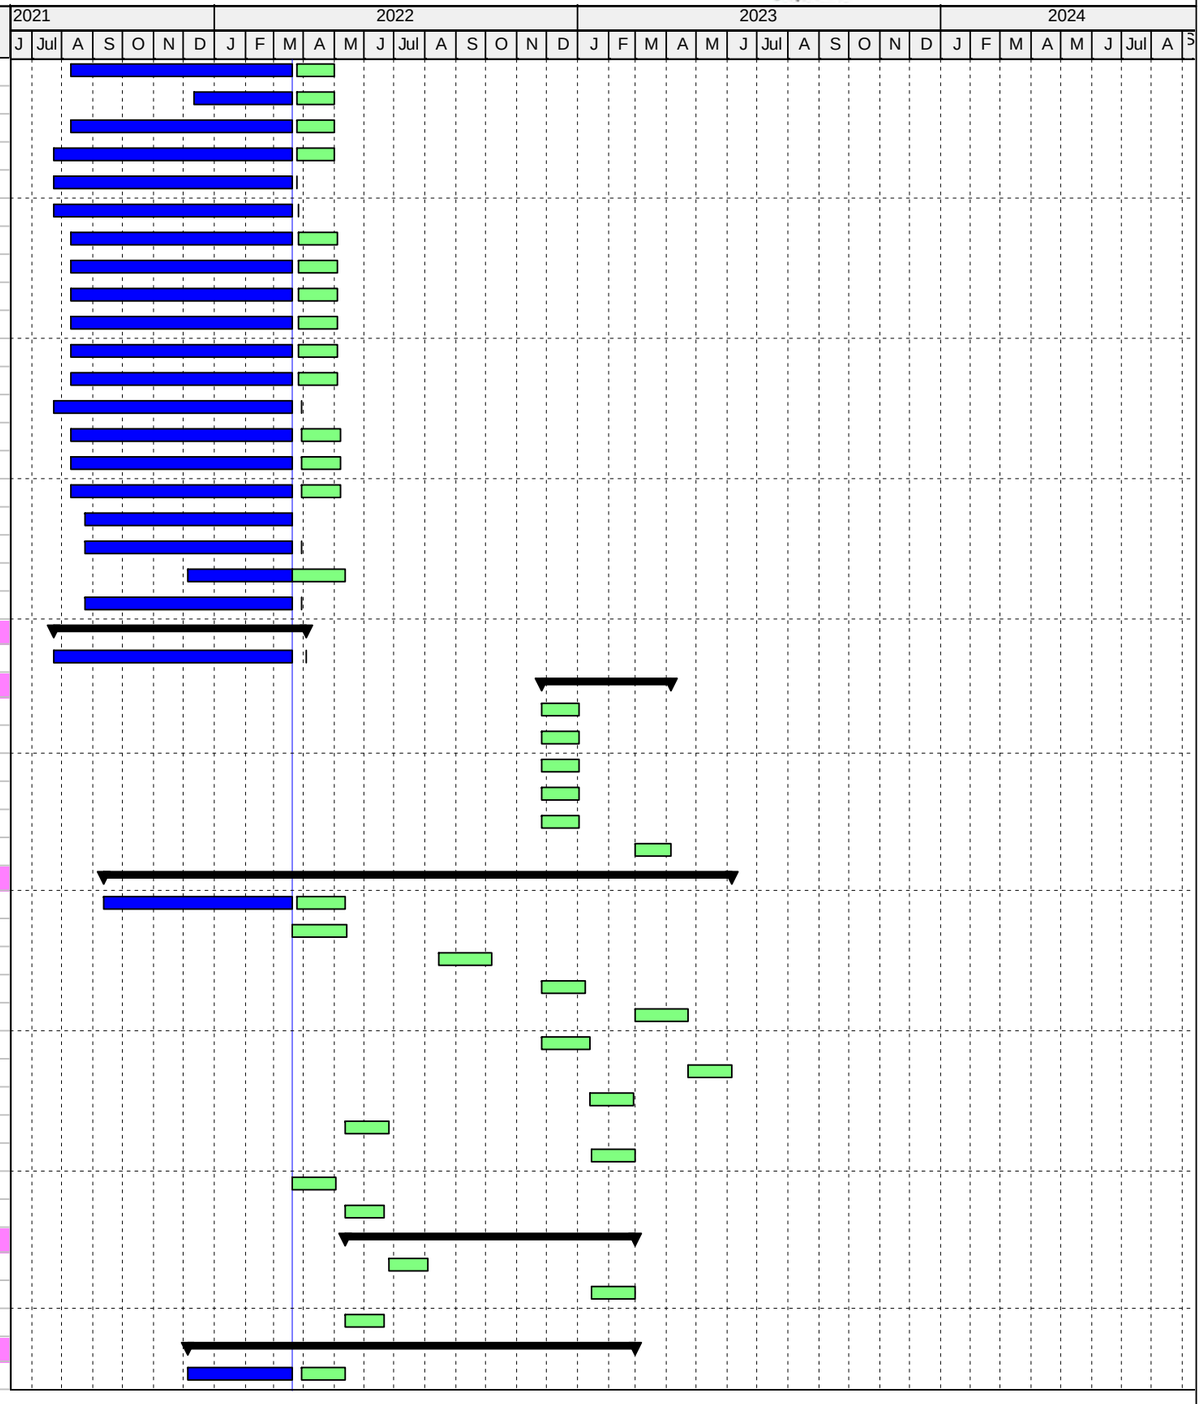


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Stress Analysis Calculations Report	44	0%	$8,046.25	15-Jan-23	27-Feb-23
P12-E	PDMS Model Review Report (30%)	65	0%	$8,046.25	26-Jun-22	29-Aug-22
P12-E	PDMS Model Review Report (60%)	50	0%	$12,069.37	07-Oct-22	25-Nov-22
P12-E	PDMS Model Review Report (90%)	50	0%	$8,046.25	26-Nov-22	14-Jan-23
P12-E	Wall Thickness Calculation Report	44	80%	$1,930.45	06-Dec-21	13-May-22
MTO		7	0%	$2,412.89	15-Jan-23	21-Jan-23
P12-E	MTO For Pipes	7	0%	$268.31	15-Jan-23	21-Jan-23
P12-E	MTO For Fittings	7	0%	$268.07	15-Jan-23	21-Jan-23
P12-E	MTO For Flanges	7	0%	$268.07	15-Jan-23	21-Jan-23
P12-E	MTO For Manual Valves	7	0%	$268.07	15-Jan-23	21-Jan-23
P12-E	MTO For Gaskets	7	0%	$268.07	15-Jan-23	21-Jan-23
P12-E	MTO For Bolt & Nuts	7	0%	$268.07	15-Jan-23	21-Jan-23
P12-E	MTO For Insulation	7	0%	$268.07	15-Jan-23	21-Jan-23
P12-E	MTO For Painting	7	0%	$268.07	15-Jan-23	21-Jan-23
P12-E	MTO For Coating of Underground Piping	7	0%	$268.07	15-Jan-23	21-Jan-23
Control & Instrumentation		593	21.09%	$32,716.49	24-Jul-21 A	13-Jan-23
Basis/Criteria		42	70%	$1,361.01	30-Aug-21	03-May-22
P12-E	Fire & Gas Detection Design Criteria	38	80%	$680.50	30-Aug-21	03-May-22
P12-E	Instrument & Control System Design Criteria	38	60%	$680.50	03-Jan-22	29-Apr-22
Specification		46	76.78%	$631.43	24-Jul-21 A	04-May-22
P12-E	Specification For Instrumentation	39	100%	$20.52	26-Jul-21 A	23-Mar-22
P12-E	Specification For Control System	39	80%	$54.30	28-Jul-21 A	30-Apr-22
P12-E	Specification For ESD System	39	80%	$54.30	28-Jul-21 A	30-Apr-22
P12-E	Specification For Instrument and Control of Package Unit Sys	39	60%	$40.73	04-Aug-21	30-Apr-22
P12-E	Specification For Control Valves	39	80%	$54.30	24-Jul-21 A	30-Apr-22
P12-E	Specification For On-off /Shut Down Valves(ESDV/MOV)	39	80%	$54.30	24-Jul-21 A	30-Apr-22
P12-E	Specification For Pressure Safety Valves(PSV)	39	100%	$54.30	24-Jul-21 A	27-Mar-22
P12-E	Specification For Fire & Gas Sensor and Devices	39	80%	$54.30	26-Jul-21 A	04-May-22
P12-E	Specification For Instrument/F&G Cables	39	60%	$54.30	04-Aug-21	04-May-22
P12-E	Specification For Control Panels and System Cabinets	39	60%	$54.30	24-Jul-21 A	04-May-22
P12-E	Specification For Fire & Gas System	39	100%	$54.30	28-Jul-21 A	20-Mar-22
P12-E	Specification For CCTV	37	60%	$81.45	25-Sep-21	25-Apr-22
Data Sheets		196	3.4%	$9,137.72	13-Oct-21	13-Aug-22
P12-E	Data Sheets For Pressure & Diff. Pressure Gauge	39	0%	$258.60	01-Jul-22	08-Aug-22
P12-E	Data Sheets For Temperature Gauge	39	0%	$258.60	01-Jul-22	08-Aug-22
P12-E	Data Sheets For Level Gauges	39	0%	$518.11	01-Jul-22	08-Aug-22
P12-E	Data Sheets For Pressure/Diff. Pressure Transmitter	39	0%	$258.60	01-Jul-22	08-Aug-22
P12-E	Data Sheets For Temperature Transmitter/Switch	39	0%	$258.60	01-Jul-22	08-Aug-22
P12-E	Data Sheets For Displacer Level Transmitter	39	0%	$518.11	01-Jul-22	08-Aug-22
P12-E	Data Sheets For Pressure/ Differential Pressure Switch	39	0%	$518.11	23-Mar-22	30-Apr-22
P12-E	Data Sheets For Level Switch	39	0%	$518.11	23-Mar-22	30-Apr-22
P12-E	Data Sheets For Pressure & Safety Relief Valves	44	0%	$431.30	01-Jul-22	13-Aug-22
P12-E	Data Sheets For ON/OFF & Shutdown Valves	44	0%	$431.30	01-Jul-22	13-Aug-22
P12-E	Data Sheets For Control/Regulator Valves	44	0%	$690.81	01-Jul-22	13-Aug-22
P12-E	Data Sheets For Diff. Pressure Flow Transmitter	40	0%	$518.11	01-Jul-22	09-Aug-22
P12-E	Data Sheets For Orifice Plate/Restriction Orifice	40	0%	$690.81	01-Jul-22	09-Aug-22
P12-E	Data Sheets For Corrosion Coupon/ Probe	40	0%	$257.68	01-Jul-22	09-Aug-22
P12-E	Data Sheets For F&G Detectors & Equipment	44	0%	$431.30	13-May-22	25-Jun-22

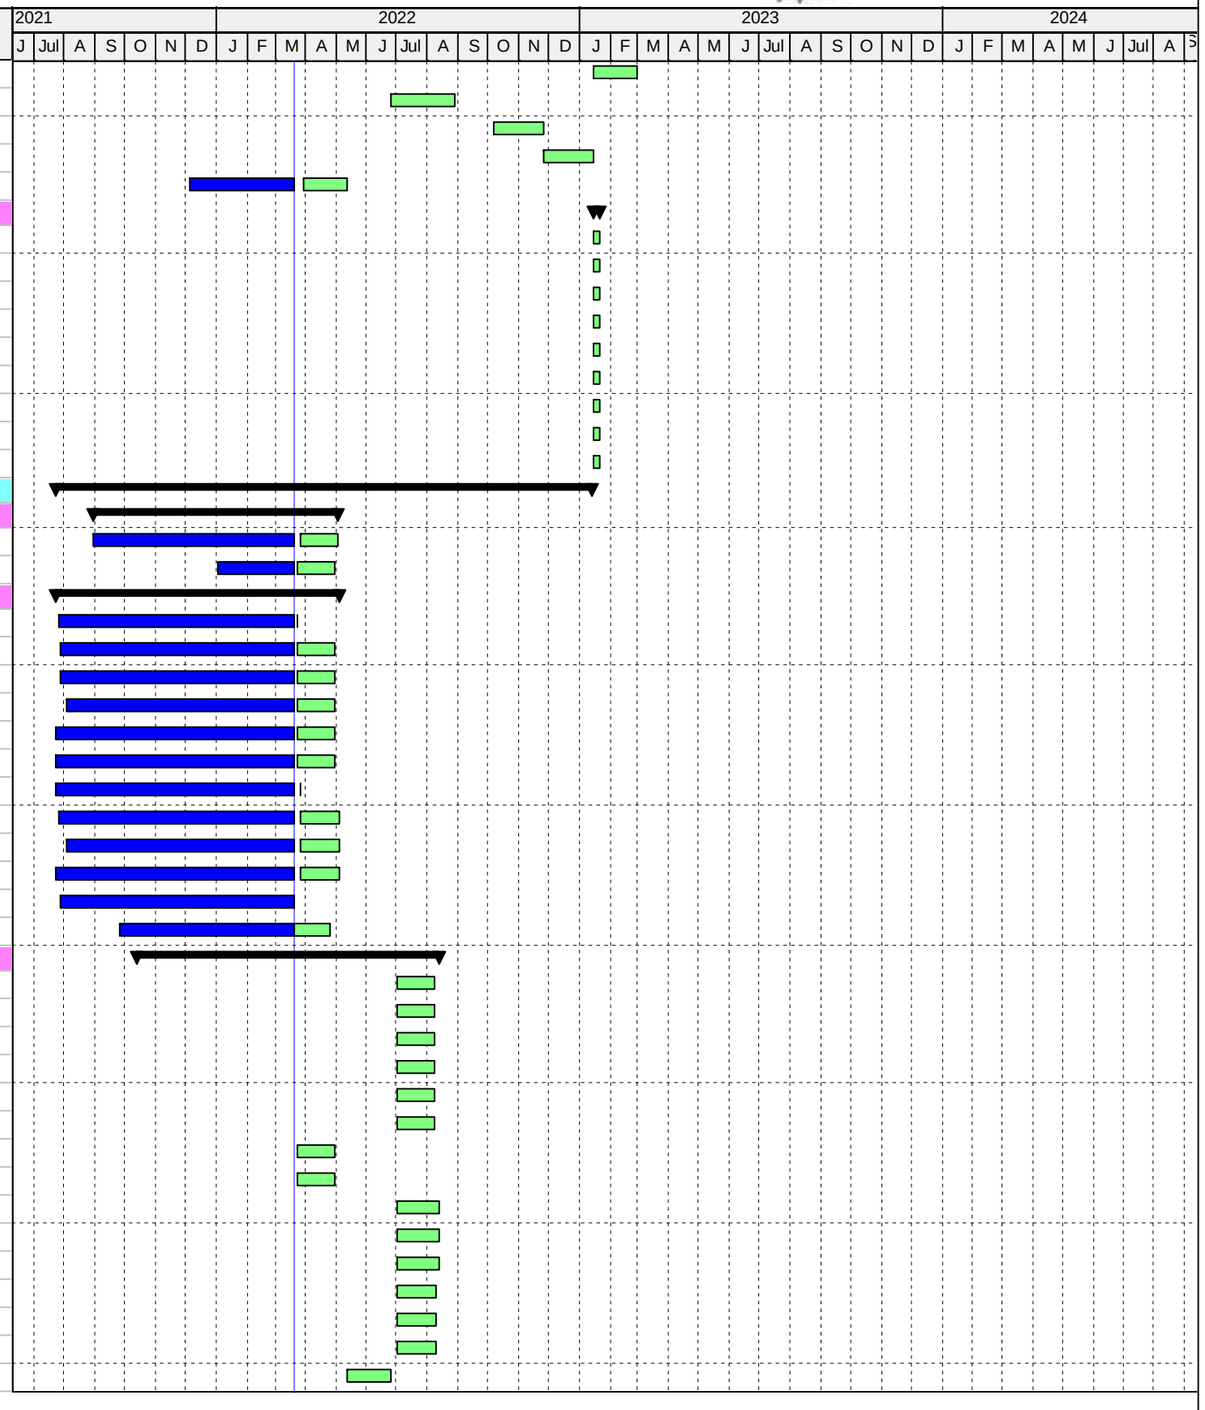


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Data Sheets For ESD Console/F&G Matrix Panel	39	0%	$518.11	13-May-22	20-Jun-22
P12-E	Data Sheets For Rotameter	39	0%	$518.11	01-Jul-22	08-Aug-22
P12-E	Data Sheets For Diff. Pressure Type Level Transmitter	40	0%	$518.11	01-Jul-22	09-Aug-22
P12-E	Data Sheets For CCTV	49	60%	$518.11	13-Oct-21	28-Jun-22
P12-E	Data Sheets For IRP Panel	36	0%	$507.14	21-May-22	25-Jun-22
Drawing/Diagram		534	15.17%	$14,195.69	30-Aug-21	13-Jan-23
P12-E	Typical Instrument Installation Drawing	35	100%	$271.14	09-Mar-22	21-Apr-22
P12-E	Control/ESD/F&G System Block Diagram Configuration	39	80%	$326.50	30-Aug-21	30-Apr-22
P12-E	Instrument Earthing Typical Diagram	35	100%	$109.31	29-Dec-21	30-Apr-22
P12-E	Instrument Hook-up Diagram	44	0%	$272.56	01-Jul-22	13-Aug-22
P12-E	ESD Level Hierarchy	42	0%	$109.31	13-May-22	23-Jun-22
P12-E	ESD System Loop Diagram	49	0%	$817.67	13-May-22	30-Jun-22
P12-E	Control System Loop Diagram	49	0%	$817.67	13-May-22	30-Jun-22
P12-E	F&G System Loop Diagram	49	0%	$817.67	13-May-22	30-Jun-22
P12-E	Instrument Air Piping and Air Header Diagram	49	0%	$435.81	26-Nov-22	13-Jan-23
P12-E	Instrument & F&G Junction Box Termination Diagram	49	60%	$326.50	13-Feb-22	13-May-22
P12-E	F&G Cause and Effect Diagram For Process Area	42	0%	$272.56	13-May-22	23-Jun-22
P12-E	F&G Cause and Effect Diagram For Buildings	42	0%	$272.56	13-May-22	23-Jun-22
P12-E	Control System Logic Diagram	49	0%	$217.19	13-May-22	30-Jun-22
P12-E	ESD Logic Diagram	49	0%	$545.11	13-May-22	30-Jun-22
P12-E	Control Room Layout & Arrangement Drawing	39	60%	$381.86	02-Feb-22	13-May-22
P12-E	Control Room Cable Route Layout	49	0%	$217.19	13-May-22	30-Jun-22
P12-E	Instrument Location Layout	49	0%	$435.81	26-Nov-22	13-Jan-23
P12-E	Instrument/F&G Cable Trench/Route Layout Drawing	49	60%	$545.11	25-Jan-22	13-May-22
P12-E	F&G Location Layout For Process Area	42	60%	$381.86	07-Feb-22	13-May-22
P12-E	F&G Location Layout For Buildings	42	0%	$381.86	02-Jul-22	12-Aug-22
P12-E	Block Diagram For CCTV	59	0%	$635.97	30-Apr-22	27-Jun-22
P12-E	Block Diagram For CCTV in Binak DU	59	0%	$635.97	30-Apr-22	27-Jun-22
P12-E	CCTV Equipment Layout For Area	59	0%	$476.98	13-May-22	10-Jul-22
P12-E	CCTV Equipment Layout For Desalting Unit Area	59	0%	$476.98	28-Jun-22	25-Aug-22
P12-E	Typical Instrument Installation Drawing	35	100%	$476.98	09-Mar-22	01-Jul-22
P12-E	CCTV Typical Installation Details & Notes	39	100%	$53.94	25-Sep-21	01-Jan-23
P12-E	Block Diagram For CCTV	38	0%	$809.15	13-May-22	19-Jun-22
P12-E	Block Diagram For CCTV in Binak DU	38	0%	$809.15	13-May-22	19-Jun-22
P12-E	CCTV Equipment Layout For Area	59	0%	$807.73	28-Jun-22	25-Aug-22
P12-E	CCTV Equipment Layout For Desalting Unit Area	59	0%	$807.73	28-Jun-22	25-Aug-22
P12-E	Wiring Diagram For Interposing Relay Panel (IRP)	39	0%	$249.84	11-Nov-22	19-Dec-22
List		542	46.44%	$4,959.82	25-Jan-22	28-Oct-22
P12-E	Instrument Index	49	0%	$255.93	13-May-22	30-Jun-22
P12-E	I/O List For Control System	49	60%	$682.47	25-Jan-22	13-May-22
P12-E	I/O List For ESD Systems	49	60%	$682.47	25-Jan-22	13-May-22
P12-E	I/O List For F&G Systems	49	60%	$682.47	07-Feb-22	13-May-22
P12-E	Panels & Junction Box List	42	60%	$170.62	13-Feb-22	13-May-22
P12-E	Set Point & Alarm List	44	0%	$255.93	01-Jul-22	13-Aug-22
P12-E	I&C Power Consumption Summary	42	60%	$170.62	23-Feb-22	13-May-22
P12-E	F&G Detector List	42	60%	$597.16	07-Feb-22	12-Aug-22
P12-E	Instrument /F&G Cable List	49	60%	$853.09	13-Feb-22	13-May-22
P12-E	Cable Schedule For CCTV	64	0%	$304.53	26-Aug-22	28-Oct-22

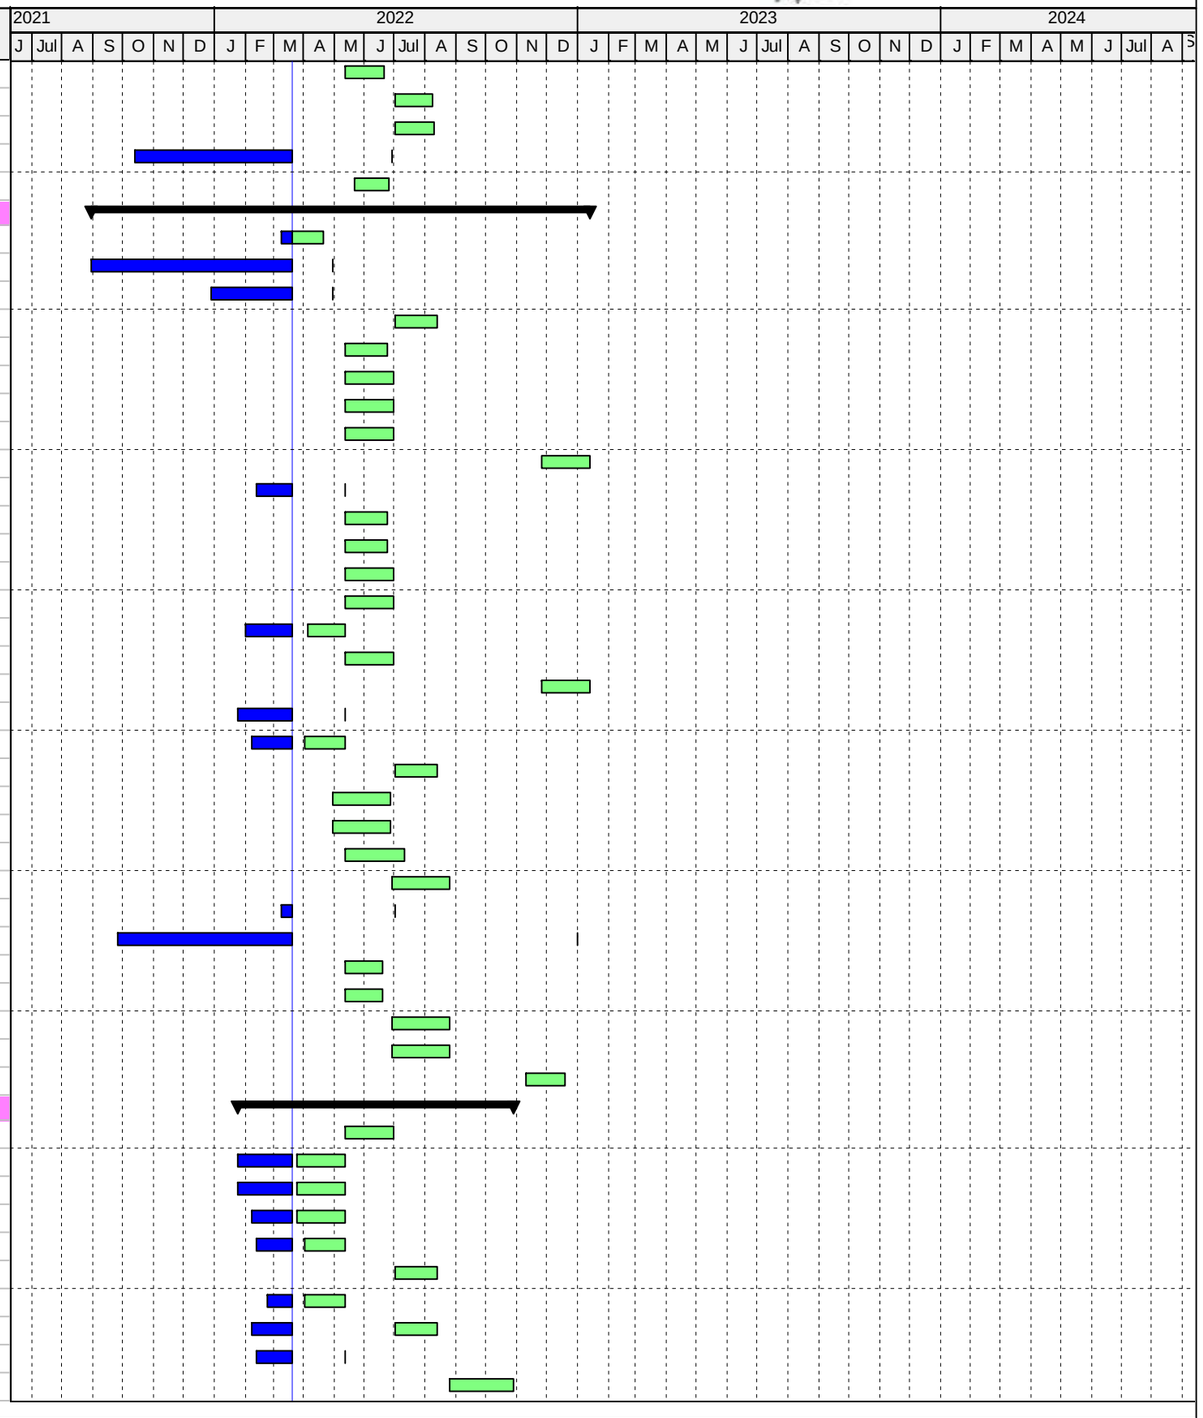


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Cable Schedule For CCTV in Binak DU Area	64	0%	$304.53	12-Jul-22	13-Sep-22
MTO		204	28.58%	$2,430.84	12-Dec-21	02-Dec-22
P12-E	MTO for Bulk Item and Installation Accessories	7	0%	$347.12	01-Jul-22	07-Jul-22
P12-E	MTO For Instrument/F&G Cable	7	0%	$347.12	13-May-22	19-May-22
P12-E	MTO For Instrument/F&G Junction box and Gland	7	0%	$347.12	13-May-22	19-May-22
P12-E	MTO For Instrument Tube and Fitting	7	0%	$347.37	14-Aug-22	20-Aug-22
P12-E	MTO For Instrument Cable Tray/Ladder	7	0%	$347.37	26-Nov-22	02-Dec-22
P12-E	MTO For CCTV	7	100%	$347.37	12-Dec-21	28-Jun-22
P12-E	MTO For CCTV in Binak DU Area	7	100%	$347.37	13-Dec-21	28-Jun-22
Safety & Fire Fighting		536	55.42%	$15,487.10	24-Jul-21 A	08-Aug-22
Basis/Criteria		44	60%	$837.85	14-Sep-21	19-Apr-22
P12-E	Active Fire Protection and Safety Concept	44	60%	$837.85	14-Sep-21	19-Apr-22
Specification		47	92.5%	$2,008.68	24-Jul-21 A	06-May-22
P12-E	Specification For Fire Fighting Equipment	44	100%	$251.08	29-Aug-21	24-Mar-22
P12-E	Specification For Hazardous Area Classification	44	100%	$251.08	24-Jul-21 A	24-Mar-22
P12-E	Specification For Fire Water System	44	80%	$251.08	24-Jul-21 A	24-Mar-22
P12-E	Specification For Environmental Job	44	60%	$251.08	11-Aug-21	06-May-22
P12-E	Specification For Total Flooding System	44	100%	$251.08	24-Jul-21 A	27-Mar-22
P12-E	Specification For Safety Equipment	44	100%	$251.08	29-Aug-21	27-Mar-22
P12-E	Specification For passive Fire protection	44	100%	$251.08	24-Jul-21 A	27-Mar-22
P12-E	Specification For Safety Signs	44	100%	$251.08	24-Jul-21 A	27-Mar-22
Calculation		360	49.09%	$1,841.42	13-Dec-21	25-Jun-22
P12-E	Calculation Note For Total Flooding Demand For Extension of	44	100%	$502.15	16-Jan-22	13-May-22
P12-E	Calculation Note For Fire Water Demand	44	80%	$502.15	13-Dec-21	13-May-22
P12-E	Fire Water Hydraulic Calculation Note	44	0%	$837.11	13-May-22	25-Jun-22
Data Sheets		536	24%	$1,925.05	20-Sep-21	08-Aug-22
P12-E	Data Sheets For Safety Equipment	44	0%	$385.01	27-Mar-22	09-May-22
P12-E	Data Sheets For Fire Fighting Equipment	44	0%	$385.01	24-Mar-22	06-May-22
P12-E	Data Sheets For Deluge valves	44	60%	$385.01	16-Jan-22	25-Jun-22
P12-E	Data Sheets For Water Spray Nozzles	44	0%	$385.01	26-Jun-22	08-Aug-22
P12-E	Data Sheets For Safety Sign	44	60%	$385.01	20-Sep-21	25-Jun-22
Drawing/Diagram		404	56.97%	$5,525.80	29-Aug-21	25-Jun-22
P12-E	Typical Installation Detail for Safety & Fire Fighting Equipment	14	100%	$670.28	29-Dec-21	27-Mar-22
P12-E	Symbol & Legend For Safety & Firefighting Systems	44	100%	$669.73	29-Aug-21	27-Mar-22
P12-E	PFD - Fire Water System	44	60%	$334.86	13-Dec-21	13-May-22
P12-E	P&ID - Fire Water Network	44	60%	$502.29	12-Feb-22	13-May-22
P12-E	P&ID - Total Flooding System For Extension of Existing Elect.	44	60%	$502.29	16-Jan-22	13-May-22
P12-E	Fire Water Network Layout	44	60%	$502.29	13-Dec-21	13-May-22
P12-E	Hazardous Area Classification Layout	44	60%	$669.73	12-Mar-22	13-May-22
P12-E	Fire Proofing Zone Layout	44	0%	$502.29	13-May-22	25-Jun-22
P12-E	Safety & Fire Fighting Equipment Location Layout	44	60%	$502.29	12-Feb-22	13-May-22
P12-E	Escape Route & Safety Sign Layout	44	0%	$669.73	13-May-22	25-Jun-22
Report		44	60%	$2,512.01	21-Nov-21	13-May-22
P12-E	Consequence Modeling Report	44	60%	$2,512.01	21-Nov-21	13-May-22
List		109	34.28%	$585.41	23-Feb-22	25-Jun-22
P12-E	Hazard Source List	44	60%	$334.50	23-Feb-22	12-May-22
P12-E	Fire Fighting Line List	44	0%	$250.91	13-May-22	25-Jun-22
MTO		51	0%	$250.89	13-May-22	02-Jul-22
P12-E	MTO For Safety & Fire Fighting Equipment	7	0%	$125.45	13-May-22	19-May-22

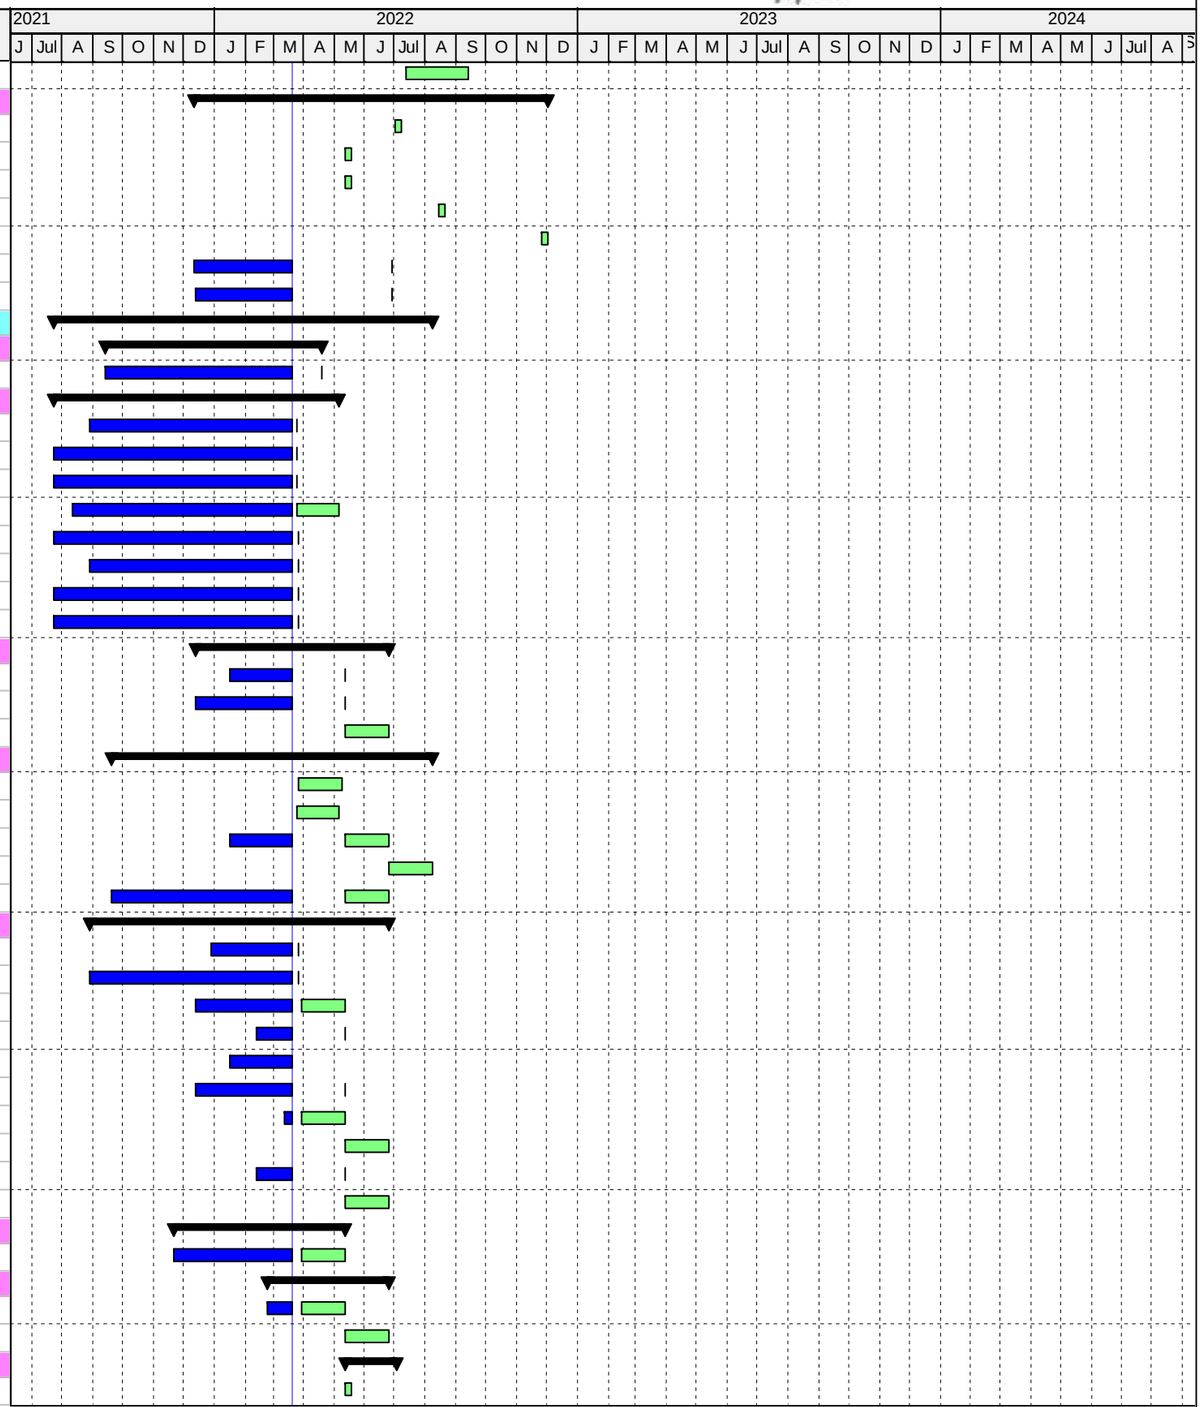


Actual Level of Effort Remaining Work Milestone
Actual Work Critical Remaining Work summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	MTO For Safety Sign	7	0%	$125.45	26-Jun-22	02-Jul-22
Electrical		584	16.54%	$30,974.20	24-Jul-21 A	07-Apr-23
Basis/Criteria		54	100%	$24.78	03-Aug-21	20-Mar-22
P12-E	Electrical System Design Criteria	54	100%	$24.78	03-Aug-21	20-Mar-22
Specification		55	100%	$281.87	24-Jul-21 A	30-Mar-22
P12-E	Specification For LV Switchgear & Motor Control Centers	49	100%	$15.64	24-Jul-21 A	24-Mar-22
P12-E	Specification For MV Switchgear	49	100%	$15.64	24-Jul-21 A	24-Mar-22
P12-E	Specification For UPS System	49	100%	$15.64	04-Aug-21	24-Mar-22
P12-E	Specification For Transformers	49	100%	$15.64	24-Jul-21 A	24-Mar-22
P12-E	Specification For DC Charger	49	100%	$15.64	04-Aug-21	24-Mar-22
P12-E	Specification For Earthing & Lightning System	49	100%	$15.64	28-Jul-21 A	24-Mar-22
P12-E	Specification For Lighting & Small Power System	49	100%	$15.64	28-Jul-21 A	27-Mar-22
P12-E	Specification For Bulk Materials	49	100%	$15.64	24-Jul-21 A	27-Mar-22
P12-E	Specification For Diesel Generator	49	100%	$15.67	28-Jul-21 A	27-Mar-22
P12-E	Specification For LV Induction Motors	49	100%	$15.67	24-Jul-21 A	27-Mar-22
P12-E	Specification For Electrical Requirements of Packaged Units	49	100%	$15.67	28-Jul-21 A	27-Mar-22
P12-E	Specification For Capacitor Bank	49	100%	$15.67	24-Jul-21 A	27-Mar-22
P12-E	Specification For Distribution & Lighting Panels	49	100%	$15.67	28-Jul-21 A	30-Mar-22
P12-E	Specification For Power & Control Cables	49	100%	$15.67	24-Jul-21 A	30-Mar-22
P12-E	Specification For Cathodic Protection System	49	100%	$15.67	31-Jul-21 A	30-Mar-22
P12-E	Specification For MV Induction Motors	49	100%	$15.67	24-Jul-21 A	30-Mar-22
P12-E	Specification For NGR	49	100%	$15.67	24-Jul-21 A	30-Mar-22
P12-E	Specification For Overhead Transmission Lines	49	100%	$15.67	28-Jul-21 A	30-Mar-22
Calculation		505	23.74%	$3,444.33	16-Nov-21	11-Jan-23
P12-E	Calculation Note For Outdoor Area Lighting System	54	0%	$717.80	13-May-22	05-Jul-22
P12-E	Calculation Note For Indoor Area Lighting System	74	0%	$287.26	14-May-22	26-Jul-22
P12-E	Calculation Note For Cable Sizing	74	0%	$287.26	13-May-22	25-Jul-22
P12-E	Calculation Note For UPS System	74	80%	$286.91	22-Nov-21	03-Aug-22
P12-E	Calculation Note For DC Charger System	74	80%	$286.91	15-Dec-21	01-Jun-22
P12-E	Calculation Note For Earthing & Lightning System	74	0%	$286.91	13-May-22	25-Jul-22
P12-E	Calculation Note For Diesel Generator Sizing	64	60%	$215.27	16-Nov-21	22-May-22
P12-E	Calculation Note For Cathodic Protection System	74	0%	$286.91	30-Oct-22	11-Jan-23
P12-E	Calculation Note For NGR Sizing	64	0%	$215.27	20-Mar-22	22-May-22
P12-E	Calculation Note for UPS of CCTV in Desalting, Production &	74	0%	$286.91	26-Aug-22	07-Nov-22
P12-E	Calculation Note for Capacitor Banks	44	80%	$286.91	22-Nov-21	13-May-22
Data Sheets		560	46.25%	$3,326.63	12-Sep-21	11-Mar-23
P12-E	Data Sheets For UPS	59	60%	$207.91	26-Dec-21	03-Aug-22
P12-E	Data Sheets For DC Charger	59	80%	$207.91	19-Dec-21	01-Jun-22
P12-E	Data Sheets For Diesel Generator	59	0%	$207.91	25-Mar-22	22-May-22
P12-E	Data Sheets For Expansion of MV Switchgear	59	80%	$207.91	22-Jan-22	20-May-22
P12-E	Data Sheets For LV Switchgear	59	60%	$207.91	19-Feb-22	20-May-22
P12-E	Data Sheets For Local Control Stations (LCS)	59	60%	$207.91	06-Feb-22	17-May-22
P12-E	Data Sheets For Capacitor Bank	59	60%	$207.91	27-Feb-22	20-May-22
P12-E	Data Sheets For LV Induction Motors	59	80%	$207.91	12-Sep-21	17-May-22
P12-E	Data Sheets For MV Induction Motors	59	80%	$207.91	12-Sep-21	17-May-22
P12-E	Data Sheets For Power & Control Cables	59	60%	$207.91	19-Feb-22	27-May-22
P12-E	Data Sheets For Power Transformers	59	60%	$207.91	02-Feb-22	17-May-22
P12-E	Data Sheets For Cathodic Protection System	59	0%	$207.91	12-Jan-23	11-Mar-23

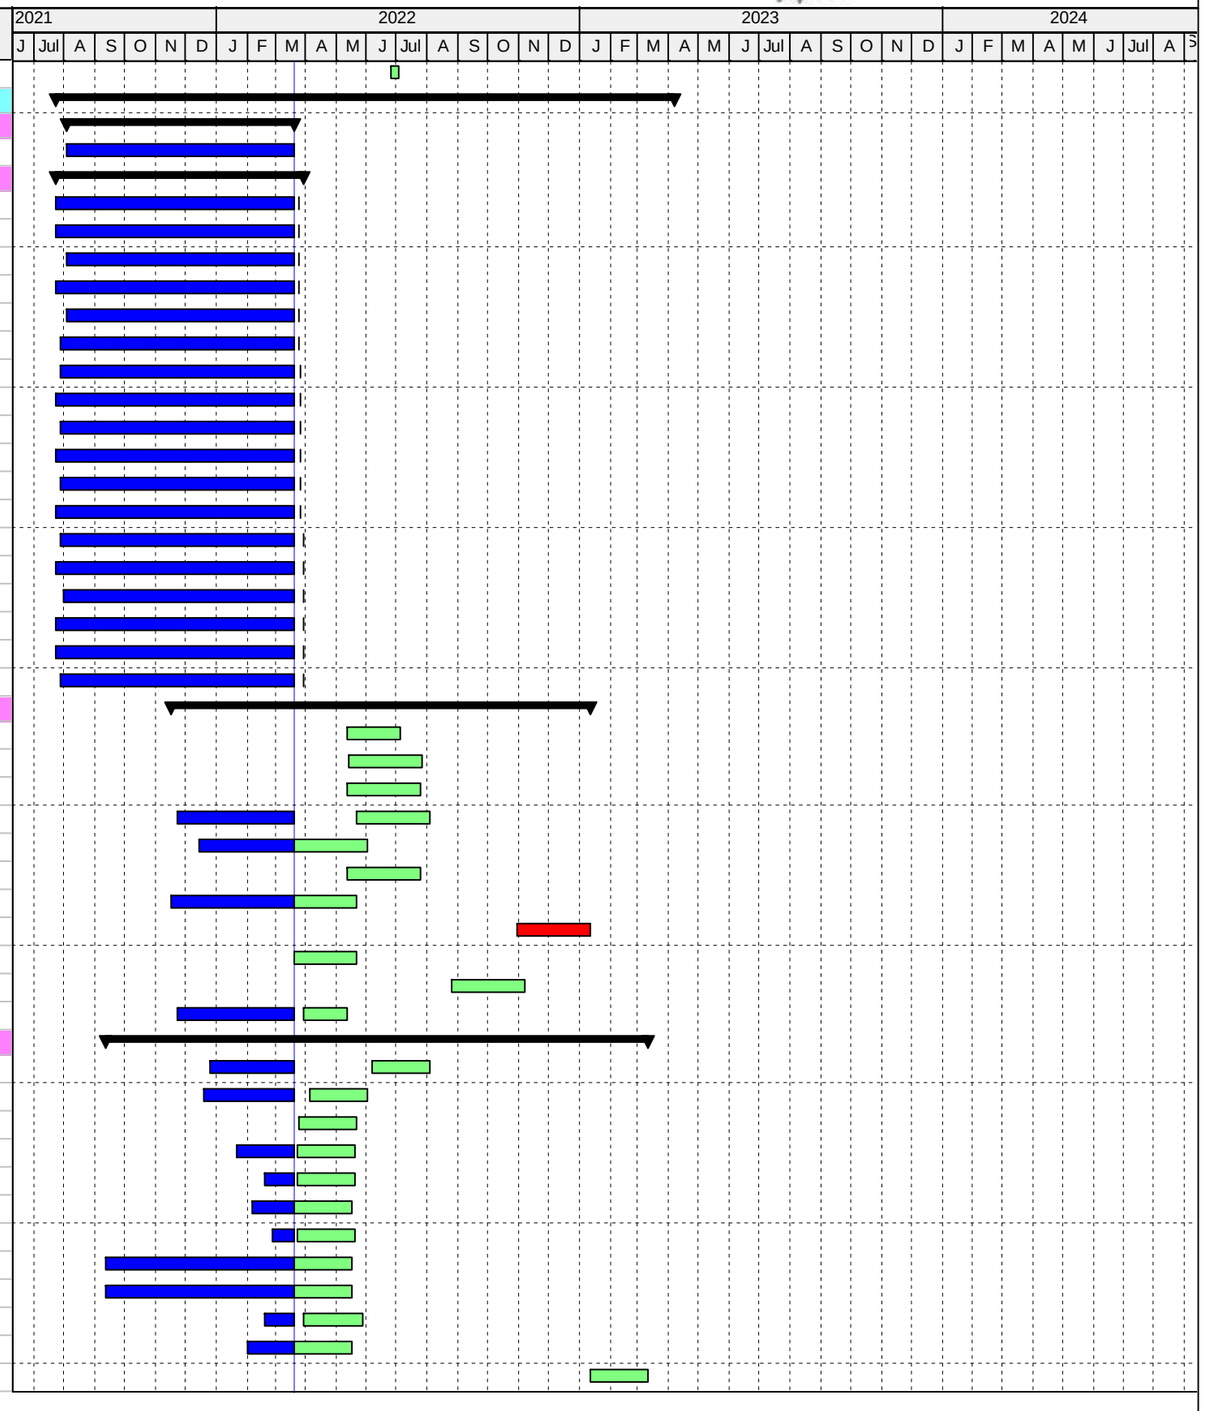


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Data Sheets For NGR	59	0%	$207.91	23-May-22	20-Jul-22
P12-E	Data Sheets For Remote Control Panel	59	0%	$207.91	21-May-22	18-Jul-22
P12-E	Data Sheets For Distribution & Lighting Panels	59	0%	$207.91	26-Sep-22	23-Nov-22
P12-E	Data Sheet for UPS of CCTV in Desalting, Production & CS U	59	60%	$207.91	02-Mar-22	25-Aug-22
Drawing/Diagram		544	12.38%	$18,339.82	09-Aug-21	06-Apr-23
P12-E	Electrical Legend and Symbols	49	100%	$11.00	09-Aug-21	30-Mar-22
P12-E	Typical Installation Details & Notes For Earthing and Lightning	14	100%	$12.84	25-Aug-21	30-Mar-22
P12-E	Typical Installation Details & Notes For Lighting System	14	100%	$12.84	25-Aug-21	30-Mar-22
P12-E	Typical Installation Details & Notes For Power System	14	100%	$12.84	25-Aug-21	30-Mar-22
P12-E	Installation Details & Notes For Cathodic Protection Systems	74	100%	$12.84	25-Aug-21	30-Mar-22
P12-E	Electrical Overall Single Line Diagram	62	60%	$430.99	24-Jan-22	20-May-22
P12-E	LV Switchgear/MCC Single Line Diagram	62	60%	$430.99	27-Dec-21	20-May-22
P12-E	Existent MV Switchgear Expansion Single Line Diagram	62	80%	$430.99	12-Jan-22	20-May-22
P12-E	Distribution and Lighting Panels Single Line Diagram	79	0%	$704.25	21-May-22	07-Aug-22
P12-E	UPS Single Line Diagram	79	60%	$352.12	26-Dec-21	03-Aug-22
P12-E	DC Charger Single Line Diagram	79	80%	$352.12	18-Dec-21	06-Jun-22
P12-E	Electrical Typical Schematic Diagrams For MV panel	35	100%	$196.24	12-Jan-22	21-May-22
P12-E	Electrical Typical Schematic Diagrams For LV panel	35	100%	$234.75	13-Dec-21	21-May-22
P12-E	Interconnection Wiring Diagram	54	0%	$390.64	18-Sep-22	10-Nov-22
P12-E	Wiring Diagram For Remote Control Panel (RCP)	62	0%	$430.99	11-Nov-22	11-Jan-23
P12-E	Wiring Diagrams For Cathodic Protection Systems	69	0%	$430.99	08-Oct-22	15-Dec-22
P12-E	Control Logic Diagram For LV Incomers and bus tie	79	60%	$352.12	16-Jan-22	06-Jun-22
P12-E	Overall Earthing Layout	79	0%	$390.64	26-Jul-22	12-Oct-22
P12-E	Earthing & Lightning Layout For Building & Shelter	64	0%	$1,406.66	26-Jul-22	27-Sep-22
P12-E	Area Lighting & Small Power Layout	82	0%	$508.01	06-Jul-22	25-Sep-22
P12-E	Lighting & Small Power Layout For Building & Shelter	66	0%	$1,878.00	27-Jul-22	30-Sep-22
P12-E	Area Electrical Cable Route & Section Layout	82	0%	$196.24	26-Jul-22	15-Oct-22
P12-E	Electrical Cable Route & Section Layout For Building & Shelte	69	0%	$2,191.61	01-Oct-22	08-Dec-22
P12-E	HVAC Power Cabling Arrangement Layout For Building	74	0%	$625.39	23-Jan-23	06-Apr-23
P12-E	Electrical Equipment Arrangement Layout For Building	54	0%	$783.11	15-Jul-22	06-Sep-22
P12-E	Cathodic Protection System Layout	79	0%	$352.12	12-Jan-23	31-Mar-23
P12-E	Capacitor Banks Single Line Diagram	79	60%	$352.12	02-Mar-22	06-Jun-22
P12-E	Power & Control Cables Termination Diagrams	62	0%	$430.99	11-Nov-22	11-Jan-23
P12-E	Single Line Diagram for UPS of CCTV in Desalting, Productio	54	0%	$390.64	08-Nov-22	31-Dec-22
P12-E	SLD for Supplying UPS of CCTV Panel in Desalting Unit	54	0%	$392.47	08-Nov-22	31-Dec-22
P12-E	SLD for Supplying UPS of CCTV Panel in Production Unit	54	0%	$392.47	08-Nov-22	31-Dec-22
P12-E	Equipment Arrangement Layout for UPS of CCTV in Desalting	79	0%	$392.47	28-Jun-22	14-Sep-22
P12-E	Equipment Arrangement Layout for UPS of CCTV in Producti	79	0%	$390.64	28-Jun-22	14-Sep-22
P12-E	Cable Route Layout for Desalting Unit	79	0%	$390.64	26-Jul-22	12-Oct-22
P12-E	Cable Route layout for Production Unit	79	0%	$390.64	26-Jul-22	12-Oct-22
P12-E	Earthing Layout for Desalting Unit	64	0%	$627.22	26-Jul-22	27-Sep-22
P12-E	Earthing Layout for Production Unit	64	0%	$627.22	26-Jul-22	27-Sep-22
P12-E	Wiring Diagram For Interposing Relay Panel (IRP)	55	0%	$430.99	11-Nov-22	04-Jan-23
List		241	6.86%	$2,741.22	16-Nov-21	23-Jan-23
P12-E	Electrical Load List	54	80%	$234.92	16-Nov-21	13-May-22
P12-E	Electrical Power & Control Cable Schedule	54	0%	$783.17	26-Jul-22	17-Sep-22
P12-E	Electrical Power & Control Drum Schedule & Cutting List	54	0%	$783.17	18-Sep-22	10-Nov-22
P12-E	Cable Schedule For Cathodic Protection System	74	0%	$313.32	26-Jul-22	07-Oct-22

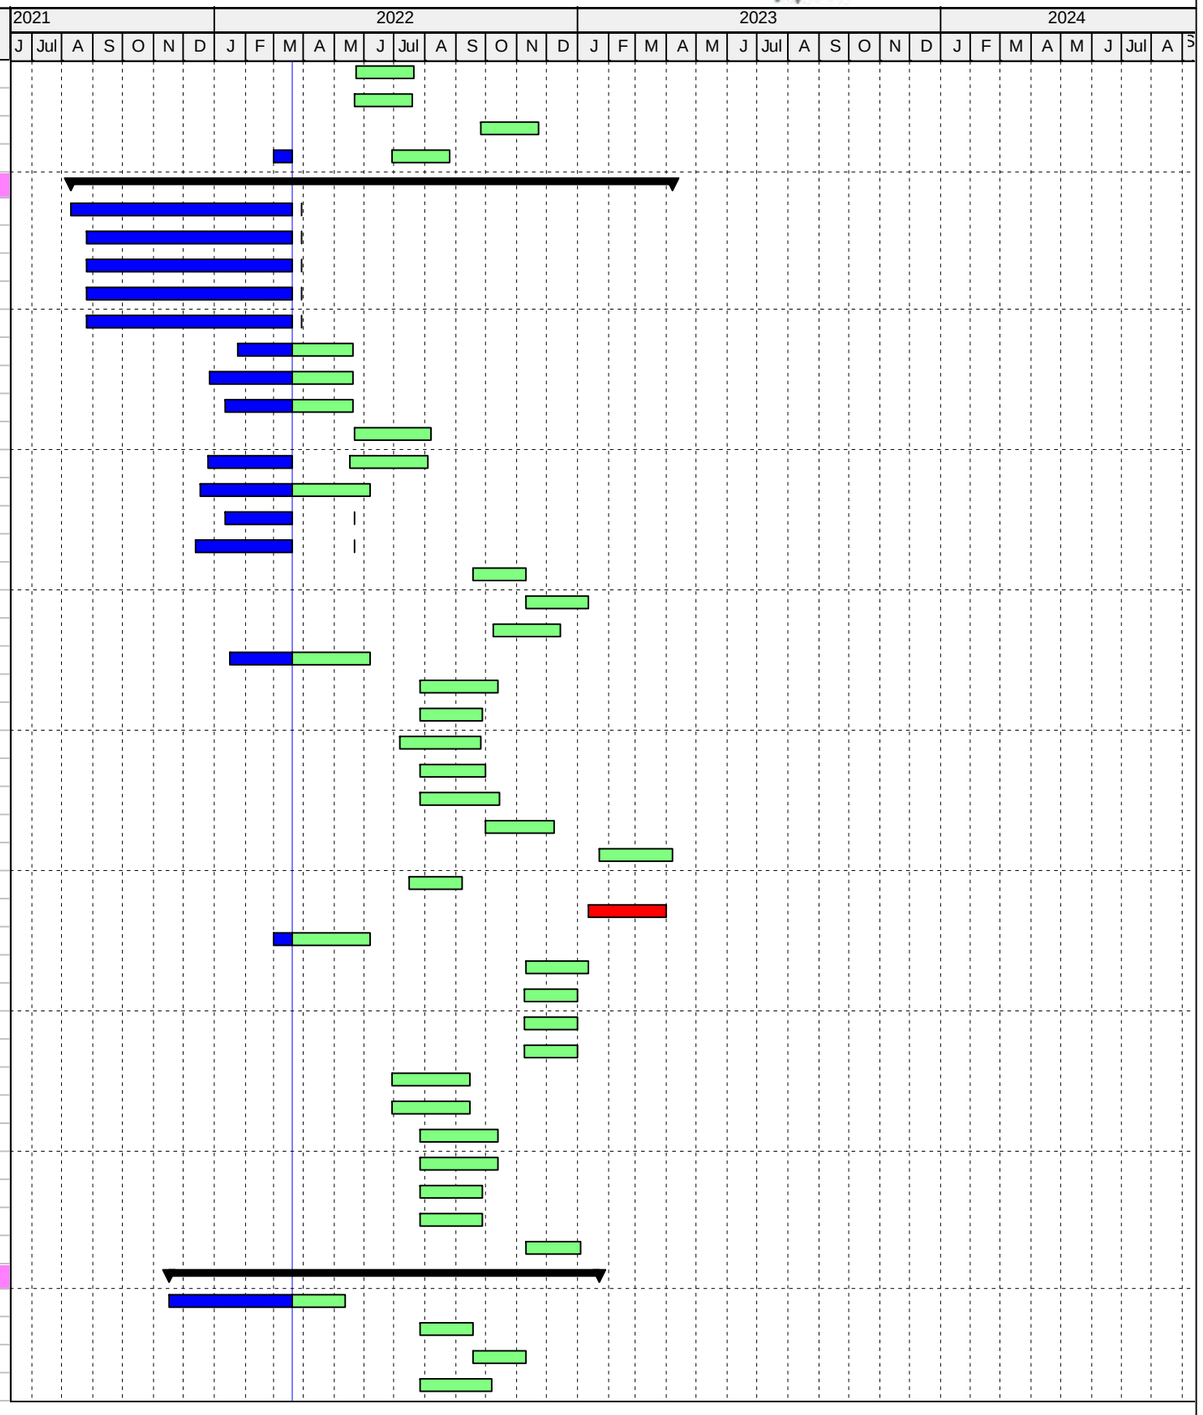


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Electrical I/O Signal List	74	0%	$626.64	11-Nov-22	23-Jan-23
Report		108	0%	$1,564.20	21-May-22	05-Sep-22
P12-E	Electrical Network (Load Flow, Motor Starting & Short Circuit)	54	0%	$782.10	21-May-22	13-Jul-22
P12-E	Relay Coordination & Setting Study Report	54	0%	$782.10	14-Jul-22	05-Sep-22
MTO		202	0%	$1,251.36	18-Sep-22	07-Apr-23
P12-E	MTO For Earthing & Lightning Systems	7	0%	$156.42	13-Oct-22	19-Oct-22
P12-E	MTO For Lighting & Small Powers	7	0%	$156.42	01-Oct-22	07-Oct-22
P12-E	MTO For Power & Control Cables	7	0%	$156.42	18-Sep-22	24-Sep-22
P12-E	MTO For Tray/Ladder and Accessories	7	0%	$312.84	09-Dec-22	15-Dec-22
P12-E	MTO For Cathodic Protection System	7	0%	$312.84	01-Apr-23	07-Apr-23
P12-E	MTO For Electrical Bulk Items	7	0%	$156.42	01-Oct-22	07-Oct-22
Intercom. & Telecomm.		425	42.61%	$13,551.21	28-Jul-21 A	18-May-23
Basis/Criteria		54	100%	$32.52	28-Jul-21 A	20-Mar-22
P12-E	Telecom. Design Criteria	54	100%	$32.52	28-Jul-21 A	20-Mar-22
Specification		52	92%	$192.43	04-Aug-21	14-May-22
P12-E	Specification For PABX	49	100%	$38.49	04-Aug-21	24-Mar-22
P12-E	Specification For PAGA	49	80%	$38.49	04-Aug-21	11-May-22
P12-E	Specification For Radio	49	100%	$38.49	04-Aug-21	24-Mar-22
P12-E	Specification For Telecommunication Tower	49	80%	$38.49	04-Aug-21	14-May-22
P12-E	Specification For Telecom. Cable	49	100%	$38.49	09-Aug-21	27-Mar-22
Data Sheets		52	100%	$2,307.77	13-Oct-21	27-Mar-22
P12-E	Data Sheets For PABX	49	100%	$461.55	13-Oct-21	24-Mar-22
P12-E	Data Sheets For PAGA	49	100%	$461.55	13-Oct-21	24-Mar-22
P12-E	Data Sheets For Radio	49	100%	$461.55	21-Nov-21	24-Mar-22
P12-E	Data Sheets For Telecom. Cable	49	100%	$461.55	13-Oct-21	27-Mar-22
P12-E	Data Sheets For Telecommunication Tower	49	100%	$461.55	13-Oct-21	27-Mar-22
Drawing/Diagram		354	33.98%	$8,453.25	28-Jul-21 A	08-Mar-23
P12-E	Telecom Systems Legend and Symbols	44	60%	$46.49	01-Aug-21	12-May-22
P12-E	Telecom Typical Installation Details & Notes	14	100%	$61.71	01-Aug-21	30-Mar-22
P12-E	Telecom Overall Block Diagram	54	0%	$928.17	20-Mar-22	12-May-22
P12-E	Typical Installation Details & Notes For Telecommunication To	35	0%	$928.17	27-Mar-22	30-Apr-22
P12-E	Block Diagram For PABX	59	100%	$928.17	28-Jul-21 A	24-Mar-22
P12-E	Block Diagram For PAGA	59	100%	$928.17	28-Jul-21 A	24-Mar-22
P12-E	Block Diagram For Radio	49	100%	$926.48	28-Jul-21 A	24-Mar-22
P12-E	Telecomm. Equipment Layout For Electrical Building	59	0%	$926.48	13-May-22	10-Jul-22
P12-E	Telecomm. Equipment Layout For Control Building	59	0%	$926.48	14-May-22	11-Jul-22
P12-E	PABX Equipment Layout For Area	59	0%	$926.48	09-Jan-23	08-Mar-23
P12-E	PAGA Equipment Layout For Area	59	0%	$926.48	26-Aug-22	23-Oct-22
List		200	0%	$1,025.83	24-Oct-22	11-May-23
P12-E	Cable Schedule For PABX	64	0%	$512.91	09-Mar-23	11-May-23
P12-E	Cable Schedule For PAGA	64	0%	$512.91	24-Oct-22	26-Dec-22
MTO		319	25%	$1,539.42	13-Dec-21	18-May-23
P12-E	MTO For PABX	7	0%	$384.85	09-Mar-23	15-Mar-23
P12-E	MTO For PAGA	7	0%	$384.85	24-Oct-22	30-Oct-22
P12-E	MTO For Radio	7	100%	$384.85	13-Dec-21	24-Mar-22
P12-E	MTO For Telecom. Cable	7	0%	$384.85	12-May-23	18-May-23
Architecture		375	21.02%	$11,615.32	18-Dec-21	11-Nov-22
Basis/Criteria		74	60%	$292.71	08-Feb-22	01-Jun-22
P12-E	Architectural Design Criteria	74	60%	$292.71	08-Feb-22	01-Jun-22

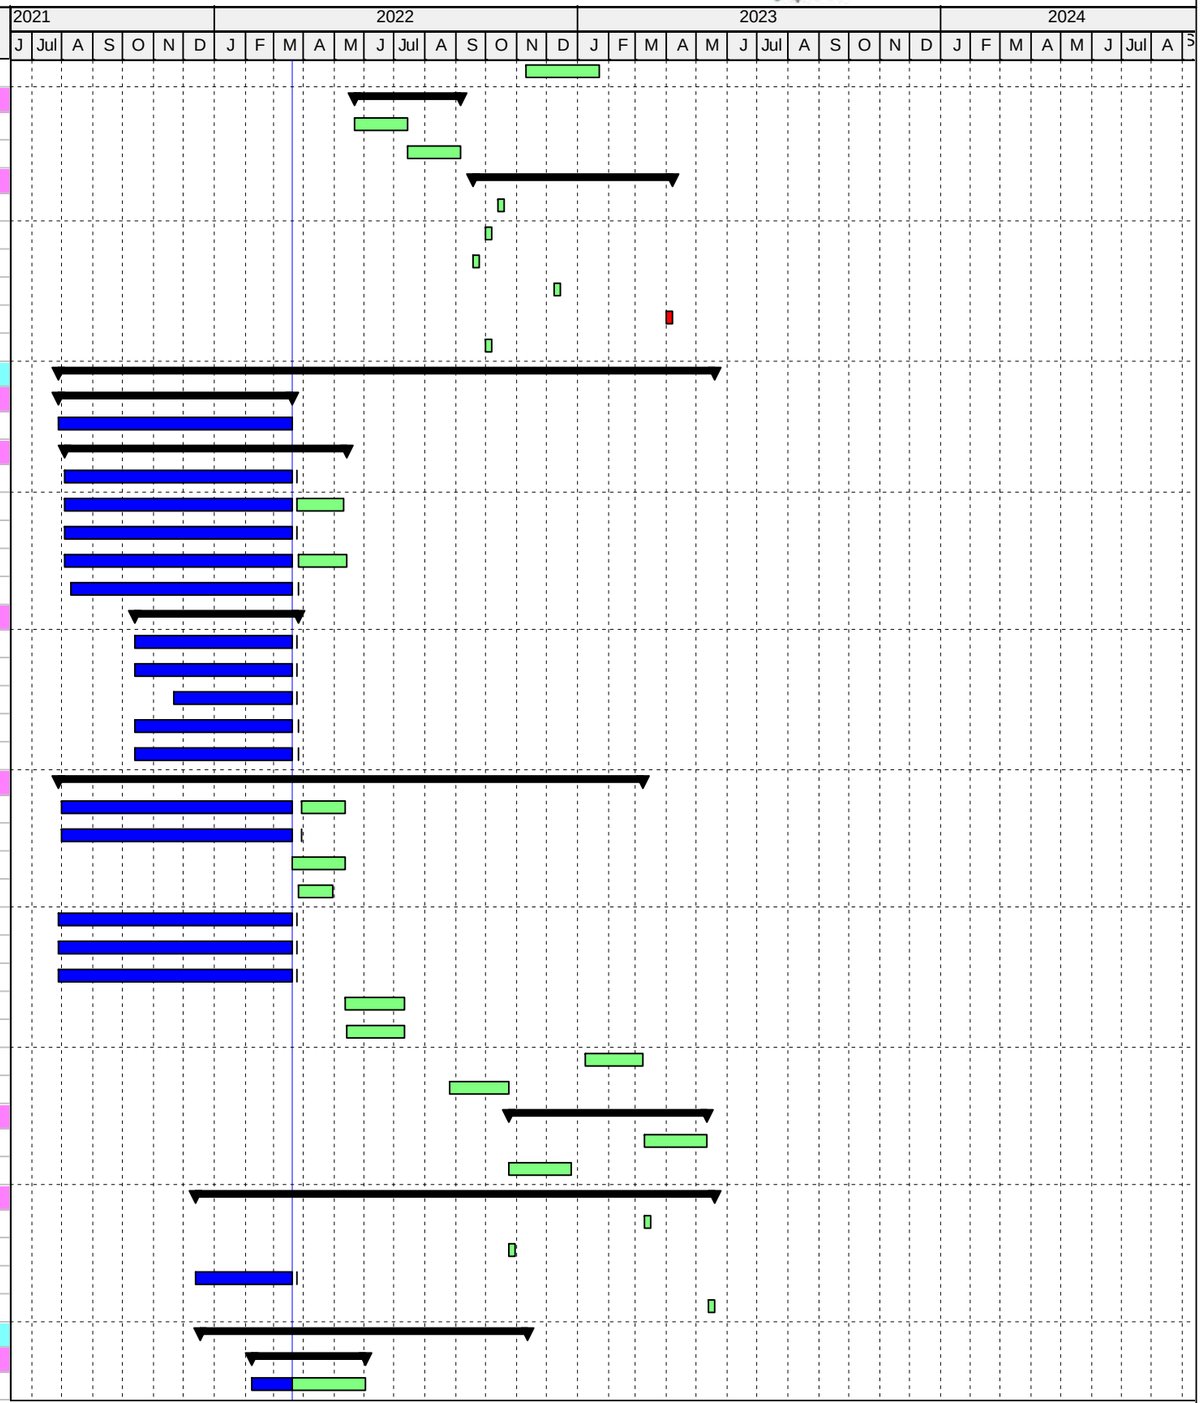


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID		Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Specification			44	0%	$364.72	20-Mar-22	02-May-22
P12-E		Buildings General Specification	44	0%	$364.72	20-Mar-22	02-May-22
Drawing/Diagram			321	23.86%	$9,496.69	18-Dec-21	11-Nov-22
P12-E		Architectural Detail Drawing For Control Building	55	60%	$1,794.87	26-Mar-22	13-May-22
P12-E		Architectural Detail Drawing For Extension of Existing Elect. B	50	60%	$1,196.58	15-Jan-22	13-May-22
P12-E		Architectural Drawing For Gas Compressors Shelter	50	0%	$1,495.73	13-May-22	01-Jul-22
P12-E		Architectural Drawing For Chemical Inj. Packages/Chemical S	50	0%	$1,196.58	13-May-22	01-Jul-22
P12-E		Architectural Drawing For Utility Shelter	50	0%	$898.39	13-May-22	01-Jul-22
P12-E		Architectural Drawing For Fire Water Pumps Shelter	50	0%	$1,196.58	13-May-22	01-Jul-22
P12-E		Architectural Drawing For Fire Shed	40	0%	$933.52	03-Oct-22	11-Nov-22
P12-E		Standard Drawing for Architectural Details	40	60%	$784.43	18-Dec-21	03-Oct-22
MTO			14	0%	$1,461.21	02-Jul-22	15-Jul-22
P12-E		MTO For Architectural Works	7	0%	$730.60	02-Jul-22	08-Jul-22
P12-E		MTO For Blast Proof Doors	7	0%	$730.60	09-Jul-22	15-Jul-22
Civil			428	2.2%	$27,102.42	01-Aug-21	21-May-23
Basis/Criteria			90	20%	$29.81	13-Feb-22	22-May-22
P12-E		Civil Design Criteria	64	60%	$9.94	13-Feb-22	22-May-22
P12-E		Design Criteria for Sewerage & Drainage	44	0%	$9.94	24-Mar-22	06-May-22
P12-E		Design Criteria for Road and Paving	44	0%	$9.94	27-Mar-22	09-May-22
Specification			94	60.01%	$149.06	09-Aug-21	06-Jun-22
P12-E		Specification For Civil Works	79	0%	$24.83	20-Mar-22	06-Jun-22
P12-E		Specification For Road & Paving	64	80%	$24.83	09-Aug-21	22-May-22
P12-E		Specification For Fence & Gate	64	100%	$24.85	18-Sep-21	20-Mar-22
P12-E		Specification For Earth Work	64	80%	$24.85	09-Aug-21	22-May-22
P12-E		Specification For Sewerage & Drainage	64	100%	$24.85	09-Aug-21	20-Mar-22
P12-E		Specification For Geological & Geotechnical Survey	44	0%	$24.85	20-Mar-22	02-May-22
Calculation			148	0%	$767.00	18-Jul-22	12-Dec-22
P12-E		Calculation Note For Inside Surface Water Drainage Channel	44	0%	$383.50	18-Jul-22	30-Aug-22
P12-E		Calculation Note for offsite flood control system	44	0%	$383.50	30-Oct-22	12-Dec-22
Drawing/Diagram			411	2.09%	$23,969.38	01-Aug-21	14-May-23
P12-E		Standard Drawing For Civil Works	64	0%	$28.76	30-Mar-22	01-Jun-22
P12-E		Standard Drawing For Slope Protection Details	64	100%	$28.76	22-Aug-21	30-Mar-22
P12-E		Standard Drawing For Roads	64	80%	$28.76	22-Aug-21	01-Jun-22
P12-E		Standard Drawing For Electrical Cable Trench	64	100%	$28.76	22-Aug-21	30-Mar-22
P12-E		Standard Drawing For Manholes	64	80%	$28.76	22-Aug-21	01-Jun-22
P12-E		Standard Drawing For Catch Basins	64	80%	$28.76	22-Aug-21	05-Jun-22
P12-E		Standard Drawing For Sewerage & Drainage Details	64	60%	$28.76	02-Feb-22	05-Jun-22
P12-E		Standard Drawing For Civil Underground Crossings	38	60%	$52.73	07-Feb-22	10-May-22
P12-E		Standard Drawing For Fence & Gate Details	64	100%	$28.76	18-Sep-21	03-Apr-22
P12-E		Standard Drawing For Concrete Continues Weight	38	100%	$52.73	01-Aug-21	20-Mar-22
P12-E		Standard Drawing For Major Floodway Crossing	38	0%	$52.73	03-Apr-22	10-May-22
P12-E		Standard Drawing For Culvert & Details	38	100%	$52.73	25-Sep-21	03-Apr-22
P12-E		Standard Drawing For Valve Box	38	100%	$52.73	12-Jan-22	03-Apr-22
P12-E		Standard Drawing For Fire Hydrant Pit	38	60%	$52.73	13-Mar-22	10-May-22
P12-E		Standard Drawing For Cable Pull Pit	64	0%	$28.76	03-Apr-22	05-Jun-22
P12-E		Standard Drawing For Pavings	38	60%	$50.34	08-Jan-22	10-May-22
P12-E		Standard Drawing For Earth Pit	38	60%	$50.34	13-Feb-22	10-May-22
P12-E		Standard Detail For Pipe Bedding	64	100%	$28.76	22-Aug-21	03-Apr-22
P12-E		Standard Details of Miscellaneous Items	64	60%	$28.76	06-Mar-22	05-Jun-22

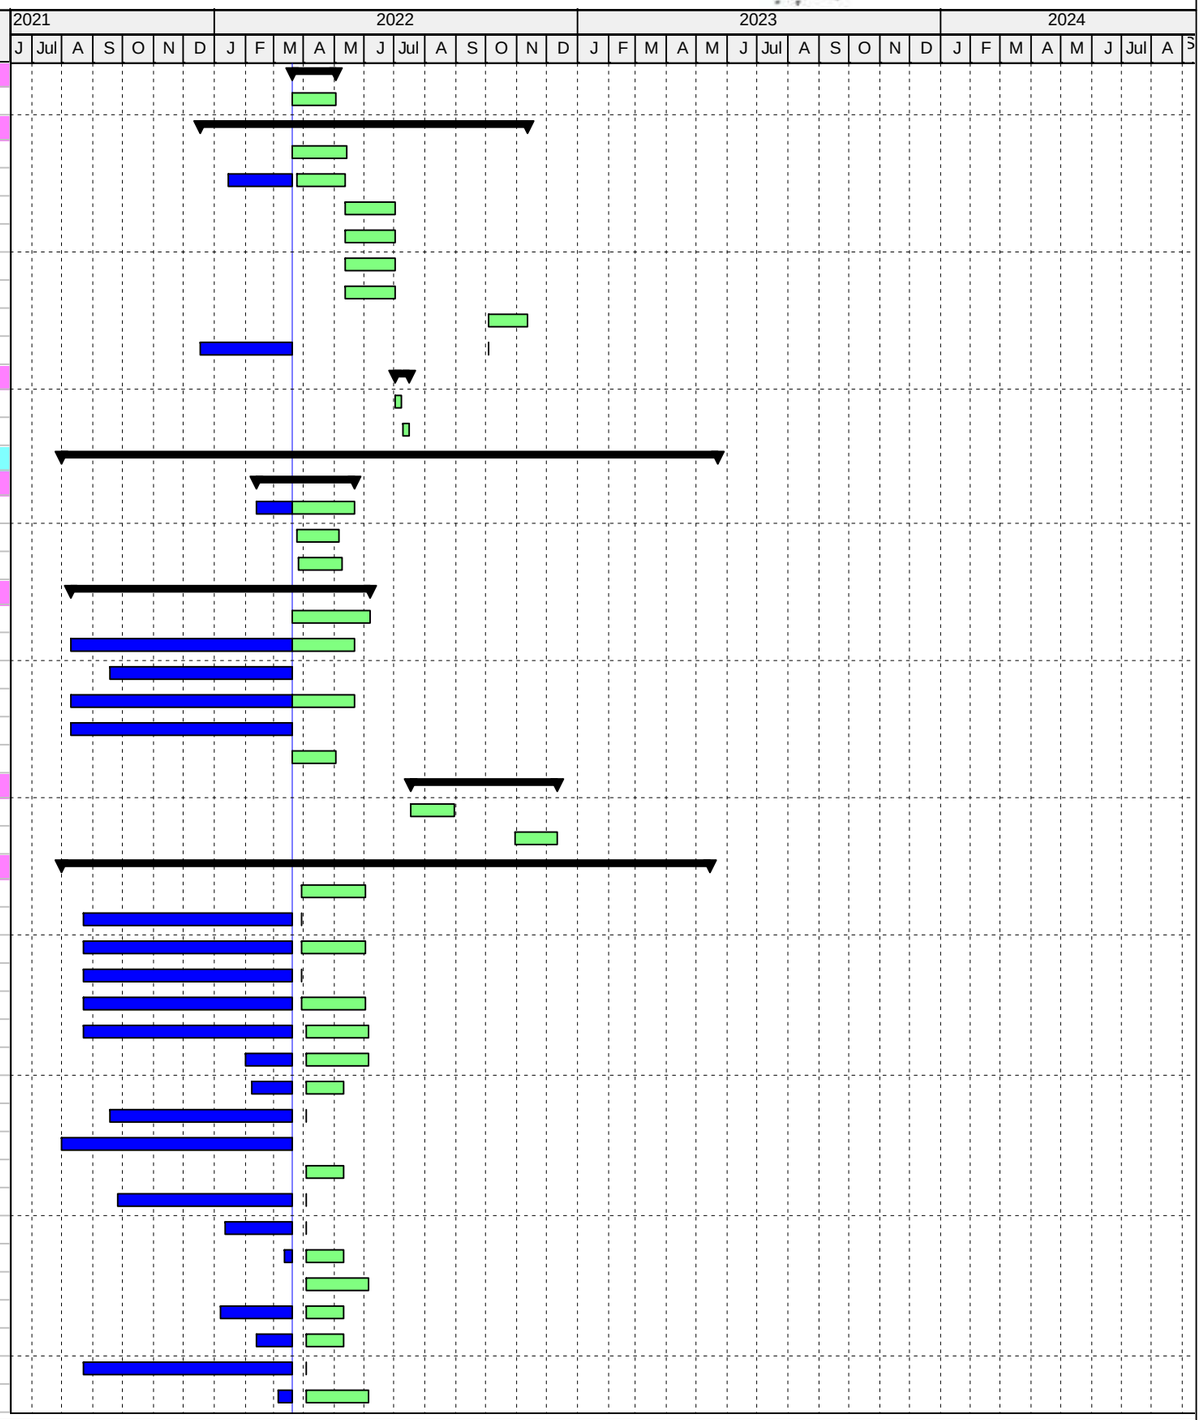

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Site Sewarage System Layout & Details	64	0%	$2,447.27	13-May-22	15-Jul-22
P12-E	Cable Trench and Duct Bank Layout	72	0%	$3,669.71	13-Oct-22	23-Dec-22
P12-E	Oil Contaminated Water System Layout	66	0%	$3,058.49	13-May-22	17-Jul-22
P12-E	Plant Clean Water Drainage System Layout & Details	66	0%	$3,058.49	13-May-22	17-Jul-22
P12-E	Road, Paving And Plant Finish Grading Layout & Sections	74	0%	$4,892.15	13-Dec-22	24-Feb-23
P12-E	Plant Underground Composite Layout	79	0%	$6,109.80	25-Feb-23	14-May-23
Report		44	0%	$767.00	30-Oct-22	12-Dec-22
P12-E	Site Visit Report (Civil Work) - GCS	44	0%	$767.00	30-Oct-22	12-Dec-22
MTO		7	0%	$1,420.17	15-May-23	21-May-23
P12-E	MTO For Civil Work	7	0%	$1,420.17	15-May-23	21-May-23
Structure		443	2.44%	$54,204.84	08-Aug-21	05-Jun-23
Basis/Criteria		64	0%	$16.26	20-Mar-22	22-May-22
P12-E	Structural Design Criteria	64	0%	$5.42	20-Mar-22	22-May-22
P12-E	Design Criteria For Steel Structure	44	0%	$5.42	20-Mar-22	02-May-22
P12-E	Design Criteria For Load & Forces	44	0%	$5.42	20-Mar-22	02-May-22
Specification		98	84.92%	$108.41	14-Aug-21	26-May-22
P12-E	Specification For Concrete Work	64	80%	$10.49	14-Aug-21	26-May-22
P12-E	Specification For Storage Tank Foundation	64	100%	$26.25	23-Nov-21	24-Mar-22
P12-E	Specification for Fabrication of Steel Structures	38	100%	$13.56	24-Jan-22	24-Mar-22
P12-E	Specification For Grouting	64	100%	$10.49	14-Aug-21	24-Mar-22
P12-E	Specification for Erection of Steel Structures	64	100%	$13.65	24-Jan-22	24-Mar-22
P12-E	Specification for Fireproofing	64	100%	$13.41	18-Sep-21	24-Mar-22
P12-E	Specification for Design of Blast Resistant Buildings	64	60%	$10.49	12-Dec-21	26-May-22
P12-E	Specification For Steel Structural Works	37	0%	$10.06	20-Mar-22	25-Apr-22
Calculation		389	0%	$4,325.55	13-May-22	05-Jun-23
P12-E	Structural Calculation Note For Control Building	54	0%	$180.38	17-Jul-22	08-Sep-22
P12-E	Calculation Report for Gas Compressors Shelter	64	0%	$180.38	25-Aug-22	27-Oct-22
P12-E	Calculation Report for Extension of Existing Elect. Building	64	0%	$180.38	06-Jul-22	07-Sep-22
P12-E	Calculation Note for Gas Compressors Foundation	44	0%	$180.38	02-Sep-22	15-Oct-22
P12-E	Calculation Note for Tank Foundation (TK-2301 A/B)	44	0%	$180.38	12-Oct-22	24-Nov-22
P12-E	Calculation Note for Utility Shelter	44	0%	$179.94	23-Apr-23	05-Jun-23
P12-E	Calculation Note for Fire Water Pump Shelter	44	0%	$179.94	22-Feb-23	06-Apr-23
P12-E	Calculation Note for Foundation of Slug Catcher Drum (V-210	44	0%	$180.38	11-Nov-22	24-Dec-22
P12-E	Calculation Note for Foundation of Dehydration Package (PK-	44	0%	$180.38	27-Oct-22	09-Dec-22
P12-E	Calculation Note for Close Drain Sump Pit (SU-2201 A)	44	0%	$180.38	13-May-22	25-Jun-22
P12-E	Calculation Note for Oily Water Sump Pit (SU-2201 B)	44	0%	$180.38	13-May-22	25-Jun-22
P12-E	Calculation Note For Compressor Area Main Sleepers	44	0%	$179.94	23-Apr-23	05-Jun-23
P12-E	Calculation Note For Flare Area Sleepers	44	0%	$179.94	23-Apr-23	05-Jun-23
P12-E	Calculation Note For Special Pipe Supports	44	0%	$179.94	23-Apr-23	05-Jun-23
P12-E	Calculation Note for1st Stage Air Coolers (AE-2101 A/B/C)	39	0%	$180.38	13-May-22	20-Jun-22
P12-E	Calculation Note for 2nd Stage Air Coolers (AE-2102 A/B/C)	44	0%	$180.38	02-Oct-22	14-Nov-22
P12-E	Calculation Note for Elevated Potable Water Tank (TK-2209)	36	0%	$180.38	12-Oct-22	16-Nov-22
P12-E	Calculation Note for Lean Glycol Storage Tank (TK-2102)	36	0%	$180.38	12-Oct-22	16-Nov-22
P12-E	Calculation Note for Nitrogen Package (PK-2204A/B)	44	0%	$180.38	19-Oct-22	01-Dec-22
P12-E	Calculation Note for Glycol Sump Pit (SU-2101)	36	0%	$180.38	27-Oct-22	01-Dec-22
P12-E	Calculation Note for Slug Pumps (P-2101A/B)	35	0%	$180.38	15-Nov-22	19-Dec-22
P12-E	Calculation Note for Utility Area Sleepers	44	0%	$179.94	26-Nov-22	08-Jan-23
P12-E	Calculation Note for Pipe rack	44	0%	$179.94	26-Nov-22	08-Jan-23
P12-E	Calculation Note for Chemical Injection and Storage Shelter	44	0%	$179.94	02-Jun-22	15-Jul-22




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Drawing/Diagram		373	2.52%	$48,833.14	08-Aug-21	06-Apr-23
P12-E	Standard Drawing For Fire Proofing	64	100%	$14.65	08-Aug-21	03-Apr-22
P12-E	Standard Drawing For Anchor Bolts	64	100%	$14.65	15-Dec-21	03-Apr-22
P12-E	Standard Drawing For Steel Stairs	64	100%	$14.65	18-Dec-21	03-Apr-22
P12-E	Standard Drawing For Operating Platform	38	100%	$24.42	27-Dec-21	30-Mar-22
P12-E	Standard Drawing For Handrail	38	100%	$24.42	18-Dec-21	30-Mar-22
P12-E	Standard Drawing For Insert Plates in Concrete	38	100%	$24.42	08-Aug-21	30-Mar-22
P12-E	Standard Details For Ladder & Safety Cage	64	100%	$14.65	15-Dec-21	03-Apr-22
P12-E	Standard Drawing For Lighting pole foundation Plan & Details	38	60%	$19.53	29-Jan-22	06-May-22
P12-E	General Notes - Steel Structures	38	100%	$19.53	25-Jan-22	30-Mar-22
P12-E	General Notes - Reinforced Concrete Structures	38	100%	$19.53	20-Dec-21	30-Mar-22
P12-E	Standard Drawing For Structural Built-up Sections	44	80%	$19.53	04-Dec-21	12-May-22
P12-E	Standard Drawing For Steel Flooring, Grating and Chequere	44	100%	$19.53	05-Jan-22	30-Mar-22
P12-E	Concrete Reinforcement Shape Code	44	0%	$19.53	30-Mar-22	12-May-22
P12-E	Standard Drawing For Septic Tank	44	80%	$19.53	22-Jan-22	12-May-22
P12-E	Foundation Location Plan	64	0%	$1,118.28	02-Feb-23	06-Apr-23
P12-E	Foundation Drawing For 1st Stage Gas Compressor (C-2101	64	0%	$1,123.16	02-Sep-22	04-Nov-22
P12-E	Foundation Drawing For 2nd Stage Gas Compressor (C-210	64	0%	$1,123.16	02-Sep-22	04-Nov-22
P12-E	Foundation Drawing For 1st Stage Air Coolers (AE-2101 A/B/	59	0%	$673.90	02-Oct-22	29-Nov-22
P12-E	Foundation Drawing For 2nd Stage Air Coolers (AE-2102 A/B	59	0%	$673.90	02-Oct-22	29-Nov-22
P12-E	Foundation Drawing For Inlet Gas K.O. Drum (V-2105)	54	0%	$561.58	11-Nov-22	03-Jan-23
P12-E	Foundation Drawing For For 1st Stage G.C. Suction Drums (	54	0%	$561.58	11-Nov-22	03-Jan-23
P12-E	Foundation Drawing For For 2nd Stage G.C. Suction Drums	54	0%	$561.58	11-Nov-22	03-Jan-23
P12-E	Foundation Drawing For 2nd Stage G.C. Discharge Drum (V-	54	0%	$561.58	11-Nov-22	03-Jan-23
P12-E	Foundation Drawing For Fuel Oil Drum (V-2206)	59	0%	$673.90	11-Nov-22	08-Jan-23
P12-E	Foundation Drawing For Instrument Air Receiver (V-2203)	74	0%	$449.26	19-Oct-22	31-Dec-22
P12-E	Foundation Drawing For Elevated Potable Water Tank (TK-2	59	0%	$673.90	12-Oct-22	09-Dec-22
P12-E	Structural Drawing For Close Drain Sump Pit (SU-2201 A)	54	0%	$561.58	13-May-22	05-Jul-22
P12-E	Foundation Drawing For Fuel Gas K.O Drum (V-2205)	74	0%	$449.26	11-Nov-22	23-Jan-23
P12-E	Foundation Drawing For Slug Catcher Drum (V-2104)	54	0%	$561.58	11-Nov-22	03-Jan-23
P12-E	Foundation Drawing For Degassing Drum (V-2106)	74	0%	$449.26	11-Nov-22	23-Jan-23
P12-E	Foundation Drawing For Nitrogen Receiver Drum (V-2204)	54	0%	$561.58	11-Nov-22	03-Jan-23
P12-E	Structural Drawing For Oily Water Sump Pit (SU-2201 B)	59	0%	$673.90	13-May-22	10-Jul-22
P12-E	Foundation Drawing For Lean Glycol Storage Tank (TK-2102)	54	0%	$561.58	12-Oct-22	04-Dec-22
P12-E	Foundation Drawing For Fire Water Storage Tanks (TK-2301	64	0%	$839.93	12-Oct-22	14-Dec-22
P12-E	Foundation Drawing For Slug Storage Tank (TK-2101)	59	0%	$673.90	12-Oct-22	09-Dec-22
P12-E	Foundation Drawing For Dehydration Package (PK-2101)	54	0%	$561.58	27-Oct-22	19-Dec-22
P12-E	Foundation Drawing For Diesel Generator (PK-2206)	54	0%	$561.58	21-Jul-22	12-Sep-22
P12-E	Foundation Drawing For Instrument & Plant Air Package (PK-	54	0%	$561.58	19-Oct-22	11-Dec-22
P12-E	Foundation Drawing For Corrosion Inhibitor Injection Package	74	0%	$449.26	09-Oct-22	21-Dec-22
P12-E	Foundation Drawing For Methanol Injection Package (PK-220	74	0%	$449.26	09-Oct-22	21-Dec-22
P12-E	Foundation Drawing For LP Flare Package (PK-2201)	64	0%	$1,123.16	09-Oct-22	11-Dec-22
P12-E	Foundation Drawing For Nitrogen Package (PK-2204A/B)	54	0%	$561.58	19-Oct-22	11-Dec-22
P12-E	Dike Wall Drawing For Lean Glycol Storage Tank (TK-2102)	54	0%	$561.58	12-Jun-22	04-Aug-22
P12-E	Dike Wall Drawing For Slug Storage Tank (TK-2101)	59	0%	$673.90	23-May-22	20-Jul-22
P12-E	Foundation Drawing For Glycol Sump Pit (SU-2101)	59	0%	$673.90	27-Oct-22	24-Dec-22
P12-E	Foundation Drawing For Glycol Transfer Pumps (P-2103 A/B)	79	0%	$278.35	15-Nov-22	01-Feb-23
P12-E	Foundation Drawing For Glycol Manual Pump (P-2102)	79	0%	$278.35	15-Nov-22	01-Feb-23

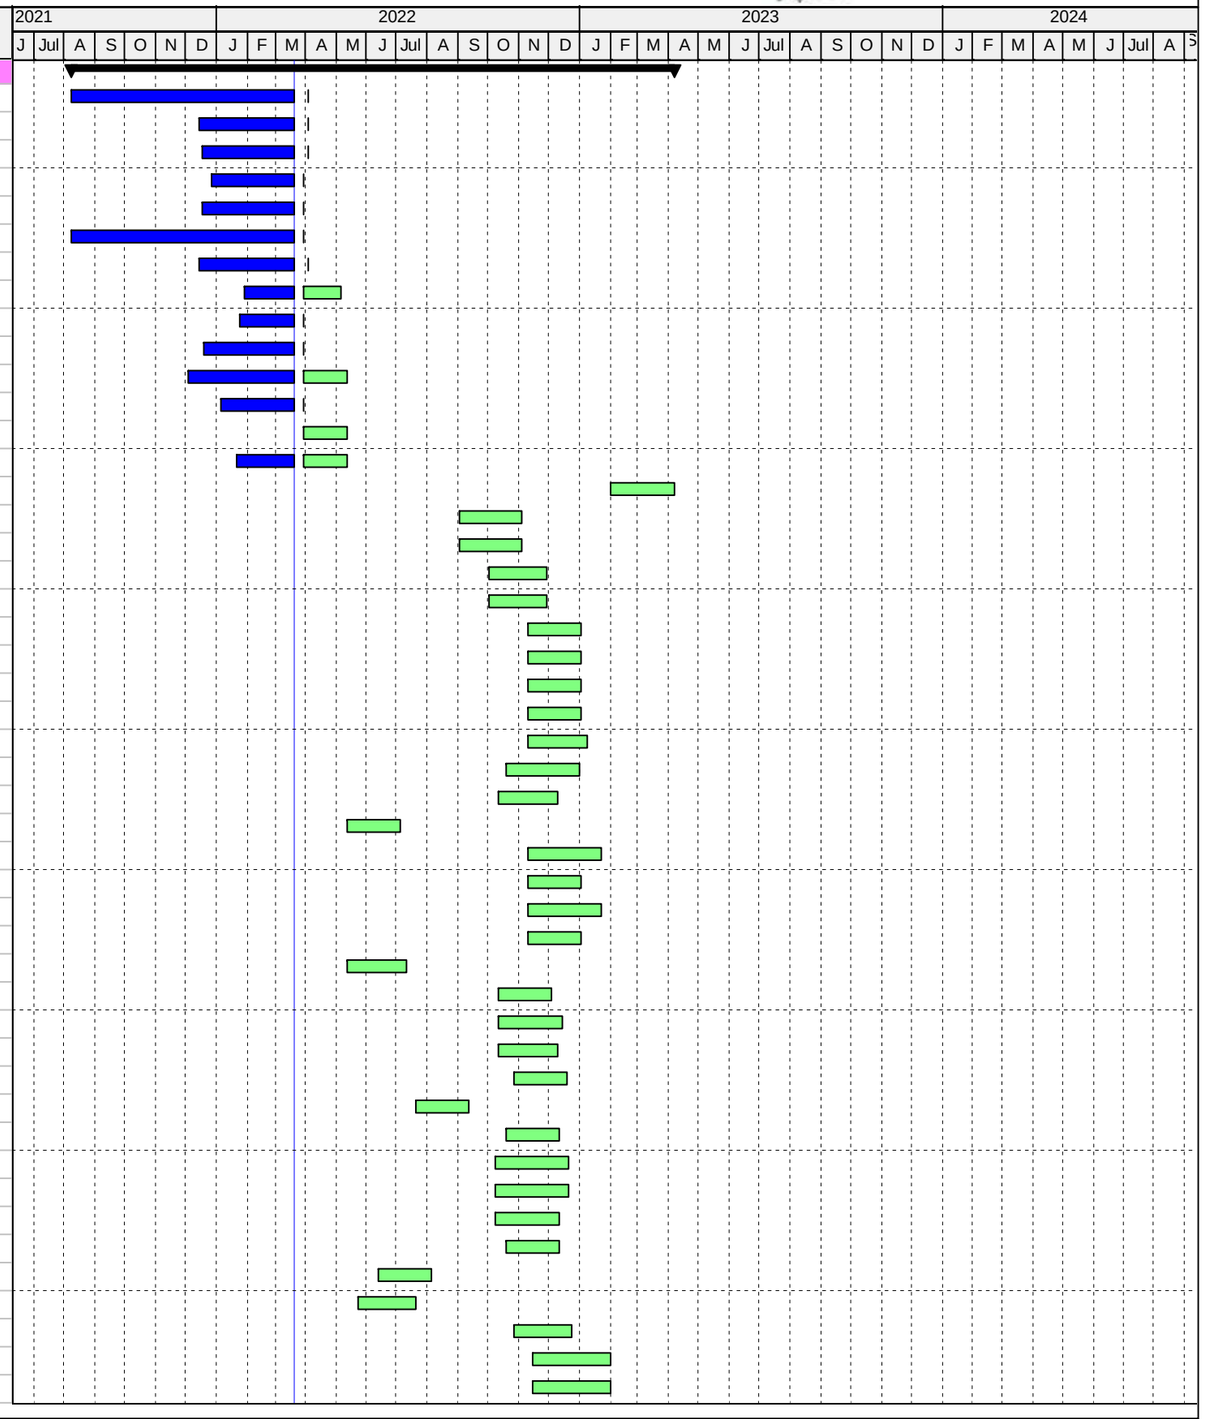


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Foundation Drawing For Fire Water Jockey Pumps (P-2302A	79	0%	$278.35	02-Oct-22	19-Dec-22
P12-E	Foundation Drawing For Fire Water Electrical Pump (P-2301	79	0%	$278.35	02-Oct-22	19-Dec-22
P12-E	Foundation Drawing For Fire Water Diesel Pumps (P-2302 E	79	0%	$278.35	02-Oct-22	19-Dec-22
P12-E	Foundation Drawing For Potable Water Pump (P-2209)	79	0%	$278.35	15-Nov-22	01-Feb-23
P12-E	Foundation Drawing For Fuel Oil Pump (P-2206)	79	0%	$278.35	15-Nov-22	01-Feb-23
P12-E	Foundation Drawing For Slug Pumps (P-2101A/B)	59	0%	$673.90	15-Nov-22	12-Jan-23
P12-E	Foundation Drawing For Compressor Area Main Sleepers	64	0%	$1,123.16	21-May-22	23-Jul-22
P12-E	Foundation Drawing For Compressor Area Secondary Sleepe	64	0%	$839.93	21-May-22	23-Jul-22
P12-E	Foundation Drawing For Utility Area Sleepers	64	0%	$1,123.16	21-May-22	23-Jul-22
P12-E	Foundation Drawing For Flare Area Sleepers	64	0%	$1,123.16	21-May-22	23-Jul-22
P12-E	Foundation Drawing For Transformer & Shelters	59	0%	$673.90	14-Oct-22	11-Dec-22
P12-E	Foundation Drawing For Pipe Supports	64	0%	$1,123.16	21-May-22	23-Jul-22
P12-E	Structural Drawing For Special Pipe Supports	64	0%	$839.93	21-May-22	23-Jul-22
P12-E	Culvert Detail Drawing	64	0%	$1,123.16	13-May-22	15-Jul-22
P12-E	Foundation Drawing For Access Platforms	64	0%	$839.93	21-May-22	23-Jul-22
P12-E	Structural Drawing For Access Platforms	66	0%	$1,406.39	21-May-22	25-Jul-22
P12-E	Foundation Drawing For Pipe rack	64	0%	$839.93	21-May-22	23-Jul-22
P12-E	Structural Drawing For Pipe rack	66	0%	$1,406.39	21-May-22	25-Jul-22
P12-E	Foundation Drawing For Lighting Poles and Towers	59	0%	$673.90	01-Oct-22	28-Nov-22
P12-E	Foundation Drawing For Chemical Injection and Storage She	74	0%	$449.26	02-Jul-22	13-Sep-22
P12-E	Structural Drawing For Chemical Injection and Storage Shelte	59	0%	$673.90	02-Jul-22	29-Aug-22
P12-E	Foundation Drawing For Gas Compressor Shelter	54	0%	$561.58	02-Jul-22	24-Aug-22
P12-E	Structural Drawing For Gas Compressor Shelter	64	0%	$1,123.16	02-Jul-22	03-Sep-22
P12-E	Foundation Drawing For Control Building	64	0%	$839.93	14-May-22	16-Jul-22
P12-E	Structural Drawing For Control Building	66	0%	$1,406.39	14-May-22	18-Jul-22
P12-E	Foundation Drawing For Extension of Existing Elect. Building	54	0%	$561.58	13-May-22	05-Jul-22
P12-E	Structural Drawing For Extension of Existing Elect. Building	64	0%	$839.93	13-May-22	15-Jul-22
P12-E	Foundation Drawing For Fire Water Pump Shelter	74	0%	$449.26	02-Jul-22	13-Sep-22
P12-E	Structural Drawing For Fire Water Pump Shelter	59	0%	$673.90	02-Jul-22	29-Aug-22
P12-E	Foundation Drawing For Utility Shelter	74	0%	$449.26	02-Jul-22	13-Sep-22
P12-E	Structural Drawing For Utility Shelter	59	0%	$673.90	02-Jul-22	29-Aug-22
P12-E	Foundation Drawing For Air Dryer Packages (PK-D-2203A/B)	44	0%	$673.90	19-Oct-22	01-Dec-22
P12-E	Foundation Drawing For Pig Launcher (PL-3101)	44	0%	$673.90	16-Oct-22	28-Nov-22
P12-E	Foundation Drawing For Ignition Package	44	0%	$673.90	09-Oct-22	21-Nov-22
P12-E	Foundation Drawing For Fire Shed	55	80%	$673.90	07-Mar-22	22-May-22
P12-E	Structural Drawing For Fire Shed	55	80%	$571.35	07-Mar-22	22-May-22
P12-E	Structural Drawing For Shelter of Transformers	39	0%	$571.35	13-May-22	20-Jun-22
MTO		7	0%	$921.48	15-Jan-23	21-Jan-23
P12-E	MTO For Steel Structures Works	7	0%	$460.74	15-Jan-23	21-Jan-23
P12-E	MTO For Structural Concrete Works	7	0%	$460.74	15-Jan-23	21-Jan-23
General		254	12.06%	$64,077.87	05-Sep-21	29-Oct-22
Risk Assessment		44	100%	$3,203.89	05-Sep-21	20-Mar-22
Procedure/Plan		44	100%	$3,203.89	05-Sep-21	20-Mar-22
P12-	HAZOP Study Procedure	44	100%	$1,067.54	25-Oct-21	20-Mar-22
P12-	HAZID Study Procedure	44	100%	$1,068.18	05-Sep-21	20-Mar-22
P12-	SIL Study Procedure	44	100%	$1,068.18	25-Oct-21	20-Mar-22
Geotechnic		104	7.06%	$54,466.19	19-Dec-21	29-Oct-22
Report		44	0%	$44,213.73	16-Sep-22	29-Oct-22
P12-	Geotechnical Investigation Report for Compressor Station	44	0%	$44,213.73	16-Sep-22	29-Oct-22

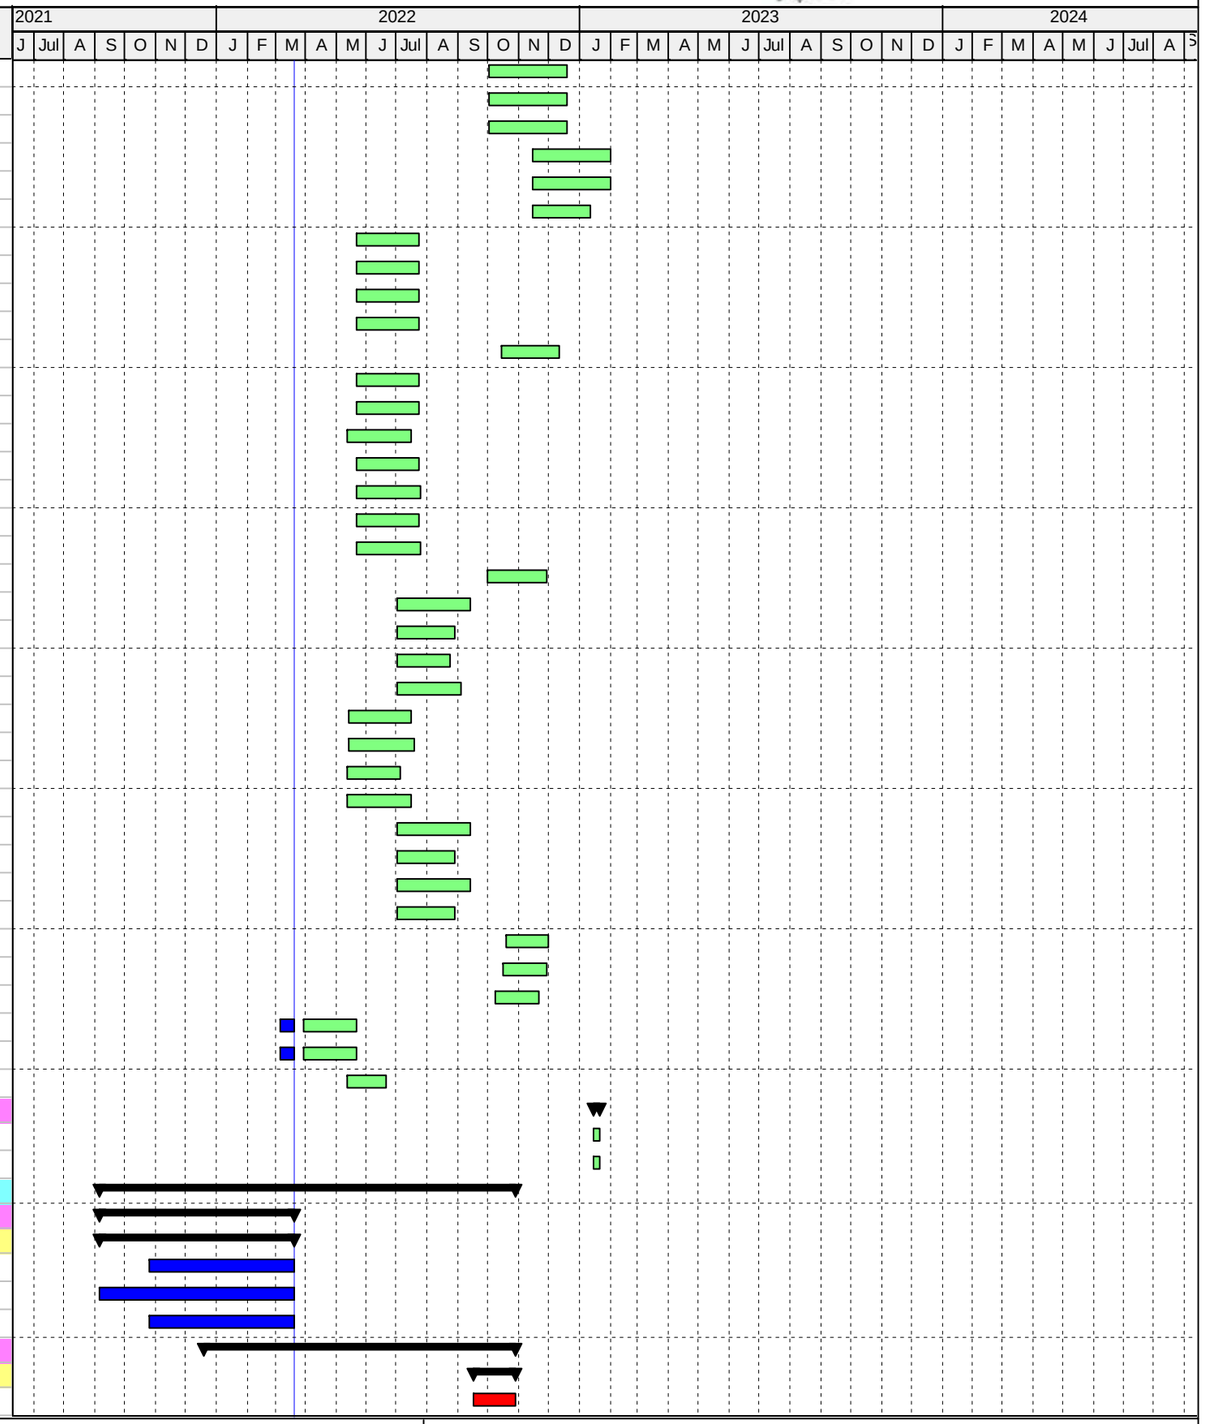


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Procedure/Plan		44	100%	$3,844.67	19-Dec-21	16-Sep-22
P12-	Geotechnical Investigation Plan for Compressor Station	44	100%	$3,844.67	19-Dec-21	16-Sep-22
Survey (Topography)		30	0%	$6,407.79	17-Aug-22	15-Sep-22
P12-	Topographical Map	30	0%	$6,407.79	17-Aug-22	15-Sep-22
QC/QA		116	10.59%	$6,407.79	20-Sep-21	13-Jul-22
QC Management		116	39%	$520.95	08-Dec-21	13-Jul-22
P12-	Project Audit Procedure	44	0%	$26.05	20-Mar-22	02-May-22
P12-	Specification For Final Data Book (FDB) Requirements	44	0%	$26.05	20-Mar-22	02-May-22
P12-	Non Conformance Control Procedure	36	0%	$26.05	03-May-22	07-Jun-22
P12-	Corrective Action Procedure	36	0%	$26.05	08-Jun-22	13-Jul-22
P12-	Material Reciving, Storage, Handling Procedure	39	60%	$26.05	20-Feb-22	27-Apr-22
P12-	Packing, Marking, Transportation Procedure	39	0%	$26.05	20-Mar-22	27-Apr-22
P12-	Criticality Assessment Procedure	39	0%	$104.19	20-Mar-22	27-Apr-22
P12-	Project Quality Plan	44	80%	$234.43	08-Dec-21	20-Mar-22
P12-	Technical Query Procedure	44	0%	$26.05	30-Mar-22	12-May-22
QC General Document		55	8.58%	$760.60	28-Nov-21	16-May-22
P12-	Quality Control Plan (QCP)	39	60%	$108.77	28-Nov-21	27-Apr-22
P12-	Specification for Welding Procedure	44	0%	$108.77	03-Apr-22	16-May-22
P12-	Heat Treatment Procedure (Pre Heating , PWHT)	44	0%	$108.77	03-Apr-22	16-May-22
P12-	Welder Performance Qualification Test (WQT) Procedure	44	0%	$108.77	03-Apr-22	16-May-22
P12-	NDT Procedure	44	0%	$108.77	03-Apr-22	16-May-22
P12-	Surface Preparation and Coating/Painting Procedure	44	0%	$108.77	03-Apr-22	16-May-22
P12-	Control of Inspection Measuring and Test Equipment Procedu	44	0%	$108.01	03-Apr-22	16-May-22
QC Discipline Document		81	8%	$5,126.23	20-Sep-21	16-May-22
Piping		51	0%	$1,281.56	27-Mar-22	16-May-22
P12	ITP For Piping Works	44	0%	$128.16	27-Mar-22	09-May-22
P12	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$144.18	03-Apr-22	16-May-22
P12	PIPING WPS (Welding Procedure Specification)	44	0%	$144.18	03-Apr-22	16-May-22
P12	PIPING PQR (Procedure Qualification Record)	44	0%	$144.18	03-Apr-22	16-May-22
P12	PIPING PWPS (Preliminary Welding Procedure Specification)	44	0%	$144.18	03-Apr-22	16-May-22
P12	PIPING WPS (Preliminary Welding Procedure Specification) f	44	0%	$144.18	03-Apr-22	16-May-22
P12	PIPING PQR (Procedure Qualification Record) for Repair We	44	0%	$144.18	03-Apr-22	16-May-22
P12	Field Joint Coating Procedure For Pipeline	44	0%	$144.18	03-Apr-22	16-May-22
P12	Pressure Test Procedure	44	0%	$144.18	03-Apr-22	16-May-22
Telecomm.		44	0%	$256.31	27-Mar-22	09-May-22
P12	ITP For Telecommunication Installation	44	0%	$256.31	27-Mar-22	09-May-22
Safety		44	0%	$256.31	27-Mar-22	09-May-22
P12	ITP For Safety Installation	44	0%	$256.31	27-Mar-22	09-May-22
Architectural		44	0%	$256.31	27-Mar-22	09-May-22
P12	ITP For Architectural Works	44	0%	$256.31	27-Mar-22	09-May-22
Mechanical		44	0%	$256.31	27-Mar-22	09-May-22
P12	ITP For Mechanical Installation	44	0%	$256.31	27-Mar-22	09-May-22
Structure		51	0%	$1,025.25	27-Mar-22	16-May-22
P12	ITP For Steel Structural Works	44	0%	$102.52	27-Mar-22	09-May-22
P12	Steel Structure WPS (Welding Procedure Specification)	44	0%	$153.79	03-Apr-22	16-May-22
P12	Steel Structure PQR (Procedure Qualification Record)	44	0%	$153.79	03-Apr-22	16-May-22
P12	Steel Structure WPS (Welding Procedure Specification) For F	44	0%	$153.79	03-Apr-22	16-May-22
P12	Steel Structure PQR (Procedure Qualification Record) For We	44	0%	$153.79	03-Apr-22	16-May-22
P12	Weld Map For Steel Structures	44	0%	$153.79	03-Apr-22	16-May-22

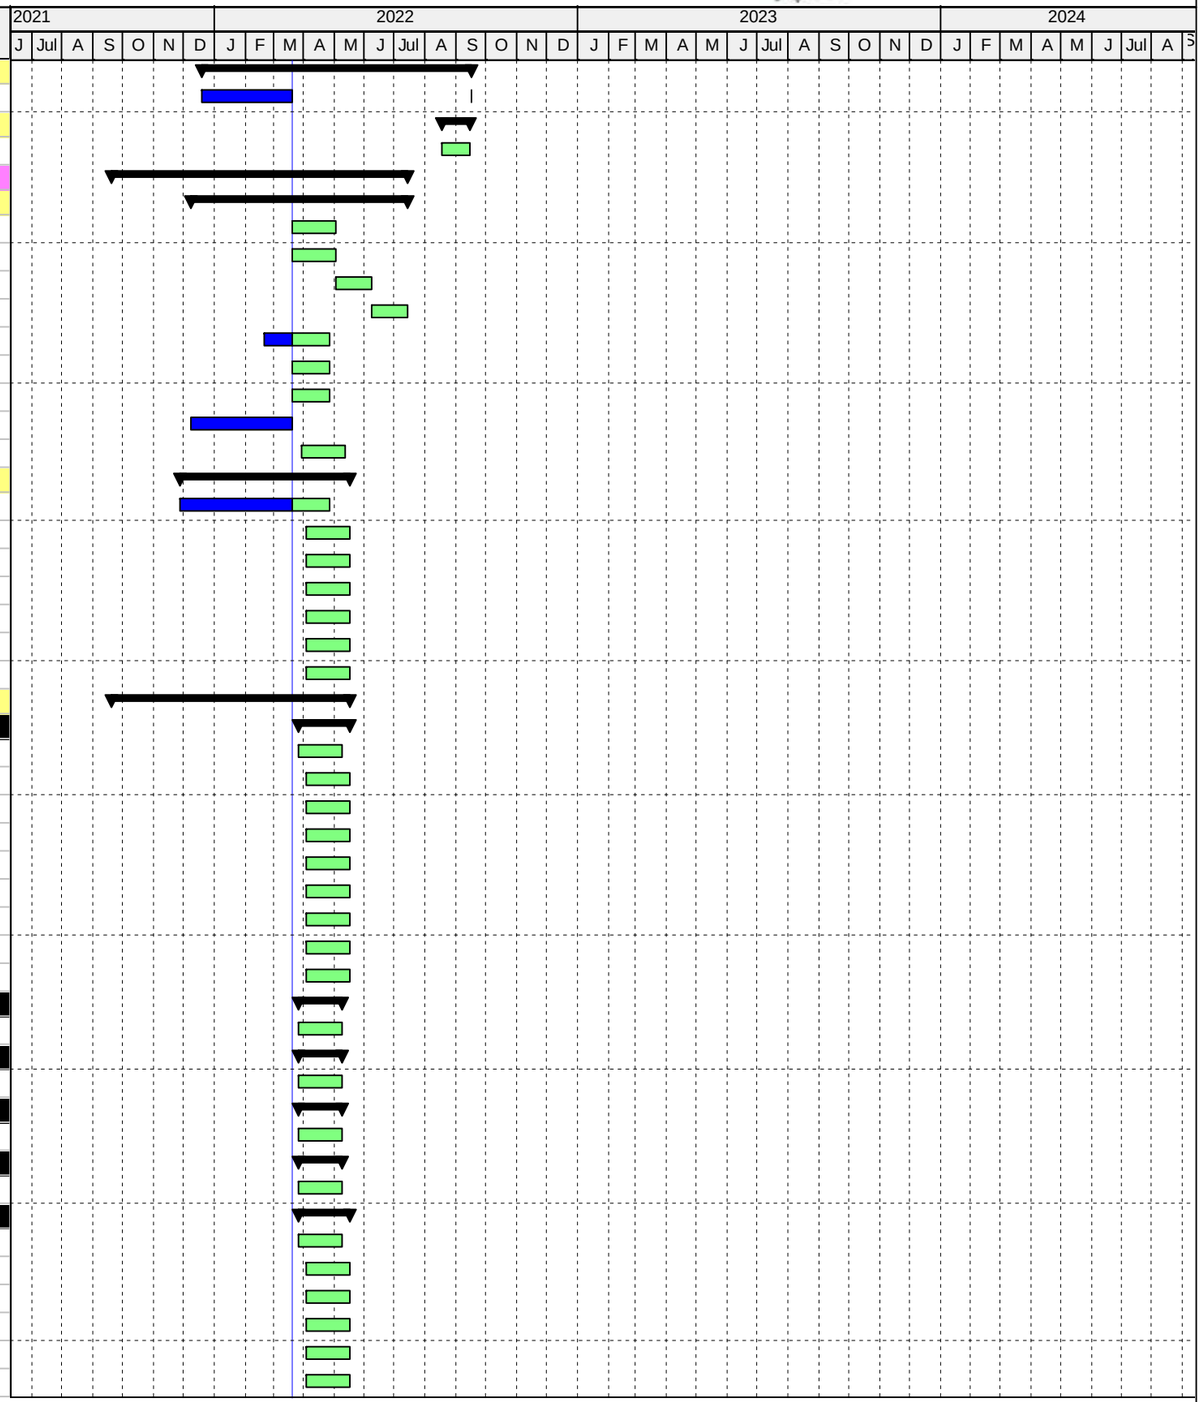

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12	NDT Plan For steel Structures	44	0%	$153.79	03-Apr-22	16-May-22
Instrumentation		44	0%	$256.31	27-Mar-22	09-May-22
P12	ITP For I&C Installation	44	0%	$256.31	27-Mar-22	09-May-22
Pipeline		74	15%	$1,025.25	16-Jan-22	16-May-22
P12	ITP For Pipeline	44	60%	$102.52	16-Jan-22	09-May-22
P12	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	60%	$153.79	23-Feb-22	16-May-22
P12	PIPELINE WPS (Welding Procedure Specification)	44	0%	$153.79	03-Apr-22	16-May-22
P12	PIPELINE PQR (Procedure Qualification Record)	44	0%	$153.79	03-Apr-22	16-May-22
P12	PIPELINE PWPS (Preliminary Welding Procedure Specificatic	44	0%	$153.79	03-Apr-22	16-May-22
P12	PIPELINE WPS (Preliminary Welding Procedure Specificatior	44	0%	$153.79	03-Apr-22	16-May-22
P12	PIPELINE PQR (Procedure Qualification Record) for Repair \	44	0%	$153.79	03-Apr-22	16-May-22
Civil		44	100%	$256.31	20-Sep-21	27-Mar-22
P12	ITP For Civil Works	44	100%	$256.31	20-Sep-21	27-Mar-22
Electrical		44	0%	$256.31	27-Mar-22	09-May-22
P12	ITP For Electrical Installation	44	0%	$256.31	27-Mar-22	09-May-22
Procurement Engineering		519	4.97%	$70,395.90	28-Nov-21	24-Aug-23
Mechanical		462	11.2%	$30,073.13	28-Nov-21	14-Nov-22
Pressure Vessels		152	10%	$2,890.03	15-Feb-22	10-Nov-22
P12-E	PMR For Pressure Vessels	10	100%	$289.00	15-Feb-22	12-Jun-22
P12-E	TBE For Pressure Vessels	45	0%	$433.50	12-Jun-22	26-Jul-22
P12-E	VDR For Pressure Vessels	7	0%	$2,167.52	04-Nov-22	10-Nov-22
Overhead Travelling Cranes		139	0%	$1,154.81	23-May-22	08-Oct-22
P12-E	PMR For Overhead Travelling Cranes	10	0%	$115.48	23-May-22	01-Jun-22
P12-E	TBE For Overhead Travelling Cranes	45	0%	$173.22	30-May-22	13-Jul-22
P12-E	VDR For Overhead Travelling Cranes	7	0%	$866.11	02-Oct-22	08-Oct-22
Gas Air Coolers		132	10%	$1,987.83	12-Feb-22	01-Oct-22
P12-E	PMR For Gas Air Coolers	10	100%	$198.78	12-Feb-22	23-May-22
P12-E	TBE For Gas Air Coolers	45	0%	$298.18	23-May-22	06-Jul-22
P12-E	VDR For Gas Air Coolers	7	0%	$1,490.88	25-Sep-22	01-Oct-22
Pumps - General Services		163	10%	$1,025.49	11-Feb-22	14-Nov-22
P12-E	PMR For Centrifugal Pumps For General Services	10	100%	$102.55	11-Feb-22	06-Jul-22
P12-E	TBE For Centrifugal Pumps For General Services	45	0%	$153.82	06-Jul-22	19-Aug-22
P12-E	VDR For Centrifugal Pumps For General Services	7	0%	$769.12	08-Nov-22	14-Nov-22
Flare Packages		139	0%	$1,437.50	23-May-22	08-Oct-22
P12-E	PMR For Flare Packages	10	0%	$143.75	23-May-22	01-Jun-22
P12-E	TBE For Flare Packages	45	0%	$215.62	30-May-22	13-Jul-22
P12-E	VDR For Flare Packages	7	0%	$1,078.12	02-Oct-22	08-Oct-22
Instrument/Plant Air & Nitrogen Packages		149	0%	$1,987.83	23-May-22	18-Oct-22
P12-E	PMR For Instrument/Plant Air & Nitrogen Packages	10	0%	$198.78	23-May-22	01-Jun-22
P12-E	TBE For Instrument/Plant Air & Nitrogen Packages	45	0%	$298.18	30-May-22	13-Jul-22
P12-E	VDR For Instrument/Plant Air & Nitrogen Packages	7	0%	$1,490.88	12-Oct-22	18-Oct-22
Fire Water Pumps		462	10%	$1,025.49	12-Feb-22	01-Oct-22
P12-E	PMR For Fire Water Pump	10	100%	$102.55	12-Feb-22	13-May-22
P12-E	TBE For Fire Water Pump	45	0%	$153.82	13-May-22	26-Jun-22
P12-E	VDR For Fire Water Pump	7	0%	$769.12	25-Sep-22	01-Oct-22
Chemical Injection Packages		139	0%	$1,299.16	23-May-22	08-Oct-22
P12-E	PMR For Chemical Injection Packages	10	0%	$129.92	23-May-22	01-Jun-22
P12-E	TBE For Chemical Injection Packages	45	0%	$194.87	30-May-22	13-Jul-22
P12-E	VDR For Chemical Injection Packages	7	0%	$974.37	02-Oct-22	08-Oct-22
Gas Dehydration Package		157	10%	$8,119.74	19-Dec-21	26-Oct-22




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	PMR For Gas Dehydration Package	10	100%	$811.97	19-Dec-21	23-May-22
P12-E	TBE For Gas Dehydration Package	45	0%	$1,217.96	23-May-22	06-Jul-22
P12-E	VDR For Gas Dehydration Package	7	0%	$6,089.81	20-Oct-22	26-Oct-22
Pumps - Process Services		163	10%	$1,025.49	09-Feb-22	14-Nov-22
P12-E	PMR For Centrifugal Pumps For Process Services	10	100%	$102.55	09-Feb-22	26-Jun-22
P12-E	TBE For Centrifugal Pumps For Process Services	45	0%	$153.82	26-Jun-22	09-Aug-22
P12-E	VDR For Centrifugal Pumps For Process Services	7	0%	$769.12	08-Nov-22	14-Nov-22
Storage Tanks		142	10%	$1,804.39	01-Feb-22	11-Oct-22
P12-E	PMR For Storage Tanks	10	100%	$180.44	01-Feb-22	23-May-22
P12-E	TBE For Storage Tanks	45	0%	$270.66	23-May-22	06-Jul-22
P12-E	VDR For Storage Tanks	7	0%	$1,353.29	05-Oct-22	11-Oct-22
Gas Compressors		169	25%	$6,315.36	28-Nov-21	01-Sep-22
P12-E	PMR For Gas Compressors	10	100%	$631.54	28-Nov-21	13-May-22
P12-E	TBE For Gas Compressors	45	100%	$947.30	02-Feb-22	13-May-22
P12-E	VDR For Gas Compressors	7	0%	$4,736.52	26-Aug-22	01-Sep-22
HVAC		109	0%	$2,463.86	03-Apr-23	20-Jul-23
Main HVAC Equipment		109	0%	$2,463.86	03-Apr-23	20-Jul-23
P12-E	PMR For Main HVAC Equipment	10	0%	$246.39	03-Apr-23	12-Apr-23
P12-E	TBE For Main HVAC Equipment	45	0%	$369.58	10-Apr-23	24-May-23
P12-E	VDR For Main HVAC Equipment	7	0%	$1,847.89	14-Jul-23	20-Jul-23
Piping		112	0%	$2,759.52	04-Jan-23	25-Apr-23
Painting		59	0%	$236.49	22-Jan-23	21-Mar-23
P12-E	PMR For Painting	10	0%	$23.65	22-Jan-23	31-Jan-23
P12-E	TBE For Painting	45	0%	$35.47	29-Jan-23	14-Mar-23
P12-E	VDR For Painting	7	0%	$177.37	15-Mar-23	21-Mar-23
Coating of Underground Piping		59	0%	$236.49	22-Jan-23	21-Mar-23
P12-E	PMR For Coating of Underground Piping	10	0%	$23.65	22-Jan-23	31-Jan-23
P12-E	TBE For Coating of Underground Piping	45	0%	$35.47	29-Jan-23	14-Mar-23
P12-E	VDR For Coating of Underground Piping	7	0%	$177.37	15-Mar-23	21-Mar-23
Pipe Supports		94	0%	$236.49	04-Jan-23	07-Apr-23
P12-E	PMR For Pipe Supports	10	0%	$23.65	04-Jan-23	13-Jan-23
P12-E	TBE For Pipe Supports	45	0%	$35.47	11-Jan-23	24-Feb-23
P12-E	VDR For Pipe Supports	7	0%	$177.37	01-Apr-23	07-Apr-23
Insulation		94	0%	$236.49	22-Jan-23	25-Apr-23
P12-E	PMR For Insulation	10	0%	$23.65	22-Jan-23	31-Jan-23
P12-E	TBE For Insulation	45	0%	$35.47	29-Jan-23	14-Mar-23
P12-E	VDR For Insulation	7	0%	$177.37	19-Apr-23	25-Apr-23
Insulation Joints		94	0%	$236.49	22-Jan-23	25-Apr-23
P12-E	PMR For Insulation Joints	10	0%	$23.65	22-Jan-23	31-Jan-23
P12-E	TBE For Insulation Joints	45	0%	$35.47	29-Jan-23	14-Mar-23
P12-E	VDR For Insulation Joints	7	0%	$177.37	19-Apr-23	25-Apr-23
Gaskets		94	0%	$236.49	22-Jan-23	25-Apr-23
P12-E	PMR For Gaskets	10	0%	$23.65	22-Jan-23	31-Jan-23
P12-E	TBE For Gaskets	45	0%	$35.47	29-Jan-23	14-Mar-23
P12-E	VDR For Gaskets	7	0%	$177.37	19-Apr-23	25-Apr-23
Flanges		94	0%	$236.49	22-Jan-23	25-Apr-23
P12-E	PMR For Flanges	10	0%	$23.65	22-Jan-23	31-Jan-23
P12-E	TBE For Flanges	45	0%	$35.47	29-Jan-23	14-Mar-23
P12-E	VDR For Flanges	7	0%	$177.37	19-Apr-23	25-Apr-23

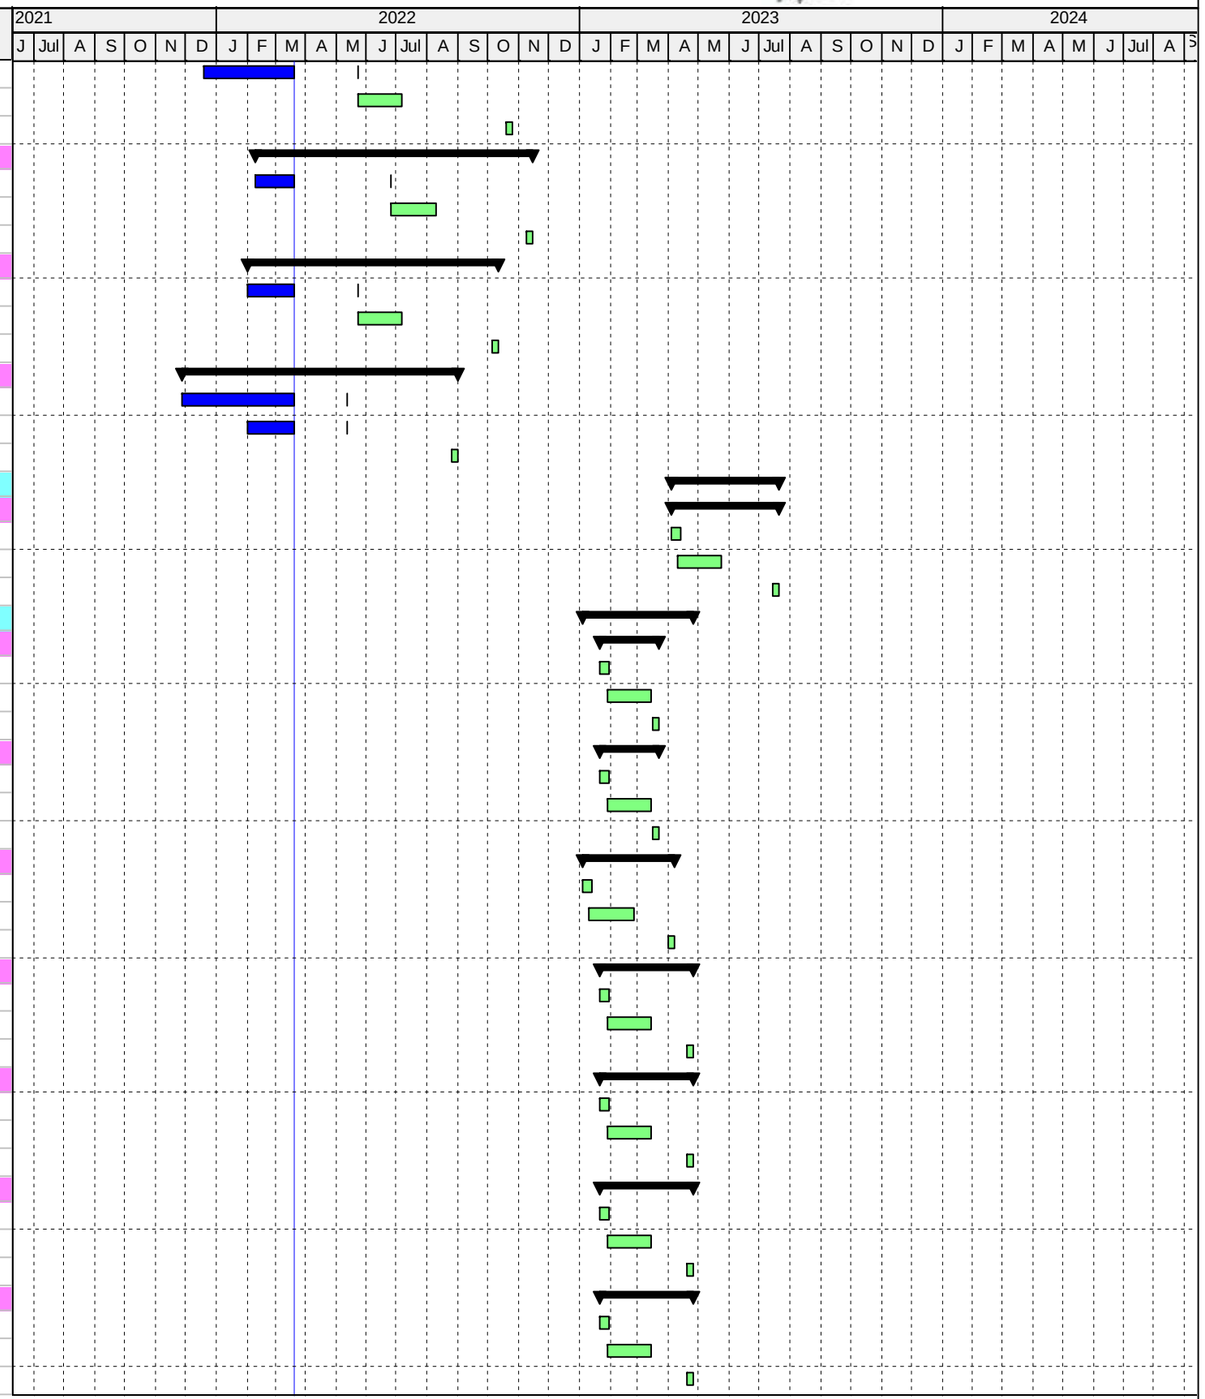


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Strainers		94	0%	$236.49	04-Jan-23	07-Apr-23
P12-E	PMR For Strainers	10	0%	$23.65	04-Jan-23	13-Jan-23
P12-E	TBE For Strainers	45	0%	$35.47	11-Jan-23	24-Feb-23
P12-E	VDR For Strainers	7	0%	$177.37	01-Apr-23	07-Apr-23
Bolt & Nuts		62	0%	$157.57	22-Jan-23	24-Mar-23
P12-E	PMR For Bolt/Nuts	10	0%	$15.76	22-Jan-23	31-Jan-23
P12-E	PMR For Bolt/Nuts	10	0%	$23.64	01-Feb-23	10-Feb-23
P12-E	VDR For Bolt/Nuts	7	0%	$118.18	18-Mar-23	24-Mar-23
Pipes		94	0%	$236.77	22-Jan-23	25-Apr-23
P12-E	PMR For Pipes	10	0%	$23.68	22-Jan-23	31-Jan-23
P12-E	TBE For Pipes	45	0%	$35.52	29-Jan-23	14-Mar-23
P12-E	VDR For Pipes	7	0%	$177.58	19-Apr-23	25-Apr-23
Manual Valves		94	0%	$236.49	22-Jan-23	25-Apr-23
P12-E	PMR For Manual Valves	10	0%	$23.65	22-Jan-23	31-Jan-23
P12-E	TBE For Manual Valves	45	0%	$35.47	29-Jan-23	14-Mar-23
P12-E	VDR For Manual Valves	7	0%	$177.37	19-Apr-23	25-Apr-23
Fittings		94	0%	$236.77	22-Jan-23	25-Apr-23
P12-E	PMR For Fittings	10	0%	$23.68	22-Jan-23	31-Jan-23
P12-E	TBE For Fitting	45	0%	$35.52	29-Jan-23	14-Mar-23
P12-E	VDR For Fitting	7	0%	$177.58	19-Apr-23	25-Apr-23
Control & Instrumentation		359	0.34%	$10,024.38	20-Dec-21	24-Apr-23
Rotameter		109	0%	$444.08	09-Aug-22	25-Nov-22
P12-E	PMR For Rotameter	10	0%	$44.41	09-Aug-22	18-Aug-22
P12-E	TBE For Rotameter	45	0%	$66.61	16-Aug-22	29-Sep-22
P12-E	VDR For Rotameter	7	0%	$333.06	19-Nov-22	25-Nov-22
Displacer Level Transmitter		109	0%	$444.08	09-Aug-22	25-Nov-22
P12-E	PMR For Displacer Level Transmitter	10	0%	$44.41	09-Aug-22	18-Aug-22
P12-E	TBE For Displacer Level Transmitter	45	0%	$66.61	16-Aug-22	29-Sep-22
P12-E	VDR For Displacer Level Transmitter	7	0%	$333.06	19-Nov-22	25-Nov-22
Level Switch		177	0%	$444.08	01-May-22	24-Oct-22
P12-E	PMR For Level Switch	10	0%	$44.41	01-May-22	10-May-22
P12-E	TBE For Level Switch	45	0%	$66.61	08-May-22	21-Jun-22
P12-E	VDR For Level Switch	7	0%	$333.06	18-Oct-22	24-Oct-22
Level Gauge		109	0%	$444.08	09-Aug-22	25-Nov-22
P12-E	PMR For Level Gauge	10	0%	$44.41	09-Aug-22	18-Aug-22
P12-E	TBE For Level Gauge	45	0%	$66.61	16-Aug-22	29-Sep-22
P12-E	VDR For Level Gauge	7	0%	$333.06	19-Nov-22	25-Nov-22
Temperature Transmitter/Switch		109	0%	$340.83	09-Aug-22	25-Nov-22
P12-E	PMR For Temperature Transmitter/Switch	10	0%	$34.08	09-Aug-22	18-Aug-22
P12-E	TBE For Temperature Transmitter/Switch	45	0%	$51.12	16-Aug-22	29-Sep-22
P12-E	VDR For Temperature Transmitter/Switch	7	0%	$255.62	19-Nov-22	25-Nov-22
Temperature Gauge		109	0%	$340.83	09-Aug-22	25-Nov-22
P12-E	PMR For Temperature Gauge	10	0%	$34.08	09-Aug-22	18-Aug-22
P12-E	TBE For Temperature Gauge	45	0%	$51.12	16-Aug-22	29-Sep-22
P12-E	VDR For Temperature Gauge	7	0%	$255.62	19-Nov-22	25-Nov-22
Pressure/ Differential Pressure Switch		109	0%	$444.08	01-May-22	17-Aug-22
P12-E	PMR For Pressure/ Differential Pressure Switch	10	0%	$44.41	01-May-22	10-May-22
P12-E	TBE For Pressure/ Differential Pressure Switch	45	0%	$66.61	08-May-22	21-Jun-22
P12-E	VDR For Pressure/ Differential Pressure Switch	7	0%	$333.06	11-Aug-22	17-Aug-22

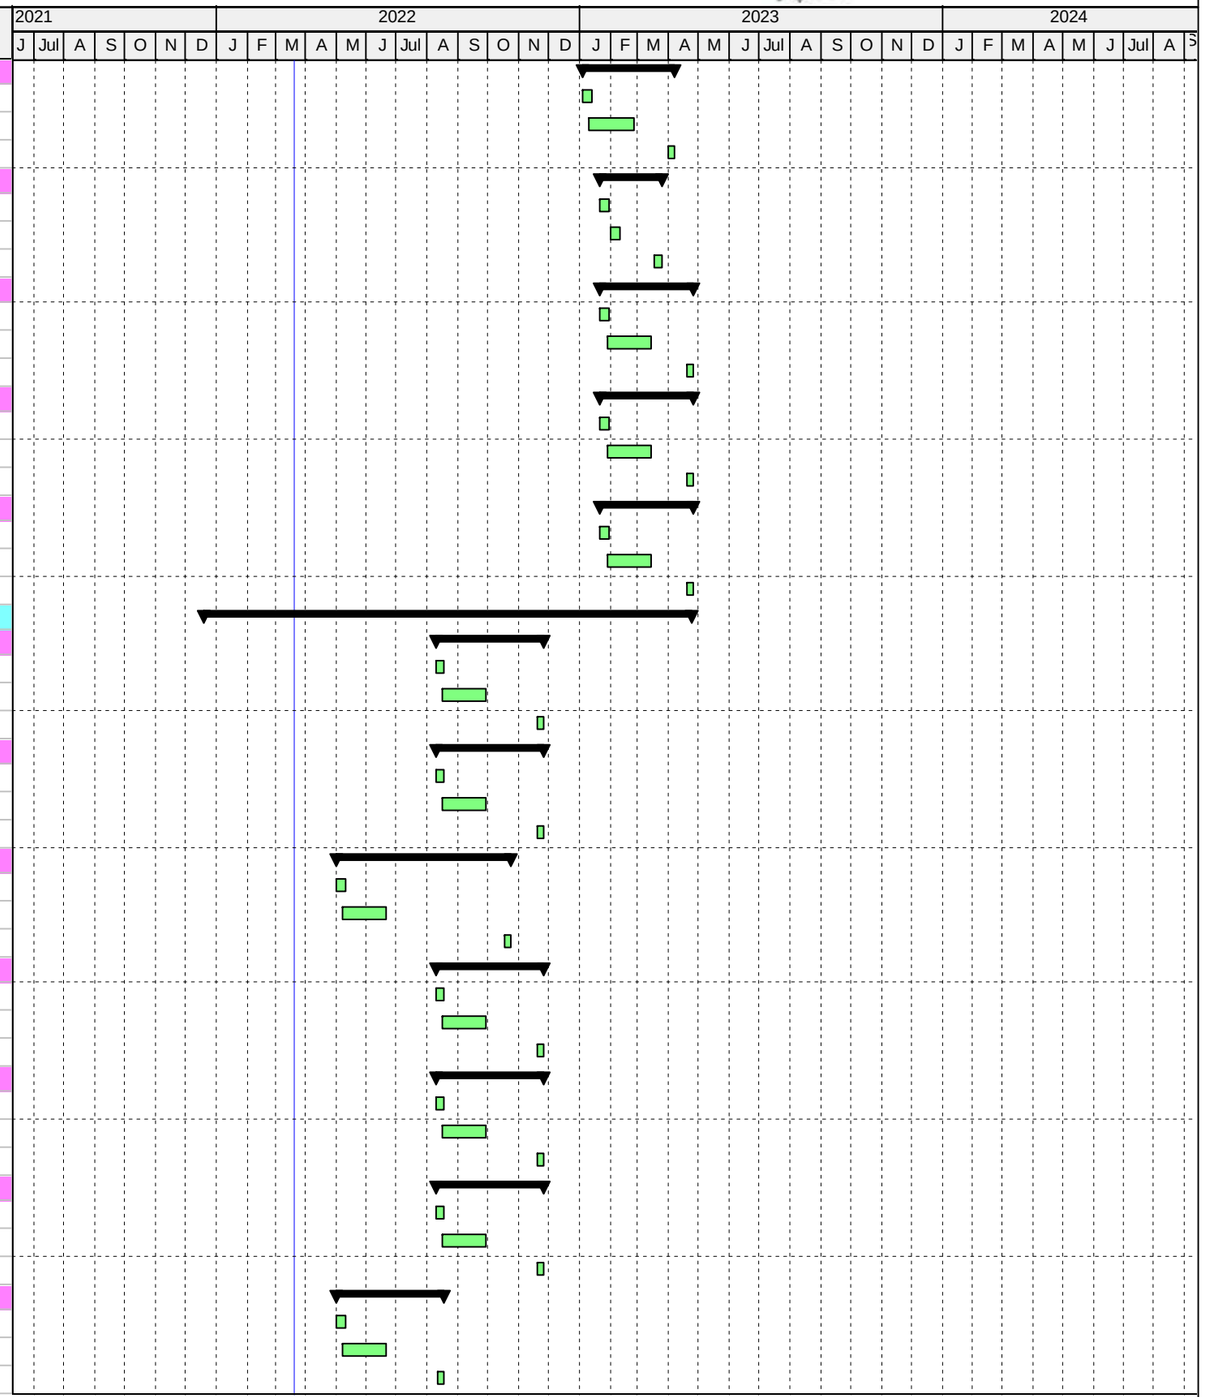


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Flow/Level /Pressure/Diff. Pressure Transmitter		258	0%	$444.08	10-Aug-22	24-Apr-23
P12-E	PMR For DP Flow /DP Level /Pressure/Diff. Pressure Transm	10	0%	$44.41	10-Aug-22	19-Aug-22
P12-E	TBE For DP Flow /DP Level /Pressure/Diff. Pressure Transm	45	0%	$66.61	17-Aug-22	30-Sep-22
P12-E	VDR For DP Flow /DP Level /Pressure/Diff. Pressure Transm	7	0%	$333.06	18-Apr-23	24-Apr-23
Differential Pressure/Pressure Gauge		110	0%	$340.83	09-Aug-22	26-Nov-22
P12-E	PMR For Differential Pressure/Pressure Gauge	10	0%	$34.08	09-Aug-22	18-Aug-22
P12-E	TBE For Differential Pressure/Pressure Gauge	45	0%	$51.12	16-Aug-22	29-Sep-22
P12-E	VDR For Differential Pressure/Pressure Gauge	7	0%	$255.62	20-Nov-22	26-Nov-22
Orifice and Restriction Orifice Plate		109	0%	$444.08	10-Aug-22	26-Nov-22
P12-E	PMR For Orifice and Restriction Orifice Plate	10	0%	$44.41	10-Aug-22	19-Aug-22
P12-E	TBE For Orifice and Restriction Orifice Plate	45	0%	$66.61	17-Aug-22	30-Sep-22
P12-E	VDR For Orifice and Restriction Orifice Plate	7	0%	$333.06	20-Nov-22	26-Nov-22
Corrosion Probe/Coupon		109	0%	$340.83	10-Aug-22	26-Nov-22
P12-E	PMR For Corrosion Probe/Coupon	10	0%	$34.08	10-Aug-22	19-Aug-22
P12-E	TBE For Corrosion Probe/Coupon	45	0%	$51.12	17-Aug-22	30-Sep-22
P12-E	VDR For Corrosion Probe/Coupon	7	0%	$255.62	20-Nov-22	26-Nov-22
F&G Devices		90	0%	$339.83	26-Jun-22	23-Sep-22
P12-E	PMR For F&G Devices	10	0%	$33.98	26-Jun-22	05-Jul-22
P12-E	TBE For F&G Devices	45	0%	$50.97	03-Jul-22	16-Aug-22
P12-E	VDR For F&G Devices	7	0%	$254.87	17-Sep-22	23-Sep-22
Pressure Safety Valves (PSV)		149	0%	$339.83	14-Aug-22	09-Jan-23
P12-E	PMR For Pressure Safety Valves (PSV)	10	0%	$33.98	14-Aug-22	23-Aug-22
P12-E	TBE For Pressure Safety Valves (PSV)	45	0%	$50.97	21-Aug-22	04-Oct-22
P12-E	VDR For Pressure Safety Valves (PSV)	7	0%	$254.87	03-Jan-23	09-Jan-23
ON/OFF & Shutdown Valves		144	0%	$340.83	14-Aug-22	04-Jan-23
P12-E	PMR For On/off & Shutdown Valves	10	0%	$34.08	14-Aug-22	23-Aug-22
P12-E	TBE For On/off & Shutdown Valves	45	0%	$51.12	21-Aug-22	04-Oct-22
P12-E	VDR For On/off & Shutdown Valves	7	0%	$255.62	29-Dec-22	04-Jan-23
Control Valves		149	0%	$613.49	14-Aug-22	09-Jan-23
P12-E	PMR For Control Valves	10	0%	$61.35	14-Aug-22	23-Aug-22
P12-E	TBE For Control Valves	45	0%	$92.02	21-Aug-22	04-Oct-22
P12-E	VDR For Control Valves	7	0%	$460.12	03-Jan-23	09-Jan-23
F&G System		193	0%	$444.08	13-May-22	21-Nov-22
P12-E	PMR For F&G System	10	0%	$44.41	13-May-22	22-May-22
P12-E	TBE For F&G System	45	0%	$66.61	20-May-22	03-Jul-22
P12-E	VDR For F&G System	7	0%	$333.06	15-Nov-22	21-Nov-22
Control System/Console/Furniture		144	0%	$444.08	21-Jun-22	11-Nov-22
P12-E	PMR For Control System/Console/Furniture	10	0%	$44.41	21-Jun-22	30-Jun-22
P12-E	TBE For Control System/Console/Furniture	45	0%	$66.61	28-Jun-22	11-Aug-22
P12-E	VDR For Control System/Console/Furniture	7	0%	$333.06	05-Nov-22	11-Nov-22
ESD System		139	0%	$444.08	13-May-22	28-Sep-22
P12-E	PMR For ESD System	10	0%	$44.41	13-May-22	22-May-22
P12-E	TBE For ESD System	45	0%	$66.61	20-May-22	03-Jul-22
P12-E	VDR For ESD System	7	0%	$333.06	22-Sep-22	28-Sep-22
Instrument/F&G Cable		134	0%	$444.08	20-May-22	30-Sep-22
P12-E	PMR For Instrument/F&G cable	10	0%	$44.41	20-May-22	29-May-22
P12-E	TBE For Instrument/F&G cable	45	0%	$66.61	27-May-22	10-Jul-22
P12-E	VDR For Instrument/F&G cable	7	0%	$333.06	24-Sep-22	30-Sep-22
Instrument Cable Tray		109	0%	$339.83	03-Dec-22	21-Mar-23

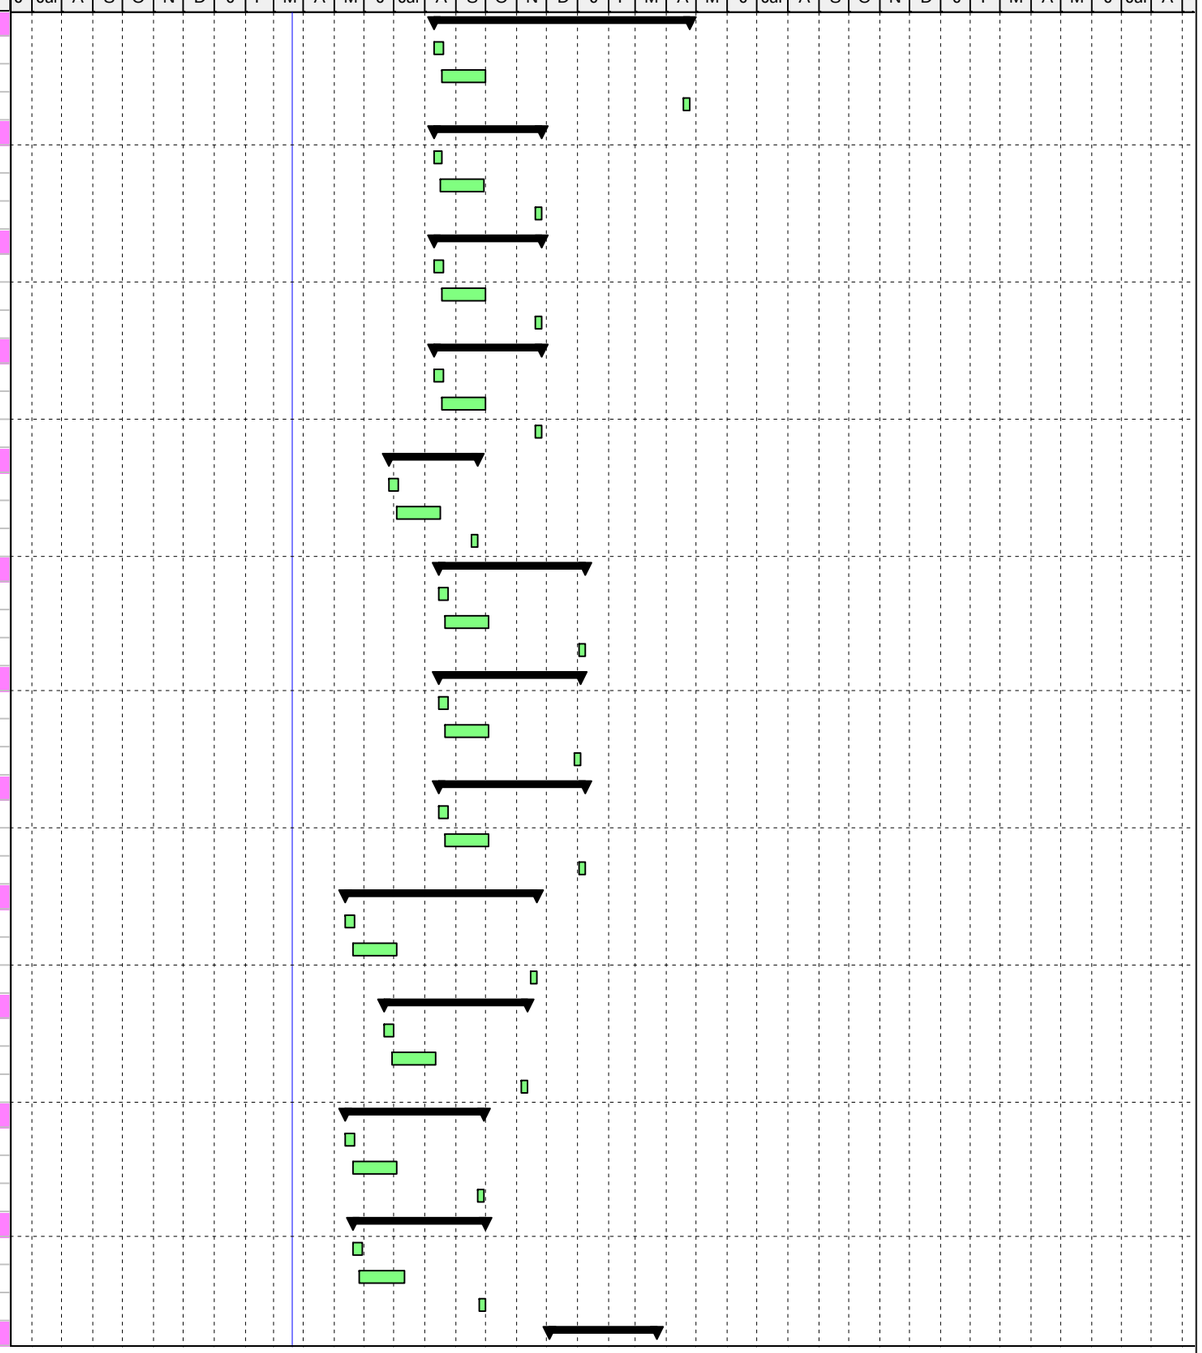


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	PMR For Instrument Cable Tray	10	0%	$33.98	03-Dec-22	12-Dec-22
P12-E	TBE For Instrument Cable Tray	45	0%	$50.97	10-Dec-22	23-Jan-23
P12-E	VDR For Instrument Cable Tray	7	0%	$254.87	15-Mar-23	21-Mar-23
Instrument/F&G Junction box and Gland		109	0%	$443.08	20-May-22	05-Sep-22
P12-E	PMR For Instrument/F&G Junction box and Gland	10	0%	$44.31	20-May-22	29-May-22
P12-E	TBE For Instrument/F&G Junction box and Gland	45	0%	$66.46	27-May-22	10-Jul-22
P12-E	VDR For Instrument/F&G Junction box and Gland	7	0%	$332.31	30-Aug-22	05-Sep-22
Instrument Tube and Fitting		109	0%	$339.83	21-Aug-22	07-Dec-22
P12-E	PMR For Instrument Tube and Fitting	10	0%	$33.98	21-Aug-22	30-Aug-22
P12-E	TBE For Instrument Tube and Fitting	45	0%	$50.97	28-Aug-22	11-Oct-22
P12-E	VDR For Instrument Tube and Fitting	7	0%	$254.87	01-Dec-22	07-Dec-22
Instrument Installation Accessories		289	0%	$339.83	08-Jul-22	22-Apr-23
P12-E	PMR For Instrument Installation Accessories	10	0%	$33.98	08-Jul-22	17-Jul-22
P12-E	TBE For Instrument Installation Accessories	45	0%	$50.97	15-Jul-22	28-Aug-22
P12-E	VDR For Instrument Installation Accessories	7	0%	$254.87	16-Apr-23	22-Apr-23
CCTV System		102	10%	$339.83	20-Dec-21	07-Oct-22
P12-E	PMR For CCTV System	10	100%	$33.98	20-Dec-21	28-Jun-22
P12-E	TBE For CCTV System	45	0%	$50.97	28-Jun-22	11-Aug-22
P12-E	VDR For CCTV System	7	0%	$254.87	01-Oct-22	07-Oct-22
IRP Panel		26	0%	$339.83	26-Jun-22	21-Jul-22
P12-E	PMR For IPR Panel	20	0%	$33.98	26-Jun-22	15-Jul-22
P12-E	TBE For IPR Panel	12	0%	$50.97	03-Jul-22	14-Jul-22
P12-E	VDR For IPR Panel	7	0%	$254.87	15-Jul-22	21-Jul-22
Safety & Fire Fighting		140	0%	$5,652.79	13-May-22	29-Sep-22
Safety Signs		52	0%	$875.62	03-Jul-22	23-Aug-22
P12-E	PMR For Safety Signs	10	0%	$87.56	03-Jul-22	12-Jul-22
P12-E	TBE For Safety Signs	45	0%	$131.34	10-Jul-22	23-Aug-22
P12-E	VDR For Safety Signs	7	0%	$656.71	11-Jul-22	17-Jul-22
Fire Fighting Equipment		59	0%	$1,194.43	20-May-22	17-Jul-22
P12-E	PMR For Fire Fighting Equipment	10	0%	$119.44	20-May-22	29-May-22
P12-E	TBE For Fire Fighting Equipment	45	0%	$179.17	27-May-22	10-Jul-22
P12-E	VDR For Fire Fighting Equipment	7	0%	$895.83	11-Jul-22	17-Jul-22
Safety Equipment		59	0%	$1,194.43	20-May-22	17-Jul-22
P12-E	PMR For Safety Equipment	10	0%	$119.44	20-May-22	29-May-22
P12-E	TBE For Safety Equipment	45	0%	$179.17	27-May-22	10-Jul-22
P12-E	VDR For Safety Equipment	7	0%	$895.83	11-Jul-22	17-Jul-22
Deluge Valve & Water Spray		81	0%	$1,194.43	11-Jul-22	29-Sep-22
P12-E	PMR For Deluge Valve & Water Spray	10	0%	$119.44	09-Aug-22	18-Aug-22
P12-E	TBE For Deluge Valve & Water Spray	45	0%	$179.17	16-Aug-22	29-Sep-22
P12-E	VDR For Deluge Valve & Water Spray	7	0%	$895.83	11-Jul-22	17-Jul-22
Total Flooding System		66	0%	$1,193.87	13-May-22	17-Jul-22
P12-E	PMR For Total Flooding System	10	0%	$119.39	13-May-22	22-May-22
P12-E	TBE For Total Flooding System	45	0%	$179.08	20-May-22	03-Jul-22
P12-E	VDR For Total Flooding System	7	0%	$895.40	11-Jul-22	17-Jul-22
Electrical		464	0%	$12,614.95	18-May-22	24-Aug-23
Telecomm UPS		214	0%	$604.26	26-Aug-22	27-Mar-23
P12-E	PMR For UPS of CCTV in Desalting, Production & CS Unit	10	0%	$60.43	26-Aug-22	04-Sep-22
P12-E	TBE for UPS of CCTV in Desalting, Production & CS Unit	45	0%	$90.64	02-Sep-22	16-Oct-22
P12-E	VDR for UPS of CCTV in Desalting, Production & CS Unit	7	0%	$453.19	21-Mar-23	27-Mar-23

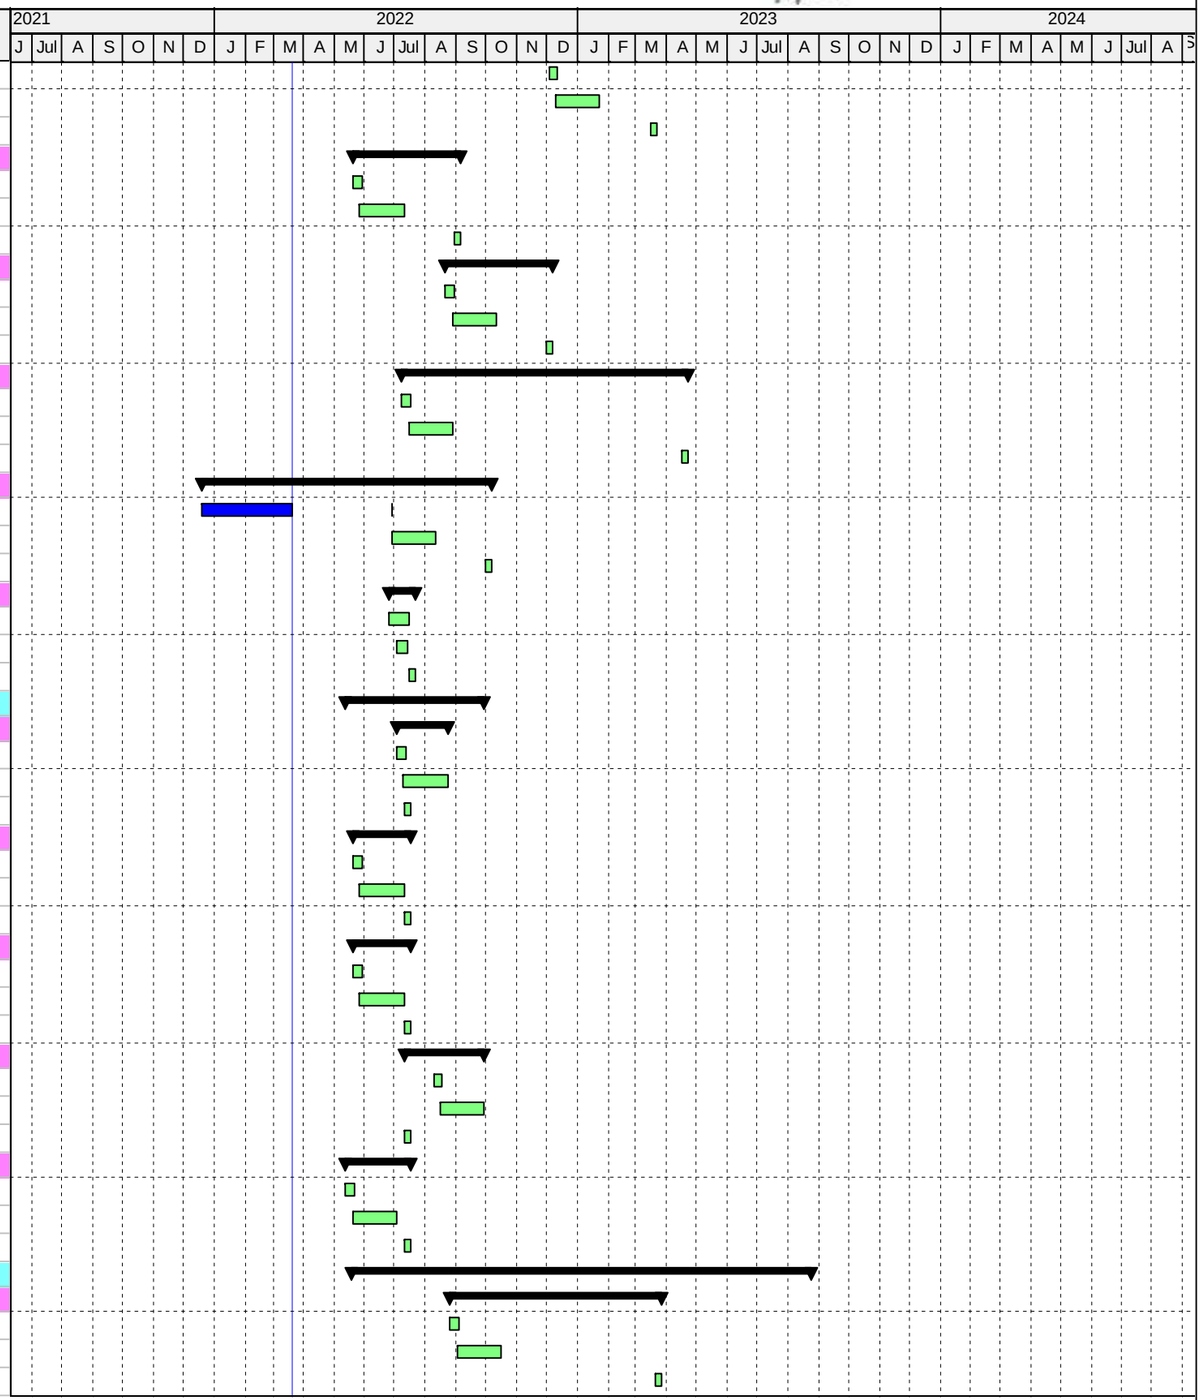


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Electrical Bulk Items		109	0%	$604.26	08-Oct-22	24-Jan-23
P12-E	PMR For Electrical Bulk Items	10	0%	$60.43	08-Oct-22	17-Oct-22
P12-E	TBE For Electrical Bulk Items	45	0%	$90.64	15-Oct-22	28-Nov-22
P12-E	VDR For Electrical Bulk Items	7	0%	$453.19	18-Jan-23	24-Jan-23
Tray/Ladder and Accessories		59	0%	$604.26	16-Dec-22	12-Feb-23
P12-E	PMR For Tray/Ladder and Accessories	10	0%	$60.43	16-Dec-22	25-Dec-22
P12-E	TBE For Tray/Ladder and Accessories	45	0%	$90.64	23-Dec-22	05-Feb-23
P12-E	VDR For Tray/Ladder and Accessories	7	0%	$453.19	06-Feb-23	12-Feb-23
Power & Control Cables		109	0%	$604.26	25-Sep-22	11-Jan-23
P12-E	PMR For Power & Control Cables	10	0%	$60.43	25-Sep-22	04-Oct-22
P12-E	TBE For Power & Control Cables	45	0%	$90.64	02-Oct-22	15-Nov-22
P12-E	VDR For Power & Control Cables	7	0%	$453.19	05-Jan-23	11-Jan-23
Cathodic Protection System		139	0%	$907.01	08-Apr-23	24-Aug-23
P12-E	VDR For Cathodic Protection System	7	0%	$680.26	18-Aug-23	24-Aug-23
P12-E	PMR For Cathodic Protection System	10	0%	$90.70	08-Apr-23	17-Apr-23
P12-E	TBE For Cathodic Protection System	45	0%	$136.05	15-Apr-23	29-May-23
NGR System		59	0%	$604.26	21-Jul-22	17-Sep-22
P12-E	PMR For NGR	10	0%	$60.43	21-Jul-22	30-Jul-22
P12-E	TBE For NGR	45	0%	$90.64	28-Jul-22	10-Sep-22
P12-E	VDR For NGR	7	0%	$453.19	11-Sep-22	17-Sep-22
Capacitor Bank		52	0%	$604.26	07-Jun-22	28-Jul-22
P12-E	PMR For Capacitor Bank	10	0%	$60.43	07-Jun-22	16-Jun-22
P12-E	TBE For Capacitor Bank	45	0%	$90.64	14-Jun-22	28-Jul-22
P12-E	VDR For Capacitor Bank	7	0%	$453.19	09-Jul-22	15-Jul-22
Local Control Station (LCS)		59	0%	$604.26	18-May-22	15-Jul-22
P12-E	PMR For Local Control Station (LCS)	10	0%	$60.43	18-May-22	27-May-22
P12-E	TBE For Local Control Station (LCS)	45	0%	$90.64	25-May-22	08-Jul-22
P12-E	VDR For Local Control Station (LCS)	7	0%	$453.19	09-Jul-22	15-Jul-22
Earthing & Lightning System		109	0%	$604.26	20-Oct-22	05-Feb-23
P12-E	PMR For Earthing & Lightning System	10	0%	$60.43	20-Oct-22	29-Oct-22
P12-E	TBE For Earthing & Lightning System	45	0%	$90.64	27-Oct-22	10-Dec-22
P12-E	VDR For Earthing & Lightning System	7	0%	$453.19	30-Jan-23	05-Feb-23
Lighting and Small Power Equipment		109	0%	$604.26	08-Oct-22	24-Jan-23
P12-E	PMR For Lighting and Small Power Equipment	10	0%	$60.43	08-Oct-22	17-Oct-22
P12-E	TBE For Lighting and Small Power Equipment	45	0%	$90.64	15-Oct-22	28-Nov-22
P12-E	VDR For Lighting and Small Power Equipment	7	0%	$453.19	18-Jan-23	24-Jan-23
Lighting & Distribution Panels		109	0%	$604.26	24-Nov-22	12-Mar-23
P12-E	PMR For Lighting & Distribution Panels	10	0%	$60.43	24-Nov-22	03-Dec-22
P12-E	TBE For Lighting & Distribution Panels	45	0%	$90.64	01-Dec-22	14-Jan-23
P12-E	VDR For Lighting & Distribution Panels	7	0%	$453.19	06-Mar-23	12-Mar-23
DC Charger		59	0%	$755.64	02-Jun-22	30-Jul-22
P12-E	PMR For DC Charger	10	0%	$75.56	02-Jun-22	11-Jun-22
P12-E	TBE For DC Charger	45	0%	$113.35	09-Jun-22	23-Jul-22
P12-E	VDR For DC Charger	7	0%	$566.73	24-Jul-22	30-Jul-22
UPS System		124	0%	$755.64	04-Aug-22	05-Dec-22
P12-E	PMR For UPS System	10	0%	$75.56	04-Aug-22	13-Aug-22
P12-E	TBE For UPS System	45	0%	$113.35	11-Aug-22	24-Sep-22
P12-E	VDR For UPS System	7	0%	$566.73	29-Nov-22	05-Dec-22
Emergency Diesel Generator		59	0%	$755.64	23-May-22	20-Jul-22

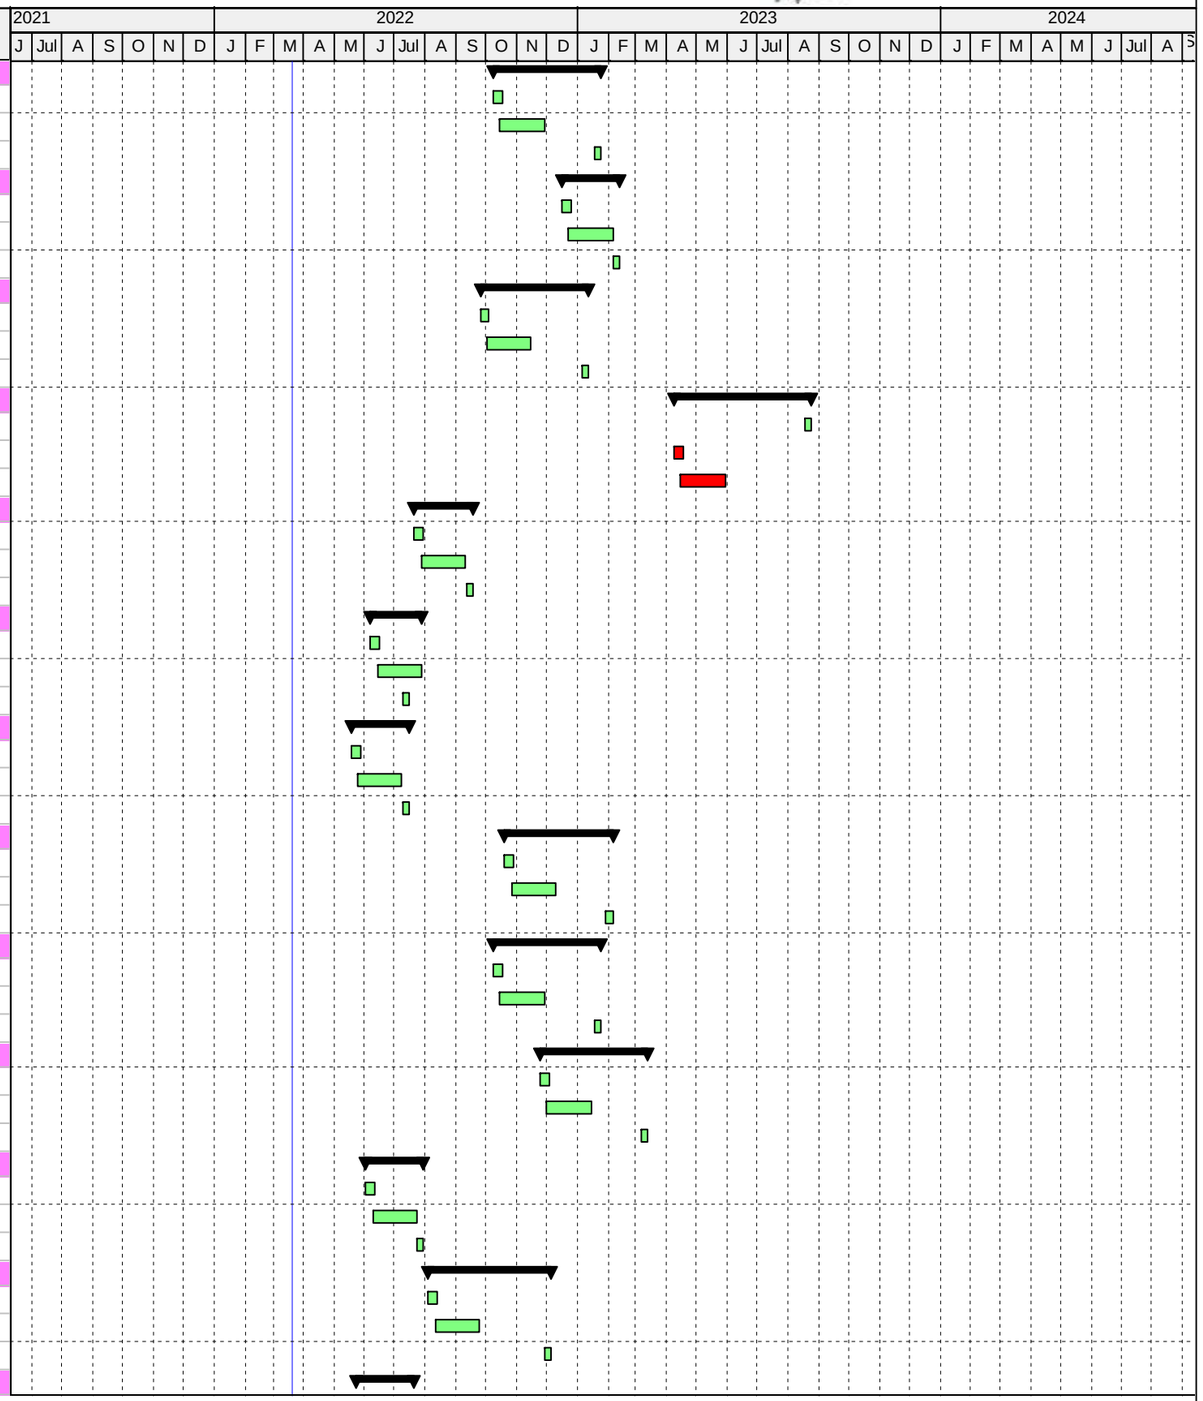


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	PMR For Emergency Diesel Generator	10	0%	$75.56	23-May-22	01-Jun-22
P12-E	TBE For Emergency Diesel Generator	45	0%	$113.35	30-May-22	13-Jul-22
P12-E	VDR For Emergency Diesel Generator	7	0%	$566.73	14-Jul-22	20-Jul-22
Existent MV Switchgear Expansion		59	0%	$1,132.82	21-May-22	18-Jul-22
P12-E	PMR For Existent MV Switchgear Expansion & RCP	10	0%	$113.28	21-May-22	30-May-22
P12-E	TBE For Existent MV Switchgear Expansion & RCP	45	0%	$169.92	28-May-22	11-Jul-22
P12-E	VDR For Existent MV Switchgear Expansion & RCP	7	0%	$849.62	12-Jul-22	18-Jul-22
LV Switchgear & MCC		59	0%	$1,511.27	21-May-22	18-Jul-22
P12-E	PMR For LV Switchgear, MCC	10	0%	$151.13	21-May-22	30-May-22
P12-E	TBE For LV Switchgear, MCC	45	0%	$226.69	28-May-22	11-Jul-22
P12-E	VDR For LV Switchgear, MCC	7	0%	$1,133.45	12-Jul-22	18-Jul-22
Transformers		149	0%	$754.37	18-May-22	13-Oct-22
P12-E	PMR For Transformers	10	0%	$75.44	18-May-22	27-May-22
P12-E	TBE For Transformers	45	0%	$113.16	25-May-22	08-Jul-22
P12-E	VDR For Transformers	7	0%	$565.78	07-Oct-22	13-Oct-22
Intercom. & Telecomm.		473	2%	$4,744.68	20-Dec-21	09-Jul-23
PAGA System		59	0%	$948.94	31-Oct-22	28-Dec-22
P12-E	PMR For PAGA System	10	0%	$94.89	31-Oct-22	09-Nov-22
P12-E	TBE For PAGA System	45	0%	$142.34	07-Nov-22	21-Dec-22
P12-E	VDR For PAGA System	7	0%	$711.70	22-Dec-22	28-Dec-22
PABX System		59	0%	$948.94	16-Mar-23	13-May-23
P12-E	PMR For PABX System	10	0%	$94.89	16-Mar-23	25-Mar-23
P12-E	TBE For PABX System	45	0%	$142.34	23-Mar-23	06-May-23
P12-E	VDR For PABX System	7	0%	$711.70	07-May-23	13-May-23
Radio System		119	10%	$948.94	20-Dec-21	03-Jul-22
P12-E	PMR For Radio System	10	100%	$94.89	20-Dec-21	24-Mar-22
P12-E	TBE For Radio System	45	0%	$142.34	24-Mar-22	07-May-22
P12-E	VDR For Radio System	7	0%	$711.70	27-Jun-22	03-Jul-22
Telecomm. Cable		150	0%	$948.94	10-Feb-23	09-Jul-23
P12-E	PMR For Telecomm. Cable	10	0%	$94.89	19-May-23	28-May-23
P12-E	TBE For Telecomm. Cable	45	0%	$142.34	26-May-23	09-Jul-23
P12-E	VDR For Telecomm. Cable	7	0%	$711.70	10-Feb-23	16-Feb-23
Telecommunication Tower		109	0%	$948.94	27-Mar-22	13-Jul-22
P12-E	PMR For Telecommunication Tower	10	0%	$94.89	27-Mar-22	05-Apr-22
P12-E	TBE For Telecommunication Tower	45	0%	$142.34	03-Apr-22	17-May-22
P12-E	VDR For Telecommunication Tower	7	0%	$711.70	07-Jul-22	13-Jul-22
Structure		69	0%	$2,062.60	22-Jan-23	31-Mar-23
Blast Proof Doors		59	0%	$687.46	01-Feb-23	31-Mar-23
P12-E	PMR For Blast Proof Doors	10	0%	$68.75	01-Feb-23	10-Feb-23
P12-E	TBE For Blast Proof Doors	45	0%	$103.12	08-Feb-23	24-Mar-23
P12-E	VDR For Blast Proof Doors	7	0%	$515.60	25-Mar-23	31-Mar-23
Anchor Bolts		59	0%	$687.46	01-Feb-23	31-Mar-23
P12-E	PMR For Anchor Bolts	10	0%	$68.75	01-Feb-23	10-Feb-23
P12-E	TBE For Anchor Bolts	45	0%	$103.12	08-Feb-23	24-Mar-23
P12-E	VDR For Anchor Bolts	7	0%	$515.60	25-Mar-23	31-Mar-23
Steel Structure		59	0%	$687.67	22-Jan-23	21-Mar-23
P12-E	PMR For Steel Structure Items	10	0%	$68.77	22-Jan-23	31-Jan-23
P12-E	TBE For Steel Structure Items	45	0%	$103.15	29-Jan-23	14-Mar-23
P12-E	VDR For Steel Structure Items	7	0%	$515.75	15-Mar-23	21-Mar-23

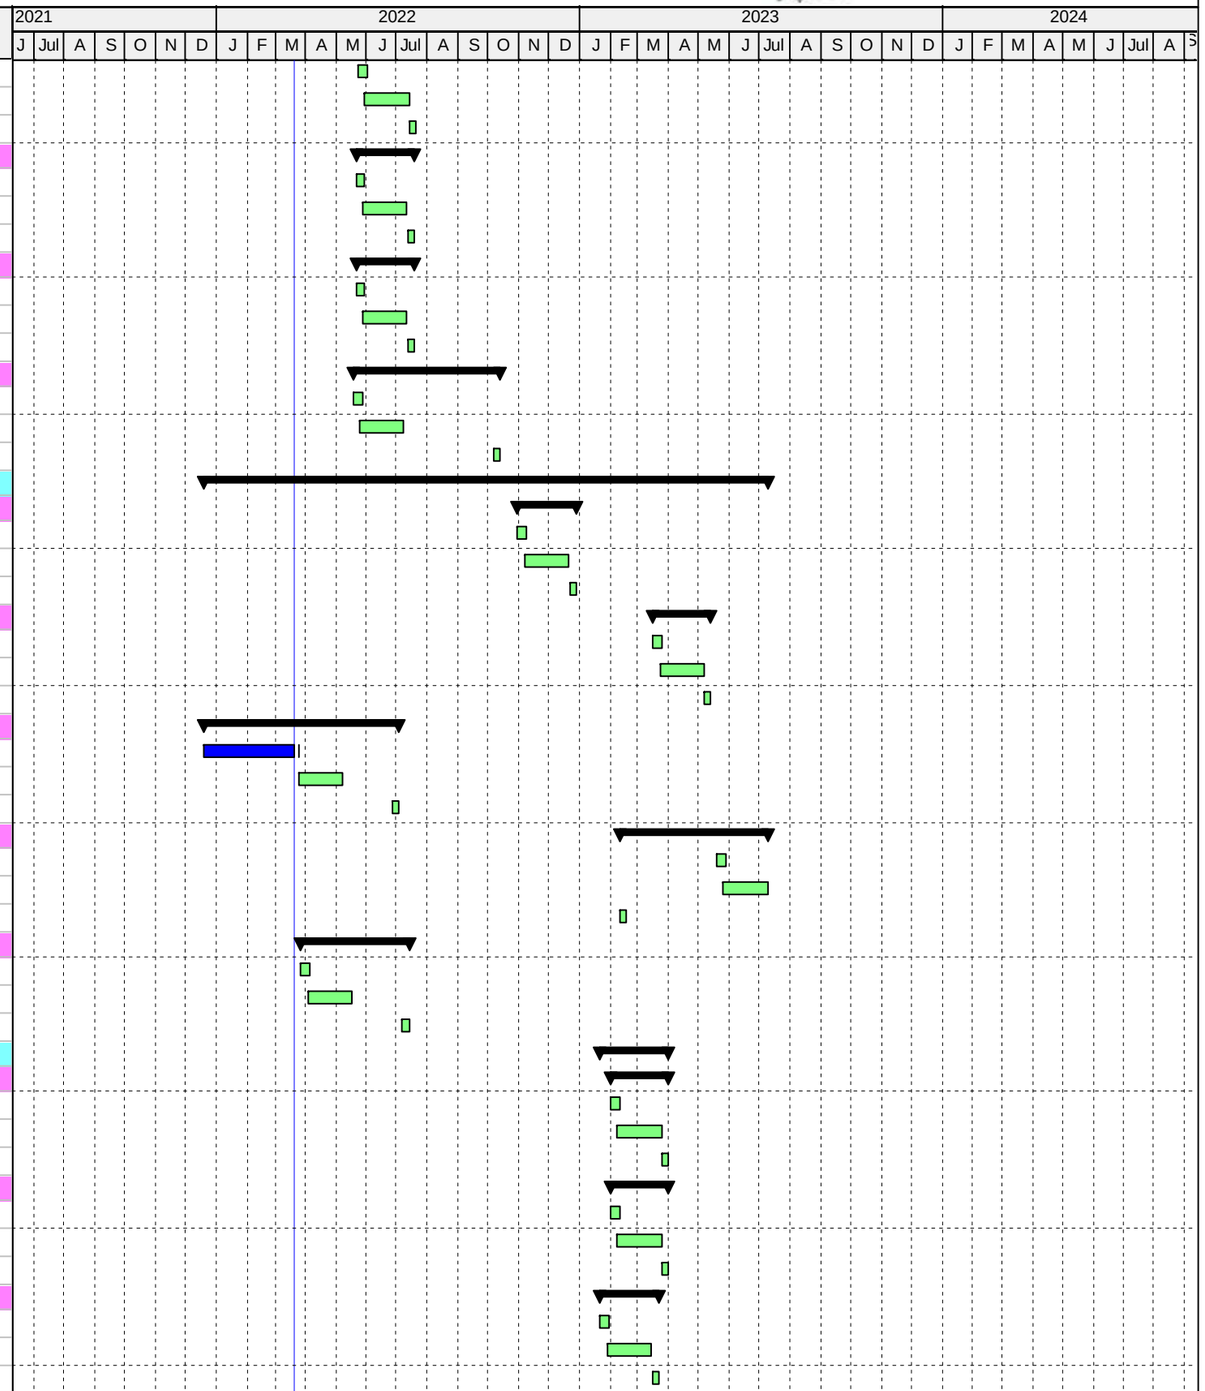

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Commissioning Engineering		739	0%	$14,079.18	20-Mar-22	27-Mar-24
P12-EP	Operability Review	5	0%	$2,815.84	03-May-22	07-May-22
P12-EP	Pre-Commissioning, Commissioning & Startup Procedure	44	0%	$8,447.51	20-Mar-22	02-May-22
P12-EP	Operating Manual	30	0%	$2,815.84	27-Feb-24	27-Mar-24
Field Engineering		629	0%	$105,593.85	18-Jul-22	06-Apr-24
P12-EP	Technical/Site Queries	44	0%	$52,796.93	18-Jul-22	30-Aug-22
P12-EP	As-Built Document Booklets	10	0%	$52,796.93	28-Mar-24	06-Apr-24
Engineering Final Documentation		44	0%	$70,395.90	07-Apr-24	20-May-24
P12-EP	Final Engineering Dossier	44	0%	$70,395.90	07-Apr-24	20-May-24
PROCUREMENT		667	0%	$17,336,310.02	08-May-22	04-Mar-24
Main Procurement		647	0%	$13,869,048.02	08-May-22	13-Feb-24
Mechanical		575	0%	$8,970,500.26	23-May-22	18-Dec-23
Gas Compressors		575	0%	$4,984,906.99	23-May-22	18-Dec-23
Gas Compressor of first & Second Stage		575	0%	$4,984,906.99	23-May-22	18-Dec-23
P12-	Tendering & Selection	60	0%	$199,396.28	23-May-22	21-Jul-22
P12-	Contract Effectiveness / PO	35	0%	$299,094.42	22-Jul-22	25-Aug-22
P12-	Manufacturing / Fabrication / Supply	480	0%	$4,486,416.29	26-Aug-22	18-Dec-23
Gas Dehydration Package		460	0%	$1,664,027.80	17-Jul-22	19-Oct-23
Dehydration Package		460	0%	$1,664,027.80	17-Jul-22	19-Oct-23
P12-	Tendering & Selection	65	0%	$66,561.11	17-Jul-22	19-Sep-22
P12-	Contract Effectiveness / PO	30	0%	$99,841.67	20-Sep-22	19-Oct-22
P12-	Manufacturing / Fabrication / Supply	365	0%	$1,497,625.02	20-Oct-22	19-Oct-23
Pressure Vessels		385	0%	$248,482.86	27-Jul-22	15-Aug-23
Inlet Knock Out Drum		360	0%	$4,646.63	06-Aug-22	31-Jul-23
P12-	Tendering & Selection	60	0%	$185.87	06-Aug-22	04-Oct-22
P12-	Contract Effectiveness / PO	30	0%	$278.80	05-Oct-22	03-Nov-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$4,181.97	04-Nov-22	31-Jul-23
1ST STAGE GAS COMPRESSION SUCTION DRUM		360	0%	$32,923.98	27-Jul-22	21-Jul-23
P12-	Tendering & Selection	60	0%	$1,316.96	27-Jul-22	24-Sep-22
P12-	Contract Effectiveness / PO	30	0%	$1,975.44	25-Sep-22	24-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$29,631.58	25-Oct-22	21-Jul-23
2nd STAGE GAS COMPRESSION SUCTION DRUM		380	0%	$26,836.15	27-Jul-22	10-Aug-23
P12-	Tendering & Selection	60	0%	$1,073.45	27-Jul-22	24-Sep-22
P12-	Contract Effectiveness / PO	30	0%	$1,610.17	25-Sep-22	24-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$24,152.53	14-Nov-22	10-Aug-23
2nd STAGE GAS COMPRESSION DISCHARGE DRUM		380	0%	$12,399.29	27-Jul-22	10-Aug-23
P12-	Tendering & Selection	60	0%	$495.97	27-Jul-22	24-Sep-22
P12-	Contract Effectiveness / PO	30	0%	$743.96	25-Sep-22	24-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$11,159.37	14-Nov-22	10-Aug-23
Diesel Oil Storage Tank		385	0%	$22,288.91	27-Jul-22	15-Aug-23
P12-	Tendering & Selection	60	0%	$891.56	27-Jul-22	24-Sep-22
P12-	Contract Effectiveness / PO	30	0%	$1,337.33	25-Sep-22	24-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$20,060.02	19-Nov-22	15-Aug-23
Instrument Air Receiver		360	0%	$11,206.58	27-Jul-22	21-Jul-23
P12-	Tendering & Selection	60	0%	$448.26	27-Jul-22	24-Sep-22
P12-	Contract Effectiveness / PO	30	0%	$672.39	25-Sep-22	24-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$10,085.92	25-Oct-22	21-Jul-23
Close drain drum		360	0%	$41,993.60	27-Jul-22	21-Jul-23
P12-	Tendering & Selection	60	0%	$1,679.74	27-Jul-22	24-Sep-22
P12-	Contract Effectiveness / PO	30	0%	$2,519.62	25-Sep-22	24-Oct-22



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-	Manufacturing / Fabrication / Supply	270	0%	$37,794.24	25-Oct-22	21-Jul-23
Potable Water Drum		360	0%	$1,466.05	27-Jul-22	21-Jul-23
P12-	Tendering & Selection	60	0%	$58.64	27-Jul-22	24-Sep-22
P12-	Contract Effectiveness / PO	30	0%	$87.96	25-Sep-22	24-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$1,319.44	25-Oct-22	21-Jul-23
Flare K.O. Drum		360	0%	$5,988.44	27-Jul-22	21-Jul-23
P12-	Tendering & Selection	60	0%	$239.54	27-Jul-22	24-Sep-22
P12-	Contract Effectiveness / PO	30	0%	$359.31	25-Sep-22	24-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$5,389.59	25-Oct-22	21-Jul-23
Fuel Gas K.O. Drum		360	0%	$7,553.88	27-Jul-22	21-Jul-23
P12-	Tendering & Selection	60	0%	$302.16	27-Jul-22	24-Sep-22
P12-	Contract Effectiveness / PO	30	0%	$453.23	25-Sep-22	24-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$6,798.49	25-Oct-22	21-Jul-23
Slug Catcher		360	0%	$68,158.85	27-Jul-22	21-Jul-23
P12-	Tendering & Selection	60	0%	$2,726.35	27-Jul-22	24-Sep-22
P12-	Contract Effectiveness / PO	30	0%	$4,089.53	25-Sep-22	24-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$61,342.96	25-Oct-22	21-Jul-23
Degassing vessel		360	0%	$13,020.50	27-Jul-22	21-Jul-23
P12-	Tendering & Selection	60	0%	$520.82	27-Jul-22	24-Sep-22
P12-	Contract Effectiveness / PO	30	0%	$781.23	25-Sep-22	24-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$11,718.45	25-Oct-22	21-Jul-23
Gas Air cooler		420	0%	$217,983.16	07-Jul-22	30-Aug-23
1ST STAGE GAS COMPRESSION AIR COOLER, AC-101 A/B/C		420	0%	$108,991.58	07-Jul-22	30-Aug-23
P12-	Tendering & Selection	60	0%	$4,359.66	07-Jul-22	04-Sep-22
P12-	Contract Effectiveness / PO	20	0%	$6,539.49	05-Sep-22	24-Sep-22
P12-	Manufacturing / Fabrication / Supply	340	0%	$98,092.42	25-Sep-22	30-Aug-23
2nd STAGE GAS COMPRESSION AIR COOLER, AC-102 A/B/C		420	0%	$108,991.58	07-Jul-22	30-Aug-23
P12-	Tendering & Selection	60	0%	$4,359.66	07-Jul-22	04-Sep-22
P12-	Contract Effectiveness / PO	20	0%	$6,539.49	05-Sep-22	24-Sep-22
P12-	Manufacturing / Fabrication / Supply	340	0%	$98,092.42	25-Sep-22	30-Aug-23
Storage Tanks		270	0%	$455,701.41	07-Jul-22	02-Apr-23
FIRE WATER STORAGE TANK, TK-102 A/B		270	0%	$283,810.84	07-Jul-22	02-Apr-23
P12-	Tendering & Selection	70	0%	$11,352.43	07-Jul-22	14-Sep-22
P12-	Contract Effectiveness / PO	20	0%	$17,028.65	15-Sep-22	04-Oct-22
P12-	Manufacturing / Fabrication / Supply	180	0%	$255,429.76	05-Oct-22	02-Apr-23
Lean Glycol Storage Tank, TK-101		270	0%	$11,802.67	07-Jul-22	02-Apr-23
P12-	Tendering & Selection	70	0%	$472.11	07-Jul-22	14-Sep-22
P12-	Contract Effectiveness / PO	20	0%	$708.16	15-Sep-22	04-Oct-22
P12-	Manufacturing / Fabrication / Supply	180	0%	$10,622.40	05-Oct-22	02-Apr-23
Slug Storage Tank, TK-103		270	0%	$160,087.91	07-Jul-22	02-Apr-23
P12-	Tendering & Selection	70	0%	$6,403.52	07-Jul-22	14-Sep-22
P12-	Contract Effectiveness / PO	20	0%	$9,605.27	15-Sep-22	04-Oct-22
P12-	Manufacturing / Fabrication / Supply	180	0%	$144,079.12	05-Oct-22	02-Apr-23
Instrument/Plant Air & Nitrogen Packages		350	0%	$348,055.41	14-Jul-22	28-Jun-23
INSTRUMENT & PLANT AIR PACKAGE		270	0%	$158,887.29	14-Jul-22	09-Apr-23
P12-	Tendering & Selection	60	0%	$6,355.49	14-Jul-22	11-Sep-22
P12-	Contract Effectiveness / PO	30	0%	$9,533.24	12-Sep-22	11-Oct-22
P12-	Manufacturing / Fabrication / Supply	180	0%	$142,998.57	12-Oct-22	09-Apr-23
Nitrogen Package, PK-108		350	0%	$189,168.12	14-Jul-22	28-Jun-23
P12-	Tendering & Selection	60	0%	$7,566.72	14-Jul-22	11-Sep-22



Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-	Contract Effectiveness / PO	20	0%	$11,350.09	12-Sep-22	01-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$170,251.30	02-Oct-22	28-Jun-23
Chemical Injection Packages		290	0%	$109,440.10	14-Jul-22	29-Apr-23
Chemical Injection Package(corrosion inhibitor), PK-105		290	0%	$47,376.62	14-Jul-22	29-Apr-23
P12-	Tendering & Selection	60	0%	$1,895.06	14-Jul-22	11-Sep-22
P12-	Contract Effectiveness / PO	20	0%	$2,842.60	12-Sep-22	01-Oct-22
P12-	Manufacturing / Fabrication / Supply	210	0%	$42,638.96	02-Oct-22	29-Apr-23
Chemical Injection Package(Methanol), PK-106		290	0%	$62,063.48	14-Jul-22	29-Apr-23
P12-	Tendering & Selection	60	0%	$2,482.54	14-Jul-22	11-Sep-22
P12-	Contract Effectiveness / PO	20	0%	$3,723.81	12-Sep-22	01-Oct-22
P12-	Manufacturing / Fabrication / Supply	210	0%	$55,857.13	02-Oct-22	29-Apr-23
Pumps - Process Services		350	0%	$110,337.15	10-Aug-22	25-Jul-23
Glycol Transfer Pumps, P-101 A/B		350	0%	$15,027.92	10-Aug-22	25-Jul-23
P12-	Tendering & Selection	60	0%	$601.12	10-Aug-22	08-Oct-22
P12-	Contract Effectiveness / PO	20	0%	$901.68	09-Oct-22	28-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$13,525.13	29-Oct-22	25-Jul-23
Glycol Manual Pump, P-102		350	0%	$9,599.33	10-Aug-22	25-Jul-23
P12-	Tendering & Selection	60	0%	$383.97	10-Aug-22	08-Oct-22
P12-	Contract Effectiveness / PO	20	0%	$575.96	09-Oct-22	28-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$8,639.40	29-Oct-22	25-Jul-23
Slug Pumps, P-110 A/B		260	0%	$85,709.90	20-Aug-22	06-May-23
P12-	Tendering & Selection	60	0%	$3,428.40	20-Aug-22	18-Oct-22
P12-	Contract Effectiveness / PO	20	0%	$5,142.59	19-Oct-22	07-Nov-22
P12-	Manufacturing / Fabrication / Supply	180	0%	$77,138.91	08-Nov-22	06-May-23
Pumps - General Services		440	0%	$191,968.71	07-Jul-22	19-Sep-23
Closed Drain KO Drum Pumps		350	0%	$42,425.08	20-Aug-22	04-Aug-23
P12-	Tendering & Selection	60	0%	$1,697.00	20-Aug-22	18-Oct-22
P12-	Contract Effectiveness / PO	20	0%	$2,545.51	19-Oct-22	07-Nov-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$38,182.58	08-Nov-22	04-Aug-23
Sump Pumps		350	0%	$26,645.26	10-Aug-22	25-Jul-23
P12-	Tendering & Selection	60	0%	$1,065.81	10-Aug-22	08-Oct-22
P12-	Contract Effectiveness / PO	20	0%	$1,598.72	09-Oct-22	28-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$23,980.73	29-Oct-22	25-Jul-23
Potable Water Pump		440	0%	$26,146.14	07-Jul-22	19-Sep-23
P12-	Tendering & Selection	60	0%	$1,045.85	07-Jul-22	04-Sep-22
P12-	Contract Effectiveness / PO	20	0%	$1,568.77	05-Sep-22	24-Sep-22
P12-	Manufacturing / Fabrication / Supply	360	0%	$23,531.52	25-Sep-22	19-Sep-23
Diesel Pump		260	0%	$58,704.03	20-Aug-22	06-May-23
P12-	Tendering & Selection	60	0%	$2,348.16	20-Aug-22	18-Oct-22
P12-	Contract Effectiveness / PO	20	0%	$3,522.24	19-Oct-22	07-Nov-22
P12-	Manufacturing / Fabrication / Supply	180	0%	$52,833.63	08-Nov-22	06-May-23
Flare KO Drum Pumps		260	0%	$38,048.20	20-Aug-22	06-May-23
P12-	Tendering & Selection	60	0%	$1,521.93	20-Aug-22	18-Oct-22
P12-	Contract Effectiveness / PO	20	0%	$2,282.89	19-Oct-22	07-Nov-22
P12-	Manufacturing / Fabrication / Supply	180	0%	$34,243.38	08-Nov-22	06-May-23
Fire Water Pumps		440	0%	$350,746.56	27-Jun-22	09-Sep-23
Jockey Pumps, P-105 A/B		350	0%	$38,311.91	10-Aug-22	25-Jul-23
P12-	Tendering & Selection	60	0%	$1,532.48	10-Aug-22	08-Oct-22
P12-	Contract Effectiveness / PO	20	0%	$2,298.71	09-Oct-22	28-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$34,480.72	29-Oct-22	25-Jul-23



Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Fire Water Pumps, P-106 A/B/C		440	0%	$312,434.65	27-Jun-22	09-Sep-23
P12-	Tendering & Selection	60	0%	$12,497.39	27-Jun-22	25-Aug-22
P12-	Contract Effectiveness / PO	20	0%	$18,746.08	26-Aug-22	14-Sep-22
P12-	Manufacturing / Fabrication / Supply	360	0%	$281,191.18	15-Sep-22	09-Sep-23
Flare Packages		350	0%	$180,307.06	14-Jul-22	28-Jun-23
LP Flare Package		350	0%	$180,307.06	14-Jul-22	28-Jun-23
P12-	Tendering & Selection	60	0%	$7,212.28	14-Jul-22	11-Sep-22
P12-	Contract Effectiveness / PO	20	0%	$10,818.42	12-Sep-22	01-Oct-22
P12-	Manufacturing / Fabrication / Supply	270	0%	$162,276.35	02-Oct-22	28-Jun-23
Crane		260	0%	$108,543.05	14-Jul-22	30-Mar-23
Main Compressors Crane		260	0%	$51,492.82	14-Jul-22	30-Mar-23
P12-	Tendering & Selection	60	0%	$2,059.71	14-Jul-22	11-Sep-22
P12-	Contract Effectiveness / PO	20	0%	$3,089.57	12-Sep-22	01-Oct-22
P12-	Manufacturing / Fabrication / Supply	180	0%	$46,343.54	02-Oct-22	30-Mar-23
Diesel Generator & Air Package Crane		260	0%	$7,022.74	14-Jul-22	30-Mar-23
P12-	Tendering & Selection	60	0%	$280.91	14-Jul-22	11-Sep-22
P12-	Contract Effectiveness / PO	20	0%	$421.36	12-Sep-22	01-Oct-22
P12-	Manufacturing / Fabrication / Supply	180	0%	$6,320.46	02-Oct-22	30-Mar-23
Corrosion Inhib. & MeOH Pack. Crane		260	0%	$7,022.74	14-Jul-22	30-Mar-23
P12-	Tendering & Selection	60	0%	$280.91	14-Jul-22	11-Sep-22
P12-	Contract Effectiveness / PO	20	0%	$421.36	12-Sep-22	01-Oct-22
P12-	Manufacturing / Fabrication / Supply	180	0%	$6,320.46	02-Oct-22	30-Mar-23
Fire Water Pumps Crane		260	0%	$43,004.76	14-Jul-22	30-Mar-23
P12-	Tendering & Selection	60	0%	$1,720.19	14-Jul-22	11-Sep-22
P12-	Contract Effectiveness / PO	20	0%	$2,580.29	12-Sep-22	01-Oct-22
P12-	Manufacturing / Fabrication / Supply	180	0%	$38,704.28	02-Oct-22	30-Mar-23
HVAC & Plumbing		200	0%	$72,119.05	25-May-23	10-Dec-23
Main HVAC Equipment		200	0%	$72,119.05	25-May-23	10-Dec-23
P12-E	Tendering & Selection	30	0%	$2,884.76	25-May-23	23-Jun-23
P12-E	Contract Effectiveness / PO	20	0%	$4,327.14	24-Jun-23	13-Jul-23
P12-E	Manufacturing / Fabrication / Supply	150	0%	$64,907.14	14-Jul-23	10-Dec-23
Piping		217	0%	$1,471,505.99	11-Feb-23	15-Sep-23
Pipes		185	0%	$768,126.13	15-Mar-23	15-Sep-23
P12-E	Tendering & Selection	15	0%	$30,725.05	15-Mar-23	29-Mar-23
P12-E	Contract Effectiveness / PO	20	0%	$46,087.57	30-Mar-23	18-Apr-23
P12-E	Manufacturing / Fabrication / Supply	150	0%	$691,313.52	19-Apr-23	15-Sep-23
Fittings		175	0%	$104,329.78	15-Mar-23	05-Sep-23
P12-E	Tendering & Selection	15	0%	$4,173.19	15-Mar-23	29-Mar-23
P12-E	Contract Effectiveness / PO	20	0%	$6,259.79	30-Mar-23	18-Apr-23
P12-E	Manufacturing / Fabrication / Supply	140	0%	$93,896.80	19-Apr-23	05-Sep-23
Flanges		180	0%	$60,331.75	15-Mar-23	10-Sep-23
P12-E	Tendering & Selection	15	0%	$2,413.27	15-Mar-23	29-Mar-23
P12-E	Contract Effectiveness / PO	20	0%	$3,619.90	30-Mar-23	18-Apr-23
P12-E	Manufacturing / Fabrication / Supply	145	0%	$54,298.57	19-Apr-23	10-Sep-23
Manual Valves		185	0%	$492,071.60	15-Mar-23	15-Sep-23
P12-E	Tendering & Selection	15	0%	$19,682.86	15-Mar-23	29-Mar-23
P12-E	Contract Effectiveness / PO	20	0%	$29,524.30	30-Mar-23	18-Apr-23
P12-E	Manufacturing / Fabrication / Supply	150	0%	$442,864.44	19-Apr-23	15-Sep-23
Gaskets		155	0%	$8,829.04	15-Mar-23	16-Aug-23
P12-E	Tendering & Selection	15	0%	$353.16	15-Mar-23	29-Mar-23



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Contract Effectiveness / PO	20	0%	$529.74	30-Mar-23	18-Apr-23
P12-E	Manufacturing / Fabrication / Supply	120	0%	$7,946.13	19-Apr-23	16-Aug-23
Bolt & Nuts		155	0%	$6,327.48	11-Feb-23	15-Jul-23
P12-E	Tendering & Selection	15	0%	$253.10	11-Feb-23	25-Feb-23
P12-E	Contract Effectiveness / PO	20	0%	$379.65	26-Feb-23	17-Mar-23
P12-E	Manufacturing / Fabrication / Supply	120	0%	$5,694.73	18-Mar-23	15-Jul-23
Insulation kits		185	0%	$2,501.56	15-Mar-23	15-Sep-23
P12-E	Tendering & Selection	15	0%	$100.06	15-Mar-23	29-Mar-23
P12-E	Contract Effectiveness / PO	20	0%	$150.09	30-Mar-23	18-Apr-23
P12-E	Manufacturing / Fabrication / Supply	150	0%	$2,251.40	19-Apr-23	15-Sep-23
Strainers		185	0%	$3,825.92	25-Feb-23	28-Aug-23
P12-E	Tendering & Selection	15	0%	$153.04	25-Feb-23	11-Mar-23
P12-E	Contract Effectiveness / PO	20	0%	$229.55	12-Mar-23	31-Mar-23
P12-E	Manufacturing / Fabrication / Supply	150	0%	$3,443.32	01-Apr-23	28-Aug-23
Pipe Supports		155	0%	$8,829.04	25-Feb-23	29-Jul-23
P12-E	Tendering & Selection	15	0%	$353.16	25-Feb-23	11-Mar-23
P12-E	Contract Effectiveness / PO	20	0%	$529.74	12-Mar-23	31-Mar-23
P12-E	Manufacturing / Fabrication / Supply	120	0%	$7,946.13	01-Apr-23	29-Jul-23
Insulation		155	0%	$5,003.12	15-Mar-23	16-Aug-23
P12-E	Tendering & Selection	15	0%	$200.12	15-Mar-23	29-Mar-23
P12-E	Contract Effectiveness / PO	20	0%	$300.19	30-Mar-23	18-Apr-23
P12-E	Manufacturing / Fabrication / Supply	120	0%	$4,502.81	19-Apr-23	16-Aug-23
Painting		155	0%	$6,327.48	15-Mar-23	16-Aug-23
P12-E	Tendering & Selection	15	0%	$253.10	15-Mar-23	29-Mar-23
P12-E	Contract Effectiveness / PO	20	0%	$379.65	30-Mar-23	18-Apr-23
P12-E	Manufacturing / Fabrication / Supply	120	0%	$5,694.73	19-Apr-23	16-Aug-23
Coating of Underground Piping		155	0%	$5,003.12	15-Mar-23	16-Aug-23
P12-E	Tendering & Selection	15	0%	$200.12	15-Mar-23	29-Mar-23
P12-E	Contract Effectiveness / PO	20	0%	$300.19	30-Mar-23	18-Apr-23
P12-E	Manufacturing / Fabrication / Supply	120	0%	$4,502.81	19-Apr-23	16-Aug-23
Control & Instrumentation		430	0%	$2,062,327.44	22-Jun-22	25-Aug-23
Control System/Console/Furniture		265	0%	$201,901.86	22-Aug-22	13-May-23
P12-E	Tendering & Selection	45	0%	$8,076.07	22-Aug-22	05-Oct-22
P12-E	Contract Effectiveness / PO	30	0%	$12,114.11	06-Oct-22	04-Nov-22
P12-E	Manufacturing / Fabrication / Supply	190	0%	$181,711.67	05-Nov-22	13-May-23
ESD System		320	0%	$151,581.07	04-Jul-22	19-May-23
P12-E	Tendering & Selection	60	0%	$6,063.24	04-Jul-22	01-Sep-22
P12-E	Contract Effectiveness / PO	20	0%	$9,094.86	02-Sep-22	21-Sep-22
P12-E	Manufacturing / Fabrication / Supply	240	0%	$136,422.96	22-Sep-22	19-May-23
F&G System		265	0%	$130,957.79	14-Jul-22	04-Apr-23
P12-E	Tendering & Selection	45	0%	$5,238.31	14-Jul-22	27-Aug-22
P12-E	Contract Effectiveness / PO	20	0%	$7,857.47	28-Aug-22	16-Sep-22
P12-E	Manufacturing / Fabrication / Supply	200	0%	$117,862.01	17-Sep-22	04-Apr-23
ON/OFF & Shutdown Valves		315	0%	$92,186.04	15-Oct-22	25-Aug-23
P12-E	Tendering & Selection	45	0%	$3,687.44	15-Oct-22	28-Nov-22
P12-E	Contract Effectiveness / PO	30	0%	$5,531.16	29-Nov-22	28-Dec-22
P12-E	Manufacturing / Fabrication / Supply	240	0%	$82,967.43	29-Dec-22	25-Aug-23
Control Valves		300	0%	$102,291.44	05-Oct-22	31-Jul-23
P12-E	Tendering & Selection	60	0%	$4,091.66	05-Oct-22	03-Dec-22



Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Contract Effectiveness / PO	30	0%	$6,137.49	04-Dec-22	02-Jan-23
P12-E	Manufacturing / Fabrication / Supply	210	0%	$92,062.30	03-Jan-23	31-Jul-23
Pressure Safety Valves (PSV)		210	0%	$88,061.38	05-Oct-22	02-May-23
P12-E	Tendering & Selection	60	0%	$3,522.46	05-Oct-22	03-Dec-22
P12-E	Contract Effectiveness / PO	30	0%	$5,283.68	04-Dec-22	02-Jan-23
P12-E	Manufacturing / Fabrication / Supply	120	0%	$79,255.24	03-Jan-23	02-May-23
F&G Devices		270	0%	$118,171.36	17-Aug-22	13-May-23
P12-E	Tendering & Selection	60	0%	$4,726.85	17-Aug-22	15-Oct-22
P12-E	Contract Effectiveness / PO	30	0%	$7,090.28	16-Oct-22	14-Nov-22
P12-E	Manufacturing / Fabrication / Supply	180	0%	$106,354.23	15-Nov-22	13-May-23
Corrosion Coupon/Probe		290	0%	$49,083.39	01-Oct-22	17-Jul-23
P12-E	Tendering & Selection	30	0%	$1,963.34	01-Oct-22	30-Oct-22
P12-E	Contract Effectiveness / PO	20	0%	$2,945.00	31-Oct-22	19-Nov-22
P12-E	Manufacturing / Fabrication / Supply	240	0%	$44,175.05	20-Nov-22	17-Jul-23
Orifice and Restriction Orifice Plate		170	0%	$91,979.80	01-Oct-22	19-Mar-23
P12-E	Tendering & Selection	30	0%	$3,679.19	01-Oct-22	30-Oct-22
P12-E	Contract Effectiveness / PO	20	0%	$5,518.79	31-Oct-22	19-Nov-22
P12-E	Manufacturing / Fabrication / Supply	120	0%	$82,781.82	20-Nov-22	19-Mar-23
Differential Pressure/Pressure Gauge		200	0%	$36,915.66	01-Oct-22	18-Apr-23
P12-E	Tendering & Selection	30	0%	$1,476.63	01-Oct-22	30-Oct-22
P12-E	Contract Effectiveness / PO	20	0%	$2,214.94	31-Oct-22	19-Nov-22
P12-E	Manufacturing / Fabrication / Supply	150	0%	$33,224.10	20-Nov-22	18-Apr-23
Flow Transmitter/Diff. Pressure Transmitter		200	0%	$84,142.96	30-Sep-22	17-Apr-23
P12-E	Tendering & Selection	30	0%	$3,365.72	30-Sep-22	29-Oct-22
P12-E	Contract Effectiveness / PO	20	0%	$5,048.58	30-Oct-22	18-Nov-22
P12-E	Manufacturing / Fabrication / Supply	150	0%	$75,728.66	19-Nov-22	17-Apr-23
Pressure/ Differential Pressure Switch		200	0%	$41,659.01	22-Jun-22	07-Jan-23
P12-E	Tendering & Selection	30	0%	$1,666.36	22-Jun-22	21-Jul-22
P12-E	Contract Effectiveness / PO	20	0%	$2,499.54	22-Jul-22	10-Aug-22
P12-E	Manufacturing / Fabrication / Supply	150	0%	$37,493.11	11-Aug-22	07-Jan-23
Temperature Gauge		170	0%	$49,702.09	30-Sep-22	18-Mar-23
P12-E	Tendering & Selection	30	0%	$1,988.08	30-Sep-22	29-Oct-22
P12-E	Contract Effectiveness / PO	20	0%	$2,982.13	30-Oct-22	18-Nov-22
P12-E	Manufacturing / Fabrication / Supply	120	0%	$44,731.88	19-Nov-22	18-Mar-23
Temperature Transmitter/Switch		200	0%	$96,516.92	30-Sep-22	17-Apr-23
P12-E	Tendering & Selection	30	0%	$3,860.68	30-Sep-22	29-Oct-22
P12-E	Contract Effectiveness / PO	20	0%	$5,791.02	30-Oct-22	18-Nov-22
P12-E	Manufacturing / Fabrication / Supply	150	0%	$86,865.23	19-Nov-22	17-Apr-23
Level Gauge		215	0%	$90,742.41	30-Sep-22	02-May-23
P12-E	Tendering & Selection	30	0%	$3,629.70	30-Sep-22	29-Oct-22
P12-E	Contract Effectiveness / PO	20	0%	$5,444.54	30-Oct-22	18-Nov-22
P12-E	Manufacturing / Fabrication / Supply	165	0%	$81,668.17	19-Nov-22	02-May-23
Level Switch		215	0%	$23,098.07	22-Jun-22	22-Jan-23
P12-E	Tendering & Selection	30	0%	$923.92	22-Jun-22	21-Jul-22
P12-E	Contract Effectiveness / PO	20	0%	$1,385.88	22-Jul-22	10-Aug-22
P12-E	Manufacturing / Fabrication / Supply	165	0%	$20,788.26	11-Aug-22	22-Jan-23
Displacer Level Transmitter		215	0%	$123,533.41	30-Sep-22	02-May-23
P12-E	Tendering & Selection	30	0%	$4,941.34	30-Sep-22	29-Oct-22
P12-E	Contract Effectiveness / PO	20	0%	$7,412.00	30-Oct-22	18-Nov-22



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Manufacturing / Fabrication / Supply	165	0%	$111,180.07	19-Nov-22	02-May-23
Rotameter		200	0%	$33,615.94	30-Sep-22	17-Apr-23
P12-E	Tendering & Selection	30	0%	$1,344.64	30-Sep-22	29-Oct-22
P12-E	Contract Effectiveness / PO	20	0%	$2,016.96	30-Oct-22	18-Nov-22
P12-E	Manufacturing / Fabrication / Supply	150	0%	$30,254.34	19-Nov-22	17-Apr-23
Instrument/F&G cable		180	0%	$77,337.28	21-Jul-22	16-Jan-23
P12-E	Tendering & Selection	45	0%	$3,093.49	21-Jul-22	03-Sep-22
P12-E	Contract Effectiveness / PO	20	0%	$4,640.24	04-Sep-22	23-Sep-22
P12-E	Manufacturing / Fabrication / Supply	115	0%	$69,603.55	24-Sep-22	16-Jan-23
Instrument Cable Tray/Ladder		170	0%	$120,027.46	24-Jan-23	12-Jul-23
P12-E	Tendering & Selection	30	0%	$4,801.10	24-Jan-23	22-Feb-23
P12-E	Contract Effectiveness / PO	20	0%	$7,201.65	23-Feb-23	14-Mar-23
P12-E	Manufacturing / Fabrication / Supply	120	0%	$108,024.71	15-Mar-23	12-Jul-23
Instrument/F&G Junction box and Gland		170	0%	$40,421.62	11-Jul-22	27-Dec-22
P12-E	Tendering & Selection	30	0%	$1,616.86	11-Jul-22	09-Aug-22
P12-E	Contract Effectiveness / PO	20	0%	$2,425.30	10-Aug-22	29-Aug-22
P12-E	Manufacturing / Fabrication / Supply	120	0%	$36,379.46	30-Aug-22	27-Dec-22
Instrument Tube and Fitting		125	0%	$50,320.79	12-Oct-22	13-Feb-23
P12-E	Tendering & Selection	30	0%	$2,012.83	12-Oct-22	10-Nov-22
P12-E	Contract Effectiveness / PO	20	0%	$3,019.25	11-Nov-22	30-Nov-22
P12-E	Manufacturing / Fabrication / Supply	75	0%	$45,288.71	01-Dec-22	13-Feb-23
Instrument Installation Accessories		230	0%	$26,604.02	29-Aug-22	15-Apr-23
P12-E	Tendering & Selection	30	0%	$1,064.16	29-Aug-22	27-Sep-22
P12-E	Contract Effectiveness / PO	20	0%	$1,596.24	28-Sep-22	17-Oct-22
P12-E	Manufacturing / Fabrication / Supply	180	0%	$23,943.62	18-Oct-22	15-Apr-23
CCTV System		215	0%	$91,361.11	12-Aug-22	14-Mar-23
P12-E	Tendering & Selection	30	0%	$3,654.44	12-Aug-22	10-Sep-22
P12-E	Contract Effectiveness / PO	20	0%	$5,481.67	11-Sep-22	30-Sep-22
P12-E	Manufacturing / Fabrication / Supply	165	0%	$82,225.00	01-Oct-22	14-Mar-23
IPR Panel		200	0%	$50,114.56	04-Jul-22	19-Jan-23
P12-E	Tendering & Selection	30	0%	$2,004.58	04-Jul-22	02-Aug-22
P12-E	Contract Effectiveness / PO	20	0%	$3,006.87	03-Aug-22	22-Aug-22
P12-E	Manufacturing / Fabrication / Supply	150	0%	$45,103.10	23-Aug-22	19-Jan-23
Safety & Fire Fighting		158	0%	$108,178.57	04-Jul-22	08-Dec-22
Total Flooding System		70	0%	$27,044.64	04-Jul-22	11-Sep-22
P12-E	Tendering & Selection	30	0%	$1,081.79	04-Jul-22	02-Aug-22
P12-E	Contract Effectiveness / PO	20	0%	$1,622.68	03-Aug-22	22-Aug-22
P12-E	Manufacturing / Fabrication / Supply	20	0%	$24,340.18	23-Aug-22	11-Sep-22
Deluge Valve & Water Spray		70	0%	$16,226.79	30-Sep-22	08-Dec-22
P12-E	Tendering & Selection	30	0%	$649.07	30-Sep-22	29-Oct-22
P12-E	Contract Effectiveness / PO	20	0%	$973.61	30-Oct-22	18-Nov-22
P12-E	Manufacturing / Fabrication / Supply	20	0%	$14,604.11	19-Nov-22	08-Dec-22
Safety Equipment		70	0%	$25,962.86	11-Jul-22	18-Sep-22
P12-E	Tendering & Selection	30	0%	$1,038.51	11-Jul-22	09-Aug-22
P12-E	Contract Effectiveness / PO	20	0%	$1,557.77	10-Aug-22	29-Aug-22
P12-E	Manufacturing / Fabrication / Supply	20	0%	$23,366.57	30-Aug-22	18-Sep-22
Fire Fighting Equipment		70	0%	$25,962.86	11-Jul-22	18-Sep-22
P12-E	Tendering & Selection	30	0%	$1,038.51	11-Jul-22	09-Aug-22
P12-E	Contract Effectiveness / PO	20	0%	$1,557.77	10-Aug-22	29-Aug-22



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Manufacturing / Fabrication / Supply	20	0%	$23,366.57	30-Aug-22	18-Sep-22
Safety Signs		70	0%	$12,981.43	24-Aug-22	01-Nov-22
P12-E	Tendering & Selection	30	0%	$519.26	24-Aug-22	22-Sep-22
P12-E	Contract Effectiveness / PO	20	0%	$778.89	23-Sep-22	12-Oct-22
P12-E	Manufacturing / Fabrication / Supply	20	0%	$11,683.29	13-Oct-22	01-Nov-22
Electrical		585	0%	$1,009,666.70	09-Jul-22	13-Feb-24
Transformers		300	0%	$24,534.90	09-Jul-22	04-May-23
P12-E	Tendering & Selection	60	0%	$981.40	09-Jul-22	06-Sep-22
P12-E	Contract Effectiveness / PO	30	0%	$1,472.09	07-Sep-22	06-Oct-22
P12-E	Manufacturing / Fabrication / Supply	210	0%	$22,081.41	07-Oct-22	04-May-23
LV Switchgear & MCC		265	0%	$104,096.64	12-Jul-22	02-Apr-23
P12-E	Tendering & Selection	45	0%	$4,163.87	12-Jul-22	25-Aug-22
P12-E	Contract Effectiveness / PO	30	0%	$6,245.80	26-Aug-22	24-Sep-22
P12-E	Manufacturing / Fabrication / Supply	190	0%	$93,686.97	25-Sep-22	02-Apr-23
New MV Switchgear (3.3 kV) & Existent MV Switchgear Expansion		200	0%	$194,966.64	29-Jul-22	13-Feb-23
P12-E	Tendering & Selection	30	0%	$7,798.67	29-Jul-22	27-Aug-22
P12-E	Contract Effectiveness / PO	20	0%	$11,698.00	28-Aug-22	16-Sep-22
P12-E	Manufacturing / Fabrication / Supply	150	0%	$175,469.98	17-Sep-22	13-Feb-23
Emergency Diesel Generator		400	0%	$42,002.13	17-Jul-22	20-Aug-23
P12-E	Tendering & Selection	50	0%	$1,680.09	17-Jul-22	04-Sep-22
P12-E	Contract Effectiveness / PO	30	0%	$2,520.13	05-Sep-22	04-Oct-22
P12-E	Manufacturing / Fabrication / Supply	320	0%	$37,801.92	05-Oct-22	20-Aug-23
UPS System		275	0%	$96,019.30	25-Sep-22	26-Jun-23
P12-E	Tendering & Selection	45	0%	$3,840.77	25-Sep-22	08-Nov-22
P12-E	Contract Effectiveness / PO	20	0%	$5,761.16	09-Nov-22	28-Nov-22
P12-E	Manufacturing / Fabrication / Supply	210	0%	$86,417.37	29-Nov-22	26-Jun-23
DC Charger		255	0%	$96,019.30	24-Jul-22	04-Apr-23
P12-E	Tendering & Selection	45	0%	$3,840.77	24-Jul-22	06-Sep-22
P12-E	Contract Effectiveness / PO	20	0%	$5,761.16	07-Sep-22	26-Sep-22
P12-E	Manufacturing / Fabrication / Supply	190	0%	$86,417.37	27-Sep-22	04-Apr-23
Lighting & Distribution Panels		200	0%	$13,428.57	15-Jan-23	02-Aug-23
P12-E	Tendering & Selection	30	0%	$537.14	15-Jan-23	13-Feb-23
P12-E	Contract Effectiveness / PO	20	0%	$805.71	14-Feb-23	05-Mar-23
P12-E	Manufacturing / Fabrication / Supply	150	0%	$12,085.71	06-Mar-23	02-Aug-23
Lighting and Small Power Equipment		200	0%	$33,621.90	29-Nov-22	16-Jun-23
P12-E	Tendering & Selection	30	0%	$1,344.88	29-Nov-22	28-Dec-22
P12-E	Contract Effectiveness / PO	20	0%	$2,017.31	29-Dec-22	17-Jan-23
P12-E	Manufacturing / Fabrication / Supply	150	0%	$30,259.71	18-Jan-23	16-Jun-23
Earthing & Lightning System		200	0%	$24,030.07	11-Dec-22	28-Jun-23
P12-E	Tendering & Selection	30	0%	$961.20	11-Dec-22	09-Jan-23
P12-E	Contract Effectiveness / PO	20	0%	$1,441.80	10-Jan-23	29-Jan-23
P12-E	Manufacturing / Fabrication / Supply	150	0%	$21,627.06	30-Jan-23	28-Jun-23
Local Control Station (LCS)		200	0%	$5,351.23	29-Jul-22	13-Feb-23
P12-E	Tendering & Selection	30	0%	$214.05	29-Jul-22	27-Aug-22
P12-E	Contract Effectiveness / PO	20	0%	$321.07	28-Aug-22	16-Sep-22
P12-E	Manufacturing / Fabrication / Supply	150	0%	$4,816.11	17-Sep-22	13-Feb-23
Capacitor Bank		200	0%	$40,083.77	29-Jul-22	13-Feb-23
P12-E	Tendering & Selection	30	0%	$1,603.35	29-Jul-22	27-Aug-22
P12-E	Contract Effectiveness / PO	20	0%	$2,405.03	28-Aug-22	16-Sep-22



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Manufacturing / Fabrication / Supply	150	0%	$36,075.39	17-Sep-22	13-Feb-23
NGR System		200	0%	$1,312.57	16-Jul-22	31-Jan-23
P12-E	Tendering & Selection	30	0%	$52.50	16-Jul-22	14-Aug-22
P12-E	Contract Effectiveness / PO	20	0%	$78.75	15-Aug-22	03-Sep-22
P12-E	Manufacturing / Fabrication / Supply	150	0%	$1,181.31	04-Sep-22	31-Jan-23
Cathodic Protection System		260	0%	$54,622.97	30-May-23	13-Feb-24
P12-E	Tendering & Selection	60	0%	$2,184.92	30-May-23	28-Jul-23
P12-E	Contract Effectiveness / PO	20	0%	$3,277.38	29-Jul-23	17-Aug-23
P12-E	Manufacturing / Fabrication / Supply	180	0%	$49,160.67	18-Aug-23	13-Feb-24
Power & Control Cables		215	0%	$205,467.17	16-Nov-22	18-Jun-23
P12-E	Tendering & Selection	30	0%	$8,218.69	16-Nov-22	15-Dec-22
P12-E	Contract Effectiveness / PO	20	0%	$12,328.03	16-Dec-22	04-Jan-23
P12-E	Manufacturing / Fabrication / Supply	165	0%	$184,920.46	05-Jan-23	18-Jun-23
Tray/Ladder and Accessories		215	0%	$43,819.53	13-Dec-22	15-Jul-23
P12-E	Tendering & Selection	30	0%	$1,752.78	13-Dec-22	11-Jan-23
P12-E	Contract Effectiveness / PO	20	0%	$2,629.17	12-Jan-23	31-Jan-23
P12-E	Manufacturing / Fabrication / Supply	165	0%	$39,437.58	01-Feb-23	15-Jul-23
Electrical Bulk Items		140	0%	$16,659.50	29-Nov-22	17-Apr-23
P12-E	Tendering & Selection	30	0%	$666.38	29-Nov-22	28-Dec-22
P12-E	Contract Effectiveness / PO	20	0%	$999.57	29-Dec-22	17-Jan-23
P12-E	Manufacturing / Fabrication / Supply	90	0%	$14,993.55	18-Jan-23	17-Apr-23
Telecomm UPS		215	0%	$13,630.50	05-Sep-22	07-Apr-23
P12-E	Tendering & Selection	30	0%	$545.22	05-Sep-22	04-Oct-22
P12-E	Contract Effectiveness / PO	20	0%	$817.83	05-Oct-22	24-Oct-22
P12-E	Manufacturing / Fabrication / Supply	165	0%	$12,267.45	25-Oct-22	07-Apr-23
Intercom & Telecom		583	0%	$174,750.01	08-May-22	11-Dec-23
PAGA System		215	0%	$18,139.05	22-Dec-22	24-Jul-23
P12-E	Tendering & Selection	30	0%	$725.56	22-Dec-22	20-Jan-23
P12-E	Contract Effectiveness / PO	20	0%	$1,088.34	21-Jan-23	09-Feb-23
P12-E	Manufacturing / Fabrication / Supply	165	0%	$16,325.15	10-Feb-23	24-Jul-23
PABX System		155	0%	$18,139.05	17-Oct-22	20-Mar-23
P12-E	Tendering & Selection	30	0%	$725.56	17-Oct-22	15-Nov-22
P12-E	Contract Effectiveness / PO	20	0%	$1,088.34	16-Nov-22	05-Dec-22
P12-E	Manufacturing / Fabrication / Supply	105	0%	$16,325.15	06-Dec-22	20-Mar-23
Radio System		155	0%	$49,716.38	08-May-22	09-Oct-22
P12-E	Tendering & Selection	30	0%	$1,988.66	08-May-22	06-Jun-22
P12-E	Contract Effectiveness / PO	20	0%	$2,982.98	07-Jun-22	26-Jun-22
P12-E	Manufacturing / Fabrication / Supply	105	0%	$44,744.74	27-Jun-22	09-Oct-22
Telecomm. Cable		155	0%	$35,019.90	10-Jul-23	11-Dec-23
P12-E	Tendering & Selection	30	0%	$1,400.80	10-Jul-23	08-Aug-23
P12-E	Contract Effectiveness / PO	20	0%	$2,101.19	09-Aug-23	28-Aug-23
P12-E	Manufacturing / Fabrication / Supply	105	0%	$31,517.91	29-Aug-23	11-Dec-23
Telecommunication Tower		155	0%	$53,735.63	18-May-22	19-Oct-22
P12-E	Tendering & Selection	30	0%	$2,149.43	18-May-22	16-Jun-22
P12-E	Contract Effectiveness / PO	20	0%	$3,224.14	17-Jun-22	06-Jul-22
P12-E	Manufacturing / Fabrication / Supply	105	0%	$48,362.06	07-Jul-22	19-Oct-22
Customs Clearance & Delivery To Site		523	0%	$1,733,631.00	12-Sep-22	16-Feb-24
Mechanical		273	0%	$1,121,312.53	31-Mar-23	28-Dec-23
Gas Compressors		10	0%	$623,113.37	19-Dec-23	28-Dec-23
P12-E	Gas Compressor of first & Second Stage	10	0%	$623,113.37	19-Dec-23	28-Dec-23




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Gas Dehydration Package		10	0%	$208,003.47	20-Oct-23	29-Oct-23
P12-E	Dehydration Package	10	0%	$208,003.47	20-Oct-23	29-Oct-23
Pressure Vessels		28	0%	$31,060.36	22-Jul-23	18-Aug-23
P12-E	Inlet Knock Out Drum	3	0%	$580.83	01-Aug-23	03-Aug-23
P12-E	1ST STAGE GAS COMPRESSION SUCTION DRUM	3	0%	$4,115.50	11-Aug-23	13-Aug-23
P12-E	2nd STAGE GAS COMPRESSION SUCTION DRUM	3	0%	$3,354.52	22-Jul-23	24-Jul-23
P12-E	2nd STAGE GAS COMPRESSION DISCHARGE DRUM	3	0%	$1,549.91	11-Aug-23	13-Aug-23
P12-E	Diesel Oil Storage Tank	3	0%	$2,786.11	16-Aug-23	18-Aug-23
P12-E	Instrument Air Receiver	3	0%	$1,400.82	22-Jul-23	24-Jul-23
P12-E	Close drain drum	3	0%	$5,249.20	22-Jul-23	24-Jul-23
P12-E	Potable Water Drum	3	0%	$183.26	22-Jul-23	24-Jul-23
P12-E	Flare K.O. Drum	3	0%	$748.55	22-Jul-23	24-Jul-23
P12-E	Fuel Gas K.O. Drum	3	0%	$944.23	22-Jul-23	24-Jul-23
P12-E	Slug Catcher	3	0%	$8,519.86	22-Jul-23	24-Jul-23
P12-E	Degassing vessel	3	0%	$1,627.56	22-Jul-23	24-Jul-23
Gas Air Coolers		10	0%	$27,247.89	31-Aug-23	09-Sep-23
P12-E	1ST STAGE GAS COMPRESSION AIR COOLER	10	0%	$13,623.95	31-Aug-23	09-Sep-23
P12-E	2nd STAGE GAS COMPRESSION AIR COOLER	10	0%	$13,623.95	31-Aug-23	09-Sep-23
Storage Tank		10	0%	$56,962.68	03-Apr-23	12-Apr-23
P12-E	FIRE WATER STORAGE TANK	10	0%	$35,476.36	03-Apr-23	12-Apr-23
P12-E	Lean Glycol Storage Tank	10	0%	$1,475.33	03-Apr-23	12-Apr-23
P12-E	Slug Storage Tank	10	0%	$20,010.99	03-Apr-23	12-Apr-23
Instrument/Plant Air & Nitrogen Packages		90	0%	$43,506.93	10-Apr-23	08-Jul-23
P12-E	INSTRUMENT & PLANT AIR PACKAGE	10	0%	$19,860.91	10-Apr-23	19-Apr-23
P12-E	Nitrogen Package	10	0%	$23,646.01	29-Jun-23	08-Jul-23
Chemical Injection Packages		10	0%	$13,680.01	30-Apr-23	09-May-23
P12-E	Chemical Injection Package(corrosion inhibitor)	10	0%	$5,922.08	30-Apr-23	09-May-23
P12-E	Chemical Injection Package(Methanol)	10	0%	$7,757.94	30-Apr-23	09-May-23
Pumps - Process Services		83	0%	$13,792.14	07-May-23	28-Jul-23
P12-E	Glycol Transfer Pumps	3	0%	$1,878.49	26-Jul-23	28-Jul-23
P12-E	Glycol Manual Pump	3	0%	$1,199.92	26-Jul-23	28-Jul-23
P12-E	Slug Pumps	3	0%	$10,713.74	07-May-23	09-May-23
Pumps - General Services		139	0%	$23,996.09	07-May-23	22-Sep-23
P12-E	Potable Water Pump	3	0%	$3,268.27	20-Sep-23	22-Sep-23
P12-E	Diesel Pump	3	0%	$7,338.00	07-May-23	09-May-23
P12-E	Sump Pumps	3	0%	$3,330.66	26-Jul-23	28-Jul-23
P12-E	Closed Drain KO Drum Pumps	3	0%	$5,303.14	05-Aug-23	07-Aug-23
P12-E	Flare KO Drum Pumps	3	0%	$4,756.02	07-May-23	09-May-23
Fire Water Pumps		49	0%	$43,843.32	26-Jul-23	12-Sep-23
P12-E	Fire Water Pumps	3	0%	$39,054.33	10-Sep-23	12-Sep-23
P12-E	Jockey Pumps	3	0%	$4,788.99	26-Jul-23	28-Jul-23
Flare Packages		10	0%	$22,538.38	29-Jun-23	08-Jul-23
P12-E	LP Flare Package	10	0%	$22,538.38	29-Jun-23	08-Jul-23
Overhead Travelling Cranes		10	0%	$13,567.88	31-Mar-23	09-Apr-23
P12-E	Main Compressors Crane	10	0%	$6,436.60	31-Mar-23	09-Apr-23
P12-E	Diesel Generator & Air Package Crane	10	0%	$877.84	31-Mar-23	09-Apr-23
P12-E	Corrosion Inhib. & MeOH Pack. Crane	10	0%	$877.84	31-Mar-23	09-Apr-23
P12-E	Fire Water Pumps Crane	10	0%	$5,375.59	31-Mar-23	09-Apr-23
HVAC & Plumbing		10	0%	$9,014.88	11-Dec-23	20-Dec-23

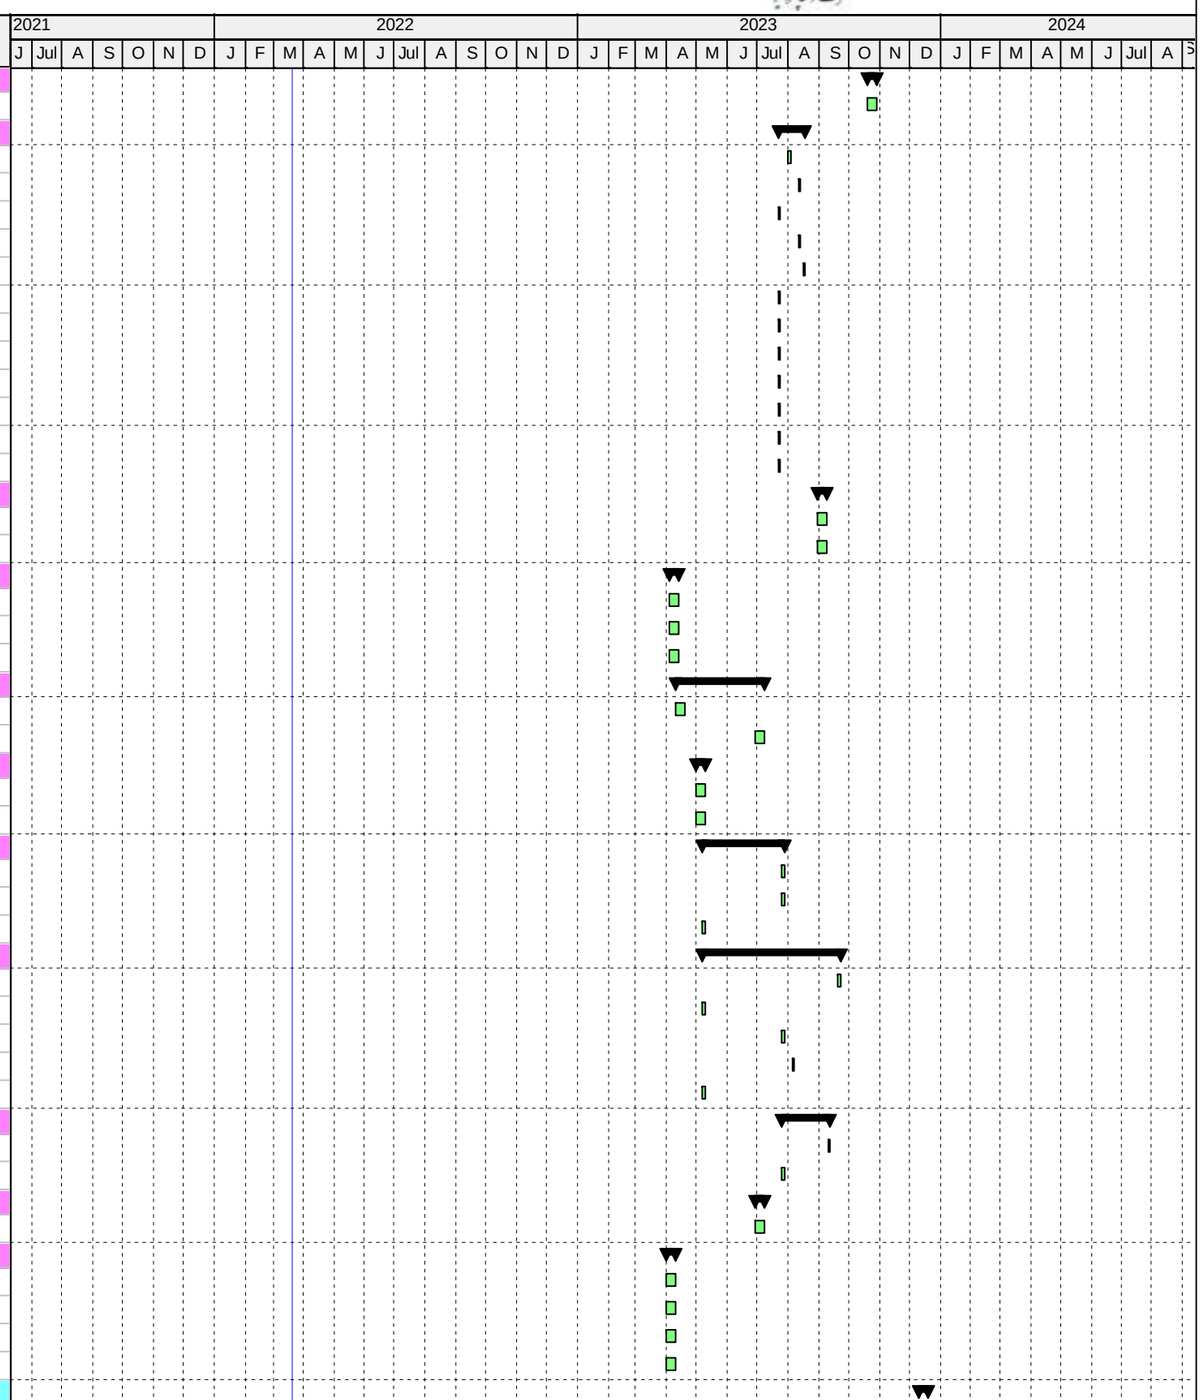

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-EF	Main HVAC Equipment	10	0%	$9,014.88	11-Dec-23	20-Dec-23
Piping		65	0%	$183,938.25	16-Jul-23	18-Sep-23
P12-EF	Pipes	3	0%	$96,015.77	16-Sep-23	18-Sep-23
P12-EF	Fittings	3	0%	$13,041.22	06-Sep-23	08-Sep-23
P12-EF	Flanges	7	0%	$7,541.47	11-Sep-23	17-Sep-23
P12-EF	Manual Valves	3	0%	$61,508.95	16-Sep-23	18-Sep-23
P12-EF	Gaskets	3	0%	$1,103.63	17-Aug-23	19-Aug-23
P12-EF	Bolt & Nuts	3	0%	$790.93	16-Jul-23	18-Jul-23
P12-EF	Insulation kits	3	0%	$312.70	16-Sep-23	18-Sep-23
P12-EF	Strainers	3	0%	$478.24	29-Aug-23	31-Aug-23
P12-EF	Pipe Supports	3	0%	$1,103.63	30-Jul-23	01-Aug-23
P12-EF	Insulation	7	0%	$625.39	17-Aug-23	23-Aug-23
P12-EF	Painting	7	0%	$790.93	17-Aug-23	23-Aug-23
P12-EF	Coating of Underground Piping	7	0%	$625.39	17-Aug-23	23-Aug-23
Control & Instrumentation		244	0%	$257,790.93	28-Dec-22	28-Aug-23
P12-EF	Control System/Console/Furniture	3	0%	$25,237.73	14-May-23	16-May-23
P12-EF	ESD System	3	0%	$18,947.63	20-May-23	22-May-23
P12-EF	F&G System	3	0%	$16,369.72	05-Apr-23	07-Apr-23
P12-EF	ON/OFF & Shutdown Valves	3	0%	$11,523.25	26-Aug-23	28-Aug-23
P12-EF	Control Valves	3	0%	$12,786.43	01-Aug-23	03-Aug-23
P12-EF	Pressure Safety Valves (PSV)	3	0%	$11,007.67	03-May-23	05-May-23
P12-EF	F&G Devices	3	0%	$14,771.42	14-May-23	16-May-23
P12-EF	Corrosion Probe/Coupon	3	0%	$6,135.42	18-Jul-23	20-Jul-23
P12-EF	Orifice and Restriction Orifice Plate	3	0%	$11,497.48	20-Mar-23	22-Mar-23
P12-EF	Differential Pressure/Pressure Gauge	3	0%	$4,614.46	19-Apr-23	21-Apr-23
P12-EF	Flow/Level /Pressure/Diff. Pressure Transmitter	3	0%	$10,517.87	18-Apr-23	20-Apr-23
P12-EF	Pressure/ Differential Pressure Switch	3	0%	$5,207.38	08-Jan-23	10-Jan-23
P12-EF	Temperature Gauge	3	0%	$6,212.76	19-Mar-23	21-Mar-23
P12-EF	Temperature Transmitter/Switch	3	0%	$12,064.62	18-Apr-23	20-Apr-23
P12-EF	Level Gauge	3	0%	$11,342.80	03-May-23	05-May-23
P12-EF	Level Switch	3	0%	$2,887.26	03-May-23	05-May-23
P12-EF	Displacer Level Transmitter	3	0%	$15,441.68	03-May-23	05-May-23
P12-EF	Rotameter	3	0%	$4,201.99	18-Apr-23	20-Apr-23
P12-EF	Instrument/F&G Cable	3	0%	$9,667.16	17-Jan-23	19-Jan-23
P12-EF	Instrument Cable Tray	3	0%	$15,003.43	13-Jul-23	15-Jul-23
P12-EF	Instrument/F&G Junction box and Gland	3	0%	$5,052.70	28-Dec-22	30-Dec-22
P12-EF	Instrument Tube and Fitting	3	0%	$6,290.10	14-Feb-23	16-Feb-23
P12-EF	Instrument Installation Accessories	3	0%	$3,325.50	16-Apr-23	18-Apr-23
P12-EF	CCTV System	3	0%	$11,420.14	15-Mar-23	17-Mar-23
P12-EF	IPR Panel	3	0%	$6,264.32	20-Jan-23	22-Jan-23
Safety & Fire Fighting		10	0%	$13,522.32	12-Sep-22	21-Sep-22
P12-EF	Total Flooding System	10	0%	$3,380.58	12-Sep-22	21-Sep-22
P12-EF	Deluge Valve & Water Spray	10	0%	$2,028.35	12-Sep-22	21-Sep-22
P12-EF	Safety Equipment	10	0%	$3,245.36	12-Sep-22	21-Sep-22
P12-EF	Fire Fighting Equipment	10	0%	$3,245.36	12-Sep-22	21-Sep-22
P12-EF	Safety Signs	10	0%	$1,622.68	12-Sep-22	21-Sep-22
Electrical		381	0%	$126,208.34	01-Feb-23	16-Feb-24
P12-EF	Transformers	3	0%	$3,066.86	05-May-23	07-May-23



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-EF	LV Switchgear & MCC	3	0%	$13,012.08	03-Apr-23	05-Apr-23
P12-EF	Existent MV Switchgear Expansion	3	0%	$24,370.83	03-Apr-23	05-Apr-23
P12-EF	Emergency Diesel Generator	3	0%	$5,250.27	21-Aug-23	23-Aug-23
P12-EF	UPS System	3	0%	$12,002.41	27-Jun-23	29-Jun-23
P12-EF	DC Charger	3	0%	$12,002.41	19-Jun-23	21-Jun-23
P12-EF	Lighting & Distribution Panels	3	0%	$1,678.57	03-Aug-23	05-Aug-23
P12-EF	Lighting and Small Power Equipment	3	0%	$4,202.74	29-Jun-23	01-Jul-23
P12-EF	Earthing & Lightning System	3	0%	$3,003.76	29-Jun-23	01-Jul-23
P12-EF	Local Control Station (LCS)	3	0%	$668.90	14-Feb-23	16-Feb-23
P12-EF	Capacitor Bank	3	0%	$5,010.47	14-Feb-23	16-Feb-23
P12-EF	NGR System	3	0%	$164.07	01-Feb-23	03-Feb-23
P12-EF	Cathodic Protection System	3	0%	$6,827.87	14-Feb-24	16-Feb-24
P12-EF	Power & Control Cables	3	0%	$25,683.40	19-Jun-23	21-Jun-23
P12-EF	Tray/Ladder and Accessories	3	0%	$5,477.44	16-Jul-23	18-Jul-23
P12-EF	Electrical Bulk Items	3	0%	$2,082.44	19-Jun-23	21-Jun-23
P12-EF	Telecomm UPS	3	0%	$1,703.81	08-Apr-23	10-Apr-23
Intercom & Telecom		431	0%	$21,843.75	10-Oct-22	14-Dec-23
P12-EF	PAGA System	3	0%	$2,267.38	25-Jul-23	27-Jul-23
P12-EF	PABX System	3	0%	$2,267.38	25-Jul-23	27-Jul-23
P12-EF	Radio System	3	0%	$6,214.55	10-Oct-22	12-Oct-22
P12-EF	Telecomm. Cable	3	0%	$4,377.49	12-Dec-23	14-Dec-23
P12-EF	Telecommunication Tower	3	0%	$6,716.95	20-Oct-22	22-Oct-22
Inspection		516	0%	$346,726.20	22-Sep-22	19-Feb-24
Mechanical		288	0%	$224,262.51	10-Apr-23	22-Jan-24
Gas Compressors		25	0%	$124,622.67	29-Dec-23	22-Jan-24
P12-E	Gas Compressor of first & Second Stage	25	0%	$124,622.67	29-Dec-23	22-Jan-24
Gas Dehydration Package		15	0%	$41,600.69	30-Oct-23	13-Nov-23
P12-E	Dehydration Package	15	0%	$41,600.69	30-Oct-23	13-Nov-23
Pressure Vessels		28	0%	$6,212.07	25-Jul-23	21-Aug-23
P12-E	Inlet Knock Out Drum	3	0%	$116.17	04-Aug-23	06-Aug-23
P12-E	1ST STAGE GAS COMPRESSION SUCTION DRUM	3	0%	$823.10	25-Jul-23	27-Jul-23
P12-E	2nd STAGE GAS COMPRESSION SUCTION DRUM	3	0%	$670.90	14-Aug-23	16-Aug-23
P12-E	2nd STAGE GAS COMPRESSION DISCHARGE DRUM	3	0%	$309.98	14-Aug-23	16-Aug-23
P12-E	Diesel Oil Storage Tank	3	0%	$557.22	19-Aug-23	21-Aug-23
P12-E	Instrument Air Receiver	3	0%	$280.16	25-Jul-23	27-Jul-23
P12-E	Close drain drum	3	0%	$1,049.84	25-Jul-23	27-Jul-23
P12-E	Potable Water Drum	3	0%	$36.65	25-Jul-23	27-Jul-23
P12-E	Flare K.O. Drum	3	0%	$149.71	25-Jul-23	27-Jul-23
P12-E	Fuel Gas K.O. Drum	3	0%	$188.85	25-Jul-23	27-Jul-23
P12-E	Slug Catcher	3	0%	$1,703.97	25-Jul-23	27-Jul-23
P12-E	Degassing vessel	3	0%	$325.51	25-Jul-23	27-Jul-23
Gas Air Coolers		20	0%	$5,449.58	10-Sep-23	29-Sep-23
P12-E	1ST STAGE GAS COMPRESSION AIR COOLER	15	0%	$2,724.79	10-Sep-23	24-Sep-23
P12-E	2nd STAGE GAS COMPRESSION AIR COOLER	20	0%	$2,724.79	10-Sep-23	29-Sep-23
Storage Tank		15	0%	$11,392.54	13-Apr-23	27-Apr-23
P12-E	FIRE WATER STORAGE TANK	10	0%	$7,095.27	13-Apr-23	22-Apr-23
P12-E	Lean Glycol Storage Tank	15	0%	$295.07	13-Apr-23	27-Apr-23
P12-E	Slug Storage Tank	10	0%	$4,002.20	13-Apr-23	22-Apr-23
Instrument/Plant Air & Nitrogen Packages		83	0%	$8,701.39	20-Apr-23	11-Jul-23




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	INSTRUMENT & PLANT AIR PACKAGE	3	0%	$3,972.18	20-Apr-23	22-Apr-23
P12-E	Nitrogen Package	3	0%	$4,729.20	09-Jul-23	11-Jul-23
Chemical Injection Packages		15	0%	$2,736.00	10-May-23	24-May-23
P12-E	Chemical Injection Package(corrosion inhibitor)	10	0%	$1,184.42	10-May-23	19-May-23
P12-E	Chemical Injection Package(Methanol)	15	0%	$1,551.59	10-May-23	24-May-23
Pumps - Process Services		83	0%	$2,758.43	10-May-23	31-Jul-23
P12-E	Glycol Transfer Pumps	3	0%	$375.70	29-Jul-23	31-Jul-23
P12-E	Glycol Manual Pump	3	0%	$239.98	29-Jul-23	31-Jul-23
P12-E	Slug Pumps	3	0%	$2,142.75	10-May-23	12-May-23
Pumps - General Services		139	0%	$4,799.22	10-May-23	25-Sep-23
P12-E	Potable Water Pump	3	0%	$653.65	23-Sep-23	25-Sep-23
P12-E	Diesel Pump	3	0%	$1,467.60	10-May-23	12-May-23
P12-E	Sump Pumps	3	0%	$666.13	29-Jul-23	31-Jul-23
P12-E	Closed Drain KO Drum Pumps	3	0%	$1,060.63	08-Aug-23	10-Aug-23
P12-E	Flare KO Drum Pumps	3	0%	$951.20	10-May-23	12-May-23
Fire Water Pumps		49	0%	$8,768.66	29-Jul-23	15-Sep-23
P12-E	Fire Water Pumps	3	0%	$7,810.87	13-Sep-23	15-Sep-23
P12-E	Jockey Pumps	3	0%	$957.80	29-Jul-23	31-Jul-23
Flare Packages		20	0%	$4,507.68	09-Jul-23	28-Jul-23
P12-E	LP Flare Package	20	0%	$4,507.68	09-Jul-23	28-Jul-23
Overhead Travelling Cranes		15	0%	$2,713.58	10-Apr-23	24-Apr-23
P12-E	Main Compressors Crane	10	0%	$1,287.32	10-Apr-23	19-Apr-23
P12-E	Diesel Generator & Air Package Crane	15	0%	$175.57	10-Apr-23	24-Apr-23
P12-E	Corrosion Inhib. & MeOH Pack. Crane	5	0%	$175.57	10-Apr-23	14-Apr-23
P12-E	Fire Water Pumps Crane	15	0%	$1,075.12	10-Apr-23	24-Apr-23
HVAC & Plumbing		10	0%	$1,802.98	21-Dec-23	30-Dec-23
P12-EI	Main HVAC Equipment	10	0%	$1,802.98	21-Dec-23	30-Dec-23
Piping		65	0%	$36,787.65	19-Jul-23	21-Sep-23
P12-EI	Pipes	3	0%	$19,203.15	19-Sep-23	21-Sep-23
P12-EI	Fittings	3	0%	$2,608.24	09-Sep-23	11-Sep-23
P12-EI	Flanges	3	0%	$1,508.29	18-Sep-23	20-Sep-23
P12-EI	Manual Valves	3	0%	$12,301.79	19-Sep-23	21-Sep-23
P12-EI	Gaskets	3	0%	$220.73	20-Aug-23	22-Aug-23
P12-EI	Bolt & Nuts	3	0%	$158.19	19-Jul-23	21-Jul-23
P12-EI	Insulation kits	3	0%	$62.54	19-Sep-23	21-Sep-23
P12-EI	Strainers	3	0%	$95.65	01-Sep-23	03-Sep-23
P12-EI	Pipe Supports	3	0%	$220.73	02-Aug-23	04-Aug-23
P12-EI	Insulation	3	0%	$125.08	24-Aug-23	26-Aug-23
P12-EI	Painting	3	0%	$158.19	24-Aug-23	26-Aug-23
P12-EI	Coating of Underground Piping	3	0%	$125.08	24-Aug-23	26-Aug-23
Control & Instrumentation		256	0%	$51,558.19	31-Dec-22	12-Sep-23
P12-EI	Control System/Console/Furniture	15	0%	$5,047.55	17-May-23	31-May-23
P12-EI	ESD System	10	0%	$3,789.53	23-May-23	01-Jun-23
P12-EI	F&G System	15	0%	$3,273.94	08-Apr-23	22-Apr-23
P12-EI	ON/OFF & Shutdown Valves	15	0%	$2,304.65	29-Aug-23	12-Sep-23
P12-EI	Control Valves	10	0%	$2,557.29	04-Aug-23	13-Aug-23
P12-EI	Pressure Safety Valves (PSV)	15	0%	$2,201.53	06-May-23	20-May-23
P12-EI	F&G Devices	15	0%	$2,954.28	17-May-23	31-May-23
P12-EI	Corrosion Probe/Coupon	10	0%	$1,227.08	21-Jul-23	30-Jul-23

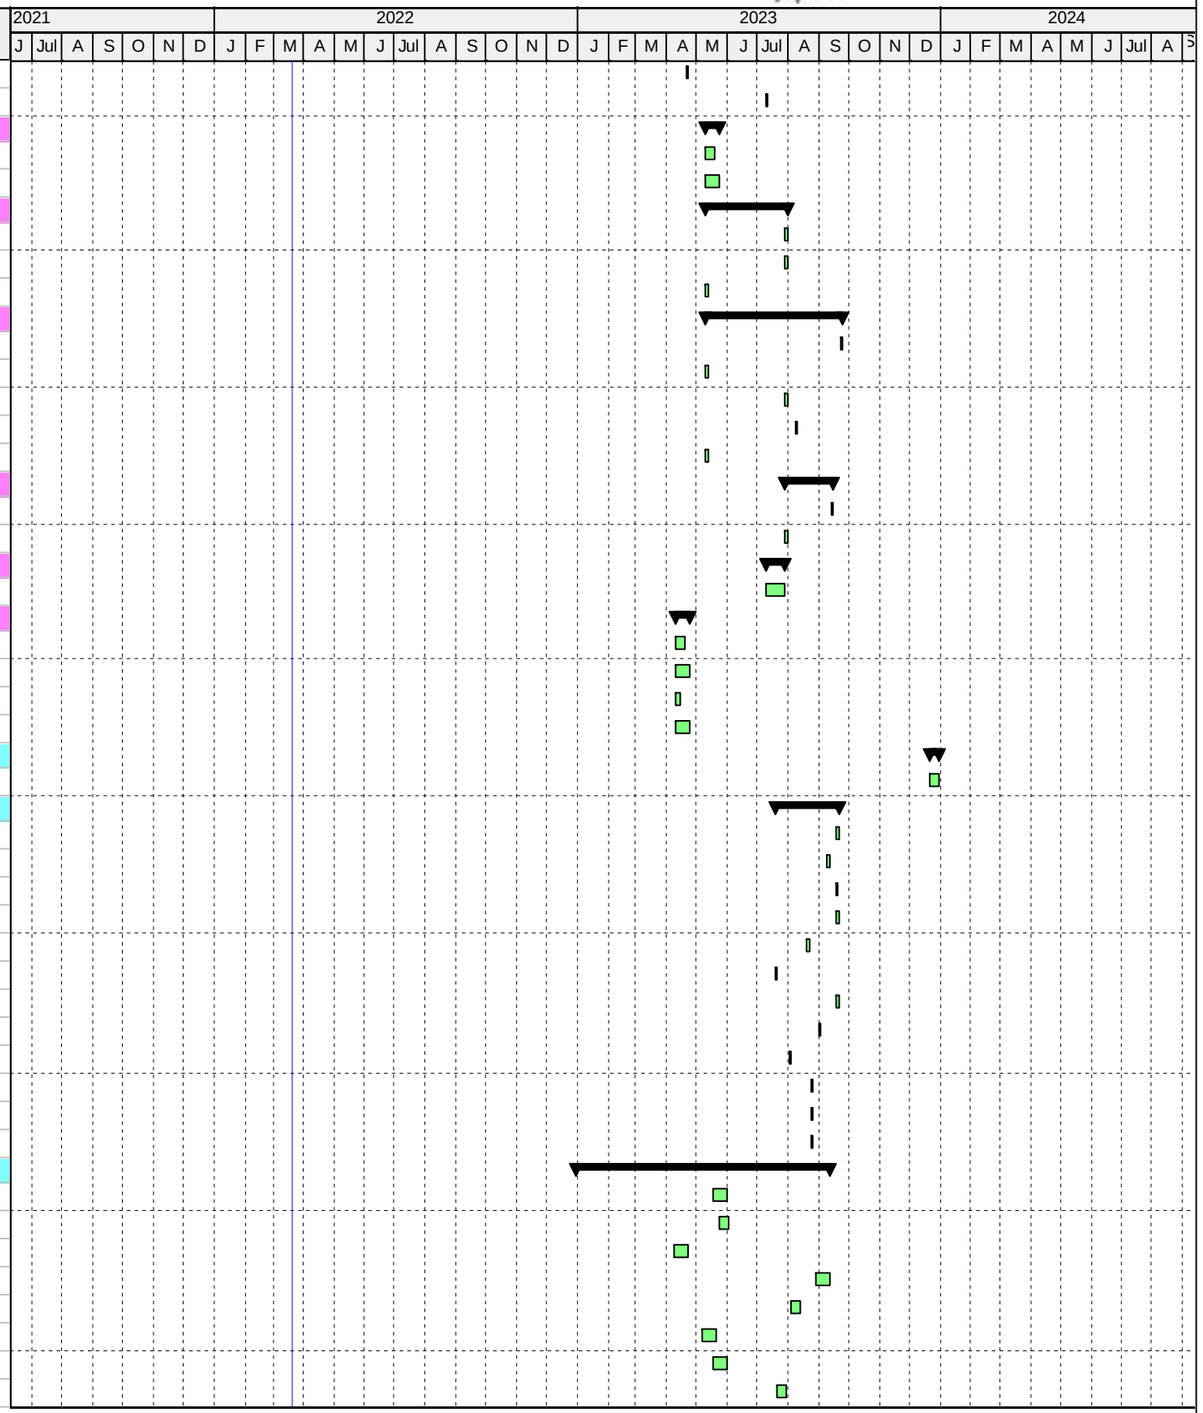

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-EF	Orifice and Restriction Orifice Plate	15	0%	$2,299.50	23-Mar-23	06-Apr-23
P12-EF	Differential Pressure/Pressure Gauge	15	0%	$922.89	22-Apr-23	06-May-23
P12-EF	Flow/Level /Pressure/Diff. Pressure Transmitter	20	0%	$2,103.57	21-Apr-23	10-May-23
P12-EF	Pressure/ Differential Pressure Switch	15	0%	$1,041.48	11-Jan-23	25-Jan-23
P12-EF	Temperature Gauge	15	0%	$1,242.55	22-Mar-23	05-Apr-23
P12-EF	Temperature Transmitter/Switch	15	0%	$2,412.92	21-Apr-23	05-May-23
P12-EF	Level Gauge	15	0%	$2,268.56	06-May-23	20-May-23
P12-EF	Level Switch	15	0%	$577.45	06-May-23	20-May-23
P12-EF	Displacer Level Transmitter	15	0%	$3,088.34	06-May-23	20-May-23
P12-EF	Rotameter	15	0%	$840.40	21-Apr-23	05-May-23
P12-EF	Instrument/F&G Cable	10	0%	$1,933.43	20-Jan-23	29-Jan-23
P12-EF	Instrument Cable Tray	15	0%	$3,000.69	16-Jul-23	30-Jul-23
P12-EF	Instrument/F&G Junction box and Gland	15	0%	$1,010.54	31-Dec-22	14-Jan-23
P12-EF	Instrument Tube and Fitting	15	0%	$1,258.02	17-Feb-23	03-Mar-23
P12-EF	Instrument Installation Accessories	20	0%	$665.10	19-Apr-23	08-May-23
P12-EF	CCTV System	20	0%	$2,284.03	18-Mar-23	06-Apr-23
P12-EF	IPR Panel	15	0%	$1,252.86	23-Jan-23	06-Feb-23
Safety & Fire Fighting		30	0%	$2,704.46	22-Sep-22	21-Oct-22
P12-EF	Total Flooding System	15	0%	$676.12	22-Sep-22	06-Oct-22
P12-EF	Deluge Valve & Water Spray	15	0%	$405.67	22-Sep-22	06-Oct-22
P12-EF	Safety Equipment	20	0%	$649.07	22-Sep-22	11-Oct-22
P12-EF	Fire Fighting Equipment	30	0%	$649.07	22-Sep-22	21-Oct-22
P12-EF	Safety Signs	20	0%	$324.54	22-Sep-22	11-Oct-22
Electrical		381	0%	$25,241.67	04-Feb-23	19-Feb-24
P12-EF	Transformers	3	0%	$613.37	08-May-23	10-May-23
P12-EF	LV Switchgear & MCC	3	0%	$2,602.42	06-Apr-23	08-Apr-23
P12-EF	Existent MV Switchgear Expansion	3	0%	$4,874.17	06-Apr-23	08-Apr-23
P12-EF	Emergency Diesel Generator	3	0%	$1,050.05	24-Aug-23	26-Aug-23
P12-EF	UPS System	3	0%	$2,400.48	30-Jun-23	02-Jul-23
P12-EF	DC Charger	3	0%	$2,400.48	22-Jun-23	24-Jun-23
P12-EF	Lighting & Distribution Panels	3	0%	$335.71	06-Aug-23	08-Aug-23
P12-EF	Lighting and Small Power Equipment	3	0%	$840.55	02-Jul-23	04-Jul-23
P12-EF	Earthing & Lightning System	3	0%	$600.75	02-Jul-23	04-Jul-23
P12-EF	Local Control Station (LCS)	3	0%	$133.78	17-Feb-23	19-Feb-23
P12-EF	Capacitor Bank	3	0%	$1,002.09	17-Feb-23	19-Feb-23
P12-EF	NGR System	3	0%	$32.81	04-Feb-23	06-Feb-23
P12-EF	Cathodic Protection System	3	0%	$1,365.57	17-Feb-24	19-Feb-24
P12-EF	Power & Control Cables	3	0%	$5,136.68	22-Jun-23	24-Jun-23
P12-EF	Tray/Ladder and Accessories	3	0%	$1,095.49	19-Jul-23	21-Jul-23
P12-EF	Electrical Bulk Items	3	0%	$416.49	22-Jun-23	24-Jun-23
P12-EF	Telecomm UPS	3	0%	$340.76	11-Apr-23	13-Apr-23
Intercom & Telecom		431	0%	$4,368.75	13-Oct-22	17-Dec-23
P12-EF	PAGA System	3	0%	$453.48	28-Jul-23	30-Jul-23
P12-EF	PABX System	3	0%	$453.48	28-Jul-23	30-Jul-23
P12-EF	Radio System	3	0%	$1,242.91	13-Oct-22	15-Oct-22
P12-EF	Telecomm. Cable	3	0%	$875.50	15-Dec-23	17-Dec-23
P12-EF	Telecommunication Tower	3	0%	$1,343.39	23-Oct-22	25-Oct-22
Submmiting Vendor Data Book		508	0%	$520,089.30	07-Oct-22	26-Feb-24




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Mechanical		286	0%	$336,393.76	15-Apr-23	25-Jan-24
Gas Compressors		3	0%	$186,934.01	23-Jan-24	25-Jan-24
P12-E	Gas Compressor of first & Second Stage	3	0%	$186,934.01	23-Jan-24	25-Jan-24
Gas Dehydration Package		3	0%	$62,401.04	14-Nov-23	16-Nov-23
P12-E	Dehydration Package	3	0%	$62,401.04	14-Nov-23	16-Nov-23
Pressure Vessels		28	0%	$9,318.11	28-Jul-23	24-Aug-23
P12-E	Inlet Knock Out Drum	3	0%	$174.25	07-Aug-23	09-Aug-23
P12-E	1ST STAGE GAS COMPRESSION SUCTION DRUM	3	0%	$1,234.65	28-Jul-23	30-Jul-23
P12-E	2nd STAGE GAS COMPRESSION SUCTION DRUM	3	0%	$1,006.36	17-Aug-23	19-Aug-23
P12-E	2nd STAGE GAS COMPRESSION DISCHARGE DRUM	3	0%	$464.97	17-Aug-23	19-Aug-23
P12-E	Diesel Oil Storage Tank	3	0%	$835.83	22-Aug-23	24-Aug-23
P12-E	Instrument Air Receiver	3	0%	$420.25	28-Jul-23	30-Jul-23
P12-E	Close drain drum	3	0%	$1,574.76	28-Jul-23	30-Jul-23
P12-E	Potable Water Drum	3	0%	$54.98	28-Jul-23	30-Jul-23
P12-E	Flare K.O. Drum	3	0%	$224.57	28-Jul-23	30-Jul-23
P12-E	Fuel Gas K.O. Drum	3	0%	$283.27	28-Jul-23	30-Jul-23
P12-E	Slug Catcher	3	0%	$2,555.96	28-Jul-23	30-Jul-23
P12-E	Degassing vessel	3	0%	$488.27	28-Jul-23	30-Jul-23
Gas Air Coolers		8	0%	$8,174.37	25-Sep-23	02-Oct-23
P12-E	1ST STAGE GAS COMPRESSION AIR COOLER	3	0%	$4,087.18	25-Sep-23	27-Sep-23
P12-E	2nd STAGE GAS COMPRESSION AIR COOLER	3	0%	$4,087.18	30-Sep-23	02-Oct-23
Storage Tank		8	0%	$17,088.80	23-Apr-23	30-Apr-23
P12-E	FIRE WATER STORAGE TANK	3	0%	$10,642.91	23-Apr-23	25-Apr-23
P12-E	Lean Glycol Storage Tank	3	0%	$442.60	28-Apr-23	30-Apr-23
P12-E	Slug Storage Tank	3	0%	$6,003.30	23-Apr-23	25-Apr-23
Instrument/Plant Air & Nitrogen Packages		83	0%	$13,052.08	23-Apr-23	14-Jul-23
P12-E	INSTRUMENT & PLANT AIR PACKAGE	3	0%	$5,958.27	23-Apr-23	25-Apr-23
P12-E	Nitrogen Package	3	0%	$7,093.80	12-Jul-23	14-Jul-23
Chemical Injection Packages		8	0%	$4,104.00	20-May-23	27-May-23
P12-E	Chemical Injection Package(corrosion inhibitor)	3	0%	$1,776.62	25-May-23	27-May-23
P12-E	Chemical Injection Package(Methanol)	3	0%	$2,327.38	20-May-23	22-May-23
Pumps - Process Services		83	0%	$4,137.64	13-May-23	03-Aug-23
P12-E	Glycol Transfer Pumps	3	0%	$563.55	01-Aug-23	03-Aug-23
P12-E	Glycol Manual Pump	3	0%	$359.97	01-Aug-23	03-Aug-23
P12-E	Slug Pumps	3	0%	$3,214.12	13-May-23	15-May-23
Pumps - General Services		139	0%	$7,198.83	13-May-23	28-Sep-23
P12-E	Potable Water Pump	3	0%	$980.48	26-Sep-23	28-Sep-23
P12-E	Diesel Pump	3	0%	$2,201.40	13-May-23	15-May-23
P12-E	Sump Pumps	3	0%	$999.20	01-Aug-23	03-Aug-23
P12-E	Closed Drain KO Drum Pumps	3	0%	$1,590.94	11-Aug-23	13-Aug-23
P12-E	Flare KO Drum Pumps	3	0%	$1,426.81	13-May-23	15-May-23
Fire Water Pumps		49	0%	$13,153.00	01-Aug-23	18-Sep-23
P12-E	Fire Water Pumps	3	0%	$11,716.30	16-Sep-23	18-Sep-23
P12-E	Jockey Pumps	3	0%	$1,436.70	01-Aug-23	03-Aug-23
Flare Packages		3	0%	$6,761.51	29-Jul-23	31-Jul-23
P12-E	LP Flare Package	3	0%	$6,761.51	29-Jul-23	31-Jul-23
Overhead Travelling Cranes		13	0%	$4,070.36	15-Apr-23	27-Apr-23
P12-E	Main Compressors Crane	3	0%	$1,930.98	20-Apr-23	22-Apr-23
P12-E	Diesel Generator & Air Package Crane	3	0%	$263.35	25-Apr-23	27-Apr-23

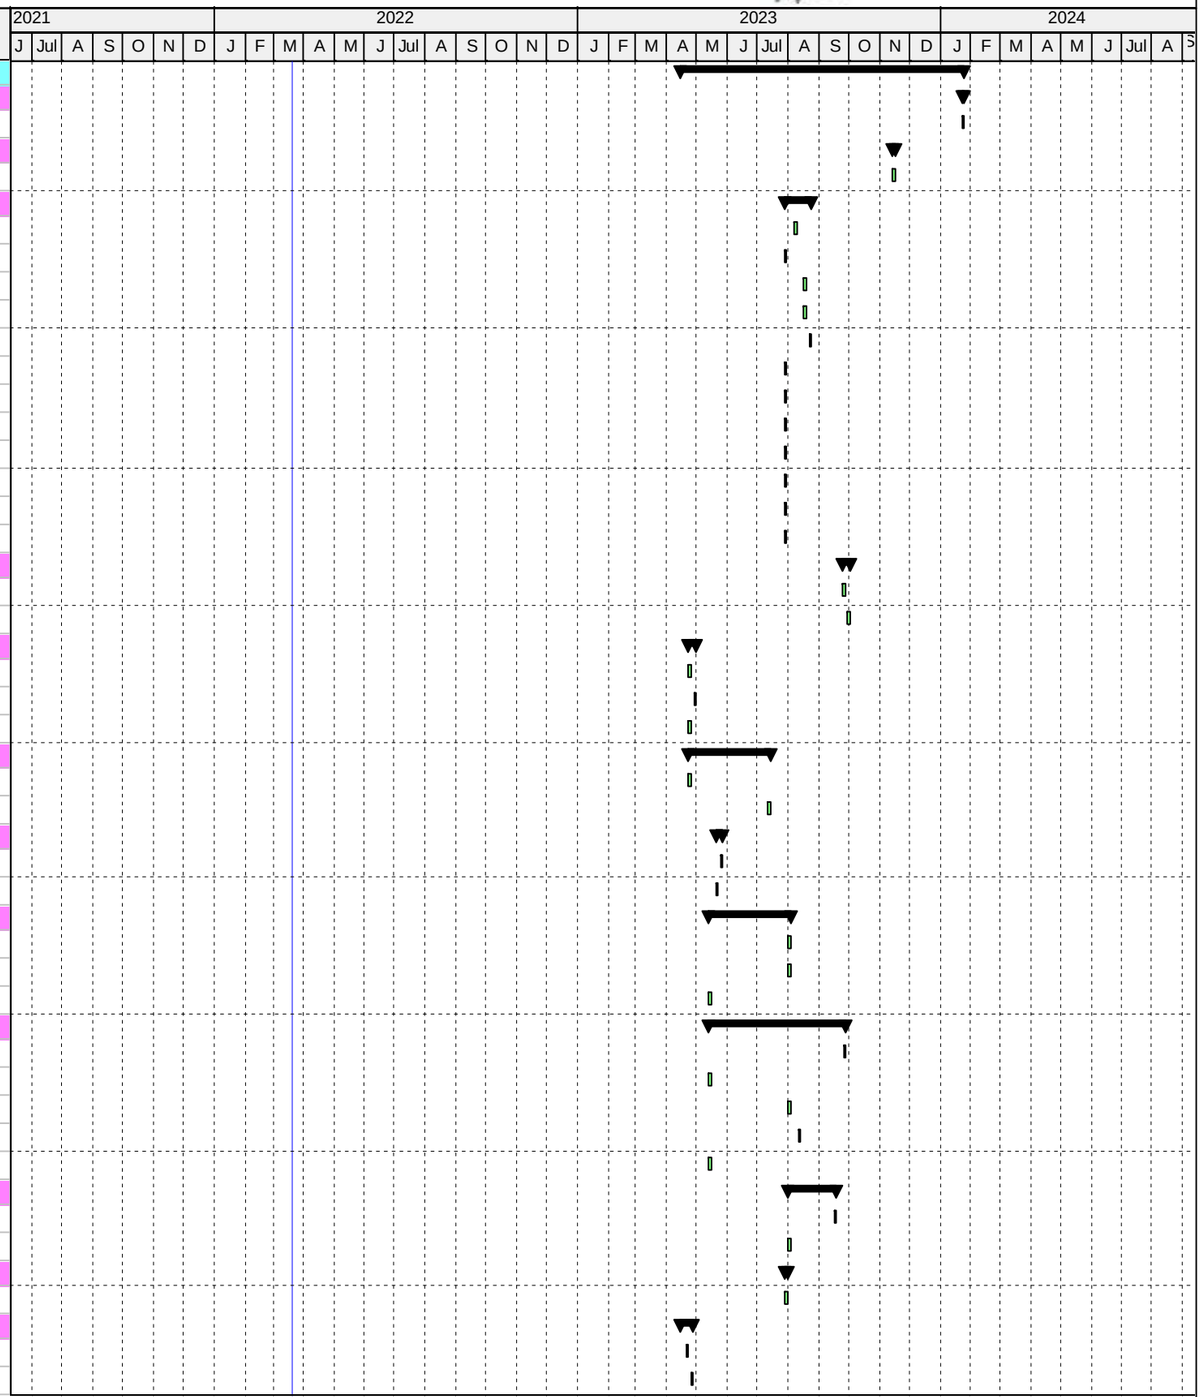


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Corrosion Inhib. & MeOH Pack. Crane	3	0%	$263.35	15-Apr-23	17-Apr-23
P12-E	Fire Water Pumps Crane	3	0%	$1,612.68	25-Apr-23	27-Apr-23
HVAC & Plumbing		7	0%	$2,704.46	31-Dec-23	06-Jan-24
P12-EF	Main HVAC Equipment	7	0%	$2,704.46	31-Dec-23	06-Jan-24
Piping		174	0%	$55,181.47	08-Apr-23	28-Sep-23
P12-EF	Pipes	7	0%	$28,804.73	22-Sep-23	28-Sep-23
P12-EF	Fittings	7	0%	$3,912.37	12-Sep-23	18-Sep-23
P12-EF	Flanges	7	0%	$2,262.44	21-Sep-23	27-Sep-23
P12-EF	Manual Valves	7	0%	$18,452.69	22-Sep-23	28-Sep-23
P12-EF	Gaskets	7	0%	$331.09	23-Aug-23	29-Aug-23
P12-EF	Bolt & Nuts	7	0%	$237.28	22-Jul-23	28-Jul-23
P12-EF	Insulation kits	5	0%	$93.81	26-Apr-23	30-Apr-23
P12-EF	Strainers	7	0%	$143.47	04-Sep-23	10-Sep-23
P12-EF	Pipe Supports	7	0%	$331.09	08-Apr-23	14-Apr-23
P12-EF	Insulation	7	0%	$187.62	22-Sep-23	28-Sep-23
P12-EF	Painting	7	0%	$237.28	27-Aug-23	02-Sep-23
P12-EF	Coating of Underground Piping	7	0%	$187.62	27-Aug-23	02-Sep-23
Control & Instrumentation		248	0%	$77,337.28	15-Jan-23	19-Sep-23
P12-EF	Control System/Console/Furniture	7	0%	$7,571.32	01-Jun-23	07-Jun-23
P12-EF	ESD System	7	0%	$5,684.29	02-Jun-23	08-Jun-23
P12-EF	F&G System	7	0%	$4,910.92	23-Apr-23	29-Apr-23
P12-EF	ON/OFF & Shutdown Valves	7	0%	$3,456.98	13-Sep-23	19-Sep-23
P12-EF	Control Valves	7	0%	$3,835.93	14-Aug-23	20-Aug-23
P12-EF	Pressure Safety Valves (PSV)	7	0%	$3,302.30	21-May-23	27-May-23
P12-EF	F&G Devices	7	0%	$4,431.43	01-Jun-23	07-Jun-23
P12-EF	Corrosion Probe/Coupon	7	0%	$1,840.63	31-Jul-23	06-Aug-23
P12-EF	Orifice and Restriction Orifice Plate	7	0%	$3,449.24	07-Apr-23	13-Apr-23
P12-EF	Differential Pressure/Pressure Gauge	7	0%	$1,384.34	07-May-23	13-May-23
P12-EF	Flow/Level /Pressure/Diff. Pressure Transmitter	7	0%	$3,155.36	11-May-23	17-May-23
P12-EF	Pressure/ Differential Pressure Switch	7	0%	$1,562.21	26-Jan-23	01-Feb-23
P12-EF	Temperature Gauge	7	0%	$1,863.83	06-Apr-23	12-Apr-23
P12-EF	Temperature Transmitter/Switch	7	0%	$3,619.38	06-May-23	12-May-23
P12-EF	Level Gauge	7	0%	$3,402.84	21-May-23	27-May-23
P12-EF	Level Switch	7	0%	$866.18	21-May-23	27-May-23
P12-EF	Displacer Level Transmitter	7	0%	$4,632.50	21-May-23	27-May-23
P12-EF	Rotameter	7	0%	$1,260.60	06-May-23	12-May-23
P12-EF	Instrument/F&G Cable	7	0%	$2,900.15	30-Jan-23	05-Feb-23
P12-EF	Instrument Cable Tray	7	0%	$4,501.03	31-Jul-23	06-Aug-23
P12-EF	Instrument/F&G Junction box and Gland	7	0%	$1,515.81	15-Jan-23	21-Jan-23
P12-EF	Instrument Tube and Fitting	7	0%	$1,887.03	04-Mar-23	10-Mar-23
P12-EF	Instrument Installation Accessories	7	0%	$997.65	09-May-23	15-May-23
P12-EF	CCTV System	7	0%	$3,426.04	07-Apr-23	13-Apr-23
P12-EF	IPR Panel	7	0%	$1,879.30	07-Feb-23	13-Feb-23
Safety & Fire Fighting		22	0%	$4,056.70	07-Oct-22	28-Oct-22
P12-EF	Total Flooding System	7	0%	$1,014.17	07-Oct-22	13-Oct-22
P12-EF	Deluge Valve & Water Spray	7	0%	$608.50	07-Oct-22	13-Oct-22
P12-EF	Safety Equipment	7	0%	$973.61	12-Oct-22	18-Oct-22
P12-EF	Fire Fighting Equipment	7	0%	$973.61	22-Oct-22	28-Oct-22

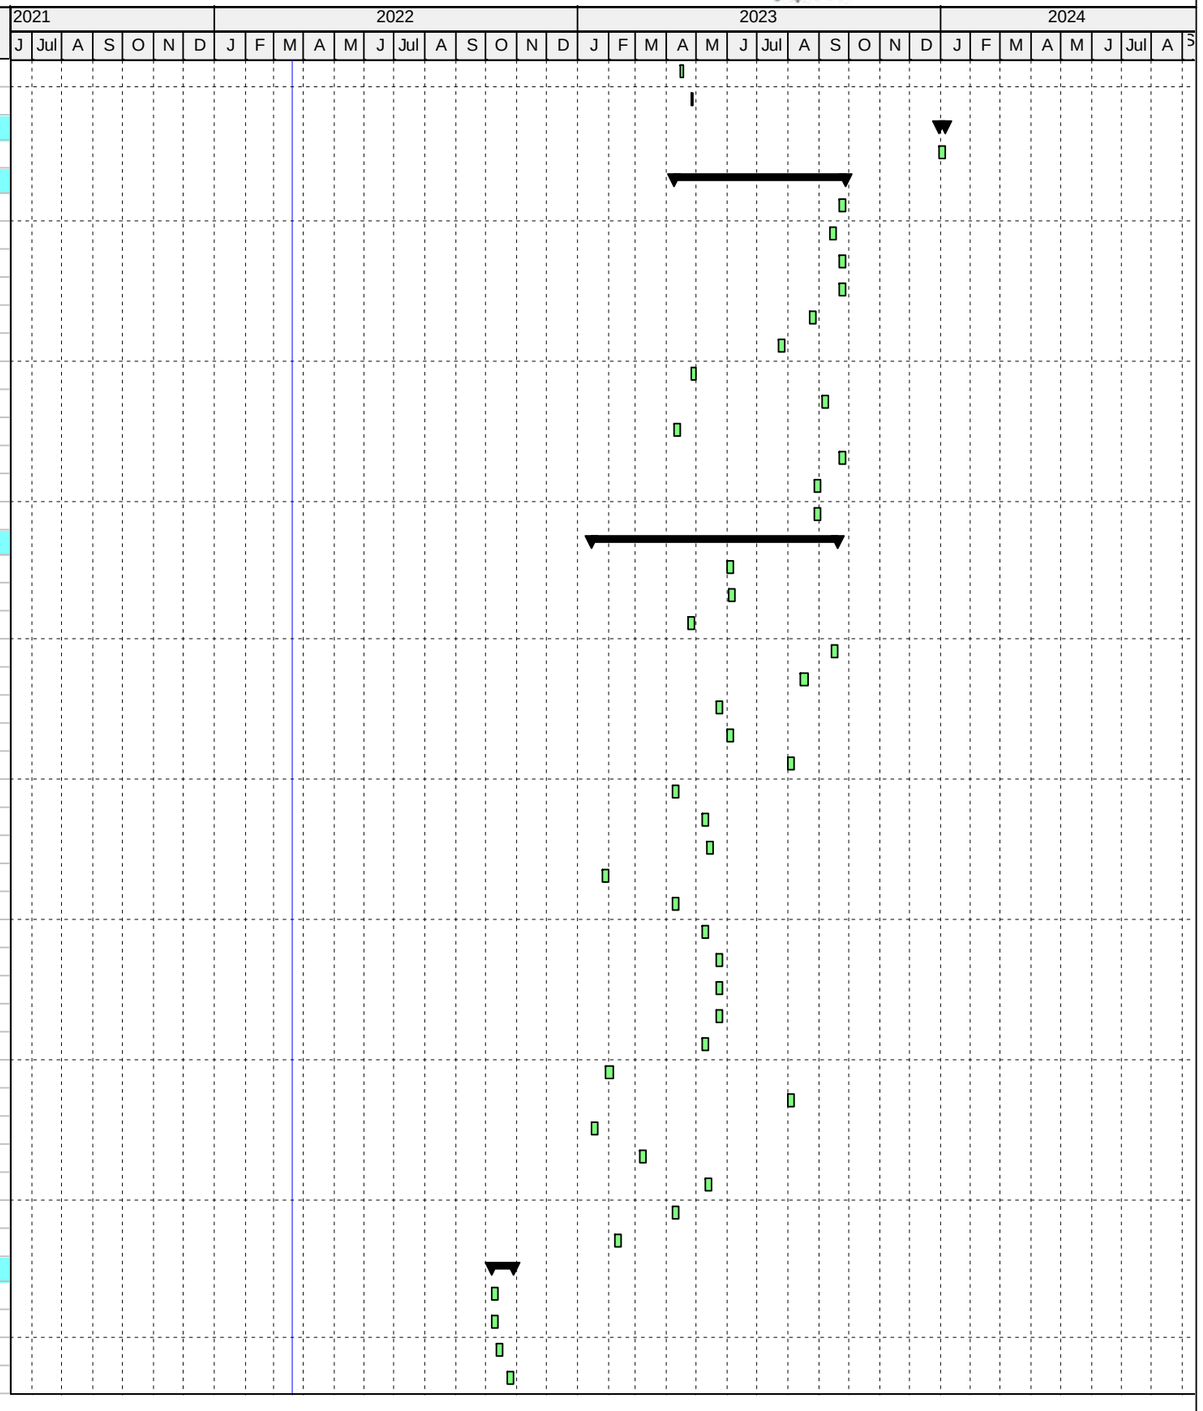

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-EI	Safety Signs	7	0%	$486.80	12-Oct-22	18-Oct-22
Electrical		385	0%	$37,862.50	07-Feb-23	26-Feb-24
P12-EI	Transformers	7	0%	$920.06	11-May-23	17-May-23
P12-EI	LV Switchgear & MCC	7	0%	$3,903.62	09-Apr-23	15-Apr-23
P12-EI	Existent MV Switchgear Expansion	7	0%	$7,311.25	09-Apr-23	15-Apr-23
P12-EI	Emergency Diesel Generator	7	0%	$1,575.08	27-Aug-23	02-Sep-23
P12-EI	UPS System	7	0%	$3,600.72	03-Jul-23	09-Jul-23
P12-EI	DC Charger	7	0%	$3,600.72	25-Jun-23	01-Jul-23
P12-EI	Lighting & Distribution Panels	7	0%	$503.57	09-Aug-23	15-Aug-23
P12-EI	Lighting and Small Power Equipment	7	0%	$1,260.82	05-Jul-23	11-Jul-23
P12-EI	Earthing & Lightning System	7	0%	$901.13	05-Jul-23	11-Jul-23
P12-EI	Local Control Station (LCS)	7	0%	$200.67	20-Feb-23	26-Feb-23
P12-EI	Capacitor Bank	7	0%	$1,503.14	20-Feb-23	26-Feb-23
P12-EI	NGR System	7	0%	$49.22	07-Feb-23	13-Feb-23
P12-EI	Cathodic Protection System	7	0%	$2,048.36	20-Feb-24	26-Feb-24
P12-EI	Power & Control Cables	7	0%	$7,705.02	25-Jun-23	01-Jul-23
P12-EI	Tray/Ladder and Accessories	7	0%	$1,643.23	22-Jul-23	28-Jul-23
P12-EI	Electrical Bulk Items	7	0%	$624.73	25-Jun-23	01-Jul-23
P12-EI	Telecomm UPS	7	0%	$511.14	14-Apr-23	20-Apr-23
Intercom & Telecom		435	0%	$6,553.13	16-Oct-22	24-Dec-23
P12-EI	PAGA System	7	0%	$680.21	31-Jul-23	06-Aug-23
P12-EI	PABX System	7	0%	$680.21	31-Jul-23	06-Aug-23
P12-EI	Radio System	7	0%	$1,864.36	16-Oct-22	22-Oct-22
P12-EI	Telecomm. Cable	7	0%	$1,313.25	18-Dec-23	24-Dec-23
P12-EI	Telecommunication Tower	7	0%	$2,015.09	26-Oct-22	01-Nov-22
Delivering Spare Part		508	0%	$866,815.50	14-Oct-22	04-Mar-24
Mechanical		286	0%	$589,434.54	18-Apr-23	28-Jan-24
Gas Compressors		3	0%	$327,548.77	26-Jan-24	28-Jan-24
P12-E	Gas Compressor of first & Second Stage	3	0%	$327,548.77	26-Jan-24	28-Jan-24
Gas Dehydration Package		3	0%	$109,340.11	17-Nov-23	19-Nov-23
P12-E	Dehydration Package	3	0%	$109,340.11	17-Nov-23	19-Nov-23
Pressure Vessels		28	0%	$16,327.34	31-Jul-23	27-Aug-23
P12-E	Inlet Knock Out Drum	3	0%	$305.32	10-Aug-23	12-Aug-23
P12-E	1ST STAGE GAS COMPRESSION SUCTION DRUM	3	0%	$2,163.37	31-Jul-23	02-Aug-23
P12-E	2nd STAGE GAS COMPRESSION SUCTION DRUM	3	0%	$1,763.35	20-Aug-23	22-Aug-23
P12-E	2nd STAGE GAS COMPRESSION DISCHARGE DRUM	3	0%	$814.73	20-Aug-23	22-Aug-23
P12-E	Diesel Oil Storage Tank	3	0%	$1,464.56	25-Aug-23	27-Aug-23
P12-E	Instrument Air Receiver	3	0%	$736.36	31-Jul-23	02-Aug-23
P12-E	Close drain drum	3	0%	$2,759.32	31-Jul-23	02-Aug-23
P12-E	Potable Water Drum	3	0%	$96.33	31-Jul-23	02-Aug-23
P12-E	Flare K.O. Drum	3	0%	$393.49	31-Jul-23	02-Aug-23
P12-E	Fuel Gas K.O. Drum	3	0%	$496.35	31-Jul-23	02-Aug-23
P12-E	Slug Catcher	3	0%	$4,478.59	31-Jul-23	02-Aug-23
P12-E	Degassing vessel	3	0%	$855.55	31-Jul-23	02-Aug-23
Gas Air Coolers		8	0%	$14,323.26	28-Sep-23	05-Oct-23
P12-E	1ST STAGE GAS COMPRESSION AIR COOLER	3	0%	$7,161.63	28-Sep-23	30-Sep-23
P12-E	2nd STAGE GAS COMPRESSION AIR COOLER	3	0%	$7,161.63	03-Oct-23	05-Oct-23
Storage Tank		8	0%	$29,943.27	26-Apr-23	03-May-23
P12-E	FIRE WATER STORAGE TANK	3	0%	$18,648.67	26-Apr-23	28-Apr-23




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	Lean Glycol Storage Tank	3	0%	$775.53	01-May-23	03-May-23
P12-E	Slug Storage Tank	3	0%	$10,519.07	26-Apr-23	28-Apr-23
Instrument/Plant Air & Nitrogen Packages		83	0%	$22,870.06	26-Apr-23	17-Jul-23
P12-E	INSTRUMENT & PLANT AIR PACKAGE	3	0%	$10,440.18	26-Apr-23	28-Apr-23
P12-E	Nitrogen Package	3	0%	$12,429.88	15-Jul-23	17-Jul-23
Chemical Injection Packages		8	0%	$7,191.10	23-May-23	30-May-23
P12-E	Chemical Injection Package(corrosion inhibitor)	3	0%	$3,113.03	28-May-23	30-May-23
P12-E	Chemical Injection Package(Methanol)	3	0%	$4,078.07	23-May-23	25-May-23
Pumps - Process Services		83	0%	$7,250.04	16-May-23	06-Aug-23
P12-E	Glycol Transfer Pumps	3	0%	$987.46	04-Aug-23	06-Aug-23
P12-E	Glycol Manual Pump	3	0%	$630.75	04-Aug-23	06-Aug-23
P12-E	Slug Pumps	3	0%	$5,631.83	16-May-23	18-May-23
Pumps - General Services		139	0%	$12,613.90	16-May-23	01-Oct-23
P12-E	Potable Water Pump	3	0%	$1,718.01	29-Sep-23	01-Oct-23
P12-E	Diesel Pump	3	0%	$3,857.33	16-May-23	18-May-23
P12-E	Sump Pumps	3	0%	$1,750.81	04-Aug-23	06-Aug-23
P12-E	Closed Drain KO Drum Pumps	3	0%	$2,787.67	14-Aug-23	16-Aug-23
P12-E	Flare KO Drum Pumps	3	0%	$2,500.07	16-May-23	18-May-23
Fire Water Pumps		49	0%	$23,046.89	04-Aug-23	21-Sep-23
P12-E	Fire Water Pumps	3	0%	$20,529.49	19-Sep-23	21-Sep-23
P12-E	Jockey Pumps	3	0%	$2,517.40	04-Aug-23	06-Aug-23
Flare Packages		3	0%	$11,847.63	01-Aug-23	03-Aug-23
P12-E	LP Flare Package	3	0%	$11,847.63	01-Aug-23	03-Aug-23
Overhead Travelling Cranes		13	0%	$7,132.16	18-Apr-23	30-Apr-23
P12-E	Main Compressors Crane	3	0%	$3,383.50	23-Apr-23	25-Apr-23
P12-E	Diesel Generator & Air Package Crane	3	0%	$461.45	28-Apr-23	30-Apr-23
P12-E	Corrosion Inhib. & MeOH Pack. Crane	3	0%	$461.45	18-Apr-23	20-Apr-23
P12-E	Fire Water Pumps Crane	3	0%	$2,825.76	28-Apr-23	30-Apr-23
Piping		7	0%	$62,844.12	29-Sep-23	05-Oct-23
P12-EI	Manual Valves	7	0%	$62,844.12	29-Sep-23	05-Oct-23
Control & Instrumentation		237	0%	$116,153.28	02-Feb-23	26-Sep-23
P12-EI	Control System/Console/Furniture	7	0%	$12,126.40	08-Jun-23	14-Jun-23
P12-EI	ESD System	7	0%	$9,106.42	09-Jun-23	15-Jun-23
P12-EI	F&G System	7	0%	$9,106.42	30-Apr-23	06-May-23
P12-EI	ON/OFF & Shutdown Valves	7	0%	$1,823.61	20-Sep-23	26-Sep-23
P12-EI	Control Valves	7	0%	$2,427.60	21-Aug-23	27-Aug-23
P12-EI	Pressure Safety Valves (PSV)	7	0%	$1,823.61	28-May-23	03-Jun-23
P12-EI	F&G Devices	7	0%	$8,339.81	08-Jun-23	14-Jun-23
P12-EI	Corrosion Probe/Coupon	7	0%	$2,950.29	07-Aug-23	13-Aug-23
P12-EI	Orifice and Restriction Orifice Plate	7	0%	$5,528.90	14-Apr-23	20-Apr-23
P12-EI	Differential Pressure/Pressure Gauge	7	0%	$2,218.53	14-May-23	20-May-23
P12-EI	Flow/Level /Pressure/Diff. Pressure Transmitter	7	0%	$11,255.25	18-May-23	24-May-23
P12-EI	Pressure/ Differential Pressure Switch	7	0%	$1,010.53	02-Feb-23	08-Feb-23
P12-EI	Temperature Gauge	7	0%	$2,985.14	13-Apr-23	19-Apr-23
P12-EI	Temperature Transmitter/Switch	7	0%	$7,038.89	13-May-23	19-May-23
P12-EI	Level Gauge	7	0%	$12,881.40	28-May-23	03-Jun-23
P12-EI	Level Switch	7	0%	$1,382.22	28-May-23	03-Jun-23
P12-EI	Displacer Level Transmitter	7	0%	$21,046.97	28-May-23	03-Jun-23
P12-EI	Rotameter	7	0%	$2,032.68	13-May-23	19-May-23

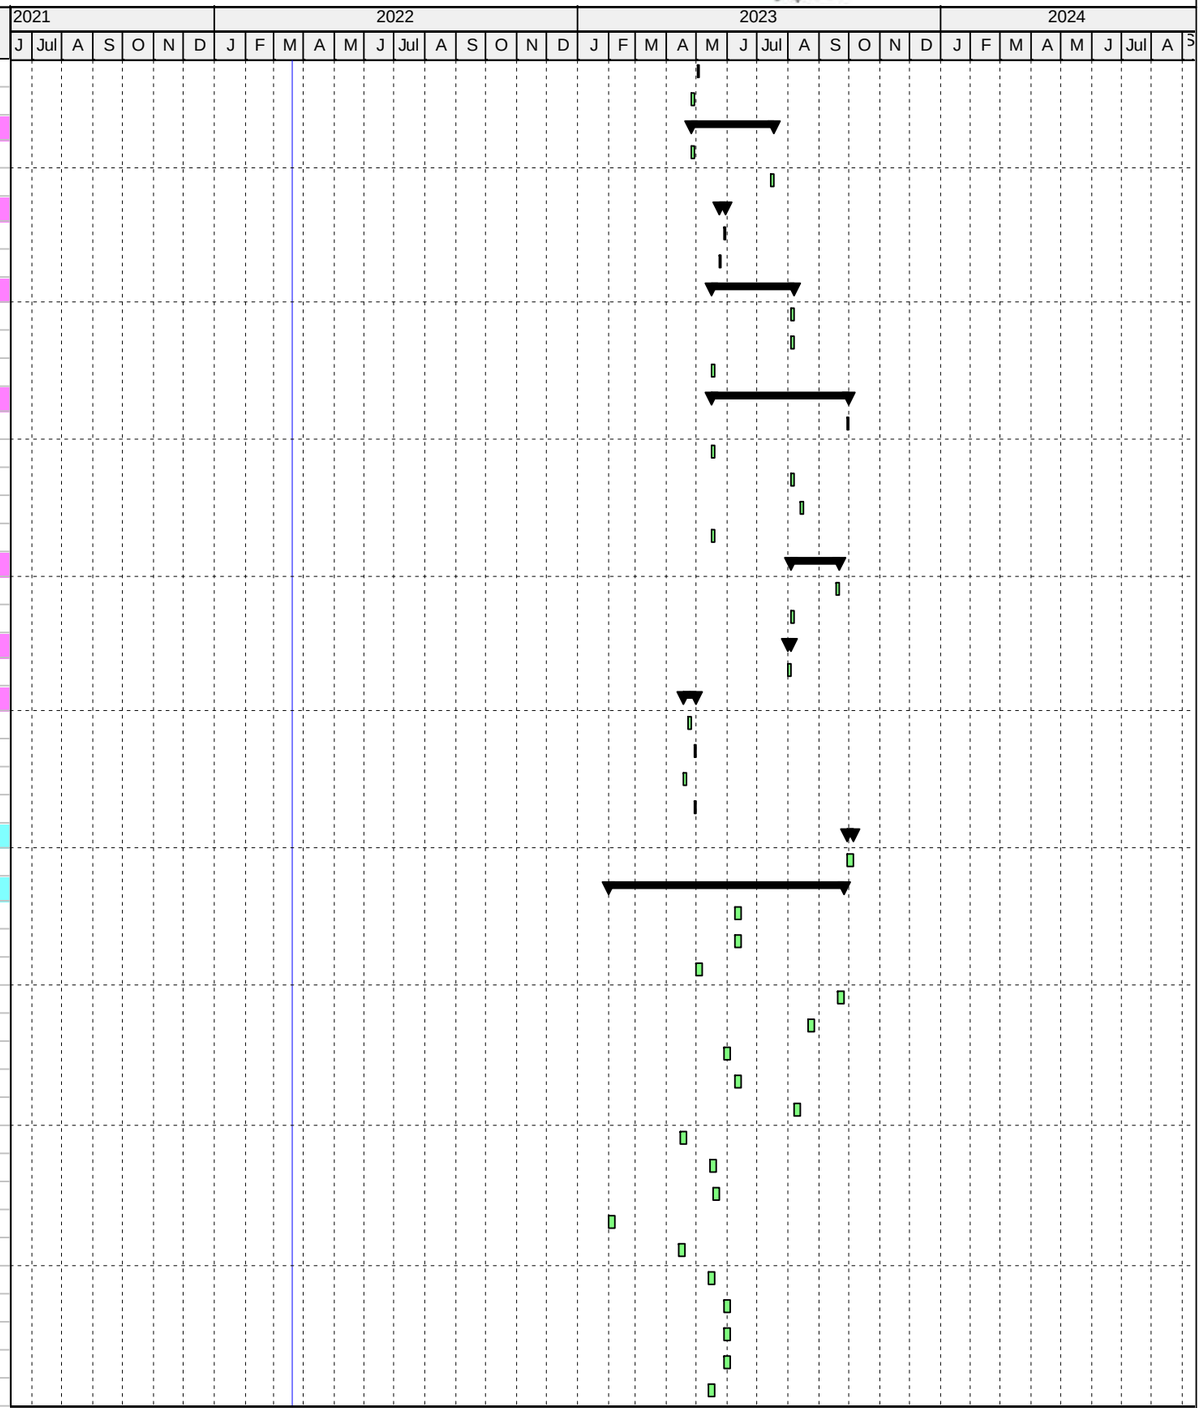

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-EI	CCTV System	7	0%	$534.31	14-Apr-23	20-Apr-23
P12-EI	IPR Panel	7	0%	$534.31	14-Feb-23	20-Feb-23
Safety & Fire Fighting		22	0%	$5,634.30	14-Oct-22	04-Nov-22
P12-EI	Total Flooding System	7	0%	$2,253.72	14-Oct-22	20-Oct-22
P12-EI	Deluge Valve & Water Spray	7	0%	$1,239.55	14-Oct-22	20-Oct-22
P12-EI	Fire Fighting Equipment	7	0%	$2,141.03	29-Oct-22	04-Nov-22
Electrical		385	0%	$92,749.26	14-Feb-23	04-Mar-24
P12-EI	Transformers	7	0%	$2,726.83	18-May-23	24-May-23
P12-EI	LV Switchgear & MCC	7	0%	$8,653.51	16-Apr-23	22-Apr-23
P12-EI	Existent MV Switchgear Expansion	7	0%	$7,076.77	16-Apr-23	22-Apr-23
P12-EI	Emergency Diesel Generator	7	0%	$2,420.76	03-Sep-23	09-Sep-23
P12-EI	UPS System	7	0%	$8,430.91	10-Jul-23	16-Jul-23
P12-EI	DC Charger	7	0%	$8,430.91	02-Jul-23	08-Jul-23
P12-EI	Lighting & Distribution Panels	7	0%	$1,493.26	16-Aug-23	22-Aug-23
P12-EI	Lighting and Small Power Equipment	7	0%	$1,493.26	12-Jul-23	18-Jul-23
P12-EI	Earthing & Lightning System	7	0%	$2,671.18	12-Jul-23	18-Jul-23
P12-EI	Local Control Station (LCS)	7	0%	$593.60	27-Feb-23	05-Mar-23
P12-EI	Capacitor Bank	7	0%	$5,574.23	27-Feb-23	05-Mar-23
P12-EI	NGR System	7	0%	$148.40	14-Feb-23	20-Feb-23
P12-EI	Cathodic Protection System	7	0%	$42,646.11	27-Feb-24	04-Mar-24
P12-EI	Telecomm UPS	7	0%	$389.55	21-Apr-23	27-Apr-23
CONSTRUCTION		712	0%	$3,605,059.00	13-May-22	23-Apr-24
Compressor Station		712	0%	$3,569,008.41	13-May-22	23-Apr-24
Civil, Structure & Architecture		425	0%	$761,269.49	18-Jul-22	15-Sep-23
Site Preparation		30	0%	$11,419.04	18-Jul-22	16-Aug-22
P12-E	Site Preparation	30	0%	$11,419.04	18-Jul-22	16-Aug-22
Land Scape		342	0%	$106,577.73	17-Aug-22	24-Jul-23
P12-E	Open Ditch	30	0%	$20,249.77	17-Aug-22	15-Sep-22
P12-E	Ditch	30	0%	$15,986.66	17-Aug-22	15-Sep-22
P12-E	Cable Trenches	80	0%	$17,052.44	24-Dec-22	13-Mar-23
P12-E	Drainage System	80	0%	$19,183.99	14-Jan-23	03-Apr-23
P12-E	Walkways	60	0%	$9,592.00	25-Feb-23	25-Apr-23
P12-E	Oily Water Separator	45	0%	$17,052.44	26-Apr-23	09-Jun-23
P12-E	Septic Tank	45	0%	$7,460.44	10-Jun-23	24-Jul-23
Foundations		154	0%	$365,409.36	07-Apr-23	07-Sep-23
Drums & Vessels		154	0%	$20,426.38	07-Apr-23	07-Sep-23
P12-	Inlet Knock Out Drum, V-101	30	0%	$655.69	09-Aug-23	07-Sep-23
P12-	1ST STAGE GAS COMPRESSION SUCTION DRUM, V-102	45	0%	$1,965.02	07-Apr-23	21-May-23
P12-	2nd STAGE GAS COMPRESSION SUCTION DRUM, V-103	45	0%	$2,357.20	07-Apr-23	21-May-23
P12-	2nd STAGE GAS COMPRESSION DISCHARGE DRUM, V-	45	0%	$3,601.17	07-Apr-23	21-May-23
P12-	Diesel Oil Storage Tank, V-105	30	0%	$1,178.60	07-Apr-23	06-May-23
P12-	Instrument Air Receiver, V-106	35	0%	$1,309.33	07-Apr-23	11-May-23
P12-	Close drain drum, V-107	35	0%	$2,095.75	07-Apr-23	11-May-23
P12-	Potable Water Drum, V-108	45	0%	$1,440.06	07-Apr-23	21-May-23
P12-	Flare K.O. Drum, V-109	45	0%	$1,174.52	07-Apr-23	21-May-23
P12-	Fuel Gas K.O. Drum, V-110	30	0%	$721.05	07-Apr-23	06-May-23
P12-	Slug Catcher, V-111	30	0%	$2,161.11	07-Apr-23	06-May-23
P12-	Degassing vessel, V-112	30	0%	$1,766.88	07-Apr-23	06-May-23
Storage Tank		35	0%	$15,968.39	07-Apr-23	11-May-23




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-	FIRE WATER STORAGE TANK, TK-102	30	0%	$10,847.33	07-Apr-23	06-May-23
P12-	Lean Glycol Storage Tank, TK-101	30	0%	$651.51	07-Apr-23	06-May-23
P12-	Slug Storage Tank, TK-103	35	0%	$4,469.55	07-Apr-23	11-May-23
Air cooler		90	0%	$8,002.46	07-Apr-23	05-Jul-23
P12-	Air Cooler	90	0%	$8,002.46	07-Apr-23	05-Jul-23
Packages		90	0%	$71,766.40	07-Apr-23	05-Jul-23
P12-	Dehydration Package, PK-101	60	0%	$43,059.84	07-Apr-23	05-Jun-23
P12-	Diesel Generator, PK-102	30	0%	$1,794.16	07-Apr-23	06-May-23
P12-	INSTRUMENT & PLANT AIR PACKAGE, PK-103	90	0%	$7,176.64	07-Apr-23	05-Jul-23
P12-	Chemical Injection Package(corrosion inhibitor), PK-105	90	0%	$1,435.33	07-Apr-23	05-Jul-23
P12-	Chemical Injection Package(Methanol), PK-106	30	0%	$1,794.16	07-Apr-23	06-May-23
P12-	LP Flare Package, PK-107	60	0%	$9,329.63	07-Apr-23	05-Jun-23
P12-	Nitrogen Package, PK-108	60	0%	$7,176.64	07-Apr-23	05-Jun-23
Pumps		45	0%	$12,423.92	07-Apr-23	21-May-23
P12-	Glycol Transfer Pumps, P-101 A/B	45	0%	$606.29	07-Apr-23	21-May-23
P12-	Glycol Manual Pump, P-102	15	0%	$242.27	07-Apr-23	21-Apr-23
P12-	Closed Drain KO Drum Pumps, P-103 A/B	20	0%	$485.78	07-Apr-23	26-Apr-23
P12-	Sump Pumps, P-104 A/B	20	0%	$485.78	07-Apr-23	26-Apr-23
P12-	Jockey Pumps, P-105 A/B	10	0%	$1,262.27	07-Apr-23	16-Apr-23
P12-	Fire Water Pumps, P-106 A/B/C	15	0%	$6,551.13	07-Apr-23	21-Apr-23
P12-	Potable Water Pump, P-107	10	0%	$242.27	07-Apr-23	16-Apr-23
P12-	Diesel Pump, P-108	20	0%	$121.75	07-Apr-23	26-Apr-23
P12-	Flare KO Drum Pumps, P-109 A/B	20	0%	$970.31	07-Apr-23	26-Apr-23
P12-	Slug Pumps, P-110 A/B	20	0%	$1,456.08	07-Apr-23	26-Apr-23
Compressor		90	0%	$236,821.80	07-Apr-23	05-Jul-23
P12-	Gas Compressor of first Stage,C-101/2 A/B/C	90	0%	$236,821.80	07-Apr-23	05-Jul-23
Shelters		333	0%	$114,190.42	17-Aug-22	15-Jul-23
Compressor Station Shelter		55	0%	$41,873.63	22-May-23	15-Jul-23
P12-	Foundation	25	0%	$10,468.41	22-May-23	15-Jun-23
P12-	fabrication	35	0%	$23,030.50	22-May-23	25-Jun-23
P12-	installation	20	0%	$8,374.73	26-Jun-23	15-Jul-23
Chemical Injection Package Shelter		65	0%	$12,172.70	17-Aug-22	20-Oct-22
P12-	Foundation	30	0%	$3,043.17	17-Aug-22	15-Sep-22
P12-	fabrication	35	0%	$6,694.98	17-Aug-22	20-Sep-22
P12-	installation	30	0%	$2,434.54	21-Sep-22	20-Oct-22
Air Compressor Shelter		85	0%	$12,184.12	02-Dec-22	24-Feb-23
P12-	Foundation	30	0%	$3,046.03	02-Dec-22	31-Dec-22
P12-	fabrication	40	0%	$6,701.27	02-Dec-22	10-Jan-23
P12-	installation	45	0%	$2,436.82	11-Jan-23	24-Feb-23
Pipe Rack		85	0%	$26,640.63	17-Aug-22	09-Nov-22
P12-	Foundation	60	0%	$6,660.16	17-Aug-22	15-Oct-22
P12-	fabrication	45	0%	$14,652.34	17-Aug-22	30-Sep-22
P12-	installation	40	0%	$5,328.13	01-Oct-22	09-Nov-22
Fire Shed		50	0%	$10,665.39	30-Aug-22	18-Oct-22
P12-	Foundation	25	0%	$2,666.35	30-Aug-22	23-Sep-22
P12-	fabrication	20	0%	$5,865.96	30-Aug-22	18-Sep-22
P12-	installation	30	0%	$2,133.08	19-Sep-22	18-Oct-22
Emergency Diesel generator Shelter		55	0%	$10,653.97	14-Sep-22	07-Nov-22
P12-	Foundation	25	0%	$2,663.49	14-Sep-22	08-Oct-22

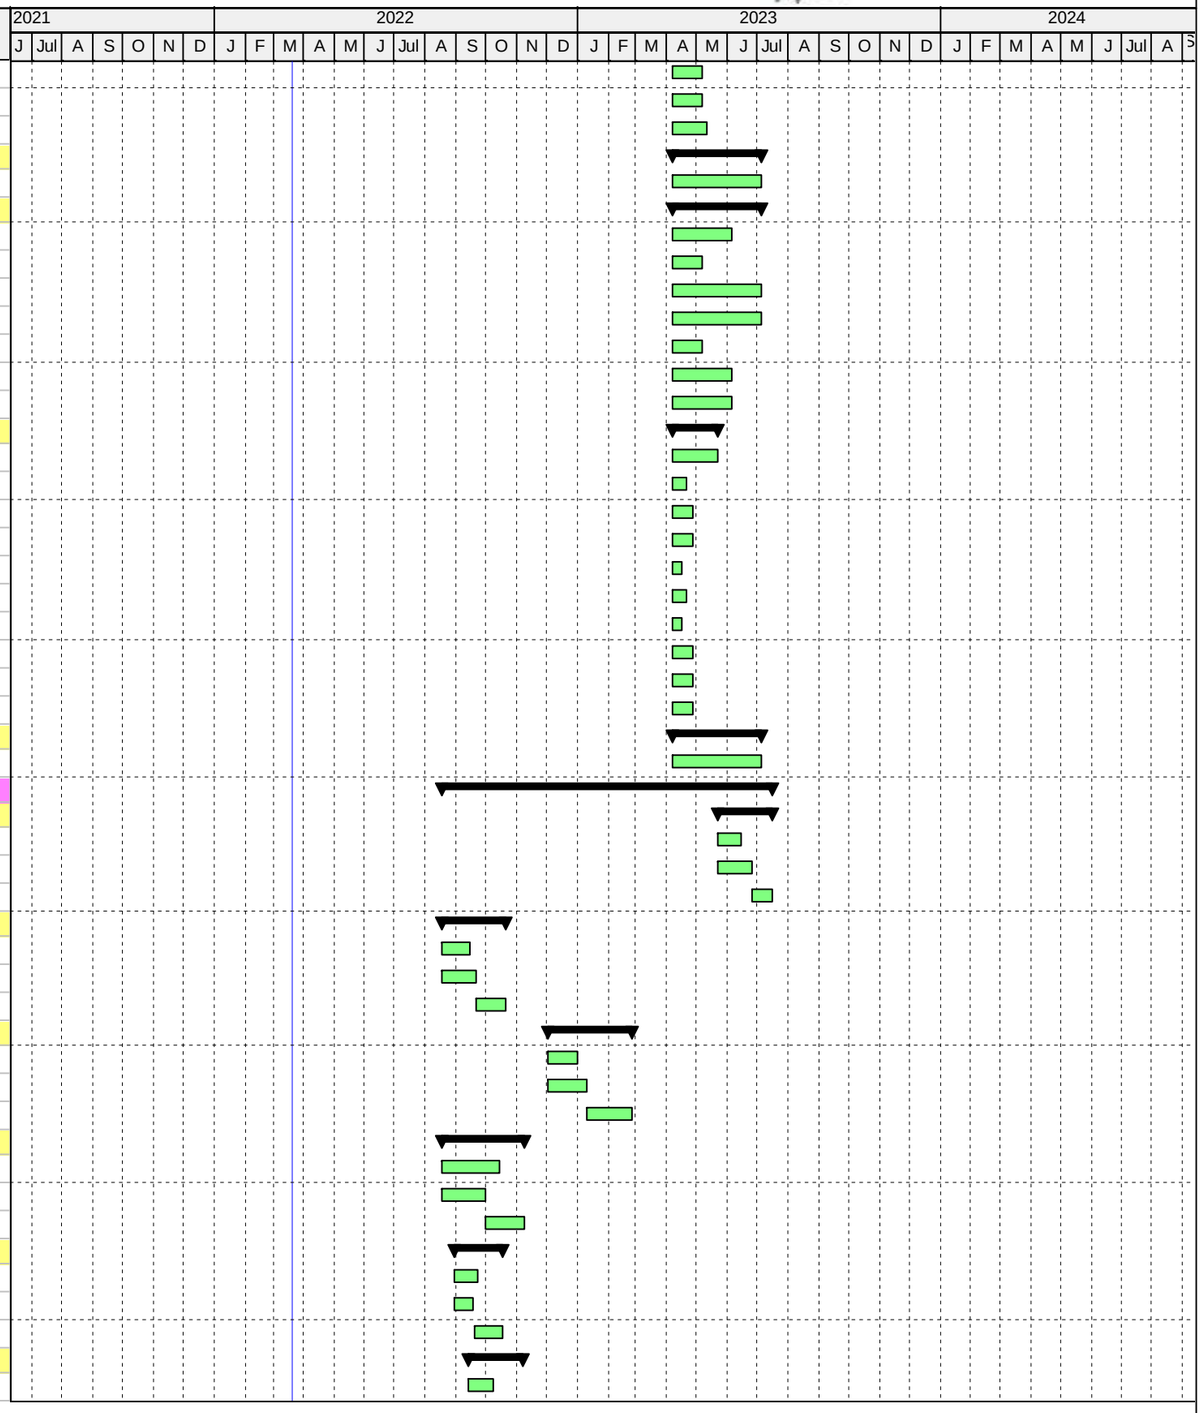

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-	fabrication	30	0%	$5,859.68	14-Sep-22	13-Oct-22
P12-	installation	25	0%	$2,130.79	14-Oct-22	07-Nov-22
Buildings		395	0%	$121,803.12	17-Aug-22	15-Sep-23
Switchgear Extension		388	0%	$37,758.97	17-Aug-22	08-Sep-23
Foundation		102	0%	$11,705.28	17-Aug-22	26-Nov-22
P12	Excavation & Soil Transfer (Removing of Vegetal Soil)	30	0%	$2,341.06	17-Aug-22	15-Sep-22
P12	Levelling	25	0%	$234.11	01-Sep-22	25-Sep-22
P12	Lean Concrete	2	0%	$1,170.53	26-Sep-22	27-Sep-22
P12	Reinforced Work	45	0%	$2,341.06	13-Sep-22	27-Oct-22
P12	Formwork	30	0%	$936.42	13-Oct-22	11-Nov-22
P12	Main Concrete Pouring	5	0%	$4,565.06	12-Nov-22	16-Nov-22
P12	Backfilling & Compaction	10	0%	$117.05	17-Nov-22	26-Nov-22
Structure		80	0%	$15,103.59	01-Feb-23	21-Apr-23
P12	Steel Material Supply	35	0%	$7,551.79	01-Feb-23	07-Mar-23
P12	Shop Fabrication of Steel Structure	30	0%	$3,020.72	08-Mar-23	06-Apr-23
P12	Structural Installation	20	0%	$3,020.72	28-Mar-23	16-Apr-23
P12	Structural Painting	5	0%	$1,510.36	17-Apr-23	21-Apr-23
Architectural		140	0%	$10,950.10	22-Apr-23	08-Sep-23
P12	Wall Execution	30	0%	$5,745.72	27-May-23	25-Jun-23
P12	Roof Covering	25	0%	$725.09	16-Jun-23	10-Jul-23
P12	Roof Execution (Block Joist, Concrete Pouring)	30	0%	$1,653.49	11-Jul-23	09-Aug-23
P12	Building Walkway (around Building)	35	0%	$326.08	22-Apr-23	26-May-23
P12	Joinery (Cornice, Façade, Plaster)	30	0%	$2,499.72	10-Aug-23	08-Sep-23
Administration and Control Building		278	0%	$84,044.15	12-Dec-22	15-Sep-23
Foundation		137	0%	$26,053.69	12-Dec-22	27-Apr-23
P12	Excavation & Soil Transfer (Removing of Vegetal Soil)	45	0%	$5,210.74	12-Dec-22	25-Jan-23
P12	Levelling	30	0%	$521.07	11-Jan-23	09-Feb-23
P12	Lean Concrete	2	0%	$2,605.37	10-Feb-23	11-Feb-23
P12	Reinforced Work	45	0%	$5,210.74	21-Jan-23	06-Mar-23
P12	Formwork	50	0%	$2,084.29	12-Feb-23	02-Apr-23
P12	Main Concrete Pouring	10	0%	$10,160.94	03-Apr-23	12-Apr-23
P12	Backfilling & Compaction	15	0%	$260.54	13-Apr-23	27-Apr-23
Structure		95	0%	$33,617.66	25-Mar-23	27-Jun-23
P12	Steel Material Supply	45	0%	$16,808.83	25-Mar-23	08-May-23
P12	Shop Fabrication of Steel Structure	30	0%	$6,723.53	29-Apr-23	28-May-23
P12	Structural Installation	35	0%	$6,723.53	14-May-23	17-Jun-23
P12	Structural Painting	15	0%	$3,361.77	13-Jun-23	27-Jun-23
Architectural		80	0%	$24,372.80	28-Jun-23	15-Sep-23
P12	Wall Execution	25	0%	$11,910.52	28-Jun-23	22-Jul-23
P12	Roof Covering	30	0%	$2,901.58	13-Jul-23	11-Aug-23
P12	Roof Execution (Block Joist, Concrete Pouring)	25	0%	$3,700.11	02-Aug-23	26-Aug-23
P12	Building Walkway (around Building)	20	0%	$1,251.74	25-Jul-23	13-Aug-23
P12	Joinery (Cornice, Façade, Plaster)	20	0%	$4,608.86	27-Aug-23	15-Sep-23
Finish Grading		15	0%	$41,869.82	25-Jul-23	08-Aug-23
P12-E	Finish Grading	15	0%	$41,869.82	25-Jul-23	08-Aug-23
Piping		211	0%	$737,357.14	30-Jul-23	25-Feb-24
P12-EF	Pipe sleeper/Support	95	0%	$110,603.57	30-Jul-23	01-Nov-23
P12-EF	Material Handeling	90	0%	$73,735.71	19-Sep-23	17-Dec-23
P12-EF	Fit-Up & Welding	95	0%	$368,678.57	29-Sep-23	01-Jan-24




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-EI	NDT	75	0%	$51,615.00	13-Nov-23	26-Jan-24
P12-EI	Acid Washing	20	0%	$36,867.86	06-Feb-24	25-Feb-24
P12-EI	Hydrotest	20	0%	$58,988.57	17-Jan-24	05-Feb-24
P12-EI	insulation & Painting	80	0%	$36,867.86	29-Sep-23	17-Dec-23
Mechanical		522	0%	$1,070,702.52	19-Oct-22	23-Mar-24
Instalation of Pumps		50	0%	$53,963.41	17-Apr-23	05-Jun-23
P12-E	Glycol Transfer Pumps, P-101 A/B	15	0%	$2,633.41	22-May-23	05-Jun-23
P12-E	Glycol Manual Pump, P-102	15	0%	$1,052.29	22-Apr-23	06-May-23
P12-E	Closed Drain KO Drum Pumps, P-103 A/B	15	0%	$2,109.97	27-Apr-23	11-May-23
P12-E	Sump Pumps, P-104 A/B	15	0%	$2,109.97	27-Apr-23	11-May-23
P12-E	Jockey Pumps, P-105 A/B	15	0%	$5,482.68	17-Apr-23	01-May-23
P12-E	Fire Water Pumps, P-106 A/B/C	15	0%	$28,454.90	22-Apr-23	06-May-23
P12-E	Potable Water Pump, P-107	15	0%	$1,052.29	17-Apr-23	01-May-23
P12-E	Diesel Pump, P-108	15	0%	$528.84	27-Apr-23	11-May-23
P12-E	Flare KO Drum Pumps, P-109 A/B	15	0%	$4,214.54	27-Apr-23	11-May-23
P12-E	Slug Pumps, P-110 A/B	15	0%	$6,324.51	27-Apr-23	11-May-23
Instalation of Compressor		60	0%	$693,922.31	24-Jan-24	23-Mar-24
P12-E	Gas Compressor of first & Second Stage,C-101 A/B/C - C-10	60	0%	$693,922.31	24-Jan-24	23-Mar-24
Instalation of Packages		120	0%	$210,285.98	07-May-23	03-Sep-23
P12-E	Dehydration Package, PK-101	45	0%	$126,171.59	06-Jun-23	20-Jul-23
P12-E	Diesel Generator, PK-102	45	0%	$5,257.15	07-May-23	20-Jun-23
P12-E	INSTRUMENT & PLANT AIR PACKAGE, PK-103	30	0%	$21,028.60	06-Jul-23	04-Aug-23
P12-E	Chemical Injection Package(corrosion inhibitor), PK-105	60	0%	$4,205.72	06-Jul-23	03-Sep-23
P12-E	Chemical Injection Package(Methanol), PK-106	60	0%	$5,257.15	07-May-23	05-Jul-23
P12-E	LP Flare Package, PK-107	50	0%	$27,337.18	06-Jun-23	25-Jul-23
P12-E	Nitrogen Package, PK-108	60	0%	$21,028.60	06-Jun-23	04-Aug-23
Instalation of Crane		315	0%	$16,381.75	19-Oct-22	29-Aug-23
P12-E	Main Compressors Crane, CR-101	45	0%	$7,352.13	16-Jul-23	29-Aug-23
P12-E	Diesel Generator & Air Package Crane, CR-102	45	0%	$1,364.60	08-Nov-22	22-Dec-22
P12-E	Corrosion Inhib. & MeOH Pack. Crane, CR-103	45	0%	$1,364.60	21-Oct-22	04-Dec-22
P12-E	Fire Water Pumps Crane, CR-104	45	0%	$6,300.42	19-Oct-22	02-Dec-22
Instalation of Drums & Vessels		139	0%	$32,763.50	07-May-23	22-Sep-23
P12-E	Inlet Knock Out Drum, V-101	15	0%	$1,051.71	08-Sep-23	22-Sep-23
P12-E	1ST STAGE GAS COMPRESSION SUCTION DRUM, V-102	20	0%	$3,145.30	22-May-23	10-Jun-23
P12-E	2nd STAGE GAS COMPRESSION SUCTION DRUM, V-103	20	0%	$3,780.91	22-May-23	10-Jun-23
P12-E	2nd STAGE GAS COMPRESSION DISCHARGE DRUM, V-:	20	0%	$5,776.20	22-May-23	10-Jun-23
P12-E	Diesel Oil Storage Tank, V-105	15	0%	$1,890.45	07-May-23	21-May-23
P12-E	Instrument Air Receiver, V-106	15	0%	$2,100.14	12-May-23	26-May-23
P12-E	Close drain drum, V-107	15	0%	$3,361.53	12-May-23	26-May-23
P12-E	Potable Water Drum, V-108	15	0%	$2,309.83	22-May-23	05-Jun-23
P12-E	Flare K.O. Drum, V-109	20	0%	$1,890.45	22-May-23	10-Jun-23
P12-E	Fuel Gas K.O. Drum, V-110	15	0%	$1,156.55	07-May-23	21-May-23
P12-E	Slug Catcher, V-111	15	0%	$3,466.38	07-May-23	21-May-23
P12-E	Degassing vessel, V-112	16	0%	$2,834.04	07-May-23	22-May-23
Instalation of Storage Tank		20	0%	$36,082.68	07-May-23	26-May-23
P12-E	FIRE WATER STORAGE TANK, TK-102	15	0%	$24,510.96	07-May-23	21-May-23
P12-E	Lean Glycol Storage Tank, TK-101	15	0%	$1,472.17	07-May-23	21-May-23
P12-E	Slug Storage Tank, TK-103	15	0%	$10,099.54	12-May-23	26-May-23
Instalation of Air cooler		60	0%	$27,302.91	06-Jul-23	03-Sep-23

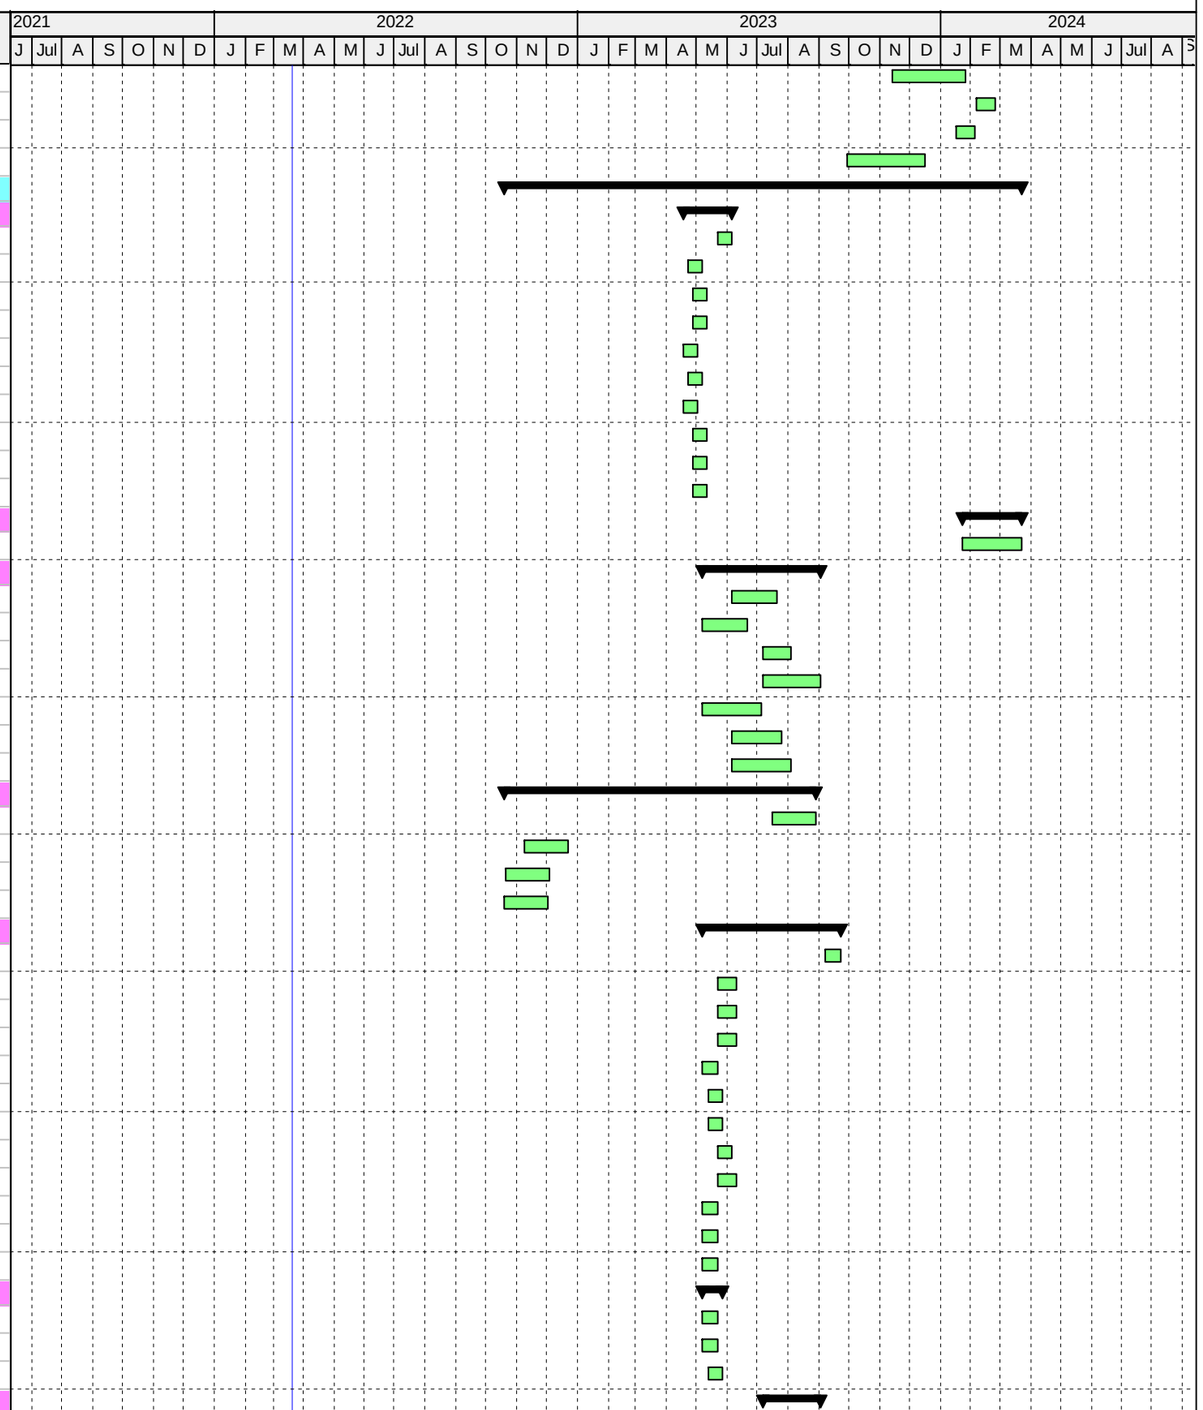


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-E	1ST STAGE GAS COMPRESSION AIR COOLER, AC-101 A	60	0%	$13,651.46	06-Jul-23	03-Sep-23
P12-E	2nd STAGE GAS COMPRESSION AIR COOLER, AC-102 A	60	0%	$13,651.46	06-Jul-23	03-Sep-23
HVAC System		40	0%	$35,690.08	27-Aug-23	05-Oct-23
P12-EI	Installation HVAC Equipment For new Control Room	30	0%	$17,845.04	27-Aug-23	25-Sep-23
P12-EI	Installation HVAC Equipment For SwitchgearBuilding	30	0%	$10,707.03	01-Sep-23	30-Sep-23
P12-EI	Plumbing & Pipe work	30	0%	$7,138.02	06-Sep-23	05-Oct-23
Electrical		320	0%	$404,368.65	26-Apr-23	10-Mar-24
Diesel Generator		30	0%	$14,516.83	27-Aug-23	25-Sep-23
P12-E	Diesel Generator	30	0%	$14,516.83	27-Aug-23	25-Sep-23
Power&Distribution Transformer		30	0%	$20,744.11	09-Sep-23	08-Oct-23
P12-E	Power&Distribution Transformer	30	0%	$20,744.11	09-Sep-23	08-Oct-23
Low voltage cabling		47	0%	$33,198.67	09-Oct-23	24-Nov-23
P12-E	Cable Laying	30	0%	$11,585.48	09-Oct-23	07-Nov-23
P12-E	Cable Arragement	5	0%	$11,585.48	08-Nov-23	12-Nov-23
P12-E	Test after cabling(Megger&continuity Test)	5	0%	$3,319.87	13-Nov-23	17-Nov-23
P12-E	Cable Marking&Tag	2	0%	$3,983.84	18-Nov-23	19-Nov-23
P12-E	Cable Lug & Gland	5	0%	$2,723.99	20-Nov-23	24-Nov-23
High voltage cabling		47	0%	$29,033.67	09-Oct-23	24-Nov-23
P12-E	Cable Laying	30	0%	$10,132.01	09-Oct-23	07-Nov-23
P12-E	Cable Arragement	5	0%	$10,132.01	08-Nov-23	12-Nov-23
P12-E	Test after cabling(Megger&continuity Test)	5	0%	$2,903.37	13-Nov-23	17-Nov-23
P12-E	Cable Marking&Tag	2	0%	$3,484.04	18-Nov-23	19-Nov-23
P12-E	Cable Lug & Gland	5	0%	$2,382.25	20-Nov-23	24-Nov-23
Lighting tower		45	0%	$22,806.39	26-Apr-23	09-Jun-23
P12-E	Lighting tower	45	0%	$22,806.39	26-Apr-23	09-Jun-23
HV,MV Panel/ Switchgear Installation		25	0%	$8,410.87	16-Sep-23	10-Oct-23
P12-E	HV,MV Panel/ Switchgear Installation	25	0%	$8,410.87	16-Sep-23	10-Oct-23
LV Panel / Switchgear / Mcc Installation		30	0%	$101,496.53	16-Sep-23	15-Oct-23
P12-E	LV Panel / Switchgear / Mcc Installation	30	0%	$101,496.53	16-Sep-23	15-Oct-23
Earthing & Lightgning System Installation		35	0%	$24,868.67	16-Sep-23	20-Oct-23
P12-E	Earthing System Installtion	35	0%	$24,868.67	16-Sep-23	20-Oct-23
UPS & DC System & Battery Charger Installtion		30	0%	$20,744.11	16-Sep-23	15-Oct-23
P12-E	UPS & DC System & Battery Charger Installtion	30	0%	$20,744.11	16-Sep-23	15-Oct-23
MV&LV Capacitor Bank Installation		25	0%	$20,744.11	16-Sep-23	10-Oct-23
P12-E	MV&LV Capacitor Bank Installation	25	0%	$20,744.11	16-Sep-23	10-Oct-23
Cables Termination		15	0%	$8,289.56	25-Nov-23	09-Dec-23
P12-E	Cables Termination	15	0%	$8,289.56	25-Nov-23	09-Dec-23
power socket Building &Shelters		30	0%	$8,289.56	09-Sep-23	08-Oct-23
P12-E	power socket Building &Shelters	30	0%	$8,289.56	09-Sep-23	08-Oct-23
Lighting System Installation Building &Shelters		35	0%	$8,289.56	17-Jun-23	21-Jul-23
P12-E	Lighting System Installation Building &Shelters	35	0%	$8,289.56	17-Jun-23	21-Jul-23
Local Control Panle Installation(LCS)		30	0%	$20,744.11	16-Sep-23	15-Oct-23
P12-E	Local Control Panle Installation(LCS)	30	0%	$20,744.11	16-Sep-23	15-Oct-23
CableTray&Ladder/MV,LV Switchgear		30	0%	$41,488.22	09-Sep-23	08-Oct-23
P12-E	CableTray&Ladder/MV,LV Switchgear	30	0%	$41,488.22	09-Sep-23	08-Oct-23
Conduit		15	0%	$6,227.28	25-Jun-23	09-Jul-23
P12-E	Conduit	15	0%	$6,227.28	25-Jun-23	09-Jul-23
Cathodic system		20	0%	$14,476.40	20-Feb-24	10-Mar-24
P12-E	Cathodic system	20	0%	$14,476.40	20-Feb-24	10-Mar-24
Control & Instrumentation		584	0%	$428,637.91	13-May-22	17-Dec-23

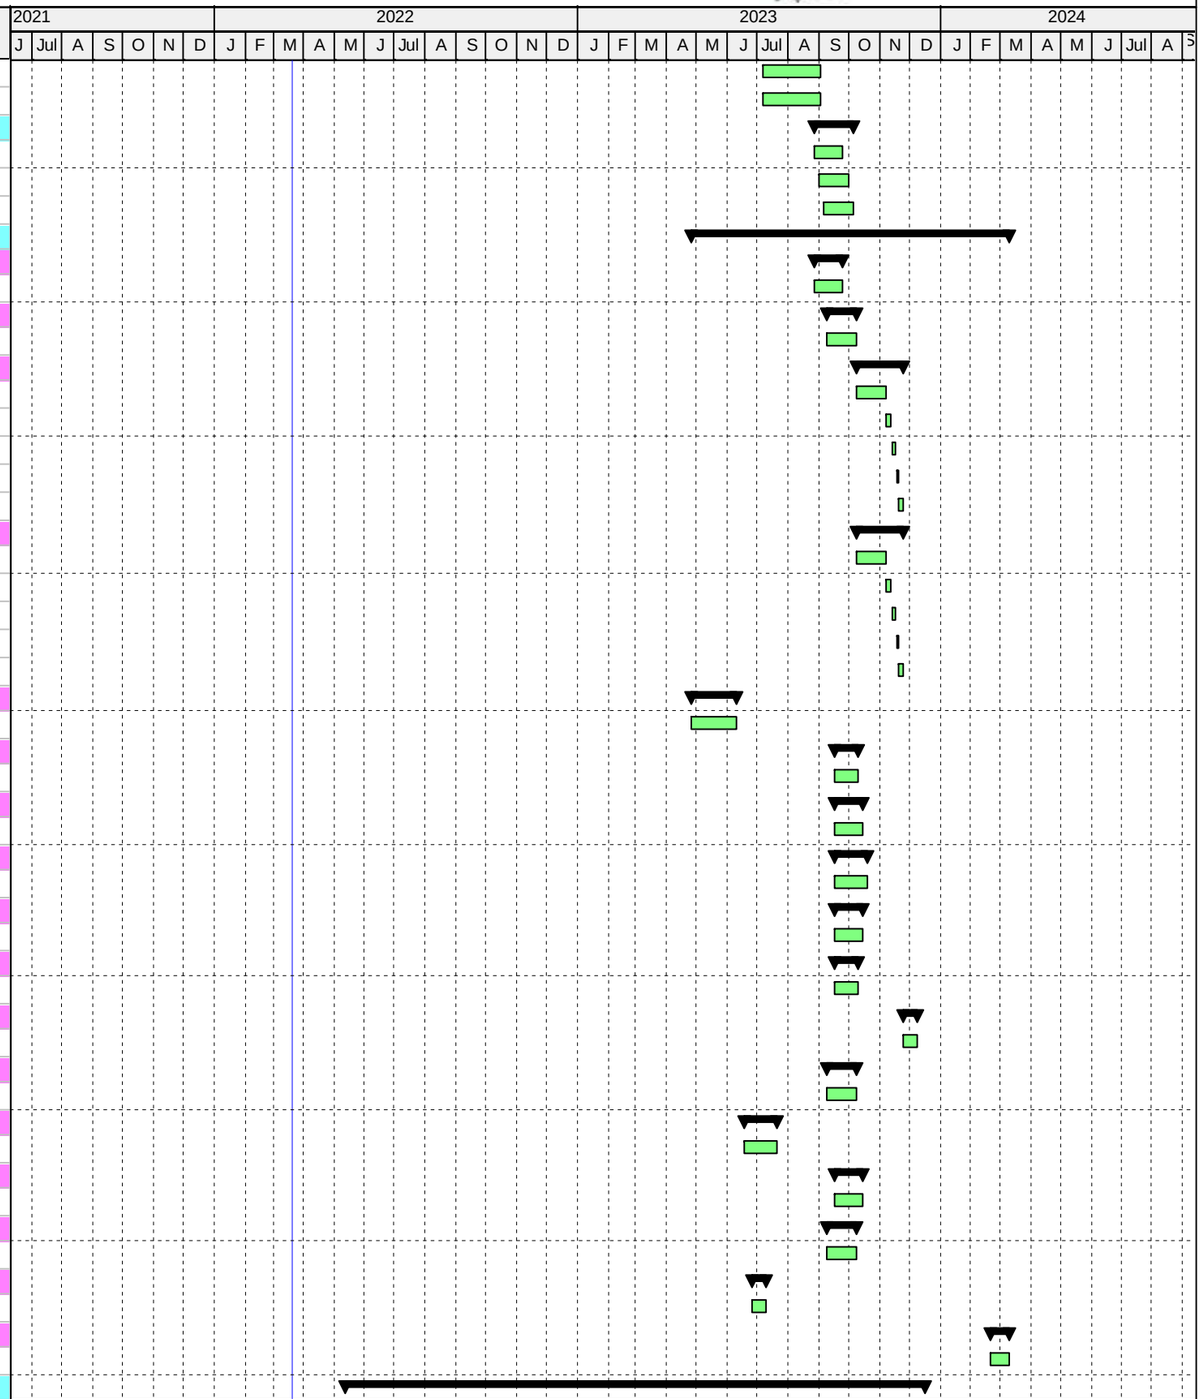


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
Tray&Ladder		30	0%	$25,718.27	30-Oct-22	28-Nov-22
P12-E	Tray & Ladder	25	0%	$15,430.96	30-Oct-22	23-Nov-22
P12-E	support installation for cable trays	30	0%	$10,287.31	30-Oct-22	28-Nov-22
CONDUIT		60	0%	$9,987.26	13-May-22	11-Jul-22
P12-E	Conduit	35	0%	$9,787.52	13-May-22	16-Jun-22
P12-E	Handover(ITP Delivery)	25	0%	$199.75	17-Jun-22	11-Jul-22
Junction Boxes		15	0%	$18,560.02	09-Sep-23	23-Sep-23
P12-E	Digital (on/off)	15	0%	$14,140.97	09-Sep-23	23-Sep-23
P12-E	Analog	10	0%	$4,419.05	09-Sep-23	18-Sep-23
CABLING		62	0%	$62,881.18	14-Mar-23	14-May-23
P12-E	Cable Laying	45	0%	$31,440.59	14-Mar-23	27-Apr-23
P12-E	Cable Arragement	5	0%	$9,432.18	28-Apr-23	02-May-23
P12-E	Test after cabling(continuity Test)	5	0%	$3,144.06	03-May-23	07-May-23
P12-E	Cable Marking&Tag	2	0%	$6,288.12	08-May-23	09-May-23
P12-E	Connection & Glanding	5	0%	$12,576.24	10-May-23	14-May-23
DCS System		37	0%	$25,718.27	16-Sep-23	22-Oct-23
P12-E	marshaling cabinets	15	0%	$19,545.89	16-Sep-23	30-Sep-23
P12-E	operator desks	10	0%	$3,086.19	01-Oct-23	10-Oct-23
P12-E	engineering sations	5	0%	$2,057.46	11-Oct-23	15-Oct-23
P12-E	printers	2	0%	$514.37	16-Oct-23	17-Oct-23
P12-E	operator stations	5	0%	$514.37	18-Oct-23	22-Oct-23
ESD System		37	0%	$25,718.27	16-Sep-23	22-Oct-23
P12-E	marshaling cabinets	15	0%	$19,545.89	16-Sep-23	30-Sep-23
P12-E	operator desks	10	0%	$3,086.19	01-Oct-23	10-Oct-23
P12-E	engineering sations	5	0%	$2,057.46	11-Oct-23	15-Oct-23
P12-E	printers	2	0%	$514.37	16-Oct-23	17-Oct-23
P12-E	operator stations	5	0%	$514.37	18-Oct-23	22-Oct-23
F & G System		32	0%	$25,718.27	16-Sep-23	17-Oct-23
P12-E	F & G system panel	15	0%	$8,229.85	16-Sep-23	30-Sep-23
P12-E	operator station & printer	2	0%	$3,086.19	01-Oct-23	02-Oct-23
P12-E	engineering station	5	0%	$3,600.56	03-Oct-23	07-Oct-23
P12-E	operator stations	5	0%	$1,285.91	08-Oct-23	12-Oct-23
P12-E	Gas detectors	10	0%	$2,057.46	01-Oct-23	10-Oct-23
P12-E	flame detectors	5	0%	$2,057.46	13-Oct-23	17-Oct-23
P12-E	emergency push buttons	5	0%	$514.37	01-Oct-23	05-Oct-23
P12-E	manual alarm call points (MAC)	10	0%	$771.55	01-Oct-23	10-Oct-23
P12-E	smoke detectors	5	0%	$2,057.46	01-Oct-23	05-Oct-23
P12-E	heat detectors	10	0%	$2,057.46	01-Oct-23	10-Oct-23
CCTV		311	0%	$37,162.91	24-Nov-22	30-Sep-23
P12-E	suport & stands	5	0%	$10,033.98	01-Jan-23	05-Jan-23
P12-E	cameras installation	10	0%	$7,804.21	01-Jan-23	10-Jan-23
P12-E	control room monitoring System	10	0%	$8,547.47	16-Sep-23	25-Sep-23
P12-E	control room recorder & MUX & I/0 cards	5	0%	$6,689.32	26-Sep-23	30-Sep-23
P12-E	cabling	30	0%	$4,087.92	24-Nov-22	23-Dec-22
CO2 System		30	0%	$12,859.14	21-Jul-22	19-Aug-22
P12-E	INSTRUMENT HOOK UP Installation	30	0%	$12,859.14	21-Jul-22	19-Aug-22
FIELDINSTRUMENT		535	0%	$184,314.30	01-Jul-22	17-Dec-23
Installation		35	0%	$129,020.01	13-Nov-23	17-Dec-23
P12-	FE - FLOW ELEMENTS (ORIFICE PLATE & FLANGE) Orifi	35	0%	$12,256.90	13-Nov-23	17-Dec-23

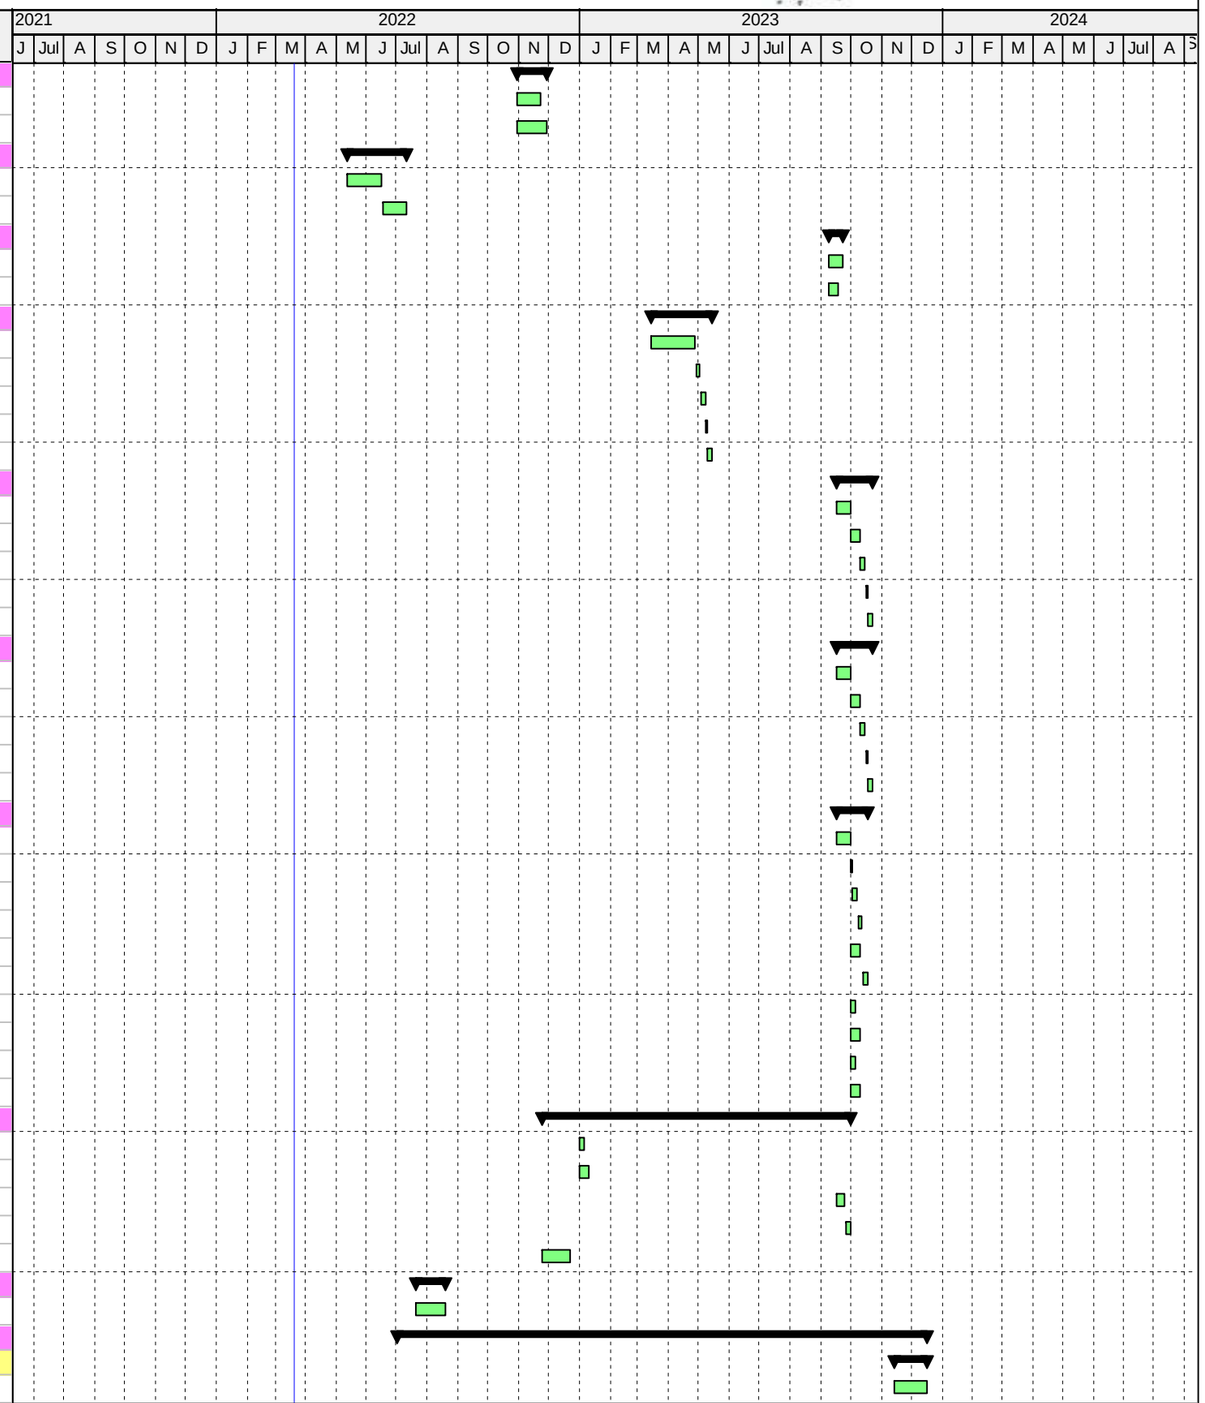


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Progress %	Budgete	Start	Finish
P12-	FI - FLOW INDICATOR ARMORED METAL TUBE ROTAM	30	0%	$34,616.07	13-Nov-23	12-Dec-23
P12-	CC - CORROSION COUPON	30	0%	$16,862.92	13-Nov-23	12-Dec-23
P12-	CP/CT - CORROSION PROBE / TRANSMITTER WITH DA	25	0%	$12,256.90	13-Nov-23	07-Dec-23
P12-	PG - PRESSURE GAUGE	25	0%	$11,031.21	13-Nov-23	07-Dec-23
P12-	PDG - DIFFERENTIAL PRESSURE GAUGE	20	0%	$8,270.18	13-Nov-23	02-Dec-23
P12-	PT - SMART PRESSURE TRANSMITTER	25	0%	$4,593.11	13-Nov-23	07-Dec-23
P12-	FT - SMART DIFF. (FLOW) PRESSURE TRANSMITTER	20	0%	$7,663.79	13-Nov-23	02-Dec-23
P12-	PDT - SMART DIFFERENTIAL PRESSURE TRANSMITTER	25	0%	$9,212.03	13-Nov-23	07-Dec-23
P12-	FTV & PCV (flow control valve -Pressure awitch valve)	20	0%	$3,225.50	28-Nov-23	17-Dec-23
P12-	On/Off Valve	20	0%	$2,580.40	13-Nov-23	02-Dec-23
P12-	PSL & PSH & PSHH & PSLL presure switvh low	20	0%	$3,225.50	13-Nov-23	02-Dec-23
P12-	TT - SMART TEMPERATURE TRANSMITTER	20	0%	$3,225.50	13-Nov-23	02-Dec-23
Calibration		20	0%	$55,294.29	01-Jul-22	20-Jul-22
P12-	Calibration	20	0%	$55,294.29	01-Jul-22	20-Jul-22
Intercom & Telecom		60	0%	$23,912.36	12-May-23	10-Jul-23
P12-EI	Telephone System	30	0%	$7,173.71	12-May-23	10-Jun-23
P12-EI	Telecome Tower Instalation	25	0%	$10,760.56	11-Jun-23	05-Jul-23
P12-EI	VHF System	30	0%	$5,978.09	11-Jun-23	10-Jul-23
Safety & Fire Fighting		30	0%	$35,690.08	01-Jan-23	30-Jan-23
P12-EI	Safety & Fire Fighting	30	0%	$35,690.08	01-Jan-23	30-Jan-23
Pre-commissioning		27	0%	$71,380.17	28-Mar-24	23-Apr-24
P12-EI	Pre-commissioning	20	0%	$64,242.15	28-Mar-24	16-Apr-24
P12-EI	Ready for Comm.Certificate(RFCC)	7	0%	$7,138.02	17-Apr-24	23-Apr-24
Job Site HSE Supervision (Surface)		630	0%	$36,050.59	18-Jul-22	07-Apr-24
Job Site HSE Supervision (Surface)		630	0%	$36,050.59	18-Jul-22	07-Apr-24
P12-EI	Job Site HSE Supervision (Surface)	630	0%	$36,050.59	18-Jul-22	07-Apr-24
Commissioning, Startup & Handover		60	0%	$309,151.95	24-Apr-24	22-Jun-24
Commissioning		40	0%	$92,745.55	24-Apr-24	02-Jun-24
P12-EP	Materials & Utilities Ready for Commissioning	25	0%	$4,637.28	24-Apr-24	18-May-24
P12-EP	Receiving Facilities Ready for Commissioning	20	0%	$4,637.28	04-May-24	23-May-24
P12-EP	Permits Obtained for Commissioning	20	0%	$4,637.28	09-May-24	28-May-24
P12-EP	Integrated Commissioning	18	0%	$74,196.48	14-May-24	31-May-24
P12-EP	Ready for Startup Certificate (RFSU)	12	0%	$4,637.23	22-May-24	02-Jun-24
Startup & Performance Test		20	0%	$123,660.80	24-May-24	12-Jun-24
P12-EP	Startup & Performance Test Run	15	0%	$98,928.64	24-May-24	07-Jun-24
P12-EP	Start of Production (SOP)	20	0%	$24,732.16	24-May-24	12-Jun-24
Handover		30	0%	$92,745.60	24-May-24	22-Jun-24
P12-EP	Compiling & Submitting Final Documentation	22	0%	$27,823.68	24-May-24	14-Jun-24
P12-EP	Training of Operator's Personnel	18	0%	$37,098.24	31-May-24	17-Jun-24
P12-EP	Provisional Acceptance Certificate (PAC)	15	0%	$27,823.68	08-Jun-24	22-Jun-24

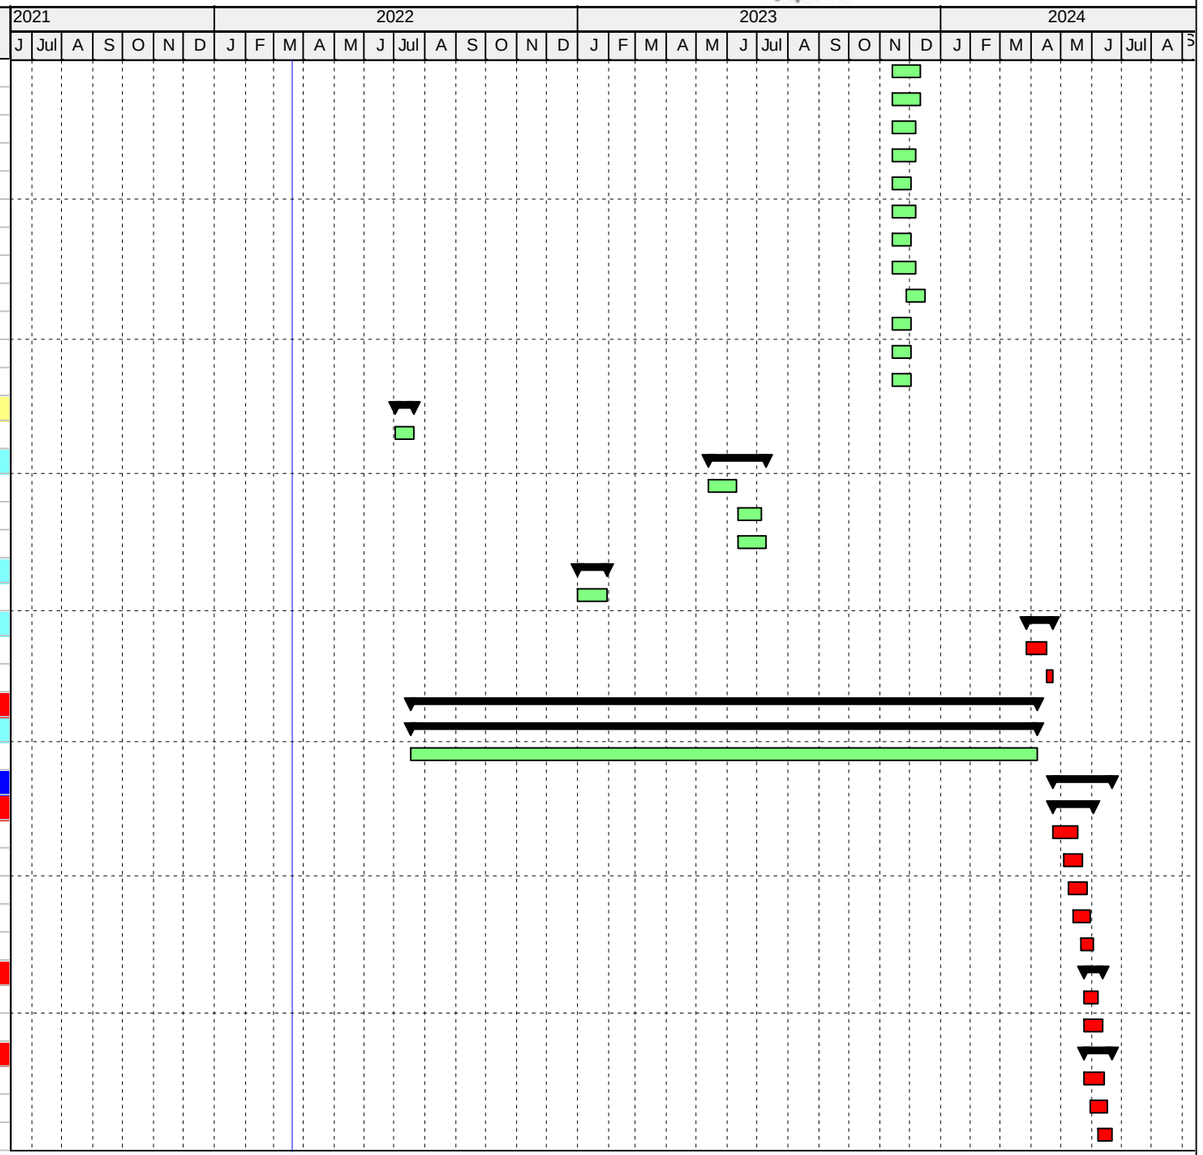

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
